



**USAID**  
FROM THE AMERICAN PEOPLE

**West Bank / Gaza**

## **Local Construction Program (LCP)**


*IQC Basic Contract No.: AID-294-I-13-00002*

*Task Order Contact No.: AID-294-TO-13-00009*

*BIDDU - BEIT ANAN ROAD PROJECT - BDU*

*CONSTRUCTION MONTHLY PROGRESS REPORT*

*REPORTING PERIOD: OCTOBER 23 - NOVEMBER 30, 2013*

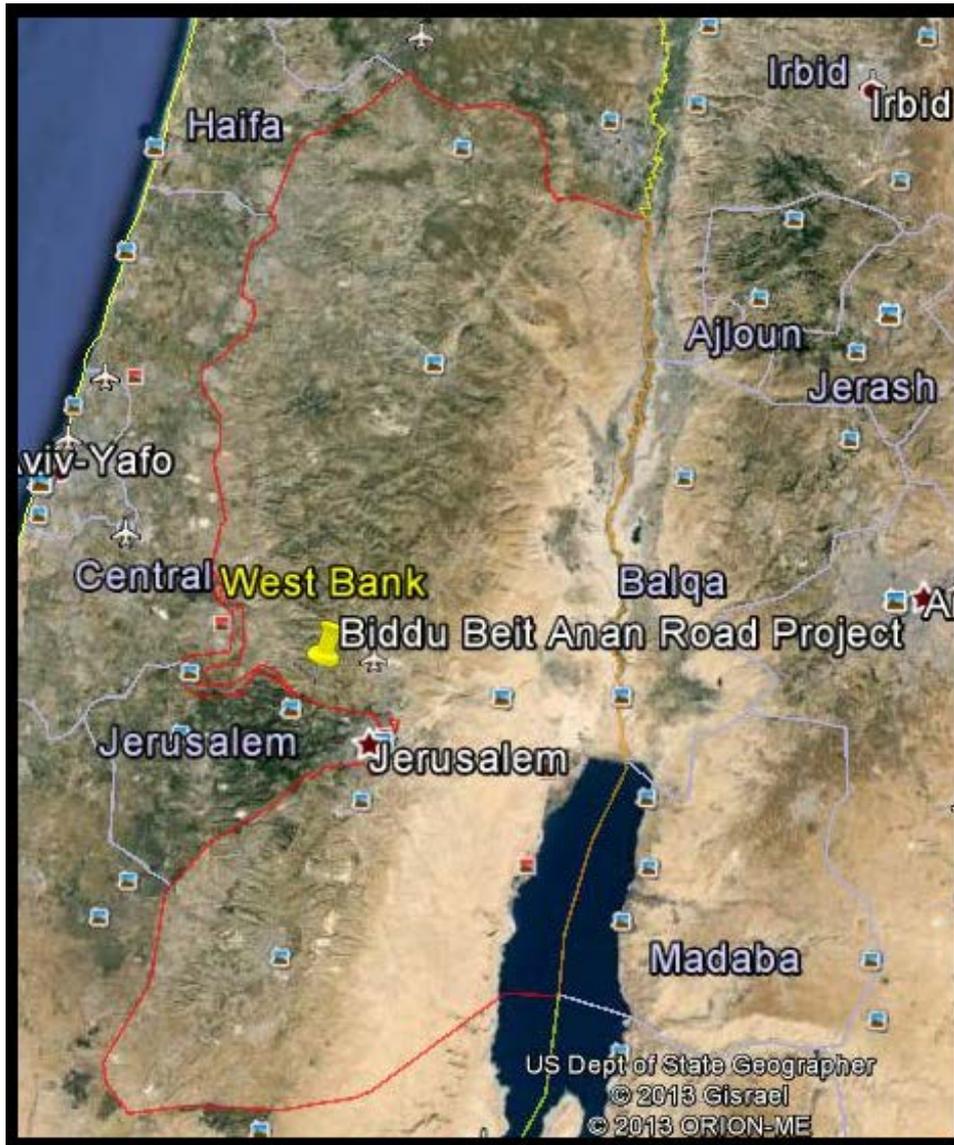

**Submitted by: Saqqa & Khoudary General Contracting Company (SAK)**

**December 05, 2013**

## **Local Construction Program (LCP)**

**Task Order Contract No.: AID - 294 - TO - 13 - 00009**  
**BIDDU BEIT ANAN ROAD PROJECT - BDU**

## **Construction Monthly Progress Report**

**Reporting Period: October 23 - November 30, 2013**

Contractor:

**Saqqa & Khoudary General Contracting Company (SAK)**

**This report is made possible by the support of the American People through the United States Agency for International Development (USAID). The contents of this report are the sole responsibility of Saqqa and Khoudary and do not necessarily reflect the views of USAID or the United State Government.**

## Table of Contents

1	Task Order Overview	5
2	Safety	7
3	Environmental Compliance	8
4	Traffic Control Measures	8
5	Community Outreach	8
6	Gender Action Plan	8
7	Coordination Meeting	8
8	Meetings	9
9	Site visitor	9
10	Material and Equipment Delivered to Site	9
11	Progress and Scheduling	9
12	Activities During this Reporting Period	9
13	Planned Activities for Next Month	9
14	Indicator No1	10
15	Indicator No2	10
16	Working / Non – Working Days	10
17	Site Memos	10
18	Inspection Requests	10
19	Quality Control and Test Results	11
20	Submittals	11
21	Request for Information	11
22	Transmittals	11
23	Payments	12
24	Variation Order	12
25	Variation Order request	12
26	Obstacles and Challenges	12
27	Progress Photos	13
	Annexes	15
	Materials - Equipment Receiving Log	
	Detailed Time Schedule	
	Progress S – Curve versus Actual	
	Site Memos Log	
	Inspection Requests Log	
	Submittal Log	
	RFI's Log	
	Geo – Mis Data	

## 1. Task Order Overview

### 1.1. Description of the Project


This project consists of upgrading 2.15 km of the Biddu Beit Anan Road. The road is a two-lane main road that connects the town of Biddu with the community of Beit Anan through the town of Al Qubeibieh in the Governorate of Jerusalem. The existing roadways suffer from deteriorated surfaces due to extended lack of maintenance and repair.

The scope of work consists of excavation works, embankment filling, pavement layer construction, installation of storm water drainage systems, installation of safety features (signage, road marking, cat eyes, handrails and guardrails), concrete gravity walls, retaining walls and any other items needed to complete the project.


### 1.2. Project General Information

<b>Project Name:</b>	Biddu Beit Anan Road
<b>Project No.:</b>	AID-294-I-13-00002
<b>Task Order No.:</b>	AID-294-13-00009
<b>Award Date:</b>	September 18, 2013
<b>NTP Date:</b>	October 23, 2013
<b>Contract Value:</b>	USD 1,653,135.00
<b>BOQ Line Item Amount:</b>	USD 1,346,452.50
<b>Day Work Amount:</b>	USD 300,000
<b>Modified BOQ Line Item:</b>	USD 1,346,452.50
<b>Modified Day Work Amount:</b>	USD 300,000
<b>Start Date Of Construction Activity:</b>	Not started during the reporting period
<b>Contractual Period Of Performance:</b>	October 23, 2013 to May 20, 2014
<b>Contractual End Date And The Modified Contractual End Date:</b>	May 20, 2014
<b>Estimated Completion Date:</b>	May 20, 2014
<b>Project Location (Area and governorate):</b>	The project located in Jerusalem Governorate in Area B, except 340 meters are located in Area C, between stations (1+780) and (2+060).

### 1.3. Project Key Map

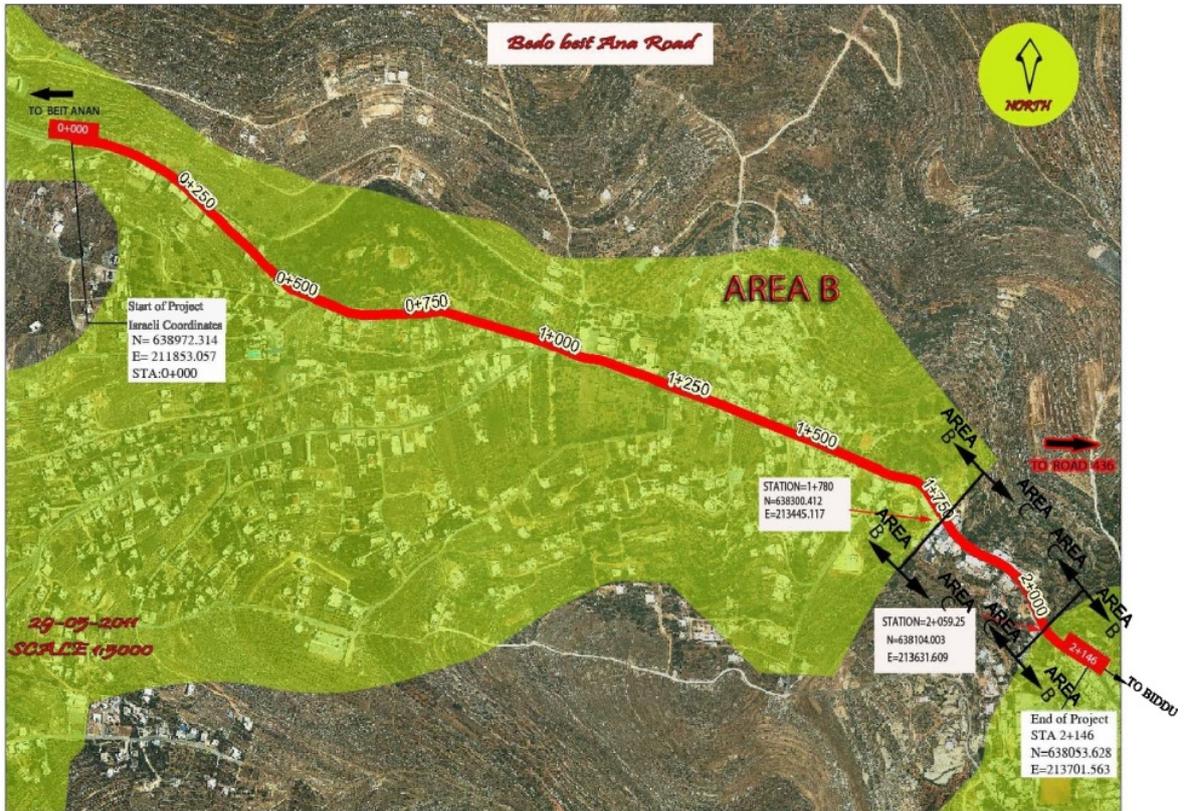

## 1.4. Project Dashboard Status

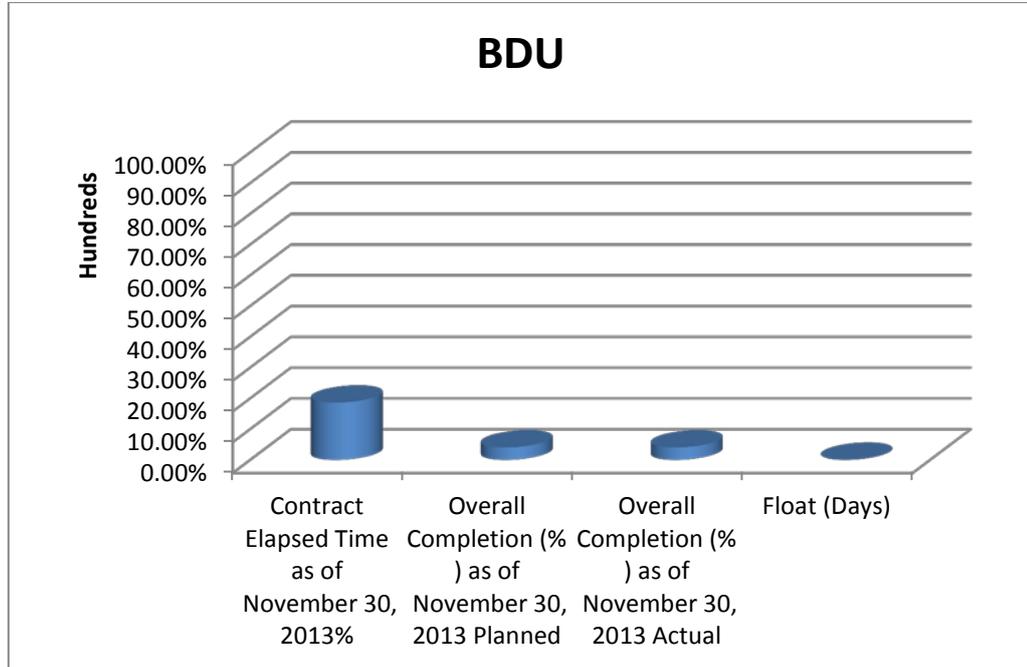

	<b>BDU</b>
<b>Contract Elapsed Time as of November 30, 2013 [%]</b>	18.57%
<b>Overall Completion (%) as of November 30, 2013 Planned</b>	4%
<b>Overall Completion (%) as of November 30, 2013 Actual</b>	4%
<b>Float (Days)</b>	0

## 2. Safety

### 2.1. Traffic and Safety Management

Traffic plan including access roads and detours was submitted for approval to the CMC in order to provide safe access roads.

All engineers and labors have the required safety equipment and they were instructed to use it during all working hours.

### 2.2. Safety Meetings

Internal Toolbox meeting was conducted to train SAK staff for the safety rules and regulations on November 25, 2013.

### **2.3. Accident Status**

Not applicable during this reporting period.

### **2.4. Notice of Unsafe Condition**

None reported during this reporting period.

### **2.5. Safety Conclusion**

Safety Plan was submitted for approval to the CMC, it was reviewed and general comments found. SAK will re-submit the plan during the first week of December. Safety equipment PPE were purchased and prepared to be used upon construction.

## **3. Environmental Compliance**

Environmental Monitoring and Mitigation Plan –one of the required pre-construction submittals was submitted and approved by CMC.

## **4. Traffic Control Measures**

Not applicable during this reporting period.

## **5. Community Outreach**

- 5.1. Arrangements were made with all concerned utilities providers and municipalities to locate all services to avoid any damages during construction period.
- 5.2. Awareness session was arranged and conducted in the Women Local Council in Al Qubebeh village on November 18.
- 5.3. A second awareness session was conducted in Al Qubeibeh Secondary Girls School on November 19.
- 5.4. Preparation works for Projects' Flyers.

## **6. Gender Action Plan**

During this reporting period, the following actions were done under the gender plan within the Biddu project:

- 6.1. Two female engineers were hired under this task order, one of them to work as a site engineer and the other as an office engineer.
- 6.2. Female restroom was constructed on the site.
- 6.3. The site has been made accessible to female visitors and employees.

## **7. Security Coordination Meetings**

- 7.1. Coordination meeting with ICA was held on Jerusalem ICA office on November 20, 2013 to negotiate the overall project – Attached attendees table.
- 7.2. SAK provided two security guards, one located site and the another located at Biddu Beit Anan primary office, they will be available for 24 hours a day 7 days a week.
- 7.3. Several official letters were established and sent to Electrical Company (GETCO), Communication Company (PALTEL), Water Authority, Local Police, and Local Community Councils informing them that SAK about to start construction activities.

## **8. Meetings**

Introductory meeting was held in CMC main office on November 12, 2013.

## **9. Site Visitors**

No visitors during this reporting period.

## **10. Material and Equipment Delivered on Site**

10.1. Material Delivered to Site: Concrete B-300 was delivered on site to cast the foundation of the temporary project signs – Attached table.

10.2. Equipment on Site: An excavator (JCB) and a wheel crane were delivered on site to be used in installation of the temporary project signs – Attached table.

10.3. No procurement activities were done during the reporting period.

## **11. Progress and Scheduling**

Construction phase did not started during this reporting period, once the site was handed over on October 29, 2013, the pre-construction submittals and the mobilization activities were immediately started and still ongoing.

Both 30 Day Schedule and 60 Day Operation of Plan were submitted and approved during the reporting period, while the CPM submittal is still on going and to be completed by the first 10 days of the next reporting period. Both 30 Day Schedule and 60 Day Operation of Plan are attached (Attachment No. 1 and 2).

## **12. Activities During this Reporting Period**

### **12.1. Mobilization:**

- 12.1.1. All required Guarantees and Insurances were provided.
- 12.1.2. Engineers Primary Field Office was provided and furnished.
- 12.1.3. Project Signs are supplied and installed on assigned places.
- 12.1.4. All required permits and approvals are obtained.
- 12.1.5. IT facilities were submitted, approved and provided to CMC.
- 12.1.6. Safety program is conducted and still on-going.
- 12.1.7. Temporary site office and female bathrooms were constructed.
- 12.1.8. On site storage yard was constructed.
- 12.1.9. Site condition survey was done.

### **12.2. Pre-Construction Submittals**

Attached in Item 20 below.

## **13. Planned Activities for Next Month**

The following are the main activities planned for next reporting period:

- a. Complete working in pre-construction submittals.

- b. Complete working in construction submittals, works should include: shop drawings of concrete gravity walls, road works up to station (1+000), submit material for approval for curbstone, asphalt and guardrail and handrails.
- c. Starting concrete gravity wall from station (0+265) to station (0+295).
- d. Starting concrete gravity wall from station (0+410) to station (0+440).
- e. Starting road works from station (0+000) to station (0+600), work includes: relocating existing poles, excavation, subgrade works, topping layers, and base course layer.

Please see the attached 60 Day Plan of Operation.

#### **14. Indicator No. 01 – Number of Kilometers of Transportation Infrastructure Rehabilitated Through the USAID Assistance**

Target value = 2.15 Km

Number of kilometers constructed previously = 0 Km

Number of kilometers constructed or repaired during this reporting period = 0 Km

Total cumulative number of kilometers constructed = 0 Km.

#### **15. Indicator No. 02 – Manpower Generated – Days of Employment**

Target value = 2500 Man – Days.

Employment generated previously = 0 Man - Days.

Employment generated this reporting period = 169 Man – Days.

Total cumulative employment generated to date = 169 Man – Days.

All information are based on the daily reports and meet the five quality standards.

All information are up to date and accurate.

#### **16. Working / Non – Working Days**

Month	No. of WD	No. of Non WD
October, 2013	8	1
November, 2013	25	5
<b>Total</b>	<b>33</b>	<b>6</b>

All the above non-working days were as a result of official holidays (Fridays).

#### **17. Site Memos**

Non issued during this reporting period.

#### **18. Inspection Requests**

Only one Inspection Request was issued during the reporting period – Attached Inspection Requests Log.

## 19. Quality Control and Test Results

Quality Control Plan (QCP) was prepared and submitted to CMC for approval on November 24, 2013. The (QCP) includes the proposed quality control program that should be followed during the construction phase, including the forms of recording the quality control operations, control activities, testing, administration of the system for both onsite and offsite work.

### Test Results:

No tests were done during the reporting period.

## 20. Submittals

Both pre-construction and construction submittals are ongoing. It is expected that all preconstruction submittals will be completed by the second week of December 2013, while the construction submittals will be on going during the next monthly report's period. The status for submittals is attached.

## 21. Request for Information

No RFI were issued during this reporting period.

## 22. Transmittals

Table of transmittals

S/No.	Description	Submitting Date
TRS-13-00009-(E-C)-001	Conformed Documents and Permits	October 23,2013
TRS-13-00009-(E-C)-002	Cell phones and Simcards	November 05,2013
TRS-13-00009-(E-C)-003	1. 30 Days Schedule. 2. Project Key Staff.	November 10,2013
TRS-13-00009-(E-C)-004	Subcontractor Approval	November 11,2013
TRS-13-00009-(E-C)-005	1. Project Key Staff. 2. Qualification of Testing Labs. 3. Computer System.	November 12,2013
TRS-13-00009-(E-C)-006	1. DJR-from October 23 - to November 18, 2013. 2. Layout of Engineers Field Office. 3. Method Statement-Highway Excavation. 4. Primary Field Office Furniture.	November 19,2013
TRS-13-00009-(E-C)-007	Computer System	November 20,2013
TRS-13-00009-(E-C)-008	1. 60Day Plan of Operation. 2. Dilapidation Survey. 3. DJR-November 19, 2013.	November 21,2013
TRS-13-00009-(E-C)-009	1. Contractor's All Risk Policy & Workmen. 2. Compensation Policy.	November 21,2013

TRS-13-00009-(E-C)-010	<ol style="list-style-type: none"> <li>1. Submittal Schedule.</li> <li>2. Critical Path Method Schedule.</li> <li>3. DJR-from November, 20 to November, 23 2013.</li> </ol>	November 24,2013
TRS-13-00009-(E-C)-011	Project temporary Sign location	November 25,2013
TRS-13-00009-(E-C)-012	<ol style="list-style-type: none"> <li>1. Safety Plan.</li> <li>2. Environmental Monitoring and Mitigation Plan.</li> <li>3. Temporary Project Sign Detail.</li> <li>4. DJR-November, 24 2013 to November, 26 2013.</li> </ol>	November 27,2013

### 23. Payments

No payments were submitted during this reporting period, while the accrued amount is USD 51,292 (Mobilization Payment).

### 24. Variation Orders

No variation orders were issued during this reporting period.

### 25. Variation Order Requests

No variation orders were issued during this reporting period.

### 26. Obstacles and Challenges

No obstacles were observed during this reporting period.

## 27. Progress Photos



**Project Temporary Sign**



**Installation Works for Storage Yard**



**Install Security Fence for Site Storage Yard**



**Women Awareness Session in Al-Qbeibeh Local Council**

# Annexes

# Material, Equipment Receiving Log

**Materials Delivered on Site:**

<b>Item</b>	<b>Description</b>	<b>Quantity</b>	<b>Location</b>
1	Concrete B-300	3 Cu M	Foundation of Project Signs

**Equipment on Site:**

<b>Description</b>	<b>Quantity</b>
Excavator (JCB)	1
Wheel Crane	1

# Detailed Time Schedule

Saqqa and Khoudary General Contracting		30-Day Schedule					Biddu Beit Anan Road Project														
Activity ID	Activity Name	Original Duration	Start	Finish	Free Float	Total Float	October 2013					November 2013				December 2013			January 2014		
							29	06	13	20	27	03	10	17	24	01	08	15	22	29	05
<b>TO13-09 30-Days Schedule/Reviewed</b>		31d	23-Oct-13	22-Nov-13	0d	0d	22-Nov-13, TO13-09 30-Days Schedule/Reviewed														
<b>TO13-09.1 Milestones</b>		31d	23-Oct-13	22-Nov-13	0d	0d	22-Nov-13, TO13-09.1 Milestones														
MILE-01	Notice to Proceed (NTP)	0d	23-Oct-13		0d	0d	◆ Notice to Proceed (NTP)														
MILE-02	Completion of 30 days plan	0d		22-Nov-13	0d	0d	◆ Completion of 30 days plan														
MILE-03	Start Mobilization	0d	23-Oct-13		0d	1d	→ Start Mobilization														
MILE-04	Finish Mobilization	0d		22-Nov-13	0d	0d	◆ Finish Mobilization														
MILE-05	Start Pre Construction Submittals	0d	23-Oct-13		0d	0d	→ Start Pre Construction Submittals														
MILE-06	Finish Pre Construction Submittal	0d		21-Nov-13	1d	1d	◆ Finish Pre Construction Submittal														
<b>TO13-09.2 Coordination Works</b>		31d	23-Oct-13	22-Nov-13	0d	0d	22-Nov-13, TO13-09.2 Coordination Works														
A1000	Coordination Work with the Israel and other parties	31d	23-Oct-13	22-Nov-13	0d	0d	■ Coordination Work with the Israel and other parties														
<b>TO13-09.3 Mobilization Sec 01505</b>		31d	23-Oct-13	22-Nov-13	0d	0d	22-Nov-13, TO13-09.3 Mobilization Sec 01505														
MOB-01	Insurances & Security Premiums	1d	27-Oct-13*	27-Oct-13	26d	26d	→ Insurances & Security Premiums														
MOB-02	Project Signs	20d	23-Oct-13	11-Nov-13	11d	11d	■ Project Signs														
MOB-03	Contractors storage yards	20d	29-Oct-13*	17-Nov-13	5d	5d	■ Contractors storage yards														
MOB-04	Engineers & Contractors Field Offices	10d	26-Oct-13*	04-Nov-13	0d	0d	■ Engineers & Contractors Field Offices														
MOB-05	Site Condition Surveys	18d	24-Oct-13*	10-Nov-13	12d	12d	■ Site Condition Surveys														
MOB-06	Establish Safety Programs	15d	01-Nov-13*	15-Nov-13	7d	7d	■ Establish Safety Programs														
MOB-07	Mobilize Equipment and IT Facilities	5d	05-Nov-13*	09-Nov-13	0d	0d	■ Mobilize Equipment and IT Facilities														

■ Actual Work   
 ■ Critical Remaining Work   
 ▼ Summary  
■ Remaining Work   
 ◆ Milestone

Saqqa and Khoudary General Contracting		30-Day Schedule					Biddu Beit Anan Road Project																	
Activity ID	Activity Name	Original Duration	Start	Finish	Free Float	Total Float	October 2013					November 2013				December 2013				January 2014				
							29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	
MOB-08	Temporary Construction Facilities	13d	10-Nov-13*	22-Nov-13	0d	0d																		
MOB-09	Mobilization Completion	30d	24-Oct-13	22-Nov-13*	0d	0d																		
<b>TO13-09.4 Submittals</b>		30d	23-Oct-13	21-Nov-13	0d	1d																		
<b>TO13-09.4.1 Preconstruction Submittals</b>		30d	23-Oct-13	21-Nov-13	0d	1d																		
PRE-SUB-01	Submittals Schedule	14d	23-Oct-13	05-Nov-13	0d	0d																		
PRE-SUB-01.5	Submittals Schedule approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-02	30-Day Schedule	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-02.5	30-Day Schedule approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-03	Project Signs	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-03.5	Project Signs approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-04	Quality Control Plan & testing laboratory	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-04.5	Quality Control Plan & testing laboratory approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-05	60 Day Operation Plan	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-05.5	60 Day Operation Plan approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-06	Environmental Mitigation and Monitoring Plan	10d	23-Oct-13	01-Nov-13	0d	7d																		
PRE-SUB-06.5	Environmental Mitigation and Monitoring Plan approval	14d	02-Nov-13	15-Nov-13	6d	7d																		
PRE-SUB-07	Traffic Plan	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-07.5	Traffic Plan approval	14d	06-Nov-13	19-Nov-13	2d	3d																		


█ Actual Work   
 █ Critical Remaining Work   
 ▼ Summary  
█ Remaining Work   
 ◆ Milestone

Saqqa and Khoudary General Contracting			30-Day Schedule					Biddu Beit Anan Road Project																
Activity ID	Activity Name	Original Duration	Start	Finish	Free Float	Total Float	October 2013					November 2013				December 2013				January 2014				
							29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	
PRE-SUB-08	Engineer's Field Offices, Equip. & Service	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-08.5	Engineer's Field Offices, Equip. & Service approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-09	CPM Construction Schedule (Baseline)	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-09.5	CPM Construction Schedule (Baseline) approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-10	Safety Plan	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-10.5	Safety Plan approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-11	Subcontractors profile	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-11.5	Subcontractors profile approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-12	General construction method statement	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-12.5	General construction method statement approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-13	Construction Risk Management Program	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-13.5	Construction Risk Management Program approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-14	Dilapidation Survey	14d	23-Oct-13	05-Nov-13	0d	3d																		
PRE-SUB-14.5	Dilapidation Survey approval	14d	06-Nov-13	19-Nov-13	2d	3d																		
PRE-SUB-15	Bank guarantee	9d	23-Oct-13	02-Nov-13	0d	5d																		
PRE-SUB-15.5	Bank guarantee approval	14d	02-Nov-13	16-Nov-13	5d	6d																		
PRE-SUB-16	List of Permits and Licenses	14d	23-Oct-13	07-Nov-13	0d	0d																		
PRE-SUB-16.5	List of Permits and Licenses approval	14d	07-Nov-13	21-Nov-13	0d	1d																		

█ Actual Work   
 █ Critical Remaining Work   
 ▼ Summary  
█ Remaining Work   
 ◆ Milestone

Saqqa and Khoudary General Contracting		30-Day Schedule					Biddu Beit Anan Road Project																	
Activity ID	Activity Name	Original Duration	Start	Finish	Free Float	Total Float	October 2013					November 2013				December 2013				January 2014				
							29	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	
PRE-SUB-17	Key Personnel	14d	23-Oct-13	07-Nov-13	0d	0d																		
PRE-SUB-17.5	Key Personnel approval	14d	07-Nov-13	21-Nov-13	0d	1d																		
PRE-SUB-18	Office layout	14d	23-Oct-13	07-Nov-13	0d	0d																		
PRE-SUB-18.5	Office layout approval	14d	07-Nov-13	21-Nov-13	0d	1d																		

█ Actual Work   
 █ Critical Remaining Work   
 ▼ Summary  
█ Remaining Work   
 ◆ Milestone

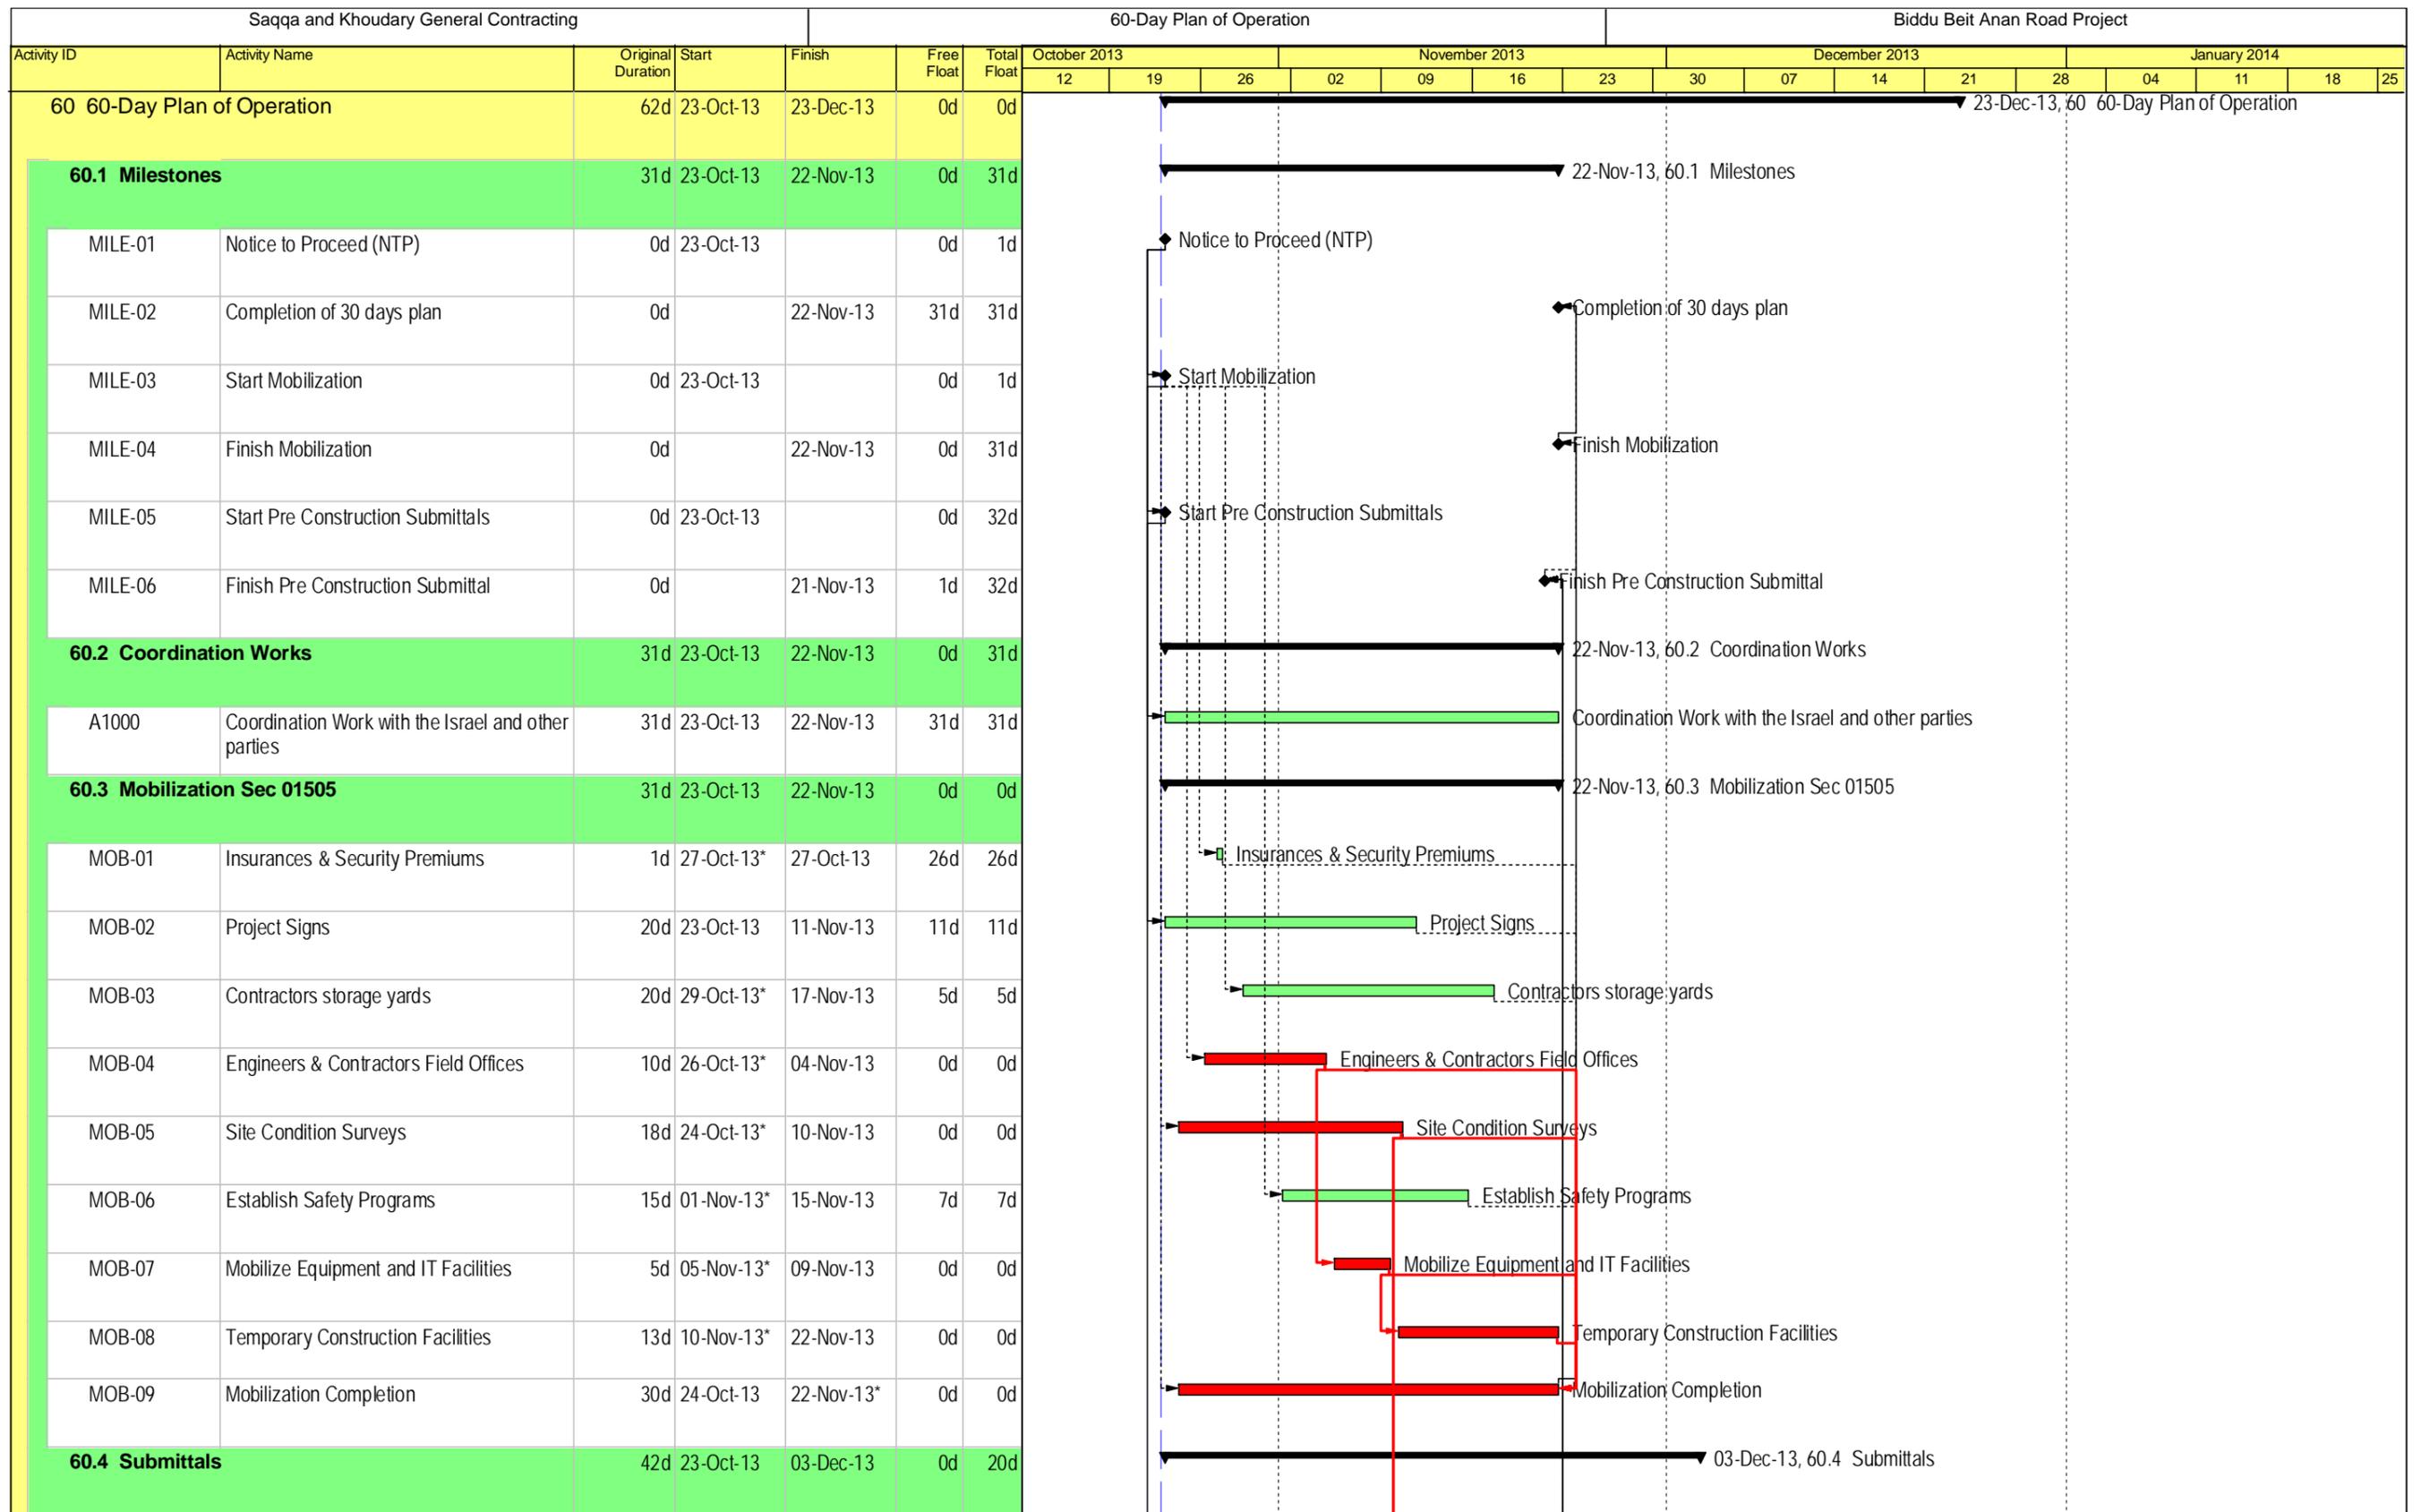


█ Actual Work   
 █ Critical Remaining Work   
 ▼ Summary  
█ Remaining Work   
 ◆ Milestone

Saqqa and Khoudary General Contracting							60-Day Plan of Operation							Biddu Beit Anan Road Project											
Activity ID	Activity Name	Original Duration	Start	Finish	Free Float	Total Float	October 2013			November 2013				December 2013			January 2014								
							12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25			
<b>60.4.1 Preconstruction Submittals</b>		30d	23-Oct-13	21-Nov-13	0d	32d	21-Nov-13, 60.4.1 Preconstruction Submittals																		
PRE-SUB-01	Submittals Schedule	14d	23-Oct-13	05-Nov-13	0d	32d	Submittals Schedule																		
PRE-SUB-01	Submittals Schedule approval	14d	06-Nov-13	19-Nov-13	2d	34d	Submittals Schedule approval																		
PRE-SUB-02	30-Day Schedule	14d	23-Oct-13	05-Nov-13	0d	34d	30-Day Schedule																		
PRE-SUB-02	30-Day Schedule approval	14d	06-Nov-13	19-Nov-13	2d	34d	30-Day Schedule approval																		
PRE-SUB-03	Project Signs	14d	23-Oct-13	05-Nov-13	0d	34d	Project Signs																		
PRE-SUB-03	Project Signs approval	14d	06-Nov-13	19-Nov-13	2d	34d	Project Signs approval																		
PRE-SUB-04	Quality Control Plan & testing laboratory	14d	23-Oct-13	05-Nov-13	0d	34d	Quality Control Plan & testing laboratory																		
PRE-SUB-04	Quality Control Plan & testing laboratory approval	14d	06-Nov-13	19-Nov-13	2d	34d	Quality Control Plan & testing laboratory approval																		
PRE-SUB-05	60 Day Operation Plan	14d	23-Oct-13	05-Nov-13	0d	34d	60 Day Operation Plan																		
PRE-SUB-05	60 Day Operation Plan approval	14d	06-Nov-13	19-Nov-13	2d	34d	60 Day Operation Plan approval																		
PRE-SUB-06	Environmental Mitigation and Monitoring Plan	10d	23-Oct-13	01-Nov-13	0d	38d	Environmental Mitigation and Monitoring Plan																		
PRE-SUB-06	Environmental Mitigation and Monitoring Plan approval	14d	02-Nov-13	15-Nov-13	6d	38d	Environmental Mitigation and Monitoring Plan approval																		
PRE-SUB-07	Traffic Plan	14d	23-Oct-13	05-Nov-13	0d	34d	Traffic Plan																		
PRE-SUB-07	Traffic Plan approval	14d	06-Nov-13	19-Nov-13	2d	34d	Traffic Plan approval																		
PRE-SUB-08	Engineer's Field Offices, Equip. & Service	14d	23-Oct-13	05-Nov-13	0d	34d	Engineer's Field Offices, Equip. & Service																		
PRE-SUB-08	Engineer's Field Offices, Equip. & Service approval	14d	06-Nov-13	19-Nov-13	2d	34d	Engineer's Field Offices, Equip. & Service approval																		
PRE-SUB-09	CPM Construction Schedule (Baseline)	14d	23-Oct-13	05-Nov-13	0d	34d	CPM Construction Schedule (Baseline)																		
PRE-SUB-09	CPM Construction Schedule (Baseline) approval	14d	06-Nov-13	19-Nov-13	2d	34d	CPM Construction Schedule (Baseline) approval																		
PRE-SUB-10	Safety Plan	14d	23-Oct-13	05-Nov-13	0d	34d	Safety Plan																		
PRE-SUB-10	Safety Plan approval	14d	06-Nov-13	19-Nov-13	2d	34d	Safety Plan approval																		


█ Actual Work   
 █ Critical Remaining Work   
 ▼ Summary  
█ Remaining Work   
 ◆ Milestone



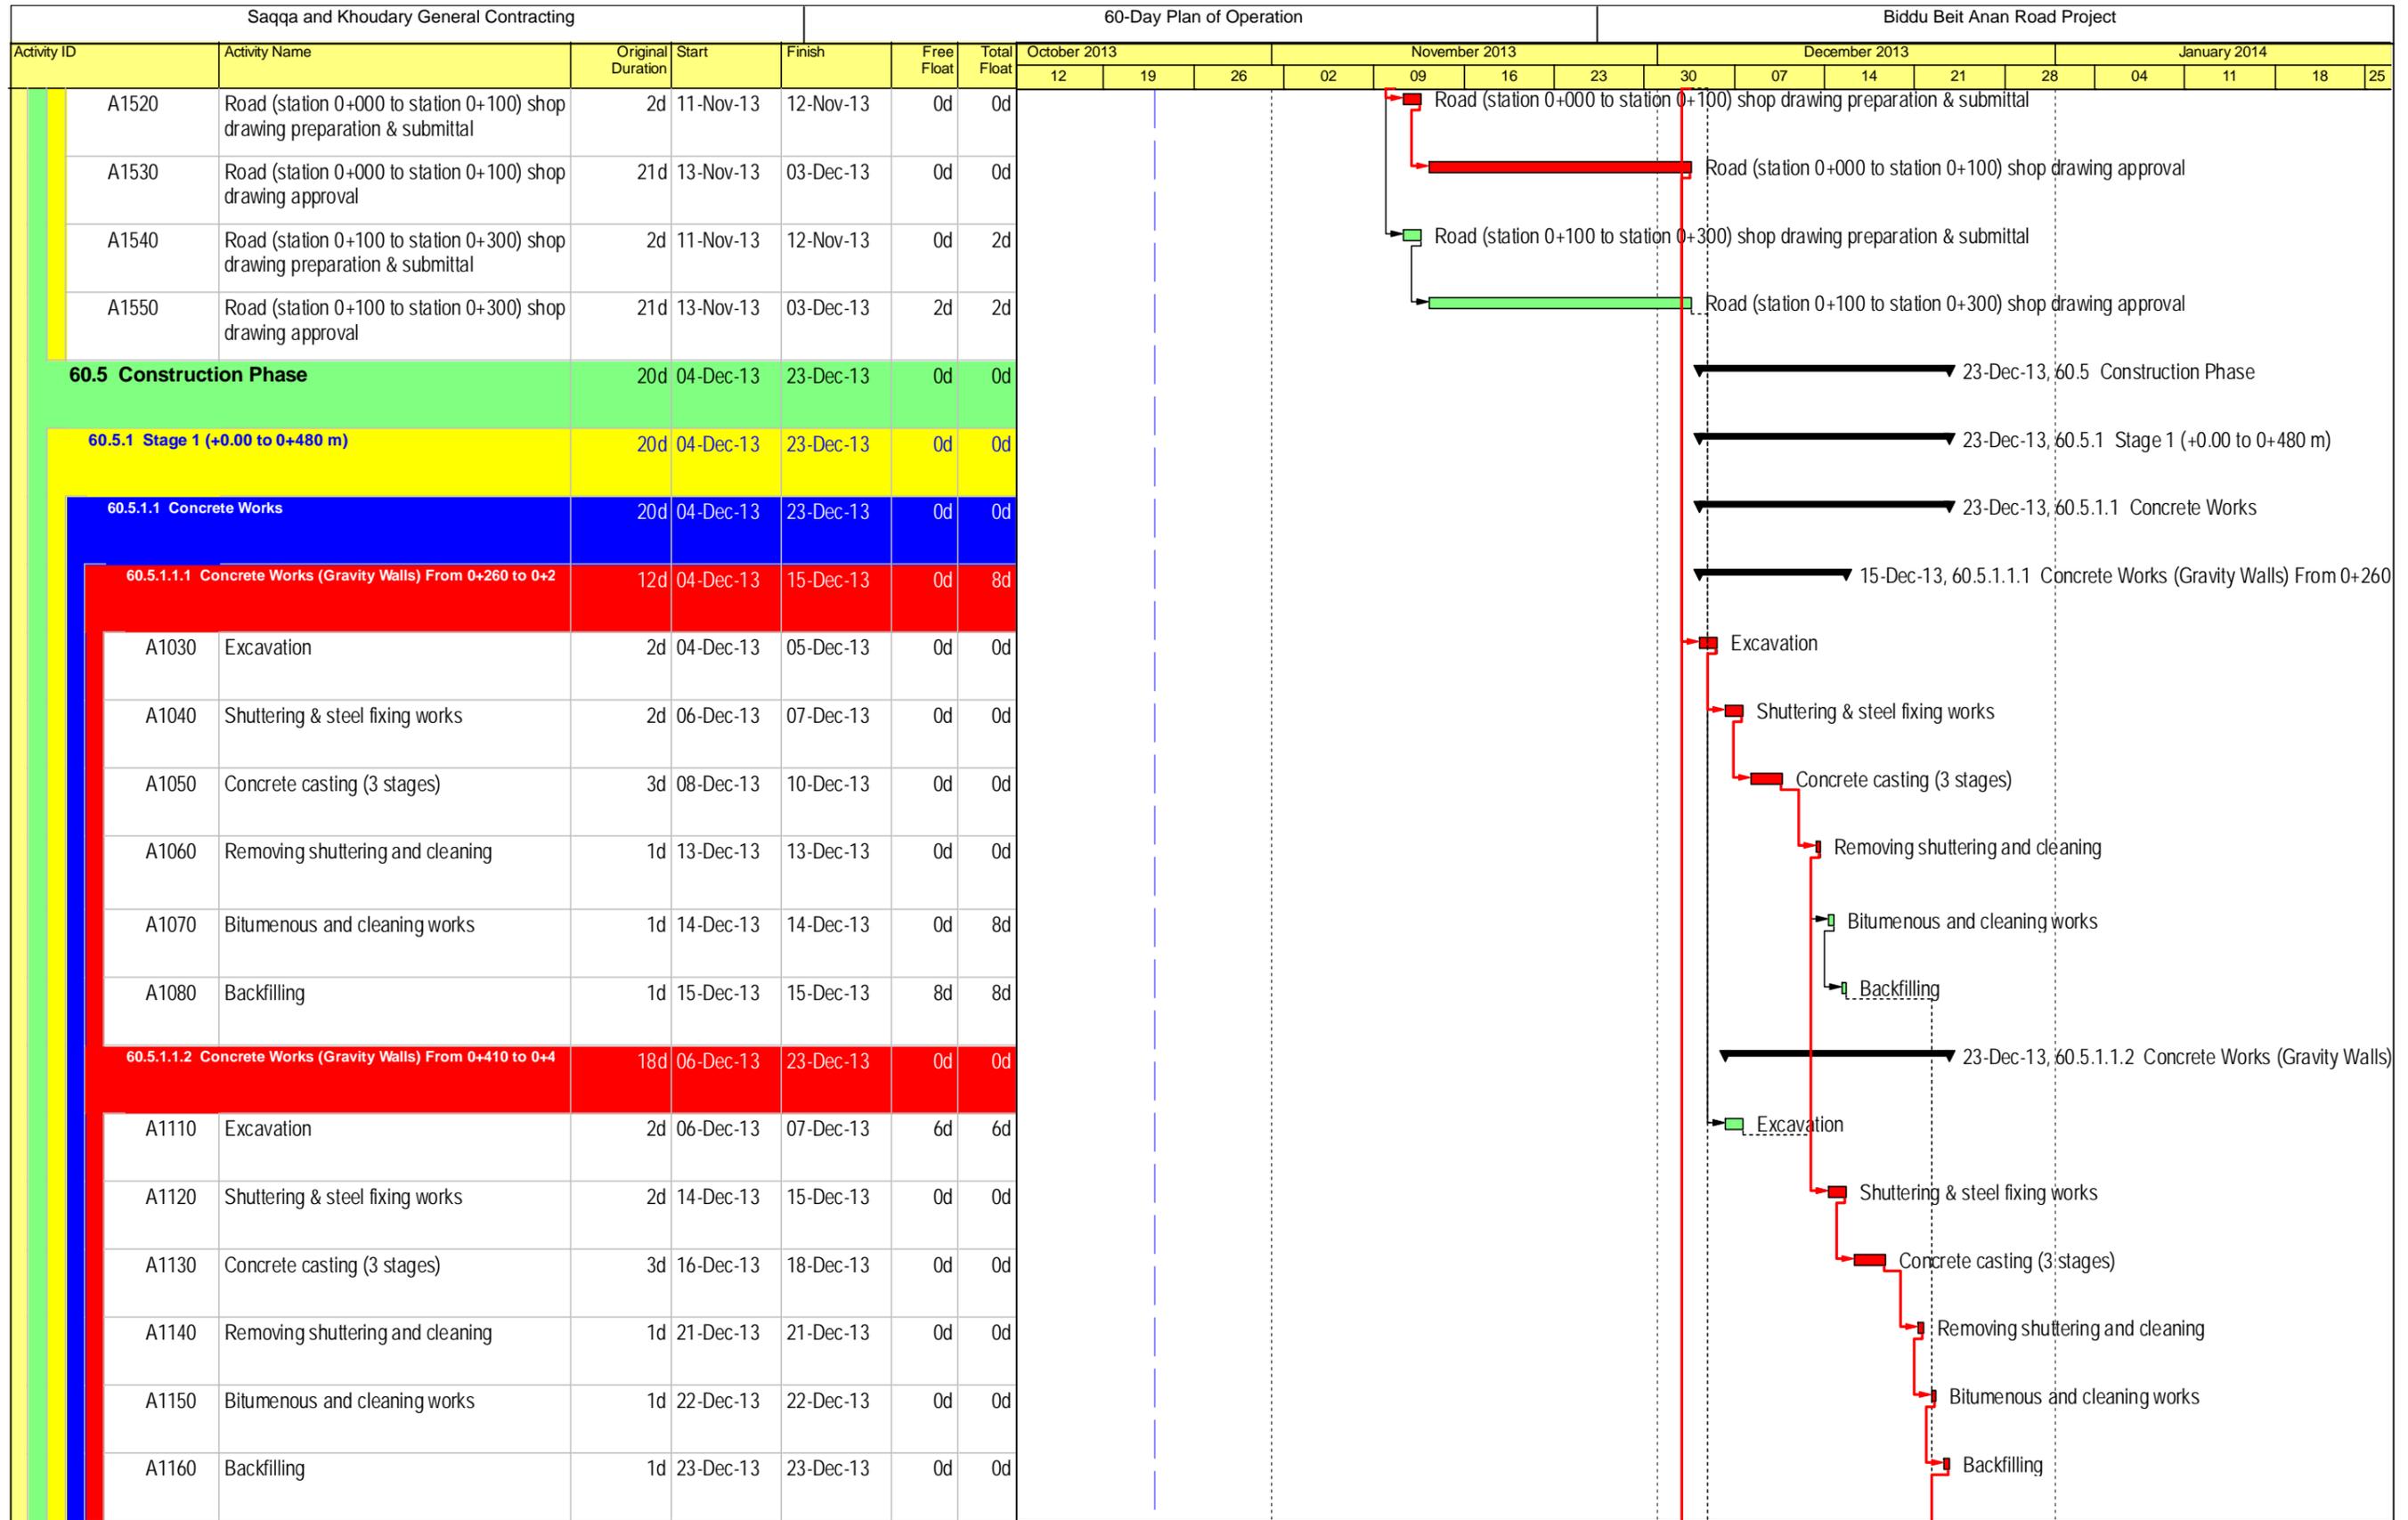

█ Actual Work   
 █ Critical Remaining Work   
 ▶ Summary  
█ Remaining Work   
 ◆ Milestone

Saqqa and Khoudary General Contracting							60-Day Plan of Operation							Biddu Beit Anan Road Project						
Activity ID	Activity Name	Original Duration	Start	Finish	Free Float	Total Float	October 2013			November 2013				December 2013				January 2014		
							12	19	26	02	09	16	23	30	07	14	21	28	04	11
<b>60.5.1.3 Road Works</b>		20d	04-Dec-13	23-Dec-13	0d	0d														
<b>60.5.1.3.1 From station 0+00 to station 0+100</b>		13d	04-Dec-13	16-Dec-13	0d	7d														
A1190	Excavation to specified levels	2d	04-Dec-13	05-Dec-13	0d	0d														
A1200	Subgrade leveling, watering, and compaction	1d	06-Dec-13	06-Dec-13	0d	7d														
A1210	Subgrade approval and testing	1d	07-Dec-13	07-Dec-13	0d	7d														
A1220	Supply and lay 20 cm topping layer	1d	08-Dec-13	08-Dec-13	0d	7d														
A1230	Topping leveling, watering, and compaction	1d	09-Dec-13	09-Dec-13	0d	7d														
A1240	Topping approval and testing	1d	10-Dec-13	10-Dec-13	0d	7d														
A1250	Supply and lay 20 cm basecourse, first layer	1d	11-Dec-13	11-Dec-13	0d	7d														
A1260	Basecourse first layer leveling, watering, and compaction	1d	12-Dec-13	12-Dec-13	0d	7d														
A1270	Basecourse first layer approval and testing	1d	13-Dec-13	13-Dec-13	0d	7d														
A1280	Supply and lay 20 cm basecourse, second layer	1d	14-Dec-13	14-Dec-13	0d	7d														
A1290	Basecourse second layer leveling, watering, and compaction	1d	15-Dec-13	15-Dec-13	0d	7d														
A1300	Basecourse second layer approval and testing	1d	16-Dec-13	16-Dec-13	7d	7d														
<b>60.5.1.3.2 From station 0+100 to station 0+300</b>		18d	06-Dec-13	23-Dec-13	0d	0d														
A1310	Relocating the existing high voltage poles & telephoe poles	1d	06-Dec-13	06-Dec-13	0d	0d														
A1311	Excavation to specified levels	2d	07-Dec-13	08-Dec-13	0d	0d														
A1320	Subgrade leveling, watering, and compaction	2d	09-Dec-13	10-Dec-13	0d	0d														
A1330	Subgrade approval and testing	1d	10-Dec-13	10-Dec-13	0d	0d														
A1340	Supply and lay 20 cm topping layer	2d	11-Dec-13	12-Dec-13	0d	0d														
A1350	Topping leveling, watering, and compaction	1d	12-Dec-13	12-Dec-13	0d	0d														

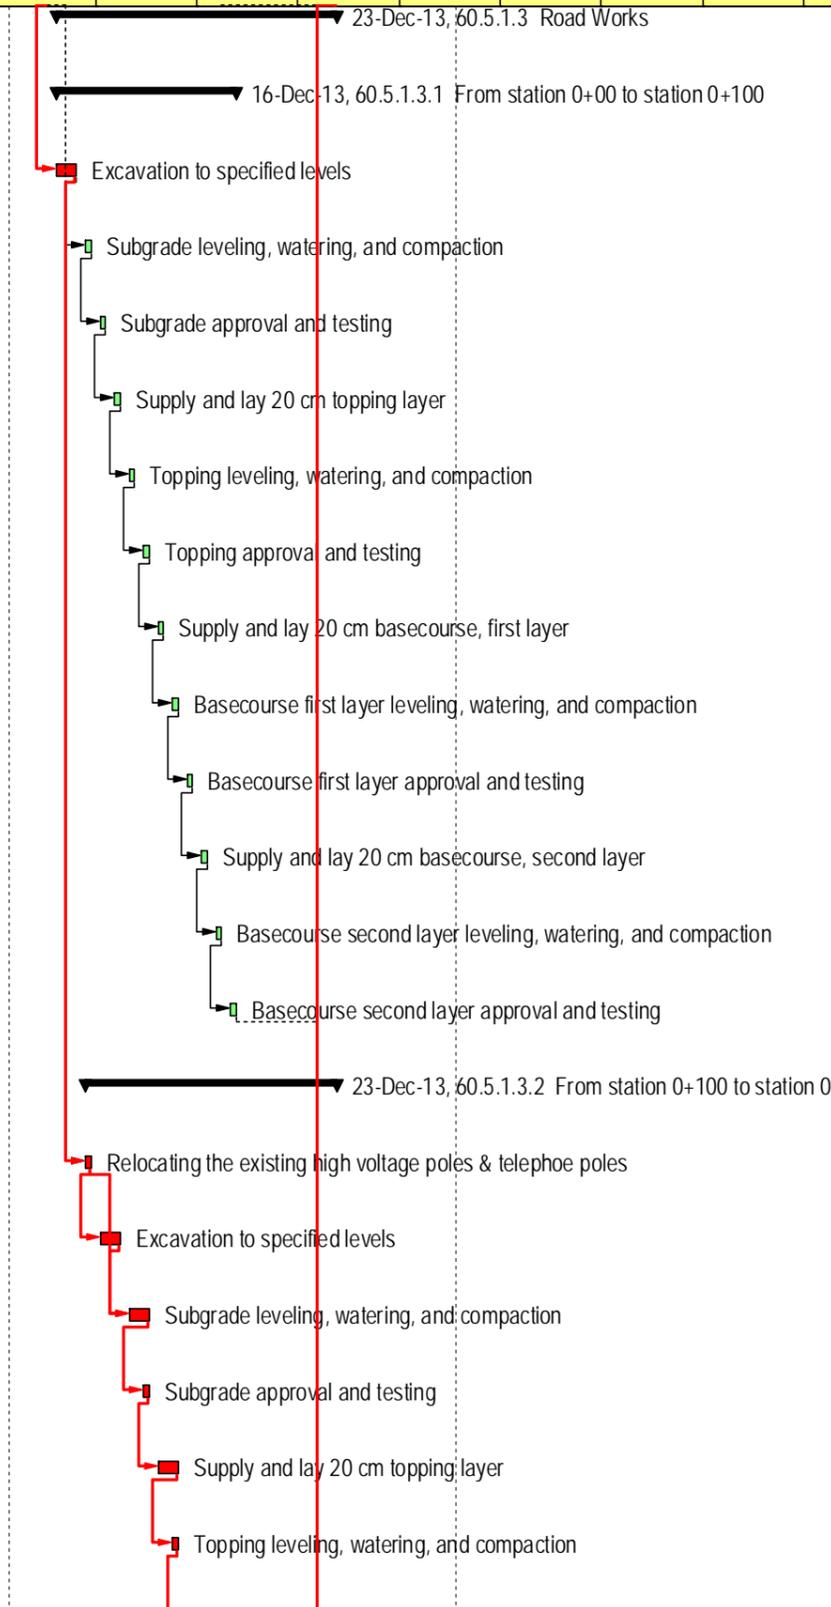

█ Actual Work    █ Critical Remaining Work    ▾ Summary  
█ Remaining Work    ◆ Milestone

Saqqa and Khoudary General Contracting							60-Day Plan of Operation							Biddu Beit Anan Road Project													
Activity ID	Activity Name	Original Duration	Start	Finish	Free Float	Total Float	October 2013			November 2013				December 2013				January 2014									
							12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25					
A1360	Topping approval and testing	1d	13-Dec-13	13-Dec-13	0d	0d																					
A1370	Supply and lay 20 cm basecourse, first layer	2d	14-Dec-13	15-Dec-13	0d	0d																					
A1380	Basecourse first layer leveling, watering, and compaction	1d	16-Dec-13	16-Dec-13	0d	0d																					
A1390	Basecourse first layer approval and testing	1d	17-Dec-13	17-Dec-13	0d	0d																					
A1400	Supply, build and casting backing of curbstone	2d	18-Dec-13	19-Dec-13	0d	0d																					
A1410	Supply and lay 20 cm basecourse, Second layer	2d	20-Dec-13	21-Dec-13	0d	0d																					
A1420	Basecourse second layer leveling, watering, and compaction	1d	22-Dec-13	22-Dec-13	0d	0d																					
A1430	Basecourse second layer approval and testing	1d	23-Dec-13	23-Dec-13	0d	0d																					
A1440	Supply and lay 15 cm basecourse for sidewalks	1d	20-Dec-13	20-Dec-13	0d	0d																					
A1450	Leveling, watering, and compaction of basecourse for sidewalks	1d	21-Dec-13	21-Dec-13	0d	0d																					
A1460	Approval and testing of basecourse for sidewalks	1d	22-Dec-13	22-Dec-13	0d	0d																					
A1466	Construct 10cm-concrete Side walk & Ramps	1d	23-Dec-13	23-Dec-13	0d	0d																					
A1470	Completion of 60-day schedule	0d		23-Dec-13	0d	0d																					

█ Actual Work   
 █ Critical Remaining Work   
 ▼ Summary  
█ Remaining Work   
 ◆ Milestone

# Progress S-Curve Versus Actual

S – Curve will be available upon the final revision of CPM Schedule completed

# Site Memos Log

# Inspection Requests Log

**Inspection Requests Log:**

<b>S. No.</b>	<b>Description</b>	<b>Submitting Date</b>
IR-13-09-001-A	Installing of Two Project Signs	November 25, 2013

# Submittals Log

**Submittals Log:**

No.	Submittal Code	Submit Date	Description	Approval Responsibility	Status	Date of CMC Response
1	SUB-13-09-001A	Nov.03, 2013	Project's Insurances	USAID	E	Nov. 21,2013
2	SUB-13-09-002A	Nov.03, 2013	Cell Phones and Simcards	Black & Veatch	E	Nov. 24, 2013
3	SUB-13-09-003A	Nov.03, 2013	Submittal Schedule	Black & Veatch	C	Nov. 24, 2013
4	SUB-13-09-004A	Nov.05, 2013	30 Day Schedule	Black & Veatch	A	Nov. 10, 2013
5	SUB-13-09-005A	Nov.03, 2013	Project Key Staff	USAID	C	Nov. 10,2013
6	SUB-13-09-006A	Nov.05, 2013	Qualification of Testing Labs	Black & Veatch	B	Nov. 12, 2013
7	SUB-13-09-007A	Nov.10, 2013	Subcontractors Approval	Black & Veatch	C	Nov. 11, 2013
8	SUB-13-09-008A	Nov.17, 2013	Computer System	Black & Veatch	B	Nov. 19, 2013
9	SUB-13-09-009A	Nov.17, 2013	Layout of Engineers Field Office	Black & Veatch	B	Nov. 18, 2013
11	SUB-13-09-0010A	Nov.17, 2013	60 Day Plan of Operation	Black & Veatch	B	Nov. 20, 2013
11	SUB-13-09-0011A	Nov.17, 2013	Excavation Method Statement	Black & Veatch	E	Nov. 19, 2013
12	SUB-13-09-0012A	Nov.17, 2013	Primary Field Office Furniture	Black & Veatch	B	Nov. 18, 2013
13	SUB-13-09-0013A	Nov.17, 2013	Dilapidation Survey	Black & Veatch	B	Nov. 20, 2013
14	SUB-13-09-0014A	Nov.20, 2013	Project Sign Location	Black & Veatch	B	Nov. 25, 2013
15	SUB-13-09-0015A	Nov.20, 2013	Critical Path Method Schedule	Black & Veatch	C	Nov. 24, 2013
16	SUB-13-09-0016A	Nov.24, 2013	Safety Plan	Black & Veatch	C	Nov. 26, 2013
17	SUB-13-09-0017A	Nov.24, 2013	Quality Control Plan	Black & Veatch		Not Yet
18	SUB-13-09-0018A	Nov.24, 2013	Environmental Mitigation Plan	Black & Veatch	B	Nov. 27, 2013
19	SUB-13-09-0019A	Nov.28, 2013	Shop Drawings Road Works (0+000 to 0+600)	Black & Veatch		Not Yet

20	SUB-13-09-0020A	Nov.25, 2013	Temporary Project Sign Details	Black & Veatch	B	Nov. 25, 2013
21	SUB-13-09-0021A	Nov.26, 2013	Digital Cameras Details	Black & Veatch	B	Nov. 26, 2013
22	SUB-13-09-0022A	Nov.26, 2013	Traffic Control Plan	Black & Veatch		Not Yet
23	SUB-13-09-0023A	Nov.28, 2013	General Method Statement	Black & Veatch		Not Yet
24	SUB-13-09-0024A	Nov.28, 2013	Concrete Job Mix	Black & Veatch		Not Yet
<p>A= No Exception Noted, B=Make Correction Noted, C=Amend – Resubmit, D=Reject – Resubmit, E=Review Not Required.</p>						

# Request For Information Log

# Geo-MIS Data

**USAID WEST BANK/ GAZA**  
**LOCAL CONTRACTOR PROGRAM**  
**CONTRACT NO. : AID-294-1-13-00002**  
**TASK ORDER NO. : AID-294-13-00009**  
**TASK ORDER SHORT NAME: BDU**  
**TEMPORARY JOB DAYS REPORT**

Task Order Name: BDU  
 Sub-project or Activity Name: BDU  
 CONTRACTOR: Saqq and Khudary Co.  
 SUBCONTRACTOR(s): NA

DATE	Site Staff Job Days **													Man-days*				
	Worker/Classification (Hours)												Total Management	Total Engineers	Total Skilled	Total Unskilled	Total Other	
	Management			Engineers		Skilled labor			Unskilled labor		Other							
	Project Manager	Quality Control Manager	Safety & Envi. Manager	Site Engineer	Office Engineer	Foreman	Skilled Labor	Equipment Operator	Flagman	Unskilled Labor								
October 1, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 2, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 3, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 4, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 5, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 6, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 7, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 8, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 9, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 10, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 11, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 12, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 13, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 14, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 15, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 16, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 17, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 18, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 19, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 20, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 21, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 22, 2013	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	0	0	0	0	0	
October 23, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
October 24, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
October 25, 2013	0	0	0	0	0	0	0	0	0	12	0	0	0	0	0	1.5	0	
October 26, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
October 27, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
October 28, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
October 29, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
October 30, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
October 31, 2013	8	8	8	0	0	0	0	0	0	0	0	0	3	0	0	0	0	
<b>Total of Month</b>													<b>24</b>	<b>0</b>	<b>0</b>	<b>1.5</b>	<b>0</b>	

\* Total Man-days = Total Hours / 8

\*\* This data collection sheet is for Local (CCN) staff only, expatriate and third country national employee shall not be included.

**USAID WEST BANK/ GAZA**  
**LOCAL CONTRACTOR PROGRAM**  
**CONTRACT NO. : AID-294-1-13-00002**  
**TASK ORDER NO. : AID-294-13-00009**  
**TASK ORDER SHORT NAME: BDU**  
**TEMPORARY JOB DAYS REPORT**

Task Order Name: BDU  
 Sub-project or Activity Name: BDU  
 CONTRACTOR: Saqq and Khudary Co.  
 SUBCONTRACTOR(s): NA

DATE	Site Staff Job Days **																	
	Worker/Classification (Hours)											Man-days*						
	Management			Engineers		Skilled labor			Unskilled labor		Other		Total Management	Total Engineers	Total Skilled	Total Unskilled	Total Other	
	Project Manager	Quality Control Manager	Safety & Envi. Manager	Site Engineer	Office Engineer	Foreman	Skilled Labor	Equipment Operator	Flagman	Unskilled Labor	Surveyor	Drivers						
November 1, 2013	0	0	0	0	0	0	0	0	0	8	0	0	0	0	0	0	1	0
November 2, 2013	8	8	8	0	0	0	0	0	0	0	8	0	3	0	0	0	0	1
November 3, 2013	8	8	8	0	0	0	0	0	0	0	8	0	3	0	0	0	0	1
November 4, 2013	8	8	8	0	0	0	0	0	0	0	8	0	3	0	0	0	0	1
November 5, 2013	8	8	8	0	0	0	0	0	0	0	8	0	3	0	0	0	0	1
November 6, 2013	8	8	8	0	0	0	0	0	0	0	8	0	3	0	0	0	0	1
November 7, 2013	8	8	8	0	0	0	0	0	0	0	8	0	3	0	0	0	0	1
November 8, 2013	0	0	0	0	0	0	0	0	0	12	0	0	0	0	0	0	1.5	0
November 9, 2013	8	8	8	0	0	0	0	0	0	0	8	0	3	0	0	0	0	1
November 10, 2013	8	8	8	0	8	0	0	0	0	0	8	0	3	1	0	0	0	1
November 11, 2013	8	8	8	0	8	0	0	0	0	0	8	0	3	1	0	0	0	1
November 12, 2013	8	8	8	0	8	0	0	0	0	0	8	0	3	1	0	0	0	1
November 13, 2013	8	8	8	0	8	0	0	0	0	0	8	0	3	1	0	0	0	1
November 14, 2013	8	8	8	0	16	0	0	0	0	12	8	0	3	2	0	1.5	1	
November 15, 2013	0	0	0	0	0	0	0	0	0	12	0	0	0	0	0	1.5	0	
November 16, 2013	8	8	8	0	8	0	0	0	0	0	8	0	3	1	0	0	0	1
November 17, 2013	8	8	8	0	16	0	0	0	0	0	8	0	3	2	0	0	0	1
November 18, 2013	8	8	8	0	8	0	0	0	0	0	8	0	3	1	0	0	0	1
November 19, 2013	8	8	8	0	16	0	0	0	0	0	8	0	3	2	0	0	0	1
November 20, 2013	8	8	8	0	16	0	0	0	0	8	8	0	3	2	0	1	1	
November 21, 2013	8	8	8	0	16	0	0	0	0	8	8	0	3	2	0	1	1	
November 22, 2013	0	0	0	0	0	0	0	0	0	8	0	0	0	0	0	1	0	
November 23, 2013	8	8	8	0	16	0	0	0	0	8	8	0	3	2	0	1	1	
November 24, 2013	8	8	8	0	8	0	0	0	0	8	8	0	3	1	0	1	1	
November 25, 2013	8	8	8	0	8	0	12	0	0	8	8	12	3	1	1.5	1	2.5	
November 26, 2013	8	8	8	0	8	0	0	0	0	8	8	0	3	1	0	1	1	
November 27, 2013	8	8	8	0	8	0	0	0	0	8	8	0	3	1	0	1	1	
November 28, 2013	8	8	8	0	8	0	0	0	0	8	8	0	3	1	0	1	1	
November 29, 2013	0	0	0	0	0	0	0	0	0	8	0	0	0	0	0	1	0	
November 30, 2013	8	8	8	0	8	0	0	0	0	8	8	0	3	1	0	1	1	
<b>Total of Month</b>													<b>75</b>	<b>24</b>	<b>1.5</b>	<b>16.5</b>	<b>26.5</b>	

\* Total Man-days = Total Hours / 8

\*\* This data collection sheet is for Local (CCN) staff only, expatriate and third country national employee shall not be included.

\*\*\*

**USAID WEST BANK/ GAZA**  
**LOCAL CONTRACTOR PROGRAM**  
**CONTRACT NO. AID-294-I-13-00002**  
**TASK ORDER NO. AID-294-13-00009**  
**TASK ORDER SHORT NAME: BDU**  
**Temporay Job Days Summary Report**

Task Order Name: BDU

PERIOD FROM: October 23,2013

Sub-project or Activity Name:BDU

PERIOD TO:November 30,2013

CONTRACTOR: Saqqa and Khudary Co.Ltd

Date		Site Staff Job Days**					Total Job Days	No of Full Time Equivalent (FTE) Jobs in the Month*	Notes of Comments
Month	Year	Management	Engineers	Skilled Labor	Unskilled Labor	Other			
October	2013	24.0			1.5		26	1	
November	2013	75.0	24.0	1.5	16.5	26.5	144	6	
December	2013						0	0	
January	2014						0	0	
February	2014						0	0	
March	2014						0	0	
April	2014						0	0	
May	2014						0	0	
June	2014						0	0	
July	2014						0	0	
August	2014						0	0	
September	2014						0	0	
<b>Total of FY 2014</b>							<b>169</b>	<b>7.100840336</b>	
October	2014						0	0	
November	2014						0	0	
December	2014						0	0	
January	2015						0	0	
February	2015						0	0	
March	2015						0	0	
April	2015						0	0	
May	2015						0	0	
June	2015						0	0	
July	2015						0	0	
August	2015						0	0	
September	2015						0	0	
<b>Total of FY 2015</b>							<b>0</b>	<b>0</b>	

Note :

\* No of Full Time Equivalent (FTE) Jobs in the Month = Total Job Days / Avg. Days in the Month(23.8)

\*\* This data collection sheet is for Palestinian staff only , experts and foreign employee shall not be included.
