



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

## MONTHLY PROGRESS REPORT

TASK ORDER NO. 13-00012

Multiple Roads in the South Area (MRSII)

APCO/ArCon

March, 2015





# MONTHLY TASK ORDER PROGRESS REPORT

## INFRASTRUCTURE NEEDS PROGRAM

Contract No. 294-I-00-12-00005

Task Order No. AID-294-TO-13-00012

**From Mar. 01, 2015 to Mar. 25, 2015**

### **DISCLAIMER**

"This report is made possible by the support of the American People through the United States Agency for International Development (USAID). The contents of this report are the sole responsibility of APCO/ArCon and do not necessarily reflect the views of USAID or the United States Government."



# USAID | WEST BANK/GAZA

**USAID Contract No.:** \_\_\_\_\_ 294-I-00-12-00005 \_\_\_\_\_  
**TO No.:** \_\_\_\_\_ 13-00012 \_\_\_\_\_  
**Contractor:** \_\_\_\_\_ APCO/ArCon Construction and Services \_\_\_\_\_  
**T.O Key Personnel (shared among 3 Projects):** Eng. Rashid Saed- T.O.M  
 Eng. Zuhair Ghayadah- QCM  
 Mr. Abdullah Hasheem-S.E.O starting Jan. 14,15  
 Eng. Radwan Taha - Surveyor  
 Eng. Romel Shalaldeh – PE 01  
 Eng. Murad Eghrayieb – PE 02  
**Project Engineers** Eng. Saed Abu Rayyan – PE 03

Monthly Progress  
Report number 17

## TABLE OF CONTENTS


Task Order Overview.....	2-4
Safety .....	5
Environmental Compliance.....	5
Traffic Control Measures.....	5
Community Outreach and Gender Consideration.....	5
Coordination .....	5
Site Visitors.....	5-6
Material or Equipment Delivered to Site.....	6
Progress and Scheduling.....	6
Activities during this Reporting Period.....	6-7
Indicator No. 01- Number of kilometers of transportation infrastructure constructed or repaired through USG assistance	7
Working / Non-working Days.....	7-8
Indicator No. 02- Generated Person-Days of Employment.....	8-9
Site Memos.....	9
Procurement.....	9
Inspection requests.....	9
Quality Control and Test Results.....	10-11
Submittals .....	12
RFIs.....	12
Transmittals.....	12-14
Payments.....	14
Variation Order .....	14-15
Variation Order Requests.....	15-17
Obstacles and Challenges.....	17
Progress Photos.....	18-25
Annexes	
A Materials- Equipment Receiving Log.....	26-30
B Detailed As Built Time Schedule for the Project.....	31-65
C Progress S-Curve versus Actual.....	66-70
D Site Memos Log.....	71-79
E Inspection Requests Log.....	80-137
F Submittals Log for the Reporting Period.....	138-203
G RFI's Log for the Reporting Period.....	204-206
H Geo-MIS Data Collection Sheet.....	207-215
Generated Person-Days of Employment	
I Risk Register Log.....	216-218



# USAID | WEST BANK/GAZA

## TASK ORDER OVERVIEW

Task Order Project Name	Multiple Roads Project in the South area (MRSII)
Contract No.	294-I-00-12-00005
Task Order No.	AID-294-TO-13-00012
Employer	USAID
Contractor	APCO/ArCon
Engineer / CMC	Black and Veatch
Notice of Award (NOA)	Sep. 19, 2013
Notice To Proceed (NTP)	Nov. 01, 2013
Task Order Completion Date	Oct. 31, 2014
Modified Completion Date	Mar. 19, 2015 (Per VO#14)
Task Order Contract Value	\$12,259,300
Projects Total Value	\$11,759,300
Day Work	\$500,000.00
Modified Projects Total Value	\$12,135,877.09 (Per VO#15)
Modified Day Work	\$123,422.91 (Per VO#15)

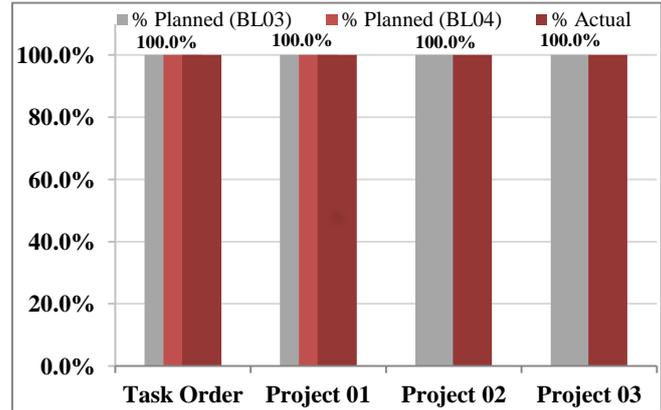

### Project 01- Dura- Hebron (Sinjer) Road

**Project Description** A busy 3.7 km 2 lane regional road connecting Dura to Hebron and surrounding localities spanning Areas A and B, and passing through a densely populated area with commercial and light industrial activities on both sides. The construction activities included the followings:

- Construction of a total of 3,732 l.m. of Dura – Hebron (Sinjer) Road.
- Construction of a total of 184 l.m. of Ma’sarah Road.
- Construction of a total of 890.5 l.m. of simple access roads.
- Milling and overlay of a total of 864.4 l.m. of Dura main road.
- Installation of a total of 3,053.08 l.m. of 6” water pipeline.
- Installation of a total of 1,124.39 l.m. of 4” water pipeline.
- Installation of a total of 7,982.17 l.m. of 2” water pipeline.
- Installation of a total of 1,658.91 l.m. of 3/4” water pipeline.
- Installation of a total of 309.53 l.m. of Ø100cm storm water pipeline.
- Installation of a total of 228.46 l.m. of Ø80cm storm water pipeline.
- Installation of a total of 1,311 l.m. of Ø60cm storm water pipeline.
- Installation of a total of 96 of street lighting poles.

**Statement of Work (SOW)** The SOW consists of excavation works, embankment filling, pavement layer construction, construction of retaining structures, installation and/or rehabilitation of storm water drainage systems, installation of new water lines, milling and overlay, installation of safety features (signage, lighting poles, road marking, cat eyes, and guardrails) and any other work items needed to complete this activity as specified.

Project Location	Dura and Hebron, Hebron District (Area A and B)
Project Value	\$8,243,912
Modified Project Value	\$8,090,019.07 (Per VO#15)
Subcontractor Name	Technical Group Company
Start of Construction	January 15, 2014
Contractual period of Performance	365 Calendar days
Contractual End Date	Oct. 31, 2014
Modified period of Performance	504 Calendar days (Per VO#14)
Modified End Date	Mar. 19, 2015 (Per VO#14)
Actual Completion Date	Mar. 19, 2015
Construction Site Handover	March 25, 2015
Final Acceptance Certificate	March 19, 2015





# USAID | WEST BANK/GAZA

## Project 02- Samu'- Yatta Road

### Project Description

Comprised of 2 separate segments, segment A of 4.718km 2 lane main road connecting Samu' and Yatta communities passing through unpopulated agricultural lands located in areas A and C. Segment B totally located in Area C, 438 meter serving as Samu' entrance and connecting to HWY 60.

Day work amount was utilized to extend the project scope and perform additional works including:

- Pavement of parking area.
- Installation of 4" steel water pipeline QTY 1,750 l.m.
- Installation of 3" steel water pipeline QTY 746 l.m.
- Installation of 2" Galvanized water pipe QTY 109.6 l.m.
- Installation of double 6" UPVC crossing for future water connections to pipeline.
- Construction of Stone Boulder
- Milling and overlay of 400 l.m road segment towards Samu' town and 130 l.m of road linking between Yatta main hospital and the center of Yatta city.

### Statement of Work (SOW)

The SOW consists of excavation works, embankment filling, pavement layer construction, construction of retaining structures and boulders, installation and/or rehabilitation of storm water drainage systems, water pipeline installation, milling and overlay, installation of safety features (signage, road marking, cat eyes, and guardrails) and any other work items needed to complete this activity as specified.

### Project Location

Yatta and Samu' cities, Hebron District (Area A and C)

### Project Value

\$2,240,867

### Modified Project Value

\$2,760,036.30 (Per VO#09)

### Subcontractor Name

Al Fakher Company

### Start of Construction

Jan. 19, 2014

### Contractual period of Performance

270 Calendar Days

### Contractual End Date

July 28, 2014

### Modified period of Performance

332 Calendar Days (per VO#06)

### Modified End Date

September 28, 2014 (per VO#06)

### Construction Site Handover

September 25, 2014

### Final Acceptance Certificate


September 28, 2014

### Planned Percentage of Completion

100%

### Actual Percentage of Completion

100%

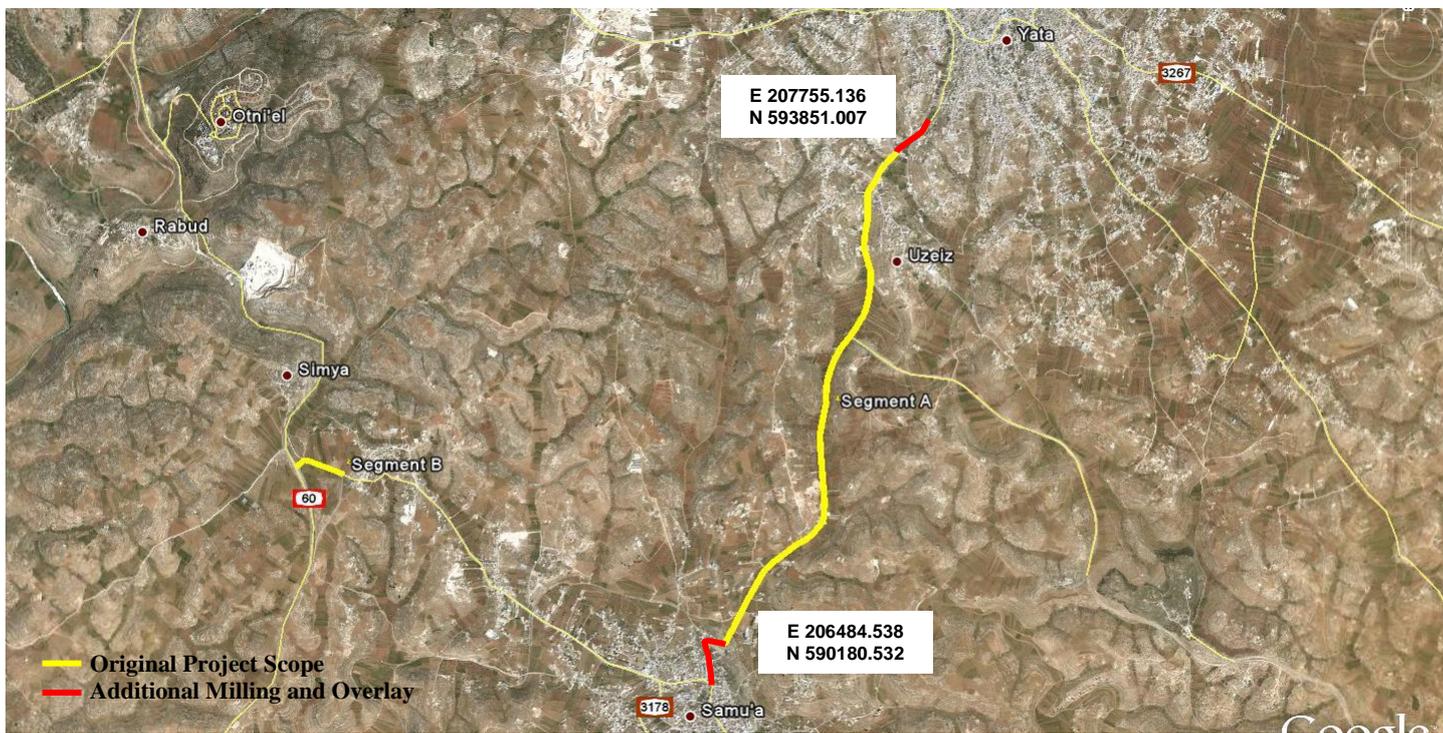




# USAID | WEST BANK/GAZA

## Project 03- Milling and Overlay of Bethlehem Internal Roads

Project Description	<p>Upgrading approximately 4.08km of Bethlehem internal roads sited in Area A which is a densely populated neighborhood in Bethlehem. The following roads were upgraded:</p> <ol style="list-style-type: none"> <li>1- Milling and Overlay of 288.00 of Wadi Shaheen Road. 288.00 lm</li> <li>2- Milling and Overlay of 1,170.20 LM of Wadi Ma'ali Road. 1,170.20 lm</li> <li>3- Milling and Overlay of 229.20 LM of Al-Dibs Road. 229.20 lm</li> <li>4- Milling and Overlay of 135.00 LM of Al Shepherd Road. 135.00 lm</li> <li>5- Reconstructing of 210.00 LM of Al-Qet'ah Road. 210.00 lm</li> <li>6- Milling and Overlay of 240.40 LM of .Al-Attan &amp; WSSA Intersection. 240.40 lm</li> <li>7- Milling and Overlay of 1,152.77 LHS and 1,111.20 LM RHS of Hebron-Jerusalem Road. 1,152.77 lm</li> <li>8- Milling and Overlay of 233.25 LM of Festival Yard at Al Sha'eb Road. 233.25 lm</li> <li>9- Milling and Overlay of 280.70 LM of Karkafa Road. 280.70 lm</li> <li>10- Milling and Overlay of 143.75 LM of Philips Road. 143.75 lm</li> </ol>
Statement of Work (SOW)	<p>The SOW consists of the milling of the existing asphalt layer and the overlay of a fresh asphalt layer. Work also includes excavation works, patching works, reconstruction works, construction of sidewalks, rehabilitation of existing sidewalks, installation of safety features (signage, road marking, cat eyes, and guardrails) and any other work items needed to complete this project as specified.</p>
Project Location	Bethlehem, Bethlehem Governorate (Area A)
Project Value	\$1,274,521
Modified Project Value	\$1,285,821.72 (Per VO#04)
Subcontractor Name	Al Tarifi Company
Start of Construction	Nov. 02, 2013.
Contractual period of Performance	180 Calendar Days
Contractual End Date	Apr. 29, 2014
Modified period of Performance	187 Calendar Days (Per VO#03)
Modified End Date	May 06, 2014 (Per VO#03)
Actual Completion Date	May 05, 2014
Final Acceptance Certificate	May 06, 2014
Planned Percentage of Completion	100%
Actual Percentage of Completion	100%

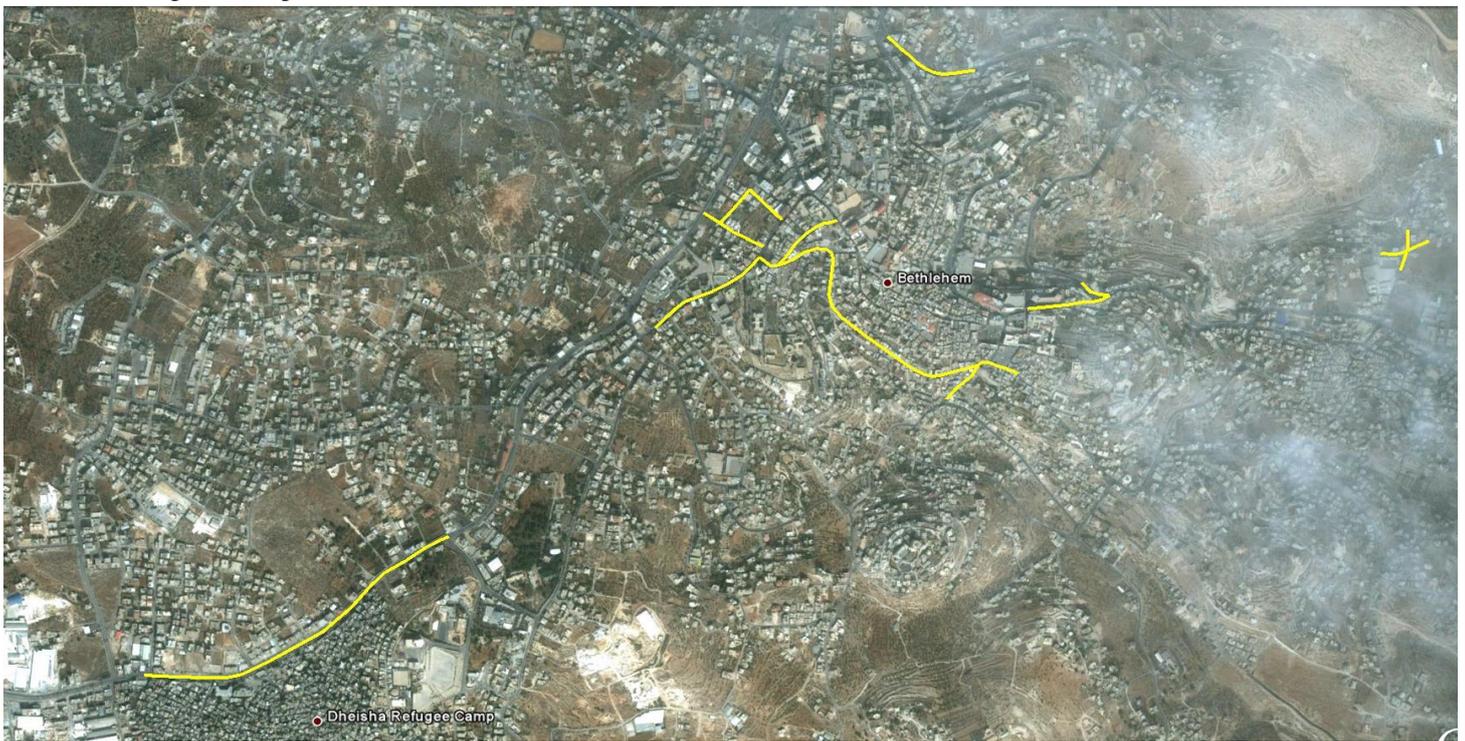



# USAID | WEST BANK/GAZA

## SAFETY:

During this reporting period, no accidents were reported, and zero Notices of Unsafe Condition (NUC) were issued.

## ENVIRONMENTAL COMPLIANCE:

Environmental mitigation plan addressing the responsive actions to special conditions was submitted to the CMC. Approval received on Jan. 02, 2014. Environmental mitigation plan measures (dust control, public safety, dumping of materials, olive trees relocation and other measures) were implemented during this reporting period. One environmental checklist (ECL) was received from BV on Mar. 24, 2015 for the month of February highlighting two site-specific concerns: 1) Backfilling behind gravity walls and 2) Adjacent Lands restoration (stockpiling areas). APCO/ArCon adhered to mentioned notes and closed all pending ECLs.

## TRAFFIC CONTROL MEASURES:

Detailed traffic control plans for Projects 01, 02 and 03 (located in Areas A and B) were approved and stamped by the Traffic Higher Council at the Palestinian Ministry of Transport, copies of stamped plans were submitted to CMC and approved.

APCO/ArCon coordinated with concerned local police department / local municipalities during the implementation of traffic control plans for detours located in area A and B, copies of approved traffic plans were handed to the local councils and police, and APCO/ArCon received stamped copies from the concerned local councils. On site traffic control measures were implemented and inspected by CMC in road segments where construction works started.

## COMMUNITY OUTREACH, PUBLIC INFORMATION AND GENDER CONSIDERATION:

Coordination meetings with community, local councils and utility owners were conducted during this reporting period as detailed below coordination log.

## COORDINATION:

During this reporting period, the following coordinations and meetings occurred :

Date	Attendees	Subject	Description
<b>Project 01 - DUR</b>			
March 19, 2015	Black & Veatch- Ahmad Hreibat. APCO- Rashid Al-Said. TGC- Mohammad Fairs.	Coordination Meeting	Discuss homeowner's objections on asphalt wearing layer from St. 2+380 to St. 2+480. Issue resolved.
March 19, 2015	USAID- Ms. Sonia Massis. Dura Municipality- Salah Rabai. APCO- Rashid Al-Said.	Coordination Meeting	Discuss final preparation for Dura project handover.

## SITE VISITORS:

Date	Company	Location	Description
March 05, 2015	USAID- Eng. Sonia Massis.	Project 01-DUR	Site visit to follow-up work progress, quality and safety.
March 10, 2015	USAID- Eng. Sonia Massis.	Project 01-DUR	Site visit to follow-up work progress, quality and safety.
March 19, 2015	USAID- Eng. Sonia Massis.	Project 01-DUR	Site visit to follow-up work progress, quality and safety.
March 25, 2015	USAID- Eng. Sonia Massis & Mr. Peter Riley. Dura municipality -Mohammad Sameer Al-Nammora, Salah Rabai, Maher Awawdeh MoPWH- Fa'ek Al Deik, Afeef Al Saed, Ali Thwaib, Khaled Hnehn, Musa Khaled, Hana' Shaheen and Mohammad Adawi. Interior Ministry, Police & Security- Ala' Al Tamimi.	Project 01-DUR	Project final walkthrough and handover.



# USAID | WEST BANK/GAZA


## MATERIAL OR EQUIPMENT DELIVERED TO SITE:

Please refer to **Annex A-** Equipment and Material receiving log.

## PROGRESS and SCHEDULING:

### % of Completion:

- Project 01- Excavation	100%
- Project 01- Base course	100%
- Project 01- Steel Pipeline	100%
- Project 01- Concrete Pipe	100%
- Project 01- Concrete Works	100%
- Project 01- Curbstone	100%
- Project 01- Asphalt Works	100%
- Project 02- Excavation	100%
- Project 02- Topping layer	100%
- Project 02- Base course	100%
- Project 02- Concrete Works	100%
- Project 02- Concrete Pipe	100%
- Project 02- Steel Pipeline	100%
- Project 02- Asphalt Works	100%
- Project 03- Excavation	100%
- Project 03- Base course	100%
- Project 03- Milling	100%
- Project 03- Asphalt wearing	100%
- Project 03- Curbstone	100%
- Project 03- Concrete works	100%
- Project 03- Interlock Block	100%

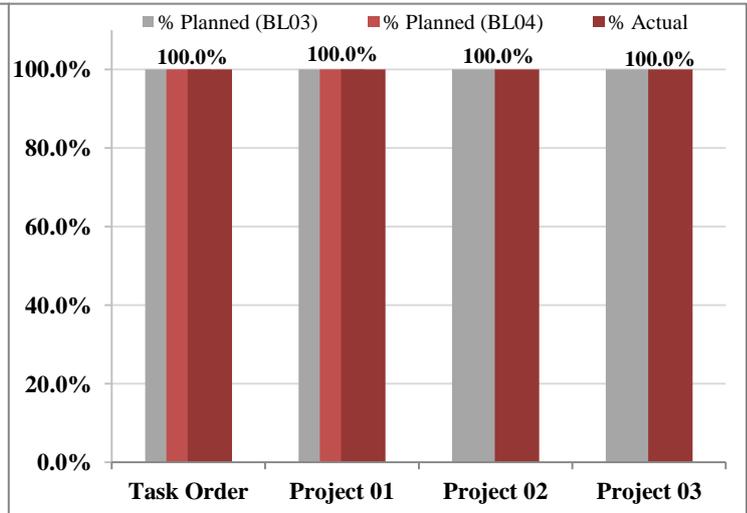

Overall percentages of completion are :

<u>Completion%</u>	<u>T.O</u>	<u>P 01</u>	<u>P 02</u>	<u>P 03</u>
<u>Planned BL3</u>	100%	100%	100%	100%
<u>Planned BL4</u>	100%	100%		
<u>Actual %</u>	100%	100%	100%	100%

Refer to **Appendix C** Progress s-curve planned versus Actual.

## ACTIVITIES DURING THIS REPORTING PERIOD:

### Project 01

- Continue and complete washout chamber works at St. 3+380 and house connections (Finishing testing and disinfection).
- Finish works for storm water outfall at St. 1+300, St. 2+300, St.3+000 and St 3+230.
- Continue and finish paving asphalt works for simple access from St. 1+700 to St. 3+700.
- Complete and finish retaining wall construction from St. 1+775 to St. 1+785 LHS.
- Complete installation works for street lighting from St. 3+200 to St. 3+700.
- Continue and finish works in curbstone and sidewalks from St. 3+400 to St. 3+660.
- Continue and finish base course 2<sup>nd</sup> layer from St. 3+480 to St. 3+700.
- Continue and finish handrail installation from St. 0+000 to St. 3+700.
- Continue and finish asphalt binder layer works from St. 3+480 to St. 3+700.
- Continue and finish asphalt wearing layer from St. 1+600 to St. 3+700.
- Continue and finish landscaping works at intersection at St. 0+320 RHS.
- Continue and finish parapet wall works from St. 3+000 to St. 3+230 and from St. 3+290 to St. 3+309 LHS.
- Start and finish road marking works from St 0+000 to St 3+700.
- Continue and finish installation of traffic signs from St. 0+000 to St. 3+700.
- Continue and finish works on punch list items.
- Install all road furniture.
- Handover the project.

Project was completed on time and handed over to USAID and MOPWH on March 25, 2015.



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

## Project 02

- Project was completed and handed over to USAID and MOPWH on September 25, 2014.

## Project 03

- Project was completed and handed over to USAID and MOPWH on May 05, 2014.

Refer to **Appendix B** for detailed as built time schedule for each project.

### INDICATOR NO. 01- Number of kilometers of transportation infrastructure constructed or repaired through USG assistance:

<b>Project 01-</b>	
Total Road reconstruction (100% Completed)	4.807 Km
Additional Milling and Overlay	0.891 Km
Target value	4.100 Km
Number of kilometers constructed or repaired through end of this reporting period=	<b>5.698 Km</b>
<b>Project 02-</b>	
Total Road reconstruction (100% Completed)	4.392 Km
Additional Milling and Overlay	0.764 Km
Target value	4.520 Km
Number of kilometers constructed or repaired through end of this reporting period=	<b>5.156 Km</b>
<b>Project 03-</b>	
Total Road rehabilitated (100% Completed)	4.083 Km
Target value	2.800 Km
Number of kilometers constructed or repaired through end of this reporting period.	<b>4.083Km</b>

### WORKING / NON-WORKING DAYS

#### Project 01-DUR

1	Total Period of Performance (Original)	365
2	Total Excusable delays/approved extensions	139
3	Modified Period of Performance	504
4	Modified Completion Date	March 19, 2015
5	No. of Working Days during this reporting Period	16
6	Accumulated Working Days	396
7	Total No. of non-working days (Holidays and weekends) during this reporting Period	2
8	Accumulated non-working days (Holidays and weekends)	82
9	No. of other non-working days during this month**	1
10	Accumulated other non-working days	26

\*\* work stopped due to rainy weather

#### Project 02-SAM

1	Total Period of Performance (Original)	270
2	Total Excusable delays/approved extensions	62
3	Modified Period of Performance	332
4	Modified Completion Date	September 28, 2014
5	No. of Working Days during this reporting Period	0
6	Accumulated Working Days	268
7	Total No. of non-working days (Holidays and weekends) during this reporting Period	0
8	Accumulated non-working days (Holidays and weekends)	53



# USAID | WEST BANK/GAZA

9	No. of other non-working days during this month**	0
10	Accumulated other non-working days	11

## Project 03-BTH

1	Total Period of Performance (Original)	180
2	Total Excusable delays/approved extensions	7
3	Modified Period of Performance	187
4	Modified Completion Date	May 06, 2014
5	No. of Working Days during this reporting Period	0
6	Accumulated Working Days	151
7	Total No. of non-working days (Holidays and weekends) during this reporting Period	0
8	Accumulated non-working days (Holidays and weekends)	28
9	No. of other non-working days during this month**	0
10	Accumulated other non-working days	8

## INDICATOR NO. 2: GENERATED PERSON-DAYS OF EMPLOYMENT:

(Note: numbers are rounded to the nearest integer number - man-day)

All reported materials are up to date and meet the five quality data standards (Clause H.9).

This indicator count only local Palestinian staff whose time is charged to the USAID activity (the Contractor at the “prime” and “first tier” subcontractor level only). Neither expatriate person days of employment (i.e. those worked by American or other Third Country National staff) nor management nor administrative person days of employment (i.e. program level and other general and administrative staff shared among multiple task orders) are included. All reported person-days are calculated based on the approved Daily Joint Reports.

Total Job Days (Male and Female)	No. of Full Time Equivalent (FTE) Jobs = (Total Job Days / 23.8)
Generated previously = 33,741.2 Man-days	Generated previously = 1,417.7
During this reporting period = 2,000.2 Man-days	During this reporting period = 84
Total generated to-date = 35,741.4 Man-days	Total generated to-date = 1,501.7 (rounded to nearest FTE)
Female Employment	
Generated Previously = 494.9 Man-days	Generated previously = 20.8 ≈ 21
During this reporting period = 26.8 Man-days	During this reporting period = 1.1 ≈ 1
Total generated to-date = <b>521.6</b> Man-days	Total generated to-date = 21.9 ≈ 22 (rounded to nearest FTE)

## Task Order

- Target value= **31,369** Man-Days
- Employment generated previously = 33,741.2 ≈ 33,741 Man-Days (per CMC audit up to Oct. 31, 2014)
- Employment generated this month = 2,000.2 ≈ 2,000 Man-Days
- Total cumulative employment generated (Male and Female) to-date= 35,741.4 ≈ 35,741 Man-Days
- Total cumulative female employment generated previously = 494.9 ≈ 495 Man-Days
- Total cumulative female employment generated this month= 26.8 Man-Days
- Total cumulative female employment to-date= **521.6** ≈ **522** Man-Days



# USAID | WEST BANK/GAZA

## Project 1:

- Target value= **21,063** Man-Days
- Employment generated previously = 21,606.8≈21,607 Man-Days (per CMC audit up to Oct. 31, 2014)
- Employment generated this month = 2,000.2 ≈ 2,000 Man-Days
- Total cumulative employment generated to-date= **23,607** Man-Days
- Total cumulative female employment generated previously = 221.1 Man-Days
- Total cumulative female employment generated this month = 26.8 Man-Days
- Total cumulative female employment to-date= **247.9** Man-Days

## Project 2

- Target value= **7,497** Man-Days
- Employment generated previously = **8,278.1** ≈8,278 Man-Days (per CMC audit up to Oct. 31, 2014)
- Employment generated this month =0 Man-Days
- Total cumulative employment generated to-date= **8,278.1** ≈8,278 Man-Days
- Total cumulative female employment generated previously = 260.3≈ 260 Man-Days
- Total cumulative female employment generated this month = 0 Man-Days
- Total cumulative female employment to-date= **260.3**≈ 260 Man-Days

## Project 3:

- Target value= **2,809** Man-Days
- Employment generated previously = 3,856 Man-Days (per CMC audit up to July 31, 2014)
- Employment generated this month =0 Man-Days
- Total cumulative employment generated to-date= **3,856** Man-Days
- Total cumulative female employment generated previously = 14 Man-Days
- Total cumulative female employment generated this month= 0 Man-Days
- Total cumulative female employment to-date= **14** Man-Days

## SITE MEMO:

- See Appendix D Site Memos log

## PROCUREMENT:

No special procurements, all materials are within the West Bank. For details of delivered material, please refer to the attached "**Materials Receiving Log/ March 2015**"

## INSPECTION REQUEST:

Up to this reporting period **1,316** inspection requests were issued as follow:

Project No.	No. of IRs	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit
<b>P01 (DUR)</b>	932	932	0	819	3	32	78
<b>P02 (SAM)</b>	227	227	0	203	0	5	19
<b>P03 (BTH)</b>	157	157	0	132	0	0	25
<b>Total</b>	<b>1316</b>	<b>1316</b>	<b>0</b>	<b>1154</b>	<b>3</b>	<b>37</b>	<b>122</b>
<b>%</b>		<b>100%</b>	<b>0.0%</b>	<b>87.7%</b>	<b>0.2%</b>	<b>2.8%</b>	<b>9.3%</b>

Please refer to **Appendix E-** Inspection Requests log.

## Non Compliance Report Log - NCR -

No NCRs were issued during this reporting period.



# USAID | WEST BANK/GAZA

## QUALITY CONTROL AND TEST RESULTS:

Up to this reporting period **893** test reports were submitted as follow:

MRSII	No. of Tests	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review No Required
No.	893	893	0	788	50	49	4	2
%		100%	0.0%	88.2%	5.6%	5.5%	0.4%	0.2%

Tests Log summary table up to this reporting period

Material Description	Test description	Number of tests	Pass	Fail	Notes (Action taken for failed tests)
<b>Project 01- DUR</b>					
Concrete Wall	Soil Testing & Geotechnical Investigation	6	6	0	
Concrete	Compressive Strength	289	288	1	8 tests were resubmitted due to editing reports test location 1 test was resubmitted after a core test was conducted and passed.
Sub-grade	Modified Proctor Test	42	42	0	
	Field Density Test	49	49	0	2 tests were resubmitted due to lab recommendation and 1 test was resubmitted after report information editing.
	Soil classification Test	1	1	0	
	Soil Aggregate Material Test	5	5	0	
Topping	Field Density Test	1	1	0	
	Soil Aggregate Material Testing	3	3	0	
Base Course	Field Density Test	85	85	0	6 tests were resubmitted due to correcting test location and reference proctor.
	Site Comprehensive	25	24	1	Material was improved, retested and passed.
	Modified Proctor Test	16	16	0	1 test was resubmitted due to editing test location.
	Quality Assurance test	2	2	0	
Steel Bars	Site Testing Reinforcement bars	3	3	0	
Binder Layer	Bituminous Paving Mixture Testing Report	18	17	1	Retest for asphalt stiffness passed and was resubmitted.
	Prime coat	15	15	0	
	Core Test	7	6	1	1 test was resubmitted after thickness retest.
Wearing Layer	Bituminous Paving Mixture Testing Report	19	19	0	
	Tack coat	11	11	0	
	Core Test	3	3	0	
Sand material	Aggregate Test Report	2	2	0	
Bedding material & single size backfilling	Aggregate Test Report	4	4	0	
Curbstone	Pre-cast Concrete Curbstone	4	4	0	1 submittal was resubmitted due to editing report test location.
Filling material	Soil Aggregate Material Testing	1	1	0	
Cast iron covers	Testing samples	1	1	0	
Water pipeline	Disinfection Test	2	2	0	



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

Material Description	Test description	Number of tests	Pass	Fail	Notes (Action taken for failed tests)
<b>Project 02- SAM</b>					
Base Course Material	Quality Assurance Test	2	2	0	
	Site Comprehensive Test	18	18	0	
	Field Density Test	33	33	0	1 test to be resubmitted after report information editing
	Modified proctor	1	1	0	
Topping Material	Field Density Test	30	30	0	2 submittals were resubmitted due to proctor reference
Topping Material	Modified Proctor Test	2	2	0	
	Quality Assurance	1	1	0	
	Soil Aggregate Material Testing	14	14	0	
Filling Material	Field Density Test	6	6	0	1 test was resubmitted due reference proctor.
	Soil Aggregate Material Testing	4	4	0	
	Single size aggregate	1	1	0	
Sub-grade	Field Density (FD) Test	34	33	1	8 resubmitted due to reference proctor
	Modified Proctor Test	12	12	0	
	Soil Aggregate Material Testing	9	9	0	
Concrete Gravity Wall	Geotechnical Investigation Report	2	2	0	
Concrete Retaining Wall	Geotechnical Investigation Report	1	1	0	
Concrete	Concrete Compressive	10	10	0	
Asphalt	Bituminous Paving Mixture	21	21	0	4 Reports were returned (Action C) and resubmitted as the report data need to be edited and modified.
	Core Test	2	2	0	
MC Prime coat	Prime coat application rate	2	2	0	
RC Tack coat	Tack coat application rate	1	1	0	
<b>Project 03- BTH</b>					
Asphalt (Wearing Layer)	Bituminous Paving Mixture	16	16	0	
	Asphalt Core Test	6	5	1	1 resubmitted due to need for retest compaction for two points
Asphalt	Tack Coat	1	1	0	
Sub-grade	Field Density Test	11	11	0	1 submittal was resubmitted due to correcting test location
	Proctor Test	1	1	0	
	Modified Proctor Test	3	3	0	
	Soil Aggregate Material Test	2	2	0	
Base Course	Field Density Test	17	17	6	7 tests were resubmitted due to proctor reference
	Comprehensive strength	3	3	0	
	Modified Proctor Test	1	1	0	



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

**SUBMITTALS:**

- See Appendix F Submittals log for this reporting period including test submittals.

Up to this reporting period 420 submittals were submitted as the following:

MRSII	No. of SUB	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review Not required
No.	420	420	0	33	268	84	8	27
%		100%	0.0%	7.9%	63.8%	20.0%	1.9%	6.4%

**RFI:**

- See Appendix G RFI's log for this reporting period.

**TRANSMITTALS:**

**Outgoing / Incoming USAID Transmittals (USAID/ APCO/ArCon)**

Date	Contractor	Sender/Recipient	Subject
March 02, 2015	By Email	USAID/ APCO/ArCon	Re: TO 13-00012 MRSII: Final MoM No. 018
March 02, 2015	By Email	USAID/ APCO/ArCon	Re: TO 13-00012 MRSII: Final MoM No. 018
March 05, 2015	By Email	APCO/ArCon/ USAID	T.O 12- February 2015 - Monthly Report- Draft
March 09, 2015	By Email	USAID/ APCO/ArCon	VO 14
March 12, 2015	By Email	USAID/ APCO/ArCon	AID-294-TO-13-00012 / Notification of Defected Work - Project 3
March 12, 2015	By Email	APCO/ArCon/ USAID	RE: AID-294-TO-13-00012 / Notification of Defected Work -
March 12, 2015	By Email	USAID/ APCO/ArCon	CPARS Notification (Contract: AID294I1200005
March 17, 2015	By Email	USAID/ APCO/ArCon	Re: TO 13-00012 MRSII: RE: Task Order 12, Project 01 Dura-
March 18, 2015	By Email	USAID/ APCO/ArCon	CO Monthly Meeting
March 19, 2015	By Email	USAID/ APCO/ArCon	Toad Order No. AID-294-TO-13-00012 / Variation Order No. 15
March 20, 2015	By Email	APCO/ArCon/ USAID	RE: Toad Order No. AID-294-TO-13-00012 / Variation Order No.
March 20, 2015	By Email	USAID/ APCO/ArCon	COR Comments: T.O 12- February 2015 - Monthly Report- Draft
March 21, 2015	By Email	APCO/ArCon/ USAID	RE: COR Comments: T.O 12- February 2015 - Monthly Report-
March 23, 2015	By Email	APCO/ArCon/ USAID	TO#04 and TO#12 Equitable Adjustment
March 23, 2015	By Email	USAID/ APCO/ArCon	COR Approval: T.O 12- February 2015 - Monthly Report-
March 23, 2015	By Email	APCO/ArCon/ USAID	RE: COR Approval: T.O 12- February 2015 - Monthly Report-

**Outgoing / Incoming Consultant Correspondences (B&V/ APCO/ArCon)**

Date	Contractor	Sender/Recipient	Subject
March 01, 2015	By Email	B&V/ APCO/ArCon	TO 13-00012 MRSII: Draft MOM No. 021
March 01, 2015	By Email	APCO/ArCon/ B&V	TO -13-00012 Dura (wall from St 1+770 to St 1+785 LHS)
March 01, 2015	By Email	APCO/ArCon/ B&V	TO -13-00012 Dura (Sidewalk & Curbstone from St 2+300 to St 2+380 LHS)
March 01, 2015	By Email	B&V/ APCO/ArCon	RE: TO -13-00012 Dura (wall from St 1+770 to St 1+785 LHS)
March 01, 2015	By Email	B&V/ APCO/ArCon	RE: TO -13-00012 Dura (Sidewalk & Curbstone from St 2+300 to St 2+380 LHS)
March 01, 2015	By Email	B&V/ APCO/ArCon	RE: All Task Orders: As-Built Drawings Submittal delays
March 01, 2015	By Email	B&V/ APCO/ArCon	All Task Orders: RE: Thermoplastic Paint, Signage



# USAID | WEST BANK/GAZA

<b>Date</b>	<b>Contractor Trans. No.</b>	<b>Sender/Recipient</b>	<b>Subject</b>
March 02, 2015	By Email	APCO/ArCon/ B&V	RE: TO 13-00012 MRSII: Final MoM No. 018
March 02, 2015	By Email	APCO/ArCon/ B&V	T.O.12:SM-13-00012-DUR-E-C-125
March 02, 2015	By Email	B&V/ APCO/ArCon	RE: T.O.12:SM-13-00012-DUR-E-C-125
March 02, 2015	By Email	B&V/ APCO/ArCon	RE: TO -13-00012 Dura (Sidewalk & Curbstone from St 2+300 to St 2+380 LHS)
March 02, 2015	By Email	B&V/ APCO/ArCon	TO 13-00012 MRSII: Copy For Engineer Record.
March 02, 2015	By Email	B&V/ APCO/ArCon	RE: TO 13-00012 MRSII: Copy For Engineer Record
March 02, 2015	By Email	B&V/ APCO/ArCon	RE: TO 13-00012 MRSII: Copy For Engineer Record.
March 03, 2015	By Email	B&V/ APCO/ArCon	TO 13-00012 MRSII: Final MOM No. 021
March 03, 2015	By Email	APCO/ArCon/ B&V	RE: All Task Orders: RE: Thermoplastic Paint, Signage
March 04, 2015	By Email	B&V/ APCO/ArCon	RE: TO 13-00012: Dura VOR #20C
March 04, 2015	By Email	B&V/ APCO/ArCon	TO 13 00012 MRSII: Initial Punch List for Project No 1
March 05, 2015	By Email	APCO/ArCon/ B&V	All Task Orders- Geo-MIS Data - February 2015
March 05, 2015	By Email	APCO/ArCon/ B&V	FW: TO 13-00012: Dura VOR #20C
March 05, 2015	By Email	APCO/ArCon/ B&V	FW: TO 13-00012: Dura VOR #23B
March 05, 2015	By Email	B&V/ APCO/ArCon	TO 13-00012 MRSII: Variation Order #14
March 05, 2015	By Email	APCO/ArCon/ B&V	RE: TO 13-00012 MRSII: Variation Order #14
March 08, 2015	By Email	B&V/ APCO/ArCon	RE: TO 13 00012 MRSII: Repair of Damaged Under Ground Utilities
March 08, 2015	By Email	B&V/ APCO/ArCon	TO 13 00012 MRSII: Curb Stone Paint
March 08, 2015	By Email	B&V/ APCO/ArCon	TO 13 00012 MRSII: Manhole Cover Adjustment
March 09, 2015	By Email	APCO/ArCon/ B&V	FW: All Task Orders: As-Built Drawings Submittal delays
March 09, 2015	By Email	APCO/ArCon/ B&V	RE: All Task Orders: RE: Thermoplastic Paint, Signage
March 12, 2015	By Email	APCO/ArCon/ B&V	T.O.12: DUR Saturday Planned activities
March 12, 2015	By Email	APCO/ArCon/ B&V	FW: TO 13-00012: Dura VOR #20C
March 12, 2015	By Email	APCO/ArCon/ B&V	TO 13-00012: Dura VOR #23B
March 12, 2015	By Email	APCO/ArCon/ B&V	TO12-DUR- TECHNICAL PROPOSAL-dresser
March 12, 2015	By Email	APCO/ArCon/ B&V	TO12-DUR- water line testing lab
March 13, 2015	By Email	APCO/ArCon/ B&V	TO12-DUR- asphalt surface cleaning and washing
March 14, 2015	By Email	B&V/ APCO/ArCon	RE: TO12-DUR- water line testing lab
March 14, 2015	By Email	B&V/ APCO/ArCon	RE: TO12-DUR- asphalt surface cleaning and washing
March 14, 2015	By Email	APCO/ArCon/ B&V	TO12_ DUR_ CMC services
March 15, 2015	By Email	APCO/ArCon/ B&V	TO-13-00012 - DURA - sewer leakage inside water chamber
March 15, 2015	By Email	B&V/ APCO/ArCon	FW: Traffic Sign Materials Specifications - All roads
March 16, 2015	By Email	B&V/ APCO/ArCon	FW: Handing Over - Dura-Hebron (Sinjir) Road
March 16, 2015	By Email	APCO/ArCon/ B&V	CMC services
March 16, 2015	By Email	APCO/ArCon/ B&V	Task Order 14, Project 01 Dura- Handover
March 16, 2015	By Email	APCO/ArCon/ B&V	RE: Task Order 14, Project 01 Dura- Handover
March 17, 2015	By Email	B&V/ APCO/ArCon	TO 13-00012 MRSII: RE: Task Order 12, Project 01 Dura-Handover
March 17, 2015	By Email	B&V/ APCO/ArCon	Re: TO 13-00012 MRSII: RE: Task Order 12, Project 01 Dura-Handover
March 18, 2015	By Email	B&V/ APCO/ArCon	RE: TO 13-00012 MRSII: RE: Task Order 12, Project 01 Dura-Handover
March 18, 2015	By Email	APCO/ArCon/ B&V	TO12-DUR- Epoxy material inside water chambers
March 19, 2015	By Email	APCO/ArCon/ B&V	T.O.12: DUR Friday and Saturday Planned activities
March 19, 2015	By Email	APCO/ArCon/ B&V	Project Outcome and Performance Indicator
March 22, 2015	By Email	B&V/ APCO/ArCon	RE: Task Order 14, Project 01 Dura- Handover



# USAID | WEST BANK/GAZA

Date	Contractor Trans. No.	Sender/Recipient	Subject
March 22, 2015	By Email	B&V/ APCO/ArCon	RE: Project Outcome and Performance Indicator
March 22, 2015	By Email	APCO/ArCon/ B&V	RE: Task Order 14, Project 01 Dura- Handover
March 24, 2015	By Email	APCO/ArCon/ B&V	RE: AID-294-TO-13-00012 / Notification of Defected Work - Project 3

## PAYMENTS:

Voucher Number	Submitted Date	Amount	Retention Amount	Amount Received	Date Received
01	January 20, 2014	\$ 447,973.34	\$0.00	\$ 447,973.34	January 31, 2014
02	February 09, 2014	\$ 297,902.28	\$0.00	\$ 297,902.28	February 28, 2014
03	March 25, 2014	\$ 556,484.93	\$0.00	\$ 556,484.93	April 09, 2014
04	April 16, 2014	\$ 480,513.49	\$0.00	\$ 480,513.49	May 06, 2014
05	May 21, 2014	\$ 719,793.88	\$0.00	\$ 719,793.88	June 12, 2014
06	June 03, 2014	\$ 347,821.55	\$0.00	\$ 347,821.55	June 23, 2014
07	July 16, 2014	\$ 977,964.61	\$0.00	\$ 977,964.61	August 08, 2014
08	Sep. 04, 2014	\$1,366,208.61	\$0.00	\$1,366,208.61	Sep. 23, 2014
09	October 15, 2014	\$1,474,689.68	\$0.00	\$1,474,689.68	Nov. 07, 2014
10	Nov. 18, 2014	\$ 595,543.27	\$0.00	\$595,543.27	Dec. 15, 2014
11	Dec. 11, 2014	\$ 654,531.88	\$0.00	\$654,531.88	Dec. 15, 2014
12	Jan. 06, 2015	\$1,052,251.88	\$0.00	\$1,052,251.88	Jan. 20, 2015
13	Feb. 11, 2015	\$ 480,436.63	\$0.00	\$480,436.63	Feb. 27, 2015
14	Mar. 23, 2015	\$1,521,762.30	\$0.00	Not received yet	
<b>Total</b>		<b>\$ 10,973,878.33</b>	<b>\$0.00</b>	<b>\$ 9,452,116.03</b>	

APCO/ArCon total accrued expenditures \$1,161,998.76

## VARIATION ORDERS

VO No.	DESCRIPTION	VO Status (AP/P E/RE /RJ)			Date Sent to B&V	USAD Approval Date	Variation order Amount	Time Ex. Calendar Days
		APCO	B&V	USAID				
01	New Project layout for project 3	AP	AP	AP	Feb. 04, 2014	Feb. 06, 2014	\$8,190	00
02	Additional Water Pipeline, Valve Chambers, Topping Layer and New Definitive Quantities at Project 1 Additional Water Pipeline at Project 2 Additional Roads and Pre-Final Quantities at Project 3.	AP	AP	AP	April 02, 2014	April 16, 2014	\$58,377	P. 01- 34 P. 02- 07
03	New Items, Pre-Final Quantities and Time Extension at Project #3	AP	AP	AP	April 28, 2014	April 29, 2014	\$11,676.9	P.03 – 07
04	Final Definitive Quantities and final list of roads at Project 03	AP	AP	AP	May 06, 2014	May 19, 2014	\$16,206.82	00



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

VO No.	DESCRIPTION	VO Status (AP/PE/RE/RJ)			Date Sent to B&V	USAD Approval Date	Variation order Amount	Time Ex. Calendar Days
		APCO	B&V	USAID				
05	Changes in the Requirements, New Items and New Project Definitive Quantities at Project 01 and Project 02 and Time Extension at Project 02	AP	AP	AP	July 01, 2014	July 14, 2014	\$112,787.01	P.02- 30
06	Project 2: Additional Water Pipelines, New Project Definitive Quantities and Time Extension.	AP	AP	AP	Aug. 06, 2014	Aug. 08, 2014	\$192,071.98	P.02- 25
07	Project 1: De-Scoping of Road Segment from Station 3+700 to Station 4+045.9	AP	AP	AP	Aug. 10, 2014	Aug. 28, 2014	\$(290,350.0)	P.01- (12)
08	PROJECT 02: Extension Limits of Samu'- Yatta Road - Additional Asphalt Milling and Overlay Activities and Pre-Final Definitive Quantities	AP	AP	AP	Sep. 17, 2014	Sep. 24, 2014	\$(189,226.12)	00
09	Administrative Variation Order for Final Definitive Quantities at Project 02	AP	AP	AP	Oct. 16, 2014	Oct. 23, 2014	\$(14,060.81)	00
10	Time Extension at Project #01	AP	AP	AP	Nov. 10, 2014	Nov. 17, 2014	\$0.00	P. 01- 46
11	Additional Works and Time Extension for Project #01	AP	AP	AP	Dec. 18, 2014	Dec. 19, 2014	\$(151,225.50)	P. 01- 24
12	Additional Retaining Walls and Time Extension for Project #01	AP	AP	AP	Dec. 31, 2014	Jan. 21, 2015	\$105,550.00	P. 01- 24
13	Weather Delay Time Extension for Project #01	AP	AP	AP	Feb. 18, 2015	Feb. 18, 2015	\$0.00	P. 01- 14
14	Weather Delay Time Extension for Project #01	AP	AP	AP	Mar. 05, 2015	Mar. 09, 2015	\$0.00	P.01- 09
15	New Items and New Definitive Quantities for Project#01	AP	AP	AP	Mar. 15, 2015	Mar. 19, 2015	\$138,127.57	00

AP: Approved PE: Pending RE: Revise RJ: Rejected

### VARIATION ORDER REQUESTS:

VOR No.	DESCRIPTION		Date Sent to B&V	Variation order Amount	Time Ex.
01	Urgent Works for Bethlehem Internal Roads	Revision A	Feb. 06, 2014	\$162,228.75 / Resubmitted	00 Calendar Day
		Revision B	March 31, 2014	\$146,291.79 Rejected by CMC- Submitted as a Claim to USAID	00 Calendar Day
02	Revised BOQ Quantities, Additional 4" pipes Installation works, 3/4" risers and Valves Chambers Construction and Time Extension	Revision A	Feb. 05, 2014	\$ 283,616.90/ Resubmitted	P01- 55 Calendar Days
		Revision B	Feb. 19, 2014	\$ 267,086.40/ Resubmitted	P01- 55 Calendar Days
		Revision C	March 02, 2014	\$172,706.40/ Approved, included under VO#02	P01- 54 Calendar Days
03	Project 01: Provide two Layers of 7cm asphalt from Sta.0+000 to Sta.0+280	Revision A	April 21, 2014	\$145,040/ Resubmitted	0
		Revision B	April 27, 2014	\$145,040/ Included under VO#05	0



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

VOR No.	DESCRIPTION		Date Sent to B&V	Variation order Amount	Time Ex.
04	Project 03:Change in additional works and time extension	Revision A	April 21,2014	\$138,973.60/ Resubmitted	P02- 24 days
		Revision B	April 27,2014	\$12,129.94/ Partially included-VO#03	P03- 6 days
05	Project 02: Replace Box culvert, 6" UPVC pipe crossing, topping, and Raising PGL	Revision A	May 19, 2014	\$0.00 Partially approved - VO#05	P02- 24 Days
		Revision B	June 12, 2014	\$0.00 Closed under VO#05	P02- 24 Days
		Revision C	Sep. 04, 2014	\$ 2,734.08 Response received from CMC.	0
06	Project 02- Stone Boulders from Sta. A3+295 to Sta. 3+345	Revision A	May 20, 2014	\$138,615.74 Revise Resubmit	P02- 34 Days
		Revision B	June 8, 2014	\$46,060.00 Closed under VO#05	P02- 34 Days
07	Project 01:Guard Rail Type ESP4-N2	Revision A	May 21, 2014	\$22,620.00 Closed under VO#05	0
08	Project 02: Gravity Retaining wall from Sta.A0+040 to Sta.0+074 and new items.	Revision A	June 30, 2014	\$35,361.2 Closed under VO#05	P02- 24 Days
09	Project 01: Gravity walls, Retaining walls, redesign, and new definitive quantities.	Revision A	June 23, 2014	\$115,028.76 Noted	P01- 46 Days
10	Project 02- Scope of Work, Additional Works & New Items- Install 4", 3" and 2" water pipelines from Sta. 2+200 to Sta. 4+150 and Time Impact Analysis	Revision A	July 15, 2014	\$188,968.98 Revise Resubmit	To be evaluated
		Revision B	July 24, 2014	\$ 136,615.95 Closed under VO#06	P02- 25 Days
11	Project 03- Scope of Work, Additional Works & New Items- Maintenance work of existing waste water line in Al Ein Road.	Revision A	July 09, 2014	\$8,886.59 Retracted.	0
12	Project 01- Scope of Work: Comprehensive Time Impact Analysis with Request for Time Extension	Revision A	July 22, 2014	\$---- Revise Resubmit	P01- 38 Days
		Revision B	October 2, 2014	\$---- Closed under VO#10	P01- 32Days
13	Project 03- Maintenance work of existing waste water line in Al Ein Road	Revision A	Aug. 12, 2014	\$10,233.92 To refer to COR regarding submitted VOR	0
14	Project 01- New Stone Boulders located from Sta. 2+300 to Sta. 2+360	Revision A	Aug. 17, 2014	\$51,403.20 Closed – Not required	P01- 40 Days
15	Project 02- Scope of Work : Additional Works & New Items- Crushed Aggregate Compacted Base Course Layer 150 mm thick Class A-Supply and install 60 cm concrete hand hole for future crossings	Revision A	Sep. 04, 2014	\$ 23,520.00 Closed under VO#08	0
16	Project 02- Scope of Work- Asphalt leveling course	Revision A	Sep. 08, 2014	\$ 7,344.00 Closed under VO#08	0
17	Project 02- Scope of Work- New Items- Cast Iron manholes cover	Revision A	Sep. 28, 2014	\$3,456 Not Required	0
18	Project 01- Changes in the requirements and additional works- Milling and asphalt re-surfacing for a section of Dura Main road with total length of 600 lineal meter and supplying and installation of handrail -Construction of additional reinforced concrete retaining walls.	Revision A	Dec. 17, 2014	Closed under VO#11	P01- 24 Days



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

VOR No.	DESCRIPTION		Date Sent to B&V	Variation order Amount	Time Ex.
19	Project 01- Raining days and weather condition time impact analysis with request for time extension	Revision A	Jan. 29, 2015	\$---- Closed under VO#13	P01- 19 Days
20	Project 01- Changes in the requirements, new items and revised scope of work: Revised requirement of 2" Gate Valve inside the water chambers Sta. 0+279 , Sta. 3+170 and Sta. 3+520, 2- Storm water manhole Covers , 3- Combined water chamber 4" gate valve with 3" ARV at Sta. 2+150, 4- Construction of Garbage containers, 5- Cast In place Skew shape and larger dimensions of Storm Manhole #3 at Sta. 0+320, 6- Cast in place Storm Manhole #5 at Sta. 0+320, 7- KANAFLEX (HDPE) and precast concrete storm water pipe line with reinforced concrete manhole for the outfall Sta. 1+300 L.H.S, 8- Additional new item and change in the original scope of works, 9- Additional 400 mm storm water pipe line from Sta. 1+620 to Sta. 1+695 R.H.S, 10- Maintenance of existing reinforced concrete steps from Sta. 0+590 to Sta. 0+605 L.H.S, 11- Construction of pedestrian crossing, 12- Supply and install new 2" water pipe line crossing, 13- Construction of boundary wall with wire mesh fence, 14- Construction of reinforced concrete stair B-300, and Time Extension	Revision A	Feb. 01, 2015	\$---- Revise Resubmit	To be submitted
		Revision B	Feb. 15, 2015	\$---- Revise Resubmit	Time impact analysis will be submitted upon CMC request
		Revision C	Mar. 05, 2015	\$---- Closed under VO#15	0
21	Project 01- Changes in the requirements, new items and revised scope of work and Time extension: Construction of roundabout at St. 0+000, supply and install galvanized steel handrail, supply and install steel handrail for pedestrians, roundabout landscaping, relocation of existing pole and supply and install new lighting pole.	Revision A	Feb. 26, 2015	\$---- Closed under VO#15	0
22	Project 01- Delays due to weather condition and security situation time impact analysis with request for time extension	Revision A	Mar. 01, 2015	\$0.00 Closed under VO#14	P01- 17 Days
23	Project 01- Changes in the requirements, new items and revised scope of work : KANAFLEX (HDPE) and precast concrete storm water pipe line with reinforced concrete manhole for the outfall Sta. 1+300 L.H.S	Revision A	Mar. 01, 2015	\$---- Noted	0
		Revision B	Mar. 04, 2015	\$---- Closed under VO#15	0
24	Project 01- Time impact analysis with request for time extension.	Revision A	Mar. 15, 2015	\$0.00 Project was handed over on time.	0

## OBSTACLES AND CHALLENGES

### Project 01- DUR

No major obstacles were encountered during this reporting period. Objections from landowners continued to slow down work progress and punch list works for example: at St. 2+300 landowner demolished the casted gravity wall at the simple access, and removed and damaged the formwork. APCO workers left the site and avoided any contact with the resident. BV personnel were informed via. email and they instructed the Contractor to leave the wall as it is. Despite all these conditions, project was completed and handed over on time.



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

## PROGRESS PHOTOS:

### Project 01- DUR



Project 01- from St. 0+200 to St. 0+380 Backward- Before construction.



Project 01- from St. 0+200 to St. 0+380 Backward- After completing construction activities.



Project 01- from St. 0+080 to St. 0+140 Forward- Before construction.



Project 01- from St. 0+080 to St. 0+140 Forward - After completing construction activities.



Project 01- at St. 0+560 Forward- Before construction.



Project 01- at St. 0+560 Forward - After completing construction activities.



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE



Project 01- at St. 0+660 Backward- Before construction.



Project 01- at St. 0+660 Backward- After completing construction activities.



Project 01- at St. 0+840 Forward- Before construction.



Project 01- at St. 0+840 Forward- After completing construction activities.



Project 01- at St. 1+000 Forward- Before construction.



Project 01- at St. 1+000 Forward- After completing construction activities.



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE



Project 01- at St. 1+080 Forward- Before construction.



Project 01- at St. 1+080 Forward- After completing construction activities.



Project 01- at St. 1+660 Forward- Before construction.



Project 01- at St. 1+660 Forward- After completing construction activities.



Project 01- at St. 1+880 Forward- Before construction.



Project 01- at St. 1+880 Forward- After completing construction activities.



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE



Project 01- at St. 2+020 Forward- Before construction.



Project 01- at St. 2+020 Forward- After completing construction activities.




Project 01- at St. 2+100 Backward- Before construction.



Project 01- at St. 2+100 Backward- After completing construction activities.



Project 01- During night - After completing construction activities.

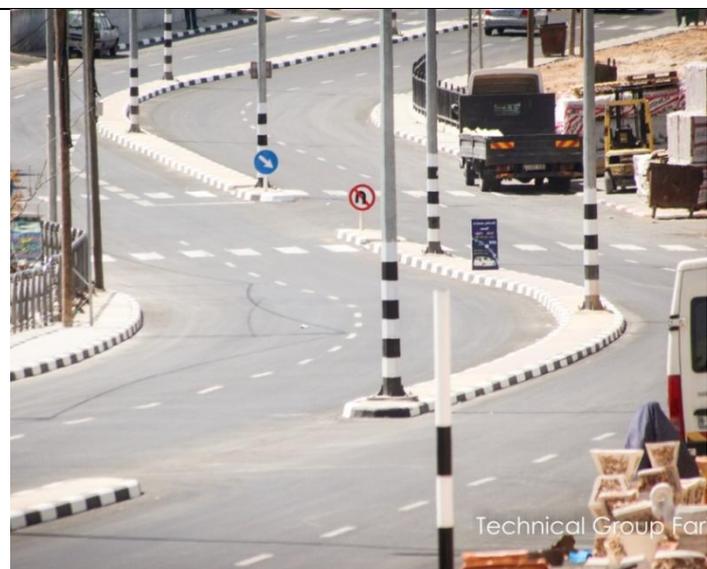

Project 01- Road marking and furniture - After completing construction activities.



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE

## Project 02- SAM



Segment A- Intersection at St. 0+000 Forward- Before construction.



Segment A- Intersection at St. 0+000 Forward- After completing construction activities.



Segment A- St. 1+260 Backward- Before construction.



Segment A- St. 1+260 Backward- After completing construction activities.



Segment A- St. 1+260 Forward- Before construction.



Segment A- St. 1+260 Forward- After completing construction activities.



# USAID | WEST BANK/GAZA



2014/02/13 10:34 AM

Segment A- St. 2+640 Backward- Before construction.



09/29/2014 02:24 PM

Segment A- St. 2+640 Backward- After completing construction activities.



2014/02/13 10:50 AM

Segment A- St. 3+200 Backward- Before construction.



09/29/2014 02:28 PM

Segment A- St. 3+200 Backward- After completing construction activities.



2014/02/13 10:47 AM

Segment A- St. 3+200 Forward- Before construction.



09/29/2014 02:26 PM

Segment A- St. 3+200 Forward- After completing construction activities.



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE



Segment B- St. 0+320 Backward – Before Construction.



Segment B- St. 0+320 Backward – After completing construction activities.

## Project 03- BTH



Before Construction – WSSA Intersection



After completing construction Activities (WSSA Intersection).



After completing construction Activities (Wadi Ma'ali Road).



After completing construction Activities (Al Karkafa Road).



# USAID | WEST BANK/GAZA

FROM THE AMERICAN PEOPLE



Permanent Sign installed at Al-Qeta'a – Wadi Ma'ali Roads.



After completing construction Activities (Wadi Shaheen Road).

## A | Materials- Equipments Receiving Log

Project 01: Dura - Hebron (Sinjir) Road  
 USAID Contract No. 294-I-00-12-00005  
 Contractor: APCO/ArCon



**Title: Equipment receiving log/March 2015**

Date	Grader Cat, G12, H140, Motor		Finisher		Bob Cat		JCB		Steel Compactor		Dump Truck Actors, 2007		Crane		WATER TANK 10M3		Wheel Loader		Dossan Wheel		Excavator Volvo		Pneumatic roller		RC Sprayer		MC Sprayer		Concrete pump		Concrete Vibrator		Concrete transit Mixer		Welding Machine		Bomag Compactor		Asphalt Cuter		Plate Compactor		
	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site	Quantity in use	Quantity site			
1-Mar	1		2		2		3		2		10		1		1							1		2		1						1		7		1		1		1		2	
2-Mar	1		1		2		3		2		10				1		1						1		2						1		5				1		1		2		
3-Mar	1				2		3		1		2		1		1															1		6				1		1		2			
4-Mar	1				2		2		1		3		1		1															1		2								1			
5-Mar	1				2		3		1		2		1		1													1		2		7				1		1		2			
6-Mar																																											
7-Mar	1		1		2		3		2		10		1		1								2				1			2		6		1		1		1		2			
8-Mar	1		1		2		3		2		6		1		1								1			1			2		6					1		1		2			
9-Mar	1		1		2		3		2		10		1		1								2		1			1		1		3				1		1		2			
10-Mar					2		3		1		2		1		1											1			1		7					1		1		2			
11-Mar			1		2		3		2		10		1		1								2		0.5			1		1		7							1		2		
12-Mar																																											
13-Mar							2																																				
14-Mar					2		3		1		2		2		1														1		7					1		1		2			
15-Mar					2		3		1		2		2		1												1			1		5				1		1		2			
16-Mar			1		2		3		2		10		1		1								2		1				1		4					1		1		2			
17-Mar					2		3		1		2		1		1				1							1		1		1		7				1		1		2			
18-Mar					2		3		1		2		1		1												1			1		5					1		1		2		
19-Mar			1				3		2		10		1		1		2						2		1				1		4					1		1		2			
20-Mar																																											
21-Mar					2		3				2				1														1		4						1				2		
22-Mar	1				2		3		1		2				1														1		4		1		1		1		1		2		
23-Mar	1		1		2		3		2		4		1		1								1			1			1		4					1		1		2			
24-Mar			1		2		3		2		2		1		1									1			1		1		4					1		1		2			
25-Mar																																											
26-Mar					2		2																																				
27-Mar																																											
28-Mar					2		2				1											1							1		2												
29-Mar					2		2				1											1							1		6												
30-Mar					1		2				1		1																1		5												
31-Mar					1		2				1		1															1															

Project 01: Dura - Hebron (Sinjir) Road  
 USAID Contract No. 294-I-00-12-00005  
 Contractor: APCO/ArCon



**Title: Materials Receiving Log/ March 2015**

<b>Date</b>	<b>Material Delivered to Site</b>	<b>Quantity</b>
1-Mar	Ready mixed concrete B250 without foliya	30.5 m <sup>3</sup>
	Dry mix concrete	4 m <sup>3</sup>
	Base course	100 m <sup>3</sup>
	Asphalt	512 Ton
	Ready mix concrete B-250	15 m <sup>3</sup>
2-Mar	Ready mixed concrete B250 without foliya	16 m <sup>3</sup>
	Dry mix concrete	6 m <sup>3</sup>
	Base course	10 m <sup>3</sup>
	Asphalt	404 Ton
	Ready mix concrete B-250	5 m <sup>3</sup>
3-Mar	Base course	80 m <sup>3</sup>
	Ready mix concrete B-200	9 m <sup>3</sup>
	Dry mix concrete	7 m <sup>3</sup>
	Ready mix concrete B-250	28 m <sup>3</sup>
4-Mar	Base course	100 m <sup>3</sup>
	Ready mix concrete B-250	6 m <sup>3</sup>
	Dry mix concrete	5 m <sup>3</sup>
5-Mar	Ready mix concrete B-250	40.5 m <sup>3</sup>
6-Mar		
7-Mar	Ready mix concrete B-250	4.5 m <sup>3</sup>
	Ready mixed concrete B250 without foliya	34 m <sup>3</sup>
	Dry mix concrete	4 m <sup>3</sup>
	Asphalt	400 Ton
8-Mar	Ready mix concrete B-250	12 m <sup>3</sup>
	Ready mixed concrete B250 without foliya	18 m <sup>3</sup>
	Dry mix concrete	7 m <sup>3</sup>
	Curb Stone	500 lm
	Ready mix concrete B-200	4 m <sup>3</sup>
	Asphalt	120 Ton
9-Mar	Ready mix concrete B-250	5 m <sup>3</sup>
	Dry mix concrete	7 m <sup>3</sup>
	Ready mix concrete B-200	9 m <sup>3</sup>
	Asphalt	500 Ton
10-Mar	Dry mix concrete	8 m <sup>3</sup>
	Ready mix concrete B-200	3 m <sup>3</sup>
	Asphalt	35 Ton
	Ready mix concrete B-250	29.5 m <sup>3</sup>
	Curb Stone	240 lm

Project 01: Dura - Hebron (Sinjir) Road  
 USAID Contract No. 294-I-00-12-00005  
 Contractor: APCO/ArCon



**Title: Materials Receiving Log/ March 2015**

<b>Date</b>	<b>Material Delivered to Site</b>	<b>Quantity</b>
11-Mar	Ready mix concrete B-250	22.5 m <sup>3</sup>
	Dry mix concrete	5 m <sup>3</sup>
	Asphalt	500 Ton
	Ready mixed concrete B250 without foliya	18 m <sup>3</sup>
12-Mar		
13-Mar		
14-Mar	Ready mixed concrete B250 without foliya	33.5 m <sup>3</sup>
	Ready mix concrete B-250	8 m <sup>3</sup>
	Dry mix concrete	6 m <sup>3</sup>
15-Mar	Ready mixed concrete B250 without foliya	18 m <sup>3</sup>
	Ready mix concrete B-250	14.5 m <sup>3</sup>
	Dry mix concrete	3 m <sup>3</sup>
	Asphalt	38 Ton
	Sand	20 Ton
16-Mar	Ready mixed concrete B250 without foliya	18 m <sup>3</sup>
	Ready mix concrete B-250	9.5 m <sup>3</sup>
	Dry mix concrete	3 m <sup>3</sup>
	Asphalt	540 Ton
17-Mar	Ready mixed concrete B250 without foliya	27 m <sup>3</sup>
	Ready mix concrete B-250	18.5 m <sup>3</sup>
	Asphalt	56 Ton
	Ready mix concrete B-200	4 m <sup>3</sup>
18-Mar	Ready mixed concrete B250 without foliya	15 m <sup>3</sup>
	Ready mix concrete B-250	10.5 m <sup>3</sup>
	Dry mix concrete	4 m <sup>3</sup>
	Asphalt	32 Ton
19-Mar	Ready mixed concrete B250 without foliya	18 m <sup>3</sup>
	Ready mix concrete B-250	15 m <sup>3</sup>
	Asphalt	400 Ton
20-Mar		
21-Mar	Ready mixed concrete B250 without foliya	18 m <sup>3</sup>
	Ready mix concrete B-250	7 m <sup>3</sup>
	Ready mix concrete B-200	4.5 m <sup>3</sup>
22-Mar	Ready mixed concrete B250 without foliya	15 m <sup>3</sup>
	Ready mix concrete B-250	14.5 m <sup>3</sup>
23-Mar	Ready mixed concrete B250 without foliya	17.5 m <sup>3</sup>
	Asphalt	102 Ton
	Dry mix concrete	4 m <sup>3</sup>

Project 01: Dura - Hebron (Sinjir) Road  
 USAID Contract No. 294-I-00-12-00005  
 Contractor: APCO/ArCon



**Title: Materials Receiving Log/ March 2015**

<b>Date</b>	<b>Material Delivered to Site</b>	<b>Quantity</b>
24-Mar	Ready mixed concrete B250 without foliya	29 m <sup>3</sup>
	Asphalt	62 Ton
25-Mar	Ready mixed concrete B250 without foliya	18 m <sup>3</sup>
	Ready mix concrete B-250	15 m <sup>3</sup>
	Asphalt	400 Ton
26-Mar		
27-Mar		
28-Mar	Ready mix concrete B-200	14 m <sup>3</sup>
29-Mar	Ready mix concrete B-200	18 m <sup>3</sup>
	Ready mix concrete B-250	13 m <sup>3</sup>
	Dry mix concrete	5 m <sup>3</sup>
30-Mar	Ready mix concrete B-200	15 m <sup>3</sup>
	Ready mix concrete B-250	11.5 m <sup>3</sup>
31-Mar		

**B | Detailed Cu'Dwlv' Time Schedule for the Project**

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float	2014												2015			
							Qtr 4		Qtr 1			Qtr 2			Qtr 3			Qtr 4		Qtr 1		Qtr 2
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
<b>Multiple Roads Project South II</b>							19-Mar-1															
<b>Milestones</b>							19-Mar-1															
<b>General Milestones</b>							19-Mar-1															
MRSII0100	Start Date NTP	0d	100%	01-Nov-13 A			19-Mar-1															
MRSII0110	Completion Multiple Roads Project in the South West Bank	0d	100%		19-Mar-15 A		19-Mar-1															
<b>Intermediate Milestones</b>							19-Mar-1															
<b>Completion Milestones</b>							19-Mar-1															
MRSII0130	Completion (Project 03) Milling and Overlay of Bethlehem Internal Roads	0d	100%	06-May-14 A	06-May-14 A		19-Mar-1															
MRSII0140	Completion (Project 02) Samu' -Yatta Road	0d	100%		28-Sep-14 A		19-Mar-1															
MRSII0150	Completion (Project 01) Dura - Hebron (Sinjer) Road	0d	100%		19-Mar-15 A		19-Mar-1															
<b>Preconstruction Milestones</b>							15-Jul-14 A															
MRSII0180	Start Preconstruction Submittal	0d	100%	03-Nov-13 A			15-Jul-14 A															
MRSII0190	Finish Preconstruction Submittal	0d	100%		15-Jul-14 A		15-Jul-14 A															
<b>PROJECT 01 Dura - Hebron (Sinjer) Road</b>							19-Mar-1															
<b>Mobilization</b>							30-Dec-13 A															
MRSII0200	Start Mobilization	0d	100%	02-Nov-13 A			30-Dec-13 A															
MRSII0210	Finish Mobilization	0d	100%		30-Dec-13 A		30-Dec-13 A															
<b>Shop Drawing</b>							24-Feb-15 A															
MRSII0220	Start Shop Drawing Submittal	0d	100%	26-Nov-13 A			24-Feb-15 A															
MRSII0230	Finish Shop Drawing Submittal	0d	100%		24-Feb-15 A		24-Feb-15 A															
<b>Material</b>							15-Sep-14 A															
MRSII0240	Start Material Submittal	0d	100%	28-Nov-13 A			15-Sep-14 A															
MRSII0250	Finish Material submittal	0d	100%		15-Sep-14 A		15-Sep-14 A															
<b>Construction</b>							19-Mar-1															
MRSII0260	Start Construction (Ground Breaking)	0d	100%	15-Jan-14 A			19-Mar-1															
MRSII0270	Finish Construction Phase	0d	100%		19-Mar-15 A		19-Mar-1															
<b>Project Duration</b>							19-Mar-1															
MRSII0280	Project Duration (Calendar Days)	332d	100%	01-Nov-13 A	19-Mar-15 A		19-Mar-1															
MRSII0290	Project Duration (Working Days)	257d	100%	01-Nov-13 A	19-Mar-15 A		19-Mar-1															
MRSII0300	Construction Duration (Working Days)	195d	100%	15-Jan-14 A	19-Mar-15 A		19-Mar-1															
<b>PROJECT 02 Samu' -Yatta Road</b>							28-Sep-14 A															
<b>Mobilization</b>							04-Jan-14 A															
MRSII0310	Start Mobilization	0d	100%	02-Nov-13 A			04-Jan-14 A															
MRSII0320	Finish Mobilization	0d	100%		04-Jan-14 A		04-Jan-14 A															
<b>Shop Drawing</b>							19-Aug-14 A															
MRSII0330	Start Shop Drawing Submittal	0d	100%	17-Nov-13 A			19-Aug-14 A															
MRSII0340	Finish Shop Drawing Submittal	0d	100%		19-Aug-14 A		19-Aug-14 A															

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float	2014												2015			
							Qtr 4		Qtr 1			Qtr 2			Qtr 3		Qtr 4		Qtr 1		Qtr 2	
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
<b>Material</b>							05-Aug-14 A															
MRSII0350	Start Material Submittal	0d	100%	28-Nov-13 A			[Gantt bar from Nov to Aug]															
MRSII0360	Finish Material submittal	0d	100%		05-Aug-14 A		[Milestone diamond at Aug]															
<b>Construction</b>							28-Sep-14 A															
MRSII0370	Start Construction (Ground Breaking)	0d	100%	19-Jan-14 A			[Gantt bar from Jan to Sep]															
MRSII0380	Finish Construction Phase	0d	100%		28-Sep-14 A		[Milestone diamond at Sep]															
<b>Project Duration</b>							28-Sep-14 A															
MRSII0390	Project Duration (Calendar Days)	221d	100%	01-Nov-13 A	28-Sep-14 A		[Summary bar from Nov to Sep]															
MRSII0400	Project Duration (Working Days)	175d	100%	01-Nov-13 A	28-Sep-14 A		[Summary bar from Nov to Sep]															
MRSII0410	Construction Duration (Working Days)	112d	100%	19-Jan-14 A	28-Sep-14 A		[Summary bar from Jan to Sep]															
<b>PROJECT 03 Milling and Overlay of Bethlehem Internal Roads</b>							06-May-14 A															
<b>Mobilization</b>							23-Dec-13 A															
MRSII0420	Start Mobilization	0d	100%	01-Nov-13 A			[Gantt bar from Nov to Dec]															
MRSII0430	Finish Mobilization	0d	100%		23-Dec-13 A		[Milestone diamond at Dec]															
<b>Shop Drawing</b>							22-Apr-14 A															
MRSII0440	Start Shop Drawing Submittal	0d	100%	08-Dec-13 A			[Gantt bar from Dec to Apr]															
MRSII0450	Finish Shop Drawing Submittal	0d	100%		22-Apr-14 A		[Milestone diamond at Apr]															
<b>Material</b>							25-Mar-14 A															
MRSII0460	Start Material Submittal	0d	100%	28-Nov-13 A			[Gantt bar from Nov to Mar]															
MRSII0470	Finish Material submittal	0d	100%		25-Mar-14 A		[Milestone diamond at Mar]															
<b>Construction</b>							04-May-14 A															
MRSII0480	Start Construction (Ground Breaking)	0d	100%	02-Nov-13 A			[Gantt bar from Nov to May]															
MRSII0490	Finish Construction Phase	0d	100%		04-May-14 A		[Milestone diamond at May]															
<b>Project Duration</b>							06-May-14 A															
MRSII0500	Project Duration (Calendar Days)	93d	100%	01-Nov-13 A	06-May-14 A		[Summary bar from Nov to May]															
MRSII0510	Project Duration (Working Days)	68d	100%	01-Nov-13 A	06-May-14 A		[Summary bar from Nov to May]															
MRSII0520	Construction Duration (Working Days)	61d	100%	02-Nov-13 A	04-May-14 A		[Summary bar from Nov to May]															
<b>Task order Duration</b>							19-Mar-15 A															
MRSII0530	Project Duration (Calendar Days)	364d	100%	01-Nov-13 A	19-Mar-15 A		[Summary bar from Nov to Mar 2015]															
MRSII0540	Project Duration (Working Days)	281d	100%	01-Nov-13 A	19-Mar-15 A		[Summary bar from Nov to Mar 2015]															
<b>Pre Construction Phase</b>							15-Jul-14 A															
<b>Pre Construction Submittals</b>							15-Jul-14 A															
MRSII0560	30- Day Schedule ( Pre Construction Submittals & Mobilization phase)	10d	100%	03-Nov-13 A	11-Nov-13 A		[Summary bar from Nov to Nov]															
MRSII0570	Bank Guarantee Certificates	10d	100%	03-Nov-13 A	19-Nov-13 A		[Summary bar from Nov to Nov]															
MRSII0590	Testing Lab	10d	100%	04-Nov-13 A	11-Jan-14 A		[Summary bar from Nov to Jan]															

Actual Work    Milestone Actual    Actual Level of Effort    Summary

Date	Revision	Checked	Approved
01-Apr-15			

































Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float	2014												2015						
							Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1		Qtr 2	
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
<b>Asphalt binder</b>																									
DUR1845	Base course Preparation before applying asphalt (re -compacted)	1d	100%	01-Mar-15 A	07-Mar-15 A																				
DUR2925	5 cm Asphalt Simple Access	1d	100%	07-Mar-15 A	07-Mar-15 A																				
DUR1850	5 cm Asphalt Binder Course Including Prime Coat & Adjusted level manholes	2d	100%	07-Mar-15 A	07-Mar-15 A																				
<b>Street Lighting Poles and Curbstone</b>																									
DUR1285	Foundation & Civil Works of Street Lighting Poles	2d	100%	02-Feb-15 A	04-Mar-15 A																				
DUR2865	Install Street Lighting Poles	1d	100%	03-Mar-15 A	03-Mar-15 A																				
DUR1860	Concrete Curbstone and Side Walk	5d	100%	08-Mar-15 A	08-Mar-15 A																				
DUR2955	interlock works	5d	100%	09-Mar-15 A	09-Mar-15 A																				
<b>Asphalt Wearing</b>																									
DUR2419-new	5 cm Asphalt Wearing Course Including Tack Coat	2d	100%	15-Mar-15 A	15-Mar-15 A																				
<b>Phase #3 Main road Intersections @ 0+000</b>																									
<b>Intersections @ 0+000 Area A RHS &amp; LHS Area A</b>																									
DUR2020	Implement Traffic Control and Safety Plan / Coordination with local Authorities	26d	100%	07-Jun-14 A	30-Sep-14 A																				
DUR2030	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level RHS	2d	100%	08-Jun-14 A	11-Jun-14 A																				
DUR2040	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level LHS	2d	100%	08-Jun-14 A	11-Jun-14 A																				
DUR2050	20 cm Thick Base Course- First Layer RHS	2d	100%	15-Jun-14 A	15-Jun-14 A																				
DUR2070	20 cm Thick Base Course- First Layer LHS	2d	100%	15-Jun-14 A	15-Jun-14 A																				
DUR2080	20 cm Thick Base Course- Second Layer RHS	2d	100%	16-Jun-14 A	16-Jun-14 A																				
DUR2090	20 cm Thick Base Course- Second Layer LHS	2d	100%	16-Jun-14 A	16-Jun-14 A																				
DUR2120	Concrete Curbstone and Side Walk	8d	100%	29-Jun-14 A	01-Oct-14 A																				
DUR2110	5 cm Asphalt Binder Course Including Prime Coat	2d	100%	22-Jul-14 A	22-Jul-14 A																				
DUR2130	Interlock works	5d	100%	14-Aug-14 A	01-Oct-14 A																				
DUR2150	Stone wall works at Round About -0+090 to 0+106 RHS	5d	100%	02-Sep-14 A	08-Sep-14 A																				
DUR2140	5 cm Asphalt Wearing Course Including Tack Coat	5d	100%	30-Sep-14 A	30-Sep-14 A																				
DUR2162-new	Handrail	5d	100%	29-Oct-14 A	02-Nov-14 A																				
<b>Phase #4 Milling and asphalt re-surfacing for Dura Main Road (Al Fawwar) with Lm 600 m.</b>																									
DUR2450-new	Milling for existing Asphalt up to 40 mm.	4d	100%	23-Dec-14 A	24-Dec-14 A																				
DUR2410-new	Asphalt leveling where required.	2d	100%	27-Dec-14 A	30-Dec-14 A																				
DUR2420-new	Furnish 70 mm Asphalt wearing course Including Tack coat	2d	100%	27-Dec-14 A	30-Dec-14 A																				
DUR2440-new	Asphalt patching where required.	2d	100%	27-Dec-14 A	30-Dec-14 A																				
<b>Phase #5 Reinstatement of existing road @drainage outfall route from st.0+300 RHS(ALMa'sarah)lm 150</b>																									
DUR2460-new	Road Excavation Including (Cut/Fill) to the required sub grade levels	4d	100%	27-Dec-14 A	03-Jan-15 A																				





















Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float	2014												2015					
							Qtr 4		Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1		Qtr 2	
							Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
<b>Implement Traffic Control</b>							7d																	
BTH0100	Start Implement Traffic Control	7d	100%	03-Nov-13 A	02-Jan-14 A		[Gantt bar from Nov to Dec 2014]																	
<b>Phase#1 Segment A Hebron Jerusalem Road</b>							168d																	
<b>Hebron Jerusalem Road RHS</b>							168d																	
BTH0460	Implement traffic control & safety Plan /Coordination with local Authorities	31d	100%	31-Dec-13 A	04-Mar-14 A		[Gantt bar from Dec 2014 to Mar 2015]																	
BTH0470	Milling	3d	100%	03-Jan-14 A	12-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0500	Asphalt Patching and Leveling Course	8d	100%	18-Jan-14 A	23-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0480	Saw Cut Existing Asphalt, Road Excavation, Backfill, Base Course Layer for patching	10d	100%	18-Jan-14 A	26-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0520	5 cm Asphalt Wearing Course Including Tack Coat or Prime Coat	3d	100%	20-Jan-14 A	23-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0490	Curbstone	10d	100%	21-Jan-14 A	22-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0515	Manhole adjustment	2d	100%	23-Jan-14 A	23-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0510	Interlock Block, Concrete work for ramps and sidewalks	7d	100%	03-Feb-14 A	03-Feb-14 A		[Gantt bar in Feb 2014]																	
BTH0525	Thermoplastic painting, Cat eyes & traffic signs	10d	100%	01-Mar-14 A	01-May-14 A		[Gantt bar from Mar to May 2014]																	
BTH0535-new	Install new Hand Rail	5d	100%	10-Apr-14 A	13-Apr-14 A		[Gantt bar in Apr 2014]																	
<b>Hebron Jerusalem Road LHS</b>							84d																	
BTH0530	Implement traffic control & safety Plan /Coordination with local Authorities	31d	100%	09-Nov-13 A	04-Mar-14 A		[Gantt bar from Nov 2014 to Mar 2015]																	
BTH0540	Milling	3d	100%	12-Jan-14 A	14-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0550	Saw Cut Existing Asphalt, Road Excavation, Backfill, Base Course Layer for patching	10d	100%	18-Jan-14 A	19-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0560	Curbstone	10d	100%	22-Jan-14 A	25-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0570	Asphalt Patching and Leveling Course	8d	100%	23-Jan-14 A	27-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0590	5 cm Asphalt Wearing Course Including Tack Coat or Prime Coat	3d	100%	23-Jan-14 A	27-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0585	Manhole adjustment	2d	100%	23-Jan-14 A	26-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0580	Interlock Block, Concrete work for ramps and sidewalks	7d	100%	03-Feb-14 A	22-Feb-14 A		[Gantt bar in Feb 2014]																	
BTH0595	Thermoplastic painting, Cat eyes & traffic signs	10d	100%	01-Mar-14 A	01-May-14 A		[Gantt bar from Mar to May 2014]																	
BTH0596-new	Install new Hand Rail	5d	100%	10-Apr-14 A	13-Apr-14 A		[Gantt bar in Apr 2014]																	
<b>Phase#2 Segment B Bethlehem Internal Roads</b>							190d																	
<b>Wadi Ma'ali Road (1560 M)</b>							105d																	
BTH0600	Implement traffic control & safety Plan /Coordination with local Authorities	28d	100%	14-Jan-14 A	03-May-14 A		[Gantt bar from Jan to May 2014]																	
BTH0610	Milling	2d	100%	15-Jan-14 A	16-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0645	Manhole adjustment	2d	100%	15-Jan-14 A	21-Mar-14 A		[Gantt bar from Jan to Mar 2014]																	
BTH0640	Asphalt Patching and Leveling Course	7d	100%	23-Jan-14 A	24-Mar-14 A		[Gantt bar from Jan to Mar 2014]																	
BTH0620	Saw Cut Existing Asphalt, Road Excavation, Backfill, Base Course Layer for patching	8d	100%	24-Jan-14 A	24-Jan-14 A		[Gantt bar in Jan 2014]																	
BTH0660	5 cm Asphalt Wearing Course Including Tack Coat or Prime Coat	2d	100%	25-Jan-14 A	24-Mar-14 A		[Gantt bar from Jan to Mar 2014]																	










# C | Progress S-Curve Versus Actual

Construction Progress S-Curve

Total Contract Value: \$ 12,259,300  
 Total Contract Value (VO10-BL3): \$ 12,043,425  
 Total Contract Value (Without Day work): \$ 11,759,300  
 Total Contract Value (VO12-BL4): \$ 11,997,749.5  
 Total Contract Value (VO15): \$ 12,135,877.1  
 Project Duration : 365 Calendar Days  
 Time Extension 139 Calendar Days  
 Revised Project Duration : 504 Calendar Days  
 NTP Date: 1-Nov-13

\* Day Work Not Included

	November. 2013	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	June. 2014	July. 2014	August. 2014	September. 2014	October. 2014	November. 2014	December. 2014	January. 2015	February. 2015	March. 2015	TOTAL
Planned Value (Baseline3)	\$ 230,744	\$ 195,822	\$ 505,070	\$ 250,813	\$ 959,828	\$ 700,376	\$ 314,171	\$ 900,832	\$ 962,731	\$ 734,230	\$ 1,364,227	\$ 719,148	\$ 824,207	\$ 2,531,263	\$ 849,963			\$ 12,043,425
Planned Value (CUM)	\$ 230,744	\$ 426,566	\$ 931,636	\$ 1,182,449	\$ 2,142,277	\$ 2,842,653	\$ 3,156,824	\$ 4,057,656	\$ 5,020,387	\$ 5,754,617	\$ 7,118,844	\$ 7,837,992	\$ 8,662,199	\$ 11,193,462	\$ 12,043,425			
% Planned	1.9%	1.6%	4.2%	2.1%	8.0%	5.8%	2.6%	7.5%	8.0%	6.1%	11.3%	6.0%	6.8%	21.0%	7.1%	0.0%	0.0%	100%
% Planned (CUM) BL3	1.9%	3.5%	7.7%	9.8%	17.8%	23.6%	26.2%	33.7%	41.7%	47.8%	59.1%	65.1%	71.9%	92.9%	100.0%	100.0%	100.0%	
Planned Value (Baseline4)	\$ 230,744	\$ 195,822	\$ 505,070	\$ 250,813	\$ 959,828	\$ 700,376	\$ 314,171	\$ 900,832	\$ 962,731	\$ 734,230	\$ 1,364,227	\$ 719,148	\$ 595,847	\$ 951,469	\$ 762,970	\$ 1,849,472		\$ 11,997,750
Planned Value (CUM)	\$ 230,744	\$ 426,566	\$ 931,636	\$ 1,182,449	\$ 2,142,277	\$ 2,842,653	\$ 3,156,824	\$ 4,057,656	\$ 5,020,387	\$ 5,754,617	\$ 7,118,844	\$ 7,837,992	\$ 8,433,839	\$ 9,385,308	\$ 10,148,278	\$ 11,997,750	\$ 11,997,750	
% Planned	1.9%	1.6%	4.2%	2.1%	8.0%	5.8%	2.6%	7.5%	8.0%	6.1%	11.4%	6.0%	5.0%	7.9%	6.4%	15.4%	0.0%	100.00%
% Planned (CUM) BL4	1.9%	3.6%	7.8%	9.9%	17.9%	23.7%	26.3%	33.8%	41.8%	48.0%	59.3%	65.3%	70.3%	78.2%	84.6%	100.0%	100.0%	
Actual Value	\$ 230,744	\$ 195,822	\$ 505,070	\$ 250,813	\$ 959,828	\$ 700,376	\$ 314,171	\$ 900,832	\$ 962,731	\$ 734,230	\$ 1,364,227	\$ 719,148	\$ 595,847	\$ 951,469	\$ 618,070	\$ 593,042	\$ 1,539,457	\$ 12,135,877.1
Actual Value (CUM)	\$ 230,744	\$ 426,566	\$ 931,636	\$ 1,182,449	\$ 2,142,277	\$ 2,842,653	\$ 3,156,824	\$ 4,057,656	\$ 5,020,387	\$ 5,754,617	\$ 7,118,844	\$ 7,837,992	\$ 8,433,839	\$ 9,385,308	\$ 10,003,378	\$ 10,596,420	\$ 12,135,877	
% Actual	1.9%	1.6%	4.2%	2.1%	7.9%	5.8%	2.6%	7.4%	7.9%	6.1%	11.2%	5.9%	4.9%	7.8%	5.1%	4.9%	12.7%	100.0%
% Actual (CUM)	1.9%	3.5%	7.7%	9.7%	17.7%	23.4%	26.0%	33.4%	41.4%	47.4%	58.7%	64.6%	69.5%	77.3%	82.4%	87.3%	100.0%	

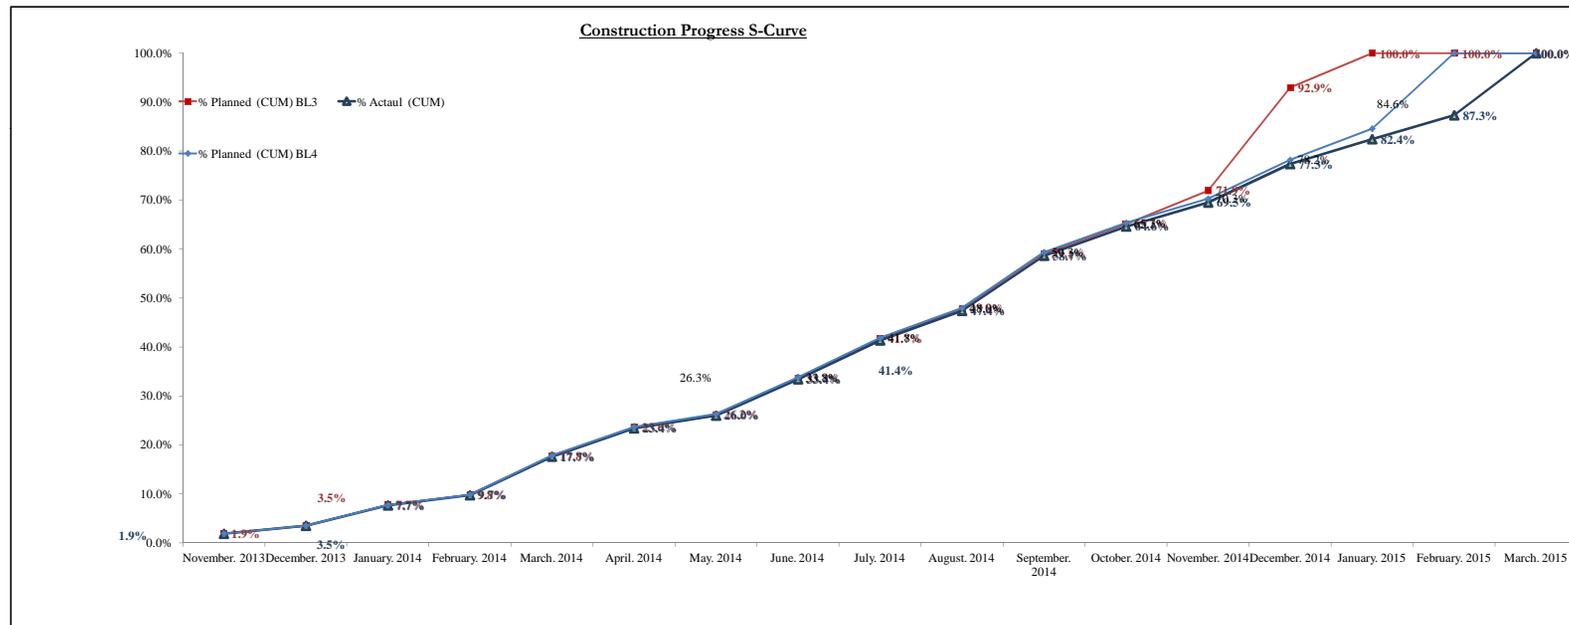


Construction Progress S-Curve

Total Contract Value (Original): \$ 8,243,912  
 Total Contract Value (VO12): \$ 7,951,892  
 Total Contract Value (VO15): \$ 8,090,019  
 Project Duration : 365 Calendar Days  
 Time Extension 139 Calendar Days  
 Revised Project Duration : 504 Calendar Days  
 NTP Date: 1-Nov-13

\* Day Work Not Included

	November. 2013	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	June. 2014	July. 2014	August. 2014	September. 2014	October. 2014	November. 2014	December. 2014	January. 2015	February. 2015	March. 2015	TOTAL	
Planned Value (Baseline1)	\$289,896	\$29,107	\$175,588	\$298,310	\$599,458	\$679,641	\$1,103,496	\$1,150,109	\$338,527	\$924,351	\$751,703	\$1,903,726							\$8,243,912
Planned Value (CUM)	\$289,896	\$319,003	\$494,590	\$792,900	\$1,392,359	\$2,071,999	\$3,175,495	\$4,325,605	\$4,664,132	\$5,588,482	\$6,340,186	\$8,243,912	\$8,243,912	\$8,243,912	\$8,243,912	\$8,243,912	\$8,243,912	\$8,243,912	\$8,243,912
% Planned	3.5%	0.4%	2.1%	3.6%	7.3%	8.2%	13.4%	14.0%	4.1%	11.2%	9.1%	23.1%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	100%
% Planned (CUM) BL1	3.5%	3.9%	6.0%	9.6%	16.9%	25.1%	38.5%	52.5%	56.6%	67.8%	76.9%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%	100.0%
Planned Value (Baseline4)	\$ 161,915	\$ 124,722	\$ 79,917	\$ 59,652	\$ 180,256	\$ 329,508	\$ 111,638	\$ 575,630	\$ 374,358	\$ 381,499	\$ 679,830	\$ 733,209	\$ 595,847	\$ 951,469	\$ 762,970	\$ 1,849,472	\$ -	\$ -	\$ 7,951,892
Planned Value (CUM)	\$ 161,915	\$ 286,637	\$ 366,554	\$ 426,206	\$ 606,462	\$ 935,970	\$ 1,047,608	\$ 1,623,238	\$ 1,997,596	\$ 2,379,095	\$ 3,058,925	\$ 3,792,134	\$ 4,387,981	\$ 5,339,450	\$ 6,102,420	\$ 7,951,892	\$ 7,951,892	\$ 7,951,892	\$ 7,951,892
% Planned	2.0%	1.6%	1.0%	0.8%	2.3%	4.1%	1.4%	7.2%	4.7%	4.8%	8.5%	9.2%	7.5%	12.0%	9.6%	23.3%	0.0%	0.0%	100.00%
% Planned (CUM) BL4	2.0%	3.6%	4.6%	5.4%	7.6%	11.8%	13.2%	20.4%	25.1%	29.9%	38.5%	47.7%	55.2%	67.1%	76.7%	100.0%	100.0%	100.0%	100.0%
Actual Value	\$ 161,915	\$ 124,722	\$ 79,917	\$ 59,652	\$ 180,256	\$ 329,508	\$ 111,638	\$ 575,630	\$ 374,358	\$ 381,499	\$ 679,830	\$ 733,209	\$ 595,847	\$ 951,469	\$ 618,070	\$ 593,042	\$ 1,539,457	\$ -	\$ 8,090,019
Actual Value (CUM)	\$ 161,915	\$ 286,637	\$ 366,554	\$ 426,206	\$ 606,462	\$ 935,970	\$ 1,047,608	\$ 1,623,238	\$ 1,997,596	\$ 2,379,095	\$ 3,058,925	\$ 3,792,134	\$ 4,387,981	\$ 5,339,450	\$ 5,957,520	\$ 6,550,562	\$ 8,090,019	\$ -	\$ 8,090,019
% Actual	2.0%	1.5%	1.0%	0.7%	2.2%	4.1%	1.4%	7.1%	4.6%	4.7%	8.4%	9.1%	7.4%	11.8%	7.6%	7.3%	19.0%	0.0%	100.0%
% Actual (CUM)	2.0%	3.3%	4.5%	5.3%	7.5%	11.6%	12.9%	20.1%	24.7%	29.4%	37.8%	46.9%	54.2%	66.0%	73.6%	81.0%	100.0%	100.0%	100.0%

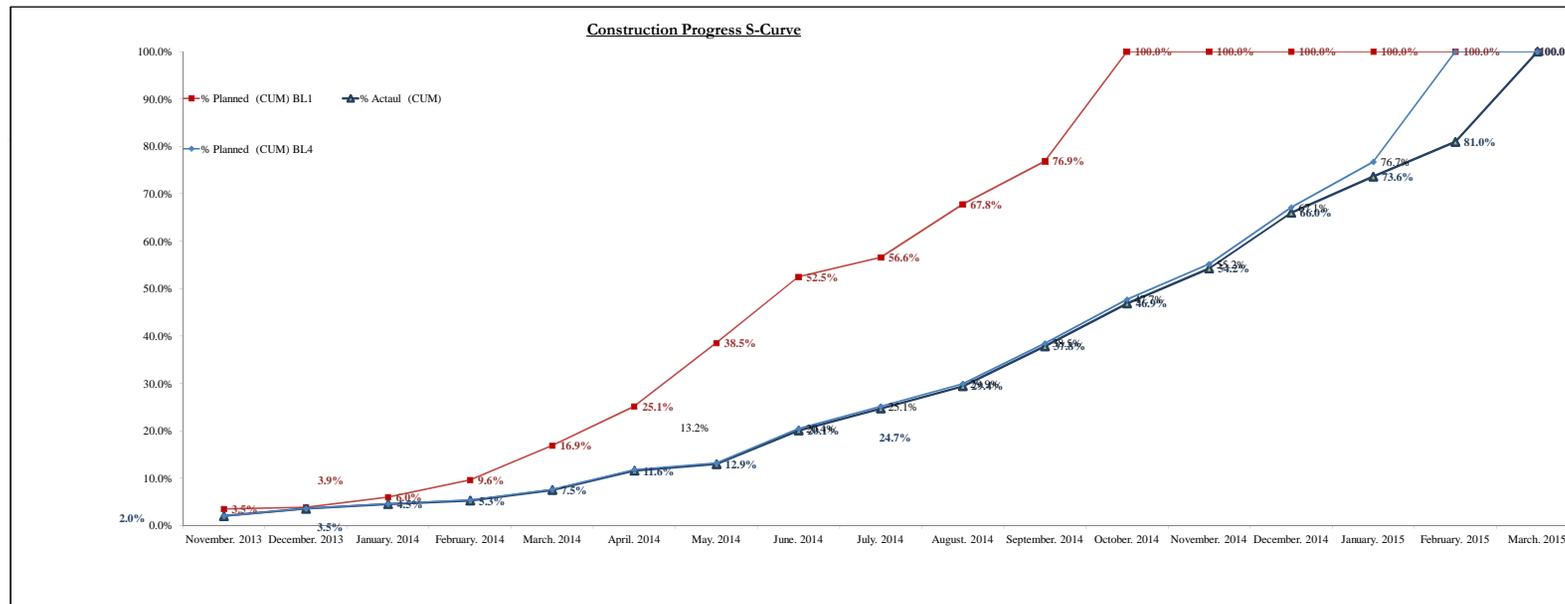


### Construction Progress S-Curve

Total Contract Value (Original): \$ 2,240,867  
 Total Contract Value (VO6): \$ 2,584,871  
 Total Contract Value (VO9): \$ 2,760,036  
 Project Duration : 270 Calender Days  
 Time Extension 62 Calender Days  
 Revised Project Duration : 332 Calender Days  
 NTP Date: 1-Nov-13

**\* Day Work Not Included**

	November. 2013	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	June. 2014	July. 2014	August. 2014	September. 2014	TOTAL
Planned Value (Baseline1)	\$ 81,952	\$ 6,678	\$ 62,080	\$ 198,262	\$ 252,794	\$ 374,920	\$ 464,511	\$ 402,516	\$ 397,154			\$2,240,867
Planned Value (CUM)	\$ 81,952	\$ 88,630	\$ 150,711	\$ 348,972	\$ 601,766	\$ 976,687	\$ 1,441,198	\$ 1,843,713	\$ 2,240,867	\$ 1,843,713	\$ 2,240,867	
% Planned	3.7%	0.3%	2.8%	8.8%	11.3%	16.7%	20.7%	18.0%	17.7%	0.0%	0.0%	100%
% Planned (CUM) BL1	3.7%	4.0%	6.7%	15.6%	26.9%	43.6%	64.3%	82.3%	100.0%	100.0%	100.0%	
Planned Value (Baseline3)	\$ 43,915	\$ 35,078	\$ 66,673	\$ 136,047	\$ 183,314	\$ 190,826	\$ 167,541	\$ 325,202	\$ 588,374	\$ 352,730	\$ 495,171	\$ 2,584,871
Planned Value (CUM)	\$ 43,915	\$ 78,993	\$ 145,666	\$ 281,713	\$ 465,027	\$ 655,853	\$ 823,394	\$ 1,148,596	\$ 1,736,970	\$ 2,089,700	\$ 2,584,871	
% Planned	1.7%	1.4%	2.6%	5.3%	7.1%	7.4%	6.5%	12.6%	22.8%	13.6%	19.2%	100.00%
% Planned (CUM) BL3	1.7%	3.1%	5.6%	10.9%	18.0%	25.4%	31.9%	44.4%	67.2%	80.8%	100.0%	
Actual Value	\$ 43,915	\$ 35,078	\$ 66,673	\$ 136,047	\$ 183,314	\$ 190,826	\$ 167,541	\$ 325,202	\$ 588,374	\$ 352,730	\$ 670,336	\$ 2,760,036
Actual Value (CUM)	\$ 43,915	\$ 78,993	\$ 145,666	\$ 281,713	\$ 465,027	\$ 655,853	\$ 823,394	\$ 1,148,596	\$ 1,736,970	\$ 2,089,700	\$ 2,760,036	
% Actual	1.6%	1.3%	2.4%	4.9%	6.6%	6.9%	6.1%	11.8%	21.3%	12.8%	24.3%	100.0%
% Actual (CUM)	1.6%	2.9%	5.3%	10.2%	16.8%	23.8%	29.8%	41.6%	62.9%	75.7%	100.0%	

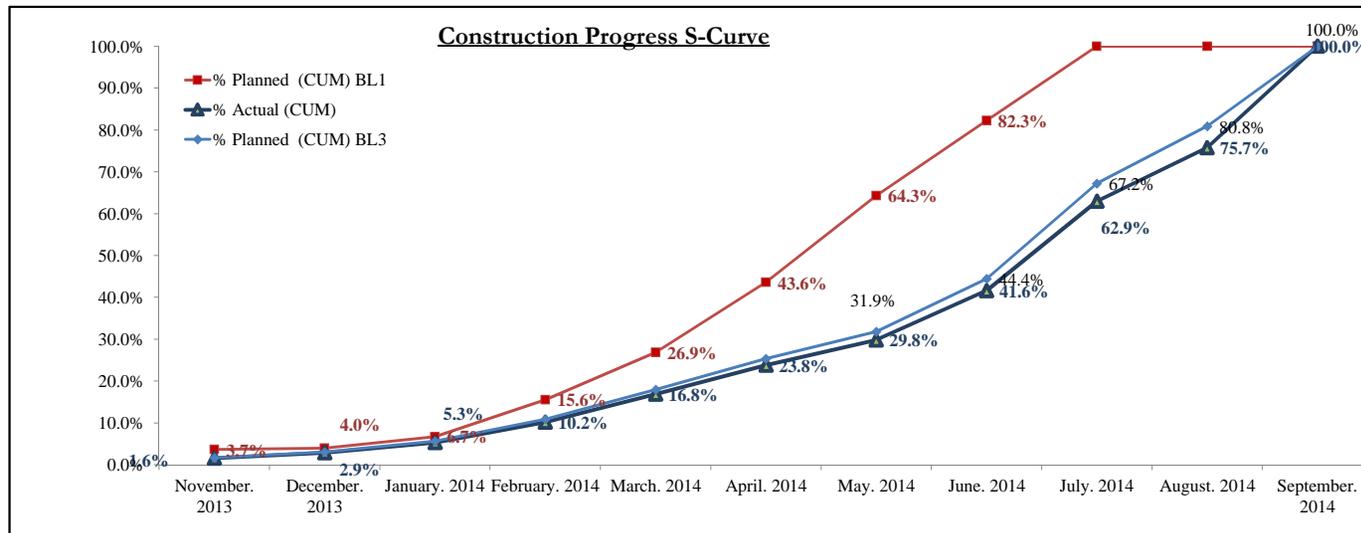


**PROJECT 03 Milling and Overlay of Bethlehem Internal Roads**

**Construction Progress S-Curve**

Total Contract Value (Original): \$ 1,274,521  
 Total Contract Value (VO4): \$ 1,285,822  
 Project Duration : 180 Calender Days  
 Time Extension 7 Calender Days  
 Revised Project Duration : 187 Calender Days  
 NTP Date: 1-Nov-13  
 \* Day Work Not Included

	November. 2013	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	TOTAL
Planned Value (Baseline1)	\$ 44,818	\$ 14,715	\$ 259,528	\$ 323,996	\$ 310,815	\$ 320,649		\$1,274,521
Planned Value (CUM)	\$ 44,818	\$ 59,533	\$ 319,061	\$ 643,057	\$ 953,872	\$ 1,274,521	\$ 1,274,521	
% Planned	3.5%	1.2%	20.4%	25.4%	24.4%	25.2%	0.0%	100%
% Planned (CUM) BL1	3.5%	4.7%	25.0%	50.5%	74.8%	100.0%	100.0%	
Planned Value (Baseline2)	\$ 24,915	\$ 36,022	\$ 358,479	\$ 55,114	\$ 596,258	\$ 180,043	\$ 34,991	\$ 1,285,822
Planned Value (CUM)	\$ 24,915	\$ 60,937	\$ 419,416	\$ 474,530	\$ 1,070,788	\$ 1,250,831	\$ 1,285,822	
% Planned	1.9%	2.8%	27.9%	4.3%	46.4%	14.0%	2.7%	100.00%
% Planned (CUM) BL2	1.9%	4.7%	32.6%	36.9%	83.3%	97.3%	100.0%	
Actual Value	\$ 24,915	\$ 36,022	\$ 358,479	\$ 55,114	\$ 596,258	\$ 180,043	\$ 34,991	\$ 1,285,822
Actual Value (CUM)	\$ 24,915	\$ 60,937	\$ 419,416	\$ 474,530	\$ 1,070,788	\$ 1,250,831	\$ 1,285,822	
% Actual	1.9%	2.8%	27.9%	4.3%	46.4%	14.0%	2.7%	100.0%
% Actual (CUM)	1.9%	4.7%	32.6%	36.9%	83.3%	97.3%	100.0%	

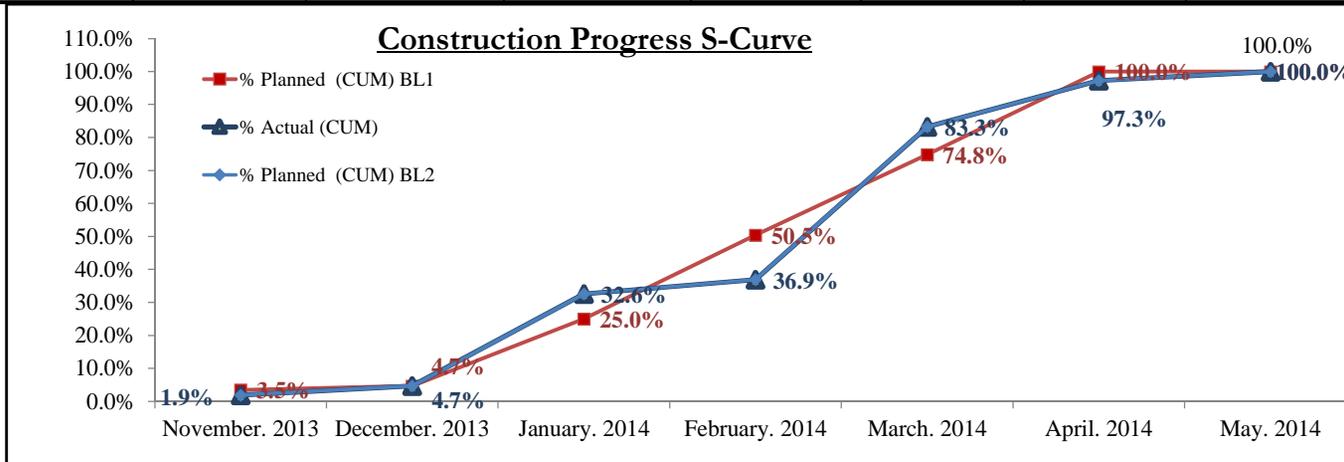

## **D | Site Memos Log**

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (E-C)**



SUBMITTAL				TRACKING DATES	Remarks
Spec. No.	Site Memo No.	Subject	Project	Submitted on (M/D/Y)	
	SM-13-00012-BTH-E-C-001	Project 03-BTH-Milling & Overlay of Bethlehem Internal Roads-New Project Layout	BTH	12/22/13	Site Instruction
	SM-13-00012-DUR-E-C-002	Increase the Carriageway Lane	DUR	12/30/13	Site Instruction
	SM-13-00012-DUR-E-C-003	Dura-Hebron (Sinjir) Road-Project 01-Detour Safety Enhancement	DUR	01/13/14	Site Instruction
	SM-13-00012-SAM-E-C-004	Rising the PGL in Project 02-AL Samua' Yatta Road	SAM	01/14/14	Site Instruction
	SM-13-00012-DUR-E-C-005	Water Pipeline at Project 01-Dura-Hebron (Sinjir) Road	DUR	01/14/14	Site Instruction
	SM-13-00012-BTH-E-C-006	Asphalt Finish Quality at Project No.3-BTH	BTH	01/28/14	Record of Unsatisfactory Work Practice
	SM-13-00012-SAM-E-C-007	Establishing Parking Area from St.0+150 to St.0+260 RHS at Project No.2-SAM	SAM	01/28/14	Site Instruction
	SM-13-00012-DUR-E-C-008	Water Pipeline at Project 01-Dura-Hebron (Sinjir) Road	DUR	01/30/14	Other
	SM-13-00012-BTH-E-C-009	Plan & Profile of the Intersection at St.1+020 of Wadi Ma'ali Road	BTH	01/30/14	Site Instruction
	SM-13-00012-BTH-E-C-010	Road Widening at AL Dibs Road-Project 03	BTH	02/05/14	Site Instruction
	SM-13-00012-BTH-E-C-011	Reconstruction of AL Qeta'a Road-Project 03	BTH	02/05/14	Site Instruction
	SM-13-00012-DUR-E-C-012	Existing Water Network Repair-Project 01	DUR	02/12/14	Record of Unsatisfactory Work Practice
	SM-13-00012-DUR-E-C-013	Relocation of Existing Utilities Poles	DUR	02/12/14	Site Instruction
	SM-13-00012-BTH-E-C-014	AL Dibs Road at St.0+150 RHS-Existing Grotto (Cave) within the Carriage Way at Project No.3	BTH	02/12/14	Site Instruction
	SM-13-00012-BTH-E-C-015	Asphalt Crack Sealing at Project 03	BTH	02/12/14	Site Instruction
	SM-13-00012-SAM-E-C-016	Stone Wall Location related to Road Centerline at Project 02	SAM	02/16/14	Site Instruction
	SM-13-00012-BTH-E-C-017	AL Dibs Road at St.0+150 RHS-Existing Grotto (Cave) within the Carriage Way at Project No.3	BTH	02/16/14	Site Instruction
	SM-13-00012-DUR-E-C-018	Storm Water Manhole Cover-Project 01	DUR	02/16/14	Site Instruction
	SM-13-00012-BTH-E-C-019	Road Section Between AL Shepherd & AL Dibs Road at Project 03	BTH	02/16/14	Site Instruction
	SM-13-00012-BTH-E-C-020	Festival Yard in Beit Sahour at Project 03	BTH	02/17/14	Site Instruction
	SM-13-00012-DUR-E-C-021	Site Memo regarding Soil Classification Below Sub-grade Level from St.0+030 to St.0+280	DUR	02/18/14	Site Instruction
	SM-13-00012-BTH-E-C-022	Punch List for Hebron-Jerusalem Road at Project 03	BTH	02/19/14	Site Instruction
	SM-13-00012-SAM-E-C-023	Pipe Culvert at Sta.A0+280 at Project 02	SAM	02/20/14	Site Instruction
	SM-13-00012-BTH-E-C-024	Unsatisfactory Work of Asphalt Wearing layer at Wadi Ma'ali Road at Project 03	BTH	03/03/14	Record of Unsatisfactory Work Practice
	SM-13-00012-BTH-E-C-025	Response to Your "Notice of Unsafe Condition Correction at Project 03"	BTH	03/04/14	Other
	SM-13-00012-DUR-E-C-026	Reconstruct of Existing Wall from Sta.0+192 to Sta.0+210 RHS at Project 01	DUR	03/09/14	Site Instruction

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (E-C)**



SUBMITTAL				TRACKING DATES	Remarks
Spec. No.	Site Memo No.	Subject	Project	Submitted on (M/D/Y)	
	SM-13-00012-SAM-E-C-027	Layout of Parking Lot from Sta.A0+150 to Sta.A0+260 RHS at Project 02	SAM	03/10/14	Other
	SM-13-00012-BTH-E-C-028	Layout of medians of Al Sha'eb Intersection at Project 03	BTH	03/17/14	Site Instruction
	SM-13-00012-BTH-E-C-029	Galvanized Steel Handrail at Project 03	BTH	03/19/14	Site Instruction
	SM-13-00012-SAM-E-C-030	Replacing Existing Culvert at Sta.A0+770 at Project 02	SAM	03/23/14	Site Instruction
	SM-13-00012-SAM-E-C-031	Installation of 6" Future Ducts at Project 02	SAM	03/23/14	Site Instruction
	SM-13-00012-DUR-E-C-032	Construction of Concrete Sheet at Project 01	DUR	04/01/14	Site Instruction
	SM-13-00012-SAM-E-C-033	Shifting the Center Line at Project 02	SAM	04/01/14	Site Instruction
	SM-13-00012-BTH-E-C-034	Casting Concrete Over Trench at Project 03	BTH	04/01/14	Site Instruction
	SM-13-00012-BTH-E-C-035	Construction of Concrete Wall Beside Al Eain Building at Project 03	BTH	04/07/14	Site Instruction
	SM-13-00012-BTH-E-C-036	Asphalt Crack Repair in Hebron Jerusalem Road at Project 03	BTH	04/07/14	Site Instruction
	SM-13-00012-DUR-E-C-037	Unacceptable Concrete Finish of Retaining Wall from Sta.0+444 to Sta.0+474 RHS at Project 01	DUR	04/09/14	Record of Non Quality Compliance
	SM-13-00012-DUR-E-C-038	Construction of Concrete Steps Works at Project 01	DUR	04/09/14	Site Instruction
	SM-13-00012-BTH-E-C-039	Additional Works at Project 03	BTH	04/10/14	Site Instruction
	SM-13-00012-DUR-E-C-040	Asphalt Pavement Layers from Sta.0+000 to Sta.0+280 at Project 01	DUR	04/10/14	Site Instruction
	SM-13-00012-MRSII-E-C-041	Office Security Personnel at MRSII	MRSII	04/10/14	Site Instruction
	SM-13-00012-BTH-E-C-042	Side Walk from Sta.0+105 to Sta.0+148 RHS -Al Qeta'a Road at Project 03	BTH	04/15/14	Site Instruction
	SM-13-00012-BTH-E-C-043	Initial Punch List For Some Roads at Project #03	BTH	04/16/14	Site Instruction
	SM-13-00012-BTH-E-C-044	initial Punch List For Some Roads at Project #03	BTH	04/16/14	Site Instruction
	SM-13-00012-DUR-E-C-045	Construction of Concrete Walls at Project 01	DUR	04/23/14	Site Instruction
	SM-13-00012-DUR-E-C-046	Joint Walkthrough from Sta.0+060 to Sta.0+280 at Project 01	DUR	04/29/14	Record of Joint Walkthrough
	SM-13-00012-DUR-E-C-047	Construction of Stone Wall at Project # 01	DUR	04/30/14	Site Instruction
	SM-13-00012-BTH-E-C-048	Initial Punch List for Roads at Project #03	BTH	04/30/14	Site Instruction
	SM-13-00012-DUR-E-C-049	Existing Damaged Septic Tank at Sta.0+450 LHS at Project 01	DUR	05/11/14	Site Instruction
	SM-13-00012-DUR-E-C-050	Protection of Water Pipelines and Road Structural Layer from Seepage Septic Tank at Project 01	DUR	05/15/14	Site Instruction
	SM-13-00012-BTH-E-C-051	Asphalt Repair -Punch List at Project 03	BTH	05/18/14	Site Instruction
	SM-13-00012-DUR-E-C-052	Slow Rate of Progress causing Public disruption at Project 01	DUR	05/18/14	Site Instruction
	SM-13-00012-SAM-E-C-053	Construction of New Boulder Wall at Project 02	SAM	05/18/14	Site Instruction
	SM-13-00012-SAM-E-C-054	Construction of 4" Water Pipeline at Project 02	SAM	05/18/14	Site Instruction
	SM-13-00012-DUR-E-C-055	Proposed Roundabout 's Details at Project 01	DUR	05/18/14	Site Instruction
	SM-13-00012-DUR-E-C-056	Construction of Concrete Walls at Project 01	DUR	05/20/14	Site Instruction
	SM-13-00012-DUR-E-C-057	Unsafe Condition at Project 01	DUR	05/26/14	Record of Unsatisfactory Work

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (E-C)**



SUBMITTAL				TRACKING DATES	Remarks
Spec. No.	Site Memo No.	Subject	Project	Submitted on (M/D/Y)	
	SM-13-00012-DUR-E-C-058	Letter from Dura Municipality -Providing Local People with Potable Water at Project 01	DUR	06/09/14	Site Instruction
	SM-13-00012-DUR-E-C-059	Response to Contractor Site Memo SM-13-00012-DUR-C-E-028 at Project 01	DUR	06/10/14	Site Instruction
	SM-13-00012-DUR-E-C-060	Retaining Wall from Sta.0+988 to Sta.1+010 RHS at Project 01	DUR	06/10/14	Site Instruction
	SM-13-00012-DUR-E-C-061	Unsatisfactory Work Practice / Non Quality Compliance for Concrete works - Median at Project 01	DUR	06/18/14	Record of Non Quality Compliance
	SM-13-00012-SAM-E-C-062	Intersection at Sta.A0+000 Project 02	SAM	06/18/14	Site Instruction
	SM-13-00012-SAM-E-C-063	Additional Works at Project 02	SAM	06/22/14	Site Instruction
	SM-13-00012-DUR-E-C-064	Joint Walkthrough from Sta.3+200 to Sta.3+500 at Project 01	DUR	06/22/14	Record of Joint Walkthrough
	SM-13-00012-DUR-E-C-065	Joint Walkthrough from Sta.3+500 to Sta.4+040 at Project 01	DUR	06/22/14	Record of Joint Walkthrough
	SM-13-00012-DUR-E-C-066	Response to Contractor Site Memo SM-13-00012-DUR-C-E-033 at Project 01	DUR	06/24/14	Other
	SM-13-00012-DUR-E-C-067	Traffic Plan at Project 01	DUR	06/30/14	Site Instruction
	SM-13-00012-DUR-E-C-068	Letters from Dura Municipality -Repair Old Water Pipelines at Project 01	DUR	07/02/14	Site Instruction
	SM-13-00012-DUR-E-C-069	Response to Contractors' Site Memorandum -SM -13-00012-DUR-C-E-033 at Project 01	DUR	07/02/14	Site Instruction
	SM-13-00012-DUR-E-C-070	Construction of Interlocking Tiles Blocks instead of Landscaping Section at Project 01	DUR	07/03/14	Site Instruction
	SM-13-00012-SAM-E-C-071	Asphalt Quality for Segment from Sta.1+950 to Sta.1+990 LHS at Project 02	SAM	07/05/14	Record of Non Quality Compliance
	SM-13-00012-DUR-E-C-072	Night Shift Working Plan at Project 01	DUR	07/06/14	Site Instruction
	SM-13-00012-DUR-E-C-073	Public Inconvenience at Project 01	DUR	07/09/14	Site Instruction
	SM-13-00012-DUR-E-C-074	Installation of 2" and 6" water Pipelines from Sta.1+250 to Sta.1+460 -Project 01	DUR	07/09/14	Record of Non Quality Compliance
	SM-13-00012-DUR-E-C-075	Water Issues at Project #01	DUR	07/09/14	Site Instruction
	SM-13-00012-DUR-E-C-076	Letter from Dura Municipality at Project 01	DUR	07/10/14	Site Instruction
	SM-13-00012-DUR-E-C-077	Record of Unsafe Condition- Poor Safety Measures at Project #01	DUR	07/16/14	Record of Unsafe Condition
	SM-13-00012-DUR-E-C-078	Water Outage and Damaging of the Existing Water Pipeline at Project # 01	DUR	07/16/14	Site Instruction
	SM-13-00012-SAM-E-C-079	Asphalt Finish Quality for Segment from Sta.A0+960 & at Sta.A0+676 LHS at Project t#02	SAM	07/16/14	Site Instruction / Record of Non Quality Compliance
	SM-13-00012-DUR-E-C-080	Changes in Trench Dimension for Water Pipes at Project # 01	DUR	07/16/14	Site Instruction
	SM-13-00012-DUR-E-C-081	Letters from Dura Municipality -Public Inconvenience at Project # 01	DUR	07/16/14	Site Instruction
	SM-13-00012-DUR-E-C-082	Letters from Dura Municipality -Public Inconvenience at Project # 01	DUR	07/20/14	Site Instruction

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (E-C)**



SUBMITTAL				TRACKING DATES	Remarks
Spec. No.	Site Memo No.	Subject	Project	Submitted on (M/D/Y)	
	SM-13-00012-DUR-E-C-083	Cutting Off the medium Voltage Cable at Project 01	DUR	07/20/14	Site Instruction
	SM-13-00012-SAM-E-C-084	Modified Scope of Work for Segment B at Project 02	SAM	07/20/14	Site Instruction
	SM-13-00012-DUR-E-C-085	Minutes of Meeting in Dura Municipality on July 07 ,2014 at Project 01	DUR	07/20/14	Site Instruction
	SM-13-00012-DUR-E-C-086	Responses of Contractor's Site Memo "SM-13-00012-DUR-C-E-038 " at Project 01	DUR	07/22/14	Site Instruction
	SM-13-00012-DUR-E-C-087	Responses of Contractor's Site Memo "SM-13-00012-DUR-C-E-040 " at Project 01	DUR	07/24/14	Other
	SM-13-00012-DUR-E-C-088	The Sources of Grill Cover for the Catch Basin at Project 01	DUR	07/27/14	Record of Non Quality Compliance
	SM-13-00012-DUR-E-C-089	Reponses to Contractors Site Memo "SM-13-00012-C-E-042" Project 01	DUR	07/27/14	Other
	SM-13-00012-DUR-E-C-090	Boulder Wall Detail at Sta.2+300 to Sta.2+360 at Project 01	DUR	08/13/14	Site Instruction
	SM-13-00012-DUR-E-C-091	Public Inconvenience at Project 01	DUR	08/14/14	Site Instruction
	SM-13-00012-SAM-E-C-092	Civil Works for Water Chamber at Project 02	SAM	08/17/14	Site Instruction
	SM-13-00012-DUR-E-C-093	Construction of Gravity Wall in lieu of Proposed Boulder Wall at Project 01	DUR	09/02/14	Site Instruction
	SM-13-00012-DUR-E-C-094	Defected Exiting Asphalt Layer at Outfall Direction at Sta.0+320 at Project 01	DUR	09/03/14	Record of Unsatisfactory Work Practice
	SM-13-00012-SAM-E-C-095	Concrete Finish for Pipe Crossing Head Walls at Project 02	SAM	09/03/14	Site Instruction
	SM-13-00012-SAM-E-C-096	Joint Walkthrough from Sta.A0+000 to Sta.A4+120 & from Sta.B 0+115 to Sta.B 0+320 at Project 02	SAM	09/07/14	Record of Joint Walkthrough
	SM-13-00012-DUR-E-C-097	Letter From Dura Municipality -Damaged Water Pipeline at Project 01	DUR	09/11/14	Site Instruction
	SM-13-00012-SAM-E-C-098	Initial Punch List at Project 02	SAM	09/11/14	Site Instruction
	SM-13-00012-SAM-E-C-099	Response to Contractor's Site Memo SM-13-00012-SAM-C-E-044 at Project 02	SAM	09/11/14	Site Instruction
	SM-13-00012-DUR-E-C-100	Letter from Dura Municipality at Project 01	DUR	09/14/14	Site Instruction
	SM-13-00012-SAM-E-C-101	Initial Punch List Segment A from Sta.A2+800 to Sta.A4+280 at Project 02	SAM	09/21/14	Site Instruction
	SM-13-00012-SAM-E-C-102	Manhole Covers at Project 02	SAM	09/23/14	Site Instruction
	SM-13-00012-DUR-E-C-103	Construction of 2" Water Pipeline and House Riser at Sta.0+300 at Project 01	DUR	09/30/14	Site Instruction
	SM-13-00012-DUR-E-C-104	Shifting the Road Center Line in Project 01	DUR	10/15/14	Site Instruction
	SM-13-00012-DUR-E-C-105	Remove and Reconstruct the Septic Tank at Sta.1+850 LHS at Project 01	DUR	10/15/14	Site Instruction
	SM-13-00012-DUR-E-C-106	Construction of Gravity Wall from Sta.3+308 to St.3+325 LHS at Project 01	DUR	10/19/14	Site Instruction

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (E-C)**



SUBMITTAL				TRACKING DATES	Remarks
Spec. No.	Site Memo No.	Subject	Project	Submitted on (M/D/Y)	
	SM-13-00012-DUR-E-C-107	Layout and Details for Intersection Landscape at Sta.0+300 at Project 01	DUR	10/28/14	Site Instruction
	SM-13-00012-DUR-E-C-108	Modifying the PGL for the section from Sta.2+310 to Sta.2+390 at Project 01	DUR	10/30/14	Site Instruction
	SM-13-00012-DUR-E-C-109	Installation of Handrail at Project 01	DUR	11/02/14	Site Instruction
	SM-13-00012-DUR-E-C-110	Design Drawings for the Retaining Wall from Sta.3+610 to Sta.3+656 LHS at Project 01	DUR	11/04/14	Site Instruction
	SM-13-00012-DUR-E-C-111	Base Width of the Gravity Walls at Project 01	DUR	11/12/14	Site Instruction
	SM-13-00012-DUR-E-C-112	Joint Walkthrough from Sta.0+000 to Sta.3+700 at Project 01	DUR	11/12/14	Record of Joint Walkthrough
	SM-13-00012-DUR-E-C-113	Letter from Dura Municipality- Water Pipelines at Project 01	DUR	11/17/14	Site Instruction
	SM-13-00012-DUR-E-C-114	Letter from Dura Municipality - Storm Water Drainage at Project 01	DUR	11/17/14	Site Instruction
	SM-13-00012-DUR-E-C-115	Detail for the wall section from Sta.3+632.80 to Sta. 3+649 LHS at Project 01	DUR	11/17/14	Site Instruction
	SM-13-00012-DUR-E-C-116	Remedy detail or the gravity wall from Sta.3+455 to Sta.3+474 LHS at Project #01	DUR	11/18/14	Site Instruction
	SM-13-00012-DUR-E-C-117	Garbage Containers Lay-by at Project #01	DUR	11/18/14	Site Instruction
	SM-13-00012-DUR-E-C-118	Letter from Dura Municipality at Project 01	DUR	11/26/14	Site Instruction
	SM-13-00012-DUR-E-C-119	Construction of Stair Flight for the house at Sta.0+760 RHS at Project 01	DUR	11/26/14	Site Instruction
	SM-13-00012-DUR-E-C-120	Replace the clay material A6-A7 by Topping material from Sta.3+100 to Sta.3+00 RHS at Project 01	DUR	11/26/14	Site Instruction
	SM-13-00012-DUR-E-C-121	Existing Dumped Material beside the Road from Sta.3+000 to Sta.3+240 LHS - Project 01	DUR	12/02/14	Site Instruction
	SM-13-00012-DUR-E-C-122	Additional Works at Project 01	DUR	12/09/14	Site Instruction
	SM-13-00012-DUR-E-C-123	Construction of Retaining Wall instead of Boulder Wall at Project # 01	DUR	12/16/14	Site Instruction
	SM-13-00012-DUR-E-C-124	Structural Details for Stair at Sta.3+375 LHS and at Sta.3+392 LHS at Project 01	DUR	12/28/14	Site Instruction
	SM-13-00012-DUR-E-C-125	Locations of Septic Tanks at Project 01	DUR	01/11/15	Site Instruction / Record of Joint Walkthrough
	SM-13-00012-DUR-E-C-126	Structural Details for Stair at Sta.3+339 LHS, at Sta.3+535 LHS and at Sta.3+459 LHS at Project 01	DUR	01/12/15	Site Instruction
	SM-13-00012-DUR-E-C-127	Quantity Calculation for Rubble Concrete at Project 01	DUR	01/15/15	Site Instruction
	SM-13-00012-DUR-E-C-128	Asphalt Quality for Segment from Sta.0+190 to Sta.0+870 RHS & LHS and Manhole covers at Project 01	DUR	01/21/15	Record of Non Quality Compliance
	SM-13-00012-DUR-E-C-129	Additional Works at Project 01	DUR	01/29/15	Site Instruction

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (E-C)**



<b>SUBMITTAL</b>				<b>TRACKING DATES</b>	
<b>Spec. No.</b>	<b>Site Memo No.</b>	<b>Subject</b>	<b>Project</b>	<b>Submitted on (M/D/Y)</b>	<b>Remarks</b>
	SM-13-00012-DUR-E-C-130	Response to Contractor's Site Memo SM-13-00012-DUR-C-E-049 at Project 01	DUR	02/10/15	Site Instruction
	SM-13-00012-DUR-E-C-131	Typical Detail for Side Road at Sta. 3+360 RHS at Project 01	DUR	02/18/15	Site Instruction
	SM-13-00012-DUR-E-C-132	Response to Contractor's Site Memo SM-13-00012-DUR-C-E-050 at Project 01	DUR	02/25/15	Site Instruction
	SM-13-00012-DUR-E-C-133	Response to Contractor's Site Memo SM-13-00012-DUR-C-E-052 at Project 01	DUR	03/11/15	Site Instruction
	SM-13-00012-DUR-E-C-134	Punch List at Project # 01	DUR	03/17/15	Site Instruction

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (C-E)**



SUBMITTAL				TRACKING DATES	Remarks
Spec. No.	Site Memo No.	Subject	Project	Submitted on (M/D/Y)	
	SM-13-00012-DUR-C-E-001	Water Pipe Line at Project No.1 Dura-Hebron (Sinjir) Road	DUR	01/20/14	Other
	SM-13-00012-BTH-C-E-002	Casting Reinforced Concrete B-250-Electrucity Trench-Project 03	BTH	01/22/14	Record of Verbal Site Instruction
	SM-13-00012-DUR-C-E-003	Obstruction in Dura-Hebron (Sinjir) Road-Project 01	DUR	01/27/14	Other
	SM-13-00012-SAM-C-E-004	Soil Classification of Sub-garde-A-7-Project 02	SAM	01/29/14	Other
	SM-13-00012-DUR-C-E-005	Soil Classification Below the Sub-grade Level From St.0+030 to St.0+280-Project 01	DUR	02/06/14	Other
	SM-13-00012-BTH-C-E-006	Al Dibs Road at St.0+150 RHS-Existing Grotto (Cave) within the Carriage Way-BTH	BTH	02/10/14	Other
	SM-13-00012-SAM-C-E-007	Limits of Sub-grade in Yatta-AL Samu' Road	SAM	02/10/14	Other
	SM-13-00012-BTH-C-E-008	Existing Trench at AL Qet'ah & AL Dibs Roads-Project 03	BTH	02/13/14	Other
	SM-13-00012-BTH-C-E-009	Additional Work in Bethlehem -Project 03	BTH	02/20/14	Record of Verbal Site Instruction
	SM-13-00012-BTH-C-E-010	Additional Asphalt Work in Bethlehem -Project 03	BTH	02/27/14	Record of Verbal Site Instruction
	SM-13-00012-DUR-C-E-011	Site Memo # 21-E-C-Dated February 18,2014-Project 01	DUR	03/02/14	Other
	SM-13-00012-DUR-C-E-012	Re-Location of Three Storm Water Manholes-Project 01	DUR	03/02/14	Other
	SM-13-00012-BTH-C-E-013	Obstacles in Wadi Ma'ali Road-Bethlehem-Project 03	BTH	03/10/14	Other
	SM-13-00012-SAM-C-E-014	Confirmation of Verbal Site Instruction -Project 02	SAM	03/10/14	Record of Verbal Site Instruction
	SM-13-00012-SAM-C-E-015	Reference to Site Memo #7 E to C -Project 02	SAM	03/10/14	Other
	SM-13-00012-SAM-C-E-016	Partially suspension of work-Project 02	SAM	03/17/14	Other
	SM-13-00012-BTH-C-E-017	Boundary Wall ,Al Dibis Road -Project 03	BTH	03/18/14	Other
	SM-13-00012-BTH-C-E-018	Hindering of works-Beit Sahour's Intersection -Project 03	BTH	03/18/14	Other
	SM-13-00012-BTH-C-E-019	Al Dibs Road Boundary Walls-BTH-Project 03	BTH	03/27/14	Other
	SM-13-00012-BTH-C-E-020	PWA and Bethlehem Municipality Water Lines Works in Al Quitta Road, Project 03	BTH	03/27/14	Other
	SM-13-00012-BTH-C-E-021	Existing Arch connection of Wadi Shaheen with Wadi Maali roads	BTH	04/06/14	Record of Verbal Site Instruction
	SM-13-00012-BTH-C-E-022	Replacement of Existing Sidewalk -Al Qet'a Road -Project 03	BTH	04/15/14	Record of Verbal Site Instruction
	SM-13-00012-DUR-C-E-023	Existing Damaged Septic Tank at Sta.0+450 LHS -Project 01	DUR	05/07/14	Other
	SM-13-00012-SAM-C-E-024	Side Slopes -RHS-Project 02	SAM	05/07/14	Record of Verbal Site Instruction
	SM-13-00012-DUR-C-E-025	CMC Response to RFI # 19	DUR	05/08/14	Other
	SM-13-00012-BTH-C-E-026	Asphalt Repair -Punch List -Project 03	BTH	05/11/14	Other

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT  
 Site Memo Log (C-E)**



SUBMITTAL				TRACKING DATES	Remarks
Spec. No.	Site Memo No.	Subject	Project	Submitted on (M/D/Y)	
	SM-13-00012-DUR-C-E-027	Side Walk from Sta.0+180 to Sta.0+240-Project 01	DUR	06/09/14	Other
	SM-13-00012-DUR-C-E-028	Median -Project 01	DUR	06/09/14	Other
	SM-13-00012-DUR-C-E-029	Retaining Wall from Sta.0+988 to Sta.1+010 RHS -Project 01	DUR	06/09/14	Other
	SM-13-00012-DUR-C-E-030	Gravity Wall at Sta.2+310 RHS -Project 01	DUR	06/10/14	Other
	SM-13-00012-DUR-C-E-031	Site Obstacles -Project 01	DUR	06/11/14	Other
	SM-13-00012-DUR-C-E-032	Site Obstacles -Project 01	DUR	06/22/14	Other
	SM-13-00012-DUR-C-E-033	SM-13-00012-DUR-E-C-064 -Project 01	DUR	06/23/14	Other
	SM-13-00012-DUR-C-E-034	Extending of Retaining Wall from Sta.1+600 to Sta.1+620 -Project 01	DUR	07/07/14	Other
	SM-13-00012-SAM-C-E-035	Installation of Curbstone -Project 02	SAM	07/07/14	Other
	SM-13-00012-SAM-C-E-036	Working at Segment B -Project 02	SAM	07/09/14	Other
	SM-13-00012-DUR-C-E-037	PALTEL-Project 01	DUR	07/10/14	Other
	SM-13-00012-DUR-C-E-038	Existing concrete wall from St.0+512 to St.0+545 RHS-Project 01	DUR	07/15/14	Other
	SM-13-00012-DUR-C-E-039	SM-13-00012-DUR-E-C-073 -Project 01	DUR	07/15/14	Other
	SM-13-00012-DUR-C-E-040	Coordination -Project 01	DUR	07/20/14	Other
	SM-13-00012-DUR-C-E-041	Work Activities in Dura till July 19,2014 -Project 01	DUR	07/20/14	Other
	SM-13-00012-DUR-C-E-042	Obstacles -Project 01	DUR	07/20/14	Other
	SM-13-00012-DUR-C-E-043	SM-13-00012-DUR-E-C-087 - Project 01	DUR	07/24/14	Other
	SM-13-00012-SAM-C-E-044	Asphalt Quality Remedey Plan -Project 02	SAM	08/26/14	Site Instruction
	SM-13-00012-SAM-C-E-045	TO 12- Site Memo-13-00012-SAM-E-C-096	SAM	09/08/14	Other
	SM-13-00012-DUR-C-E-046	TO 12- Scope of Work for access road at Sta.0+300 RHS	DUR	09/16/14	Record of Verbal Site Instruction
	SM-13-00012-SAM-C-E-047	TO 12- Stopping Works over the Boulders Wall	SAM	09/21/14	Other
	SM-13-00012-DUR-C-E-048	T.O.12: Side walk from Sta.0+380 to Sta.0+400 LHS	DUR	10/20/14	Record of Verbal Site Instruction
	SM-13-00012-DUR-C-E-049	T.O.12: Sewage Water Leakage into the Water Line Trench	DUR	01/20/15	Other
	SM-13-00012-DUR-C-E-050	T.O.12: Confirmation for Verbal Site Instructions	DUR	02/09/15	Record of Verbal Site Instruction
	SM-13-00012-DUR-C-E-051	T.O.12: Works Stopped at Parapet Wall from Sta.3+343 to Sta.3+370	DUR	02/24/15	Other
	SM-13-00012-DUR-C-E-052	T.O.12: Dura Pending Issues and Concerns	DUR	03/08/15	Others

# E | Inspection Requests Log

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-001-A	Traffic Control Safety Measures from St.0+000 to St.0+500-Sinjir Road	01/15/14	01/15/14	01/16/14	1	A
	IR-13-00004-DUR-002-A	Start Excavation Work from St.0+000 to St.0+500 LHS-Sinjir Road	01/15/14	01/15/14	01/15/14	0	A
	IR-13-00004-DUR-003-A	Start Excavation Work from St.0+000 to St.0+500 RHS-Sinjir Road	01/21/14	01/22/14	01/22/14	0	A
	IR-13-00004-DUR-004-A	Inspection for Delivered Water Steel Pipes 6"&2"-Storage Yard Area	01/28/14	01/29/14	01/29/14	0	A
	IR-13-00004-DUR-005-A	Start Excavation Work for Water Pipe Line from St.0+000 to St.0+500	02/03/14	02/04/14	02/05/14	1	A
	IR-13-00004-DUR-006-A	Start Installation Works for Water Pipe Line 6"&2" LHS from St.0+000 to St.0+500	02/04/14	02/04/14	02/05/14	1	A
	IR-13-00004-DUR-007-A	Backfilling Single Size for Water Pipe Line 6"&2" with installation of warning tape from St.0+048 to St.0+130 LHS	02/05/14	02/05/14	02/06/14	1	A
	IR-13-00004-DUR-008-A	Start Excavation Works for Water Pipe Line 2" from St.0+000 to St.0+500 RHS	02/05/14	02/05/14	02/06/14	1	A
	IR-13-00004-DUR-009-A	Check Installation of pipes for Water Line 6"&2" LHS including Single Size Bedding from St.0+048 to St.0+130-Quantity of 6"=86.04 LM & Quantity of 2"=85.05 LM	02/05/14	02/05/14	02/06/14	1	A
	IR-13-00004-DUR-010-A	Check Installation of Water Pipe Line 2" from St.0+041 to St.0+162 RHS-Quantity=115.23 LM	02/06/14	02/06/14	02/07/14	1	A
	IR-13-00004-DUR-011-A	Check Backfilling Single Size for Water Pipe Line 2" with installation warning tape from St.0+041 to St.0+162 RHS	02/06/14	02/06/14	02/07/14	1	A
	IR-13-00004-DUR-012-A	Check Backfilling Single Size for Water Pipe Line 2" with installation warning tape from St.0+130 to St.0+176 LHS	02/06/14	02/06/14	02/07/14	1	A
	IR-13-00004-DUR-013-A	Check Installation for Water Pipe Line 2" with installation of warning tape from St.0+130 to St.0+176 LHS-Quantity of 6"=47.93 LM & Quantity of 2"=48.33 LM	02/06/14	02/06/14	02/07/14	1	A
	IR-13-00004-DUR-014-A	Check Installation of Water Pipe Line 6"&2" LHS Including Single Size Bedding from St.0+176 to St.0+260-Quantity of 6"=85.49 LM & Quantity of 2"=83.45 LM	02/09/14	02/09/14	02/10/14	1	A
	IR-13-00004-DUR-015-A	Check Backfilling Single Size for Water Pipe Lines 6"&2" LHS Including installation warning tape from St.0+176 to St.0+260	02/09/14	02/09/14	02/10/14	1	A
	IR-13-00004-DUR-016-A	Check Backfilling Single Size for Water Pipe Line 6"&2" LHS including Installation of Warning Tape from St.0+036 to St.0+048	02/10/14	02/10/14	02/11/14	1	A
	IR-13-00004-DUR-017-A	Check Installation Pipe for Water Line 2" LHS including Single Size Bedding from St.0+406 to St.0+496 & from St.0+339 to St.0+400-Quantity of 2"=90.22+60.15=150.37 LM	02/10/14	02/10/14	02/11/14	1	C
	IR-13-00004-DUR-017-B	Check Installation Pipe for Water Line 2" LHS including Single Size Bedding from St.0+406 to St.0+496 & from St.0+339 to St.0+400-Quantity of 2"=90.22+60.15=150.37 LM	02/13/14	02/13/14	02/13/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-018-A	Check Backfilling Single Size for Water Line 2" LHS including Installation of Warning Tape from St.0+406 to St.0+496 & from St.0+339 to St.0+400	02/10/14	02/10/14	02/11/14	1	C
	IR-13-00004-DUR-018-B	Check Backfilling Single Size for Water Line 2" LHS including Installation of Warning Tape from St.0+406 to St.0+496 & from St.0+339 to St.0+401	02/13/14	02/13/14	02/13/14	0	A
	IR-13-00004-DUR-019-A	Check Installation pipes for Water Line 6"&2" LHS including Single Size Bedding from St.0+036 to St.0+048-Quantity of 6"=12.33 LM/Quantity of 2"=12.13 LM	02/10/14	02/10/14	02/11/14	1	A
	IR-13-00004-DUR-020-A	Visual Inspection for formwork Material (Ply Wood, Timber & PVC Concrete Spacer)	02/19/14	02/20/14	02/20/14	0	A
	IR-13-00004-DUR-021-A	Visual Inspection for Electrical Fitting (Galvanized Steel Strip 30*3mm & Grounding Conductor Copper Bar 1.5 m)	02/19/14	02/20/14	02/20/14	0	D
	IR-13-00004-DUR-021-B	Visual Inspection for Electrical Fitting (Galvanized Steel Strip 30*3mm & Grounding Conductor Copper Bar Length 1.5 m),cobra 3" PVC pipe, warning tape & un-isolated wire	03/13/14	03/13/14	03/13/14	0	A
	IR-13-00004-DUR-022-A	Welder Training & Testing-at Abu Zainah Workshop at AL Fara'a Camp near Nablus-for Dura-Hebron (Sinjer) Road	02/25/14	02/27/14	03/03/14	4	C
	IR-13-00004-DUR-022-B	Welder Training & Testing-at Abu Zainah Workshop at AL Fara'a Camp near Nablus-for Dura-Hebron (Sinjer) Road	02/28/14	02/28/14	02/28/14	0	A
	IR-13-00004-DUR-023-A	Casting Blinding Concrete for Retaining Wall from St.0+026 to St.0+054 LHS-Quantity =6 m3	02/27/14	03/01/14	03/03/14	2	A
	IR-13-00004-DUR-024-A	Casting Concrete for Retaining Wall Footing from St.0+033 to St.0+051.5- LHS-Quantity=13.6 m3	03/03/14	03/04/14	03/05/14	1	A
	IR-13-00004-DUR-025-A	Casting Blinding Concrete for Retaining Wall B-150-from St.0+444 to St.0+474 RHS	03/05/14	03/05/14	03/06/14	1	A
	IR-13-00004-DUR-026-A	Check Installation of Storm Water Drainage -RC Pipes 600mm Dia. With Single Size Bedding , Installation of MH 12 at St.0+116, MH11 at St.0+154	03/09/14	03/09/14	03/09/14	0	A
	IR-13-00004-DUR-027-A	Check Installation of Storm Water Drainage -RC Pipes 600 mm Dia. With Single Size Bedding, Installation of MH1 (at St.0+186.5) to MH11(at St.0+154)-Quantity of 600mm Dia.Pipes=31.67 lm	03/10/14	03/11/14	03/12/14	1	A
	IR-13-00004-DUR-028-A	Handing Over Sub-grade Layer from St.0+020 to St.0+180	03/11/14	03/11/14	03/12/14	1	C
	IR-13-00004-DUR-028-B	Handing Over Sub-grade Layer from St.0+040 to St.0+160	03/13/14	03/13/14	03/13/14	0	A
	IR-13-00004-DUR-029-A	Check Casting Concrete B-250 for Retaining Wall Foundation from St.0+444 to St.0+474	03/12/14	03/13/14	03/13/14	0	A
	IR-13-00004-DUR-030-A	Check Installation of Storm Water Drainage -RC Pipes 600mm Dia. With Single Size Bedding , Installation of MH#2 (at St.0+242), from MH1(at St.0+186) to MH2 (at St.0+242)Quantity of 600mm Dia.Pipes=55.25 lm	03/12/14	03/13/14	03/13/14	0	C

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-030-B	Check Installation of Storm Water Drainage -RC Pipes 600mm Dia. With Single Size Bedding , Installation of MH#2 (at St.0+242), from MH1(at St.0+186) to MH2 (at St.0+242)Quantity of 600mm Dia.Pipes=55.25 lm	03/17/14	03/18/14	03/18/14	0	A
	IR-13-00004-DUR-031-A	Check Casting Concrete B-250 for Storm Water Encasement From St. 0+154 to St. 0+186 RHS	03/16/14	03/16/14	03/18/14	2	A
	IR-13-00004-DUR-032-A	Visual Inspection for Street Light Cable 5 * 16 mm2 N2 XY	03/16/14	03/17/14	03/18/14	1	A
	IR-13-00004-DUR-033-A	Check Installation of Storm Water Drainage RC pipe 600mm Dia. with single size bedding From MH#03(at St.0+294 ) to MH#2 (at St.0+242)	03/17/14	03/18/14	03/18/14	0	A
	IR-13-00004-DUR-034-A	Check Installation pipes for PW 2’’ line RHS including single size bedding from St.0+162 to St.0+294 RHS and from St 0+029 to St.0+041RHS	03/18/14	03/19/14	03/19/14	0	A
	IR-13-00004-DUR-035-A	Check casting concrete B250 for Retaining Wall from St. 0+034.15 to St. 0+050.5 LHS	03/19/14	03/20/14	03/20/14	0	A
	IR-13-00004-DUR-036-A	Handing over Topping Layer from St. 0+060 to St. 0+110 LHS & 0+110 to 0+140 RHS +LHS	03/19/14	03/20/14	03/20/14	0	D
	IR-13-00004-DUR-036-B	Handing over Topping Layer from St. 0+060 to St. 0+110 LHS & 0+110 to 0+140 RHS +LHS	03/21/14	03/21/14	03/21/14	0	A
	IR-13-00004-DUR-037-A	Check casting concrete B250 for storm water encasement from St. 0+117 to St. 0+153 RHS	03/19/14	03/20/14	03/20/14	0	A
	IR-13-00004-DUR-038-A	Casting concrete B-250 for Retaining Walls from St.0+444 to St.0+474 RHS	03/20/14	03/22/14	03/24/14	2	C
	IR-13-00004-DUR-038-B	Casting concrete B-250 for Retaining Walls from St.0+444 to St.0+460 RHS	03/24/14	03/24/14	03/25/14	1	A
	IR-13-00004-DUR-039-A	Check Casting Concrete B250 for Gravity Wall from St.0+732 to St.0+755 RHS & from St.0+779 to St.0+800 RHS	03/22/14	03/23/14	03/24/14	1	D
	IR-13-00004-DUR-039-B	Check Casting Concrete B250 for Gravity Wall - Stage1, from St.0+732 to St.0+755 RHS & from St.0+779 to St.0+800 RHS	03/24/14	03/25/14	03/26/14	1	A
	IR-13-00004-DUR-040-A	Check Casting Blinding Concrete B150 for Boundary Wall from St. 0+189 to St.0+201 & from St.0+207 to St.0+210	03/25/14	03/25/14	03/27/14	2	C
	IR-13-00004-DUR-040-B	Check Casting Blinding Concrete B150 for Boundary Wall from St. 0+189.1 to St.0+199 & from St.0+205 to St.0+209.41	03/27/14	03/27/14	03/31/14	4	A
	IR-13-00004-DUR-041-A	Check Casting Concrete B250 for Boundary Wall Foundation from St. 0+189 to St.0+198.9 & from St.0+205.7 to St.0+210	03/25/14	03/26/14	03/27/14	1	C
	IR-13-00004-DUR-041-B	Check Casting Concrete B250 for Boundary Wall Foundation from St. 0+189.1 to St.0+199 & from St.0+205 to St.0+209.41	03/27/14	03/27/14	03/31/14	4	A
	IR-13-00004-DUR-042-A	Check Casting Concrete B250 for Gravity Wall / Stage #2 ,from St.0+732 to St.0+755 RHS * from St.0+779 to St.0+800 RHS	03/25/14	03/26/14	03/27/14	1	D
	IR-13-00004-DUR-042-B	Check Casting Concrete B250 for Gravity Wall / Stage #2 ,from St.0+732 to St.0+755 RHS * from St.0+779 to St.0+800 RHS	03/27/14	03/29/14	03/31/14	2	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-043-A	Handing over sub grade layer from St.0+140 to St.0+240	03/30/14	03/30/14	03/31/14	1	A
	IR-13-00004-DUR-044-A	Handing over topping layer from St.0+040 to St.0+140	03/30/14	03/30/14	03/31/14	1	A
	IR-13-00004-DUR-045-A	Casting concrete B-250 for Retaining Walls from St.0+460 to St.474	03/27/14	03/29/14	03/31/14	2	A
	IR-13-00004-DUR-046-A	Casting Concrete B- 250 for Boundary Wall from St. 0+189.1 to St.0+199 & from St.0+205 to St.0+209.41	03/27/14	03/29/14	03/31/14	2	A
	IR-13-00004-DUR-047-A	Installation of storm water drainage RC pipe 800mm dia ,with single size bedding from MH4 (at St. 0+306 ) to MH5 (at St. 0+373.89)	03/29/14	03/30/14	03/31/14	1	A
	IR-13-00004-DUR-048-A	Check Casting Blinding Concrete B-150 for Storm Water Manhole #03 at St.0+306 RHS	04/02/14	04/03/14	04/03/14	0	D
	IR-13-00004-DUR-048-B	Check Casting Blinding Concrete B-150 for Storm Water Manhole #03 at St.0+306 RHS	04/09/14	04/09/14	04/10/14	1	A
	IR-13-00004-DUR-049-A	Check Bituminous Coating & Start Backfilling Works for Concrete Retaining Wall from St.0+444 to St.0+470 RHS	04/08/14	04/09/14	04/09/14	0	C
	IR-13-00004-DUR-049-B	Check Bituminous Coating & Start Backfilling Works for Concrete Retaining Wall from St.0+444 to St.0+470 RHS	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00004-DUR-050-A	Check Installation Pipes for PW 6&2" line LHS including single size bedding from St.0+264.96 to 0+463.32 (2" LHS) & from St.0+266.79 to St.462.95 (6" LHS)	04/08/14	04/09/14	04/10/14	1	A
	IR-13-00004-DUR-051-A	Check Installation Pipes for PW 6&2" line LHS including installation of W.tape from St.0+264.96 to 0+463.32 (2" LHS) & from St.0+266.79 to St.462.95 (6" LHS)	04/08/14	04/09/14	04/10/14	1	A
	IR-13-00004-DUR-052-A	Check Pressure for PW 6,2" line, from St.0+036 to St.0+462.95 (6" LHS), from St.0+036 to St.463.32 (2" LHS) & from St.0+028.95 to 0+487.24 (2" RHS)	04/08/14	04/09/14	04/10/14	1	A
	IR-13-00004-DUR-053-A	Handing Over of Sub-grade Layer from St.0+340 to St.0+440	04/09/14	04/10/14	04/10/14	0	C
	IR-13-00004-DUR-053-B	Handing Over of Sub-grade Layer from St.0+340 to St.0+440	04/14/14	04/14/14	04/14/14	0	A
	IR-13-00004-DUR-054-A	Handing Over Base Course-1st Layer from St.0+050 to St.0+230	04/08/14	04/08/14	04/10/14	2	A
	IR-13-00004-DUR-055-A	Casting Concrete for Manhole#3 Foundation	04/10/14	04/12/14	04/12/14	0	A
	IR-13-00004-DUR-056-A	Handing Over of Sub-grade Layer from St.0+240 to St.0+280	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00004-DUR-057-A	Handing Over Base Course-1st Layer from St.0+340 to St.0+440	04/10/14	04/12/14	04/12/14	0	C
	IR-13-00004-DUR-057-B	Handing Over Base Course-1st Layer from St.0+340 to St.0+440	04/15/14	04/16/14	04/17/14	1	D
	IR-13-00004-DUR-057-C	Handing Over Base Course-1st Layer from St.0+340 to St.0+440	05/08/14	05/10/14	05/11/14	1	A
	IR-13-00004-DUR-058-A	Check Backfilling Single Size for PW2" Line RHS including W tape Installation From St.0+487.24 to St.0+653.24	04/13/14	04/13/14	04/15/14	2	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-059-A	Check Installation pipes for PW2" Line RHS including Single Size Bedding from St.0+487.24 to St.0+653.24	04/13/14	04/13/14	04/13/14	0	A
	IR-13-00004-DUR-060-A	Check Installation House connection 3/4 "as per attached list , including single size bedding from st 0+041 to 0+459 LHS & RHS Dura (Sinjir) Hebron Road	04/15/14	04/15/14	04/16/14	1	A
	IR-13-00004-DUR-061-A	Check backfilling single size for House connection 3/4 "as per attached list , including installation of W.tape. From St 0+041 to St 0+459 LHS & RHS-Dura (Sinjir)-Hebron Road	04/15/14	04/15/14	04/16/14	1	A
	IR-13-00004-DUR-062-A	Check Installation House connection 3/4 " as per attached list , including single size bedding from St 0+300 to 0+660 LHS & RHS- Dura (Sinjir)-Hebron Road	04/15/14	04/16/14	04/16/14	0	A
	IR-13-00004-DUR-063-A	Check Backfilling single size for House connection 3/4 , including installation of W.tape From St. 0+300 to 0+660 LHS & RHS	04/15/14	04/16/14	04/16/14	0	A
	IR-13-00004-DUR-064-A	Check Installation PW LINE 2", including single size bedding from St.0+653.24 to 0+780 RHS	04/15/14	04/15/14	04/16/14	1	A
	IR-13-00004-DUR-065-A	Check Backfilling single size for PW LINE 2" , including installation Wtape From St. 0+653.24 to St.0+780 RHS	04/15/14	04/15/14	04/16/14	1	A
	IR-13-00004-DUR-066-A	Check Casting Concrete for Wall of storm water MH3 & slabs with Stair at St.0+744 RHS	04/15/14	04/16/14	04/17/14	1	A
	IR-13-00004-DUR-067-A	Check Installation of PW Line 2", house connection, including single size bedding at St.0+370 LHS	04/15/14	04/16/14	04/17/14	1	A
	IR-13-00004-DUR-068-A	Check Backfilling single size for PW LINE 2" house connection , including installation of W . Tape at St. 0+370 LHS	04/15/14	04/16/14	04/16/14	0	A
	IR-13-00004-DUR-069-A	Check Installation of Catch Basin with 400 mm crossing at St. 0+115 & 0+ 245 (at Center Line) & at St. 0+187 LHS	04/16/14	04/16/14	04/17/14	1	D
	IR-13-00004-DUR-069-B	Check Installation of Catch Basin with 400 mm crossing at St. 0+115 & 0+ 245 (at Center Line) & at St. 0+187 LHS	04/20/14	04/21/14	04/22/14	1	D
	IR-13-00004-DUR-069-C	Check Installation of Catch Basin with 400 mm crossing at St. 0+115 & 0+ 245 (at Center Line) & at St. 0+187 LHS	11/24/14	11/24/14	11/25/14	1	A
	IR-13-00004-DUR-070-A	Handing Over Installation of Curbstone from St.0+050 to St.0+280 RHS&LHS	04/17/14	04/17/14	04/21/14	4	D
	IR-13-00004-DUR-070-B	Handing Over Installation of Curbstone from St.0+050 to St.0+280 RHS&LHS	12/17/14	12/17/14	12/18/14	1	A
	IR-13-00004-DUR-071-A	Handing Over Base Course 2nd Layer from St.0+050 to St.0+280	04/17/14	04/17/14	04/21/14	4	D
	IR-13-00004-DUR-071-B	Handing Over Base Course 2nd Layer from St.0+050 to St.0+280	04/21/14	04/21/14	04/22/14	1	B
	IR-13-00004-DUR-072-A	Handing Over Sub-grade Layer from St.0+280 to St.0+340	04/17/14	04/20/14	04/21/14	1	D

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-072-B	Handing Over of Sub-grade Layer from St.0+280 to St.0+340, Except areas around high voltage Poles T St.0+290 & St.0+300 LHS	04/23/14	04/23/14	04/23/14	0	A
	IR-13-00004-DUR-073-A	Handing Over Base Course-1st Layer from St.0+440 to St.0+500	04/17/14	04/20/14	04/21/14	1	D
	IR-13-00004-DUR-073-B	Handing Over Base Course-1st Layer from St.0+440 to St.0+500	05/01/14	05/03/14	05/07/14	4	A
	IR-13-00004-DUR-074-A	Start Spreading work of MC from St.0+050 to St.0+280	04/21/14	04/21/14	04/22/14	1	B
	IR-13-00004-DUR-075-A	Start Asphalt Work from St.0+050 to St.0+280	04/21/14	04/21/14	04/22/14	1	B
	IR-13-00004-DUR-076-A	Casting Blinding Concrete for Boundary Wall from St.0+813 to St.0+825 RHS	04/22/14	04/22/14	04/23/14	1	A
	IR-13-00004-DUR-077-A	Casting Concrete B-250 for Parapet Wall for Gravity Wall from St.0+732 to St.0+755 & from St.0+779 to St.0+800 RHS	04/22/14	04/22/14	04/27/14	5	A
	IR-13-00004-DUR-078-A	Installation of storm water pipe 800mm dia from St.0+378.52 to St.0+420 LHS	04/22/14	04/23/14	04/24/14	1	A
	IR-13-00004-DUR-079-A	Installation of storm water pipe 600mm dia from St.0+420.54 to St.0+468.66 LHS	04/22/14	04/23/14	04/24/14	1	D
	IR-13-00004-DUR-079-B	Installation of storm water pipe 600mm dia from St.0+420.54 to St.0+468.66 LHS	05/08/14	05/10/14	05/11/14	1	A
	IR-13-00004-DUR-080-A	Installation of storm water pipe 1000mm dia from St.0+001 to St.0+027.7& from St.0+029.7 to St.0+072.41	04/22/14	04/24/14	04/24/14	0	A
	IR-13-00004-DUR-081-A	Base Courese-1st Layer from St.0+340 to St.0+440	04/23/14	04/23/14	04/24/14	1	A
	IR-13-00004-DUR-082-A	Casting Concrete B-250 for Boundary Wall Foundation from St.0+812 to St.0+825 RHS	04/24/14	04/24/14	04/27/14	3	A
	IR-13-00004-DUR-083-A	Installation of Storm Water Pipe 600 mm dia from St. 0+470.66 to St. 0+508.36 & from St. 0+510.36 to St. 0+541.86 LHS	04/24/14	04/24/14	04/24/14	0	D
	IR-13-00004-DUR-083-B	Installation of Storm Water Pipe 600 mm dia from St. 0+470.66 to St. 0+508.36 & from St. 0+510.36 to St. 0+541.86 LHS	05/08/14	05/10/14	05/11/14	1	A
	IR-13-00004-DUR-084-A	Casting Concrete B-250 for Boundary Wall from St. 0+812 to St. 0+825 RHS	04/24/14	04/26/14	04/27/14	1	D
	IR-13-00004-DUR-084-B	Casting Concrete B-250 for Boundary Wall from St. 0+812 to St. 0+825 RHS	04/28/14	04/28/14	04/29/14	1	A
	IR-13-00004-DUR-085-A	Handing over Base Course-1st layer from St. 0+280 to St. 0+340 except areas around high voltage poles at St. 0+290 & St.0+300 LHS	04/24/14	04/26/14	04/27/14	1	A
	IR-13-00004-DUR-086-A	Installation work of Storm Water Pipe 600 mm dia from St. 0+543.86 to St. 0+558.86 LHS	04/27/14	04/27/14	04/28/14	1	A
	IR-13-00004-DUR-087-A	Installation Work of Storm Water Pipe 600 mm dia from St. 0+561 to St. 0+604.7 & from St.0+606.7 to St.0+639.9 LHS	04/28/14	04/29/14	04/29/14	0	D

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-087-B	Installation Work of Storm Water Pipe 600 mm dia from St. 0+561 to St. 0+604.7 & from St.0+606.7 to St.0+639.9 LHS	04/30/14	04/30/14	04/30/14	0	D
	IR-13-00004-DUR-087-C	Installation Work of Storm Water Pipe 600 mm dia from St. 0+561 to St. 0+604.7 & from St.0+606.7 to St.0+639.9 LHS	05/08/14	05/10/14	05/11/14	1	A
	IR-13-00004-DUR-088-A	Installation Work of Storm Water Pipe 600 mm Dia. From St.0+641.76 to St.0+683.41 LHS	04/29/14	04/29/14	04/30/14	1	A
	IR-13-00004-DUR-089-A	Installation of two PVC Conduits, Grounding cables, Concrete Blocks, Warning Tape & Backfilling Sand from St.0+060 to St.0+170 for Street Lighting Median	04/29/14	04/29/14	04/30/14	1	A
	IR-13-00004-DUR-090-A	Installation of PW Pipes 6" & 2" with Single Size Bedding & W tape Installation from St.0+458 to St.0+720 LHS	04/29/14	04/30/14	04/30/14	0	A
	IR-13-00004-DUR-091-A	Handing Over Sub-grade Layer from St.0+440 to St.0+560	04/30/14	05/01/14	05/04/14	3	D
	IR-13-00004-DUR-091-B	Handing Over Sub-grade Layer from St.0+440 to St.0+560	05/20/14	05/21/14	05/22/14	1	D
	IR-13-00004-DUR-091-C	Handing Over Sub-grade Layer from St.0+440 to St.0+560	05/24/14	05/24/14	05/25/14	1	A
	IR-13-00004-DUR-092-A	Installation Work of Storm Water Pipe 600 mm Dia.from St.0+685.41 MH12 to St.0+735 MH13 LHS	04/30/14	05/01/14	05/04/14	3	D
	IR-13-00004-DUR-092-B	Installation Work of Storm Water Pipe 600 mm Dia.from St.0+685.41 MH12 to St.0+735 MH13 LHS	05/08/14	05/10/14	05/11/14	1	A
	IR-13-00004-DUR-093-A	Casting Blinding Concrete for Boundary Wall from St.0+460 to St.0+472 LHS	04/30/14	05/01/14	05/04/14	3	D
	IR-13-00004-DUR-093-B	Casting Blinding Concrete for Boundary Wall from St.0+460 to St.0+472 LHS	05/05/14	05/05/14	05/06/14	1	D
	IR-13-00004-DUR-093-C	Casting Blinding Concrete for Boundary Wall from St.0+460 to St.0+472 LHS	05/22/14	05/22/14	05/23/14	1	A
	IR-13-00004-DUR-094-A	Installation Work of Storm Water Pipe 600 mm Dia.from MH13 to MH14 LHS	04/30/14	05/03/14	05/04/14	1	D
	IR-13-00004-DUR-094-B	Installation Work of Storm Water Pipe 600 mm Dia.from MH13 to MH14 LHS	05/05/14	05/05/14	05/06/14	1	D
	IR-13-00004-DUR-094-C	Installation Work of Storm Water Pipe 600 mm Dia.from MH13 (St.0+737) to MH14 (St.0+784.51)LHS	05/08/14	05/10/14	05/11/14	1	A
	IR-13-00004-DUR-095-A	Installation of Storm Water Pipe 400 mm Dia. & Catch Basin at Crossing St.0+420 & St.0+376	05/04/14	05/04/14	05/06/14	2	A
	IR-13-00004-DUR-096-A	Installation of Curbstone for Median from St.0+060 to St.0+280	05/05/14	05/06/14	05/07/14	1	C
	IR-13-00004-DUR-096-B	Installation of Curbstone for Median from St.0+060 to St.0+280	12/17/14	12/17/14	12/18/14	1	A
	IR-13-00004-DUR-097-A	Handing Over Sub-grade from St.0+540 to St.0+680	05/07/14	05/07/14	05/08/14	1	C
	IR-13-00004-DUR-097-B	Handing Over Sub-grade from St.0+540 to St.0+680	05/10/14	05/10/14	05/11/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-098-A	Check Installation House Connection 3/4" as per attached list, including W.tape with Single Size bedding	04/08/14	04/10/14	04/11/14	1	A
	IR-13-00004-DUR-099-A	Start Installation of 2" Water Pipe Line from St.0+795 to St.0+900 RHS	05/10/14	05/10/14	05/11/14	1	A
	IR-13-00004-DUR-100-A	Start Installation of 2"&6" Water Pipe Line from St.0+720 to St.0+790 LHS	05/11/14	05/12/14	05/12/14	0	A
	IR-13-00004-DUR-101-A	Start Installation of Storm Water Pipes (Manhole 14 to Manhole15) from St.0+780 to St.0+840	05/11/14	05/12/14	05/12/14	0	A
	IR-13-00004-DUR-102-A	Start Installation of Water Pipe Line 4" at St.0+300 RHS	05/11/14	05/12/14	05/13/14	1	A
	IR-13-00004-DUR-103-A	Check Installation of Storm Water R.C Pipes 600mm Dia.from St.0+786.51 to St.0+837.68 & from St.0+838.68 to St.0+876.8	05/13/14	05/14/14	05/15/14	1	A
	IR-13-00004-DUR-104-A	Check Installation of Manhole 15 at St.0+838.68 & Manhole#16 at St.0+877.88	05/13/14	05/14/14	05/15/14	1	A
	IR-13-00004-DUR-105-A	Check Installation of Steel Pipeline 6" from St.0+726.7 to St.0+787.78	05/13/14	05/14/14	05/15/14	1	A
	IR-13-00004-DUR-106-A	Check Installation of 3/4" threaded galvanized Steel Pipeline with no internal cement lining at St.0+813, St.0+831, St.0+873, St.0+849, St.0+885, St.0+900 & St.0+936 RHS	04/13/14	04/14/14	04/18/14	4	A
	IR-13-00004-DUR-107-A	Check Installation of 2" threaded galvanized Steel Pipeline with no internal cement lining from St.0+729.83 to St.0+790.13 LHS& from St.0+795 to St.0+915 RHS	05/13/14	05/14/14	05/18/14	4	A
	IR-13-00004-DUR-108-A	Start Installation of 2"&6" water pipe line from St.0+790 to St.1+050	05/14/14	05/14/14	05/18/14	4	A
	IR-13-00004-DUR-109-A	Casting Concrete B-200 for Gravity Wall-1st Stage from St.0+950 to St.0+995 RHS	05/15/14	05/17/14	05/18/14	1	D
	IR-13-00004-DUR-109-B	Casting Concrete B-200 for Gravity Wall-1st Stage from St.0+950 to St.0+995 RHS	05/18/14	05/19/14	05/20/14	1	A
	IR-13-00004-DUR-110-A	Casting Concrete B-200 for Gravity Wall-1st Stage from St.0+800 to St.0+813.5	05/15/14	05/17/14	05/18/14	1	D
	IR-13-00004-DUR-110-B	Casting Concrete B-200 for Gravity Wall-1st Stage from St.0+800 to St.0+813.6	05/18/14	05/19/14	05/20/14	1	A
	IR-13-00004-DUR-111-A	Blinding Concrete for Boundary Wall from St.0+388 to St.0+395 RHS	05/18/14	05/18/14	05/19/14	1	A
	IR-13-00004-DUR-112-A	Casting Encasement Concrete B-250 from St.0+817 to St.0+833.5, from St.0+850 to St.0+854.1 & from St.0+880 to St.0+889.85	05/18/14	05/18/14	05/19/14	1	A
	IR-13-00004-DUR-113-A	Casting concrete for Boundary Wall foundation from St.0+388 to St.0+395 RHS	05/19/14	05/20/14	05/21/14	1	A
	IR-13-00004-DUR-114-A	Check installation Street Lighting Pipes , Grounding Cable , Sand Bedding , Concrete blocks & Warning Tap	05/19/14	05/19/14	05/21/14	2	A
	IR-13-00004-DUR-115-A	Casting Concrete-B 200- for Gravity wall-2nd Stage from St.0+950 to St.0+995 RHS	05/20/14	05/21/14	05/22/14	1	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-116-A	Casting Concrete-B 200- for Gravity Wall-2nd Stage from St.0+800 to St.0+813.5	05/20/14	05/21/14	05/22/14	1	A
	IR-13-00004-DUR-117-A	Handing Over Sub Grade Layer from St.0+680 to St.0+800	05/20/14	05/21/14	05/22/14	1	D
	IR-13-00004-DUR-117-B	Handing Over Sub Grade Layer from St.0+680 to St.0+800	05/25/14	05/26/14	05/26/14	0	A
	IR-13-00004-DUR-118-A	Blinding Concrete for Retaining Wall from St.0+447 to 0+472 LHS	05/20/14	05/21/14	05/22/14	1	D
	IR-13-00004-DUR-118-B	Blinding Concrete for Retaining Wall from St.0+447 to 0+472 LHS	05/22/14	05/22/14	05/23/14	1	A
	IR-13-00004-DUR-119-A	Casting Concrete B 250-for Boundary Wall from St.0+388 to St.0+398 RHS	05/22/14	05/22/14	05/22/14	0	A
	IR-13-00004-DUR-120-A	Handing Over Sub Grade Layer for Side walk from St.0+060 to 0+220 RHS& LHS	05/22/14	05/22/14	05/22/14	0	A
	IR-13-00004-DUR-121-A	Handing Over Base Course Layer for Sidewalk from St.0+060 to St.0+220 RHS & LHS	05/22/14	05/24/14	05/25/14	1	D
	IR-13-00004-DUR-121-B	Handing Over Base Course Layer for Sidewalk from St.0+060 to St.0+220 RHS & LHS	05/26/14	05/26/14	05/27/14	1	A
	IR-13-00004-DUR-122-A	Casting Concrete B-200 for Gravity Wall-3rd Stage from St.0+793.94 to St.0+803.44	05/22/14	05/24/14	05/25/14	1	A
	IR-13-00004-DUR-123-A	Handing Over Sub grade Layer from St.0+440 to St.0+560, refer to accepted IR-13-00012-DUR-091-C	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-124-A	Handing Over Sub-grade Layer from St.0+680 to St.0+900,	05/22/14	05/24/14	05/25/14	1	D
	IR-13-00004-DUR-124-B	Handing Over Sub-grade Layer from St.0+680 to St.0+900	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00004-DUR-125-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape & Blocks from St.0+440 to St.0+510	5/22/2014	5/24/2014	05/25/14	1	D
	IR-13-00004-DUR-125-B	Installation of Street Lighting Pipes, Ground Cable, Warning Tape & Blocks from St.0+440 to St.0+510	5/25/2014	5/26/2014	5/27/2014	1	A
	IR-13-00004-DUR-126-A	Casting Concrete B-200 for Gravity Wall-4th Stage from St.0+793.94 to St.0+803.44 & from St.0+955 to St.0+966.5	05/25/14	05/25/14	05/26/14	1	D
	IR-13-00004-DUR-126-B	Casting Concrete B-200 for Gravity Wall-4th Stage from St.0+793.94 to St.0+803.44 & from St.0+955 to St.0+966.5	05/27/14	05/27/14	05/28/14	1	A
	IR-13-00004-DUR-127-A	Installation Storm Water Pipe(1000 mm Dia.) with Single Size from St.0+072.41 to 0+115 Out Full Direction	05/25/14	05/25/14	05/26/14	1	D
	IR-13-00004-DUR-127-B	Installation Storm Water Pipe(1000 mm Dia.) with Single Size from St.0+072.41 to 0+115 Out Full Direction	05/26/14	05/26/14	05/27/14	1	A
	IR-13-00004-DUR-128-A	Casting Concrete-B250- for Retaining Wall Foundation from St.0+447 to St.0+472	05/25/14	05/26/14	05/27/14	1	D

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-128-B	Casting Concrete-B250- for Retaining Wall Foundation from St.0+447 to St.0+472	05/28/14	05/28/14	05/28/14	0	D
	IR-13-00004-DUR-128-C	Casting Concrete-B250- for Retaining Wall Foundation from St.0+447 to St.0+472 LHS	05/29/14	05/31/14	06/01/14	1	A
	IR-13-00004-DUR-129-A	Handing Over Sub Grade Layer fro St.0+680 to St.0+780	05/26/14	05/26/14	05/27/14	1	A
	IR-13-00004-DUR-130-A	Backfilling Storm Water Pipe (1000 mm Dia.) with Single Size from St.0+072.41 to 0+115 Out Full Direction	05/26/14	05/26/14	05/27/14	1	A
	IR-13-00004-DUR-131-A	Start Casting Concrete-B 250- for Side Walk from St.0+090 to St.0+260 LHS&RHS	05/27/14	05/27/14	05/28/14	1	D
	IR-13-00004-DUR-131-B	Start Casting Concrete-B 250- for Side Walk from St.0+090 to St.0+260 LHS&RHS	06/01/14	06/02/14	06/02/14	0	A
	IR-13-00004-DUR-132-A	Start Construction Stone Wall from St.0+250 to St. 0+275 RHS	05/27/14	05/28/14	05/28/14	0	D
	IR-13-00004-DUR-132-B	Start Construction Stone Wall from St.0+250 to St. 0+275 RHS	09/10/14	09/10/14	09/11/14	1	A
	IR-13-00004-DUR-133-A	Sub Grade Layer from St.0+840 to St.0+920	05/27/14	05/27/14	05/28/14	1	A
	IR-13-00004-DUR-134-A	Installation Storm Water Pipe(1000 mm Dia.) with Single Size from MH#3a to MH#4A Outfall Direction	05/28/14	05/28/14	05/29/14	1	D
	IR-13-00004-DUR-134-B	Installation Storm Water Pipe(1000 mm Dia.) with Single Size from MH#3a to MH#4A Outfall Direction	09/15/14	09/15/14	09/16/14	1	A
	IR-13-00004-DUR-135-A	Casting Concrete B-200 for Gravity Wall-5th Stage from St.0+966.5 to St.0+990	05/28/14	05/28/14	05/29/14	1	A
	IR-13-00004-DUR-136-A	Start Excavation Works for 2" Water Pipeline from St.1+000 to St.1+500 RHS	05/28/14	05/28/14	05/29/14	1	A
	IR-13-00004-DUR-137-A	Start Excavation Works Widening Road from St.1+000 to St.1+500	05/28/14	05/29/14	05/29/14	0	C
	IR-13-00004-DUR-137-B	Start Excavation Works Widening Road from St.1+000 to St.1+500	06/01/14	06/01/14	06/02/14	1	A
	IR-13-00004-DUR-138-A	Base Course 1st Layer from St.0+540 to 0+780	06/01/14	06/02/14	06/02/14	0	D
	IR-13-00004-DUR-138-B	Base Course 1st Layer from St.0+540 to 0+780	06/01/14	06/01/14	06/02/14	1	A
	IR-13-00004-DUR-139-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape & Blocks from St.0+510 to 0+700	06/02/14	06/03/14	06/03/14	0	A
	IR-13-00004-DUR-140-A	Base Course 1st Layer from St.0+740 to St.0+900	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00004-DUR-141-A	Installation 2" Water Pipe line Including Single Size, Bedding, Warning Tape with Backfill Single Size from St.1+110 to St.1+224 RHS	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00004-DUR-142-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape & Blocks from St.0+700 to 0+800	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00004-DUR-143-A	Casting Concrete Encasement around 2" Water Pipe Line from St.1+137.5 to St.1+145 RHS	06/03/14	06/03/14	06/04/14	1	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-144-A	Installation 2" Water Pipe line Including Single Size, Bedding, Warning Tape with Backfill Single Size from St.1+224 to St.1+320 RHS	06/04/14	06/05/14	06/05/14	0	A
	IR-13-00004-DUR-145-A	Installation Storm Water Pipe (1000 mm Dia) outfall Direction from MH7a to MH8a	11/24/14	11/24/14	11/25/14	1	A
	IR-13-00004-DUR-146-A	Installation Storm Water Pipe (1000 mm Dia) outfall Direction from MH5a to MH7a	06/05/14	06/07/14	06/09/14	2	A
	IR-13-00004-DUR-147-A	Base Course 1st Layer from St.0+560 to 0+740 RHS & LHS	06/05/14	06/07/14	06/08/14	1	A
	IR-13-00004-DUR-148-A	Installation 2" Water Pipe line Including Single Size, Bedding, Warning Tape with Backfill Single Size from St.1+350 to St.1+400 RHS	06/05/14	06/07/14	06/09/14	2	A
	IR-13-00004-DUR-149-A	Casting Concrete-B 250- for Retaining Wall from St. 0+447 to St.0+472 LHS	06/05/14	06/07/14	06/08/14	1	A
	IR-13-00004-DUR-150-A	Casting Blinding Concrete for Retaining Wall from St.1+557 to St.1+570.8 LHS	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00004-DUR-151-A	Sample for Concrete of Side Walk from St.0+189 to St.0+199 RHS	06/05/14	06/05/14	06/08/14	3	A
	IR-13-00004-DUR-152-A	Excavation and Reduced Level Works for Footing of Retaining Wall from St.1+557 to 1+570.8 LHS	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00004-DUR-153-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape & Blocks from St.0+800 to 1+050	06/05/14	06/05/14	06/09/14	4	A
	IR-13-00004-DUR-154-A	Installation Storm Water Pipe (1000 mm Dia.) Outfall Direction from MH6a to MH7a, refer to accepted IR-13-00012-DUR-146-A	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-155-A	Installation 2" Water Pipe line Including Single Size, Bedding, Warning Tape with Backfill Single Size from St.1+400 to St.1+500 RHS	06/07/14	06/07/14	06/09/14	2	A
	IR-13-00004-DUR-156-A	Installation 2" & 6" water pipe line including single size, bedding, warning tap with backfill single size from St. 1+050 to St.1+110 LHS.	06/08/14	06/08/14	06/09/14	1	A
	IR-13-00004-DUR-157-A	Casting concrete B-250 for water chamber foundation at St.0+517 LHS	06/08/14	06/08/14	06/09/14	1	A
	IR-13-00004-DUR-158-A	Casting concrete for gravity wall stage#1 from St. 0+077,5 to St.0+020A (access road)	06/08/14	06/08/14	06/09/14	1	A
	IR-13-00004-DUR-159-A	Installation 2" & 6" water pipe line including single size, bedding, warning tap with backfill single size from St. 1+110 to St.1+200 LHS.	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00004-DUR-160-A	Casting concrete for gravity wall stage#2 from St. 0+077,5 to St.0+020A (access road)	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00004-DUR-161-A	Start benching, widening works for roundabout area at St.0+000	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00004-DUR-162-A	Casting encasement Concrete for (400 mm Dia.) Crossing at St.0+560 & St.0+610	06/10/14	06/10/14	06/12/14	2	A
	IR-13-00004-DUR-163-A	Installation 2" water pipe line including single size, bedding, warning tap with backfill single size from St. 1+500 to 1+553.65 RHS.	06/10/14	06/10/14	06/12/14	2	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-164-A	Base course 2 <sup>st</sup> layer from St.0+570 to St.0+900 RHS & LHS, refer to accepted IR-13-00012-DUR-170-A and IR-13-00012-DUR-173-A	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-165-A	Casting encasement concrete for (400 mm Dia.) crossing at 0+641, 0+687, 0+841 & 0+880	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00004-DUR-166-A	Casting blinding concrete for retaining wall from St.0+980 to St.0+990.80 LHS	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00004-DUR-167-A	Casting concrete B-250 for water chamber #3 walls at St.0+517 LHS	06/12/14	06/12/14	06/15/14	3	A
	IR-13-00004-DUR-168-A	Start mockup sample for stone wall works from St.0+250 to 0+275 RHS & at St.0+140 LHS	06/12/14	06/12/14	06/15/14	3	D
	IR-13-00004-DUR-168-B	Start mockup sample for stone wall works from St.0+250 to 0+275 RHS & at St.0+140 LHS	09/09/14	09/10/14	09/11/14	1	A
	IR-13-00004-DUR-169-A	Casting blinding concrete for retaining wall from St.1+570.8 to St.1+587.10 LHS	06/12/14	06/12/14	06/15/14	3	A
	IR-13-00004-DUR-170-A	Handing over base course 2 <sup>nd</sup> layer from St.0+570 to St.0+720 RHS & LHS	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00004-DUR-171-A	Installation 2" water Pipe Line including Single Size, Bedding, warning tap with backfill single size from St.2+100 to St.2+350	11/24/14	11/24/14	11/25/14	1	A
	IR-13-00004-DUR-172-A	Casting concrete for retaining wall foundation from Sta.0+980 to 0+990.80LHS	06/12/14	06/12/14	06/15/14	3	A
	IR-13-00004-DUR-173-A	Base course 2nd layer from St.0+720 to St.0+900 RHS & LHS	06/15/14	06/15/14	06/16/14	1	A
	IR-13-00004-DUR-174-A	Installation 2" water pipe line including single size, bedding, warning tape with backfill single size from St. 1+553.65 to 1+688.25 RHS.	06/14/14	06/14/14	06/15/14	1	A
	IR-13-00004-DUR-175-A	Handing over sub grade layer for roundabout at St.0+000 RHS ( widening area)	06/15/14	06/15/14	06/16/14	1	A
	IR-13-00004-DUR-176-A	Start prime coat spraying & asphalt binder course (5cm) from St.0+570 to 0+900	06/15/14	06/15/14	06/16/14	1	A
	IR-13-00004-DUR-177-A	Handing over 2" water pipe line including single size, bedding, warning tap with backfill single size from St.2+085 to St.2+175.5 RHS	06/15/14	06/15/14	06/16/14	P	A
	IR-13-00004-DUR-178-A	Sample of Interlock works from St.0+070 to St.0+100 LHS	06/15/14	06/15/14	06/16/14	1	D
	IR-13-00004-DUR-178-B	Sample of Interlock works from St.0+070 to St.0+100 LHS	08/05/14	08/05/14	08/07/14	2	A
	IR-13-00004-DUR-179-A	Start excavation works for widening from St.3+400 to St.3+500 RHS	06/15/14	06/15/14	06/16/14	1	C
	IR-13-00004-DUR-179-B	Start excavation works for widening from St.3+400 to St.3+500 RHS	11/09/14	11/10/14	11/11/14	1	A
	IR-13-00004-DUR-180-A	Start excavation works for proposed gravity wall from St.3+610 to St.3+640 LHS	06/15/14	06/15/14	06/16/14	1	D
	IR-13-00004-DUR-180-B	Start excavation works for proposed gravity wall from St.3+610 to St.3+640 LHS	11/09/14	11/10/14	11/11/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-181-A	Casting concrete of wall for retaining wall from St.0+980 to 0+990.80 LHS	06/17/14	06/18/14	06/19/14	1	A
	IR-13-00004-DUR-182-A	Casting concrete for water chamber #3 top slab at St.0+517 LHS	06/15/14	06/16/14	06/17/14	1	A
	IR-13-00004-DUR-183-A	Casting concrete for concrete wall from St.0+988 to St.1+010 RHS ( 1 <sup>st</sup> stage )	06/15/14	06/16/14	06/17/14	1	A
	IR-13-00004-DUR-184-A	Excavation works and reduced level for gravity wall from St.2+402.10 to St.2+417.10 RHS	06/16/14	06/16/14	06/17/14	1	A
	IR-13-00004-DUR-185-A	Casting concrete for lateral support of existing stone wall from St.1+850 to St.1+875 RHS	06/16/14	06/16/14	06/17/14	1	A
	IR-13-00004-DUR-186-A	Start curbstone works from St.0+000 to 0+070 RHS	06/16/14	06/16/14	06/17/14	1	A
	IR-13-00004-DUR-187-A	prime coat application from St.0+760 to St.0+890, refer to accepted IR-13-00012-DUR-176-A	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-188-A	Base course 2 <sup>nd</sup> layer from St.0+330 to St.0+490	06/17/14	06/18/14	06/22/14	4	A
	IR-13-00004-DUR-189-A	Start asphalt binder course ( 5cm) from St.0+760 to St.0+890, refer to accepted IR-13-00012-DUR-176-A	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-190-A	Installation 2" water pipe line including single size, bedding, warning tape with backfill single size from St. 1+688.25 to 1+848.75 RHS	06/17/14	06/17/14	06/18/14	1	A
	IR-13-00004-DUR-191-A	Casting concrete for island from St.0+060 to St.0+280	06/18/14	06/18/14	06/19/14	1	D
	IR-13-00004-DUR-191-B	Casting concrete for island from St.0+060 to St.0+280	12/30/14	12/30/14	12/31/14	1	A
	IR-13-00004-DUR-192-A	Casting concrete for retaining wall foundation from St.1+570.80 to St.1+587 LHS	06/18/14	06/18/14	06/19/14	1	A
	IR-13-00004-DUR-193-A	Start prime coat application from St.0+330 to St.0+480	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00004-DUR-194-A	Start asphalt binder course (5cm) from St.0+330 to St.0+480	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00004-DUR-195-A	Casting concrete for concrete wall from St.0+988 to St.1+010 RHS (2nd stage )	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00004-DUR-196-A	Casting concrete for gravity wall from St.2+402.10 to St.2+417.10 (1st Stage)	06/15/14	06/16/14	06/16/14	0	A
	IR-13-00004-DUR-197-A	Location of gravity wall from St.2+402.10 to St.2+417.10	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00004-DUR-198-A	Casting concrete for lateral support of existing stone wall from St.1+850 to St.1+875 RHS ( 2 <sup>nd</sup> stage )	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00004-DUR-199-A	Casting concrete for retaining wall from St.0+988 to St.1+010 RHS ( 3 <sup>rd</sup> Stage)	06/19/14	06/22/14	06/23/14	1	A
	IR-13-00004-DUR-200-A	Casting concrete for lateral support of existing stone wall from St.1+850 to St.1+875 RHS ( 3 <sup>rd</sup> Stage)	06/19/14	06/22/14	06/23/14	1	A
	IR-13-00004-DUR-201-A	Casting concrete for gravity wall from St.2+402.10 to St.2+417.10 RHS ( 2nd Stage)	06/19/14	06/22/14	06/23/14	1	A

**USAID WEST BANK/ GAZA**  
**INFRASTRUCTURE NEEDS PROGRAM INPII**  
**CONTRACT NO. AID-294-TO-12-00005**  
**TASK ORDER #12, Multiple Roads Project (South)**  
**Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-202-A	Installation 2" water pipe line including single size, bedding, warning tape with backfill single size from St. 1+848.5 to 2+085 RHS.	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00004-DUR-203-A	Start excavation works to match sub grade level from ST.1+050 to 1+200	06/21/14	06/22/14	06/22/14	0	D
	IR-13-00004-DUR-203-B	Start excavation works to match sub grade level from ST.1+050 to 1+200	06/27/14	06/28/14	06/29/14	1	A
	IR-13-00004-DUR-204-A	Installation of curbstone for Median from St.0+580 to St.0+760	06/23/14	06/23/14	06/24/14	1	A
	IR-13-00004-DUR-205-A	Casting concrete for retaining wall from St.0+988 to St.1+010 RHS ( 4 Stage)	06/23/14	06/23/14	06/24/14	1	A
	IR-13-00004-DUR-206-A	Casting concrete for lateral support of existing stone wall from St.1+850 to St. 1+875 RHS ( 4 Stage)	06/23/14	06/23/14	06/24/14	1	A
	IR-13-00004-DUR-207-A	Base course 2 <sup>nd</sup> layer at roundabout at St.0+000 RHS (widening area)	06/23/14	06/23/14	06/24/14	1	C
	IR-13-00004-DUR-207-B	Base course 2 <sup>nd</sup> layer at roundabout at St.0+000 RHS (widening area)	07/21/14	07/22/14	07/23/14	1	A
	IR-13-00004-DUR-208-A	Handing Over for Sub Grade Layer from St.0+900 to St.1+040	06/25/14	06/25/14	06/26/14	1	C
	IR-13-00004-DUR-208-B	Handing Over for Sub Grade Layer from St.0+900 to St.1+040	06/29/14	06/29/14	06/30/14	1	A
	IR-13-00004-DUR-209-A	Installation of Storm Water Drainage RC Pipe 600mm dia , with Single Size Bedding from MH24 to MH23	06/23/14	06/23/14	06/24/14	1	D
	IR-13-00004-DUR-209-B	Installation of Storm Water Drainage RC Pipe 600mm dia , with Single Size Bedding from MH24 to MH23	06/25/14	06/25/14	06/26/14	1	A
	IR-13-00004-DUR-210-A	Installation of Storm Water Drainage RC Pipe 600mm dia , with Single Size Bedding from MH23 to MH22	06/23/14	06/23/14	06/24/14	1	D
	IR-13-00004-DUR-210-B	Installation of Storm Water Drainage RC Pipe 600mm dia , with Single Size Bedding from MH23 to MH22	06/25/14	06/25/14	06/26/14	1	A
	IR-13-00004-DUR-211-A	Start Median Base Course Works from St.0+580 to St.0+760	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00004-DUR-212-A	Installation of Curbstone from St.0+760 to St.0+880	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00004-DUR-213-A	Installation of Curbstone from St.0+320 to St.0+480	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00004-DUR-214-A	Casting concrete for top slab of septic tank at St.0+447 LHS	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00004-DUR-215-A	Handing over stone wall from St.0+250 to ST.0+275 RHS	06/25/14	06/25/14	06/26/14	1	D
	IR-13-00004-DUR-215-B	Handing over stone wall from St.0+250 to ST.0+275 RHS	09/15/14	08/31/14	09/16/14	1	A
	IR-13-00004-DUR-216-A	Installation of Storm Water Drainage Rc Pipe 600mm Dia. , with Single Size Bedding from MH21 to MH20	06/25/14	06/25/14	06/26/14	1	A
	IR-13-00004-DUR-217-A	Casing concrete for gravity wall from St.2+390 to St.2+402 RHS (1 <sup>st</sup> Stage)	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00004-DUR-218-A	Installation of curbstone from St.0+580 to St.0+760 RHS	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00004-DUR-219-A	Casting Concrete for Stair at St.0+970 LHS	06/26/14	06/28/14	06/29/14	1	D
	IR-13-00004-DUR-219-B	Casting Concrete for Stair at St.0+970 LHS	07/06/14	07/07/14	07/07/14	0	A
	IR-13-00004-DUR-220-A	Casting Concrete for Median from St.0+600 to St.0+800	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00004-DUR-221-A	Casting Blinding Concrete for Retaining Wall from St.1+587to St.1+600 LHS	06/26/14	06/26/14	06/29/14	3	A
	IR-13-00004-DUR-222-A	Installation of curbstone from St.0+010 to St.0+050 RHS & LHS	06/29/14	06/29/14	07/01/14	2	C

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-222-B	Installation of curbstone from St.0+010 to St.0+050 RHS & LHS	12/17/14	12/17/14	12/17/14	0	A
	IR-13-00004-DUR-223-A	Handing over Base course layer 2 <sup>nd</sup> from St.0+280 to St.0+330 LHS except area around electrical poles	06/29/14	06/29/14	06/30/14	1	A
	IR-13-00004-DUR-224-A	Casting concrete for gravity wall stage #3 from St.A0+020 to St.A0+077.5	06/29/14	06/30/14	06/30/14	0	A
	IR-13-00004-DUR-225-A	Casting concrete for gravity wall stage #2 from 2+390 to 3+402 RHS	06/29/14	06/30/14	06/30/14	0	A
	IR-13-00004-DUR-226-A	Casting concrete for retaining wall Stage #1 from St.1+557 to St.1+571 LHS	06/29/14	06/30/14	07/01/14	1	D
	IR-13-00004-DUR-226-B	Casting concrete for retaining wall Stage #1 from St.1+557 to St.1+571 LHS	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00004-DUR-227-A	Handing over base course 1 <sup>st</sup> layer from St.0+900 to St.1+000	06/29/14	06/30/14	07/01/14	1	A
	IR-13-00004-DUR-228-A	Casting blinding concrete for storm water manhole from MH17 to MH22	06/29/14	06/30/14	07/01/14	1	C
	IR-13-00004-DUR-228-B	Casting blinding concrete for storm water manhole from MH17 to MH23	08/22/14	08/22/14	08/23/14	1	A
	IR-13-00004-DUR-229-A	Start curbstone for roundabout at St.0+000	06/30/14	06/30/14	07/01/14	1	A
	IR-13-00004-DUR-230-A	Interlock works from St.0+010 to 0+050	06/30/14	07/01/14	07/02/14	1	D
	IR-13-00004-DUR-230-B	Interlock works from St.0+010 to 0+050 LHS	11/09/14	11/10/14	11/11/14	1	A
	IR-13-00004-DUR-231-A	Casting concrete for gravity wall stage #1 from St.2+230 to St.2+273 RHS	07/02/14	07/03/14	07/03/14	0	A
	IR-13-00004-DUR-232-A	Visual inspection for edge beam – (Al-Ameer & Al-Soos Co.)	07/02/14	07/03/14	07/03/14	0	C
	IR-13-00004-DUR-232-B	Visual inspection for edge beam – ( Al-Soos Co.)	03/10/15	03/10/15	03/10/15	0	A
	IR-13-00004-DUR-233-A	Installation 2” water pipe line including single size, bedding, warning tape with backfill single size from St.1+035 to St.1+100 RHS	07/02/14	07/03/14	07/03/14	0	A
	IR-13-00004-DUR-234-A	Sub grade layer from St.1+050 to St.1+200	07/03/14	07/05/14	07/06/14	1	D
	IR-13-00004-DUR-234-B	Sub grade layer from St.1+040 to St.1+120	08/19/14	08/19/14	08/20/14	1	A
	IR-13-00004-DUR-235-A	Installation 2” & 6” water pipe line including single size, bedding, warning tap with backfill single size from St. 1+600 to St.2+000 LHS.	07/03/14	07/05/14	07/06/14	1	C
	IR-13-00004-DUR-235-B	Installation 2” & 6” water pipe line including single size, bedding, warning tap with backfill single size from St. 1+800 to St.2+000 LHS.	07/11/14	07/12/14	07/12/14	0	A
	IR-13-00004-DUR-236-A	Casting concrete for gravity wall from St.2+230 to St.2+273 RHS ( 2 <sup>nd</sup> Stage)	07/03/14	07/05/14	07/06/14	1	D
	IR-13-00004-DUR-236-B	Casting concrete for gravity wall from St.2+230 to St.2+273 RHS ( 2 <sup>nd</sup> Stage)	07/08/14	07/09/14	07/09/14	0	A
	IR-13-00004-DUR-237-A	Casting concrete for retaining wall from St.1+557 to St.1+587 LHS (2 <sup>nd</sup> Stage)	07/03/14	07/05/14	07/06/14	1	D
	IR-13-00004-DUR-237-B	Casting concrete for retaining wall from St.1+557 to St.1+587 LHS (2 <sup>nd</sup> Stage)	07/22/14	07/23/14	07/23/14	0	A
	IR-13-00004-DUR-238-A	Casting concrete for retaining wall foundation from St1+587 to St.1+600 LHS	07/03/14	07/05/14	07/06/14	1	A
	IR-13-00004-DUR-239-A	Safety measures for night shift works	07/05/14	07/05/14	07/06/14	1	D
	IR-13-00004-DUR-239-B	Safety measures for night shift works	08/10/14	08/10/14	08/11/14	1	A
	IR-13-00004-DUR-240-A	Start welding for 2” & 6” water pipeline from St.1+650 to St.1+750 LHS	07/05/14	07/05/14	07/06/14	1	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-241-A	Casting concrete for island from St.0+570 to St.0+620	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00004-DUR-242-A	Installation of curbstone from St.0+570 to St.0+700 LHS	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00004-DUR-243-A	Casting concrete for stairs at St.0+970 LHS	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00004-DUR-244-A	Casting concrete for side walk from St.0+640 to St.0+660 LHS	07/08/14	07/09/14	07/10/14	1	A
	IR-13-00004-DUR-245-A	Base course 2nd layer from St.0+900 to St.1+000	07/10/14	07/12/14	07/13/14	1	D
	IR-13-00004-DUR-245-B	Base course 2nd layer from St.0+900 to St.1+000	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00004-DUR-246-A	Base course 1 <sup>st</sup> layer from St.1+000 to St.1+040	07/10/14	07/12/14	07/13/14	1	A
	IR-13-00004-DUR-247-A	Installation 2" & 6" water pipe line including single size, bedding, warning tap with backfill single size from St. 1+890 to St.2+000 LHS.	07/10/14	07/12/14	07/13/14	1	A
	IR-13-00004-DUR-248-A	Base course 1 <sup>st</sup> layer from St.0+480 to St.0+560	07/10/14	07/12/14	07/13/14	1	A
	IR-13-00004-DUR-249-A	Installation 2" & 6" water pipe line including single size, bedding, warning tap with backfill single size from St. 1+770 to St.1+830 LHS.	07/10/14	07/10/14	07/13/14	3	A
	IR-13-00004-DUR-250-A	Casting concrete for gravity wall from St.2+230 to St.2+273 RHS ( 3 <sup>rd</sup> Stage)	07/10/14	07/12/14	07/13/14	1	A
	IR-13-00004-DUR-251-A	Casting concrete for retaining wall from St.1+557 to St.1+571 LHS	07/10/14	07/12/14	07/13/14	1	A
	IR-13-00004-DUR-252-A	Installation of Curbstone for Median from St.0+760 to St.0+880	07/13/14	07/14/14	07/15/14	1	A
	IR-13-00004-DUR-253-A	Casting concrete for retaining wall from St.1+557 to St.1+571 LHS (2 <sup>nd</sup> Stage)	07/16/14	07/17/14	07/17/14	0	C
	IR-13-00004-DUR-253-B	Casting concrete for retaining wall from St.1+557 to St.1+571 LHS (2 <sup>nd</sup> Stage)	07/20/14	07/20/14	07/21/14	1	A
	IR-13-00004-DUR-254-A	Casting concrete for gravity wall from St.2+242.9 to ST.2+257.7 RHS (1 <sup>st</sup> Stage)	07/16/14	07/17/14	07/17/14	0	A
	IR-13-00004-DUR-255-A	Installation 2" & 6" water pipe line including single size, bedding, warning tap with backfill single size from St. 2+000 to St.2+187 LHS.	07/16/14	07/17/14	07/17/14	0	A
	IR-13-00004-DUR-256-A	Installation 2" & 6" water pipe line including single size, bedding, warning tap with backfill single size from St.1+200 to St.1+380 LHS	07/16/14	07/17/14	07/17/14	0	A
	IR-13-00004-DUR-257-A	Base course 2 <sup>nd</sup> layer from St.0+010 to St.0+060	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00004-DUR-258-A	Check installation curbstone round about at St.0+000	07/20/14	07/20/14	07/20/14	0	A
	IR-13-00004-DUR-259-A	Casting concrete for gravity wall from St.2+242.9 to St.2+257.7 RHS (2 <sup>nd</sup> Stage)	07/20/14	07/21/14	07/22/14	1	A
	IR-13-00004-DUR-260-A	Casting blinding concrete for retaining wall from St.1+634 to St.1+677 RHS	07/20/14	07/21/14	07/21/14	0	D
	IR-13-00004-DUR-260-B	Casting blinding concrete for retaining wall from St.1+634 to St.1+677 RHS	08/06/14	10/25/14	08/07/14	0	A
	IR-13-00004-DUR-261-A	Base course 2 <sup>nd</sup> layer from St.0+280 to St.0+330 RHS&LHS	07/20/14	07/21/14	07/22/14	1	A
	IR-13-00004-DUR-262-A	Base course 2 <sup>nd</sup> layer from St.0+480 to St.0+560 RHS&LHS	07/20/14	07/21/14	07/22/14	1	A
	IR-13-00004-DUR-263-A	Start Prime coat application from St.0+010 to St.0+060 , St.0+280 to St.0+330 & St.0+890 to St.1+040 RHS&LHS	07/20/14	07/21/14	07/22/14	1	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-264-A	Start asphalt binder course from St.0+010 to St.0+060 , St.0+280 to St.0+330 & St.0+890 to St.1+040 RHS&LHS	07/20/14	07/21/14	07/22/14	1	A
	IR-13-00004-DUR-265-A	Installation 2" & 6" water pipe line including single size, bedding, warning tap with backfill single size from St. 2+187 to St.2+340 LHS.	07/22/14	07/23/14	07/24/14	1	A
	IR-13-00004-DUR-266-A	Casting concrete for gravity wall from St.2+242.9 to St.2+257.7 RHS (3 <sup>rd</sup> Stage)	07/22/14	07/23/14	07/24/14	1	A
	IR-13-00004-DUR-267-A	Casting concrete for gravity wall from St.2+625 to St.2+644 RHS (1 <sup>st</sup> Stage)	08/03/14	08/03/14	08/04/14	1	A
	IR-13-00004-DUR-268-A	Casting concrete for side walk from St.0+855 to St.0+880 LHS	08/03/14	08/02/14	08/04/14	2	A
	IR-13-00004-DUR-269-A	Installation storm water pipe (600 mm Dia.) from St.1+381.35 to St.1+423.85 LHS	08/03/14	08/03/14	08/04/14	1	A
	IR-13-00004-DUR-270-A	Casting concrete for gravity wall from St.2+625 to St.2+644 RHS (2nd Stage)	08/05/14	08/05/14	08/06/14	1	A
	IR-13-00004-DUR-271-A	Installation of curbstone for median from St.0+880 to St.1+020	08/05/14	08/05/14	08/06/14	1	A
	IR-13-00004-DUR-272-A	Casting concrete for gravity wall from St.2+625 to St.2+644 RHS (3 <sup>rd</sup> Stage)	08/05/14	08/06/14	08/07/14	1	A
	IR-13-00004-DUR-273-A	Casting concrete for gravity wall from St.2+625 to St.2+644 RHS (4 <sup>th</sup> Stage)	08/07/14	08/07/14	08/08/14	1	A
	IR-13-00004-DUR-274-A	Check installation of steel for retaining wall from St.1+587 to St.1+602 LHS	08/07/14	08/07/14	08/07/14	0	A
	IR-13-00004-DUR-275-A	Casting concrete for gravity wall from St.2+625 to St.2+644 RHS (5 <sup>th</sup> Stage)	08/09/14	08/09/14	08/11/14	2	A
	IR-13-00004-DUR-276-A	Casting concrete for retaining wall from St.1+587 to St.1+602 LHS	08/09/14	08/10/14	08/11/14	1	A
	IR-13-00004-DUR-277-A	Sub grade layer from St.1+120 to St.1+260 LHS & RHS except area electrical poles.	08/09/14	08/10/14	08/10/14	0	A
	IR-13-00004-DUR-278-A	Casting concrete for median from St.0+880 to St.1+030	08/07/14	08/09/14	08/10/14	1	C
	IR-13-00004-DUR-278-B	Casting concrete for median from St.0+880 to St.1+030	03/10/15	03/10/15	03/10/15	0	A
	IR-13-00004-DUR-279-A	Casting concrete gravity wall from St.2+644 to St.2+665 RHS (1 <sup>st</sup> Stage).	08/10/14	08/11/14	08/11/14	0	A
	IR-13-00004-DUR-280-A	Casting concrete gravity wall from St.2+644 to St.2+665 RHS (2nd Stage).	08/11/14	08/12/14	08/13/14	2	A
	IR-13-00004-DUR-281-A	Casting concrete for retaining wall foundation from St.1+634 to St.1+670 RHS	08/12/14	08/13/14	08/14/14	1	A
	IR-13-00004-DUR-282-A	Casting concrete for gravity wall from St.1+815 to 1+825.35 RHS (1 <sup>st</sup> Stage)	08/12/14	08/12/14	08/13/14	1	A
	IR-13-00004-DUR-283-A	Casting concrete gravity wall from St.2+644 to St.2+665 RHS (3 <sup>rd</sup> Stage).	08/12/14	08/13/14	08/13/14	1	A
	IR-13-00004-DUR-284-A	Casting blinding concrete for retaining wall from St.1+602 to St.1+620 LHS	08/12/14	08/13/14	08/14/14	1	A
	IR-13-00004-DUR-285-A	Check installation of steel for retaining wall from St.1+571 to St.1+588.5 LHS	08/13/14	08/13/14	08/13/14	0	A
	IR-13-00004-DUR-286-A	Casting concrete for gravity wall from St.1+815 to 1+825.35 RHS (2nd Stage)	08/13/14	08/13/14	08/17/14	4	A
	IR-13-00004-DUR-287-A	Casting concrete for retaining wall from St.1+571 to St.1+588.5 LHS ( Stage#1)	08/14/14	08/16/14	08/18/14	2	A
	IR-13-00004-DUR-288-A	Casting concrete for gravity wall from St.2+644 to 2+665 RHS (4th Stage)	08/13/14	08/14/14	08/14/14	0	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-289-A	Casting concrete for gravity wall from St.1+815 to 1+825.35 RHS (3rd Stage)	08/14/14	08/15/14	08/14/14	0	A
	IR-13-00004-DUR-290-A	Casting concrete for gravity wall from St.2+644 to 2+665 RHS (5th Stage)	08/17/14	08/17/14	08/18/14	1	A
	IR-13-00004-DUR-291-A	Sub-grade Layer from St.1+800 to St.1+980 LHS	08/17/14	08/17/14	08/18/14	1	A
	IR-13-00004-DUR-292-A	Sub-grade Layer from St.1+800 to St.1+920 RHS	08/18/14	08/18/14	08/19/14	1	A
	IR-13-00004-DUR-293-A	Handover Sub-grade Layer from St.1+320 to St.1+380 LHS&RHS	08/19/14	08/19/14	08/20/14	1	A
	IR-13-00004-DUR-294-A	casting concrete for retaining wall from St.1+571 to St.1+588.5 LHS ( Stage#2)	08/19/14	08/19/14	08/20/14	1	C
	IR-13-00004-DUR-294-B	casting concrete for retaining wall from St.1+571 to St.1+588.5 LHS ( Stage#2)	08/23/14	08/23/14	08/24/14	1	A
	IR-13-00004-DUR-295-A	casting concrete for retaining wall foundation from St.1+615 to St.1+625 LHS .	08/19/14	08/19/14	08/20/14	1	A
	IR-13-00004-DUR-296-A	Installation and backfilling (2" & 6") water pipe line from St. 2+400 to St.2+550 LHS.	08/21/14	08/23/14	08/24/14	1	C
	IR-13-00004-DUR-296-B	Installation and backfilling (2" & 6") water pipe line from St. 2+400 to St.2+550 LHS.	08/25/14	08/25/14	08/26/14	1	A
	IR-13-00004-DUR-297-A	Sub-grade Layer from St.1+980 to St.2+100 LHS	08/21/14	08/23/14	08/24/14	1	D
	IR-13-00004-DUR-297-B	Sub-grade Layer from St.1+980 to St.2+100 LHS	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00004-DUR-298-A	Casting concrete for stairs (B250) from St.0+636 RHS & 0+853 LHS	08/23/14	08/23/14	08/24/14	1	A
	IR-13-00004-DUR-299-A	casting concrete for retaining wall from St.1+602 to St.1+615 LHS ( Stage#1)	08/23/14	08/23/14	08/24/14	1	A
	IR-13-00004-DUR-300-A	Installation and backfilling (2" & 6") water pipe line from St. 2+340 to St.2+400 LHS.	08/24/14	08/24/14	08/25/14	1	A
	IR-13-00004-DUR-301-A	Installation and backfilling (2" & 6") water pipe line from St. 2+550 to St.2+700 LHS.	08/26/14	08/26/14	08/27/14	1	A
	IR-13-00004-DUR-302-A	Installation 2" water pipe line from St. 2+432 to St.2+480 RHS.	08/27/14	08/27/14	08/28/14	1	A
	IR-13-00004-DUR-303-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.1+100 to 1+240	08/27/14	08/27/14	08/28/14	1	A
	IR-13-00004-DUR-304-A	Check installation of steel for retaining wall from St.1+615 to St.1+621 LHS	08/27/14	08/27/14	08/28/14	1	A
	IR-13-00004-DUR-305-A	Installation Storm Water Pipe (1000 mm Dia) outfall Direction at St.0+320 from St.0+118.61 to St.0+158.31	08/27/14	08/27/14	08/28/14	1	A
	IR-13-00004-DUR-306-A	Casting concrete for foundation of storm water manhole at St.1+300 LHS	08/27/14	08/27/14	08/28/14	1	A
	IR-13-00004-DUR-307-A	Casting concrete for R.W from St.1+615 to St.1+621 LHS	08/28/14	08/28/14	08/30/14	2	A
	IR-13-00004-DUR-308-A	Installation and backfilling (2" & 6") water pipe line from St. 2+700 to St.2+750 LHS.	08/28/14	08/28/14	08/30/14	2	A
	IR-13-00004-DUR-309-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.1+050 to 1+100	08/28/14	08/28/14	08/30/14	2	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-310-A	Installation and backfilling (2" & 6") water pipe line from St. 2+750 to St.2+850 LHS.	08/28/14	08/30/14	08/31/14	1	A
	IR-13-00004-DUR-311-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.1+240 to 1+300	08/28/14	08/30/14	08/31/14	1	A
	IR-13-00004-DUR-312-A	Cheek reinforcement works for steel of retaining wall from St.1+634 to St.1+646 & from St.1+657.5 to St.1+669.5 RHS	08/28/14	08/30/14	08/31/14	1	A
	IR-13-00004-DUR-313-A	Installation and backfilling (2" & 4") water pipe line from St. 2+850 to St.2+920 LHS.	08/30/14	08/30/14	08/31/14	1	A
	IR-13-00004-DUR-314-A	Installation and backfilling (2" & 6") water pipe line from St. 1+380 to St.1+500 LHS.	08/30/14	08/30/14	08/31/14	1	A
	IR-13-00004-DUR-315-A	Installation 2" water pipe line from St. 2+480 to St.2+640 RHS.	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00004-DUR-316-A	Installation and backfilling (2" & 4") water pipe line from St. 2+920 to St.3+000 LHS.	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00004-DUR-317-A	casting concrete for retaining wall from St.1+634 to St.1+646 & from St.1+657.5 to St.1+669.5 RHS	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00004-DUR-318-A	start backfilling works for retaining wall from St.1+557 to St.1+620 LHS ( using rock fill material of 60 cm each layer thickens as per lab recommendation )	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00004-DUR-319-A	Installation and backfilling (2" & 4") water pipe line from St. 3+000 to St.3+100 LHS.	09/01/14	09/01/14	09/02/14	1	A
	IR-13-00004-DUR-320-A	Installation and backfilling (2" & 4") water pipe line from St. 3+100 to St.3+200 LHS.	09/02/14	09/02/14	09/03/14	1	A
	IR-13-00004-DUR-321-A	Check installation of steel reinforcement for storm water MH at St.1+300 LHS.	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00004-DUR-322-A	Installation 2" water pipe line from St. 2+640 to St.2+700 RHS.	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00004-DUR-323-A	casting concrete for gravity wall stage #1 from St.1+944 to St.1+983.15 RHS	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00004-DUR-324-A	casting concrete for storm water MH walls at St.1+300 LHS.	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00004-DUR-325-A	Handing over base course for sidewalk layer at roundabout	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00004-DUR-326-A	Handing over steel reinforcement works for retaining wall from St.1+646 to St.1+657RHS.	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00004-DUR-327-A	casting concrete for retaining wall from St.1+646 to St.1+657.5 RHS	09/04/14	09/04/14	09/06/14	2	A
	IR-13-00004-DUR-328-A	casting concrete for gravity wall 2nd stage from St.1+944 to St.1+983.15 RHS	09/04/14	09/04/14	09/06/14	2	A
	IR-13-00004-DUR-329-A	Installation of storm water Pipe from Sta. 1+423.85 to Sta. 1+520 LHS.	09/04/14	09/06/15	09/07/14	1	A
	IR-13-00004-DUR-330-A	Installation 2" water pipe line from St. 2+700 to St.2+780 RHS.	09/04/14	09/06/15	09/07/14	1	A
	IR-13-00004-DUR-331-A	Casting concrete for gravity wall 3rd Stage from Sta. 1+972 to Sta. 1+983.15 RHS	09/04/14	09/06/15	09/07/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-332-A	Installation of storm water Pipe from Sta. 1+520 to Sta. 1+570 LHS.	09/07/14	09/07/14	09/08/14	1	A
	IR-13-00004-DUR-333-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.1+300 to 1+340	09/07/14	09/07/14	09/08/14	1	A
	IR-13-00004-DUR-334-A	Casting concrete for gravity wall 4th stage from St.1+944 to St.1+957 RHS & from St.1+972 to St.1+983.15 RHS	09/08/14	09/08/14	09/09/14	1	A
	IR-13-00004-DUR-335-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.1+340 to 1+660	09/09/14	09/09/14	09/10/14	1	A
	IR-13-00004-DUR-336-A	Installation and backfilling (2" & 6") water pipe line from St. 1+500 to St.1+600 LHS.	09/09/14	09/09/14	09/10/14	1	A
	IR-13-00004-DUR-337-A	Casting concrete for gravity wall 5th stage from St.1+972 to St.1+983.15 RHS	09/09/14	09/09/14	09/10/14	1	A
	IR-13-00004-DUR-338-A	Casting concrete for retaining wall foundation from St.A0+007 to St.A0+015 at access road at St. 0+320	09/09/14	09/09/14	09/10/14	1	A
	IR-13-00004-DUR-339-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.1+660 to 1+900	09/10/14	09/10/14	09/11/14	1	A
	IR-13-00004-DUR-340-A	Installation of storm water Pipe from Sta. 1+570 to Sta. 1+609 LHS.	09/10/14	09/10/14	09/11/14	1	A
	IR-13-00004-DUR-341-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.1+900 to 2+100	09/11/14	09/11/14	09/13/14	2	A
	IR-13-00004-DUR-342-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.2+100 to 2+200	09/11/14	09/13/14	09/14/14	1	A
	IR-13-00004-DUR-343-A	Installation and backfilling for water line house connection from St. 1+020 to St.1+400 RHS.	09/11/14	09/11/14	09/13/14	2	A
	IR-13-00004-DUR-344-A	Casting concrete for gravity wall 1st stage from St.2+323 to St.2+343 RHS	09/13/14	09/13/14	09/14/14	1	A
	IR-13-00004-DUR-345-A	Casting concrete for gravity wall 1st stage from St.2+835 to St.2+845 RHS	09/13/14	09/13/14	09/14/14	1	A
	IR-13-00004-DUR-346-A	Installation and backfilling (2" & 6") water pipe line from St. 1+600 to St.1+638 LHS.	09/13/14	09/13/14	09/14/14	1	A
	IR-13-00004-DUR-347-A	Casting concrete for gravity wall 2nd stage from St.2+323 to St.2+343 RHS	09/14/14	09/14/14	09/15/14	1	A
	IR-13-00004-DUR-348-A	Casting concrete for gravity wall 2nd stage from St.2+835 to St.2+845 RHS	09/14/14	09/14/14	09/14/14	0	A
	IR-13-00004-DUR-349-A	Installation and backfilling for water line house connection at Sta. 1+020, 1+040, 1+104, 1+128, 1+152, 1+176, 1+192, 1+222 & 1+248 LHS	09/14/14	09/14/14	09/15/14	1	A
	IR-13-00004-DUR-350-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape & Blocks from St.0+020 to St.0+060	09/14/14	09/14/14	09/15/14	1	A
	IR-13-00004-DUR-351-A	Casting concrete for gravity wall 3rd stage from St.2+323 to St.2+343 RHS	09/15/14	09/15/14	09/16/14	1	A
	IR-13-00004-DUR-352-A	Casting concrete for gravity wall 3rd stage from St.2+835 to St.2+845 RHS	09/15/14	09/15/14	09/16/14	1	A
	IR-13-00004-DUR-353-A	Handover Sub-grade Layer from St.1+380 to St.1+460 LHS&RHS	09/15/14	09/15/14	09/16/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-354-A	Installation and backfilling for water line house connection at Sta.1+283LHS,1+305LHS, 1+359LHS, 1+374RHS, 1+390LHS, 1+400RHS, 1+412LHS, 1+418LHS, 1+420RHS, 1+442LHS, 1+440RHS, 1+466LHS, 1+480RHS, 1+515RHS, 1+530LHS, 1+535RHS, 1+550RHS, 1+760RHS, 1+736RHS, 1+782RHS, 1+818RHS, 1+850 RHS	09/15/14	09/15/14	09/16/14	1	A
	IR-13-00004-DUR-355-A	Handing over steel reinforcement works for retaining wall from St.A0+007 to St.A0+015 at access road at St.0+320.	09/16/14	09/16/14	09/17/14	1	A
	IR-13-00004-DUR-356-A	Casting concrete for gravity wall 4th stage from St.2+323 to St.2+343 RHS	09/16/14	09/16/14	09/17/14	1	A
	IR-13-00004-DUR-357-A	Casting concrete for gravity wall 4th stage from St.2+825 to St.2+835 RHS	09/16/14	09/16/14	09/17/14	1	A
	IR-13-00004-DUR-358-A	Installation and backfilling for water line house connection at Sta(1+592 RHS,1+610RHS ,1+805RHS ,1+887RHS ,1+953LHS ,1+977LHS ,2+003LHS ,1+675RHS ).	09/16/14	09/16/14	09/17/14	1	A
	IR-13-00004-DUR-359-A	Casting concrete for gravity wall 5th stage from St.2+323 to St.2+343 RHS	09/17/14	09/17/14	09/18/14	1	A
	IR-13-00004-DUR-360-A	Casting concrete for retaining wall from St.A0+007 to St.A0+015 at access road at St.0+320.	09/17/14	09/17/14	09/18/14	1	A
	IR-13-00004-DUR-361-A	Casting concrete for gravity wall 6th stage from St.2+323 to St.2+343 RHS	09/18/14	09/18/14	09/20/14	2	A
	IR-13-00004-DUR-362-A	Casting concrete for gravity wall from Sta. 2+306 to Sta. 2+323 RHS (1st stage).	09/18/14	09/20/14	09/21/14	1	A
	IR-13-00004-DUR-363-A	Sub-grade Layer from Sta. 1+260 to Sta. 1+320 except locations of catch basin and 400mm crossing pipes.	09/18/14	09/20/14	09/21/14	1	A
	IR-13-00004-DUR-364-A	Sub-grade Layer from Sta. 1+460 to Sta. 1+550.	09/18/14	09/18/14	09/20/14	2	A
	IR-13-00004-DUR-365-A	Installation and backfilling for water line house connection house at Sta. ( 1+626R, 1+760L, 1+782L, 1+790L, 1+860L, 1+940R, 2+009R ,2+030R, 2+030L, 2+040R, 2+060R,2+093R,2+124R,1+705R)	09/18/14	09/18/14	09/20/14	2	A
	IR-13-00004-DUR-366-A	Base course 1st layer from St.1+040 to St.1+220	09/20/14	09/20/14	09/21/14	1	A
	IR-13-00004-DUR-367-A	Casting concrete for foundation of water chamber at St.0+010 LHS	09/20/14	09/20/14	09/21/14	1	A
	IR-13-00004-DUR-368-A	Casting concrete for foundation of water chamber at St.0+280 LHS	09/21/14	09/21/14	09/22/14	1	A
	IR-13-00004-DUR-369-A	Sub-grade Layer from Sta. 1+640 to Sta. 1+800.	09/22/14	09/22/14	09/23/14	1	A
	IR-13-00004-DUR-370-A	Casting concrete for gravity wall from Sta. 3+370 to Sta. 3+432 LHS ( 1st stage).	09/22/14	09/22/14	09/23/14	1	A
	IR-13-00004-DUR-371-A	Casting concrete for gravity wall from Sta. 2+306 to Sta. 2+323 RHS (2nd stage).	09/22/14	09/22/14	09/23/14	1	A
	IR-13-00004-DUR-372-A	Sub-grade Layer from Sta. 1+920 to Sta. 2+120 RHS	09/23/14	09/23/14	09/23/14	0	A
	IR-13-00004-DUR-373-A	Sub-grade Layer from Sta. 2+120 to Sta. 2+200 RHS&LHS	09/23/14	09/23/14	09/23/14	0	A
	IR-13-00004-DUR-374-A	Casting concrete for water chamber walls at St.0+010 LHS	09/23/14	09/23/14	09/23/14	0	A
	IR-13-00004-DUR-375-A	Installation and backfilling for water line house connection house at Sta. (1+630L ,2+200R,2+170R,1+730L,1+700L,1+685L,2+180R,1+660L)	09/23/14	09/23/14	09/23/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-376-A	Casting concrete for gravity wall from Sta. 3+370 to Sta. 3+432 LHS ( 2nd stage).	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00004-DUR-377-A	Casting concrete for gravity wall from Sta. 2+306 to Sta. 2+323 RHS (3rd stage).	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00004-DUR-378-A	Base course 2nd layer from St.1+000 to St.1+220	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00004-DUR-379-A	Installation and backfilling for 2" steel water pipe line from Sta. 0+000 to Sta. 0+170 at access road at Sta. 0+320 RHS .	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00004-DUR-380-A	Casting concrete for gravity wall from Sta. 2+306 to Sta. 2+323 RHS (4th stage).	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00004-DUR-381-A	Start Prime coat application from St.1+040 to St.1+200 RHS&LHS	09/24/14	09/24/14	09/24/14	0	A
	IR-13-00004-DUR-382-A	Start asphalt binder layer from St.1+040 to St.0+200 RHS&LHS	09/24/14	09/24/14	09/24/14	0	A
	IR-13-00004-DUR-383-A	Base course 1st layer from St.1+980 to St.2+100 RHS&LHS	09/24/14	09/24/14	09/25/14	1	A
	IR-13-00004-DUR-384-A	Base course 1st layer from St.1+740 to St.1+880 RHS&LHS	09/24/14	09/24/14	09/25/14	1	A
	IR-13-00004-DUR-385-A	Sub-grade Layer from Sta. 1+550 to Sta. 1+640.	09/24/14	09/24/14	09/25/14	1	A
	IR-13-00004-DUR-386-A	Check installation of steel reinforcement for walls of water chamber at Sta. 0+290 LHS.	09/25/14	09/25/14	09/25/14	0	A
	IR-13-00004-DUR-387-A	Handing over Base course layer for simple access road at Sta. 0+320 RHS.	09/25/14	09/26/14	09/27/14	1	A
	IR-13-00004-DUR-388-A	Handing Base Course 1st layer from Sta. 1+220 to 1+400 RHS&LHS.	09/25/14	09/27/14	09/28/14	1	A
	IR-13-00004-DUR-389-A	Handing Base course 1st layer from Sta. 2+120 to Sta. 2+200.	09/25/14	09/27/14	09/27/14	0	A
	IR-13-00004-DUR-390-A	Casting concrete (3rd stage) for the G.W at Sta. 3+395 to 3+432.8 LHS.	09/25/14	09/27/14	09/28/14	1	A
	IR-13-00004-DUR-391-A	Base course 1 <sup>st</sup> layer from Sta. 1+880 to 2+000	09/25/14	09/25/14	09/27/14	2	A
	IR-13-00004-DUR-392-A	Casting concrete for gravity wall from Sta. 2+306 to Sta. 2+323 RHS (5th stage).	09/27/14	09/27/14	09/28/14	1	A
	IR-13-00004-DUR-393-A	Casting concrete for the G.W at Sta. 3+395 to 3+432.8 LHS 4th stage.	09/28/14	09/28/14	09/29/14	1	A
	IR-13-00004-DUR-394-A	Start Prime coat application at simple access road at Sta. 0+320.	09/29/14	09/29/14	09/30/14	1	A
	IR-13-00004-DUR-395-A	Casting concrete for the G.W at Sta. 3+395 to 3+432.8 LHS 5th stage.	09/29/14	09/29/14	09/30/14	1	A
	IR-13-00004-DUR-396-A	Start asphalt works from at simple access road at Sta. 0+320.	09/29/14	09/29/14	09/30/14	1	A
	IR-13-00004-DUR-397-A	Start tack coat application at roundabout area.	09/30/14	09/30/14	09/30/14	0	A
	IR-13-00004-DUR-398-A	Start asphalt works at roundabout area.	09/30/14	09/30/14	09/30/14	0	A
	IR-13-00004-DUR-399-A	Base course 2nd layer from St.1+780 to St.2+180 RHS & from St.1+780 to St.2+000 LHS	09/30/14	09/30/14	09/30/14	0	A
	IR-13-00004-DUR-400-A	Start Prime coat application from St.1+780 to St.2+180 RHS and from St.1+780 to St.2+000 LHS	10/01/14	10/01/14	10/02/14	1	A
	IR-13-00004-DUR-401-A	Start asphalt works from St.1+780 to St.2+180 RHS and from St.1+780 to St.2+000 LHS	10/01/14	10/01/14	10/02/14	1	A
	IR-13-00004-DUR-402-A	Base course 1 <sup>st</sup> layer from Sta. 1+480 to 1+560 RHS&LHS	10/08/14	10/08/14	10/09/14	1	A
	IR-13-00004-DUR-403-A	Handing over B.C 1st layer 1+560 to 1+740 RHS&LHS.	10/09/14	10/11/14	10/12/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-404-A	Handing B.C 2nd layer from Sta. 2+000 to Sta. 2+180 LHS.	10/12/14	10/12/14	10/13/14	1	A
	IR-13-00004-DUR-405-A	Handing B.C 2nd layer from Sta. 1+200 to 1+400 RHS&LHS	10/12/14	10/12/14	10/13/14	1	A
	IR-13-00004-DUR-406-A	curbstone Installation works except median closing area from St.1+060 to St.1+190	10/13/14	10/13/14	10/14/14	1	C
	IR-13-00004-DUR-406-B	curbstone Installation works except median closing area from St.1+060 to St.1+190	01/03/15	01/04/15	01/04/15	0	A
	IR-13-00004-DUR-407-A	Start excavation works to match sub grade level from St.2+200 to 3+000	10/13/14	10/13/14	10/15/14	2	D
	IR-13-00004-DUR-407-B	Start excavation works to match sub grade level from St.2+200 to 3+000	11/09/14	11/09/14	11/11/14	2	A
	IR-13-00004-DUR-408-A	Casting concrete for the G.W at Sta. 3+339 to 3+351.6 LHS 1st stage.	10/13/14	10/13/14	10/14/14	1	A
	IR-13-00004-DUR-409-A	Casting concrete for the G.W at Sta. 3+459 to 3+470.6 LHS 1st stage.	10/13/14	10/13/14	10/14/14	1	A
	IR-13-00004-DUR-410-A	Casting concrete for the G.W at Sta. 3+480.7 to 3+500.7 LHS 1st stage.	10/13/14	10/13/14	10/14/14	1	A
	IR-13-00004-DUR-411-A	Sample for street lighting pole foundation at Sta. 1+100.	10/13/14	10/13/14	10/14/14	1	D
	IR-13-00004-DUR-411-B	Sample for street lighting pole foundation at Sta. 1+130.	10/18/14	10/18/14	10/19/14	1	A
	IR-13-00004-DUR-412-A	Sub-grade Layer at access road at Sta. 0+517 LHS.	10/14/14	10/14/14	10/15/14	1	A
	IR-13-00004-DUR-413-A	Casting concrete for the G.W at Sta. 3+339 to 3+351.6 LHS 2nd stage.	10/14/14	10/14/14	10/15/14	1	A
	IR-13-00004-DUR-414-A	Casting concrete for the G.W at Sta. 3+459 to 3+470.6 LHS 2nd stage.	10/14/14	10/14/14	10/15/14	1	A
	IR-13-00004-DUR-415-A	Casting concrete for the G.W at Sta. 3+480.7 to 3+500.7 LHS 2nd stage.	10/14/14	10/14/14	10/15/14	1	A
	IR-13-00004-DUR-416-A	Casting concrete for the G.W at Sta. 3+500.7 to 3+514.07 LHS 1st stage.	10/15/14	10/15/14	10/15/14	0	A
	IR-13-00004-DUR-417-A	Base course 1 <sup>st</sup> layer from Sta. 1+400 to 1+480 LHS	10/15/14	10/15/14	10/15/14	0	A
	IR-13-00004-DUR-418-A	Check installation of steel reinforcement for foundation of water chamber-04 at Sta. 1+060 LHS.	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00004-DUR-419-A	Installation and backfilling of storm water Pipe from Sta. 2+256 to Sta. 2+297.	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00004-DUR-420-A	Casting concrete for the G.W at Sta. 3+339 to 3+351.6 LHS 3rd stage.	10/16/14	10/18/14	10/19/14	1	A
	IR-13-00004-DUR-421-A	Casting concrete for the G.W at Sta. 3+459 to 3+470.6 LHS 3rd stage.	10/16/14	10/18/14	10/19/14	1	A
	IR-13-00004-DUR-422-A	Casting concrete for the G.W at Sta. 3+480.7 to 3+500.7 LHS 3rd stage.	10/16/14	10/18/14	10/19/14	1	A
	IR-13-00004-DUR-423-A	Casting concrete for the G.W at Sta. 3+500.7 to 3+514.07 LHS 2nd stage.	10/16/14	10/18/14	10/19/14	1	D
	IR-13-00004-DUR-423-B	Casting concrete for the G.W at Sta. 3+500.7 to 3+514.07 LHS 2nd stage.	10/22/14	10/22/14	10/23/14	1	A
	IR-13-00004-DUR-424-A	Handing over base course Layer at access road at Sta. 0+517 LHS.	10/16/14	10/18/14	10/19/14	1	A
	IR-13-00004-DUR-425-A	Handing over Base course 2nd layer from Sta. 1+400 to Sta. 1+780 LHS.	10/16/14	10/18/14	10/19/14	1	C
	IR-13-00004-DUR-425-B	Handing over Base course 2nd layer from Sta. 1+400 to Sta. 1+780 LHS.	10/23/14	10/23/14	10/23/14	0	A
	IR-13-00004-DUR-426-A	Handing over installation storm 600 dia from MH02 at Sta. 2+297.59 to MH03 at Sta. 2+346.94.	10/16/14	10/18/14	10/19/14	1	D
	IR-13-00004-DUR-426-B	Handing over installation storm 600 dia from MH02 at Sta. 2+297.59 to MH03 at Sta. 2+346.94.	10/26/14	10/26/14	10/27/14	1	A
	IR-13-00004-DUR-427-A	Check installation of steel reinforcement for wall of water chamber-04 at Sta. 1+060 LHS.	10/20/14	10/20/14	10/20/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-428-A	Installation and backfilling for water line house connection house at Sta. (2+297L, 2+320L , 2+347L ,2+464L ,2+440L ,2+422L)	10/20/14	10/20/14	10/21/14	1	A
	IR-13-00004-DUR-429-A	Handing over installation & backfilling storm 600 dia from MH03 at Sta. 2+347 to MH04 at Sta. 2+387.5.	10/21/14	10/21/14	10/22/14	1	A
	IR-13-00004-DUR-430-A	Casting concrete for the G.W at Sta. 3+480.7 to 3+500.7 LHS 4th stage.	10/22/14	10/22/14	10/23/14	1	A
	IR-13-00004-DUR-431-A	Base course 2nd layer from Sta. 1+400 to Sta. 1+780 RHS.	10/23/14	10/23/14	10/25/14	2	A
	IR-13-00004-DUR-432-A	casting concrete for walls of storm water MH-02 at Sta. 2+297	10/23/14	10/23/14	10/23/14	0	A
	IR-13-00004-DUR-433-A	Casting concrete for sidewalk at simple access at Sta. 0+520 LHS	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00004-DUR-434-A	Casting concrete for the G.W at Sta. 3+500.7 to 3+514.07 LHS 3rd stage.	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00004-DUR-435-A	Curbstone works at simple access at Sta. 0+520 LHS.	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00004-DUR-436-A	Installation and backfilling for 2" water pipe line from Sta. 2+333 to Sta. 2+432 RHS .	10/23/14	10/23/14	10/25/14	2	A
	IR-13-00004-DUR-437-A	Installation and backfilling for water line house connection house 3/4" at Sta. (2+260, 2+278, 2+366,2+384)& 2" at Sta. 0+850LHS	10/25/14	10/25/14	10/26/14	1	A
	IR-13-00004-DUR-438-A	Start Prime coat application from Sta. 1+200 to Sta. 1+500 LHS&RHS.	10/26/14	10/26/14	10/27/14	1	A
	IR-13-00004-DUR-439-A	Start asphalt works from Sta. 1+200 to Sta. 1+500 LHS&RHS.	10/26/14	10/26/14	10/27/14	1	A
	IR-13-00004-DUR-440-A	Sub-grade Layer from Sta. 2+660 to Sta. 2+760 LHS&RHS.	10/26/14	10/26/14	10/27/14	1	A
	IR-13-00004-DUR-441-A	Base course works at simple access at Sta. 1+630 RHS	10/27/14	10/27/14	10/28/14	1	A
	IR-13-00004-DUR-442-A	Base course works at simple access at Sta. 1+620 LHS.	10/27/14	10/27/14	10/28/14	1	A
	IR-13-00004-DUR-443-A	Casting concrete for the G.W at Sta. 3+500.7 to 3+514.07 LHS 4th stage.	10/27/14	10/27/14	10/28/14	1	A
	IR-13-00004-DUR-444-A	Continue asphalt works from Sta. 1+500 to Sta. 1+780 LHS&RHS.	10/27/14	10/27/14	10/28/14	1	A
	IR-13-00004-DUR-445-A	Start Prime coat application from at simple access at Sta. 1+620 LHS.	10/27/14	10/27/14	10/28/14	1	A
	IR-13-00004-DUR-446-A	Start Prime coat application from at simple access at Sta. 1+630 RHS.	10/28/14	10/27/14	10/28/14	1	A
	IR-13-00004-DUR-447-A	Start Prime coat application at simple access at Sta. 0+520 LHS.	10/28/14	10/28/14	10/29/14	1	A
	IR-13-00004-DUR-448-A	Start asphalt works at simple access at Sta. 0+520 LHS.	10/28/14	10/28/14	10/29/14	1	A
	IR-13-00004-DUR-449-A	Casting concrete for stair at Sta. 1+004 LHS	10/28/14	10/28/14	10/29/14	1	A
	IR-13-00004-DUR-450-A	Base course and check steel reinforcement for sidewalk from Sta. 1+156 to Sta. 1+186 RHS.	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00004-DUR-451-A	start handrail installation for roundabout Area at Sta. 0+000 RHS	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00004-DUR-452-A	casting concrete for street lighting pole foundation from Sta. 1+840 to Sta. 2+160 .	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00004-DUR-453-A	Installation and backfilling for water line house connection house 3/4" at Sta. (2+622LHS,2+652LHS,2+676LHS,2+695LHS,2+749LHS,2+765LHS,2+843LH S,2+881LHS,2+893LHS,2+923LHS,3+057LHS,3+100LHS) & 2" at Sta. (2+790LHS,2+976LHS, 2+708LHS)	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00004-DUR-454-A	Sub-grade Layer from Sta. 2+220 to Sta. 2+280 RHS.	10/29/14	10/29/14	10/30/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-455-A	Sub-grade Layer from Sta. 2+400 to Sta. 2+500 LHS & RHS.	10/30/14	10/30/14	11/01/14	2	C
	IR-13-00004-DUR-455-B	Sub-grade Layer from Sta. 2+420 to Sta. 2+500 LHS & RHS.	11/03/14	11/03/14	11/03/14	0	A
	IR-13-00004-DUR-456-A	Casting concrete for sidewalk from Sta. 1+150 to Sta. 1+180 RHS	10/30/14	10/30/14	10/30/14	0	A
	IR-13-00004-DUR-457-A	Installation handrail at roundabout at Sta. 0+000.	10/30/14	11/01/14	11/02/14	1	A
	IR-13-00004-DUR-458-A	Sub grade works for simple access roads at Sta. 0+950 RHS, Sta. 0+470 RHS, Sta. 0+700 LHS, Sta. 0+860 LHS, Sta. 0+920 LHS.	10/30/14	11/01/14	11/02/14	1	A
	IR-13-00004-DUR-459-A	Casting concrete for street lighting pole foundation from Sta. 1+200 to Sta. 1+500	10/30/14	11/01/14	11/02/14	1	A
	IR-13-00004-DUR-460-A	Installation and backfilling for water line house connection house 3/4" at Sta. (2+479RHS,2+550RHS,2+574RHS,2+593RHS,2+622RHS,2+677RHS)	10/30/14	10/30/14	11/01/14	2	A
	IR-13-00004-DUR-461-A	Sub-grade Layer from Sta. 2+500 to Sta. 2+660 RHS & LHS.	11/02/14	11/02/14	11/03/14	1	C
	IR-13-00004-DUR-461-B	Sub-grade Layer from Sta. 2+500 to Sta. 2+660 RHS & LHS.	11/03/14	11/03/14	11/03/14	0	A
	IR-13-00004-DUR-462-A	Handing over installation storm 600 dia from MH02 to MH05 at Sta. 2+300.	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-463-A	Installation and backfilling for water line house connection house 3/4" at Sta. ( 2+504RHS, 2+455RHS, 2+442RHS, 2+730RHS, 2+767RHS, 2+724RHS) and 2" at Sta.(2+473RHS, 2+516 2" RHS)	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-464-A	Casting concrete for stair at simple access at Sta. 1+630 RHS	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00004-DUR-465-A	Casting concrete for street lighting pole foundation from Sta. 1+500 to Sta. 1+840	11/03/14	11/03/14	11/04/14	1	A
	IR-13-00004-DUR-466-A	Sub-grade Layer from Sta. 2+220 to Sta. 2+280 LHS.	11/03/14	11/03/14	11/04/14	1	A
	IR-13-00004-DUR-467-A	excavated reduce level for G.W from 3+376 to 3+390 LHS	11/03/14	11/03/14	11/04/14	1	D
	IR-13-00004-DUR-467-B	excavated reduce level for G.W from 3+376 to 3+390 LHS	12/30/14	12/30/14	12/31/14	1	A
	IR-13-00004-DUR-468-A	excavated reduce level for G.W from 3+514.07 to 3+533 LHS	11/03/14	11/03/14	11/04/14	1	D
	IR-13-00004-DUR-468-B	excavated reduce level for G.W from 3+514.07 to 3+533 LHS	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00004-DUR-469-A	Casting concrete for the G.W at Sta. 3+514 to 3+533 1st stage.	11/06/14	11/08/14	11/08/14	0	A
	IR-13-00004-DUR-470-A	Casting concrete for street lighting pole foundation from Sta. 0+000 to Sta. 0+200	11/06/14	11/08/14	11/09/14	1	A
	IR-13-00004-DUR-471-A	Sub grade layer from Sta. 2+280 to 2+420	11/06/14	11/08/14	11/08/14	0	A
	IR-13-00004-DUR-472-A	Continue casting concrete 2nd stage at gravity wall from Sta. 3+514.07 to Sta. 3+533 LHS.	11/09/14	11/09/14	11/10/14	1	A
	IR-13-00004-DUR-473-A	Casting concrete for street lighting pole foundation from Sta. 0+200 to Sta. 0+500	11/10/14	11/10/14	11/11/14	1	A
	IR-13-00004-DUR-474-A	Casting concrete for stair from Sta. 1+857 to Sta. 1+880 LHS	11/10/14	11/10/14	11/11/14	1	A
	IR-13-00004-DUR-475-A	Bituminous Coating prior to start Backfilling Works for gravity Walls at the following station; from Sta. 3+339 to Sta. 3+351 LHS, from Sta. 3+459 to 3+470.6 LHS & from Sta. 3+500.7 to Sta. 3+514.07 LHS	11/10/14	11/10/14	11/11/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-476-A	electrical fittings for street lighting (Junction box board panel & 3*1.5mm lighting cable)	11/10/14	11/11/14	11/12/14	1	A
	IR-13-00004-DUR-477-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.2+200 to 2+360	11/11/14	11/11/14	11/12/14	1	A
	IR-13-00004-DUR-478-A	Start installation of electrical lighting pole from Sta. 0+010 to Sta. 0+500	11/11/14	11/11/14	11/12/14	1	A
	IR-13-00004-DUR-479-A	installation of water mechanical fitting for water chamber-02 at Sta. 0+280 LHS	11/12/14	11/12/14	11/13/14	1	D
	IR-13-00004-DUR-479-B	installation of water mechanical fitting for water chamber-02 at Sta. 0+280 LHS	03/17/15	03/17/15	03/17/15	0	A
	IR-13-00004-DUR-480-A	Visual inspection for street lighting Flexure and Lamp	11/12/14	11/12/14	11/12/14	0	D
	IR-13-00004-DUR-480-B	Visual inspection for street lighting Flexure and Lamp	12/30/14	12/30/14	12/31/14	1	A
	IR-13-00004-DUR-481-A	Close out of October 2014 environmental check list.	11/12/14	11/13/14	11/13/14	1	D
	IR-13-00004-DUR-481-B	Close out of October 2014 environmental check list.	11/30/14	12/01/14	12/02/14	1	C
	IR-13-00004-DUR-481-C	Close out of October 2014 environmental check list.	03/18/15	03/18/15	03/18/15	0	A
	IR-13-00004-DUR-482-A	casting concrete for street lighting pole foundation from sta. 0+500 to 0+700	11/13/14	11/15/14	11/17/14	2	A
	IR-13-00004-DUR-483-A	casting concrete for street lighting pole foundation from sta. 0+700 to 0+900	11/13/14	11/16/14	11/17/14	1	A
	IR-13-00004-DUR-484-A	Installation for storm water line st 2+840 to 2+860 RHS	11/13/14	11/13/14	11/13/14	0	A
	IR-13-00004-DUR-485-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.2+360 to 2+860	11/13/14	11/13/14	11/13/14	0	A
	IR-13-00004-DUR-486-A	Continue casting concrete 3rd stage at gravity wall from Sta. 3+514.07 to Sta. 3+533 LHS.	11/13/14	11/16/14	11/17/14	1	A
	IR-13-00004-DUR-487-A	Continue casting concrete 1st stage at gravity wall from Sta. 3+377 to Sta. 3+390 LHS.	11/13/14	11/16/14	11/18/14	2	D
	IR-13-00004-DUR-487-B	Casting concrete 1st stage at gravity wall from Sta. 3+377 to Sta. 3+395 LHS.	11/19/14	11/19/14	11/20/14	1	A
	IR-13-00004-DUR-488-A	Base course 1st layer from Sta. 2+200 to Sta. 2+400 .	11/13/14	11/15/14	11/15/14	0	A
	IR-13-00004-DUR-489-A	Casting concrete for sidewalk from Sta. 1+400 to Sta. 1+440 RHS	11/13/14	11/15/14	11/17/14	2	A
	IR-13-00004-DUR-490-A	Base course 1st layer from Sta. 2+400 to Sta. 2+720 .	11/16/14	11/16/14	11/17/14	1	A
	IR-13-00004-DUR-491-A	Start Ruble concrete for the Retaining wall from Sta. 3+635 to 3+652	11/17/14	11/17/14	11/17/14	0	A
	IR-13-00004-DUR-492-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.2+860 to 3+150	11/18/14	11/17/14	11/18/14	1	A
	IR-13-00004-DUR-493-A	Casting concrete for stair from Sta. 1+415 to Sta. 1+422 RHS	11/18/14	11/17/14	11/18/14	1	A
	IR-13-00004-DUR-494-A	Installation 400mm pipe for storm water line and casting encasement concrete at Sta. 2+253	11/18/14	11/18/14	11/19/14	1	A
	IR-13-00004-DUR-495-A	Casting Ruble concrete for the Retaining wall from Sta. 3+639 to 3+654 2nd stage	11/18/14	11/18/14	11/19/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-496-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.3+150 to 3+300	11/19/14	11/18/14	11/19/14	1	A
	IR-13-00004-DUR-497-A	Handing over Base course layer for simple access roads at Sta. 0+950 RHS, Sta. 0+470 RHS, Sta. 0+720 LHS, Sta. 0+850 LHS, Sta. 0+920 LHS and Sta. 0+770 RHS.	11/19/14	11/19/14	11/20/14	1	A
	IR-13-00004-DUR-498-A	Casting concrete for sidewalk from Sta. 1+350 to Sta. 1+400 RHS	11/19/14	11/19/14	11/20/14	1	A
	IR-13-00004-DUR-499-A	Casting Ruble concrete for the Retaining wall from Sta. 3+639 to 3+654 3rd stage	11/19/14	11/20/14	11/20/14	0	A
	IR-13-00004-DUR-500-A	Casting blinding concrete for the Retaining wall from Sta. 3+624 to 3+639 LHS	11/19/14	11/20/14	11/20/14	0	A
	IR-13-00004-DUR-501-A	Sub-grade Layer from Sta. 2+760 to 2+840 LHS&RHS.	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00004-DUR-502-A	Handing over B.C 2nd layer from Sta. 2+420 to 2+700	11/20/14	11/20/14	11/22/14	2	D
	IR-13-00004-DUR-502-B	Handing over B.C 2nd layer from Sta. 2+420 to 2+700	12/04/14	12/04/14	12/04/14	0	A
	IR-13-00004-DUR-503-A	Casting concrete for sidewalk from Sta. 1+992 to Sta. 2+010 RHS and 1+875 to Sta. 1+887 RHS	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00004-DUR-504-A	Start prime coat spraying & asphalt Wearing layer for simple access roads at Sta. 0+950 RHS, Sta. 0+470 RHS, Sta. 0+720 LHS, Sta. 0+850 LHS, Sta. 0+920 LHS and Sta. 0+770 RHS.	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00004-DUR-505-A	Casting concrete 4th stage at gravity wall from Sta. 3+514.07 to Sta. 3+533 LHS.	11/25/14	11/25/14	11/25/14	0	A
	IR-13-00004-DUR-506-A	Casting concrete 2nd stage at gravity wall from Sta. 3+377 to Sta. 3+395 LHS.	11/25/14	11/25/14	11/25/14	0	A
	IR-13-00004-DUR-507-A	Base course 1st layer from Sta. 2+720 to Sta. 2+840 .	11/30/14	11/29/14	11/30/14	1	A
	IR-13-00004-DUR-508-A	Casting concrete 3rd stage at gravity wall from Sta. 3+377 to Sta. 3+395 LHS.	11/30/14	11/30/14	11/30/14	1	A
	IR-13-00004-DUR-509-A	Casting concrete for sidewalk from Sta. 0+000 to Sta. 0+050 at out fall direction at Sta. 0+320	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00004-DUR-510-A	Installation handrail from Sta. 0+250 to Sta. 0+275 RHS.	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00004-DUR-511-A	Installation 4" water pipe line (feeder line connecting with 6" main pipe line) crossing road at Sta. 1+050 .	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00004-DUR-512-A	Installation and backfilling for 2" water pipe line crossing road at Sta. 1+050 .	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00004-DUR-513-A	Installation and backfilling of service box MHs and installing of 2" threaded gate valve at Sta. 1+050 RHS	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00004-DUR-514-A	Installation and backfilling of 8" UPVC drainage pipes at sidewalk from Sta. 0+238 to Sta. 0+259.6 LHS.	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00004-DUR-515-A	Casting concrete for foundation of Retaining wall from Sta. 3+620 to 3+654 LHS	12/02/14	12/02/14	12/02/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-516-A	Start casting concrete for concrete edge wall foundation at intersection at Sta. 0+330 RHS.	12/03/14	12/03/14	12/03/14	0	A
	IR-13-00004-DUR-517-A	installation of storm 600mm dia from Sta. 2+861 to Sta. 2+892 RHS.	12/03/14	12/03/14	12/03/14	0	A
	IR-13-00004-DUR-518-A	Casting concrete for sidewalk from Sta. 0+224 to Sta. 0+275 RHS and from Sta. 0+250 to Sta. 0+260 LHS, and for Median from Sta. 0+180 to Sta. 0+213	12/03/14	12/03/14	12/03/14	0	A
	IR-13-00004-DUR-519-A	Casting concrete 1st stage at gravity wall from Sta. 3+308 to Sta. 3+327.5 LHS.	12/04/14	12/04/14	12/04/14	0	A
	IR-13-00004-DUR-520-A	Casting concrete for storm water MH wall at outfall at St.1+300 LHS.	12/04/14	12/04/14	12/07/14	3	D
	IR-13-00004-DUR-521-A	Start Prime coat application Sta. 2+200 to 2+680.	12/04/14	12/06/14	12/07/14	1	A
	IR-13-00004-DUR-522-A	Start asphalt binder layer from St.2+200 to St.2+680 RHS&LHS.	12/04/14	12/06/14	12/07/14	1	A
	IR-13-00004-DUR-523-A	Handing over B.C 2nd layer from Sta. 2+200 to 2+420	12/04/14	12/04/14	12/06/14	2	A
	IR-13-00004-DUR-524-A	Casting concrete for sidewalk from Sta. 1+010 to Sta. 1+055 RHS	12/07/14	12/06/14	12/07/14	1	C
	IR-13-00004-DUR-524-B	Casting concrete for sidewalk from Sta. 1+018 to Sta. 1+055 RHS (except location of garbage container lay at Sta. 1+040 due to shop owner objection)	01/19/15	01/19/15	01/19/15	0	A
	IR-13-00004-DUR-525-A	Casting concrete for sidewalk from Sta. 1+590 to Sta. 1+615 RHS	12/07/14	12/06/14	12/07/14	1	A
	IR-13-00004-DUR-526-A	Casting concrete for edge wall (at lower level) at intersection at Sta. 0+330 RHS.	12/07/14	12/06/14	12/07/14	1	A
	IR-13-00004-DUR-527-A	Casting concrete for foundation of the wall (between MH#1 and combined MH#2 & MH#3) at outfall at Sta. 1+300 LHS.	12/07/14	12/06/14	12/07/14	1	D
	IR-13-00004-DUR-528-A	Casting concrete for sidewalk from Sta. 1+630 to Sta. 1+670 RHS	12/07/14	12/07/14	12/08/14	1	A
	IR-13-00004-DUR-529-A	Start Prime coat application Sta. 2+680 to 2+780 LHS.	12/08/14	12/07/14	12/08/14	1	A
	IR-13-00004-DUR-530-A	Start asphalt binder layer from St.2+680 to St.2+780 LHS.	12/08/14	12/07/14	12/08/14	1	A
	IR-13-00004-DUR-531-A	Casting concrete 2nd stage at gravity wall from Sta. 3+308 to Sta. 3+327.5 LHS.	12/08/14	12/08/14	12/08/14	0	A
	IR-13-00004-DUR-532-A	Installation of Street Lighting Poles from St.0+500 to 1+000.	12/08/14	12/08/14	12/09/14	1	A
	IR-13-00004-DUR-533-A	check steel reinforcement and casting concrete for median from Sta. 1+280 to Sta. 1+770	12/08/14	12/08/14	12/09/14	1	A
	IR-13-00004-DUR-534-A	Sub-grade Layer from Sta. 3+000 to 3+100 LHS&RHS.	12/08/14	12/08/14	12/09/14	1	A
	IR-13-00004-DUR-535-A	installation 2'' water line house connection at Sta. 1+690 LHS, Sta. 1+845 LHS, Sta. 1+892 RHS, Sta. 1+930 LHS.	12/09/14	12/08/14	12/09/14	1	A
	IR-13-00004-DUR-536-A	Sub-grade Layer from Sta. 3+100 to 3+140 LHS&RHS.	12/09/14	12/08/14	12/09/14	1	A
	IR-13-00004-DUR-537-A	Casting concrete 3rd stage at gravity wall from Sta. 3+308 to Sta. 3+327.5 LHS.	12/09/14	12/09/14	12/10/14	1	A
	IR-13-00004-DUR-538-A	Installation 2'' water line house connection at Sta. 0+085 LHS, Sta. 0+914 LHS, Sta. 0+973 LHS, 2+061 RHS and 2+225 RHS.	12/10/14	12/09/14	12/10/14	1	A
	IR-13-00004-DUR-539-A	Casting concrete for sidewalk from Sta. 1+548 to Sta. 1+578 RHS	12/10/14	12/09/14	12/10/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-540-A	installation of storm 600mm dia from Sta. 2+894.85 to Sta. 2+944.85.	12/10/14	12/09/14	12/10/14	1	A
	IR-13-00004-DUR-541-A	check steel reinforcement for Retaining wall from Sta. 3+620 to 3+654 LHS	12/10/14	12/10/14	12/11/14	1	A
	IR-13-00004-DUR-542-A	Casting concrete for sidewalk from Sta. 0+230 to Sta. 0+250 LHS	12/10/14	12/10/14	12/11/14	1	A
	IR-13-00004-DUR-543-A	handing over 2nd topping layer from Sta.3+180 to Sta. 3+250 RHS.	12/13/14	12/11/14	12/13/14	2	A
	IR-13-00004-DUR-544-A	Installation of Storm Water Pipe 400 mm UPVC pipe with Catch Basin at Crossing from St.1+695 to St.1+610 LHS.	12/13/14	12/11/14	12/13/14	2	C
	IR-13-00004-DUR-544-B	Installation of Storm Water Pipe 400 mm UPVC pipe with Catch Basin at Crossing from St.1+695 to St.1+610 LHS.	12/30/14	12/30/14	12/31/14	1	A
	IR-13-00004-DUR-545-A	installation and backfilling of storm 800mm dia from Sta. 2+944 to Sta. 2+990.	12/13/14	12/11/14	12/13/14	2	A
	IR-13-00004-DUR-546-A	Casting concrete for sidewalk from Sta. 1+200 to Sta. 1+240 RHS, from Sta. 1+070 to Sta. 1+120 RHS	12/13/14	12/13/14	12/14/14	1	A
	IR-13-00004-DUR-547-A	Casting concrete for retaining wall 1st stage from Sta. 3+620 to Sta. 3+654 LHS.	12/13/14	12/13/14	12/14/14	1	A
	IR-13-00004-DUR-548-A	6" Water line Pressure test from Sta. 0+000 to 2+150.	12/15/14	12/14/14	12/15/14	1	A
	IR-13-00004-DUR-549-A	2" Water line pressure test from Sta. 0+400 to Sta. 1+050 LHS	12/15/14	12/14/14	12/15/14	1	A
	IR-13-00004-DUR-550-A	installation and backfilling of storm 800mm dia from Sta. 2+990 to outfall MH.	12/15/14	12/14/14	12/15/14	1	A
	IR-13-00004-DUR-551-A	Casting concrete for retaining wall 2nd stage from Sta. 3+620 to Sta. 3+654 LHS.	12/15/14	12/15/14	12/16/14	1	A
	IR-13-00004-DUR-552-A	Handrail installation works from Sta. 0+470 to Sta. 0+540 RHS	12/15/14	12/15/14	12/15/14	0	A
	IR-13-00004-DUR-553-A	2" Water line pressure test from Sta. 0+000 to Sta. 0+400 RHS	12/15/14	12/15/14	12/15/14	0	A
	IR-13-00004-DUR-554-A	Casting concrete and installation of 4" UPVC pipes for sidewalk from Sta. 1+670 to Sta. 1+700 RHS.	12/16/14	12/15/14	12/16/14	1	A
	IR-13-00004-DUR-555-A	Casting concrete for sidewalk from Sta. 1+760 to Sta. 1+782 LHS.	12/16/14	12/16/14	12/17/14	1	A
	IR-13-00004-DUR-556-A	Sub-grade Layer from Sta. 2+840 to Sta. 2+950 RHS & LHS.	12/16/14	12/16/14	12/17/14	1	A
	IR-13-00004-DUR-557-A	Start Tack coat application from Sta. 0+000 to Sta. 0+400 RHS.	12/17/14	12/17/14	12/18/14	1	A
	IR-13-00004-DUR-558-A	Start Asphalt wearing layer from Sta. 0+000 to Sta. 0+400 RHS.	12/17/14	12/17/14	12/18/14	1	A
	IR-13-00004-DUR-559-A	Casting concrete for sidewalk from Sta. 2+070 to Sta. 2+130 RHS.	12/17/14	12/17/14	12/18/14	1	A
	IR-13-00004-DUR-560-A	Casting concrete for wall of MH#4 at outfall at Sta. 1+300 LHS.	12/18/14	12/17/14	12/18/14	1	D
	IR-13-00004-DUR-561-A	Casting concrete for gravity wall 1st stage from Sta. 3+395 to Sta. 3+417 LHS.	12/18/14	12/18/14	12/18/14	0	A
	IR-13-00004-DUR-562-A	Casting concrete for street lighting pole foundation from Sta. 2+160 to Sta. 2+500	12/18/14	12/18/14	12/18/14	0	A
	IR-13-00004-DUR-563-A	Installation of storm 600mm dia from Sta. 3+211 to Sta. 3+241.70 LHS	12/18/14	12/18/14	12/18/14	0	A
	IR-13-00004-DUR-564-A	Casting concrete for sidewalk from Sta. 1+880 to Sta. 2+080 LHS.	12/21/14	12/20/14	12/21/14	1	A
	IR-13-00004-DUR-565-A	Base course 1st layer from Sta. 2+840 to Sta. 2+950 & from Sta. 3+000 to Sta. 3+140 LHS.	12/21/14	12/20/14	12/21/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-566-A	Sub-grade Layer from Sta. 2+950 to Sta. 3+000 LHS.	12/21/14	12/21/14	12/21/14	0	A
	IR-13-00004-DUR-567-A	Casting concrete for wall of MH#5 at outfall at Sta. 1+300 LHS.	12/21/14	12/21/14	12/21/14	0	D
	IR-13-00004-DUR-568-A	Casting concrete for gravity wall 2nd stage from Sta. 3+395 to Sta. 3+417 LHS.	12/22/14	12/22/14	12/22/14	0	A
	IR-13-00004-DUR-569-A	Installation of storm 600mm dia from Sta. 3+180 to Sta. 3+210 LHS	12/22/14	12/22/14	12/22/14	0	A
	IR-13-00004-DUR-570-A	2" Water line pressure test from Sta. 0+400 to Sta. 1+050 RHS	12/22/14	12/22/14	12/22/14	0	A
	IR-13-00004-DUR-571-A	Casting concrete for sidewalk from Sta. 2+080 to Sta. 2+160 LHS.	12/23/14	12/23/14	12/24/14	1	A
	IR-13-00004-DUR-572-A	Casting concrete for sidewalk from Sta. 2+240 to Sta. 2+280 LHS.	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-573-A	Casting concrete for gravity wall 1st stage from Sta. 3+417 to Sta. 3+434 LHS.	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-574-A	continue Tack coat application from Sta. 0+400 to Sta. 0+940 RHS.	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-575-A	continue Asphalt wearing layer from Sta. 0+400 to Sta. 0+940 RHS.	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-576-A	Casting concrete for gravity wall 3rd stage from Sta. 3+395 to Sta. 3+417 LHS.	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-577-A	Casting concrete for sidewalk from Sta. 1+460 to Sta. 1+480 RHS.	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-578-A	Casting concrete for concrete walls for water well at Sta. 1+100 LHS ( As per engineer verbal instruction ).	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-579-A	Casting concrete for sidewalk from Sta. 2+160 to Sta. 2+230 RHS.	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-580-A	Milling works for the additional section of Dura main road as per site memo number SM-13-00012-MRSII-122	12/24/14	12/24/14	12/24/14	0	A
	IR-13-00004-DUR-581-A	Start Tack coat application for the additional section of Dura main road from Sta. 0+000 to Sta. 0-286 RHS & LHS, as per site memo number SM-13-00012-MRSII-122.	12/25/14	12/25/14	12/25/14	0	A
	IR-13-00004-DUR-582-A	Start Asphalt wearing layer for the additional section of Dura main road from Sta. 0+000 to Sta. 0-286 RHS & LHS, as per site memo number SM-13-00012-MRSII-122.	12/25/14	12/25/14	12/25/14	0	A
	IR-13-00004-DUR-583-A	Installation and backfilling for 2" water pipe line crossing road from St.2+780 to 3+000 RHS	12/27/14	12/27/14	12/27/14	0	A
	IR-13-00004-DUR-584-A	Casting concrete for top slab of water well at Sta. 1+100 LHS ( As per engineer verbal instruction )	12/27/14	12/27/14	12/27/14	0	A
	IR-13-00004-DUR-585-A	Start Tack coat application for the additional section of Dura main road from Sta. 0+140 to Sta. 0+566 RHS & LHS, as per site memo number SM-13-00012-MRSII-122.	12/27/14	12/27/14	12/27/14	0	A
	IR-13-00004-DUR-586-A	Start Asphalt wearing layer for the additional section of Dura main road from Sta. 0+140 to Sta. 0+566 RHS & LHS, as per site memo number SM-13-00012-MRSII-122.	12/27/14	12/27/14	12/27/14	0	A
	IR-13-00004-DUR-587-A	2" Water line pressure test from Sta. 0+000 to Sta. 0+400 LHS	12/27/14	12/27/14	12/27/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-588-A	Sub-grade Layer from Sta. 2+950 to Sta. 3+000 RHS.	12/28/14	12/28/14	12/29/14	1	A
	IR-13-00004-DUR-589-A	Sub-grade Layer from Sta. 3+140 to Sta. 3+260 RHS & LHS.	12/28/14	12/28/14	12/29/14	1	A
	IR-13-00004-DUR-590-A	Installation and backfilling for 2" water pipe line crossing road from St.3+000 to 3+162.1 RHS	12/28/14	12/28/14	12/29/14	1	A
	IR-13-00004-DUR-591-A	Casting concrete for gravity wall 2nd stage from Sta. 3+413 to Sta. 3+434 LHS.	12/28/14	12/28/14	12/29/14	1	A
	IR-13-00004-DUR-592-A	Casting concrete for stair from Sta. 2+035 to Sta. 2+039 LHS, stair Sta. 2+270 to Sta. 2+276 LHS	12/28/14	12/28/14	12/29/14	1	A
	IR-13-00004-DUR-593-A	Casting concrete for sidewalk from Sta. 1+433 to Sta. 1+463 LHS	12/29/14	12/29/14	12/30/14	1	A
	IR-13-00004-DUR-594-A	Installation for water line house connection house 3/4" at Sta. ( 2+945 RHS, 2+969 RHS,3+005 RHS and 3+025 RHS)	12/30/14	12/29/14	12/30/14	1	A
	IR-13-00004-DUR-595-A	Casting concrete for stair from Sta. 1+110 to Sta. 1+124 LHS	12/30/14	12/29/14	12/30/14	1	A
	IR-13-00004-DUR-596-A	Start Tack coat application from Sta. 0+000 to Sta. 0+500 LHS.	12/30/14	12/30/14	12/30/14	0	A
	IR-13-00004-DUR-597-A	Start Asphalt wearing layer from Sta. 0+000 to Sta. 0+500 LHS.	12/30/14	12/30/14	12/30/14	0	A
	IR-13-00004-DUR-598-A	Casting concrete for gravity wall 3rd stage from Sta. 3+413 to Sta. 3+434 LHS.	12/30/14	12/30/14	12/30/14	0	A
	IR-13-00004-DUR-599-A	Casting concrete for gravity wall 1st stage from Sta. 3+471 to Sta. 3+481 LHS	12/30/14	12/30/14	12/30/14	0	A
	IR-13-00004-DUR-600-A	Installation and backfilling for water line house connection house 3/4" at Sta. ( 2+925 RHS, 3+131 RHS, 3+123 RHS, 3+090 RHS, 3+086 RHS,3+049 RHS, 2+988 RHS) and 2" at Sta.(3+105 RHS, 2+950 RHS)	12/31/14	12/30/14	12/31/14	1	A
	IR-13-00004-DUR-601-A	2" Water line pressure test from Sta. 1+050 to Sta. 2+150 LHS	12/31/14	12/30/14	12/31/14	1	A
	IR-13-00004-DUR-602-A	Continue Tack coat application from Sta. 0+500 to Sta. 0+940 LHS.	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00004-DUR-603-A	Continue Asphalt wearing layer from Sta. 0+500 to Sta. 0+940 LHS.	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00004-DUR-604-A	Excavated reduced level for the proposed retaining wall from sta. 2+770 to 2+819 RHS	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00004-DUR-605-A	casting Blinding concrete for the proposed retaining wall from sta. 2+770 to 2+819 RHS	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00004-DUR-606-A	Base course 1st layer from Sta. 3+020 to Sta. 3+140 RHS.	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00004-DUR-607-A	Casting concrete for gravity wall 2nd stage from Sta. 3+471 to Sta. 3+481 LHS.	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00004-DUR-608-A	Casting concrete for sidewalk from Sta. 1+220 to Sta. 1+260 RHS.	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00004-DUR-609-A	Base course 1st layer from Sta. 2+840 to Sta. 3+020 RHS.	01/01/15	01/01/15	01/01/15	0	A
	IR-13-00004-DUR-610-A	Casting concrete for sidewalk from Sta. 1+790 to Sta. 1+835 LHS.	01/01/15	01/01/15	01/01/15	0	A
	IR-13-00004-DUR-611-A	Casting concrete for septic tank slab at Sta. 1+460 RHS.	01/01/15	01/01/15	01/01/15	0	A
	IR-13-00004-DUR-612-A	curbstone Installation works from St.1+190 to St.1+460	01/03/15	01/03/15	01/04/15	1	A
	IR-13-00004-DUR-613-A	Casting concrete for sidewalk from Sta. 1+740 to Sta. 1+860 RHS.	01/03/15	01/03/15	01/03/15	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-614-A	Casting concrete for gravity wall 3rd stage from Sta. 3+471 to Sta. 3+481 LHS.	01/03/15	01/03/15	01/03/15	0	A
	IR-13-00004-DUR-615-A	Casting Blinding concrete for the proposed retaining wall from sta. 1+694 to 1+755 LHS	01/03/15	01/03/15	01/03/15	0	A
	IR-13-00004-DUR-616-A	Casting concrete for concrete wall at outfall at Sta. 1+300 LHS from MH#01 to MH#02	01/03/15	01/03/15	01/03/15	0	D
	IR-13-00004-DUR-617-A	Installation of two catch basins and 400 mm pipe crossing connected with outfall rout MH at Sta. 0+320 ( AL- Ma'srah road as per SM-13-00012-E-C-122).	01/03/15	01/03/15	01/04/15	1	A
	IR-13-00004-DUR-618-A	Casting Ruble concrete for the Retaining wall from Sta. 3+607 to 3+623	01/05/15	01/05/15	01/05/15	0	A
	IR-13-00004-DUR-619-A	Casting concrete for sidewalk from Sta. 0+447 to Sta. 0+550 RHS and at outfall direction at Sta. 0+320.	01/05/15	01/05/15	01/06/15	1	A
	IR-13-00004-DUR-620-A	Casting concrete for stair from Sta. 1+434 to Sta. 1+440 LHS and at Sta. 1+418 LHS.	01/05/15	01/05/15	01/06/15	1	A
	IR-13-00004-DUR-621-A	Casting concrete for septic tank top slab from Sta. 1+335 to Sta. 1+342 RHS.	01/05/15	01/05/15	01/06/15	1	A
	IR-13-00004-DUR-622-A	check steel reinforcement and casting concrete for foundation of Retaining wall from Sta. 2+771 to 2+818 RHS	01/06/15	01/06/15	01/06/15	0	A
	IR-13-00004-DUR-623-A	Casting concrete for septic tank top slab from Sta. 1+323 to Sta. 1+335 RHS.	01/06/15	01/06/15	01/06/15	0	A
	IR-13-00004-DUR-624-A	check steel reinforcement and Casting concrete for septic tank concrete sheet from (Sta. 2+898 to Sta. 2+904.3, Sta. 2+919.5 to Sta. 2+829, Sta. 3+117.4 to Sta. 3+126.2, Sta. 3+164 to Sta. 3+170.6, Sta. 3+242.5 to Sta. 3+250.2 & Sta. 3+263.3 to Sta. 3+271.5) RHS.	01/12/15	01/12/15	01/13/15	1	A
	IR-13-00004-DUR-625-A	Casting encasement concrete for 400mm pipe crossing at Sta. 2+854, Sta. 2+890 and Sta. 2+943.5 RHS.	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00004-DUR-626-A	Casting concrete for stair from Sta. 2+563 to Sta. 2+576 LHS.	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00004-DUR-627-A	2" Water line pressure test from Sta. 1+050 to Sta. 2+150 RHS	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00004-DUR-628-A	Excavation and installation works for 400 mm pipe crossing at Sta. 2+989.5, Sta. 3+210 and at Sta. 3+243.	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00004-DUR-629-A	Casting concrete works for water chamber #11 foundation at Sta. 3+170 LHS.	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00004-DUR-630-A	Casting concrete for street lighting pole foundations at round about.	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00004-DUR-631-A	Check steel reinforcement for Retaining wall from Sta. 2+771 to 2+784.42 RHS	01/15/15	01/15/15	01/15/15	0	A
	IR-13-00004-DUR-632-A	Casting concrete works for water chamber #11 top slab at Sta. 3+170 LHS.	01/15/15	01/15/15	01/15/15	0	A
	IR-13-00004-DUR-633-A	Curbstone Installation works from St.2+520 to St.2+740	01/15/15	01/15/15	01/15/15	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-634-A	Casting concrete for Retaining wall from Sta. 2+771 to 2+784.42 RHS	01/17/15	01/17/15	01/17/15	0	A
	IR-13-00004-DUR-635-A	Start disinfection test for water line from sta. 0+000 to 2+150.	01/17/15	01/17/15	01/17/15	0	A
	IR-13-00004-DUR-636-A	Casting concrete works for wall of water chamber #11 at Sta. 3+170 LHS.	01/17/15	01/17/15	01/17/15	0	A
	IR-13-00004-DUR-637-A	Casting concrete for sidewalk from Sta. 2+610 to Sta. 2+660 LHS.	01/17/15	01/17/15	01/17/15	0	A
	IR-13-00004-DUR-638-A	Casting concrete for stair at Sta. 1+080 RHS.	01/17/15	01/17/15	01/18/15	1	A
	IR-13-00004-DUR-639-A	Casting concrete for sidewalk from Sta. 2+660 to Sta. 2+703 LHS.	01/18/15	01/18/15	01/18/15	0	A
	IR-13-00004-DUR-640-A	Check steel reinforcement for Retaining wall from Sta. 2+798 to 2+818 RHS	01/18/15	01/18/15	01/18/15	0	A
	IR-13-00004-DUR-641-A	Casting concrete for Retaining wall from Sta. 2+798 to 2+818 RHS	01/18/15	01/18/15	01/18/15	0	A
	IR-13-00004-DUR-642-A	Casting concrete for sidewalk from Sta. 1+260 to Sta. 1+330 RHS.	01/18/15	01/18/15	01/18/15	0	A
	IR-13-00004-DUR-643-A	Casting concrete for sidewalk from Sta. 1+615 to Sta. 1+630 RHS.	01/18/15	01/18/15	01/18/15	0	A
	IR-13-00004-DUR-644-A	Casting concrete for sidewalk from Sta. 2+680 to Sta. 2+760 RHS.	01/19/15	01/19/15	01/20/15	1	A
	IR-13-00004-DUR-645-A	Casting concrete for stair at Sta. 2+230 RHS.	01/19/15	01/19/15	01/20/15	1	A
	IR-13-00004-DUR-646-A	installation works and Casting encasement concrete for 400mm pipe crossing from Sta. 1+300 to Sta. 1+317 and road crossing ( as per engineer instruction) .	01/19/15	01/19/15	01/20/15	1	A
	IR-13-00004-DUR-647-A	Check steel reinforcement for Retaining wall from Sta. 2+784.42 to 2+798 RHS	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00004-DUR-648-A	Casting concrete for stair from Sta. 2+654 to Sta. 2+675 LHS.	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00004-DUR-649-A	Casting concrete for Retaining wall from Sta. 2+784.42 to 2+798 RHS	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00004-DUR-650-A	Installation and backfilling for 2" water pipe line crossing road from St.3+162.1 to 3+260 RHS	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00004-DUR-651-A	Casting concrete encasement for 2" water pipe line crossing road from St.3+184.1 to 3+269.1 RHS.	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00004-DUR-652-A	Casting concrete works for water chamber top slab and foundation at Sta. 2+550 LHS.	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00004-DUR-653-A	Installation and backfilling for 2" water pipe line crossing road from St.3+260 to 3+400 RHS	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00004-DUR-654-A	Base course 2nd layer from St.2+830 to St.3+110 RHS & from St.2+780 to St.3+100 LHS	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00004-DUR-655-A	Start Prime coat application from St.2+830 to St.3+110 RHS & from St.2+780 to St.3+100 LHS	01/21/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-656-A	Casting concrete for sidewalk from Sta. 1+440 to Sta. 1+460 RHS.	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00004-DUR-657-A	casting concrete for foundation and top slap of water chamber at Sta. 3+308 LHS.	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00004-DUR-658-A	Casting concrete for water chamber concrete sheet at Sta. 2+550 LHS	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00004-DUR-659-A	Base course layer at Al-Ma'srah road from Sta. 0+000 to Sta. 0+195	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00004-DUR-660-A	Installation of Water Pipe Line 4" from Sta.2+150 to Sta. 2+217.75 LHS	01/21/15	01/21/15	01/22/15	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-661-A	Check steel reinforcement for Retaining wall foundation from Sta. 1+725 to 1+755 LHS	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-662-A	casting concrete for Retaining wall foundation from Sta. 1+725 to 1+755 LHS	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-663-A	Check steel reinforcement for water chamber walls at Sta. 2+520 LHS and at Sta. 3+308 LHS.	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-664-A	Start asphalt binder layer from St.2+780 to St.3+100 LHS.	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-665-A	Casting concrete for sidewalk from Sta. 1+583 to Sta. 1+600 RHS.	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-666-A	Installation and backfilling for 2" water pipe line crossing road from St.3+400 to 3+501.9 RHS	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-667-A	Casting concrete for sidewalk from Sta. 0+660 to Sta. 0+740 LHS.	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00004-DUR-668-A	Base course 1st layer from Sta. 3+140 to Sta. 3+260.	01/24/15	01/24/15	01/25/15	1	A
	IR-13-00004-DUR-669-A	casting concrete for water chamber walls at Sta. 2+520 LHS and at Sta. 3+308 LHS.	01/24/15	01/24/15	01/25/15	1	A
	IR-13-00004-DUR-670-A	Start asphalt binder layer from St.2+830 to St.3+080 RHS.	01/24/15	01/24/15	01/25/15	1	A
	IR-13-00004-DUR-671-A	Casting concrete for sidewalk from Sta. 2+500 to Sta. 2+600 RHS, from Sta. 2+569 to Sta. 2+590 LHS and from Sta. 2+580 to Sta. 2+600 Median.	01/24/15	01/24/15	01/25/15	1	A
	IR-13-00004-DUR-672-A	Casting concrete for sidewalk at AL-Ma'sraah road RHS and LHS	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00004-DUR-673-A	Casting concrete for water chamber foundation and top slab at Sta. 3+520 LHS.	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00004-DUR-674-A	Casting rubble concrete for retaining wall from Sta. 3+593.85 to Sta. 3+607 LHS.	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00004-DUR-675-A	Start Prime coat application for AL-Ma'sraah road	01/26/15	01/26/15	01/26/15	0	A
	IR-13-00004-DUR-676-A	Start asphalt wearing layer for AL-Ma'sraah road	01/26/15	01/26/15	01/26/15	0	A
	IR-13-00004-DUR-677-A	Casting concrete for foundation of the Retaining wall from Sta. 3+607 to 3+620	01/26/15	01/26/15	01/27/15	1	A
	IR-13-00004-DUR-678-A	Sub-grade Layer from Sta. 3+380 to Sta. 3+480 RHS & LHS.	01/26/15	01/26/15	01/27/15	1	A
	IR-13-00004-DUR-679-A	Check steel reinforcement for Retaining wall from Sta. 1+725 to 1+755 LHS	01/27/15	01/27/15	01/28/15	1	A
	IR-13-00004-DUR-680-A	Sub-grade Layer from Sta. 3+260 to Sta. 3+380 RHS & LHS.	01/27/15	01/27/15	01/28/15	1	A
	IR-13-00004-DUR-681-A	Casting concrete for sidewalk from Sta. 2+770 to Sta. 2+850 LHS.	01/27/15	01/27/15	01/28/15	1	A
	IR-13-00004-DUR-682-A	Casting concrete for retaining wall from Sta. 1+742.5 to Sta. 1+755 LHS.	01/27/15	01/27/15	01/28/15	1	A
	IR-13-00004-DUR-683-A	Casting concrete for gravity wall 1st stage from Sta. 2+818 to Sta. 2+825 RHS.	01/27/15	01/27/15	01/28/15	1	A
	IR-13-00004-DUR-684-A	Casting concrete for gravity wall support from Sta. 3+450.5 to Sta. 3+472.5 LHS.	01/27/15	01/27/15	01/28/15	1	A
	IR-13-00004-DUR-685-A	Casting concrete for water chamber wall at Sta. 3+520 LHS.	01/27/15	01/27/15	01/28/15	1	A
	IR-13-00004-DUR-686-A	Casting concrete for gravity wall 2nd stage from Sta. 2+818 to Sta. 2+825 RHS.	01/28/15	01/28/15	01/29/15	1	A
	IR-13-00004-DUR-687-A	Casting concrete for retaining wall from Sta. 1+724 to Sta. 1+742.5 LHS.	01/28/15	01/28/15	01/29/15	1	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-688-A	Casting concrete for stair wall at Sta. 3+370 LHS.	01/28/15	01/28/15	01/29/15	1	A
	IR-13-00004-DUR-689-A	Casting concrete for sidewalk from Sta. 2+794 to Sta. 2+838 LHS.	01/29/15	01/29/15	01/29/15	0	A
	IR-13-00004-DUR-690-A	Casting concrete for retaining wall foundation from Sta. 3+592 to Sta. 3+607 LHS.	01/31/15	01/31/15	02/01/15	1	A
	IR-13-00004-DUR-691-A	Casting rubble concrete for retaining wall from Sta. 3+581.70 to Sta. 3+592 LHS.	01/31/15	01/31/15	02/01/15	1	A
	IR-13-00004-DUR-692-A	Casting concrete for gravity wall 3rd stage from Sta. 2+818 to Sta. 2+825 RHS.	01/31/15	01/31/15	02/01/15	1	A
	IR-13-00004-DUR-693-A	Casting concrete for top slab from Sta. 0+760 to Sta. 0+772 RHS.	02/01/15	02/01/15	02/02/15	1	A
	IR-13-00004-DUR-694-A	Casting concrete for retaining wall foundation from Sta. 1+694.54 to Sta. 1+717.64 LHS.	02/01/15	02/01/15	02/02/15	1	A
	IR-13-00004-DUR-695-A	Casting concrete for retaining wall from Sta. 3+607 to Sta. 3+621 LHS	02/01/15	02/01/15	02/02/15	1	A
	IR-13-00004-DUR-696-A	Installation and backfilling (2" & 4") water pipe line from St. 3+308.86 to St.3+496.01 for 2" and from St. 3+323.81 to St.3+531.74 for 4" LHS.	02/01/15	02/01/15	02/02/15	1	A
	IR-13-00004-DUR-697-A	Installation and backfilling for water line house connection house 3/4" at Sta. ( 3+269 RHS, 3+287 RHS, 3+305 RHS, 3+323 RHS, 3+342 RHS,3+377 RHS, 3+414 RHS, 3+444 RHS, 3+276 LHS, 3+246 LHS, 3+468 RHS, 3+348 LHS, 3+396 RHS,3+196 LHS) and 2" at Sta.(3+205 RHS)	02/02/15	02/02/15	02/03/15	1	A
	IR-13-00004-DUR-698-A	Casting concrete for street lighting pole foundation at Sta. 2+450, Sta. 2+408, Sta. 2+650, Sta. 2+690, Sta. 2+730, Sta. 2+770.	02/02/15	02/02/15	02/03/15	1	A
	IR-13-00004-DUR-699-A	Check steel reinforcement for retaining wall from Sta. 3+607 to Sta. 3+621 LHS	02/03/15	02/03/15	02/04/15	1	A
	IR-13-00004-DUR-700-A	Casting concrete for retaining wall 2nd stage from Sta. 3+607 to Sta. 3+621 LHS	02/03/15	02/03/15	02/04/15	1	A
	IR-13-00004-DUR-701-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.3+300 to 3+400	02/03/15	02/03/15	02/04/15	1	A
	IR-13-00004-DUR-702-A	Installation and backfilling for water line house connection house 3/4" at Sta. ( 3+341 LHS, 3+324.5 LHS, 3+415 LHS, 3+433 LHS, 3+478 LHS,3+496 LHS, 2+791 RHS, 2+820 RHS) and 2" at Sta.(3+373 LHS and 2+846 RHS)	02/03/15	02/03/15	02/04/15	1	A
	IR-13-00004-DUR-703-A	Installation of Street Lighting Pipes, Ground Cable, Warning Tape from St.3+400 to 3+656	02/04/15	02/04/15	02/05/15	1	A
	IR-13-00004-DUR-704-A	Check steel reinforcement for retaining wall from Sta. 1+697.54 to Sta. 1+717.40 LHS	02/04/15	02/04/15	02/05/15	1	A
	IR-13-00004-DUR-705-A	Casting concrete for retaining wall from Sta. 1+697.54 to Sta. 1+717.40 LHS	02/04/15	02/04/15	02/05/15	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-706-A	Casting concrete for retaining wall foundation from Sta. 3+581.7 to Sta. 3+592 LHS	02/04/15	02/04/15	02/05/15	1	A
	IR-13-00004-DUR-707-A	Casting concrete for street lighting pole foundation at Sta. 2+810, Sta. 2+850, Sta. 2+890, Sta. 2+930, Sta. 2+960, Sta. 3+000, Sta. 3+040, Sta. 3+080.	02/04/15	02/04/15	02/05/15	1	A
	IR-13-00004-DUR-708-A	Casting concrete for sidewalk from Sta. 2+460 to Sta. 2+500 RHS and from Sta. 2+400 to Sta. 2+500 Median.	02/04/15	02/04/15	02/05/15	1	A
	IR-13-00004-DUR-709-A	Base course 2nd layer from St.3+100 to St.3+260 RHS & LHS	02/05/15	02/05/15	02/06/15	1	A
	IR-13-00004-DUR-710-A	Start Prime coat application from St.3+110 to St.3+250 RHS & from St.3+100 to St.3+250 LHS	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00004-DUR-711-A	Start asphalt binder layer from St.3+110 to St.3+250 RHS & from St.3+100 to St.3+250 LHS	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00004-DUR-712-A	Start Tack coat application from Sta. 0+940 to Sta. 1+630 RHS.	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00004-DUR-713-A	Start Asphalt wearing layer from Sta. 0+940 to Sta. 1+630 RHS.	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00004-DUR-714-A	Sub-grade Layer for simple access at Sta. 3+000 LHS.	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00004-DUR-715 -A	Casting concrete for retaining wall from Sta. 3+592 to Sta. 3+607 LHS	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00004-DUR-716 -A	Base course 1st layer from Sta. 3+260 to Sta. 3+480.	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00004-DUR-717 -A	Base course layer for simple access at Sta. 3+000 LHS.	02/08/15	02/08/15	02/08/15	0	A
	IR-13-00004-DUR-718 -A	Base course 2nd layer from Sta. 2+700 to Sta. 2+830 RHS.	02/08/15	02/08/15	02/08/15	0	A
	IR-13-00004-DUR-719-A	Start prime coat and asphalt binder layer from St.2+680 to St.2+830 RHS.	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00004-DUR-720 -A	Casting concrete for retaining wall 2nd stage from Sta. 3+592 to Sta. 3+607 LHS	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00004-DUR-721 -A	Casting concrete for retaining wall from Sta. 1+717.4 to Sta. 1+724 LHS	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00004-DUR-722 -A	Start prime coat and asphalt wearing layer for simple access at St.3+000 LHS	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00004-DUR-723 -A	Start prime coat and asphalt wearing layer for sidewalk from Sta. 2+990 to Sta. 3+030 RHS and from Sta. 2+840 to Sta. 2+870 LHS.	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00004-DUR-724 -A	Installation and backfilling for 2" water pipe line crossing road from St.3+501.9 to 3+693.35 RHS	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00004-DUR-725 -A	Installation and backfilling for water line house connection house 3/4" at Sta. ( 3+537 RHS, 3+555 RHS, 3+610 RHS, 3+634 RHS) and 2" at Sta.(3+524 RHS and 3+560 RHS)	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00004-DUR-726 -A	Start traffic sign installation and paint for electrical street lighting pole	02/09/15	02/09/15	02/10/15	1	D
	IR-13-00004-DUR-726 -B	Start traffic sign installation and paint for electrical street lighting pole	02/25/15	02/25/15	02/26/15	1	A
	IR-13-00004-DUR-727 -A	Casting concrete for retaining wall 1st stage from Sta. 3+580 to Sta. 3+592 LHS	02/09/15	02/09/15	02/10/15	1	A
	IR-13-00004-DUR-728 -A	Casting concrete for retaining wall 2nd stage from Sta. 3+580 to Sta. 3+592 LHS	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00004-DUR-729 -A	Median Curbstone Installation works from St.2+740 to St.3+140	02/10/15	02/10/15	02/11/15	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-730 -A	Sub grade Layer from Sta. 3+640 to Sta. 3+700 RHS & LHS.	02/11/15	02/11/15	02/12/15	1	A
	IR-13-00004-DUR-731 -A	Base course 2nd layer from St.3+260 to St.3+450 RHS & LHS.	02/14/15	02/14/15	02/15/15	1	A
	IR-13-00004-DUR-732 -A	Curbstone Installation works from St.2+740 to St.3+250 LHS except for simple access Sta. 3+000 LHS	02/15/15	02/15/15	02/16/15	1	A
	IR-13-00004-DUR-733 -A	Installation and backfilling (2" & 6") water pipe line from Sta. 3+640 to St.3+700 LHS.	02/15/15	02/15/15	02/16/15	1	A
	IR-13-00004-DUR-734 -A	Casting concrete for parapet wall from Sta. 2+409 to Sta. 2+418 RHS.	02/15/15	02/15/15	02/16/15	1	A
	IR-13-00004-DUR-735 -A	Backfilling works for retaining wall from Sta. 3+607 to Sta. 3+654	02/15/15	02/15/15	02/15/15	0	A
	IR-13-00004-DUR-736 -A	Installation and backfilling for water pipe line 2" from Sta. 3+531.20 to Sta. 3+640 and 6" from Sta. 3+590.15 to St.3+640 LHS.	02/16/15	02/16/15	02/16/15	1	A
	IR-13-00004-DUR-737 -A	Installation and backfilling for water line house connection house 3/4" at Sta. ( 3+638 LHS, 3+614 LHS, 3+584 LHS, 3+657 LHS, 3+688 LHS, 3+554 LHS, 3+536 LHS) and 2" at Sta. 3+566 LHS	02/17/15	02/17/15	02/18/15	1	A
	IR-13-00004-DUR-738 -A	Casting concrete for parapet wall from Sta. 2+398 to Sta. 2+408 RHS.	02/17/15	02/17/15	02/18/15	1	A
	IR-13-00004-DUR-739 -A	Casting concrete for Median from Sta. 2+600 to Sta. 2+840.	02/17/15	02/17/15	02/18/15	1	A
	IR-13-00004-DUR-740 -A	Casting concrete for stair wall at Sta. 0+520 LHS.	02/17/15	02/17/15	02/18/15	1	A
	IR-13-00004-DUR-741 -A	Curbstone Installation works from St.2+740 to St.3+250 RHS except for simple access Sta. (3+100 and 3+180)RHS	02/18/15	02/18/15	02/18/15	0	A
	IR-13-00004-DUR-742 -A	Casting concrete for parapet wall from Sta. 3+339 to Sta. 3+349 LHS .	02/23/15	02/23/15	02/24/15	1	A
	IR-13-00004-DUR-743 -A	Casting concrete for parapet wall from Sta. 3+309 to Sta. 3+329 LHS.	02/24/15	02/24/15	02/24/15	0	A
	IR-13-00004-DUR-744 -A	excavation works for simple access at Sta. 3+360	02/24/15	02/24/15	02/26/15	1	A
	IR-13-00004-DUR-745 -A	Sub grade Layer from Sta. 3+480 to Sta. 3+640 RHS & LHS.	02/25/15	02/25/15	02/26/15	1	A
	IR-13-00004-DUR-746 -A	Casting concrete for sidewalk from Sta. 2+760 to Sta. 2+900 RHS, from Sta. 2+930 to Sta. 2+990 LHS and Median from Sta. 2+860 to Sta. 3+000.	02/25/15	02/25/15	02/26/15	1	A
	IR-13-00004-DUR-747 -A	Curbstone Installation works from St.0+880 to St.1+060 RHS and LHS	02/25/15	02/25/15	02/26/15	1	A
	IR-13-00004-DUR-748 -A	Curbstone Installation works from St.1+460 to St.2+000 RHS, LHS and MD except for simple access at Sta.1+630 RHS and location of septic tank at Sta. 1+840 LHS.	02/25/15	02/25/15	02/26/15	1	A
	IR-13-00004-DUR-749 -A	Traffic sign foundation from Sta. 1+000 to Sta. 1+800	02/25/15	02/25/15	02/26/15	1	A
	IR-13-00004-DUR-750 -A	Start Prime coat application from St.3+250 to St.3+450	02/25/15	02/26/15	02/26/15	0	A
	IR-13-00004-DUR-751 -A	Start asphalt binder layer from St.3+250 to St.3+450	02/26/15	02/26/15	02/26/15	0	A
	IR-13-00004-DUR-752 -A	Casting concrete for sidewalk from Sta. 3+000 to Sta. 3+100 LHS, from Sta. 2+510 to Sta. 2+550 LHS and Median from Sta. 3+000 to Sta. 3+100.	02/26/15	02/26/15	02/26/15	0	A
	IR-13-00004-DUR-753 -A	Casting concrete for slab and stair at Sta.3+370 LHS.	02/26/15	02/26/15	02/26/15	0	A
	IR-13-00004-DUR-754 -A	Base course 1st layer from Sta. 3+540 to Sta. 3+700.	02/27/15	02/27/15	02/28/15	1	A
	IR-13-00004-DUR-755 -A	Start Tack coat application from Sta. 0+880 to Sta. 1+550 LHS.	02/28/15	02/28/15	02/28/15	0	A
	IR-13-00004-DUR-756 -A	Start Asphalt wearing layer from Sta. 0+880 to Sta. 1+550 LHS.	02/28/15	02/28/15	02/28/15	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-757 -A	Casting concrete for sidewalk from Sta. 2+130 to Sta. 2+145 RHS and from Sta. 1+620 to Sta. 1+755 LHS.	02/28/15	02/28/15	02/28/15	0	A
	IR-13-00004-DUR-758 -A	Casting concrete for sidewalk from Sta. 2+360 to Sta. 2+400 RHS.	03/01/15	03/01/15	03/02/15	1	A
	IR-13-00004-DUR-759 -A	sample for curbstone painting from Sta. 0+080 to Sta. 0+090 RHS.(attached photos)	03/01/15	03/01/15	03/02/15	1	D
	IR-13-00004-DUR-759 -B	sample for curbstone painting at Sta. 0+500 LHS.	03/05/15	03/07/15	03/09/15	2	D
	IR-13-00004-DUR-759 -C	sample for curbstone painting from Sta. 0+770 to Sta. 0+800 RHS.	03/10/15	03/10/15	03/10/15	1	A
	IR-13-00004-DUR-760 -A	Start Tack coat application from Sta. 1+630 to Sta. 2+200 RHS.	03/01/15	03/01/15	03/02/15	1	A
	IR-13-00004-DUR-761 -A	Start Asphalt wearing layer from Sta. 1+630 to Sta. 2+200 RHS.	03/01/15	03/01/15	03/02/15	1	A
	IR-13-00004-DUR-762 -A	Casting concrete for sidewalk from Sta. 0+330 to Sta. 0+340 RHS.	03/01/15	03/01/15	03/02/15	1	A
	IR-13-00004-DUR-763 -A	2" Water line pressure test from Sta. 2+150 to Sta. 2+800 RHS	03/02/15	03/02/15	03/03/15	1	A
	IR-13-00004-DUR-764 -A	Start Tack coat application from Sta. 2+200 to Sta. 2+800 RHS.	03/02/15	03/02/15	03/03/15	1	A
	IR-13-00004-DUR-765 -A	Start Asphalt wearing layer from Sta. 2+200 to Sta. 2+800 RHS.	03/02/15	03/02/15	03/03/15	1	A
	IR-13-00004-DUR-766 -A	Casting concrete for sidewalk from Sta. 1+880 to Sta. 1+900 RHS and from Sta. 1+940 to Sta. 1+980 RHS.	03/02/15	03/02/15	03/03/15	1	A
	IR-13-00004-DUR-767 -A	Base course 2nd layer from St.3+450 to St.3+700 RHS & LHS.	03/03/15	03/03/15	03/04/15	1	D
	IR-13-00004-DUR-767 -B	Base course 2nd layer from St.3+450 to St.3+700 RHS & LHS.	03/05/15	03/07/15	03/08/15	1	A
	IR-13-00004-DUR-768 -A	sample for manhole adjustment works using asphalt at Sta. 0+320 RHS	03/03/15	03/03/15	03/04/15	1	A
	IR-13-00004-DUR-769 -A	2" Water line pressure test from Sta. 2+800 to Sta. 3+500 RHS	03/03/15	03/03/15	03/04/15	1	A
	IR-13-00004-DUR-770 -A	Casting concrete for septic tank top slab at Sta. 1+850 LHS	03/03/15	03/03/15	03/04/15	1	A
	IR-13-00004-DUR-771 -A	Casting concrete for gravity wall at Sta. 1+755 LHS.	03/03/15	03/03/15	03/04/15	1	A
	IR-13-00004-DUR-772 -A	Casting concrete for street lighting pole foundation at Sta. 3+120, Sta. 3+160, Sta. 3+200, Sta. 3+240, Sta. 3+280.	03/04/15	03/04/15	03/04/15	0	A
	IR-13-00004-DUR-773 -A	check steel reinforcement and Casting concrete for simple access road at Sta. 3+360 RHS.	03/05/15	03/05/15	03/05/15	0	A
	IR-13-00004-DUR-774 -A	Casting concrete for street lighting pole foundation at Sta. 3+320, Sta. 3+360, Sta. 3+400, Sta. 3+440.	03/05/15	03/05/15	03/05/15	0	A
	IR-13-00004-DUR-775 -A	Permanent sign installation at Sta. 0+320 RHS	03/05/15	03/05/15	03/05/15	0	A
	IR-13-00004-DUR-776 -A	Start Prime coat application from St.3+450 to St.3+700	03/05/15	03/07/15	03/08/15	1	A
	IR-13-00004-DUR-777 -A	Start asphalt binder layer from St.3+450 to St.3+700	03/05/15	03/07/15	03/08/15	1	A
	IR-13-00004-DUR-778 -A	Start Tack coat application from Sta. 1+550 to Sta. 2+150 LHS.	03/08/15	03/07/15	03/08/15	1	A
	IR-13-00004-DUR-779 -A	Start Asphalt wearing layer from Sta. 1+550 to Sta. 2+150 LHS.	03/08/15	03/07/15	03/08/15	1	A
	IR-13-00004-DUR-780 -A	Water line pressure test for 2" from Sta. 2+150 to Sta. 2+850 LHS, 6" from Sta. 2+150 to Sta. 2+850 LHS, 4" from Sta. 2+850 to Sta. 3+520 LHS and house connection.	03/08/15	03/07/15	03/07/15	0	A
	IR-13-00004-DUR-781 -A	Casting concrete for concrete boundary wall from Sta. 3+000 to Sta. 3+260 LHS.	03/08/15	03/07/15	03/08/15	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-782 -A	Casting concrete for sidewalk from Sta. 3+060 to Sta. 3+087 RHS, from Sta. 3+309 to Sta. 3+370 LHS and for median from Sta. 3+080 to Sta. 3+450.	03/08/15	03/08/15	03/08/15	0	A
	IR-13-00004-DUR-783 -A	5 cm Asphalt layer for sidewalk from Sta. 2+879 to Sta. 2+880 RHS, from Sta. 2+905 to Sta. 2+920 RHS, from Sta. 2+960 to Sta. 3+000 LHS and from Sta. 2+927 to Sta. 2+952 RHS.	03/08/15	03/08/15	03/09/15	1	A
	IR-13-00004-DUR-784 -A	Casting concrete for edge wall from Sta. 3+140 to Sta. 3+220.	03/08/15	03/08/15	03/09/15	1	A
	IR-13-00004-DUR-785 -A	Curbstone Installation works from St.3+250 to St.3+430 LHS, RHS and from St.3+140 to St.3+430 Median (except simple access at Sta. 3+360 RHS).	03/08/15	03/08/15	03/08/15	0	A
	IR-13-00004-DUR-786 -A	Median Curbstone painting works from St.0+010 to St.1+040	03/09/15	03/09/15	03/10/15	1	D
	IR-13-00004-DUR-786 -B	Median Curbstone painting works from St.0+010 to St.1+040	03/11/15	03/11/15	03/11/15	0	A
	IR-13-00004-DUR-787 -A	Surface preparation for median curbstone before start painting from Sta. 1+060 to Sta. 1+400.	03/09/15	03/09/15	03/10/15	1	A
	IR-13-00004-DUR-788 -A	Start Tack coat application from Sta. 2+150 to Sta. 2+380 and from Sta. 2+480 to Sta. 2+860 LHS.	03/09/15	03/09/15	03/10/15	1	A
	IR-13-00004-DUR-789 -A	Start Asphalt wearing layer from Sta. 2+150 to Sta. 2+380 and from Sta. 2+480 to Sta. 2+860 LHS.	03/09/15	03/09/15	03/10/15	1	A
	IR-13-00004-DUR-790 -A	casting concrete for Parapet wall for simple access at Sta. 3+360 RHS	03/09/15	03/09/15	03/10/15	1	A
	IR-13-00004-DUR-791 -A	chlorination test for water line from Sta. 2+150 to Sta. 3+690	03/09/15	03/09/15	03/10/15	1	A
	IR-13-00004-DUR-792 -A	Water line pressure test for 2" and house connection from Sta. 2+850 to Sta. 3+700 LHS, 2" and house connection from Sta. 3+500 to Sta. 3+700 RHS, 6" from Sta. 3+520 to Sta. 3+700 LHS.	03/09/15	03/09/15	03/10/15	1	A
	IR-13-00004-DUR-793 -A	Handrail installation works from Sta. 0+800 to Sta. 0+821 RHS (original type) and from Sta. 2+770 to Sta. 2+840 RHS (New detail type)	03/10/15	03/10/15	03/11/15	1	A
	IR-13-00004-DUR-794 -A	5 cm Asphalt layer for sidewalk from Sta. 3+070 to Sta. 3+170 RHS.	03/10/15	03/10/15	03/11/15	1	A
	IR-13-00004-DUR-795 -A	Casting concrete for septic tank top slap at Sta. 2+180 LHS	03/10/15	03/10/15	03/11/15	1	A
	IR-13-00004-DUR-796 -A	Start Tack coat application from Sta. 2+800 to Sta. 3+200 RHS.	03/11/15	03/11/15	03/12/15	1	A
	IR-13-00004-DUR-797 -A	Start Asphalt wearing layer from Sta. 2+800 to Sta. 3+200 RHS.	03/11/15	03/11/15	03/12/15	1	A
	IR-13-00004-DUR-798 -A	5 cm Asphalt layer for sidewalk from Sta. 3+170 to Sta. 3+260 RHS.	03/11/15	03/11/15	03/12/15	1	A
	IR-13-00004-DUR-799-A	Casting concrete for street lighting pole foundation at Sta. 3+480, Sta. 3+520, Sta. 3+560, Sta. 3+600 and Sta. 3+640.	03/11/15	03/11/15	03/12/15	1	A
	IR-13-00004-DUR-800-A	Casting concrete for sidewalk from Sta. 2+480 to Sta. 2+490 LHS.	03/11/15	03/11/15	03/12/15	1	A
	IR-13-00004-DUR-801-A	Casting concrete for sidewalk from Sta. 3+060 to Sta. 3+250 LHS.	03/14/15	03/14/15	03/15/15	1	A
	IR-13-00004-DUR-802-A	Casting concrete for edge wall from Sta. 3+060 to Sta. 3+160 LHS.	03/14/15	03/14/15	03/15/15	1	A
	IR-13-00004-DUR-803-A	Surface preparation for median curbstone before start painting from Sta. 1+400 to Sta. 1+900 and from Sta. 1+080 to Sta. 1+400 LHS.	03/14/15	03/14/15	03/15/15	1	A
	IR-13-00004-DUR-804-A	Median Curbstone painting works from St.1+400 to St.1+900	03/15/15	03/15/15	03/15/15	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 01**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-DUR-805-A	Casting concrete for sidewalk from Sta. 2+490 to Sta. 2+515 LHS and from Sta. 3+272 to Sta. 3+309 RHS.	03/15/15	03/15/15	03/15/15	0	A
	IR-13-00004-DUR-806-A	Casting concrete for parapet wall from Sta. 3+480 to Sta. 3+494 LHS.	03/15/15	03/15/15	03/16/15	1	A
	IR-13-00004-DUR-807-A	5 cm Asphalt layer for sidewalk from Sta. 3+100 to Sta. 3+080 RHS, from Sta. 3+242 to Sta. 3+272 RHS and from Sta. 3+329 to Sta. 3+361.	03/15/15	03/15/15	03/16/15	1	A
	IR-13-00004-DUR-808-A	Surface preparation for curbstone before start painting from Sta. 1+400 to Sta. 1+900 LHS.	03/16/15	03/16/15	03/16/15	1	A
	IR-13-00004-DUR-809-A	Curbstone painting works from sta. 1+080 to 1+900 LHS	03/16/15	03/16/15	03/16/15	1	A
	IR-13-00004-DUR-810-A	Casting concrete works for edge wall from Sta. 3+278 to Sta. 3+309 and from Sta. 3+260 to Sta. 3+270 LHS.	03/16/15	03/16/15	03/17/15	1	A
	IR-13-00004-DUR-811-A	Casting concrete for parapet wall from Sta. 3+498 to Sta. 3+508 LHS.	03/16/15	03/16/15	03/17/15	1	A
	IR-13-00004-DUR-812-A	check steel reinforcement and casting concrete works for sidewalk from Sta. 3+440 to Sta. 3+466 RHS, from Sta. 3+580 to Sta. 3+654 LHS and for median from Sta. 3+370 to Sta. 3+640.	03/16/15	03/16/15	03/17/15	1	A
	IR-13-00004-DUR-813-A	Start Tack coat application from Sta. 3+200 to Sta. 3+510 RHS and from Sta. 2+860 to Sta. 3+440 LHS.	03/16/15	03/16/15	03/17/15	1	A
	IR-13-00004-DUR-814-A	Start Asphalt wearing layer from Sta. 3+200 to Sta. 3+510 RHS and from Sta. 2+860 to Sta. 3+440 LHS.	03/16/15	03/16/15	03/17/15	1	A
	IR-13-00004-DUR-815-A	Surface preparation for curbstone before start painting from Sta. 1+100 to Sta. 2+380 RHS, from Sta. 1+900 to Sta. 2+150 LHS and median curbstone from Sta. 1+900 to Sta. 2+380.	03/16/15	03/16/15	03/17/15	1	A
	IR-13-00004-DUR-816-A	Curbstone painting works from Sta. 1+100 to Sta. 2+380 RHS, from Sta. 1+900 to Sta. 2+150 LHS and median curbstone from Sta. 1+900 to Sta. 2+380.	03/16/15	03/16/15	03/17/15	1	A
	IR-13-00004-DUR-817-A	5 cm Asphalt layer for sidewalk from Sta. 3+329 to Sta. 3+361 RHS, from Sta. 3+375 to Sta. 3+385 RHS and from Sta. 3+405 to Sta. 3+420 RHS.	03/17/15	03/17/15	03/18/15	1	A
	IR-13-00004-DUR-818-A	check steel reinforcement and casting concrete works for sidewalk from Sta. 3+466 to Sta. 3+530 RHS, from Sta. 3+560 to Sta. 3+580 LHS, from Sta. 3+150 to Sta. 3+170 LHS and from Sta. 3+620 to Sta. 3+650 RHS.	03/17/15	03/17/15	03/18/15	1	A
	IR-13-00004-DUR-819-A	Casting concrete for parapet wall from Sta. 3+508 to Sta. 3+529 LHS and from Sta. 3+494 to Sta. 3+502 LHS.	03/17/15	03/17/15	03/18/15	1	A
	IR-13-00004-DUR-820-A	Casting concrete for gravity wall from Sta. 3+455 to Sta. 3+459 LHS.	03/17/15	03/17/15	03/18/15	1	A
	IR-13-00004-DUR-821-A	Surface preparation for curbstone before start painting from Sta. 2+480 to Sta. 2+840 RHS,LHS and median.	03/17/15	03/17/15	03/18/15	1	A
	IR-13-00004-DUR-822-A	asphalt surface cleaning and washing at locations of pedestrian crossing before start thermoplastic paint	03/18/15	03/18/15	03/18/15	0	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 01**

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-DUR-823-A	5 cm Asphalt layer for sidewalk from Sta. 2+905 to Sta. 2+920 LHS and from Sta. 3+655 to Sta. 3+665 RHS.	03/18/15	03/18/15	03/19/15	1	A
	IR-13-00004-DUR-824-A	check steel reinforcement and casting concrete works for sidewalk from Sta. 2+900 to Sta. 2+907 RHS, from Sta. 2+923 to Sta. 2+930 RHS and from Sta. 3+261 to Sta. 3+310 LHS.	03/18/15	03/18/15	03/19/15	1	A
	IR-13-00004-DUR-825-A	Surface preparation for curbstone before start painting from Sta. 2+840 to Sta. 3+240 RHS,LHS and median.	03/18/15	03/18/15	03/19/15	1	A
	IR-13-00004-DUR-826-A	Start Tack coat application from Sta. 2+380 to Sta. 2+480, from Sta. 3+490 to 3+700 LHS and from Sta. 3+510 to Sta. 3+700 RHS.	03/19/15	03/18/15	03/20/15	1	A
	IR-13-00004-DUR-827-A	Start Asphalt wearing layer from Sta. 2+380 to Sta. 2+480, from Sta. 3+490 to 3+700 LHS and from Sta. 3+510 to Sta. 3+700 RHS.	03/19/15	03/19/15	03/20/15	1	A
<b>DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required</b>							

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-001-A	Start Excavation Work from St.0+000 to St.0+260	01/18/14	01/19/14	01/19/14	0	A
	IR-13-00004-SAM-002-A	Sub-grade Layer from St.0+080 to St.0+240-Samu'-Yatta Road	01/28/14	01/29/14	01/29/14	0	A
	IR-13-00004-SAM-003-A	Start Backfilling in Benching Area-1st Layer from St.0+270 to St.0+310	02/03/14	02/03/14	02/04/14	1	A
	IR-13-00004-SAM-004-A	Backfilling in Benching Area-1st Layer from St.0+270 to St.0+310 LHS	02/04/14	02/04/14	02/04/14	0	A
	IR-13-00004-SAM-005-A	Excavation Work of Yard Area from St.0+140 to St.0+260 RHS	02/04/14	02/04/14	02/04/14	0	A
	IR-13-00004-SAM-006-A	Backfilling in Benching Area-2nd Layer from St.0+270 to St.0+310 LHS	02/04/14	02/04/14	02/04/14	0	A
	IR-13-00004-SAM-007-A	Sub-grade Layer from St.0+240 to St.0+500	02/04/14	02/05/14	02/06/14	1	D
	IR-13-00004-SAM-007-B	Sub-grade Layer from St.0+240 to St.0+500	02/13/14	02/13/14	02/16/14	3	A
	IR-13-00004-SAM-008-A	Topping Layer from St.0+100 to St.0+240	02/05/14	02/05/14	02/06/14	1	A
	IR-13-00004-SAM-009-A	Backfilling in Benching Area-3rd Layer from St.0+270 to St.0+310 LHS	02/05/14	02/05/14	02/06/14	1	A
	IR-13-00004-SAM-010-A	Sub-grade Layer from St.0+280 to St.0+600	02/08/14	02/09/14	02/10/14	1	D
	IR-13-00004-SAM-010-B	Sub-grade Layer from St.0+280 to St.0+600	02/10/14	02/10/14	02/11/14	1	A
	IR-13-00004-SAM-011-A	Traffic Control Plan	02/10/14	02/10/14	02/11/14	1	A
	IR-13-00004-SAM-012-A	Sub-grade Layer from St.0+020 to St.0+080	02/10/14	02/11/14	02/12/14	1	A
	IR-13-00004-SAM-013-A	Sub-grade Layer from St.0+600 to St.0+750	02/12/14	02/13/14	02/16/14	3	A
	IR-13-00004-SAM-014-A	Topping Layer -Yard Area from St.0+140 to St.0+260 RHS	02/13/14	02/13/14	02/16/14	3	A
	IR-13-00004-SAM-015-A	Topping Layer from St.0+280 to St.0+380	02/13/14	02/13/14	02/16/14	3	A
	IR-13-00004-SAM-016-A	Topping Layer from St.0+020 to St.0+100	02/17/14	02/18/14	02/20/14	2	A
	IR-13-00004-SAM-017-A	Topping Layer from St.0+240 to St.0+280	02/17/14	02/18/14	02/20/14	2	A
	IR-13-00004-SAM-018-A	Topping Layer from St.0+380 to St.0+600	02/17/14	02/18/14	02/20/14	2	A
	IR-13-00004-SAM-019-A	Topping Layer from St.0+600 to St.0+750	02/19/14	02/19/14	02/20/14	1	A
	IR-13-00004-SAM-020-A	Base Course-1st Layer from St.0+160 to St.0+640	02/24/14	02/24/14	02/27/14	3	A
	IR-13-00004-SAM-021-A	Base Course-1st Layer from St.0+040 to St.0+160 & from St.0+640 to St.0+740	02/26/14	02/27/14	02/27/14	0	A
	IR-13-00004-SAM-022-A	Sub-grade Layer from St.0+780 to St.0+880	02/26/14	02/27/14	02/27/14	0	A
	IR-13-00004-SAM-023-A	Sub-grade Layer from St.0+880 to St.1+080	02/27/14	03/01/14	03/03/14	2	A
	IR-13-00004-SAM-024-A	Backfilling in Benching Area-1st Layer from St.1+110 to St.1+170 RHS	03/01/14	03/01/14	03/04/14	3	A
	IR-13-00004-SAM-025-A	Backfilling in Benching Area-2nd Layer from St.1+110 to St.1+170 RHS	03/02/14	03/02/14	03/04/14	2	A
	IR-13-00004-SAM-026-A	Backfilling in Benching Area-3rd Layer from St1+110 TO St.1+170 RHS	03/03/14	03/04/14	03/06/14	2	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-027-A	Sub-grade Layer from St.1+110 to St.1+300	03/05/14	03/05/14	03/06/14	1	A
	IR-13-00004-SAM-028-A	Topping Layer from St.0+880 to St.1+000	03/05/14	03/06/14	03/06/14	0	A
	IR-13-00004-SAM-029-A	Topping Layer From St.1+130 to St.1+300	03/09/14	03/09/14	03/10/14	1	A
	IR-13-00004-SAM-030-A	Benching Area-1 <sup>st</sup> Layer From St.1+360 to St.1+370 RHS	03/16/14	03/16/14	03/18/14	2	A
	IR-13-00004-SAM-031-A	Benching Area-2 <sup>nd</sup> Layer From St.1+360 to St.1+370 RHS	03/16/14	03/16/14	03/18/14	2	A
	IR-13-00004-SAM-032-A	Base Course-1 <sup>st</sup> Layer From St.0+800 to St.1+000	03/16/14	03/17/14	03/18/14	1	A
	IR-13-00004-SAM-033-A	Benching Area- 3rd Layer From St.1+360 to St.1+370 RHS	03/17/14	03/17/14	03/18/14	1	A
	IR-13-00004-SAM-034-A	Handing over Benching Area-1 <sup>st</sup> Layer From St.1+450 to St.1+490 RHS	03/18/14	03/18/14	03/20/14	2	A
	IR-13-00004-SAM-035-A	Base course -1 <sup>st</sup> Layer From St.1+130 to St.1+300	03/18/14	03/18/14	03/20/14	2	A
	IR-13-00004-SAM-036-A	Sub grade Layer From St.1+300 to St.1+440	03/18/14	03/18/14	03/20/14	2	A
	IR-13-00004-SAM-037-A	Benching Area-1st Layer From St.1+570 to St.1+610 RHS	03/18/14	03/18/14	03/20/14	2	A
	IR-13-00004-SAM-038-A	Benching Area-2nd Layer From St.1+570 to St.1+610 RHS	03/19/14	03/19/14	03/20/14	1	A
	IR-13-00004-SAM-039-A	Benching Area-3rd Layer From St.1+570 to St.1+610 RHS	03/19/14	03/19/14	03/20/14	1	A
	IR-13-00004-SAM-040-A	Benching Area-2nd Layer From St.1+450 to St.1+490 RHS	03/19/14	03/20/14	03/20/14	0	A
	IR-13-00004-SAM-041-A	Benching Area-3rd Layer From St.1+450 to St.1+490 RHS	03/19/14	03/20/14	03/20/14	0	A
	IR-13-00004-SAM-042-A	Sub grade Layer From St.1+440 to St.1+580	03/23/14	03/23/14	03/25/14	2	A
	IR-13-00004-SAM-043-A	Topping Layer From St.1+300 to St.1+440	03/23/14	03/23/14	03/25/14	2	A
	IR-13-00004-SAM-044-A	Topping Layer From St.1+000 to St.1+130	03/25/14	03/25/14	04/03/14	9	A
	IR-13-00004-SAM-045-A	Topping Layer From St.1+420 to St.1+580	03/25/14	03/25/14	04/03/14	9	A
	IR-13-00004-SAM-046-A	Sub grade From St.1+580 to St.1+800	03/25/14	03/25/14	04/03/14	9	A
	IR-13-00004-SAM-047-A	Sub grade Layer From St.1+800 to St.2+000	03/27/14	03/29/14	04/03/14	5	A
	IR-13-00004-SAM-048-A	Base course 1st layer From St.1+300 to St.1+420	03/27/14	03/29/14	04/03/14	5	A
	IR-13-00004-SAM-049-A	Topping layer From St.1+580 to St.1+800	03/27/14	03/29/14	04/03/14	5	A
	IR-13-00004-SAM-050-A	Base course 1st layer From St.1+420 to St.1+580	03/30/14	03/31/14	04/03/14	3	A
	IR-13-00004-SAM-051-A	Base course 1st layer From St.1+000 to St.1+130	03/30/14	03/31/14	04/03/14	3	A
	IR-13-00004-SAM-052-A	Topping Layer from St.1+800 to St.2+000	04/01/14	04/01/14	04/03/14	2	A
	IR-13-00004-SAM-053-A	Sub-grade Layer from St.2+000 to St.2+060	04/01/14	04/01/14	04/03/14	2	A
	IR-13-00004-SAM-054-A	Base Course-1st Layer from St.1+580 to St.2+000	04/09/14	04/09/14	04/10/14	1	A
	IR-13-00004-SAM-055-A	Topping Layer from St.2+000 to St.2+060	04/09/14	04/09/14	04/10/14	1	A
	IR-13-00004-SAM-056-A	Check Sub-grade Layer from St.2+060 to St.2+180	04/08/14	04/09/14	04/09/14	0	A
	IR-13-00004-SAM-057-A	Casting Concrete for Gravity Wall from St.0+040 to St.0+074 RHS	04/08/14	04/09/14	04/17/14	8	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-058-A	Handing over Sub-grade from St.2+240 to St.2+500	04/10/14	04/12/14	04/12/14	0	A
	IR-13-00004-SAM-059-A	Handing over Benching Area From St.2+115 to St.2+150	04/10/14	04/12/14	04/12/14	0	A
	IR-13-00004-SAM-060-A	Handing Over Topping Material From St. 2+060 to St. 2+160 & From St. 2+260 to St. 2+460	04/15/14	04/15/14	04/16/14	1	A
	IR-13-00004-SAM-061-A	Handing Over Sub - Grade Layer From St. 2+500 to St. 2+620	04/16/14	04/17/14	04/17/14	0	A
	IR-13-00004-SAM-062-A	Start Installation of Pipe Culvert (1000 mm Dia.)at St.0+280	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00004-SAM-063-A	Sub-grade for Widening Area from St.1+050 to st.1+350 LHS	04/17/14	04/19/14	04/21/14	2	A
	IR-13-00004-SAM-064-A	Topping Layer for Widening Area from St.1+050 to St.1+350 LHS	04/17/14	04/19/14	04/21/14	2	A
	IR-13-00004-SAM-065-A	Base Course-1st Layer from St.2+000 to St.2+160	04/17/14	04/20/14	04/21/14	1	A
	IR-13-00004-SAM-066-A	Sub-grade Layer Work from St.2+720 to St.2+820	04/17/14	04/20/14	04/21/14	1	D
	IR-13-00004-SAM-066-B	Sub-grade Layer Work from St.2+720 to St.2+820	04/24/14	04/26/14	04/27/14	1	A
	IR-13-00004-SAM-067-A	Base Course-1st Layer Work from St.2+240 to St.2+420	04/22/14	04/23/14	04/27/14	4	A
	IR-13-00004-SAM-068-A	Topping Layer Work from St.2+500 to St.2+620	04/22/14	04/23/14	04/27/14	4	A
	IR-13-00004-SAM-069-A	Start Casting for Concrete Encasement for pipe culvert at St.A0+771	04/23/14	04/23/14	04/27/14	4	A
	IR-13-00004-SAM-070-A	Sub-grade Layer from St.2+820 to St.2+960	04/24/14	04/26/14	04/27/14	1	A
	IR-13-00004-SAM-071-A	Description: Base Course-1st Layer from St0+460 to St.0+600, refer to accepted IR-13-00012-SAM-020-A	11/09/14	11/09/14	11/09/14	0	A
	IR-13-00004-SAM-072-A	Casting Concrete B-250 for Parapet from St.0+040 to St.0+074 RHS	04/24/14	04/26/14	04/27/14	1	D
	IR-13-00004-SAM-072-B	Casting Concrete B-250 for Parapet Wall-Part 2- from St.0+040 to St.0+074 RHS	04/27/14	04/27/14	04/27/14	0	A
	IR-13-00004-SAM-073-A	Casting Concrete Encasement around Double Pipe Culvert (800 mm Dia.) at St.0+771	04/27/14	04/27/14	04/27/14	0	D
	IR-13-00004-SAM-073-B	Casting Concrete Encasement around Double Pipe Culvert (800 mm Dia.) at St.0+771	04/28/14	04/28/14	04/29/14	1	A
	IR-13-00004-SAM-074-A	Base Course-1st Layer (Widening Area) from St.1+050 to St.1+250	04/28/14	04/28/14	04/29/14	1	A
	IR-13-00004-SAM-075-A	Handing Over Base Course 1st layer from St.2+420 to 2+580	04/28/14	04/29/14	04/30/14	2	A
	IR-13-00004-SAM-076-A	Casting Concrete for Parapet Wall (Part 3) from St.0+040 to St.0+074 RHS	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00004-SAM-077-A	Handing Over Topping Layer from St.2+800 to St.3+000	04/30/14	05/03/14	05/05/14	2	D
	IR-13-00004-SAM-077-B	Handing Over Topping Layer from St.2+800 to St.3+000	05/07/14	05/08/14	05/11/14	3	A
	IR-13-00004-SAM-078-A	Casting Concrete for the Parapet of Gravity Wall (Part 4)from St.0+040 to St.0+074	05/01/14	05/01/14	05/05/14	4	A
	IR-13-00004-SAM-079-A	Casting Concrete for Inlet & Outlet Foundation of Pipe Culvert at St.0+280	05/06/14	05/06/14	05/07/14	1	A
	IR-13-00004-SAM-080-A	Handing Over Sub-grade from St.2+720 to St.3+160	05/07/14	05/07/14	05/08/14	1	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-081-A	Casting Concrete for Inlet & Outlet Wall of Pipe Culvert at St.0+280	05/08/14	05/10/14	05/11/14	1	D
	IR-13-00004-SAM-081-B	Casting Concrete for Inlet & Outlet Wall of Pipe Culvert at St.0+280	05/13/14	05/13/14	05/14/14	1	A
	IR-13-00004-SAM-082-A	Handing Over Base Course-1st Layer from St.2+800 to St.3+100	05/12/14	05/12/14	05/13/14	1	D
	IR-13-00004-SAM-082-B	Handing Over Base Course-1st Layer from St.2+800 to St.3+100	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00004-SAM-083-A	Handing Over Sub-grade from St.3+160 to St.3+260	05/12/14	05/12/14	05/13/14	1	A
	IR-13-00004-SAM-084-A	Handing Over Topping Layer from St.3+100 to St.3+240	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00004-SAM-085-A	Casting Concrete of Inlet Foundation of Pipe Culvert at St.0+771	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00004-SAM-086-A	Start Installing Pipes for Double Pipe Culvert (1000mm Dia.) at St.2+200	05/19/14	05/19/14	05/22/14	3	A
	IR-13-00004-SAM-087-A	Casting Concrete for Inlet Slab at St.0+280	05/20/14	05/20/14	05/21/14	1	A
	IR-13-00004-SAM-088-A	Casting Encasement concrete for Double Pipe Culvert at St.0+771-Part 2	05/20/14	05/20/14	05/21/14	1	A
	IR-13-00004-SAM-089-A	Casting encasement concrete under Pipe culvert at St.1+650	05/20/14	05/20/14	05/20/14	0	D
	IR-13-00004-SAM-089-B	Casting encasement concrete under Pipe culvert at St.1+650	05/20/14	05/20/14	05/21/14	1	A
	IR-13-00004-SAM-090-A	Handing Over Base Course-1st Layer from St.3+100 to St.3+220	05/22/14	05/24/14	5/25/2014	1	D
	IR-13-00004-SAM-090-B	Handing Over Base Course-1st Layer from St.3+100 to St.3+220	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00004-SAM-091-A	Topping-Layer from St.0+600 to St.0+750, refer to accepted IR-13-00012-SAM-019-A	11/09/14	11/09/14	11/09/14	0	A
	IR-13-00004-SAM-092-A	Casting Encasement Concrete around Pipe Culvert (800 mm Dia.) at St.1+650	05/22/14	05/22/14	05/25/14	3	A
	IR-13-00004-SAM-093-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.-0+020 to St.0+260	05/24/14	05/24/14	05/25/14	1	C
	IR-13-00004-SAM-093-B	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.-0+020 to St.0+260	09/28/14	09/29/14	10/01/14	2	A
	IR-13-00004-SAM-094-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.0+260 to St.0+500	05/26/14	05/26/14	05/27/14	1	C
	IR-13-00004-SAM-094-B	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.0+260 to St.0+500	09/28/14	09/29/14	10/01/14	2	A
	IR-13-00004-SAM-095-A	Casting Concrete for Inlet Head & Wings Wall of Double Pipe Culvert (800 mm Dia.) at St.0+771	05/27/14	05/27/14	05/28/14	1	A
	IR-13-00004-SAM-096-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.0+500 to St.0+640	05/27/14	05/27/14	05/28/14	1	D
	IR-13-00004-SAM-096-B	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.0+500 to St.0+640	09/28/14	09/29/14	10/01/14	2	A
	IR-13-00004-SAM-097-A	Casting Concrete for Outlet & Inlet Foundation of Pipe Culvert at St.1+650	05/29/14	05/31/14	06/03/14	3	A

**USAID WEST BANK/ GAZA**  
**INFRASTRUCTURE NEEDS PROGRAM INPII**  
**CONTRACT NO. AID-294-TO-12-00005**  
**TASK ORDER #12, Multiple Roads Project (South)**  
**Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-098-A	Casting rubble concrete under retaining wall foundation of Pipe Culvert Outlet at St.0+280 & 0+771 and Casting Rubble Concrete under Foundation of Pipe Culvert at St.1+650	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00004-SAM-099-A	Casting Concrete for Retaining Wall Foundation of Outlet for Pipe Culvert at St.0+771 LHS	06/05/14	06/05/14	06/05/14	0	A
	IR-13-00004-SAM-100-A	Casting Concrete for Retaining Wall Foundation of Outlet for Pipe Culvert at St.0+280 LHS	06/05/14	06/05/14	06/05/14	0	A
	IR-13-00004-SAM-101-A	Base course 1 <sup>st</sup> layer from St.0+600 to St.0+860	06/07/14	06/07/14	06/08/14	1	A
	IR-13-00004-SAM-102-A	Casting concrete for inlet foundation & outlet wing wall of pipe culvert (800 mm Dia.) at St.1+650	06/08/14	06/09/14	06/09/14	0	A
	IR-13-00004-SAM-103-A	Casting Concrete Encasement Under Pipe Culvert (1000 mm Dia.) at St.2+690	06/09/14	06/09/14	06/09/14	0	A
	IR-13-00004-SAM-104-A	Casting concrete B-250 for wall of retaining wall at St. 0+280 LHS ( Part#1)	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00004-SAM-105-A	Casting concrete for wall of retaining wall for outlet pipe culvert at St.0+770 (part#1)	06/16/14	06/16/14	06/16/14	0	A
	IR-13-00004-SAM-106-A	Casting concrete B-250 for wall of retaining wall at St. 0+280 LHS ( Part#2)	06/16/14	06/16/14	06/16/14	0	A
	IR-13-00004-SAM-107-A	Casting concrete for wall of retaining wall for outlet pipe culvert at St.0+770 (part#2)	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00004-SAM-108-A	Casting concrete for inlet head & wing wall of pipe culvert at St.1+650 LHS	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00004-SAM-109-A	Base course 2 <sup>nd</sup> layer from St.1+500 to St.2+400	06/19/14	06/21/14	06/22/14	1	D
	IR-13-00004-SAM-109-B	Base course 2nd layer from St.1+500 to St.2+400-refer to approved IR-13-00004-SAM-111-A & 154-A	09/28/14	09/29/14	09/29/14	0	A
	IR-13-00004-SAM-110-A	Casting concrete encasement around pipe culvert at Sta.2+690	06/19/14	06/21/14	06/22/14	1	D
	IR-13-00004-SAM-110-B	Casting concrete encasement around pipe culvert at Sta.2+690	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00004-SAM-111-A	Base Course 2nd Layer from St.1+350 to St.2+150	06/23/14	06/23/14	06/24/14	1	A
	IR-13-00004-SAM-112-A	Start Prime Coat Application (MC) from St.1+350 to 2+150	06/23/14	06/24/14	06/24/14	0	C
	IR-13-00004-SAM-112-B	Start Prime Coat Application (MC) from St.1+350 to 2+150	06/23/14	06/24/14	06/24/14	0	A
	IR-13-00004-SAM-113-A	Base course 2nd layer from St.1+100 to St.1+350	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00004-SAM-114-A	Start Prime Coat Application (MC) from St.1+100 to 1+350	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00004-SAM-115-A	Base course 2nd layer from St.0+800 to St.1+100	06/29/14	06/30/14	07/02/14	2	A
	IR-13-00004-SAM-116-A	Prime Coat Application (MC) from St.1+100 to 1+320	06/29/14	06/30/14	06/30/14	0	A
	IR-13-00004-SAM-117-A	First Stone Boulder wall from St.3+295 to St.3+335 RHS	07/02/14	07/02/14	07/02/14	0	D
	IR-13-00004-SAM-117-B	First Stone Boulder wall from St.3+295 to St.3+335 RHS	07/03/14	07/05/14	07/07/14	2	A

**USAID WEST BANK/ GAZA**  
**INFRASTRUCTURE NEEDS PROGRAM INPII**  
**CONTRACT NO. AID-294-TO-12-00005**  
**TASK ORDER #12, Multiple Roads Project (South)**  
**Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-118-A	Handing over curbstone for side walk from St.0+000 to St.0+140 RHS & Parking area	07/03/14	07/05/14	07/06/14	1	D
	IR-13-00004-SAM-118-B	Handing over curbstone works and surface preparation for side walk from St.0+000 to St.0+140 RHS & Parking area	09/16/14	09/16/14	09/18/14	2	C
	IR-13-00004-SAM-118-C	Handing over curbstone works and surface preparation for side walk from St.0+000 to St.0+140 RHS & Parking area	09/28/14	09/29/14	09/29/14	0	A
	IR-13-00004-SAM-119-A	Base course 2nd layer from St.0+000 to St.0+600	07/03/14	07/05/14	07/06/14	1	D
	IR-13-00004-SAM-119-B	Base course 2nd layer from St.0+000 to St.0+260	07/06/14	07/06/14	07/08/14	2	A
	IR-13-00004-SAM-120-A	Prime coat application (MCO) from St.0+000 to St.0+260	07/07/14	07/08/14	07/08/14	0	A
	IR-13-00004-SAM-121-A	Handing Over Base course layer for parking area from St.0+130 to 0+270 RHS	07/08/14	07/08/14	07/09/14	1	A
	IR-13-00004-SAM-122-A	Prime coat application (MCO) for parking area from St.0+130 to 0+270 RHS	07/08/14	07/08/14	07/09/14	1	A
	IR-13-00004-SAM-123-A	Base course 2 <sup>nd</sup> layer from St.0+260 to St.0+500	07/09/14	07/09/14	07/09/14	0	A
	IR-13-00004-SAM-124-A	Prime coat application from St.0+260 to St.0+500	07/09/14	07/10/14	07/10/14	0	A
	IR-13-00004-SAM-125-A	Base course 2nd layer from St.0+500 to St.0+960	07/10/14	07/10/14	07/10/14	0	A
	IR-13-00004-SAM-126-A	Second row of stone boulder wall from St.3+297 to St.3+339 RHS	07/20/14	07/20/14	07/20/14	0	A
	IR-13-00004-SAM-127-A	Prime coat application from St.0+500 to St.0+960	07/10/14	07/12/14	07/13/14	1	A
	IR-13-00004-SAM-128-A	Formwork & steel reinforcement for inlet & outlet foundation of pipe culvert at St.2+690	07/14/14	07/14/14	07/14/14	0	A
	IR-13-00004-SAM-129-A	Formwork & steel reinforcement for up stand wall of out let pipe culvert at St.0+280 LHS	07/14/14	07/14/14	07/14/14	0	A
	IR-13-00004-SAM-130-A	Topping Layer from St.23+360 to St.3+540	7/12/2014	7/13/2014	07/13/14	0	A
	IR-13-00004-SAM-131-A	Sub grade Layer from St.3+360 to St.3+860	07/16/14	06/15/14	07/17/14	1	A
	IR-13-00004-SAM-132-A	Topping Layer from St.3+540 to St.3+800	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00004-SAM-133-A	Sub Grade Layer from St.3+860 to St.4+060	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00004-SAM-134-A	Casting Concrete for Head & Wing Wall of Pipe Culvert Inlet & Outlet at St.2+690	07/20/14	07/20/14	07/20/14	0	A
	IR-13-00004-SAM-135-A	Third row of stone boulder wall from St.3+299.8 to St.3+336.3 RHS	07/23/14	07/24/14	07/24/14	0	A
	IR-13-00004-SAM-136-A	Topping Layer from St.2+620 to St.2+720	07/23/14	07/24/14	07/24/14	0	A
	IR-13-00004-SAM-137-A	Sub grade layer from St.B0+160 to St.B0+320 RHS&LHS	07/24/14	07/26/14	07/26/14	0	D
	IR-13-00004-SAM-137-B	Sub grade layer from St.B0+160 to St.B0+320 RHS&LHS -refer to approved IR-13-00004-SAM-140-A	09/28/14	09/29/14	09/29/14	0	A
	IR-13-00004-SAM-138-A	Topping layer from St.3+800 to St.4+060 RHS&LHS	08/03/14	08/03/14	08/03/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-139-A	Fourth row of stone boulder wall from St.3+299.8 to St.3+336.3 RHS	08/06/14	08/06/14	08/06/14	0	A
	IR-13-00004-SAM-140-A	Sub grade from St.B.0+120 to St.B0+320	08/06/14	08/06/14	08/07/14	1	A
	IR-13-00004-SAM-141-A	Start Excavation work for trench of Water Pipe line 3" from St.2+535 to St.2+750 LHS	08/07/14	08/07/14	08/07/14	0	A
	IR-13-00004-SAM-142-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 3" from St.2+535 to St.2+690 LHS	08/07/14	08/07/14	08/07/14	0	A
	IR-13-00004-SAM-143-A	Topping layer from St.B0+120 to St.B0+320	08/07/14	08/09/14	08/09/14	0	A
	IR-13-00004-SAM-144-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 3" from St.2+710 to St.2+850 LHS	08/07/14	08/09/14	08/09/14	0	A
	IR-13-00004-SAM-145-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 3" from St.2+850 to St.3+050 LHS	08/10/14	08/10/14	08/10/14	0	A
	IR-13-00004-SAM-146-A	Base course for side walk from St.0+000 to St.0+140 RHS	08/11/14	08/11/14	08/11/14	0	A
	IR-13-00004-SAM-147-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 3" from St.3+050 to St.3+148 LHS	08/11/14	08/11/14	08/11/14	0	A
	IR-13-00004-SAM-148-A	Casting concrete sample for side walk from St.0-032 to St.0-006 RHS	08/12/14	08/12/14	08/12/14	0	A
	IR-13-00004-SAM-149-A	fifth row of stone boulder wall from St.3+297.5 to St.3+333.91 RHS	08/12/14	08/12/14	08/12/14	0	A
	IR-13-00004-SAM-150-A	sample for casting concrete for side ditch from St.0+354 to St.0+366 RHS.	08/13/14	08/18/14	08/18/14	0	A
	IR-13-00004-SAM-151-A	Casting Concrete for Outlet & Inlet Foundation of pipe Culvert at St.2+202	08/14/14	08/16/14	08/16/14	0	A
	IR-13-00004-SAM-152-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.3+184 to St.3+284	08/17/14	08/17/14	08/17/14	0	A
	IR-13-00004-SAM-153-A	Casting concrete for side walk from St.0+000 to St.0+270 RHS	08/17/14	08/17/14	08/17/14	0	A
	IR-13-00004-SAM-154-A	Base course Layer from St.A2+180 to St.A2+600	08/19/14	08/19/14	08/19/14	0	A
	IR-13-00004-SAM-155-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.3+284 to St.3+384	08/18/14	08/18/14	08/18/14	0	A
	IR-13-00004-SAM-156-A	Casting concrete Protection from St.0-055 to St.0+060 LHS & from St.0-055 to St.0-020 RHS	08/19/14	08/19/14	08/19/14	0	A
	IR-13-00004-SAM-157-A	casting concrete for side ditch from St.0+380 to St.0+480 RHS.	08/19/14	08/19/14	08/19/14	0	A
	IR-13-00004-SAM-158-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.3+384 to St.3+650	08/19/14	08/19/14	08/19/14	0	A
	IR-13-00004-SAM-159-A	casting concrete for side ditch from St.0+480 to St.0+580 RHS.	08/20/14	08/21/14	08/21/14	0	A
	IR-13-00004-SAM-160-A	Casting concrete Protection from St.0+060 to St.0+270 LHS.	08/20/14	08/21/14	08/21/14	0	A
	IR-13-00004-SAM-161-A	Casting Concrete for Outlet head and wing wall of pipe Culvert at St.2+202	08/21/14	08/23/14	08/23/14	0	A
	IR-13-00004-SAM-162-A	base course 1st layer from Sta.B0+120 to Sta.B0+320	08/21/14	08/23/14	08/23/14	0	A
	IR-13-00004-SAM-163-A	Excavation, Bedding, Pipe Lying, Welding, Rapping, Embedding & Backfilling for Water Pipe Line 4" from St.3+650 to St.4+000	08/21/14	08/21/14	08/21/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 02**

Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-SAM-164-A	Handing Over Sub-grade from St.3+260 to St.3+360	08/26/14	08/26/14	08/26/14	0	A
	IR-13-00004-SAM-165-A	Casting concrete for inlet head & wing wall of pipe culvert at St.2+200 LHS	08/27/14	08/27/14	08/27/14	0	A
	IR-13-00004-SAM-166-A	base course 2nd layer from Sta.B0+080 to Sta.B0+320	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00004-SAM-167-A	milling works from St.0-115 to St.0+080	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00004-SAM-168-A	Tack coat application for Seg.B from St.B0-115 to St.B0+080.	08/28/14	08/30/14	08/30/14	0	A
	IR-13-00004-SAM-169-A	Prime coat application for Seg.B from St.B0+080 to St.B0+320.	08/28/14	08/30/14	08/30/14	0	A
	IR-13-00004-SAM-170-A	Start Asphalt binder layer (5cm) for Seg.B from St.B0-115 to St.B0+080	08/28/14	08/30/14	08/30/14	0	A
	IR-13-00004-SAM-171-A	Start Asphalt wearing layer for Seg.B from St.B0-115 to St.B0+320	08/28/14	08/30/14	08/30/14	0	A
	IR-13-00004-SAM-172-A	Handover topping Layer from St.3+260 to St.3+360.	08/28/14	08/30/14	08/30/14	0	A
	IR-13-00004-SAM-173-A	base course 1st layer from Sta.3+240 to Sta.3+850	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00004-SAM-174-A	Prime Coat Application (MC) from St.2+180 to 2+600	09/02/14	09/02/14	09/02/14	0	A
	IR-13-00004-SAM-175-A	base course 2nd Layer from Sta.2+600 to St.2+900	09/02/14	09/02/14	09/02/14	0	A
	IR-13-00004-SAM-176-A	Prime Coat Application (MC) from St.2+600 to 2+800	09/03/14	09/03/14	09/03/14	0	A
	IR-13-00004-SAM-177-A	Casting concrete for wall of water chamber at St.3+860 LHS	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00004-SAM-178-A	base course 1st layer from Sta.3+850 to Sta.4+100	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00004-SAM-179-A	Casting concrete protection at Sta. A2+200 LHS & RHS.	09/04/14	09/06/14	09/06/14	0	D
	IR-13-00004-SAM-179-B	Casting concrete protection at Sta. A2+200 LHS & RHS.	09/17/14	09/17/14	09/17/14	0	A
	IR-13-00004-SAM-180-A	Casting concrete protection and Sta. A2+690 LHS & RHS.	09/04/14	09/06/14	09/06/14	0	D
	IR-13-00004-SAM-180-B	Casting concrete protection and Sta. A2+690 LHS & RHS.	09/10/14	09/10/14	09/10/14	0	A
	IR-13-00004-SAM-181-A	Base course 2nd Layer from Sta. A2+900 to Sta. A3+300	09/04/14	09/06/14	09/06/14	0	A
	IR-13-00004-SAM-182-A	Casting concrete protection from Sta. B0+220 to Sta. B0+320 LHS.	09/07/14	09/07/14	09/07/14	0	A
	IR-13-00004-SAM-183-A	Location & Excavation for foundation of traffic sign from Sta. A0+000 to Sta. A2+800 LHS&RHS.	09/07/14	09/07/14	09/08/14	1	A
	IR-13-00004-SAM-184-A	casting concrete for foundation of traffic sign from Sta. A0+000 to Sta. A2+800 LHS&RHS.	09/07/14	09/07/14	09/08/14	1	A
	IR-13-00004-SAM-185-A	Hydraulic presser test for water line (2", 3" & 4") from St. A2+438 to St.A4+184 LHS.	09/06/14	09/06/14	09/07/14	1	A
	IR-13-00004-SAM-186-A	casting concrete for slab of water chamber at Sta. 3+860 LHS	09/08/14	09/08/14	09/08/14	0	A
	IR-13-00004-SAM-187-A	Casting concrete protection from Sta. B0+130 to Sta. B0+190 RHS.	09/08/14	09/08/14	09/08/14	0	A
	IR-13-00004-SAM-188-A	Casting concrete protection from Sta. B0+080 to Sta. B0+130 RHS & Casting concrete protection from Sta. B0+050 to Sta. B0+220 LHS.	09/11/14	09/11/14	09/11/14	0	A
	IR-13-00004-SAM-189-A	Base course 2nd layer from Sta. A3+700 to Sta. A3+800.	09/11/14	09/13/14	09/14/14	1	A



**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 03**



Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-BTH-001-A	Implementation of Traffic Control & Safety Plan-Wadi Shaheen Road(AL Ein Segment ) from St.0+000 to St.0+095	11/02/13	11/02/13	11/03/13	1	A
	IR-13-00004-BTH-002-A	Excavation work for 60 m trench to install 8" water line-Wadi Shaheen Road(AL Ein Segment ) from St.0+000 to St.0+095	11/02/13	11/02/13	11/03/13	1	A
	IR-13-00004-BTH-003-A	Installation work of 8"&4" water pipeline-Wadi Shaheen Road(AL Ein Segment ) from St.0+000 to St.0+095	11/02/13	11/02/13	11/03/13	1	A
	IR-13-00004-BTH-004-A	Backfilling work with single size of 8" water pipe line-Wadi Shaheen Road(AL Ein Segment ) from St.0+000 to St.0+095	11/02/13	11/03/13	11/03/13	0	A
	IR-13-00004-BTH-005-A	Casting Concrete above water line trench (30-40cm) depth on the full width of the trench-Wadi Shaheen Road-AL Ein Segment	11/02/13	11/03/13	11/03/13	0	A
	IR-13-00004-BTH-006-A	Adjustment of Manholes Covers-Wadi Shaheen Road-AL Ein Segment	11/03/13	11/04/13	11/05/13	1	A
	IR-13-00004-BTH-007-A	Milling Work-Wadi Shaheen Road-AL Ein Segment	11/04/13	11/05/13	11/05/13	0	A
	IR-13-00004-BTH-008-A	Installation work of Curbstone-Wadi Shaheen Road-AL Ein Segment	11/04/13	11/05/13	11/05/13	0	A
	IR-13-00004-BTH-009-A	Flush & Disinfection of 8" & 4" water lines-Wadi Shaheen Road-AL Ein Segment	11/04/13	11/05/13	11/05/13	0	A
	IR-13-00004-BTH-010-A	Pressure Test for 8" & 6" Water Lines-Wadi Shaheen Road-AL Ein Segment	11/04/13	11/05/13	11/05/13	0	A
	IR-13-00004-BTH-011-A	Furnishing & Applying Bituminous (RC)-Wadi Shaheen Road-AL Ein Segment	11/05/13	11/05/13	11/06/13	1	A
	IR-13-00004-BTH-012-A	Asphalt Work-Wadi Shaheen Road-AL Ein Segment	11/05/13	11/06/13	11/06/13	0	A
	IR-13-00004-BTH-013-A	Steel Reinforcement for Sidewalks-Wadi Shaheen Road-AL Ein Segment	11/12/13	11/13/13	11/13/13	0	A
	IR-13-00004-BTH-014-A	Casting Concrete for Sidewalks-Wadi Shaheen Road (AL Ein Segment) RHS	11/12/13	11/13/13	11/13/13	0	A
	IR-13-00004-BTH-015-A	Installation of (No Entrance) Sign-Wadi Shaheen Road(AL Ein Segment) RHS	11/12/13	11/13/13	11/13/13	0	A
	IR-13-00004-BTH-016-A	Start Construction Excavation-Festival Yard at AL Sha'eb Intersection-Beit Sahour	12/08/13	12/09/13	12/09/13	0	A
	IR-13-00004-BTH-017-A	Start Installation of Curbstone-Festival Yard at AL Sha'eb Intersection-Beit Sahour	12/09/13	12/09/13	12/10/13	1	A
	IR-13-00004-BTH-018-A	Handing Over Compacted Sub-grade for Widening Works & Sidewalk-Festival Yard at AL Sha'eb Intersection-Beit Sahour	12/10/13	12/10/13	12/11/13	1	A
	IR-13-00004-BTH-019-A	Start Supplying & Compacting of Base Course for Widening Works & Sidewalk-Festival Yard at AL Sha'eb Intersection-Beit Sahour	12/10/13	12/10/13	12/11/13	1	A
	IR-13-00004-BTH-020-A	Start Installation of Precast Concrete Interlocking Blocks-Festival Yard at AL Sha'eb Intersection-Beit Sahour	12/10/13	12/11/13	12/11/13	0	A
	IR-13-00004-BTH-021-A	Start Installation & Fixed Traffic Control Plan-Hebron-Jerusalem Road from St.1+970 to St.3+030	01/02/14	01/02/14	01/03/14	1	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 03**



SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00004-BTH-022-A	Start Milling Works-Hebron-Jerusalem Road from St.1+970 to St.3+030	01/02/14	01/02/14	01/03/14	1	A
	IR-13-00004-BTH-023-A	Start Fixing & Adjusting the Existing Manholes at Hebron-Jerusalem Road from St.2+000 to St.3+030 LHS&RHS	01/15/14	01/15/14	01/15/14	0	A
	IR-13-00004-BTH-024-A	Start Milling Works-Wadi Ma'ali Road from St.0+070 to St.0+370 & from 0+590 to 0+970 & from 1+090 to 1+432	01/15/14	01/15/14	01/16/14	1	A
	IR-13-00004-BTH-025-A	Visual Inspection of Samples for AL Ameer Curbstone & Interlock Tiles	01/16/14	01/16/14	01/16/14	0	A
	IR-13-00004-BTH-026-A	Casting Concrete for Adjusted Manholes in Hebron-Jerusalem Road from St.2+000 to St.3+030 LHS	01/16/14	01/16/14	01/17/14	1	A
	IR-13-00004-BTH-027-A	Start Installation of Curbstone for Hebron-Jerusalem Road	01/19/14	01/19/14	01/19/14	0	A
	IR-13-00004-BTH-028-A	Start Laying of Wearing Asphalt from St.3+030 LHS-Back for Hebron-Jerusalem Road	01/19/14	01/20/14	01/20/14	0	A
	IR-13-00004-BTH-029-A	Start Adjusting Manholes from St.0+160 to St.1+440-Wadi Ma'ali Road	01/20/14	01/20/14	01/22/14	2	A
	IR-13-00004-BTH-030-A	Start Re-Construction Work of Sidewalk from St.0+580 to St.1+440 LHS&RHS-Wadi Ma'ali Road	01/20/14	01/22/14	01/22/14	0	A
	IR-13-00004-BTH-031-A	Start Adjusting & Casting Concrete for Manholes from St.2+000 to St.3+030 RHS	01/21/14	01/21/14	01/22/14	1	A
	IR-13-00004-BTH-032-A	Start Asphalt Wearing Layer from St.0+155 to St.0+370-Wad Ma'ali Road-Seg.B	01/22/14	01/23/14	01/23/14	0	A
	IR-13-00004-BTH-033-A	Median Pedestrian Crossing-Interlocking & Curbstone Works- from St.2+000 to St.3+000 in Hebron-Jerusalem Road	01/23/14	01/25/14	01/25/14	0	A
	IR-13-00004-BTH-034-A	Start Asphalt Wearing Layer-Seg.A/RHS in Hebron-Jerusalem Road	01/22/14	01/23/14	01/23/14	0	A
	IR-13-00004-BTH-035-A	Start Milling Work for ALShebard Road	01/27/14	01/28/14	01/28/14	0	A
	IR-13-00004-BTH-036-A	Adjusting Work for Manholes for AL Shebrd Road, AL Debs Road from St.0+000 to St.0+220	01/28/14	01/28/14	01/28/14	0	D
	IR-13-00004-BTH-036-B	Adjusting Work for Manholes for AL Shebrd Road, AL Debs Road from St.0+000 to St.0+220	01/29/14	01/29/14	01/29/14	0	A
	IR-13-00004-BTH-037-A	Start Milling Work for AL Attan Road from St.0+130 to St.0+280	01/29/14	01/29/14	01/29/14	0	A
	IR-13-00004-BTH-038-A	Start Milling Work for AL Debs Road from St.0+000 to St.0+220	01/27/14	01/28/14	01/28/14	0	A
	IR-13-00004-BTH-039-A	Sub-grade of Sidewalk from St.0+600 to St.0+720 LHS&RHS in Wadi Ma'ali Road	02/02/14	02/02/14	02/03/14	1	A
	IR-13-00004-BTH-040-A	Curbstone Work from St.0+600 to St.0+740 LHS&RHS in Wadi Ma'ali Road	02/02/14	02/03/14	02/03/14	0	A
	IR-13-00004-BTH-041-A	Adjusting Work for Manholes for AL Attan Road	02/06/14	02/08/14	02/09/14	1	A
	IR-13-00004-BTH-042-A	Installation of Curbstone-AL Dibs Road from St.0+000 to St.0+210	02/08/14	02/09/14	02/10/14	1	A
	IR-13-00004-BTH-043-A	Handing Over of Curbstone-AL Dibs Road from St.0+000 to St.0+210	02/13/14	02/13/14	02/17/14	4	D

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 03**



Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-BTH-043-B	Handing Over of Curbstone-AL Dibs Road from St.0+000 to St.0+210	02/18/14	02/18/14	02/18/14	0	A
	IR-13-00004-BTH-044-A	Casting Concrete for Water Pipe Line Trench-AL Dibs Road from St.0+150 to St.0+205	02/15/14	02/15/14	02/16/14	1	A
	IR-13-00004-BTH-045-A	Handing Over Curbstone-Wadi Ma'ali Road from St.0+880 to St.0+970 RHS&LHS	02/17/14	02/17/14	02/18/14	1	D
	IR-13-00004-BTH-045-B	Handing Over Curbstone-Wadi Ma'ali Road from St.0+860 to St.0+970 RHS&LHS & Intersection at St.0+880 RHS	02/22/14	02/22/14	02/23/14	1	A
	IR-13-00004-BTH-046-A	Handing Over Sub-grade of Sidewalk -Wadi Ma'ali from St.0+880 to St.0+970 LHS	02/17/14	02/17/14	02/18/14	1	A
	IR-13-00004-BTH-047-A	Handing Over Curbstone Wadi Ma'ali from St.0+740 to St.0+880 RHS & from St.0+740 to St.0+830 LHS	02/17/14	02/17/14	02/18/14	1	A
	IR-13-00004-BTH-048-A	Handing Over Curbstone-Wadi Ma'ali Road from St.0+880 to St.0+970 LHS	02/18/14	02/19/14	02/20/14	1	D
	IR-13-00004-BTH-048-B	Handing Over Curbstone-Wadi Ma'ali Road from St.0+880 to St.0+970 LHS	03/26/14	03/26/14	03/27/14	1	A
	IR-13-00004-BTH-049-A	Handing Over Curbstone-Hebron-Jerusalem Road at St.2+025, St.2+040, St.2+055, St.2+230, St.2+362, St.2+646 & St.2+670 LHS & at St.2+828 RHS	02/18/14	02/19/14	02/20/14	1	D
	IR-13-00004-BTH-049-B	Handing Over Curbstone-Hebron-Jerusalem Road at St.2+025, St.2+040, St.2+055, St.2+230, St.2+362, St.2+646 & St.2+670 LHS & at St.2+828 RHS	03/02/14	03/02/14	03/03/14	1	A
	IR-13-00004-BTH-050-A	Handing Over Curbstone-Wadi Ma'ali Road from St.1+080 to St.1+230 LHS	02/20/14	02/22/14	02/23/14	1	A
	IR-13-00004-BTH-051-A	Reconstruction Excavation Work for Sidewalk-AL Dibs Road from St.0+155 to St.0+210	02/20/14	02/22/14	02/23/14	1	A
	IR-13-00004-BTH-052-A	Start Curbstone Installation Work-AL Dibs Road from St.0+155 to St.0+210	02/20/14	02/22/14	02/23/14	1	A
	IR-13-00004-BTH-053-A	Handing Over Curbstone Work-Wadi Ma'ali Road from St.0+830 to St.0+860 LHS	02/23/14	02/23/14	02/23/14	0	A
	IR-13-00004-BTH-054-A	Milling Work of AL Dibs Road Intersection at St.0+000 & Connected Road between AL Dibs & Shephard Roads	02/22/14	02/22/14	02/23/14	1	A
	IR-13-00004-BTH-055-A	Milling Work of Karkafah Road from St.0+000 to St.0+280	02/23/14	02/23/14	02/24/14	1	A
	IR-13-00004-BTH-056-A	Milling Work of PWA from St.0+000 to St.0+280	02/24/14	02/24/14	02/25/14	1	A
	IR-13-00004-BTH-057-A	Milling Work of Festival Yard Intersection-Beit Sahour	02/24/14	02/24/14	02/25/14	1	A
	IR-13-00004-BTH-058-A	Adjustment Work of Manholes-Karkafah Road from St.0+000 to St.0+280	02/24/14	02/24/14	02/25/14	1	A
	IR-13-00004-BTH-059-A	Start Asphalt Work for AL Dibs Road from St.0+000 to St.0+210 & Intersection at St.0+000	02/25/14	02/26/14	02/26/14	0	A
	IR-13-00004-BTH-060-A	Start Asphalt Work for the Road Connected between AL Dibs & AL Shephard Roads-100 length	02/25/14	02/26/14	02/26/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 03**



Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-BTH-061-A	Start Asphalt Work for AL Shephard Road from St.0+000 to St.0+140	02/25/14	02/26/14	02/26/14	0	A
	IR-13-00004-BTH-062-A	Start Asphalt Wearing Layer Work (5cm)-Wadi Ma'ali from St.0+600 to St.0+870	02/26/14	02/27/14	03/02/14	3	A
	IR-13-00004-BTH-063-A	Start Installation of Traffic Signs at Hebron-Jerusalem Road	03/02/14	03/02/14	03/03/14	1	D
	IR-13-00004-BTH-063-B	Start Installation of Traffic Signs at Hebron-Jerusalem Road	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00004-BTH-064-A	Start Thermo-Plastic Paint at Hebron-Jerusalem Road	03/02/14	03/02/14	03/03/14	1	D
	IR-13-00004-BTH-064-B	Start Thermo-Plastic Paint at Hebron-Jerusalem Road	03/03/14	03/03/14	03/04/14	1	A
	IR-13-00004-BTH-065-A	Sample of Curbstone Painting-Wadi Ma'ali Road at St.0+860	03/04/14	03/04/14	03/06/14	2	D
	IR-13-00004-BTH-065-B	Sample of Curbstone Painting-Wadi Ma'ali Road at St.0+860	03/06/14	03/06/14	03/09/14	3	A
	IR-13-00004-BTH-066-A	Sub-grade for Sidewalk from St.1+220 to St.1+380 LHS-Wadi Ma'ali Road	03/05/14	03/05/14	03/06/14	1	A
	IR-13-00004-BTH-067-A	Start Adjustment Work of Manholes at Festival Yard Intersection (No.=9 Manholes)-Beit Sahour	03/06/14	03/06/14	03/06/14	0	D
	IR-13-00004-BTH-067-B	Start Adjustment Work of Manholes at Festival Yard Intersection (No.=9 Manholes)-Beit Sahour	03/26/14	03/26/14	03/27/14	1	A
	IR-13-00004-BTH-068-A	Handing Over Thermo-plastic Paint-Hebron-Jerusalem Road	03/06/14	03/08/14	03/09/14	1	D
	IR-13-00004-BTH-068-B	Handing Over Thermo-plastic Paint-Hebron-Jerusalem Road	04/06/14	04/06/14	04/06/14	0	A
	IR-13-00004-BTH-069-A	Start Installation of Interlock-Wadi Ma'ali Road	03/06/14	03/08/14	03/09/14	1	D
	IR-13-00004-BTH-069-B	Start Installation of Interlock-From St.1+240 to St.1+310 LHS, from St.1+410 to St.1+435 LHS & from St.1+280 to St.1+410 RHS-Wadi Ma'ali Road	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00004-BTH-070-A	Start Reconstruction Excavation Work from St.0+970 to St.1+080-Wadi Ma'ali Road	03/11/14	03/11/14	03/16/14	5	A
	IR-13-00004-BTH-071-A	Handing Over Curbstone Work-Wadi Ma'ali Road From St.1+077 to St.1+135 RHS & from St.1+175 to St.1+435 RHS & from St.1+230 to St.1+435 LHS	03/16/14	03/16/14	03/16/14	0	D
	IR-13-00004-BTH-071-B	Handing Over Curbstone Work-Wadi Ma'ali Road From St.1+077 to St.1+135 RHS & from St.1+175 to St.1+435 RHS & from St.1+230 to St.1+435 LHS	03/26/14	03/26/14	03/27/14	1	A
	IR-13-00004-BTH-072-A	Handing Over Sub-grade Work-Wadi Ma'ali Road From St.0+970 to St.1+080	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00004-BTH-073-A	Start basalt asphalt works-Al Karkafa Road	03/17/14	03/19/14	03/23/14	4	A
	IR-13-00004-BTH-074-A	Start basalt asphalt works Attan Road from St. 0+130 to St. 0+280 & PWA's intersection	03/17/14	03/20/14	03/23/14	3	A
	IR-13-00004-BTH-075-A	Start asphalt works in Beit Sahour's intersection	03/20/14	03/20/14	03/23/14	3	A
	IR-13-00004-BTH-076-A	Visual inspection for handrail sample Bethlehem office	03/20/14	03/20/14	03/23/14	3	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 03**



Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-BTH-077-A	Base course layer from St. 0+970 to St.1+070 - Wadi Ma'ali Road	03/20/14	03/20/14	03/23/14	3	D
	IR-13-00004-BTH-077-B	Base course layer from St. 0+970 to St.1+070 - Wadi Ma'ali Road	03/26/14	03/26/14	03/27/14	1	A
	IR-13-00004-BTH-078-A	Curbstone works from St. 0+970 to St.1+070 - Wadi Ma'ali Road	03/20/14	03/20/14	03/23/14	3	D
	IR-13-00004-BTH-078-B	Curbstone works from St. 0+970 to St.1+070 - Wadi Ma'ali Road	03/26/14	03/26/14	03/27/14	1	A
	IR-13-00004-BTH-079-A	Curbstone works from St. 0+600 to St.0+740 RHS&LHS - Wadi Ma'ali Road	03/20/14	03/20/14	03/23/14	3	A
	IR-13-00004-BTH-080-A	Start asphalt works from St. 0+970 to St.1+070 - Wadi Ma'ali Road	03/20/14	03/22/14	03/25/14	3	A
	IR-13-00004-BTH-081-A	Casting blinding concrete for boundary wall from St. 0+000 to St.0+043 RHS - Al Dibis Road	03/24/14	03/24/14	03/24/14	0	A
	IR-13-00004-BTH-082-A	Casting blinding concrete for boundary wall from St. 0+043 to St.0+052 LHS - Al Dibis Road	03/24/14	03/24/14	03/24/14	0	A
	IR-13-00004-BTH-083-A	Casting concrete for boundary wall foundation from St. 0+043 to St.0+052 LHS - Al Dibis Road	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00004-BTH-084-A	Casting blinding concrete for Retaining wall from St.0+003 to St.0+017 - Wadi Shahin Road	03/27/14	03/27/14	03/31/14	4	A
	IR-13-00004-BTH-085-A	Start excavation works AL Quitta Road	03/27/14	03/29/14	03/31/14	2	A
	IR-13-00004-BTH-086-A	Casting concrete for Boundary wall in Al Dibis Road RHS	03/29/14	03/29/14	03/31/14	2	A
	IR-13-00004-BTH-089-A	Casting Concrete for Boundary Wall from St.0+043 to St.0+055-AL Dibs Road	04/01/14	04/01/14	04/02/14	1	A
	IR-13-00004-BTH-090-A	Start Excavation & Compaction & Reinforcement & Casting Concrete B-250 for Trench-AL Qeita Road	04/03/14	04/03/14	04/03/14	0	A
	IR-13-00004-BTH-091-A	Start Works of Base Course Layer -AL Qeita Road	04/06/14	04/06/14	04/06/14	0	A
	IR-13-00004-BTH-092-A	Start Adjusting Manhole from St.0+000 to St.0+140-Wadi Shaheen Road	04/07/14	04/07/14	04/07/14	0	A
	IR-13-00004-BTH-093-A	Handing Over Preparation work of Curbstone painting from St.1+445 to St.0+900-Wadi Ma'ali Road	04/13/14	04/13/14	04/15/14	2	D
	IR-13-00004-BTH-093-B	Handing Over Preparation work of Curbstone painting from St.1+445 to St.0+900-Wadi Ma'ali Road	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00004-BTH-094-A	Start Installation of Handrail-Hebron-Jerusalem Road	04/10/14	04/10/14	04/13/14	3	A
	IR-13-00004-BTH-095-A	Start Installation of Curbstone -AL Qeta'a Road	04/10/14	04/11/14	04/13/14	2	D
	IR-13-00004-BTH-095-B	Start Installation of Curbstone -AL Qeta'a Road	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00004-BTH-096-A	Installation of Handrail-Hebron Jerusalem Road	04/10/14	04/12/14	04/13/14	1	A
	IR-13-00004-BTH-097-A	Start Installation of Handrail-AL Dibs Road-from St.0+000 to St.0+020 RHS & LHS	04/10/14	04/12/14	04/13/14	1	A
	IR-13-00004-BTH-098-A	Casting Concrete for Handrail-Hebron-Jerusalem Road (Bab Zqaq)at St.4+780	04/12/14	04/13/14	04/13/14	0	A

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-TO-12-00005  
TASK ORDER #12, Multiple Roads Project (South)  
Inspection Request Log - Project 03**



Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-BTH-100-A	Handing Over Curbstone -AL Qeta'a Road from St.0+000 to St.0+105 RHS & from St.0+000 to St.0+175 LHS	04/14/14	04/14/14	04/14/14	0	D
	IR-13-00004-BTH-100-B	Handing Over Curbstone -AL Qeta'a Road from St.0+000 to St.0+105 RHS & from St.0+000 to St.0+175 LHS	04/20/14	04/20/14	04/20/14	0	A
	IR-13-00004-BTH-101-A	Handing over handrail at Hebron Jerusalem Road	04/15/14	04/15/14	04/15/14	0	D
	IR-13-00004-BTH-101-B	Handing over handrail at Hebron Jerusalem Road	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00004-BTH-102-A	Start Work at existing wall (Construct 10 cm Concrete shutting of the existing concrete wall and adjust the top level) at Al Dibs Road	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00004-BTH-103-A	Casting Concrete for Handrail at Al Dibs Road	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00004-BTH-104-A	Start Installation of Curbstone At Wadi Shaheen Road	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00004-BTH-105-A	Casting Concrete for Adjusting Manholes - Al Qet'a Road	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00004-BTH-106-A	Start Asphalt Work (Wadi Shaheen Road) from St.0+100 to st.0+250	04/16/14	04/17/14	04/18/14	1	A
	IR-13-00004-BTH-107-A	Handing Over Base Course Layer -AL Qet'a Road	04/16/14	04/17/14	04/18/14	1	A
	IR-13-00004-BTH-108-A	Start Asphalt Work-AL Qet'a Road	04/16/14	04/17/14	04/18/14	1	A
	IR-13-00004-BTH-109-A	Work at Wadi Shaheen Road Widening- Base Course	04/16/14	04/16/14	04/18/14	2	A
	IR-13-00004-BTH-110-A	Work at Wadi Shaheen Road Widening- Concrete	04/16/14	04/16/14	04/18/14	2	A
	IR-13-00004-BTH-111-A	Start Removing of Parapet Retaining Wall-Wadi Ma'ali at St.1+440 RHS	04/17/14	04/17/14	04/21/14	4	A
	IR-13-00004-BTH-112-A	Casting Concrete for Boundary Wall-at AL Dibs Road	04/17/14	04/17/14	04/21/14	4	A
	IR-13-00004-BTH-114-A	Start Thermoplastic Paint at Bethlehem Roads (Beit Sahour-Festival Yard, AL Atan Road & AL Karkafah Road)	04/17/14	04/18/14	04/21/14	3	A
	IR-13-00004-BTH-115-A	Start Thermoplastic Paint at Bethlehem Roads (al Dibs Road, Philips Road & Shephared Road)	04/17/14	04/19/14	04/21/14	2	A
	IR-13-00004-BTH-116-A	Start Installation of Interlock Work (AL Qeta' Road )	04/17/14	04/20/14	04/24/14	4	A
	IR-13-00004-BTH-117-A	Handing Over Preparation work of Curbstone painting from St.0+600 to St.0+900 RHS & from St.0+660 to St.0+800 LHS-Wadi Ma'ali Road	04/21/14	04/21/14	04/21/14	0	A
	IR-13-00004-BTH-118-A	Handing Over Removing Parapet of the Retaining Wall-Wadi Ma'ali at St.1+440 RHS	04/20/14	04/20/14	04/21/14	1	A
	IR-13-00004-BTH-119-A	Installation of Permanent Sign-Wadi Ma'ali at St.0+600 & AL Qet'a Road at St.0+000 RHS	04/20/14	04/21/14	04/21/14	0	A
	IR-13-00004-BTH-120-A	Handing Over Curbstone Painting at Wadi Ma'ali from St.0+880 to St.1+445	04/21/14	04/21/14	04/21/14	0	A
	IR-13-00004-BTH-121-A	Handing Over Interlock from St.0+600 to St.1+445 RHS, from St.0+660 to St.0+800 & from St.0+880 to St.1+445	04/21/14	04/22/14	04/22/14	0	D
	IR-13-00004-BTH-121-B	Handing Over Interlock from St.0+600 to St.1+445 RHS, from St.0+660 to St.0+800 & from St.0+880 to St.1+445	04/23/14	04/23/14	04/23/14	0	A

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-TO-12-00005  
 TASK ORDER #12, Multiple Roads Project (South)  
 Inspection Request Log - Project 03**



Spec. No.	Submittal No	Description	TRACKING DATES				Approval Status (A,B,C,D,E)
			Submitted on (M/D/Y)	Requested (M/D/Y)	Returned on (M/D/Y)	Review Days	
	IR-13-00004-BTH-122-A	Start Stone Cladding for AL Qaws-Wadi Shaheen (AL Ein)at St.0+100 LHS	04/22/14	04/22/14	04/22/14	0	A
	IR-13-00004-BTH-123-A	Handing Over Base Course Layer of Sidewalk in AL Qet'a Road	04/22/14	04/22/14	04/22/14	0	A
	IR-13-00004-BTH-124-A	Handing Over Preparation Work for Curbstone Painting-AL Dibs Road	04/23/14	04/23/14	04/24/14	1	D
	IR-13-00004-BTH-124-B	Handing Over Preparation Work for Curbstone Painting-AL Dibs Road	04/27/14	04/27/14	04/28/14	1	A
	IR-13-00004-BTH-125-A	Handing Over Stone Cladding for AL Qaws (AL Ein)	04/23/14	04/23/14	04/27/14	4	A
	IR-13-00004-BTH-126-A	Installation Handrail-Wadi Ma'ali at St.0+740 LHS,at St.0+750 RHS&0+760 RHS, AR St.0+880 RHS, 1+020 RHS & 1+440 RHS	04/24/14	04/24/14	04/25/14	1	A
	IR-13-00004-BTH-127-A	Installation of Interlock Tiles-AL Qet'a Road Sidewalks	4/23/2014	4/23/2014	04/27/14	4	A
	IR-13-00004-BTH-128-A	Start Curbstone Painting at Wadi Ma'ali from St.0+600 to St.0+880 & AL Dibs Road	04/24/14	04/26/14	04/27/14	1	D
	IR-13-00004-BTH-128-B	Start Curbstone Painting at Wadi Ma'ali from St.0+600 to St.0+880 & AL Dibs Road	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00004-BTH-129-A	Start Thermoplastic Painting at Wadi Ma'ali, Wadi Shaheen Road & AL Qet'a Road	04/24/14	04/26/14	04/27/14	1	D
	IR-13-00004-BTH-129-B	Start Thermoplastic Painting at Wadi Ma'ali, Wadi Shaheen Road & AL Qet'a Road	04/27/14	04/27/14	04/28/14	1	A
	IR-13-00004-BTH-130-A	Installation of Traffic Sign at Wadi Ma'ali, AL Qet'a Road& Wadi Shaheen	04/24/14	04/26/14	04/27/14	1	A
	IR-13-00004-BTH-131-A	Casting Concrete for Handrail-Wadi Ma'ali at St.0+740 LHS, at St.0+750 &0+760 RHS, at St.1+020 RHS	04/24/14	04/24/14	04/25/14	1	A
	IR-13-00004-BTH-132-A	Handing Over Preparation Work for Curbstone Painting-Beit Sahour –Festival Yard	04/27/14	04/27/14	04/28/14	1	A
	IR-13-00004-BTH-133-A	Casting Concrete for Handrail-Wadi Shaheen Road from St.0+100 to St.0+130 LHS	04/27/14	04/27/14	04/29/14	2	D
	IR-13-00004-BTH-133-B	Casting Concrete for Handrail-Wadi Shaheen Road from St.0+100 to St.0+130 LHS	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00004-BTH-134-A	Start Thermoplastic Painting at AL Qet'a Road	05/04/14	05/04/14	05/05/14	1	A
	IR-13-00004-BTH-135-A	Installation of Steel Handrail-AL Qet'a Road	04/28/14	04/28/14	04/29/14	1	D
	IR-13-00004-BTH-135-B	Installation of Steel Handrail-AL Qet'a Road	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00004-BTH-136-A	Handing Over Preparation Curbstone for Painting-AL Qet'a Road	04/28/14	04/28/14	04/29/14	1	D
	IR-13-00004-BTH-136-B	Handing Over Preparation Curbstone for Painting-AL Qet'a Road	05/03/14	05/03/14	05/05/14	2	A

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

## **F | Submittals Log for the Reporting Period**

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-MRSII-001-A	30- Days Schedule ( Submittals Schedule)	MRSII	P	11/03/13	11/24/13	11/11/13	8	B
	SUB-13-00012-MRSII-002-A	Bank Guarantee	MRSII	P	11/03/13	11/24/13	11/19/13	16	E
	SUB-13-00012-MRSII-003-A	Temporary and Permanent Signs Submittal	MRSII	P	11/04/13	11/25/13	11/11/13	7	B
	SUB-13-00012-MRSII-004-A	Testing Labs	MRSII	P	11/04/13	11/25/13	11/11/13	7	B
	SUB-13-00012-MRSII-005-A	Subcontracting Plan	MRSII	P	11/05/13	11/26/13	11/11/13	6	C
	SUB-13-00012-MRSII-005-B	Subcontracting Plan	MRSII	P	01/20/14	02/10/14	01/29/14	9	E
	SUB-13-00012-MRSII-006-A	Quality Control Plan (QCP)	MRSII	P	11/06/13	11/27/13	11/24/13	18	C
	SUB-13-00012-MRSII-006-B	Quality Control Plan (QCP)	MRSII	P	12/23/13	01/13/14	01/02/14	10	B
	SUB-13-00012-MRSII-007-A	Field Offices Furniture and Equipment Plan	MRSII	P	11/06/13	11/27/13	11/20/13	14	C
	SUB-13-00012-MRSII-007-B	Field Offices Furniture and Equipment Plan	MRSII	P	11/26/13	12/17/13	11/27/13	1	A
	SUB-13-00012-MRSII-008-A	Field Offices location and layout-Secondary Offices	MRSII	P	11/10/13	12/01/13	11/19/13	9	C
	SUB-13-00012-MRSII-008-B	Field Offices location and layout-Secondary Offices	MRSII	P	12/25/13	01/15/14	12/30/13	5	B
	SUB-13-00012-DUR-009-A	Dilapidation Survey-Dura Hebron (Sinjir) Road -Project 01	DUR	P	11/10/13	12/01/13	11/19/13	9	B
	SUB-13-00012-DUR-010-A	Risk Management Program-Dura Hebron (Sinjir) Road -Project 01	DUR	P	11/10/13	12/01/13	11/19/13	9	B
	SUB-13-00012-SAM-011-A	Dilapidation Survey-Sama' Yatta Road -Project 02	SAM	P	11/10/13	12/01/13	11/19/13	9	B
	SUB-13-00012-SAM-012-A	Risk Management Program-Sama' Yatta Road -Project 02	SAM	P	11/10/13	12/01/13	11/19/13	9	B
	SUB-13-00012-SAM-013-A	Survey Plan from Sta.A0+000 to Sta.A4+121-Samua' Yatta Road Segment A-Project 02	SAM	P	11/10/13	12/01/13	11/21/13	11	C
	SUB-13-00012-SAM-013-B	Survey Plan from Sta.A0+000 to Sta.A4+121-Samua' Yatta Road Segment A-Project 02	SAM	P	11/28/13	12/19/13	12/17/13	19	C
	SUB-13-00012-SAM-013-C	Survey Plan from Sta.A0+000 to Sta.A4+121-Samua' Yatta Road Segment A-Project 02	SAM	P	01/02/14	01/23/14	01/06/14	4	B
	SUB-13-00012-DUR-014-A	Survey Plan from Sta.A0+000 to Sta.A4+047-Dura Hebron (Sinjir) Road-Project 01	DUR	P	11/12/13	12/03/13	11/21/13	9	C
	SUB-13-00012-DUR-014-B	Survey Plan from Sta.A0+000 to Sta.A4+047-Dura Hebron (Sinjir) Road-Project 01	DUR	P	01/04/14	01/25/14	01/06/14	2	B
	SUB-13-00012-MRSII-015-A	60-Day Plan of Operation	MRSII	P	11/12/13	12/03/13	11/27/13	15	B
	SUB-13-00012-MRSII-016-A	Project Overview Bar Chart and Master Plan	MRSII	P	11/12/13	12/03/13	11/24/13	12	E
	SUB-13-00012-DUR-017-A	Field Offices location and layout-Primary Office-Dura Hebron (Sinjir) Road-Project 01	DUR	P	11/13/13	12/04/13	11/19/13	6	B
	SUB-13-00012-BTH-018-A	Survey Plan from Sta.0+000 to Sta.5+609- Hebron Jerusalem Road Segment A-Project 03	BTH	P	11/17/13	12/08/13	11/21/13	4	B
	SUB-13-00012-MRSII-019-A	Submittal Schedule	MRSII	P	11/17/13	12/08/13	12/01/13	14	C
	SUB-13-00012-MRSII-019-B	Submittals Schedule	MRSII	P	12/23/13	01/13/14	12/29/13	6	B
	SUB-13-00012-SAM-020-A	Shop Drawings: Plan Profile and Cross Section from Sta.0+750 to Sta.1+500-Samua' Yatta Road Segment A-Project 02	SAM	S	11/17/13	12/08/13	12/04/13	17	C
	SUB-13-00012-SAM-020-B	Shop Drawings: Plan Profile and Cross Section from Sta.0+750 to Sta.1+300-Samua' Yatta Road Segment A-Project 02	SAM	S	12/23/13	01/13/14	01/05/14	13	B
	SUB-13-00012-SAM-020-C	Shop Drawings: Plan Profile and Cross Section from Sta.0+750 to Sta.1+300-Samua' Yatta Road Segment A-Project 02-as per Site Memo No. SM-13-00012-SAM-E-C-016	SAM	S	02/27/14	03/20/14	03/09/14	10	B

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-MRSII-021-A	Safety Plan	MRSII	P	11/19/13	12/10/13	12/01/13	12	C
	SUB-13-00012-MRSII-021-B	Safety Plan	MRSII	P	12/25/13	01/15/14	01/07/14	13	B
	SUB-13-00012-MRSII-022-A	Testing Labs-Water Quality Testing Center	MRSII	P	11/20/13	12/11/13	12/02/13	12	B
	SUB-13-00012-MRSII-023-A	Coordination with Local Authorities Plan and List of Permits and Licenses	MRSII	P	11/20/13	12/11/13	11/27/13	7	C
	SUB-13-00012-MRSII-023-B	Coordination with Local Authorities Plan and List of Permits and Licenses	MRSII	P	11/28/13	12/19/13	12/02/13	4	B
	SUB-13-00012-MRSII-024-A	Contractors all Risk, General Liability Insurance & Workers Compensation Insurance	MRSII	P	11/24/13	12/15/13	11/25/13	1	E
	SUB-13-00012-DUR-025-A	Shop Drawings: Plan and Profile from Sta.0+000 to Sta.0+550-Dura Hebron (Sinjir) Road-Project 01	DUR	S	11/26/13	12/17/13	12/04/13	8	C
	SUB-13-00012-DUR-025-B	Shop Drawings: Plan and Profile from Sta.0+000 to Sta.0+500-Dura Hebron (Sinjir) Road-Project 01	DUR	S	01/08/14	01/29/14	01/12/14	4	B
	SUB-13-00012-MRSII-026-A	Construction Time Schedule and S-curve	MRSII	P	11/27/13	12/18/13	12/18/13	21	C
	SUB-13-00012-MRSII-026-B	Construction Time Schedule and S-curve	MRSII	P	01/07/14	01/28/14	01/28/14	21	C
	SUB-13-00012-MRSII-026-C	Construction Time Schedule and S-curve	MRSII	P	02/11/14	03/04/14	02/13/14	2	A
	SUB-13-00012-MRSII-027-A	Prime Coat Emulsion -Pazkar Ltd.-item No. 3.01	MRSII	M	11/28/13	12/19/13	12/09/13	11	B
	SUB-13-00012-MRSII-028-A	Tack Coat Emulsion -Pazkar Ltd.-item No. 3.02	MRSII	M	11/28/13	12/19/13	12/09/13	11	B
	SUB-13-00012-BTH-029-A	Asphalt Mix Design -Wearing Asphalt 3/4 inch-Al Tarifi Asphalt Plant -item No.3.03-Project 03	BTH	M	11/28/13	12/19/13	12/10/13	12	B
	SUB-13-00012-MRSII-030-A	High Performance Thermoplastic Road Markings- Prismo Road Markings Ltd. T/A Ennis-item No. 5.03-a	MRSII	M	11/28/13	12/19/13	12/09/13	11	B
	SUB-13-00012-MRSII-031-A	Cat Eyes-Iriflix Ltd.-item No.5.03.b & c	MRSII	M	11/28/13	12/19/13	12/09/13	11	B
	SUB-13-00012-BTH-032-A	Traffic Control Plan-Milling and Overlay of Bethlehem Internal Roads-Project 03	BTH	P	11/28/13	12/19/13	12/19/13	21	B
	SUB-13-00012-DUR-033-A	Traffic Control Plan-Dura - Hebron Road -Project 01	DUR	P	12/01/13	12/22/13	12/19/13	18	B
	SUB-13-00012-BTH-034-A	Contractors all Risk, General Liability Insurance Amendment (For Submittal No.:SUB-13-00012-MRSII-024-A)	BTH	P	12/02/13	12/23/13	12/05/13	3	E
	SUB-13-00012-MRSII-035-A	Field Offices Furniture and Equipment Plan Amendment (For Submittal No.: SUB-13-00012-MRSII-007-B)	MRSII	P	12/02/13	12/23/13	12/03/13	1	A
	SUB-13-00012-BTH-036-A	Survey Plan -Segments B & C -Milling and Overlay of Bethlehem Internal Roads-Project 03	BTH	P	12/03/13	12/24/13	12/23/13	20	B
	SUB-13-00012-SAM-037-A	Shop Drawings: Plan Profile and Cross Section from Sta.0+000 to Sta.0+750-Samua' Yatta Road Segment A-Project 02	SAM	S	12/03/13	12/24/13	12/23/13	20	C
	SUB-13-00012-SAM-037-B	Shop Drawings: Plan Profile and Cross Section from Sta.0+000 to Sta.0+750-Samua' Yatta Road Segment A-Project 02	SAM	S	01/07/14	01/28/14	01/12/14	5	B
	SUB-13-00012-BTH-038-A	Shop Drawings: Plan Profile and Cross Section from Sta.0+000 to Sta.0+750-Samua' Yatta Road Segment A-Project 02	BTH	M	12/08/13	12/29/13	12/19/13	11	B
	SUB-13-00012-BTH-039-A	Concrete Mix Design- Al Abed Mixing Plant-Item 4.07.b-Milling & Overlay of Bethlehem internal Roads-Project 03	BTH	M	12/08/13	12/29/13	12/19/13	11	B
	SUB-13-00012-BTH-040-A	Shop Drawings: Plan for Segments A,B and C-Milling & Overlay of Bethlehem internal Roads-Project 03	BTH	S	12/08/13	12/29/13	12/24/13	16	B
	SUB-13-00012-SAM-041-A	Traffic Control Plan-Phase I-Samua' Yatta Road Segment A-Project 02	SAM	P	12/09/13	12/30/13	12/29/13	20	B

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	SUBMITTAL		TRACKING DATES				Approval Status (A,B,C,D,E)
			Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-SAM-042-A	Traffic Control Plan-Phase III-Samua' Yatta Road Segment B-Project 02	SAM	P	12/23/13	01/13/14	12/26/13	3	D
	SUB-13-00012-SAM-042-B	Traffic Control Plan-Phase III-Samua' Yatta Road Segment B-Project 02	SAM	P	01/09/14	01/30/14	01/14/14	5	B
	SUB-13-00012-MRSII-043-A	Environmental Mitigation Plan	MRSII	P	12/23/13	01/13/14	01/02/14	10	B
	SUB-13-00012-MRSII-044-A	Method Statement	MRSII	P	12/26/13	01/16/14	01/15/14	20	C
	SUB-13-00012-MRSII-044-B	Method Statement	MRSII	P	01/27/14	02/17/14	02/11/14	15	B
	SUB-13-00012-BTH-045-A	Dilapidation Survey Plan- Milling and Overlay of Bethlehem Internal Roads - Project 03	BTH	P	12/25/13	01/15/14	01/02/14	8	B
	SUB-13-00012-MRSII-046-A	Branding Plan	MRSII	P	12/25/13	01/15/14	01/07/14	13	E
	SUB-13-00012-MRSII-047-A	Key Personnel Plan	MRSII	P	12/25/13	01/15/14	12/30/13	5	C
	SUB-13-00012-MRSII-047-B	Key Personnel Plan	MRSII	P	01/20/14	02/10/14	01/22/14	2	E
	SUB-13-00012-DUR-048-A	Storm Water Drainage RC Pipes - PCI Co. - Project 01- BOQ item No. 4.02	DUR	M	12/25/13	01/15/14	01/05/14	11	C
	SUB-13-00012-DUR-048-B	Storm Water Drainage RC Pipes - PCI Co. - Project 01- BOQ item No. 4.02	DUR	M	03/19/14	04/09/14	04/03/14	15	B
	SUB-13-00012-DUR-048-C	Storm water Drainage pipes- PCI Co.-Item 4.02-Project 01	DUR	M	04/29/14	05/20/14	05/01/14	2	B
	SUB-13-00012-DUR-049-A	Catch Basin and heavy duty grating -PCI-CO.-Project 01- BOQ item No. 4.06-a	DUR	M	12/25/13	01/15/14	01/05/14	11	C
	SUB-13-00012-DUR-049-B	Catch Basin and heavy duty grating -PCI-CO.-Project 01- BOQ item No. 4.06-a	DUR	M	03/30/14	04/20/14	04/14/14	15	E
	SUB-13-00012-DUR-050-A	Concrete JMD- Al Wakeel Co.- Project 01- BOQ Item No. 4.07	DUR	M	12/25/13	01/15/14	01/05/14	11	C
	SUB-13-00012-DUR-050-B	Concrete JMD- Al Wakeel Co.- Project 01- BOQ Item No. 4.07	DUR	M	11/10/14	12/01/14	11/20/14	10	A
	SUB-13-00012-DUR-051-A	Steel Water Pipeline - FIP Co. - Project 01- BOQ item No. 4.22	DUR	M	12/25/13	01/15/14	01/01/14	7	B
	SUB-13-00012-SAM-052-A	Concrete Job Mix Design - Al Abed Concrete Mixing Plant- Project 02- BOQ Item No. 4.07	SAM	M	12/25/13	01/15/14	12/30/13	5	B
	SUB-13-00012-SAM-053-A	Asphalt Wearing JMF/ Tarifi Asphalt Plant/ Project 02- BOQ Item No. 3.03	SAM	M	12/25/13	01/15/14	12/30/13	5	B
	SUB-13-00012-BTH-054-A	Risk Management Program -Milling and Overlay of Bethlehem Internal Roads - Project 03	BTH	P	12/25/13	01/15/14	01/02/14	8	B
	SUB-13-00012-MRSII-055-A	Curbstone Marking Paint- Tambour- BOQ item No. 4.12	MRSII	M	12/25/13	01/15/14	01/02/14	8	B
	SUB-13-00012-MRSII-056-A	Security System	MRSII	P	12/29/13	01/19/14	01/05/14	7	C
	SUB-13-00012-MRSII-056-B	Security System	MRSII	P	01/16/14	02/06/14	01/16/14	0	B
	SUB-13-00012-BTH-057-A	Guardrail ESP4-N2-PRINS DOKKUM-Project 03-item 5.05.a	BTH	M	12/30/13	01/20/14	01/02/14	3	A
	SUB-13-00012-SAM-058-A	Guardrail ESP4-N2-PRINS DOKKUM-Project 02-item 5.05.a	SAM	M	12/30/13	01/20/14	01/02/14	3	A
	SUB-13-00012-MRSII-059-A	Pre cast concrete Curbstone- Al Ameer Co- MRSII-item 4.12	MRSII	M	01/02/14	01/23/14	01/07/14	5	B
	SUB-13-00012-DUR-060-A	Drainage Manholes-PCI- project 01-item 4.03	DUR	M	01/02/14	01/23/14	01/05/14	3	C
	SUB-13-00012-DUR-060-B	Drainage Manholes-PCI- project 01-item 4.03	DUR	M	11/10/14	12/01/14	11/20/14	10	A
	SUB-13-00012-BTH-061-A	Interlocking Block- Al Ameer Co- Project 03- item 4.13.a	BTH	M	01/02/14	01/23/14	01/07/14	5	B
	SUB-13-00012-SAM-062-A	Storm water RC pipes-Addasi Co- Project 02-item 4.02	SAM	M	01/02/14	01/23/14	01/05/14	3	C
	SUB-13-00012-SAM-062-B	Storm water RC pipes-PCI Co- Project 02-item 4.02	SAM	M	04/29/14	05/20/14	05/06/14	7	B
	SUB-13-00012-MRSII-063-A	Traffic signs material_ Netivey Hamifratz/Top Safety _item 5.01	MRSII	M	01/05/14	01/26/14	01/06/14	1	B

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-I-00-12-00005  
TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-064-A	Shop Drawings: Storm Water: Plan ,Profile and Cross Section from Sta.0+190 to Sta.0+500 -Dura Hebron Sinjir Road -Project 01	DUR	S	01/09/14	01/30/14	01/20/14	11	C
	SUB-13-00012-DUR-064-B	Shop Drawings: Storm Water: Plan ,Profile and Cross Section from Sta.0+190 to Sta.0+500 -Dura Hebron Sinjir Road -Project 01	DUR	S	02/05/14	02/26/14	02/11/14	6	B
	SUB-13-00012-DUR-065-A	Proposed Storage Area and Dumping Site- Project 01	DUR	P	01/09/14	01/30/14	01/14/14	5	B
	SUB-13-00012-DUR-066-A	Shop Drawings: Water Pipeline Plan from Sta.0+000 to Sta.0+500-Project 01	DUR	S	01/09/14	01/30/14	01/16/14	7	C
	SUB-13-00012-DUR-066-B	Shop Drawings: Water Pipeline Plan from Sta.0+000 to Sta.0+500-Project 01	DUR	S	01/23/14	02/13/14	01/30/14	7	B
	SUB-13-00012-DUR-067-A	Concrete Mix Design-Abed Co.- Project 01- BOQ item 4.07	DUR	M	01/09/14	01/30/14	01/12/14	3	B
	SUB-13-00012-DUR-068-A	Storm Water Drainage RC Pipes - PCP Co.- Project 01- BOQ item No. 4.02	DUR	M	01/09/14	01/30/14	01/12/14	3	B
	SUB-13-00012-BTH-069-A	Proposed Storage Area and Dumping Site- Project 03	BTH	P	01/16/14	02/06/14	01/16/14	0	B
	SUB-13-00012-DUR-070-A	Proposed Welders for Welders Qualification Test - CV	DUR	P	01/19/14	02/09/14	01/23/14	4	B
	SUB-13-00012-SAM-071-A	Proposed Storage Area and Dumping Site- Project 02	SAM	P	01/19/14	02/09/14	01/22/14	3	B
	SUB-13-00012-DUR-072-A	Concrete Wall from Sta.0+026 to Sta.0+054 LHS-Project 01	DUR	S	01/20/14	02/10/14	01/29/14	9	C
	SUB-13-00012-DUR-072-B	Retaining Wall from Sta.0+026 to Sta.0+054 LHS-Project 01	DUR	S	02/02/14	02/23/14	02/12/14	10	C
	SUB-13-00012-DUR-072-C	Retaining Wall from Sta.0+026 to Sta.0+054 LHS-Project 01	DUR	S	02/15/14	03/08/14	02/17/14	2	B
	SUB-13-00012-DUR-073-A	Concrete Wall from Sta.0+407 to Sta.0+421 RHS, from Sta.0+444 to Sta.0+474 RHS and from Sta.0+447 to Sta.0+472 LHS-Project 01	DUR	S	01/20/14	02/10/14	01/29/14	9	C
	SUB-13-00012-DUR-073-B	Retaining Wall from Sta.0+444 to Sta.0+474 RHS-Project 01	DUR	S	02/02/14	02/23/14	02/12/14	10	C
	SUB-13-00012-DUR-073-C	Retaining Wall from Sta.0+444 to Sta.0+474 RHS-Project 01	DUR	S	02/15/14	03/08/14	02/17/14	2	B
	SUB-13-00012-DUR-074-A	Welding Procedure for 3"-12"	DUR	P	01/23/14	02/13/14	01/26/14	3	C
	SUB-13-00012-DUR-074-B	Welding Procedure for 3"-12"	DUR	P	03/16/14	04/06/14	03/20/14	4	B
	SUB-13-00012-DUR-075-A	Base course source approval test_ DUR mobile crusher_ Project 01_ item 2.02	DUR	M	01/23/14	02/13/14	01/28/14	5	B
	SUB-13-00012-BTH-076-A	Concrete JMD alternative source_ Al Ettihad Co_ Project 03_ item 4.07.b	BTH	M	01/23/14	02/13/14	01/28/14	5	B
	SUB-13-00012-SAM-077-A	Shop Drawings: Stone Wall from Sta.A0+000 to Sta.0+060 LHS & from Sta.0+040 to Sta.0+074 RHS -Segment A-Project 02	SAM	S	01/25/14	02/15/14	02/06/14	12	B
	SUB-13-00012-DUR-078-A	Third party testing lab -Arc-Eyes -Project 01	DUR	P	01/27/14	02/17/14	01/30/14	3	B
	SUB-13-00012-MRSII-079-A	Public Relation Plan	MRSII	P	01/27/14	02/17/14	01/30/14	3	E
	SUB-13-00012-MRSII-080-A	Branding Plan -Approved Flyers (Arabic & English ) & Radio Advertisement	MRSII	P	01/30/14	02/20/14	02/03/14	4	E
	SUB-13-00012-DUR-081-A	Bedding material (Agg. Sumsom) for pipeline- item 4.22-Project 01	DUR	M	02/02/14	02/23/14	02/10/14	8	B
	SUB-13-00012-DUR-082-A	Elecometer 266 Holiday detector	DUR	M	02/03/14	02/24/14	02/04/14	1	B
	SUB-13-00012-DUR-083-A	Drainage RC Manholes- PCP-Item 4.03- Project 01	DUR	M	02/03/14	02/24/14	02/11/14	8	C
	SUB-13-00012-DUR-083-B	Drainage RC Manholes- PCP-Item 4.03- Project 01	DUR	M	02/20/14	03/13/14	02/27/14	7	B
	SUB-13-00012-DUR-084-A	Shop Drawings : Septic Tank at Sta. 0+070 -Project 01	DUR	S	02/03/14	02/24/14	02/10/14	7	E
	SUB-13-00012-DUR-085-A	Precast catch basin-PCP- item 4.06.a-Project 01	DUR	M	02/05/14	02/26/14	02/11/14	6	B
	SUB-13-00012-DUR-086-A	Cast Iron Cover & curb for catch basin- item 4.06.a-Project 01	DUR	M	02/05/14	02/26/14	02/16/14	11	C

USAID WEST BANK/ GAZA  
**INFRASTRUCTURE NEEDS PROGRAM INPII**  
**CONTRACT NO. AID-294-I-00-12-00005**  
**TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )**  
**Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-086-B	Cast Iron Cover & curb for catch basin- item 4.06.a-Project 01	DUR	M	03/30/14	04/20/14	04/20/14	21	C
	SUB-13-00012-DUR-086-C	Cast Iron Cover & curb for catch basin_Kurdieh and Sons LTD- item 4.06.a-Project 01	DUR	M	05/28/14	06/18/14	06/08/14	11	A
	SUB-13-00012-DUR-087-A	Certified Welding Inspector	DUR	P	02/05/14	02/26/14	02/10/14	5	A
	SUB-13-00012-DUR-088-A	Proposed Welders for Welders Qualification Test - CV-Ahmad Gatasha	DUR	P	02/05/14	02/26/14	02/06/14	1	B
	SUB-13-00012-MRSII-089-A	Field Offices Furniture and Equipment Plan Amendment No.02(For Submittal No.: SUB-13-00012-MRSII-007-B)	MRSII	P	02/05/14	02/26/14	02/11/14	6	B
	SUB-13-00012-DUR-090-A	Shop Drawings: Storm Water Manhole from Manhole MH03 Running Toward the Outfall : Plan and Profile from Sta.0+000 to Sta.0+255 -Dura Hebron Sinjir Road -Project 01	DUR	S	02/05/14	02/26/14	02/18/14	13	B
	SUB-13-00012-DUR-090-B	Shop Drawings: Storm Water Manhole from Manhole MH03 Running Toward the Outfall : Plan and Profile from Sta.0+000 to Sta.0+273 -Dura Hebron Sinjir Road -Project 01-For Engineering Record	DUR	S	08/11/14	09/01/14	08/17/14	6	B
	SUB-13-00012-SAM-091-A	Shop Drawings: Concrete Gravity Wall from Sta.A0+040 to Sta.A0+074 RHS-Segment A-Project 02	SAM	S	02/09/14	03/02/14	02/19/14	10	B
	SUB-13-00012-DUR-092-A	Single size backfilling material- item 4.22-Project 01	DUR	M	02/10/14	03/03/14	02/11/14	1	A
	SUB-13-00012-DUR-093-A	UPVC pipes_replacing item 4.02.a-Project 01	DUR	M	02/10/14	03/03/14	02/16/14	6	A
	SUB-13-00012-DUR-094-A	Gate valve 2,4 & 6 inch_Raphael_item 4.24 -Project 01	DUR	M	02/10/14	03/03/14	02/16/14	6	B
	SUB-13-00012-DUR-095-A	Dismantling joints 2,4&6inch_UNIJOINT_item 4.24 -Project 01	DUR	M	02/10/14	03/03/14	02/16/14	6	B
	SUB-13-00012-SAM-096-A	Selected fill material- item No. 1.02.a -Project 02	SAM	M	02/11/14	03/04/14	02/18/14	7	A
	SUB-13-00012-SAM-097-A	Topping material-item No.1.02.b -Project 02	SAM	M	02/11/14	03/04/14	02/18/14	7	A
	SUB-13-00012-DUR-098-A	Shop Drawings: Concrete Gravity Wall from Sta.0+732 to Sta.0+755 RHS and from Sta.0+779 to Sta.0+825 RHS-Project 01	DUR	S	02/11/14	03/04/14	02/17/14	6	C
	SUB-13-00012-DUR-098-B	Shop Drawings: Concrete Gravity Wall from Sta.0+732 to Sta.0+755 RHS and from Sta.0+779 to Sta.0+800 RHS-Project 01	DUR	S	02/20/14	03/13/14	03/03/14	11	B
	SUB-13-00012-DUR-099-A	Shop Drawings: Plan ,Profile and Cross Section from Sta.0+500 to Sta.1+500 -Project 01	DUR	S	02/12/14	03/05/14	02/17/14	5	C
	SUB-13-00012-DUR-099-B	Shop Drawings: Plan ,Profile and Cross Section from Sta.0+500 to Sta.1+500 -Project 01	DUR	S	02/24/14	03/17/14	02/25/14	1	B
	SUB-13-00012-DUR-099-C	Shop Drawings: Plan ,Profile and Cross Section from Sta.0+500 to Sta.1+500 -Project 01- <b>For Engineering Record</b>	DUR	S	07/17/14	08/07/14	07/27/14	10	B
	SUB-13-00012-DUR-099-D	Shop Drawings: Plan ,Profile and Cross Section from Sta.0+500 to Sta.1+500 -Project 01- <b>For Engineering Record</b>	DUR	S	09/08/14	09/29/14	09/17/14	9	B
	SUB-13-00012-DUR-100-A	Water steel flanges_item 4.24-Project 01	DUR	M	02/13/14	03/06/14	02/18/14	5	A
	SUB-13-00012-DUR-101-A	Shop Drawings: Lighting Details from Sta.0+000 to Sta.1+500-Project 01	DUR	S	02/13/14	03/06/14	02/26/14	13	C
	SUB-13-00012-DUR-101-B	Shop Drawings: Steel Lighting Poles Details from Sta.0+000 to Sta.1+500-Project 01	DUR	S	03/03/14	03/24/14	03/11/14	8	B
	SUB-13-00012-DUR-102-A	Shop Drawings : Retaining Wall from Sta.0+447 to Sta.0+472 LHS-Project 01	DUR	S	02/13/14	03/06/14	02/26/14	13	B

USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-103-A	Shop Drawings : Retaining Wall from Sta.1+108 to Sta.1+129 RHS-Project 01	DUR	S	02/15/14	03/08/14	03/03/14	16	B
	SUB-13-00012-DUR-103-B	Shop Drawings : Boundary Wall from Sta.1+108 to Sta.1+129 RHS-Project 01	DUR	S	03/17/14	04/07/14	03/19/14	2	B
	SUB-13-00012-SAM-104-A	Base course source approval test_ Rasheed crusher_ item2.02.a- Project 02	SAM	M	02/16/14	03/09/14	02/18/14	2	B
	SUB-13-00012-SAM-105-A	Shop Drawing- Stone Wall from St. A0+099 to St. A0+131 RHS	SAM	S	02/17/14	03/10/14	02/18/14	1	B
	SUB-13-00012-DUR-106-A	Galvanized Malleable Iron Fittings up to 2"- Modgal	DUR	M	02/18/14	03/11/14	02/19/14	1	B
	SUB-13-00012-SAM-107-A	Shop Drawing- Stone Wall from St. A0+282 to St. A0+383 RHS ,from St.A0+220 to St.A0+255 LHS and from St.A0+264 to St.A0+357 LHS -Project 02	SAM	S	02/18/14	03/11/14	02/27/14	9	B
	SUB-13-00012-DUR-108-A	Drainage RC Manholes_ Addasi Co.-item 4.03- Project 01	DUR	M	02/20/14	03/13/14	03/04/14	12	B
	SUB-13-00012-DUR-109-A	3 inch Procedure Qualification Record (PQR)	DUR	P	02/20/14	03/13/14	02/25/14	5	B
	SUB-13-00012-BTH-110-A	Shop Drawings : Plan Road Marking from Sta.1+900 to Sta.3+030 -Hebron Jerusalem Road Segment A- Project 03	BTH	S	02/23/14	03/16/14	02/26/14	3	B
	SUB-13-00012-BTH-111-A	Asphalt Basalt Mix Design _item No.3.03.b-Project 03	BTH	M	02/24/14	03/17/14	03/04/14	8	B
	SUB-13-00012-DUR-112-A	Shop Drawings: Retaining Wall from Sta.0+096 to Sta.0+110 RHS-Project 01	DUR	S	02/27/14	03/20/14	03/09/14	10	E
	SUB-13-00012-SAM-113-A	Shop Drawings : Pipe Culvert at Sta.0+278.5 -Segment A-Project 02	SAM	S	03/18/14	04/08/14	03/18/14	0	B
	SUB-13-00012-SAM-114-A	Shop Drawings: Stone Wall from Sta.A0+379 to Sta.0+635 LHS , from Sta.A0+389 to Sta.A 0+562 RHS and from Sta.A0+606 to Sta.A0+621 RHS - Segment A-Project 02	SAM	S	03/02/14	03/23/14	03/05/14	3	B
	SUB-13-00012-SAM-115-A	Shop Drawings: Stone Wall from Sta.0+778 to Sta.0+836 RHS -Segment A-Project 02	SAM	S	03/02/14	03/23/14	03/05/14	3	B
	SUB-13-00012-SAM-116-A	Shop Drawings: Stone Wall from Sta.A0+768 to Sta.A0+825 LHS -Segment A-Project 02	SAM	S	03/03/14	03/24/14	03/11/14	8	B
	SUB-13-00012-SAM-116-B	Shop Drawings: Stone Wall from Sta.A0+768 to Sta.A0+825 LHS -Segment A-Project 02- <b>For Engineering Record</b>	SAM	S	07/24/14	08/14/14	08/12/14	19	B
	SUB-13-00012-SAM-117-A	Shop Drawings: Stone Wall from Sta.A0+750 to Sta.A0+765 LHS and from Sta.A0+750 to Sta.A0+773 RHS -Segment A- Project 02	SAM	S	03/03/14	03/24/14	03/11/14	8	B
	SUB-13-00012-SAM-118-A	Shop Drawings: Plan ,Profile and Cross Section from Sta.1+300 to Sta.2+100 - Segment A-Project 02	SAM	S	03/03/14	03/24/14	03/12/14	9	B
	SUB-13-00012-SAM-119-A	Shop Drawings: Retaining Wall from Sta.A0+265 to Sta.A 0+284 LHS-Project 02	SAM	S	03/18/14	04/08/14	03/19/14	1	B
	SUB-13-00012-MRSII-120-A	Updated Construction Schedule	MRSII	SCH	03/04/14	03/25/14	03/17/14	13	C
	SUB-13-00012-MRSII-120-B	Updated Construction Schedule -February,2014	MRSII	SCH	03/26/14	04/16/14	04/06/14	11	B
	SUB-13-00012-BTH-121-A	Shop Drawing: Boundary Walls from Sta.0+000 to Sta.0+043 RHS and from Sta.0+043 to Sta.0+052 LHS-Project 03	BTH	S	03/06/14	03/27/14	03/11/14	5	B
	SUB-13-00012-SAM-122-A	Shop Drawings: Stone Wall from Sta.A0+843 to Sta.A 0+916 LHS-Project 02	SAM	S	03/06/14	03/27/14	03/12/14	6	B

USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-BTH-123-A	Shop Drawing: Retaining Wall from Sta.0+010 to Sta.0+017 LHS -Project 03	BTH	S	03/08/14	03/29/14	03/11/14	3	B
	SUB-13-00012-BTH-124-A	Shop Drawings : Plan ,Profile and Cross Section from Sta.0+040 to Sta.0+140 - Wadi Ma'ali Road Segment B-Project 03	BTH	S	03/10/14	03/31/14	03/12/14	2	B
	SUB-13-00012-DUR-125-A	Topping material_ TGC crusher -Project 01	DUR	M	03/10/14	03/31/14	03/11/14	1	A
	SUB-13-00012-BTH-126-A	Shop Drawings: Plan, Profile and Cross Section from Sta.0+000 to Sta.0+195- Al Qata Road -Project 03	BTH	S	03/18/14	04/08/14	03/18/14	0	B
	SUB-13-00012-BTH-127-A	Interlocking Block_ AL Sos Global Co_ _ item 4.13.a (alternative source)-Project 03	BTH	M	03/11/14	04/01/14	03/18/14	7	B
	SUB-13-00012-DUR-128-A	Street Lighting material_ item 5.08-Project 01	DUR	M	03/11/14	04/01/14	03/17/14	6	C
	SUB-13-00012-DUR-128-B	Street Lighting material_ item 5.08-Project 01	DUR	M	04/03/14	04/24/14	04/13/14	10	B
	SUB-13-00012-SAM-129-A	Shop Drawings: Stone Walls from Sta.A0+922 to Sta.A0+960 LHS and from Sta.A0+910 to Sta.A0+997 RHS-Project 02	SAM	S	03/11/14	04/01/14	03/18/14	7	B
	SUB-13-00012-BTH-130-A	Curbstone_ Al Sos Global Co_ _ item 4.12 (alternative source)-Project 03	BTH	M	03/11/14	04/01/14	03/17/14	6	B
	SUB-13-00012-DUR-131-A	Shop Drawings: Boundary Wall from Sta.0+189 to Sta.0+210 RHS-Project 01	DUR	S	03/12/14	04/02/14	03/18/14	6	B
	SUB-13-00012-SAM-132-A	Shop Drawings: Concrete gravity Wall from Sta.A1+206 to Sta.A1+247-Project 02	SAM	S	03/13/14	04/03/14	03/18/14	5	B
	SUB-13-00012-DUR-133-A	Shop Drawings: Storm Water - Plan and Profile from Sta.0+300 to Sta.0+870 - Dura Hebron Sinjir Road -Project 01	DUR	S	03/16/14	04/06/14	03/24/14	8	C
	SUB-13-00012-DUR-133-B	Shop Drawings: Storm Water - Plan and Profile from Sta.0+300 to Sta.0+870 - Dura Hebron Sinjir Road -Project 01	DUR	S	03/25/14	04/15/14	03/31/14	6	B
	SUB-13-00012-BTH-134-A	Shop Drawings: Road Marking and Traffic sign -Philips,Al Shepherd and Al Dibis Road- Segment B-Project 03	BTH	S	03/17/14	04/07/14	03/20/14	3	C
	SUB-13-00012-BTH-134-B	Shop Drawings: Road Marking and Traffic sign -Philips,Al Shepherd and Al Dibis Road- Segment B-Project 03	BTH	S	03/27/14	04/17/14	03/31/14	4	B
	SUB-13-00012-DUR-135-A	Shop Drawings: Water-Plan profile and typical section from Sta.0+530 to Sta.1+600-Project 01	DUR	S	03/17/14	04/07/14	04/06/14	20	B
	SUB-13-00012-SAM-136-A	Shop Drawings: Stone Walls from Sta.A0+995 to Sta.A1+030 LHS and from Sta.A1+000.50 to Sta.A1+027 RHS-Project 02	SAM	S	03/17/14	04/07/14	03/27/14	10	E
	SUB-13-00012-SAM-137-A	Shop Drawings: Plan , Profile and Cross Section from Sta.2+100 to Sta.3+000 - Segment A-Project 02	SAM	S	03/23/14	04/13/14	03/31/14	8	B
	SUB-13-00012-SAM-137-B	Shop Drawings: Plan , Profile and Cross Section from Sta.2+100 to Sta.3+000 - after raising PGL from Sta. 2+610 TO 2+790-Segment A-Project 02	SAM	S	05/25/14	06/15/14	06/03/14	9	B
	SUB-13-00012-SAM-137-C	Shop Drawings: Plan , Profile and Cross Section from Sta.2+100 to Sta.3+000 - after raising PGL from Sta. 2+575 TO 2+825-Segment A-Project 02- <b>For Engineering Record</b>	SAM	S	07/17/14	08/07/14	07/22/14	5	B
	SUB-13-00012-BTH-138-A	Asphalt Crack sealing material & Work method statement_ item 3.07.c-Project 03	BTH	M	03/19/14	04/09/14	03/25/14	6	B
	SUB-13-00012-DUR-139-A	Shop Drawing: Manhole #03 at Sta.0+306.7 for Storm System	DUR	S	03/23/14	04/13/14	03/31/14	8	C

USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-139-B	Shop Drawing: Manhole #03 at Sta.0+306.7 for Storm System	DUR	S	03/19/15	04/09/15	03/19/15	0	B
	SUB-13-00012-SAM-140-A	Survey Plan for Segment B from STA. 0+000 to STA. 0+400	SAM	P	03/23/14	04/13/14	04/06/14	14	B
	SUB-13-00012-MRSII-141-A	Reinforcement steel source approval_ BOQ item No.4.07.c	MRSII	M	03/24/14	04/14/14	04/06/14	13	B
	SUB-13-00012-BTH-142-A	Steel Handrail	BTH	M	03/24/14	04/14/14	03/25/14	1	A
	SUB-13-00012-SAM-143-A	Shop Drawings: Plan , Profile and Cross Section from Sta.0+000 to Sta.0+400 - Segment B-Project 02	SAM	S	03/24/14	04/14/14	04/06/14	13	C
	SUB-13-00012-SAM-143-B	Shop Drawings: Plan , Profile and Cross Section from Sta.0+000 to Sta.0+400 - Segment B-Project 02	SAM	S	04/13/14	05/04/14	04/22/14	9	B
	SUB-13-00012-DUR-144-A	Shop Drawing: Structural and Mechanical Detail for valve chambers for water pipeline (Chambers No. 01 to 08)	DUR	S	03/24/14	04/14/14	04/14/14	21	C
	SUB-13-00012-DUR-144-B	Shop Drawing: Structural and Mechanical Detail for valve chambers for water pipeline (Chambers No. 01 to 08)	DUR	S	04/20/14	05/11/14	05/01/14	11	B
	SUB-13-00012-DUR-144-C	Shop Drawing: Structural and Mechanical Detail for valve chambers for water pipeline (Chambers No. 01 to 08)- <b>For Engineering Record</b>	DUR	S	05/27/14	06/17/14	06/08/14	12	B
	SUB-13-00012-DUR-145-A	3/4" Diameter Pipes Data Sheet - Future Iron Pipe (FIP)- Project 01	DUR	M	03/24/14	04/14/14	03/31/14	7	B
	SUB-13-00012-SAM-146-A	Base course alternative source approval test _Susiya crusher-Project 02	SAM	M	03/25/14	04/15/14	04/03/14	9	B
	SUB-13-00012-SAM-147-A	Shop Drawing: Double pipe culvert at Sta.0+771 -Project 02	SAM	S	03/25/14	04/15/14	04/14/14	20	B
	SUB-13-00012-MRSII-148-A	Bitumen Protective Coating Material for Concrete Surface in Contact with Soil-Nitoproof 15	MRSII	M	03/27/14	04/17/14	04/16/14	20	B
	SUB-13-00012-SAM-149-A	Shop Drawings: Plan ,Profile and Cross Section from Sta.0+600 to Sta.0+860 - as per Site Memo No. SM-13-00012-SAM-E-C-030-(Amendment to Submittals: SUB-13-00012-SAM-020-C and SUB-13-00012-SAM-037-B)	SAM	S	03/27/14	04/17/14	04/09/14	13	B
	SUB-13-00012-BTH-150-A	Shop Drawings : Road Marking and Traffic Signs-Beit Sahour Intersection, Al Karkafa ,PWA and Al Atan Road -Project 03	BTH	S	03/27/14	04/17/14	04/06/14	10	B
	SUB-13-00012-DUR-151-A	Alternative source Holiot UPVC pipes_ replacing item 4.02.a-Project 01	DUR	M	03/30/14	04/20/14	04/09/14	10	B
	SUB-13-00012-SAM-152-A	Shop Drawings: Plan, Profile and Cross Section from Sta.1+050 to Sta.1+350 - Segment A-Project 02	SAM	S	03/31/14	04/21/14	04/09/14	9	B
	SUB-13-00012-SAM-153-A	UPVC pipes_ Royal_ 6inch for future ducts-Project 02	SAM	M	04/03/14	04/24/14	04/07/14	4	A
	SUB-13-00012-DUR-154-A	Shop Drawings: Side walk from Sta.0+000 to Sta.0+550-Project 01	DUR	S	04/06/14	04/27/14	04/10/14	4	B
	SUB-13-00012-DUR-155-A	Shop Drawings: Boundary Wall from Sta.0+815 to Sta.0+825 RHS-Project 01	DUR	S	04/07/14	04/28/14	04/14/14	7	B
	SUB-13-00012-MRSII-156-A	Updated Construction Schedule and S-curve -March 2014	MRSII	SCH	04/07/14	04/28/14	04/21/14	14	C
	SUB-13-00012-MRSII-156-B	Updated Construction Schedule and S-curve -March 2014	MRSII	SCH	04/28/14	05/19/14	04/30/14	2	B
	SUB-13-00012-MRSII-157-A	Concrete repair material	MRSII	M	04/08/14	04/29/14	04/24/14	16	B
	SUB-13-00012-DUR-158-A	Shop Drawings: Side walk from Sta.0+550 to Sta.1+500-Project 01	DUR	S	04/08/14	04/29/14	04/15/14	7	C

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-158-B	Shop Drawings: Side walk from Sta.0+550 to Sta.1+500-Project 01	DUR	S	04/17/14	05/08/14	04/28/14	11	B
	SUB-13-00012-DUR-159-A	Curbstone_ Al Sos Global Co_ item 4.12 (alternative source)-Project 01	DUR	M	04/10/14	05/01/14	04/14/14	4	B
	SUB-13-00012-BTH-160-A	Shop Drawings: Road Marking and Traffic sign -Wadi Ma'ali Road, Wadi Shaheen Road and Al Qata'a Road -Project 03	BTH	S	04/13/14	05/04/14	04/22/14	9	B
	SUB-13-00012-SAM-161-A	Shop Drawings : Stone Wall from Sta.A1+588 to Sta.A1+666 LHS -Project 02	SAM	S	04/15/14	05/06/14	04/17/14	2	B
	SUB-13-00012-SAM-162-A	Shop Drawings : Stone Wall from Sta.A1+446 to Sta.A1+458 LHS -Project 02	SAM	S	04/15/14	05/06/14	04/17/14	2	E
	SUB-13-00012-SAM-163-A	Shop Drawings : Stone Wall from Sta.A1+848 to Sta.A1+867 LHS and from Sta.1+880 to Sta.1+909 RHS -Project 02	SAM	S	04/17/14	05/08/14	04/22/14	5	B
	SUB-13-00012-DUR-164-A	Asphalt Binder JMD 3/4" -item No. 3.05.b -Project 01	DUR	M	04/17/14	05/08/14	04/21/14	4	B
	SUB-13-00012-DUR-165-A	Shop Drawings : Plan ,Profile and Cross Section from Sta.1+500 to Sta.2+040.27 -Project 01	DUR	S	04/17/14	05/08/14	04/27/14	10	B
	SUB-13-00012-DUR-165-B	Shop Drawings : Plan ,Profile and Cross Section from Sta.1+500 to Sta.2+040.27 -Project 01-For Engineering Record	DUR	S	07/13/14	08/03/14	07/22/14	9	B
	SUB-13-00012-DUR-166-A	Shop Drawings : Concrete Gravity Wall from Sta.1+694 to Sta.1+753 LHS -Project 01	DUR	S	04/20/14	05/11/14	04/28/14	8	D
	SUB-13-00012-DUR-166-B	Shop Drawings : Concrete Gravity Wall from Sta.1+694 to Sta.1+753 LHS -Project 01	DUR	S	07/08/14	07/29/14	07/15/14	7	E
	SUB-13-00012-DUR-166-C	Shop Drawings : Concrete Gravity Wall from Sta.1+694 to Sta.1+755 LHS -Project 01	DUR	S	12/15/14	01/05/15	12/21/14	6	D
	SUB-13-00012-DUR-166-D	Shop Drawings : Concrete Gravity Wall from Sta.1+694 to Sta.1+755 LHS -Project 01	DUR	S	12/30/14	01/20/15	01/06/15	7	A
	SUB-13-00012-DUR-167-A	Shop Drawings : Concrete Gravity Wall from Sta.1+557 to Sta.1+600 LHS -Project 01	DUR	S	04/20/14	05/11/14	04/28/14	8	D
	SUB-13-00012-DUR-167-B	Shop Drawings : Retaining Wall from Sta.1+557 to Sta.1+600 LHS- Project 01	DUR	S	05/04/14	05/25/14	05/10/14	6	B
	SUB-13-00012-DUR-167-C	Shop Drawings : Retaining Wall from Sta.1+557 to Sta.1+600 LHS- Project 01-For Engineering Record	DUR	S	06/16/14	07/07/14	06/18/14	2	A
	SUB-13-00012-SAM-168-A	Shop Drawing: 4" Water Pipeline Plan, Profile &Typical Section From Sta.-0+020 To Sta.0+650 (SEG.A)-Project 02	SAM	S	04/20/14	05/11/14	04/22/14	2	B
	SUB-13-00012-BTH-169-A	Proposed Project permanent Sign location -Project 03	BTH	P	04/20/14	05/11/14	04/22/14	2	B
	SUB-13-00012-SAM-170-A	Shop Drawings: Plan, Profile and Cross Section from Sta.3+000 to Sta.4+120 -Segment A -Project 02	SAM	S	04/22/14	05/13/14	05/06/14	14	B
	SUB-13-00012-SAM-170-B	Shop Drawings: Plan, Profile and Cross Section from Sta.3+000 to Sta.4+120 -Segment A -Project 02-For Engineering Record	SAM	S	06/02/14	06/23/14	06/15/14	13	B
	SUB-13-00012-DUR-171-A	Shop Drawings: Plan , Profile and Cross Section from Sta.2+030 to Sta.2+600 -Project 01	DUR	S	04/26/14	05/17/14	05/14/14	18	B
	SUB-13-00012-DUR-171-B	Shop Drawings: Plan , Profile and Cross Section from Sta.2+030 to Sta.2+600 -Project 01 -For Engineering Record	DUR	S	07/10/14	07/31/14	07/23/14	13	B

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-SAM-172-A	Shop Drawings : Stone Wall from Sta.A1+964 to Sta.A1+976 LHS and from Sta.1+946 to Sta.1+986 RHS -Project 02	SAM	S	04/27/14	05/18/14	05/06/14	9	B
	SUB-13-00012-DUR-173-A	Check valve NR-040-PN 16_item 4.24-Project 01	DUR	M	04/28/14	05/19/14	05/06/14	8	B
	SUB-13-00012-DUR-174-A	Shop Drawings: Plan , Profile for Intersection at Sta.0+320 RHS -Project 01	DUR	S	05/14/14	06/04/14	05/19/14	5	B
	SUB-13-00012-DUR-175-A	Shop Drawings: Boundary Wall from Sta.0+388 to Sta.0+398 RHS-Project 01	DUR	S	04/30/14	05/21/14	05/06/14	6	B
	SUB-13-00012-DUR-176-A	Shop Drawings: Boundary Wall from Sta.0+033 to Sta.0+040.5 RHS-Project 01	DUR	S	04/30/14	05/21/14	05/06/14	6	B
	SUB-13-00012-DUR-176-B	Shop Drawings: Boundary Wall from Sta.0+033 to Sta.0+040.5 RHS-Project 01-For Engineering Record	DUR	S	07/17/14	08/07/14	07/22/14	5	B
	SUB-13-00012-DUR-177-A	Shop Drawings : Concrete Gravity Wall from Sta.0+955 to Sta.0+990 RHS -Project 01	DUR	S	04/30/14	05/21/14	05/08/14	8	B
	SUB-13-00012-DUR-177-B	Shop Drawings : Concrete Gravity Wall from Sta.0+955 to Sta.0+990 RHS -Project 01-For Engineering Record	DUR	S	07/17/14	08/07/14	07/22/14	5	B
	SUB-13-00012-DUR-178-A	Shop Drawings : Concrete Gravity Wall from Sta.0+800 to Sta.0+813.5 RHS -Project 01	DUR	S	04/30/14	05/21/14	05/08/14	8	B
	SUB-13-00012-DUR-178-B	Shop Drawings : Concrete Gravity Wall from Sta.0+800 to Sta.0+813.5 RHS -Project 01-For Engineering Record	DUR	S	05/14/14	06/04/14	05/22/14	8	B
	SUB-13-00012-SAM-179-A	Shop Drawings : Stone Wall from Sta.A2+217 to Sta.A2+352 RHS -Project 02	SAM	S	05/06/14	05/27/14	05/12/14	6	B
	SUB-13-00012-SAM-180-A	Shop Drawings: Pipe Culvert at Sta.1+650 and Stone Wall from Sta.1+654 to Sta.1+666 LHS -Project 02	SAM	S	05/06/14	05/27/14	05/17/14	11	B
	SUB-13-00012-SAM-181-A	Shop Drawings : Stone Wall from Sta.A2+172 to Sta.A2+189 LHS and from Sta.2+245 to Sta.2+287 LHS -Project 02	SAM	S	05/07/14	05/28/14	05/12/14	5	E
	SUB-13-00012-DUR-182-A	Shop Drawings : Stone Wall from Sta.0+250 to Sta.0+275 RHS -Project 01	DUR	S	05/07/14	05/28/14	05/12/14	5	B
	SUB-13-00012-MRSII-183-A	Revised Construction Schedule and S-curve (April 30 ,2014 )	MRSII	SCH	05/07/14	05/28/14	05/20/14	13	C
	SUB-13-00012-MRSII-183-B	Revised Construction Schedule and S-curve (May 06 ,2014 )	MRSII	SCH	06/05/14	06/26/14	06/18/14	13	C
	SUB-13-00012-MRSII-183-C	Revised Construction Schedule and S-curve (May 06 ,2014 )	MRSII	SCH	06/23/14	07/14/14	07/06/14	13	B
	SUB-13-00012-MRSII-183-D	Revised Construction Schedule and S-curve (May 06 ,2014 ) -For Engineering Record	MRSII	SCH	07/13/14	08/03/14	07/20/14	7	E
	SUB-13-00012-SAM-184-A	Shop Drawings: Pipe Culvert at Sta.2+202.36 -Project 02	SAM	S	05/07/14	05/28/14	05/17/14	10	B
	SUB-13-00012-SAM-185-A	Shop Drawings: Pipe Culvert at Sta.2+690 -Project 02	SAM	S	05/08/14	05/29/14	05/17/14	9	B
	SUB-13-00012-DUR-186-A	Shop Drawings: Water :Plan , Profile and Typical Sections from Sta.1+600 to Sta.2+600 -Project 01	DUR	S	05/08/14	05/29/14	05/22/14	14	B
	SUB-13-00012-DUR-187-A	Shop Drawings: Side walk from Sta.1+500 to Sta.2+000-Project 01	DUR	S	05/11/14	06/01/14	05/26/14	15	B

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-SAM-188-A	Shop Drawings : Stone Wall from Sta.A2+620 to Sta.A2+637 RHS ,from Sta.A2+847 to Sta.A2+860 LHS and from Sta.2+841 to Sta.2+870 RHS - Project 02	SAM	S	05/14/14	06/04/14	05/21/14	7	B
	SUB-13-00012-DUR-189-A	Shop Drawings: Concrete Gravity Wall from Sta.0+077.5 to Sta.0+020 LHS - Project 01	DUR	S	05/14/14	06/04/14	05/21/14	7	B
	SUB-13-00012-SAM-190-A	Shop Drawings : Stone Wall from Sta.A2+886 to Sta.A2+950 LHS ,from Sta.A2+968 to Sta.A3+012 RHS and from Sta.2+887 to Sta.2+895 RHS - Project 02	SAM	S	05/14/14	06/04/14	05/21/14	7	B
	SUB-13-00012-DUR-191-A	Shop Drawings: Storm Water : Plan & Profile from Sta.1+335 to Sta.1+582 - Project 01	DUR	S	05/15/14	06/05/14	05/29/14	14	B
	SUB-13-00012-SAM-192-A	Shop Drawings : Stone Wall from Sta.A0+143.5 to Sta.A0+150 RHS and from Sta.0+268 to Sta.0+281 RHS -Project 02	SAM	S	05/15/14	06/05/14	05/29/14	14	B
	SUB-13-00012-MRSII-193-A	Testing Labs-Renewed Accreditation Certificate and Schedule (For Building Center Lab )- Amendment to Submittal No. : SUB-13-00012-MRSII-004-A	MRSII	P	05/18/14	06/08/14	05/22/14	4	A
	SUB-13-00012-DUR-194-A	Shop Drawings: Stone Wall from Sta.1+694 to Sta.1+753 LHS -Project 01	DUR	S	05/19/14	06/09/14	05/26/14	7	B
	SUB-13-00012-DUR-195-A	Shop Drawings: Plan , Profile and Cross Sections for Intersection at Sta.0+520 LHS -Project 01	DUR	S	05/25/14	06/15/14	05/26/14	1	B
	SUB-13-00012-DUR-196-A	Shop Drawings: Storm Water : Plan & Profile from Sta.1+090 to Sta.1+340-Project 01	DUR	S	05/19/14	06/09/14	05/29/14	10	B
	SUB-13-00012-DUR-197-A	Shop Drawings: Concrete Gravity Wall from Sta.1+940 to Sta.1+984 RHS - Project 01	DUR	S	05/20/14	06/10/14	05/26/14	6	C
	SUB-13-00012-DUR-197-B	Shop Drawings: Concrete Gravity Wall from Sta.1+940 to Sta.1+982.5 RHS - Project 01	DUR	S	06/09/14	06/30/14	06/15/14	6	B
	SUB-13-00012-DUR-198-A	Shop Drawings: Retaining Wall from Sta.1+634 to Sta.1+677 RHS -Project 01	DUR	S	05/20/14	06/10/14	05/29/14	9	D
	SUB-13-00012-DUR-198-B	Shop Drawings: Retaining Wall from Sta.1+634 to Sta.1+677 RHS -Project 01	DUR	S	06/02/14	06/23/14	06/15/14	13	B
	SUB-13-00012-DUR-199-A	Shop Drawings: Concrete Gravity Wall from Sta.1+820 to Sta.1+875 RHS - Project 01	DUR	S	05/20/14	06/10/14	05/29/14	9	B
	SUB-13-00012-SAM-200-A	Traffic Control Plan-DCL Final Written Approval and signed plans- (Amendment for SUB-13-00012-SAM-042-B-For Engineering Record)-Phase III-Samua' Yatta Road Segment B-Project 02	SAM	P	05/21/14	06/11/14	05/28/14	7	A
	SUB-13-00012-SAM-201-A	4inch Galvanized steel pipes- Avrot-Project 02	SAM	M	05/21/14	06/11/14	05/27/14	6	B
	SUB-13-00012-DUR-202-A	Shop Drawings: Plan , Profile and Cross Section from Sta.2+600 to Sta.3+180 - Project 01	DUR	S	05/25/14	06/15/14	06/03/14	9	B
	SUB-13-00012-DUR-202-B	Shop Drawings: Plan , Profile and Cross Section from Sta.2+600 to Sta.3+180 - Project 01-For Engineering Record	DUR	S	07/13/14	08/03/14	07/27/14	14	B
	SUB-13-00012-DUR-203-A	Shop Drawings: Concrete Gravity Wall from Sta.2+230 to Sta.2+273.5 RHS and Stair at Sta.2+274 RHS -Project 01	DUR	S	05/25/14	06/15/14	06/01/14	7	C

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-I-00-12-00005  
TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-203-B	Shop Drawings: Concrete Gravity Wall from Sta.2+230 to Sta.2+273.5 RHS and Stair at Sta.2+274 RHS -Project 01	DUR	S	06/08/14	06/29/14	06/15/14	7	B
	SUB-13-00012-DUR-204-A	Shop Drawings: Concrete Gravity Wall from Sta.2+307 to Sta.2+344 RHS and from Sta.2+360 to Sta.2+390 RHS -Project 01	DUR	S	05/26/14	06/16/14	06/03/14	8	E
	SUB-13-00012-DUR-205-A	Shop Drawings: Concrete Gravity Wall from Sta.2+390 to Sta.2+410 RHS - Project 01	DUR	S	05/26/14	06/16/14	06/03/14	8	B
	SUB-13-00012-DUR-205-B	Shop Drawings: Concrete Gravity Wall from Sta.2+390 to Sta.2+410 RHS - Project 01- <b>For Engineering Record</b>	DUR	S	07/22/14	08/12/14	07/27/14	5	B
	SUB-13-00012-SAM-206-A	Shop Drawings: Pipe Culvert at Sta.3+960 -Project 02	SAM	S	05/26/14	06/16/14	05/28/14	2	E
	SUB-13-00012-DUR-207-A	Shop Drawings: Side Walk from Sta.2+030 to Sta.2+600- Project 01	DUR	S	06/02/14	06/23/14	06/15/14	13	B
	SUB-13-00012-DUR-207-B	Shop Drawings: Side Walk from Sta.2+000 to Sta.2+600- Project 01-For Engineering Record	DUR	S	07/27/14	08/17/14	08/06/14	10	B
	SUB-13-00012-DUR-208-A	Shop Drawings: Retaining Wall from Sta.0+977 to Sta.0+988 LHS-Project 01	DUR	S	05/28/14	06/18/14	06/05/14	8	B
	SUB-13-00012-DUR-208-B	Shop Drawings: Retaining Wall from Sta.0+977 to Sta.0+988 LHS-Project 01-For Engineering Record	DUR	S	06/15/14	07/06/14	06/17/14	2	B
	SUB-13-00012-DUR-209-A	Shop Drawings: Roundabout at Sta.0+000 & From Sta 0+000 to sta.0+070 - Project 01	DUR	S	05/29/14	06/19/14	06/05/14	7	B
	SUB-13-00012-DUR-210-A	Shop Drawings: Concrete Wall from Sta.0+990 to Sta. 0+1010 RHS -Project 01	DUR	S	05/29/14	06/19/14	06/05/14	7	B
	SUB-13-00012-BTH-211-A	As Built Drawings: Plan, Road Marking Plan and Details for Milling and Overlay of Bethlehem Internal Roads- Project 03	BTH	S	05/29/14	06/19/14	06/15/14	17	C
	SUB-13-00012-BTH-211-B	As Built Drawings: Milling and Overlay of Bethlehem Internal Roads- -Plan, Road Marking Plane and Details -Project 03	BTH	S	06/19/14	07/10/14	07/09/14	20	C
	SUB-13-00012-BTH-211-C	As Built Drawings: Milling and Overlay of Bethlehem Internal Roads- -Plan, Road Marking Plane and Details -Project 03	BTH	S	08/19/14	09/09/14	09/09/14	21	A
	SUB-13-00012-DUR-212-A	Shop Drawings: Plan , Profile and Cross Section from Sta.3+180 to Sta.4+040 - Project 01	DUR	S	06/02/14	06/23/14	06/22/14	20	C
	SUB-13-00012-DUR-212-B	Shop Drawings: Plan , Profile and Cross Section from Sta.3+180 to Sta.3+750 - Project 01	DUR	S	08/18/14	09/08/14	09/04/14	17	C
	SUB-13-00012-DUR-212-C	Shop Drawings: Plan , Profile and Cross Section from Sta.3+180 to Sta.3+750 - Project 01	DUR	S	09/11/14	10/02/14	09/18/14	7	B
	SUB-13-00012-DUR-213-A	Shop Drawings: Concrete Gravity Wall from Sta.2+773 to Sta.2+838 RHS - Project 01	DUR	S	06/05/14	06/26/14	06/19/14	14	B
	SUB-13-00012-DUR-213-B	Shop Drawings: Concrete Gravity Wall from Sta.2+825 to Sta.2+835 RHS - Project 01- As per CMC comments on Submittal No.: SUB-13-00012-DUR-213-A	DUR	S	09/14/14	10/05/14	09/18/14	4	B
	SUB-13-00012-DUR-214-A	Shop Drawings: Concrete Gravity Wall from Sta.2+625 to Sta.2+665 RHS - Project 01	DUR	S	06/05/14	06/26/14	06/19/14	14	B
	SUB-13-00012-DUR-215-A	Shop Drawings: Stone Wall from Sta.0+070 to Sta.0+103 RHS for Roundabout at Sta.0+000-Project 01	DUR	S	06/08/14	06/29/14	06/15/14	7	B

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-I-00-12-00005  
TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-216-A	Shop Drawings: Water :Plan , Profile and Typical Sections from Sta.2+600 to Sta.3+200 -Project 01	DUR	S	06/08/14	06/29/14	06/15/14	7	B
	SUB-13-00012-SAM-217-A	Shop Drawings: Stone Boulder from Sta.A3+295 to Sta.3+332 RHS-Project 02	SAM	S	06/09/14	06/30/14	06/15/14	6	B
	SUB-13-00012-SAM-218-A	Shop Drawings: Plan , Profile and Cross Section from Sta.0+100 to Sta.0+300 for Parking Area -Segment A-Project 02	SAM	S	06/09/14	06/30/14	06/16/14	7	B
	SUB-13-00012-SAM-219-A	Shop Drawings : Plan , Profile and Cross Sections for Simple Access at Sta. 0+140 RHS-Segment A-Project 02	SAM	S	06/09/14	06/30/14	06/18/14	9	B
	SUB-13-00012-SAM-220-A	Shop Drawings : Plan , Profile and Cross Sections for Simple Access at Sta. 0+270 RHS-Segment A-Project 02	SAM	S	06/09/14	06/30/14	06/18/14	9	B
	SUB-13-00012-DUR-221-A	Shop Drawings: Concrete Gravity Wall from Sta.3+370 to Sta.3+432 LHS - Project 01	DUR	S	06/10/14	07/01/14	06/24/14	14	C
	SUB-13-00012-DUR-221-B	Shop Drawings: Concrete Gravity Wall from Sta.3+370 to Sta.3+432 LHS - Project 01	DUR	S	07/03/14	07/24/14	07/08/14	5	B
	SUB-13-00012-DUR-222-A	Shop Drawings: Storm Water : Plan & Profile from Sta.1+230 to Sta.1+400- Project 01 as per RFI No. RFI-13-00012-MRSII-026 -Amendment to Submittals : (SUB-13-00012-DUR-191-A & SUB-13-00012-DUR-196-A )	DUR	S	06/10/14	07/01/14	07/01/14	21	C
	SUB-13-00012-DUR-222-B	Shop Drawings: Storm Water : Plan & Profile from Sta.1+230 to Sta.1+620- Project 01 as per CMC Response to RFI-13-00012-MRSII-026 -Amendment to Submittals : (SUB-13-00012-DUR-191-A & SUB-13-00012-DUR-196-A )	DUR	S	07/08/14	07/29/14	07/16/14	8	B
	SUB-13-00012-DUR-223-A	Irrigation pipe Dia 16 mm for median landscaping -item No. 5.09.a -Project 01	DUR	M	06/12/14	07/03/14	06/26/14	14	C
	SUB-13-00012-DUR-223-B	Irrigation pipe Dia 16 mm for median landscaping -item No. 5.09.a -Project 01	DUR	M	11/10/14	12/01/14	11/20/14	10	A
	SUB-13-00012-DUR-224-A	Interlocking Block- AL SOUS Global Co- item 4.13.a -Project 01	DUR	M	06/15/14	07/06/14	06/17/14	2	B
	SUB-13-00012-DUR-225-A	Shop Drawings: Concrete Gravity Wall from Sta.3+455 to Sta.3+540 LHS - Project 01	DUR	S	06/16/14	07/07/14	06/26/14	10	C
	SUB-13-00012-DUR-225-B	Shop Drawings: Concrete Gravity Wall from Sta.3+455 to Sta.3+540 LHS - Project 01	DUR	S	07/06/14	07/27/14	07/08/14	2	B
	SUB-13-00012-DUR-226-A	Shop Drawings: Concrete Gravity Wall from Sta.3+610 to Sta.3+656 LHS - Project 01	DUR	S	06/18/14	07/09/14	07/07/14	19	C
	SUB-13-00012-DUR-226-B	Shop Drawings: Retaining Wall from Sta. 3+620 to Sta. 3+656 LHS Project 01	DUR	S	07/17/14	08/07/14	08/07/14	21	C
	SUB-13-00012-DUR-226-C	Shop Drawings: Retaining Wall from Sta. 3+620 to Sta. 3+652 LHS Project 01	DUR	S	11/23/14	12/14/14	11/27/14	4	C
	SUB-13-00012-DUR-226-D	Shop Drawings: Retaining Wall from Sta. 3+620 to Sta. 3+652 LHS Project 01	DUR	S	12/02/14	12/23/14	12/10/14	8	B
	SUB-13-00012-DUR-227-A	Shop Drawings: Steel Lighting Poles from Sta.1+500 to Sta.4+040-Project 01	DUR	S	06/18/14	07/09/14	06/26/14	8	C

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-227-B	Shop Drawings: Steel Lighting Poles from Sta.1+500 to Sta.4+040-Project 01	DUR	S	01/13/15	02/03/15	01/28/15	15	B
	SUB-13-00012-DUR-228-A	Shop Drawings: Water :Plan , Profile and Typical Sections from Sta.3+200 to Sta4+040 -Project 01	DUR	S	06/18/14	07/09/14	07/06/14	18	C
	SUB-13-00012-DUR-228-B	Shop Drawings: Water :Plan , Profile and Typical Sections from Sta.3+200 to Sta4+040 -Project 01	DUR	S	07/15/14	08/05/14	07/22/14	7	B
	SUB-13-00012-DUR-229-A	Shop Drawings: Concrete Gravity Wall from Sta.3+920 to Sta.3+950 LHS-Project 01	DUR	S	06/18/14	07/09/14	06/26/14	8	B
	SUB-13-00012-SAM-230-A	Shop Drawings: Crossing Pipe Culvert from Sta.0+131 to Sta.0+140 RHS -Project 02	SAM	S	06/19/14	07/10/14	06/30/14	11	E
	SUB-13-00012-DUR-231-A	Shop Drawings: Concrete Gravity Wall from Sta.3+765 to Sta.3+785 LHS-Project 01	DUR	S	06/19/14	07/10/14	06/26/14	7	B
	SUB-13-00012-SAM-232-A	Shop Drawings: Crossing Pipe Culvert from Sta.0+583.5 to Sta.0+599.5 RHS -Project 02	SAM	S	06/19/14	07/10/14	07/08/14	19	E
	SUB-13-00012-SAM-233-A	Shop Drawings: Crossing Pipe Culvert from Sta.0+727 to Sta.0+737 RHS -Project 02	SAM	S	06/19/14	07/10/14	07/08/14	19	E
	SUB-13-00012-SAM-234-A	Shop Drawings: Crossing Pipe Culvert from Sta.0+888 to Sta.0+910 RHS -Project 02	SAM	S	06/19/14	07/10/14	07/09/14	20	B
	SUB-13-00012-SAM-235-A	Asphalt wearing ¾" JMF_ Roots Co.-Item 3.03-Project 02	SAM	M	06/19/14	07/10/14	06/22/14	3	B
	SUB-13-00012-SAM-236-A	Shop Drawings: Crossing Pipe Culverts from Sta.1+416 to Sta.1+426 LHS, from Sta.1+434 to Sta.1+442 LHS, from Sta.1+460 to Sta.1+468 LHS ,from Sta.2+643 to Sta.2+653 RHS ,from Sta.3+615 to Sta.3+623 LHS and from Sta.3+719 to Sta.3+727 RHS -Project 02	SAM	S	06/23/14	07/14/14	07/09/14	16	B
	SUB-13-00012-SAM-237-A	Shop Drawings: Simple access from Sta.0+260 ,0+640 , 0+731, 1+253 ,1+383 ,1+422 ,1+439 ,1+465 ,1+583 ,1+713, 2+647 ,3+115 ,3+301 , 3+338 ,3+619 ,3+725 ,3+765 ,3+862 and 3+870 -Project 02	SAM	S	06/23/14	07/14/14	07/10/14	17	B
	SUB-13-00012-SAM-238-A	Shop Drawings: Crossing Pipe Culvert from Sta.3+331 to Sta.3+341 RHS -Project 02	SAM	S	06/24/14	07/15/14	07/09/14	15	E
	SUB-13-00012-SAM-239-A	Shop Drawings: Crossing Pipe Culvert from Sta.3+080 to Sta.3+113 RHS -Project 02	SAM	S	06/24/14	07/15/14	07/13/14	19	B
	SUB-13-00012-DUR-240-A	Shop Drawings: Storm Water : Plan , Profile and Cross Section from Sta. 2+240 to Sta.2+400 -Project 01	DUR	S	06/26/14	07/17/14	07/16/14	20	C
	SUB-13-00012-DUR-240-B	Shop Drawings: Storm Water : Plan , Profile and Cross Section from Sta. 2+240 to Sta.2+400 -Project 01	DUR	S	09/11/14	10/02/14	09/24/14	13	B
	SUB-13-00012-SAM-241-A	Shop Drawings: Stone Wall from Sta.A3+367 to Sta.3+483 LHS -Project 02	SAM	S	06/30/14	07/21/14	07/09/14	9	B
	SUB-13-00012-SAM-242-A	Shop Drawings: Stone Wall from Sta.A3+063 to Sta.3+097 LHS -Project 02	SAM	S	06/30/14	07/21/14	07/08/14	8	E

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-SAM-243-A	Shop Drawings: Stone Wall from Sta.A3+509 to Sta.A3+538 LHS, from Sta.A3+545 to Sta.A3+572 LHS ,from Sta.A3+577 to Sta.A3+615 LHS ,from Sta.A3+622 to Sta.A3+678 LHS and from Sta.A3+685 to Sta.A3+737 LHS-Project 02	SAM	S	06/30/14	07/21/14	07/13/14	13	B
	SUB-13-00012-SAM-244-A	Shop Drawings: Stone Wall from Sta.A4+072 to Sta.4+107 LHS -Project 02	SAM	S	06/30/14	07/21/14	07/09/14	9	E
	SUB-13-00012-SAM-245-A	Shop Drawings: Stone Wall from Sta.A3+266 to Sta.A3+295 LHS and from Sta.A3+306 to Sta.A3+332 LHS-Project 02	SAM	S	06/30/14	07/21/14	07/13/14	13	B
	SUB-13-00012-SAM-246-A	Shop Drawings: Stone Wall from Sta.A3+822 to Sta.3+851 RHS -Project 02	SAM	S	06/30/14	07/21/14	07/13/14	13	B
	SUB-13-00012-SAM-247-A	Shop Drawings: Plan and Details for Concrete Ditch from Sta.0+000 to Sta.4+120 -Segment A -Project 02	SAM	S	07/03/14	07/24/14	07/20/14	17	B
	SUB-13-00012-SAM-248-A	Shop Drawings: Plan and Details for Road Marking ,Traffic Sign and Guardrail from Sta.0+000 to Sta.4+120 -Segment A -Project 02	SAM	S	07/03/14	07/24/14	07/24/14	21	C
	SUB-13-00012-SAM-248-B	Shop Drawings: Plan and Details for Road Marking ,Traffic Sign and Guardrail from Sta.0+000 to Sta.4+120 -Segment A -Project 02	SAM	S	08/11/14	09/01/14	08/19/14	8	B
	SUB-13-00012-SAM-249-A	Proposed Location of Permanent Sign – Project 02	SAM	P	07/03/14	07/24/14	07/09/14	6	B
	SUB-13-00012-DUR-250-A	Shop Drawings: Formwork Design for Retaining Wall -Project 01	DUR	S	07/08/14	07/29/14	07/13/14	5	B
	SUB-13-00012-DUR-251-A	Shop Drawings: Side Walk from Sta.2+600 to Sta.3+200	DUR	S	07/08/14	07/29/14	07/22/14	14	B
	SUB-13-00012-DUR-252-A	Work Zone Traffic Control and Operations at Night(Specific Night Work Safety Plan)	DUR	P	07/08/14	07/29/14	07/15/14	7	B
	SUB-13-00012-DUR-253-A	Manhole Cast Iron Cover _ KURDIA	DUR	M	07/15/14	08/05/14	07/23/14	8	C
	SUB-13-00012-DUR-253-B	Manhole Cast Iron Cover _ KURDIA	DUR	M	11/10/14	12/01/14	11/20/14	10	A
	SUB-13-00012-DUR-254-A	Pre Cast Concrete for Water Chamber 1.50m *1.5m*2.0m- addaci Co.	DUR	M	07/24/14	08/14/14	07/27/14	3	C
	SUB-13-00012-DUR-254-B	Pre Cast Concrete for Water Chamber 1.50m *1.5m*2.0m- addaci Co.	DUR	M	08/24/14	09/14/14	09/01/14	8	D
	SUB-13-00012-DUR-254-C	Pre Cast Concrete for Water Chamber	DUR	M	09/04/14	09/25/14	09/15/14	11	B
	SUB-13-00012-SAM-255-A	Geotextile Sheet_ Urim Co.	SAM	M	08/03/14	08/24/14	08/05/14	2	A
	SUB-13-00012-DUR-256-A	Shop Drawings: Storm system outfall at Sta. 1+300 with Staircase -Project 01	DUR	S	08/05/14	08/26/14	08/26/14	21	C
	SUB-13-00012-DUR-256-B	Shop Drawings: Storm system outfall at Sta. 1+300 with Staircase -Project 01	DUR	S	11/19/14	12/10/14	12/04/14	15	C
	SUB-13-00012-MRSII-257-A	Updated Construction schedule and S-curve , July 31, 2014	MRSII	SCH	08/07/14	08/28/14	08/19/14	12	C
	SUB-13-00012-MRSII-257-B	Updated Construction schedule and S-curve , July 31, 2014	MRSII	SCH	08/27/14	09/17/14	09/01/14	5	B
	SUB-13-00012-DUR-258-A	Cast Iron MH & catch basin covers_ HADDAD Co.-Project 01	DUR	M	08/11/14	09/01/14	08/19/14	8	B
	SUB-13-00012-SAM-259-A	Updated Asphalt Wearing JMF_ Project 02_ Item No.3.03 -Project 02	SAM	M	08/11/14	09/01/14	08/19/14	8	B
	SUB-13-00012-DUR-260-A	Shop Drawings: Stone Boulder from Sta.2+306.6 to Sta.2+343.25 RHS -Project 01	DUR	S	08/25/14	09/15/14	09/02/14	8	E
	SUB-13-00012-DUR-261-A	Shop Drawings: Retaining Wall from Sta.3+339 to Sta.3+349 LHS -Project 01	DUR	S	08/31/14	09/21/14	09/03/14	3	B
	SUB-13-00012-DUR-262-A	Shop Drawings: Storm Water : Plan , Profile and Cross Section from Sta. 2+860 to Sta.2+984 -Project 01	DUR	S	09/01/14	09/22/14	09/09/14	8	C

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-262-B	Shop Drawings: Storm Water : Plan , Profile and Cross Section from Sta. 2+780 to Sta.2+984 -Project 01	DUR	S	09/11/14	10/02/14	09/24/14	13	B
	SUB-13-00012-DUR-262-C	Shop Drawings: Storm Water : Plan , Profile and Cross Section from Sta. 2+780 to Sta.2+984 -Project 01 - For Engineering Record	DUR	S	11/17/14	12/08/14	11/27/14	10	B
	SUB-13-00012-DUR-263-A	Shop Drawings: Simple access from Sta.0+000 to Sta.3+750 -Project 01	DUR	S	09/02/14	09/23/14	09/10/14	8	B
	SUB-13-00012-DUR-264-A	Shop Drawings: Simple access at Sta.0+720 LHS ,0+850 LHS, 1+630 LHS & RHS, 3+110 RHS ,3+355 RHS and 3+514 RHS -Project 01	DUR	S	09/02/14	09/23/14	09/11/14	9	B
	SUB-13-00012-DUR-265-A	Steel Handrail -Sample	DUR	M	09/02/14	09/23/14	09/04/14	2	A
	SUB-13-00012-DUR-266-A	100 cm Diameter HDPE pipe for Outfall at Sta.1+300 -Project 01	DUR	M	09/02/14	09/23/14	09/10/14	8	B
	SUB-13-00012-DUR-267-A	Shop Drawings: Storm Water : Plan , Profile and Cross Section from Sta. 3+180 to Sta.3+250 -Project 01	DUR	S	09/03/14	09/24/14	09/11/14	8	B
	SUB-13-00012-DUR-267-B	Shop Drawings: Storm Water : Plan , Profile and Cross Section from Sta. 3+180 to Sta.3+250 -Project 01-For Engineering Record	DUR	S	11/23/14	12/14/14	11/27/14	4	B
	SUB-13-00012-DUR-268-A	Shop Drawings: Concrete Gravity Wall from Sta.2+306.6 to Sta.2+343.25 RHS -Project 01-According to SM No.: SM-13-00012-DUR-E-C-093 and CMC comments on Submittal No.:SUB-13-00012-DUR-260-A	DUR	S	09/04/14	09/25/14	09/10/14	6	B
	SUB-13-00012-DUR-268-B	Shop Drawings: Concrete Gravity Wall from Sta.2+306.6 to Sta.2+343.25 RHS -Project 01-For Engineering Record	DUR	S	09/11/14	10/02/14	09/17/14	6	B
	SUB-13-00012-SAM-269-A	Shop Drawings: Plan, Details Road Marking ,Traffic Sign and Guardrail from Sta.-0+070 to Sta.0+320 -Segment B -Project 02	SAM	S	09/10/14	10/01/14	09/11/14	1	B
	SUB-13-00012-SAM-270-A	Shop Drawings: Plan and Details for Concrete Ditch from Sta.-0+070 to Sta.0+320 -Segment B -Project 02	SAM	S	09/10/14	10/01/14	09/11/14	1	B
	SUB-13-00012-DUR-271-A	Updated Asphalt JMF- Asphalt Binder -Roots Company-Item No.3.05- Project 01	DUR	M	09/24/14	10/15/14	09/24/14	0	B
	SUB-13-00012-MRSII-272-A	Updated Construction Schedule & S-Curve (August 31,2014 ) -Project 01 ,Revised Construction Schedule & S-Curve (August 31,2014 ) -Project 02 and As Built Construction Schedule & S-Curve (August 31,2014 ) -Project 03	MRSII	SCH	09/08/14	09/29/14	09/28/14	20	C
	SUB-13-00012-MRSII-272-B	Updated Construction Schedule & S-Curve (August 31,2014 ) -Project 01 ,Revised Construction Schedule & S-Curve (August 31,2014 ) -Project 02 and As Built Construction Schedule & S-Curve (August 31,2014 ) -Project 03	MRSII	SCH	09/30/14	10/21/14	10/13/14	13	B
	SUB-13-00012-DUR-273-A	Threaded Gate Valve 2 inch - alternative source-Crane -Project 01	DUR	M	09/09/14	09/30/14	09/17/14	8	D
	SUB-13-00012-DUR-273-B	Threaded Gate Valve 2 inch - alternative source-Crane -Project 01	DUR	M	03/18/15	04/08/15	03/19/15	1	A
	SUB-13-00012-MRSII-274-A	Updated Construction Schedule & S-Curve (September 30, 2014) for Project 01 - As Built Construction Schedule & S-Curve for Project 02 and Project 03	MRSII	SCH	10/12/14	11/02/14	10/19/14	7	B
	SUB-13-00012-DUR-275-A	Asphalt JMF- Alternative source- Al Harith Com.-Item No.3.05-Project 01	DUR	M	10/23/14	11/13/14	11/03/14	11	D

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-I-00-12-00005  
TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-275-B	Asphalt JMF- Alternative source- Al Harith Com.-Item No.3.05-Project 01	DUR	M	12/04/14	12/25/14	12/24/14	20	B
	SUB-13-00012-DUR-276-A	Wearing layer JMF- Roots- item 3.03 -Project 01	DUR	M	10/26/14	11/16/14	10/28/14	2	B
	SUB-13-00012-DUR-277-A	Shop Drawings: Concrete Wall from Sta.0+008.5 to Sta. 0+015.65 LHS at Simple Access Sta.0+520 -Project 01	DUR	S	10/28/14	11/18/14	11/12/14	15	C
	SUB-13-00012-DUR-277-B	Shop Drawings: Concrete Wall from Sta.0+010 to Sta. 0+015.65 LHS at Simple Access Sta.0+520 -Project 01	DUR	S	01/20/15	02/10/15	02/02/15	13	A
	SUB-13-00012-DUR-278-A	Water Service Box Manholes- PCI Co.-Project 01	DUR	M	10/29/14	11/19/14	11/03/14	5	B
	SUB-13-00012-SAM-279-A	As Built Drawings- Project 02	SAM	AS	11/06/14	11/27/14	11/26/14	20	C
	SUB-13-00012-SAM-279-B	As Built Drawings- Project 02	SAM	AS	12/11/14	01/01/15	12/24/14	13	C
	SUB-13-00012-SAM-279-C	As Built Drawings- Project 02	SAM	AS	12/30/14	01/20/15	01/15/15	16	A
	SUB-13-00012-MRSII-280-A	Updated Construction Schedule & S-Curve (October 31, 2014)-Project 01 and As Built Construction Schedule & S-Curve- Project 02 and Project 03	MRSII	SCH	11/06/14	11/27/14	11/18/14	12	B
	SUB-13-00012-DUR-281-A	Shop Drawings: Structural and Mechanical Detail for combined chambers #07 and #08 -Project 01	DUR	S	11/12/14	12/03/14	12/02/14	20	C
	SUB-13-00012-DUR-281-B	Shop Drawings: Structural and Mechanical Detail for combined chambers #07 and #08 -Project 01	DUR	S	12/10/14	12/31/14	12/22/14	12	B
	SUB-13-00012-DUR-282-A	Shop Drawings: Structural and Mechanical Detail for 2" ARV at Sta.3+308, 3" ARV at Sta.2+570, 2" Washout at Sta. 3+380, 3" Washout at Sta.2+340, Chamber #11 at Sta.3+170 and Chamber #11 at Sta. 3+520	DUR	S	11/17/14	12/08/14	12/08/14	21	B
	SUB-13-00012-DUR-283-A	Shop Drawings: Service Box Typical Detail at Sta. 0+280 RHS, Sta.0+600 LHS, Sta.0+600 RHS, Sta.1+050 (2LHS & 2RHS), Sta.2+150 (2LHS & 2RHS), Sta.3+170 (2LHS & 2RHS) -Project 01	DUR	S	11/23/14	12/14/14	12/08/14	15	B
	SUB-13-00012-DUR-284-A	Shop Drawings: Concrete Gravity Wall from Sta.3+304 to Sta.3+327 LHS - Project 01	DUR	S	11/23/14	12/14/14	11/27/14	4	C
	SUB-13-00012-DUR-284-B	Shop Drawings: Concrete Gravity Wall from Sta.3+304 to Sta.3+327 LHS - Project 01	DUR	S	12/02/14	12/23/14	12/10/14	8	B
	SUB-13-00012-DUR-285-A	Combination Air Valve_ 2" _A.R.I_ item 4.24.2.a - Project 01	DUR	M	11/23/14	12/14/14	12/04/14	11	B
	SUB-13-00012-DUR-286-A	Shop Drawings: Concrete Gravity Wall from Sta.3+233 to Sta.3+245 LHS - Project 01	DUR	S	11/26/14	12/17/14	12/04/14	8	E
	SUB-13-00012-MRSII-287-A	Revised Construction Schedule & S-Curve -November 20, 2014	MRSII	SCH	11/30/14	12/21/14	12/10/14	10	C
	SUB-13-00012-MRSII-287-B	Revised Construction Schedule & S-Curve (November 20, 2014) for Project 01 - As Built Construction Schedule & S-Curve Project 02 and Project 03	MRSII	SCH	12/15/14	01/05/15	12/21/14	6	A
	SUB-13-00012-DUR-288-A	Shop Drawings: Concrete Wall from Sta.2+984 to Sta.3+264 LHS -Project 01	DUR	S	12/18/14	01/08/15	12/22/14	4	B
	SUB-13-00012-DUR-289-A	Shop Drawings : Retaining Wall from Sta.1+694 to Sta.1+755 LHS -Project 01- As per Site Memo No.: SM-13-00012-DUR-E-C-123	DUR	S	12/18/14	01/08/15	12/22/14	4	B

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 Submittals Register Log**



Spec. No.	Submittal No	Description	Project	DV	TRACKING DATES				Approval Status (A,B,C,D,E)
					Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	SUB-13-00012-DUR-290-A	Shop Drawings :Retaining Wall from Sta.2+770 to Sta.2+825 RHS -Project 01	DUR	S	12/18/14	01/08/15	12/22/14	4	B
	SUB-13-00012-MRSII-291-A	Revised Construction Schedule & S-Curve (Jan. 14, 2015)-Project 01 As Built Construction Schedule & S-Curve Project 02 & Project 03	MRSII	SCH	01/25/15	02/15/15	02/04/15	10	C
	SUB-13-00012-MRSII-291-B	Revised Construction Schedule & S-Curve (Jan. 14, 2015)-Project 01	MRSII	SCH	02/09/15	03/02/15	02/22/15	13	B
	SUB-13-00012-DUR-292-A	Shop Drawings: Road Marking from Sta.0+000 to Sta.2+600 - Project 01	DUR	S	01/14/15	02/04/15	01/27/15	13	C
	SUB-13-00012-DUR-292-B	Shop Drawings: Road Marking from Sta.0+000 to Sta.2+600 - Project 01	DUR	S	02/08/15	03/01/15	02/19/15	11	B
	SUB-13-00012-DUR-292-C	Shop Drawings: Road Marking from Sta.0+000 to Sta.2+600 - Project 01 - For Engineering Record	DUR	S	02/23/15	03/16/15	02/24/15	1	B
	SUB-13-00012-DUR-293-A	Threaded Coupling 2" manufactured by ERBOSAN supplied from FIP -Project 01	DUR	M	01/20/15	02/10/15	01/28/15	8	B
	SUB-13-00012-DUR-294-A	Manhole adjustment work method statement -Project 01	DUR	M	01/27/15	02/17/15	01/29/15	2	C
	SUB-13-00012-DUR-294-B	Manhole adjustment work method statement -Project 01	DUR	M	03/18/15	04/08/15	03/19/15	1	A
	SUB-13-00012-DUR-295-A	Shop Drawings: Retaining Wall from Sta.3+580 to Sta.3+613 LHS -Project 01	DUR	S	02/08/15	03/01/15	02/18/15	10	B
	SUB-13-00012-DUR-296-A	Wearing layer JMF- AL Harith alternative source- item 3.03 -Project 01	DUR	M	02/11/15	03/04/15	02/18/15	7	B
	SUB-13-00012-DUR-297-A	Shop Drawings: Road Marking and Traffic Sign from Sta.2+600 to Sta.3+750 - Project 01	DUR	S	02/16/15	03/09/15	02/19/15	3	B
	SUB-13-00012-DUR-297-B	Shop Drawings: Road Marking and Traffic Sign from Sta.2+600 to Sta.3+750 - Project 01- For Engineering Record	DUR	S	02/23/15	03/16/15	02/24/15	1	B
	SUB-13-00012-DUR-298-A	Permanent Sign Approved text and Location at Sta.0+330 RHS at Dura Project 01	DUR	P	02/19/15	03/12/15	02/24/15	5	A
	SUB-13-00012-DUR-299-A	Draft As Built Drawings for Retaining Walls, Concrete Gravity Walls, Boundary Walls and Stone Walls - Project 01	DUR	AS	03/01/15	03/22/15	03/22/15	21	C
	SUB-13-00012-DUR-300-A	Draft As Built Drawings for Water Works: Plan , Profile and Typical Section from Sta.0+000 to Sta.2+000 - Project 01	DUR	AS	03/04/15	03/25/15	03/22/15	18	C
	SUB-13-00012-DUR-301-A	Draft As Built Drawings for Storm Water : Plan , Profile and Typical Section - Project 01	DUR	AS	03/04/15	03/25/15	03/25/15	21	C
	SUB-13-00012-DUR-302-A	Draft As Built Drawings for Road Works: Plan , Profile and Cross Section from Sta.0+000 to Sta.2+000 - Project 01	DUR	AS	03/04/15	03/25/15	03/25/15	21	C
	SUB-13-00012-DUR-303-A	Flanged Dresser_ Krausz-to be used as alternative dismantling joint at water chamber 12 at sta. 3+520 - Project 01	DUR	M	03/17/15	04/07/15	03/19/15	2	A
	SUB-13-00012-DUR-304-A	Shop Drawings: Side Walk from Sta.3+160 to Sta.3+700 - Project 01	DUR	S	03/18/15	04/08/15	03/19/15	1	B
<b>DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required</b>									
<p>p= preconstruction - S= Shop drawings - M= Materials -O= Others</p>									

**G | RFI's Log for the Reporting Period**

**USAID WEST BANK/ GAZA  
INFRASTRUCTURE NEEDS PROGRAM INPII  
CONTRACT NO. AID-294-I-00-12-00005  
TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
RFIs log - MRSII**



Spec. No.	RFI No	Request For Information Description	DV	TRACKING DATES				Response by
				Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	RFI-13-00012-MRSII-001	Clarification of the design details for parking area at Dura Hebron (Sinjir) Road-Project 01	DUR	11/21/13	12/12/13	12/01/13	10	Monther Ramadan
	RFI-13-00012-MRSII-002	Proposed pipe culverts, reconstruction stone walls and gravity wall from A0+750 TO A1+500 at HYW 60 Samu' -Yatta Road- Segment A-Project 02	SAM	11/21/13	12/12/13	12/04/13	13	Monther Ramadan
	RFI-13-00012-MRSII-003	Coordinates for Bench Marks and survey control points at HYW 60 Samu' - Yatta Road- Segment A-Project 02	SAM	11/21/13	12/12/13	12/01/13	10	Monther Ramadan
	RFI-13-00012-MRSII-004	Reconstruction of stone wall, concrete walls ,staircase based on actual site conditions at Dura Hebron (Sinjer) Road-Project 01	DUR	11/25/13	12/16/13	12/02/13	7	Monther Ramadan
	RFI-13-00012-MRSII-005	Design of concrete slab on grade ramps subjected to traffic load at all projects of Task order # 12	MRSII	12/04/13	12/25/13	12/22/13	18	Monther Ramadan
	RFI-13-00012-MRSII-006	Missing intersection at Sta.A0+260 ,and site condition from sta. A0+000 to A0+750 at HYW 60 Samu' - Yatta Road- Segment .A / Task order # 12	SAM	12/23/13	01/13/14	01/05/14	13	Monther Ramadan
	RFI-13-00012-MRSII-007	New scope of work for Dura - Hebron (Sinjer) Road, Project # 01	DUR	12/26/13	01/16/14	12/29/13	3	Monther Ramadan
	RFI-13-00012-MRSII-008	Storm water manholes in Dura – Hebron (Sinjir) Road, TO # 12	DUR	01/14/14	02/04/14	01/30/14	16	Monther Ramadan
	RFI-13-00012-MRSII-009	Storm water drainage system-Dura Hebron (Sinjir) Road -Project 01	DUR	01/23/14	02/13/14	01/30/14	7	Monther Ramadan
	RFI-13-00012-MRSII-010	Site conditions and design requirement to be considered for shop drawings at Dura – Hebron (Sinjir) Road, Project #1 (TO #12).	DUR	02/13/14	03/06/14	03/06/14	21	Monther Ramadan
	RFI-13-00012-MRSII-011	Location and design section for Stone walls at HYW 60 Samu' - Yatta Road-Segment .A / Task order # 12	SAM	02/18/14	03/11/14	03/10/14	20	Monther Ramadan
	RFI-13-00012-MRSII-012	Design table for gravity wall at Dura road project, TO # 12	DUR	02/23/14	03/16/14	03/09/14	14	Monther Ramadan
	RFI-13-00012-MRSII-013	Storm outlet at sta. 1+080 Dura project, TO # 12	DUR	02/27/14	03/20/14	03/12/14	13	Monther Ramadan
	RFI-13-00012-MRSII-014	Storm water drainage pipe culvert at sta. 1+612 Al Samu' Yatta Road, TO 13-00012	SAM	04/10/14	05/01/14	04/23/14	13	Monther Ramadan
	RFI-13-00012-MRSII-015	Storm water drainage system from sta. 0+000 to sta. 0+850 Dura Project, TO 13-00012	DUR	04/15/14	05/06/14	04/30/14	15	Monther Ramadan
	RFI-13-00012-MRSII-016	Re-Design of road from Sta.1+500 to Sta.2+000-Dura Project -T.O.12	DUR	04/17/14	05/08/14	04/23/14	6	Monther Ramadan
	RFI-13-00012-MRSII-017	Existing box culvert at sta. 2+200 Project #2, TO # 12	SAM	04/27/14	05/18/14	05/06/14	9	Monther Ramadan
	RFI-13-00012-MRSII-018	Existing box culvert at sta. 2+690 Project #2, TO # 12	SAM	04/27/14	05/18/14	04/28/14	1	Monther Ramadan
	RFI-13-00012-MRSII-019	Shop drawings preparation from sta. 1+500 to sta. 2+000 (Working out of Road ROW), Project #1, TO # 12	DUR	05/01/14	05/22/14	05/06/14	5	Monther Ramadan
	RFI-13-00012-MRSII-020	Required WO & ARV between 1+500 to 2+600 in Dura – Hebron (Sinjir) Road, TO # 12	DUR	05/08/14	05/29/14	05/28/14	20	Monther Ramadan
	RFI-13-00012-MRSII-021	Trench for water network at Dura – Hebron (Sinjir) Road, TO # 12	DUR	05/15/14	06/05/14	05/18/14	3	Monther Ramadan
	RFI-13-00012-MRSII-022	Storm water drainage outfall @ sta. 0+300 Dura Project, TO 13-00012	DUR	06/02/14	06/23/14	06/03/14	1	Monther Ramadan
	RFI-13-00012-MRSII-023	Site conditions and design requirement to be considered for shop drawings at Dura from sta.2+600 to 3+180 – Hebron (Sinjir) Road, Project #1 (TO #12).	DUR	06/03/14	06/24/14	06/18/14	15	Monther Ramadan

**USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER #12, MULTIPLE ROADS PROJECT ( SOUTH II )  
 RFIs log - MRSII**



Spec. No.	RFI No	Request For Information Description	DV	TRACKING DATES				Response by
				Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	RFI-13-00012-MRSII-024	Rubble concrete and location for the foundation of retaining wall at sta. 1+557 to 1+600 LHS Dura Hebron (Sinjer) Road –Task order #12	DUR	06/08/14	06/29/14	06/10/14	2	Monther Ramadan
	RFI-13-00012-MRSII-025	Asphalt Milling and overlay to be considered for shop drawings at Dura from sta.3+700 to 4+040 – Hebron (Sinjir) Road, Project #1 (TO #12).	DUR	06/10/14	07/01/14	06/23/14	13	Monther Ramadan
	RFI-13-00012-MRSII-026	Storm drainage system from 1+080 to 4+040 at sta. 4+040 Dura project, TO # 12	DUR	06/10/14	07/01/14	07/01/14	21	Monther Ramadan
	RFI-13-00012-MRSII-027	Site conditions and design requirement to be considered for shop drawings at Dura from sta. 3+180 – to 4+040 Hebron (Sinjir) Road, Project #1 (TO #12).	DUR	06/12/14	07/03/14	06/17/14	5	Monther Ramadan
	RFI-13-00012-MRSII-028	Required washout and air relieve valve chambers from Sta.3+180 to Sta. 4+040- at Dura Hebron (Sinjer) Road-Project 01 / Task order # 12	DUR	06/18/14	07/09/14	07/02/14	14	Monther Ramadan
	RFI-13-00012-MRSII-029	Concrete parapet above proposed stone wall at Dura Hebron (Sinjer) Road: Task order # 12	DUR	06/24/14	07/15/14	06/30/14	6	Monther Ramadan
	RFI-13-00012-MRSII-030	Concrete ditch and concrete protection at HYW 60 Samu' - Yatta Road-Segment .A / Task order # 12	SAM	08/03/14	08/24/14	08/17/14	14	Monther Ramadan
	RFI-13-00012-MRSII-031	Steel anchor bolts for the street lighting at Dura – Hebron (Sinjir) Road, TO # 12	DUR	08/19/14	09/09/14	08/20/14	1	Monther Ramadan
	RFI-13-00012-MRSII-032	Construction risk for the proposed concrete gravity wall from sta. 3+460 to 3+480 / Dura – Hebron (Sinjir) Road, Project #1/ Task order # 12	DUR	08/25/14	09/15/14	09/01/14	7	Monther Ramadan
	RFI-13-00012-MRSII-033	CMC Response to Construction risk for the proposed concrete gravity wall from sta. 3+460 to 3+480 / Dura – Hebron (Sinjir) Road, Project #1/ Task order # 12	DUR	09/04/14	09/25/14	09/11/14	7	Monther Ramadan
	RFI-13-00012-MRSII-034	Change of Sidewalk steel reinforcement - Dura – Hebron (Sinjir) Road, Project #1	DUR	11/16/14	12/07/14	11/18/14	2	Monther Ramadan
	RFI-13-00012-MRSII-035	Raising profile from sta. 3+480 to sta. 3+640 -Dura – Hebron (Sinjir) Road, Project #1	DUR	02/15/15	03/08/15	02/18/15	3	Monther Ramadan

**H | Geo-MIS DATA COLLECTION SHEET**  
**Generated Person Days of Employment**

USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER NO. AID-294-TO-13-00012  
 Multiple Roads South-MRSII  
 Temproray Job Days Summary Report

Task Order Name: Multiple Roads South - MRSII  
 Sub-project or Activity Name: Project 01- Dura - Hebron Road  
 CONTRACTOR: APCO/ArCon

PERIOD FROM: November 01, 2013  
 PERIOD TO: March 31, 2015

Date		Site Staff Job Days**					Total Job Days	No of Full Time Equivalent (FTE) Jobs in the Month*	Notes of Comments
Month	Year	Management	Engineers	Skilled Labor	Unskilled Labor	Other			
October	2012						0	0	
November	2012						0	0	
December	2012						0	0	
January	2013						0	0	
February	2013						0	0	
March	2013						0	0	
April	2013						0	0	
May	2013						0	0	
June	2013						0	0	
July	2013						0	0	
August	2013						0	0	
September	2013						0	0	
<b>Total of FY 2013</b>							<b>0</b>	<b>0</b>	
October	2013						0	0	
November	2013	1.5	0.0	16.0	0.0	0.0	17.5	0.7	
December	2013	8.7	0.0	1.0	27.5	0.0	37.2	1.6	
January	2014	39.8	93.4	149.9	135.5	0.0	418.5	17.6	
February	2014	36.0	108.6	170.5	130.0	0.0	445.1	18.7	
March	2014	40.8	130.5	479.8	238.8	0.0	889.8	37.4	
April	2014	62.4	117.7	681.9	344.6	0.0	1206.6	50.7	
May	2014	48.5	103.0	683.4	357.8	0.0	1192.7	50.1	
June	2014	77.3	119.9	928.4	697.4	0.0	1823.0	76.6	
July	2014	45.8	50.8	688.5	393.3	0.0	1178.2	49.5	
August	2014	79.1	126.6	1405.5	811.5	0.0	2422.8	101.8	
September	2014	88.3	107.9	1298.2	808.8	0.0	2303.1	96.8	
<b>Total of FY 2014</b>							<b>11934.4</b>	<b>501.4</b>	
October	2014	123.9	100.4	976.8	584.9	0.0	1786.0	75.0	
November	2014	144.4	123.7	1006.3	685.8	0.0	1960.1	82.4	
December	2014	155.1	151.1	1341.3	908.5	0.0	2556.1	107.4	
January	2015	99.9	122.1	917.7	627.0	0.0	1766.7	74.2	
February	2015	102.4	117.2	799.5	584.5	0.0	1603.7	67.4	
March	2015	131.6	130.2	942.7	795.8	0.0	2000.2	84.0	
April	2015						0.0	0.0	
May	2015						0.0	0.0	
June	2015						0.0	0.0	
July	2015						0.0	0.0	
August	2015						0.0	0.0	
September	2015						0.0	0.0	
<b>Total of FY 2015</b>							<b>11672.7</b>	<b>490.4</b>	

Note :  
 \* No of Full Time Equivalent (FTE) Jobs in the Month = Total Job Days / Avg. Days in the Month(23.8)  
 \*\* This data collection sheet is for Palestinian staff only , experts and foreign employee shall not be included.

USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER NO. AID-294-TO-13-00012  
 Multiple Roads South-MRSII  
 Temproray Job Days Summary Report

Task Order Name: Multiple Roads South - MRSII  
 Sub-project or Activity Name: Project 02- Samu'- Yatta Road  
 CONTRACTOR: APCO/ArCon

PERIOD FROM: November 01, 2013  
 PERIOD TO: December 31, 2014

Date		Site Staff Job Days**					Total Job Days	No of Full Time Equivalent (FTE) Jobs in the Month*	Notes of Comments
Month	Year	Management	Engineers	Skilled Labor	Unskilled Labor	Other			
October	2012						0	0	
November	2012						0	0	
December	2012						0	0	
January	2013						0	0	
February	2013						0	0	
March	2013						0	0	
April	2013						0	0	
May	2013						0	0	
June	2013						0	0	
July	2013						0	0	
August	2013						0	0	
September	2013						0	0	
Total of FY 2013							0	0	
October	2013						0	0	
November	2013	1.5	0.0	14.0	0.0	0.0	15.5	0.7	
December	2013	8.7	0.0	0.0	0.0	0.0	8.7	0.4	
January	2014	39.8	21.0	152.5	108.0	0.0	321.3	13.5	
February	2014	36.0	48.0	338.0	122.5	0.0	544.5	22.9	
March	2014	40.5	56.0	429.5	263.0	0.0	789.0	33.2	
April	2014	42.0	60.6	529.9	296.0	0.0	928.5	39.0	
May	2014	45.5	63.0	529.5	260.8	0.0	898.8	37.8	
June	2014	50.0	64.5	570.4	469.4	0.0	1154.3	48.5	
July	2014	42.0	46.0	446.3	327.0	0.0	861.3	36.2	
August	2014	49.5	62.0	605.3	476.0	0.0	1192.8	50.1	
September	2014	52.0	69.5	752.1	690.0	0.0	1563.6	65.7	
Total of FY 2014							8278.1	347.8	
October	2014	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
November	2014						0.0	0.0	
December	2014						0.0	0.0	
January	2015						0.0	0.0	
February	2015						0.0	0.0	
March	2015						0.0	0.0	
April	2015						0.0	0.0	
May	2015						0.0	0.0	
June	2015						0.0	0.0	
July	2015						0.0	0.0	
August	2015						0.0	0.0	
September	2015						0.0	0.0	
Total of FY 2015							0.0	0.0	

Note :

\* No of Full Time Equivalent (FTE) Jobs in the Month = Total Job Days / Avg. Days in the Month(23.8)

\*\* This data collection sheet is for Palestinian staff only , experts and foreign employee shall not be included.

USAID WEST BANK/ GAZA  
 INFRASTRUCTURE NEEDS PROGRAM INPII  
 CONTRACT NO. AID-294-I-00-12-00005  
 TASK ORDER NO. AID-294-TO-13-00012  
 Multiple Roads South-MRSII  
 Temporarily Job Days Summary Report

Task Order Name: Multiple Roads South - MRSII

PERIOD FROM: November 01, 2013

Sub-project or Activity Name: Project 03- Milling and Overlay of Bethlehem Internal Roads

PERIOD TO: June 30, 2014

CONTRACTOR: APCO/ArCon

Date		Site Staff Job Days**					Total Job Days	No of Full Time Equivalent (FTE) Jobs in the Month*	Notes of Comments
Month	Year	Management	Engineers	Skilled Labor	Unskilled Labor	Other			
October	2012						0	0	
November	2012						0	0	
December	2012						0	0	
January	2013						0	0	
February	2013						0	0	
March	2013						0	0	
April	2013						0	0	
May	2013						0	0	
June	2013						0	0	
July	2013						0	0	
August	2013						0	0	
September	2013						0	0	
Total of FY 2013							0	0	
October	2013						0	0	
November	2013	4.4	38.0	97.8	48.3	0.0	188.4	7.9	
December	2013	11.1	41.0	38.9	33.5	0.0	124.5	5.2	
January	2014	39.4	58.1	384.8	263.9	0.0	746.1	31.3	
February	2014	36.0	54.0	313.6	291.0	0.0	694.6	29.2	
March	2014	43.1	60.1	594.5	385.4	0.0	1083.1	45.5	
April	2014	42.0	94.8	404.4	320.1	0.0	861.3	36.2	
May	2014	19.5	29.9	47.3	61.8	0.0	158.4	6.7	
June	2014	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
July	2014						0.0	0.0	
August	2014						0.0	0.0	
September	2014						0.0	0.0	
Total of FY 2014							3856.3	162.0	
October	2014						0	0	
November	2014						0	0	
December	2014						0	0	
January	2015						0	0	
February	2015						0	0	
March	2015						0	0	
April	2015						0	0	
May	2015						0	0	
June	2015						0	0	
July	2015						0	0	
August	2015						0	0	
September	2015						0	0	
Total of FY 2015							0	0	

Note :

\* No of Full Time Equivalent (FTE) Jobs in the Month = Total Job Days / Avg. Days in the Month(23.8)

\*\* This data collection sheet is for Palestinian staff only , experts and foreign employee shall not be included.

Note: Numbers are rounded to nearest integer number.

**Total Generated Man-days per fiscal year**

Project Name	DV	FY14												FY15					
		QRT 1 Oct. 1, 2013 to Dec. 31, 2013			QRT 2 Jan. 1, 2014 to Mar. 31, 2014			QRT 3 Apr. 1, 2014 to June. 30, 2014			QRT 4 Jul. 1, 2014 to Sep. 30, 2014			QRT 1 Oct. 1, 2014 to Dec. 31, 2014			QRT 2 Jan. 1, 2015 to Mar. 31, 2015		
		October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
<b>Total</b>	MRSII	<b>0.0</b>	<b>221.4</b>	<b>170.4</b>	<b>1485.9</b>	<b>1684.3</b>	<b>2761.9</b>	<b>2996.3</b>	<b>2249.8</b>	<b>2977.3</b>	<b>2039.5</b>	<b>3615.5</b>	<b>3866.7</b>	<b>1786.0</b>	<b>1960.1</b>	<b>2556.1</b>	<b>1766.7</b>	<b>1603.7</b>	<b>2000.2</b>
PROJECT 01	DUR	0.0	17.5	37.2	418.5	445.1	889.8	1206.6	1192.7	1823.0	1178.2	2422.8	2303.1	1786.0	1960.1	2556.1	1766.7	1603.7	2000.2
PROJECT 02	SAM	0.0	15.5	8.7	321.3	544.5	789.0	928.5	898.8	1154.3	861.3	1192.8	1563.6	0.0	0.0	0.0	0.0	0.0	0.0
PROJECT 03	BTH	0.0	188.4	124.5	746.1	694.6	1083.1	861.3	158.4	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

Project Name	DV	FY14 & FY15	(FTE) Jobs
<b>Total</b>	MRSII	<b>35741.4</b>	<b>1501.7</b>
PROJECT 01	DUR	<b>23607.0</b>	<b>991.9</b>
PROJECT 02	SAM	<b>8278.1</b>	<b>347.8</b>
PROJECT 03	BTH	<b>3856.3</b>	<b>162.0</b>

**Total Femal Employment days per fiscal year**

Project Name	DV	FY14												FY15					
		QRT 1 Oct. 1, 2013 to Dec. 31, 2013			QRT 2 Jan. 1, 2014 to Mar. 31, 2014			QRT 3 Apr. 1, 2014 to June. 30, 2014			QRT 4 Jul. 1, 2014 to Sep. 30, 2014			QRT 1 Oct. 1, 2014 to Dec. 31, 2014			QRT 2 Jan. 1, 2015 to Mar. 31, 2015		
		October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
<b>Total</b>	MRSII	<b>0.0</b>	<b>0.0</b>	<b>0.0</b>	<b>36.0</b>	<b>48.0</b>	<b>49.4</b>	<b>51.5</b>	<b>49.9</b>	<b>25.8</b>	<b>18.4</b>	<b>45.0</b>	<b>54.0</b>	<b>21.1</b>	<b>25.6</b>	<b>25.8</b>	<b>22.0</b>	<b>22.5</b>	<b>26.8</b>
PROJECT 01	DUR	0.0	0.0	0.0	24.0	24.0	17.0	8.6	11.0	0.0	0.0	6.5	13.0	21.1	25.6	25.8	22.0	22.5	26.8
PROJECT 02	SAM	0.0	0.0	0.0	12.0	24.0	29.0	34.6	37.0	25.8	18.4	38.5	41.0	0.0	0.0	0.0	0.0	0.0	0.0
PROJECT 03	BTH	0.0	0.0	0.0	0.0	0.0	3.4	8.3	1.9	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0

Project Name	DV	FY14 & FY15	Total FTE
<b>Total</b>	MRSII	<b>521.6</b>	<b>21.9</b>
PROJECT 01	DUR	247.9	10.4
PROJECT 02	SAM	260.3	10.9
PROJECT 03	BTH	13.5	0.6





**USAID WEST BANK/ GAZA**  
**INFRASTRUCTURE NEEDS PROGRAM**  
**TASK ORDER NO: AID-294-TO-12-00012**  
**Multiple Roads Project (South II)**  
**Geo-MIS DATA COLLECTION SHEET**

CONTRACTOR: APCO/ArCon

PERIOD FROM: March 01, 2015

PERIOD TO: March 31, 2015

DATE	Dura Hebron (Sinjer) Road					SubTotal	Samu' - Yatta Road					SubTotal
	Management	Engineers	Skilled labor	Unskilled labor	Other		Management	Engineers	Skilled labor	Unskilled labor	Other	
March 1, 2015	5.5	7.0	54.1	36.3		102.8	0.0	0.0	0.0	0.0		0.0
March 2, 2015	5.0	6.9	48.8	32.8		93.4	0.0	0.0	0.0	0.0		0.0
March 3, 2015	5.0	5.6	31.9	33.5		76.0	0.0	0.0	0.0	0.0		0.0
March 4, 2015	4.4	5.8	20.7	18.8		49.7	0.0	0.0	0.0	0.0		0.0
March 5, 2015	4.5	3.3	23.3	21.0		52.1	0.0	0.0	0.0	0.0		0.0
March 6, 2015	0.0	0.0	0.0	0.0		0.0	0.0	0.0	0.0	0.0		0.0
March 7, 2015	5.8	5.8	55.0	36.3		102.7	0.0	0.0	0.0	0.0		0.0
March 8, 2015	5.0	4.4	47.3	38.5		95.1	0.0	0.0	0.0	0.0		0.0
March 9, 2015	5.5	6.1	52.9	38.8		103.3	0.0	0.0	0.0	0.0		0.0
March 10, 2015	5.4	6.5	47.9	49.8		109.6	0.0	0.0	0.0	0.0		0.0
March 11, 2015	6.8	6.8	58.8	49.8		122.1	0.0	0.0	0.0	0.0		0.0
March 12, 2015	5.0	1.9	0.5	0.0		7.4	0.0	0.0	0.0	0.0		0.0
March 13, 2015	0.0	1.0	6.0	8.0		15.0	0.0	0.0	0.0	0.0		0.0
March 14, 2015	4.9	4.3	44.1	41.3		94.4	0.0	0.0	0.0	0.0		0.0
March 15, 2015	5.0	4.8	43.6	41.0		94.3	0.0	0.0	0.0	0.0		0.0
March 16, 2015	5.0	4.8	54.4	43.5		107.6	0.0	0.0	0.0	0.0		0.0
March 17, 2015	5.0	4.5	42.8	43.5		95.8	0.0	0.0	0.0	0.0		0.0
March 18, 2015	5.0	4.9	42.2	43.5		95.6	0.0	0.0	0.0	0.0		0.0
March 19, 2015	6.3	5.6	58.1	48.8		118.7	0.0	0.0	0.0	0.0		0.0
March 20, 2015	0.3	0.0	3.0	3.0		6.3	0.0	0.0	0.0	0.0		0.0
March 21, 2015	5.0	5.0	36.0	34.8		80.7	0.0	0.0	0.0	0.0		0.0
March 22, 2015	4.5	5.0	37.0	34.8		81.2	0.0	0.0	0.0	0.0		0.0
March 23, 2015	4.5	5.0	38.0	31.4		78.9	0.0	0.0	0.0	0.0		0.0
March 24, 2015	4.5	5.5	37.1	29.1		76.2	0.0	0.0	0.0	0.0		0.0
March 25, 2015	4.0	5.0	1.0	1.0		11.0	0.0	0.0	0.0	0.0		0.0
March 26, 2015	4.0	3.0	5.0	5.0		17.0	0.0	0.0	0.0	0.0		0.0
March 27, 2015	0.0	0.0	0.0	0.0		0.0	0.0	0.0	0.0	0.0		0.0
March 28, 2015	4.0	3.0	13.1	9.0		29.1	0.0	0.0	0.0	0.0		0.0
March 29, 2015	4.0	3.0	13.4	9.0		29.4	0.0	0.0	0.0	0.0		0.0
March 30, 2015	4.0	3.0	13.5	7.0		27.5	0.0	0.0	0.0	0.0		0.0
March 31, 2015	4.0	3.0	13.3	7.0		27.3						
<b>Sub Total of March 2015</b>	131.6	130.2	942.7	795.8	0.0	<b>2000.2</b>	0.0	0.0	0.0	0.0	0.0	<b>0.0</b>



**USAID WEST BANK/ GAZA**  
**INFRASTRUCTURE NEEDS PROGRAM**  
**TASK ORDER NO: AID-294-TO-12-00012**  
**Multiple Roads Project (South II)**  
**Geo-MIS DATA COLLECTION SHEET**

CONTRACTOR: APCO/ArCon

PERIOD FROM: March 01, 2015

PERIOD TO: March 31, 2015

DATE	Milling and Overlay of Bethlehem Road					Sub Total I					
	Management	Engineers	Skilled labor	Unskilled labor	Other						
March 1, 2015	0.0	0.0	0.0	0.0		0.0					
March 2, 2015	0.0	0.0	0.0	0.0		0.0					
March 3, 2015	0.0	0.0	0.0	0.0		0.0					
March 4, 2015	0.0	0.0	0.0	0.0		0.0					
March 5, 2015	0.0	0.0	0.0	0.0		0.0					
March 6, 2015	0.0	0.0	0.0	0.0		0.0					
March 7, 2015	0.0	0.0	0.0	0.0		0.0					
March 8, 2015	0.0	0.0	0.0	0.0		0.0					
March 9, 2015	0.0	0.0	0.0	0.0		0.0					
March 10, 2015	0.0	0.0	0.0	0.0		0.0					
March 11, 2015	0.0	0.0	0.0	0.0		0.0					
March 12, 2015	0.0	0.0	0.0	0.0		0.0					
March 13, 2015	0.0	0.0	0.0	0.0		0.0					
March 14, 2015	0.0	0.0	0.0	0.0		0.0					
March 15, 2015	0.0	0.0	0.0	0.0		0.0					
March 16, 2015	0.0	0.0	0.0	0.0		0.0					
March 17, 2015	0.0	0.0	0.0	0.0		0.0					
March 18, 2015	0.0	0.0	0.0	0.0		0.0					
March 19, 2015	0.0	0.0	0.0	0.0		0.0					
March 20, 2015	0.0	0.0	0.0	0.0		0.0					
March 21, 2015	0.0	0.0	0.0	0.0		0.0					
March 22, 2015	0.0	0.0	0.0	0.0		0.0					
March 23, 2015	0.0	0.0	0.0	0.0		0.0					
March 24, 2015	0.0	0.0	0.0	0.0		0.0					
March 25, 2015	0.0	0.0	0.0	0.0		0.0					
March 26, 2015	0.0	0.0	0.0	0.0		0.0					
March 27, 2015	0.0	0.0	0.0	0.0		0.0					
March 28, 2015	0.0	0.0	0.0	0.0		0.0					
March 29, 2015	0.0	0.0	0.0	0.0		0.0					
March 30, 2015	0.0	0.0	0.0	0.0		0.0					
March 31, 2015											
<b>Sub Total of March 2015</b>	0.0	0.0	0.0	0.0	0.0	<b>0.0</b>					

March , 2015	Total Job Days	No of Full Time Equivalent (FTE) Jobs
	2000.2	84.0

## I | RISK REGISTER LOG

## Risk Register Log

PROBABILITY CATEGORIES			
Description		Prob	Scale Value
H	Probable	>70%	3
M	Could happen	30-70%	2
L	Improbable	<30%	1

IMPACT CATEGORIES			
Description		Guide Scenario	Scale Value
H	Critical	Impact that involves significant delay, rework, modification or reassessment.	3
M	Serious	Impact or setback that causes delay, additional work and reassessment but containable.	2
L	Marginal	Impact has some effect causing rework or reassessment but easily handled.	1

		PROBABILITY		
		Low/Improbable	Medium/Could Happen	High/Probable
IMPACT	High/ Critical	1	2	3
	Medium/ Serious	3	6	9
	Low/ Marginal	2	4	6
		1	2	3

	Key/ Critical Risks - closely monitor, manage & develop fallback plans
	Intermediate Risks - monitor and manage to mitigate
	Minor Risks

<b>Risk Event</b>	What is it that you are working to avoid or reduce the likelihood or impact of occurring? Risks are future events that could interfere with achievement of objectives.
<b>Risk Cause</b>	What are the triggers, sources or circumstances that could act alone or together to increase the likelihood of the Risk Event occurring? There are usually multiple causes leading to a Risk Event.
<b>Risk Impact</b>	If this Risk Event did occur, how would it impact objectives? What are the longer-term or cumulative consequences?
<b>Risk Owner</b>	Who will take the lead on this mitigation?

**T.O 12- Risk Register Log**

RISK IDENTIFICATION							RISK ASSESSMENT					RISK RESPONSE			MONITORING & CONTROLLING		
REF	CATEGORY	RISK	RISK CAUSE	IMPACT/ CONSEQUEN	RAISED BY	DATE RAISED	PROBLTY.	IMPACT	RISK RATING	COST IMPACT	SCHEDULE IMPACT	RESPONSE STRATEGY	RESPONSE PLAN	RISK OWNER	STATUS	NOTES	
1	Design	No risks during this reporting period. Project was completed and handed over on time.							0								
2	Construction								0								
3	Owner								0								
4	USAID								0								
5	Contractor								0								
6	External								0								
7	Procurement								0								
8	Skills								0								
9	Complexity								0								
10	Resources								0								
11	Communications								0								
