



USAID | **PAKISTAN**
FROM THE AMERICAN PEOPLE



CONSTRUCTION MONITORING & EVALUATION PROGRAM
(Reconstruction of Flood Damaged Schools in Khyber Pakhtunkhwa)

MONTHLY PROGRESS REPORT # 09
OCTOBER, 2013

Contents

EXECUTIVE SUMMARY	1
1. THE PROJECT	3
1.1. Background	3
1.2. Location	4
1.3. Implementation Arrangements	5
1.4. The M&E Services	5
2. MAJOR ACTIVITIES UNDERTAKEN DURING THE REPORTING MONTH (OCTOBER, 2013)	6
2.1. Physical survey & assessment of new schools	6
2.2. Submission of Site & Layout Plans.....	6
2.3. Submission of Modular Drawings	6
2.4. Submission of Engineer's Estimates	6
2.5. Submission of Quarterly Progress Report.....	6
2.6. Re-Review of 24 schools of PIL-01	6
2.7. Meetings	7
3. OVERALL PROGRESS TILL END OF LAST MONTH (SEPTEMBER 30, 2013)	8
3.1. Mobilization of Staff & Establishment of Office/Residencies	8
3.2. Submission of Final Quality Assurance Plan (QAP)	8
3.3. Validation/Revalidation of Schools (1 st list)	8
3.4. Validation of Alternate Schools (2 nd list)	8
3.5. Pre-construction Survey & Assessment (1 st list)	9
3.6. Pre-construction Survey of Alternate Schools (2 nd list)	9
3.7. Preparation & submission of Site/Layout Plans (1 st List)	9
3.8. Revision & Submission of Revised Modular Drawings.....	9
3.9. Submission of Revised BOQs of all Modules	10
3.10. Submission of Quarterly Progress Reports.....	10

3.11. Meetings	10
3.12. Organization Chart and Staff Deployment.....	14
4. ORGANIZATION CHART WITH KEY STAFF DEPLOYMENT.....	15
5. ITEMS REQUIRING ACTIONS.....	20
Annexure	21
Annexure I = Minutes of Meetings	22
Annexure II = Emails	29

ABBREVIATION

ADP	Annual Development Program
BOQ	Bills of Quantities
CGI	Corrugated Galvanized Iron
C&W	Communication & Works
CO	Contracting Officer
COR	Contracting Officer's Representative
CSR	Composite Schedule Rate
DAE	Diploma of Associate Engineer
EDO	Executive District Officer
EMMP	Environmental Mitigation Measure Protocol
FAR	Fixed Amount Reimbursement
GoP	Government of Pakistan
HCC	Host Country Contracting
ITP	Inspection & Testing Plan
KP	Khyber Pakhtunkhwa
LoE	Level of Effort
M&E	Monitoring & Evaluation
PaRRSA	Provincial Reconstruction, Rehabilitation & Settlement Authority
PIL	Project Implementation Letter
PM	Project Manager
PMU	Project Management Unit
QA	Quality Assurance
QAM (Building)	Quality Assurance Manager (Building)
RA	Reimbursement Agreement
RFP	Request for Proposal
SoW	Scope of Work
TSF	Tons per Square Foot
USAID	United States Agency for International Development

EXECUTIVE SUMMARY

The Province of Khyber Pakhtunkhwa suffered heavy infrastructure damages firstly due to terrorism and militancy and thereafter due to the unprecedented floods of July 2010. United States Agency for International Development (USAID) actively supported the rehabilitation and reconstruction activities of damaged schools, health facilities, drinking water supply schemes and other infrastructure components in Malakand Division by initially obligating funds amounting to USD 36 million under an Activity Agreement (No. 391-011) signed in September, 2009 between USAID and PaRRSA on behalf of GoP. Expanding its portfolio, USAID provided funds for rehabilitation / reconstruction of other infrastructure components including irrigation, bridges and roads etc. in the calamity hit areas.

In June 2012, USAID sub-obligated additional funds amounting to USD 25 million for reconstruction of rains / floods damaged and bomb blasted schools in the affected districts of KP under Amended Activity Agreement No. 391-014. M/s AGES Consultants was assigned the task of Monitoring & Evaluation (M&E) services of these reconstruction activities under USAID/Pakistan Construction Monitoring and Evaluation Program (CMEP), for which a formal contract was signed on September 30, 2012.

The M&E Consultant has completed validation/revalidation of about more than 200 identified schools.

The 1st list of 114 damaged schools was assessed in the month of December 2012 in which 42 school were found suitable/feasible for reconstruction. Site/layout plans & validation report were shared with the stakeholders. A meeting held on May 17th, 2013 in the office of program manager PaRRSA to decide the scope of first PIL, a total of 24 out of 42 schools were agreed to be included in PIL and accordingly drawings & engineer's estimates of the aforesaid schools were prepared, reviewed and finalized. USAID has issued a signed PIL-28 to PaRRSA for further appropriate action.

Further, design for all modules were revised/improved and new modules were introduced in light of lesson learnt from the practice already invogue in Malakand.

A 2nd list of about 21 damaged schools was provided by PaRRSA in which 10 schools were found suitable/feasible for reconstruction. The site/layout plans & validation report of the feasible schools were shared with the stakeholders.

A 3rd list of 161 damaged schools was provided by PaRRSA. This 3rd list was discussed with the concerned EDO's in a meeting held on August 27th, 2013 at Saidu Sharif Swat. In light of the said meeting a revised 3rd list of 150 damaged schools was provided by PaRRSA. The physical survey & assessment of the schools were initiated and 23 schools in District Lower Dir, 29

schools in District Swat, and 11 schools in District D.I Khan have been assessed by the AGES field team in the reporting month. The assessment of the remaining schools is underway.

Physical construction activities will start subject to completion of the requisite prequalification, tendering and contracting formalities by PaRRSA. An implementation arrangement in light of the experience gained and lessons learnt from the Malakand model needs to be developed on priority so as to pursue the project implementation / physical activities without any loss of time.

1. THE PROJECT

1.1. Background

The disaster of 2010 Monsoon Flood in Khyber Pakhtunkhwa (KP) was massive and unprecedented. The flood not only deprived the local communities of their livelihoods but also created an unprotected and challenging environment for the school going children in the flood hit districts of KP.

As per data received from the Education Department of the KP, the numbers of schools either partially or fully damaged ranged in hundreds. The Government of KP was faced with the challenging task of reconstruction and restoration of these lost academic facilities at huge construction costs. Realizing the importance of early resumption of educational activities, the government appealed to national and international donors for funds to rectify and retrieve the situation. In the meantime, the Government of KP, through its concerned line departments, prepared Damage Need Assessments (DNA) of the flood affected districts.

USAID was already working in Malakand Division on the reconstruction and rehabilitation of schools, health facilities and Water & Sanitation (WatSan) infrastructures affected during the militancy period. Contemplating an expansion of its portfolio of projects in KP with regards to flood relief activities, USAID tasked AGES, (the M&E consultants for the USAID funded sub-projects in the Malakand Division) to undertake the additional work of DNA and validation for the partially and fully damaged schools in some of the districts affected by floods.

In September 2012, AGES was assigned the task of monitoring & evaluation services including Quality Assurance and Environmental Monitoring for the reconstruction activities of the damaged schools in the affected districts Khyber Pakhtunkhwa comprising Peshawar, Nowshehra, Charsadda, Malakand, Swat, Dir Upper/Lower, Shangla, DI Khan and Tank.

The project has been tasked with the objective to monitor & certify that all the proposed projects are built as per approved designs/drawings, technical specifications and to ensure environmental compliance as per USAID's and Government of Pakistan's (GoP) regulations and requirements.

1.3. Implementation Arrangements

The Economic Affairs Division (EAD) designated the Director General (DG) of Provincial Reconstruction, Rehabilitation and Settlement Authority (PaRRSA) as an Additional Representative of the Government of Pakistan (GoP) for the purposes of the implementation of Program Areas. The GoKP has established a Project Steering Committee (PSC) to provide oversight, guidance and approvals required for smooth and timely implementation of the activities. The PSC is chaired by DG PaRRSA, and comprised representatives of USAID Pakistan and relevant provincial departments involved in the planning and execution of the activities. Therefore, PaRRSA has the authority to carry out the works to be financed under a Fixed Amount Reimbursement (FAR) Agreement. Accordingly, PaRRSA is fully responsible for carrying out these works through contracting, supervising the contractor(s) and for ensuring that the contractor(s) diligently undertake the work and provide the necessary equipment, skilled and unskilled labor, and efficient supply of materials to ensure uniform and continuous progress once construction has started. A strategy is presently being debated on and under formulation by the participation of all stakeholders to decide/identify an appropriate executing agency to undertake implementation of this project, on behalf of the government of KP. M/s AGES Consultants of Peshawar have been appointed by USAID as Monitoring & Evaluation Consultants for this project.

1.4. The M&E Services

The Contract for M&E Services for the “Construction Monitoring & Evaluation Program” was signed on September 30, 2012. The M&E services comprise the following.

- Submission of Quality Assurance Plan (QAP).
- Validation / Revalidation of the July 2010 flood damage assessment done through AGES for fully damaged schools to the current status.
- Pre-Construction report of each school site to establish base line condition.
- Preparation of site plan as well as layout plans on the basis of pre-construction survey data obtained as a result of site visits.
- Review and Vetting of Project Design Drawings / Documents.
- Verifying the quality of construction/installation works and ensures conformity to the contract construction drawings, standards, technical specifications & requirements
- Site Monitoring and Inspection Reports
- Assisting, advising & reporting to USAID/PaRRSA with regard to reconstruction activities.
- Field and Laboratory Testing
- Monthly & Quarterly Progress Reports

2. MAJOR ACTIVITIES UNDERTAKEN DURING THE REPORTING MONTH (OCTOBER, 2013)

2.1. Physical survey & assessment of new schools

- 22 listed schools and 07 additional schools in District Swat have been physically surveyed and assessed by AGES field team
- 06 listed schools and 05 additional schools in District D.I Khan have been physically surveyed and assessed by AGES field team
- 23 listed schools in District Lower Dir have been physically surveyed and assessed by AGES field team

2.2. Submission of Site & Layout Plans

- Site and layout plans of 17 schools of District Peshawar, Nowshera, Charsadda & Dir Lower were shared with the stakeholders
- Preparation of draft site and layout plans of revised 3rd list assessed during the reporting month & will be shared with the stakeholders shortly for their review & comments.

2.3. Submission of Modular Drawings

Modular Drawings of 17 schools of District Peshawar, Nowshera, Charsadda & Dir Lower were shared with the stakeholders.

2.4. Submission of Engineer's Estimates

Engineer's estimates of 17 schools of District Peshawar, Nowshera, Charsadda & Dir Lower were shared with the stakeholders.

2.5. Submission of Quarterly Progress Report

Fourth Quarterly Progress Report for the quarter ending September 30, 2013 was shared with USAID/PaRRSA for their review and comments on October 9, 2013.

2.6. Re-Review of 24 schools of PIL-01

Engineer's estimates of 24 schools of PIL-01 shared by USAID were re-reviewed and resubmitted.

2.7. Meetings

- A meeting was held on October 28, 2013 in the office of District Education Officer Dir Upper. SDO (M) Dir & Warai Sub Division, ASDO (M) Sheringle & Warai Sub Division, Infrastructure Coordinator PaRRSA Dir Lower & QAM (Building) AGES CMEP attended the meeting. The list provided by PaRRSA was discussed in detail and 09 schools were dropped from the list being repaired/rehabilitated, partially damaged and no arrangement of alternate land. AGES was advised to proceed for physical survey and assessment.
- A meeting was held on October 29, 2013 in the office of District Education Officer Shangla at Alpura. DEO (M/F) Shangla, ADO P&D (M) Shangla, ADO P&D (F) Shangla, Admin Officer Shangla, Senior Clerk DEO Office Shangla, QAM (Building) AGES CMEP, Field Manager AGES CMEP, Junior Architect AGES CMEP, Ex-MPA Shangla attended the meeting. The list provided by PaRRSA was discussed in detail and 03 schools were dropped from the list being no arrangement of alternate land. AGES was advised to proceed for physical survey and assessment.

3. OVERALL PROGRESS TILL END OF LAST MONTH (SEPTEMBER 30, 2013)

3.1. Mobilization of Staff & Establishment of Office/Residencies

- Key staff of AGES was mobilized in September 2012 and preliminary meetings were conducted with the stakeholders for evolving strategy for the implementation of the project.
- Need based logistics have been provided
- Project Office at Peshawar has been established
- Residencies (02) for office as well as field staff have been established

3.2. Submission of Final Quality Assurance Plan (QAP)

QAP was reviewed in light of observations/comments made by USAID & final version shared with the stakeholders on March 13, 2013.

3.3. Validation/Revalidation of Schools (1st list)

- More than 100 schools were Validated/Revalidated till end of December 2012 and revalidation report submitted to the stakeholders during the month of January, 2013.
- Forty two (42) schools out of 114 schools were found suitable during the revalidation process. District wise position is given here under:

○ District D.I.Khan	27 out of 35 schools
○ District Tank	0 out of 02 schools
○ District Peshawar	0 out of 17 schools
○ District Charsadda	0 out of 06 schools
○ District Nowshera	0 out of 01 schools
○ District Swat	02 out of 28 schools
○ District Shangla	08 out of 12 schools
○ District Malakand	03 out of 04 schools
○ District Dir Upper/Lower	02 out of 09 schools
Total	42 out of 114 schools

3.4. Validation of Alternate Schools (2nd list)

- Twenty one (21) schools included in the list provided by USAID/PaRRSA as alternate/replacement schools against unsuitable sites, were validated by AGES during the month of June 2013.

-
- Total of 10 schools were found suitable during the validation process. District wise position is given here under:

○ District Peshawar	05 out of 12 schools
○ District Charsadda	03 out of 06 schools
○ District Nowshera	02 out of 03 schools
Total	10 out of 21 schools

3.5. Pre-construction Survey & Assessment (1st list)

After completion of revalidation process, the pre-construction survey of all 42 suitable sites was conducted and site specific data was collected. The data collected as a result of physical survey & assessment was properly documented and shared with USAID & PaRRSA.

3.6. Pre-construction Survey of Alternate Schools (2nd list)

The physical survey & assessment of 10 suitable schools incorporated in the 2nd list provided by USAID/PaRRSA was conducted by AGES. Site specific data was collected and documentation is in process.

3.7. Preparation & submission of Site/Layout Plans (1st List)

- Site/layout plans of all 42 suitable sites (1st list) as mentioned vide para 3.3 were prepared and finalized on the basis of physical survey & assessment conducted by the AGES team during the month of December, 2012 and were shared with the stakeholder for their information, review & comments along with site specific photographs.

3.8. Revision & Submission of Revised Modular Drawings

- All modules were structurally as well as architecturally revised/modified in accordance with the decisions made in the meetings held on Nov 17, 2012, Dec. 27, 2012, May 17, 2013, May 24, 2013, June 28, 2013 and lessons learnt from M&E Project Malakand and shared with the stakeholders for their comments.
- New modules for M7, M11, M12, M13, LB & LB(H) were also introduced keeping in view the land constraint, site specific condition and requirement of the students etc.
- Double/Triple storey buildings were introduced to provide sufficient accommodation to the students in the limited available area.

3.9. Submission of Revised BOQs of all Modules

The BOQ's of all modules duly revised and modified, were prepared and shared with stakeholder for their review & comments.

3.10. Submission of Quarterly Progress Reports

- First Quarterly Progress report for the quarter ending December 31, 2012 was shared with USAID/PaRRSA for the review and comments.
- Second Quarterly Progress Report for the quarter ending March 31, 2013 was shared with USAID/PaRRSA for their review & comments on April 04, 2013.
- Third Quarterly Progress Report for the quarter ending June 30, 2013 was shared with USAID/PaRRSA for their review & comments on July 08, 2013.

3.11. Meetings

1. A meeting was held in the office of PaRRSA on 24-09-2012. All the stakeholders i.e USAID, PaRRSA and AGES participated in the proceedings. Main purpose of the meeting was to evolve strategy for the way forward for implementation of the reconstruction of flood damaged schools based on the findings of the validation and damaged assessment report prepared by AGES in Year 2010.
2. A meeting was held in the Main office of AGES on 17-11-2012. Chief Infrastructure PaRRSA, Project Manager CMEP AGES, Quality Assurance Manager CMEP AGES, Partners AGES and Field Engineers AGES attended the Meeting. The purpose of meeting was to review the previous minutes of meeting and share the validation/revalidation reports prepared by AGES and to evolve further strategy for the revalidation of schools in the rest of the Districts.
3. A meeting was held in the Main Office of AGES on 27-12-2012. All the Stakeholders i.e USAID, PaRRSA and AGES participated in the meeting. The main purpose of the meeting was to review the previous minutes of meeting and share the validation/revalidation of all Districts covered under the CMEP KP.
4. Meetings were held on 15-10-2012 & 17-10-2012 in the office of EDO District Shangla. EDO & ADO District Shangla, Field Manager AGES & Field Monitor AGES attended the meeting. The purpose of meeting was to chalk out visit program needed for the revalidation of schools in District Shangla.
5. A meeting was held in the office of DTL M&E Malakand at Mingora. The M & E Engineers of M&E Project who were involved in the validation process in Year 2010 participated in the meeting beside the QAM(B) CMEP AGES, coordinator Swiss

Agency for Development and Cooperation and Field Monitor AGES. The purpose of meeting was to identify the suitable and unsuitable sites in light of survey done in year 2010.

6. A meeting was held in the office of M&E Dir at Timergara. Infrastructure Coordinator PaRRSA, Coordination Engineer M&E Dir, M&E Engineer Dir, Site Engineers M&E Dir, QAM Building CMEP AGES and Field Monitor CMEP AGES attended the meeting. The purpose of the meeting was to discuss the validation reports with the respective site engineers of M&E Dir who were involved in the validation process done in Year 2010. The suitable/unsuitable sites were identified in light of their reports.
7. A meeting was held in the Office of EDO District Malakand on 29-11-2012. EDO & ADO District Malakand, QAM(B) CMEP AGES & Field Monitor attended the meeting. The purpose of the meeting was to chalk out program for the visits of the suitable sites as pointed out by EDO Malakand.
8. A meeting was held on 05-12-2012 in the office of EDO D.I.Khan. All DDOs of the respective Tehsils, QAM (B) CMEP AGES, Field Manager and Field Monitor CMEP attended the meeting. The schools having land issues were identified and program was chalked out for the visits of suitable sites. The DDOs of the respective Tehsils were also involved in the revalidation process.
9. Introductory meeting with Country Director USAID Pakistan was held on April 17, 2013 in Islamabad.
10. A meeting was held on 17-05-2013 in the office of Programme Manager PaRRSA. Program Manager PaRRSA, Chief Infrastructure PaRRSA, Programme Manager USAID for KP, Engineer USAID, Team leader M&E AGES, CPO PaRRSA, SPO Education Department, DEO DI Khan, QAM (Building) CMEP AGES, Mid Level Specialist AGES, Field Manager AGES & Office Engineer AGES attended the meeting.

It was decided and agreed in the meeting that 24 out of 42 feasible sites/schools as re-validated & assessed by AGES shall be tagged as priority-1 having comparatively high enrollment & high future potential and will be included in PIL-1. Other issues pertaining to the project were also discussed in the meeting and decisions made accordingly.

11. A meeting was held on 24-05-2013 in the Project office CMEP Peshawar to discuss Layout Plans, modular drawings and cost estimates for PIL No.01. Chief Infrastructure PaRRSA, Partner AGES, QAM (Building) CMEP AGES, Mid Level

Specialist AGES, Field Manager AGES & Office Engineer AGES attended the meeting. Some technical modifications/changes were suggested and agreed to be incorporated in the BOQs, Architectural and Structural Drawings keeping in view the lesson learnt from M&E project

12. A meeting with Engineer USAID and Chief Infrastructure PaRRSA was held on 28-06-2013 to review & finalize the BOQ's and drawings of 24 schools selected for PIL-01
13. A meeting was held with USAID & PaRRSA in PaRRSA Secretariat Peshawar on 28-06-2013 and discussed the flood/militancy school implementation strategy and progress of school under KPRP.
14. A meeting was held on July 22, 2013 in the office of Program Manager PaRRSA. Program Manager PaRRSA, Chief Infrastructure PaRRSA, Engineer USAID, Chief Planning Officer PaRRSA, Planning Officer PaRRSA, Senior Engineer PaRRSA, QAM(Building) CMEP AGES, Mid Level Specialist AGES and Field Manager AGES attended the meeting.

Main purpose of the meeting was firstly to review the draft validation report of alternate schools submitted by AGES and secondly to get fresh list of alternate schools for physical survey and assessment.

15. A meeting was held on August 20, 2013 in the office of DEO Swabi. ADO (Male) Swabi, ADO (Female) Swabi, Field Manager (Building) CMEP and Junior Engineer CMEP attended the meeting. The (03) three listed schools were discussed & reviewed in detail before going for physical survey & assessment of the schools. Both ADOs accompanied the survey team during the validation process.
16. A meeting was held on August 26, 2013 in the office of DEO Malakand at Batkhela. Mr. Abdullah DEO(M) Malakand, Mr. Ruidar Ali QAM(Building) CMEP, Mr. Fazal Ahad Dy:DEO(M) Malakand, Mr. Fazli Subhan ADO(P&D) Malakand & Mr. Iftikhar Alam Office Engineer AGES attended the meeting. The list provided by PaRRSA was discussed in detail and all the listed schools were found suitable for physical survey & assessment. A survey team comprising of AGES Engineers & ADO (P&D) were advised to proceed for physical survey & assessment forthwith.
17. A meeting was held on August 26, 2013 in the office of DEO Lower Dir at Timergara. Mr. Shabir Ahmad Dy: DEO (E&SE) Dir Lower, Mr. Muhammad Aslam ADO (P&D) Dir Lower, Mr. Muhammad Tahir ADO(P&D) Dir Upper, Mr. Jehandar Shah ADO(P&D)F Dir Lower, Mr. Shahid Jan Infrastructure Coordinator PaRRSA & Mr. Ruidar Ali QAM(Building) CMEP attended the meeting. The list provided by PaRRSA


was discussed in detail and six (06) schools were dropped from the list being Pledged/Reconstructed by other Donor agencies or through Government ADP. AGES was given a green signal to go ahead for the physical survey & assessment of the balance seven (07) listed schools as provided by PaRRSA (Annexure-I).

18. A meeting was held on August 27, 2013 in the office of DTL M&E Swat at Saidu Sharif Swat. Mr. Shakeel Iqbal PM PaRRSA, Mr. Aurang Zeb ADO(P&D) Shangla, Mr. Akhter Naeem ADO P&D(F) Shangla, Mr. Said Rahman SPO PMU PaRRSA, Mr. Sajjad Ahmad Infrastructure Coordinator PaRRSA, Mr. Ruidar Ali QAM(Building) CMEP, Dilshad Begum DEO(F) Swat, Mr. Abdul Aziz Shaheen ADO P&D(F) Swat, Mr. Sultan Mehmood DEO(M) Swat & Mr. Muhammad Azim ADO P&D Swat attended the meeting. The list provided by PaRRSA was discussed & reviewed in detail. Some schools were dropped due to inaccessibility, some were not functional for the last 8 to 9 years (according to DEO Female), some were already Pledged/Reconstructed by other donors or through Government ADP, and some have no land being washed away due to floods July, 2010. It was decided that a final list will be submitted to PaRRSA having all informations as discussed in the meeting for physical survey & assessment (Annexure-I).
19. A meeting was held on August 28, 2013 in the office of DEO Dir Upper at Dir. Mr. Shahid Jan Infrastructure Coordinator PaRRSA, Mr. Ruidar Ali QAM(Building) CMEP & Mr. Farmanullah Representative of DEO(M&F) Dir Upper attended the meeting. The list provided by PaRRSA was discussed & reviewed in detail. Five (05) schools mentioned in the list were dropped due to having no land being washed away during the floods July 2010; two (02) schools were already Pledged/Re-constructed by other donor agencies. It was decided that a final list in light of decision made in the meeting held on August 27, 2013 with the Program Manager PaRRSA at Saidu Sharif Swat will be submitted to PaRRSA for physical survey & assessment. AGES survey team will proceed for physical survey & assessment as and when the consolidated list of schools is received from PaRRSA (Annexure-I).
20. A meeting was held on September 17, 2013 in the Project Office of CMEP Peshawar, to discuss validation report of 12 alternate sites of district Nowshera, Swabi & Kohat and actual site specific BOQ's of 24 schools of PIL-01. Chief Infrastructure PaRRSA, QAM(Building) CMEP AGES, Mid Level Specialist AGES, Field Manager AGES, Office Engineer AGES and Quantity Surveyor AGES attended the meeting.

3.12. Organization Chart and Staff Deployment

The M&E Consultants organization chart and staff deployment is presented in the next section.

4. ORGANIZATION CHART WITH KEY STAFF DEPLOYMENT

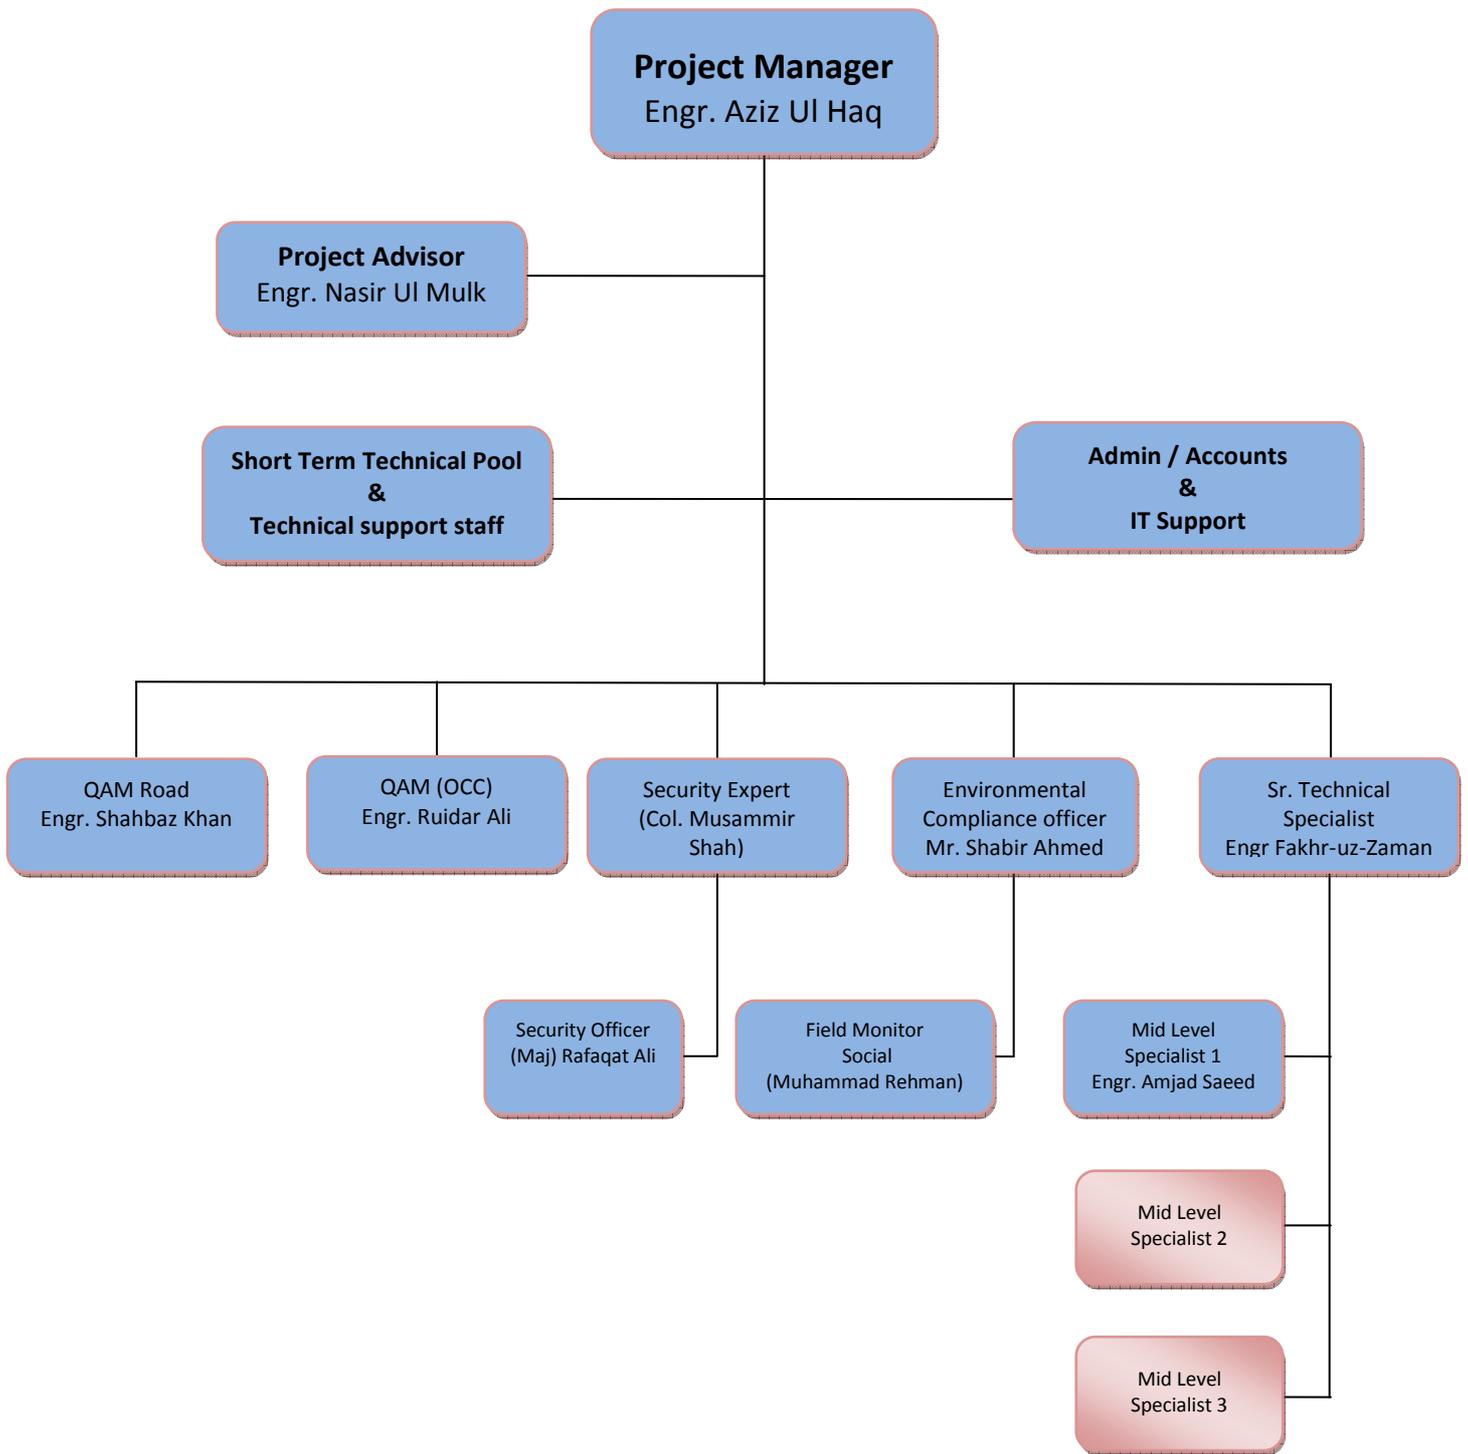

LEGEND:



Mobilized



To be mobilized with expansion of work

PROJECT MANAGER OFFICE – STAFF DEPLOYMENT

S.No.	Name	Designation	
1	Aziz-ul-Haq	Project Manager	ROAD COMPONENT
2	Fakhr uz Zaman	Senior Technical Specialist	
3	Shabir Ahmad Khan	Environmental Compliance Officer	
4	Amjad Saeed	Mid-Level Specialist	
5	Saqib Maqbool	Junior Engineer	
6	Arshad Khan	CAD Operator	
7	Sohail Anjum	Senior Surveyor	
8	Abdul Waheed	Manager Admin/Finance	
9	Amir Habib	IT Officer	
10	Muhammad Bilal	Assistant Accountant	
11	Faizan Khan	Computer Operator	
12	Muhamamd Rehman	Field Monitor Social	OTHER CONSTRUCTION COMPONENT
13	Anwar Dad	Quantity Surveyor	
14	Waqar ul Mulk	Junior Architect	
15	Naeem Jan	Senior Surveyor	
16	Muhammad Waqas	Survey Assistant	
17	Muhammad Ayaz	Survey Assistant	
18	Muhammad Zeeshan Atta	Survey Assistant	
19	Sana ullah	Accountant	

QUALITY ASSURANCE MANAGER OFFICE (Other Construction Component)

S.No.	Name	Designation
1	Ruidar Ali	QAM (OCC)
2	Muhammad Humayun	Field Manager M&E
3	Iftikhar Alam Khan	Office Engineer
4	Fida Ullah	Computer Operator

**Figure 4.1: TEAM COMPOSITION-BUILDING COMPONENTS
USAID/PAKISTAN CONSTRUCTION MONITORING AND EVALUATION PROGRAM**



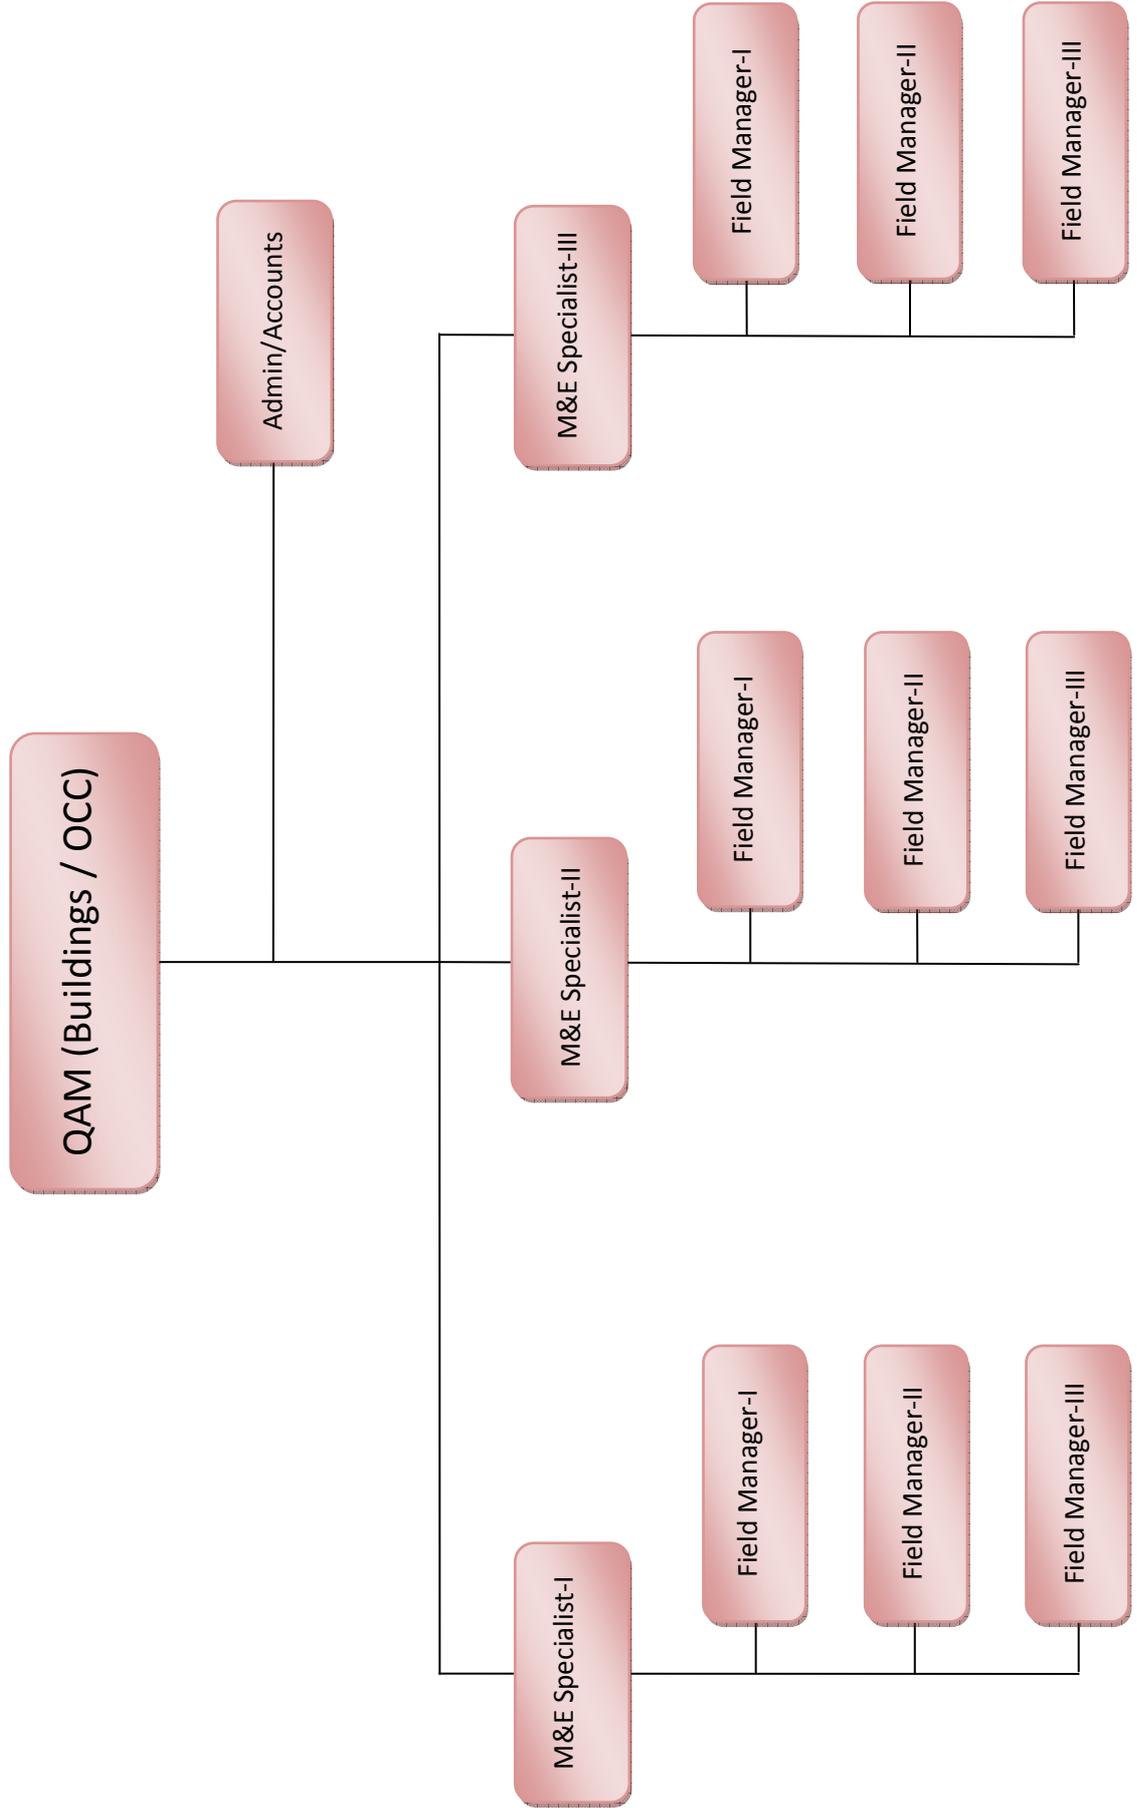


Figure 4.2: TEAM COMPOSITION-BUILDING COMPONENTS
USAID/PAKISTAN CONSTRUCTION MONITORING AND EVALUATION PROGRAM



**Figure 4.3: TYPICAL M&E SETUP –BUILDINGS
USAID/PAKISTAN CONSTRUCTION MONITORING AND EVALUATION PROGRAM**

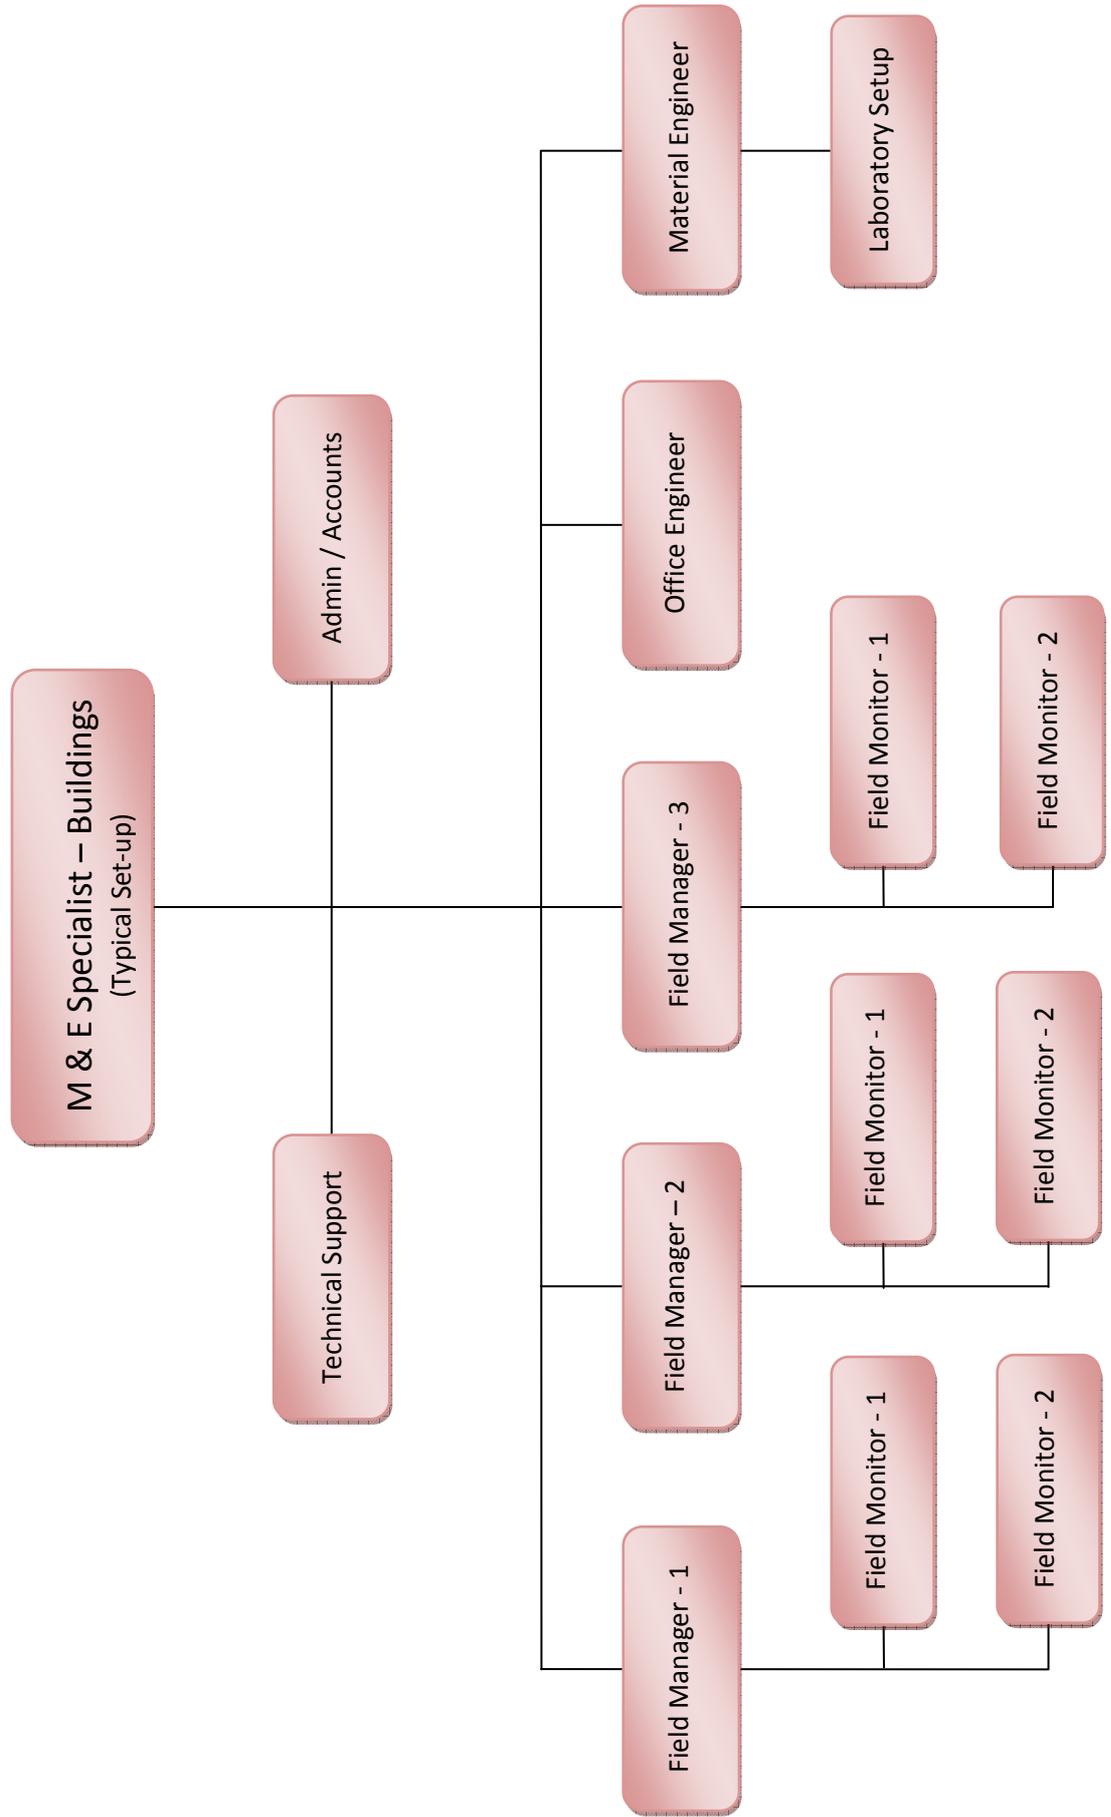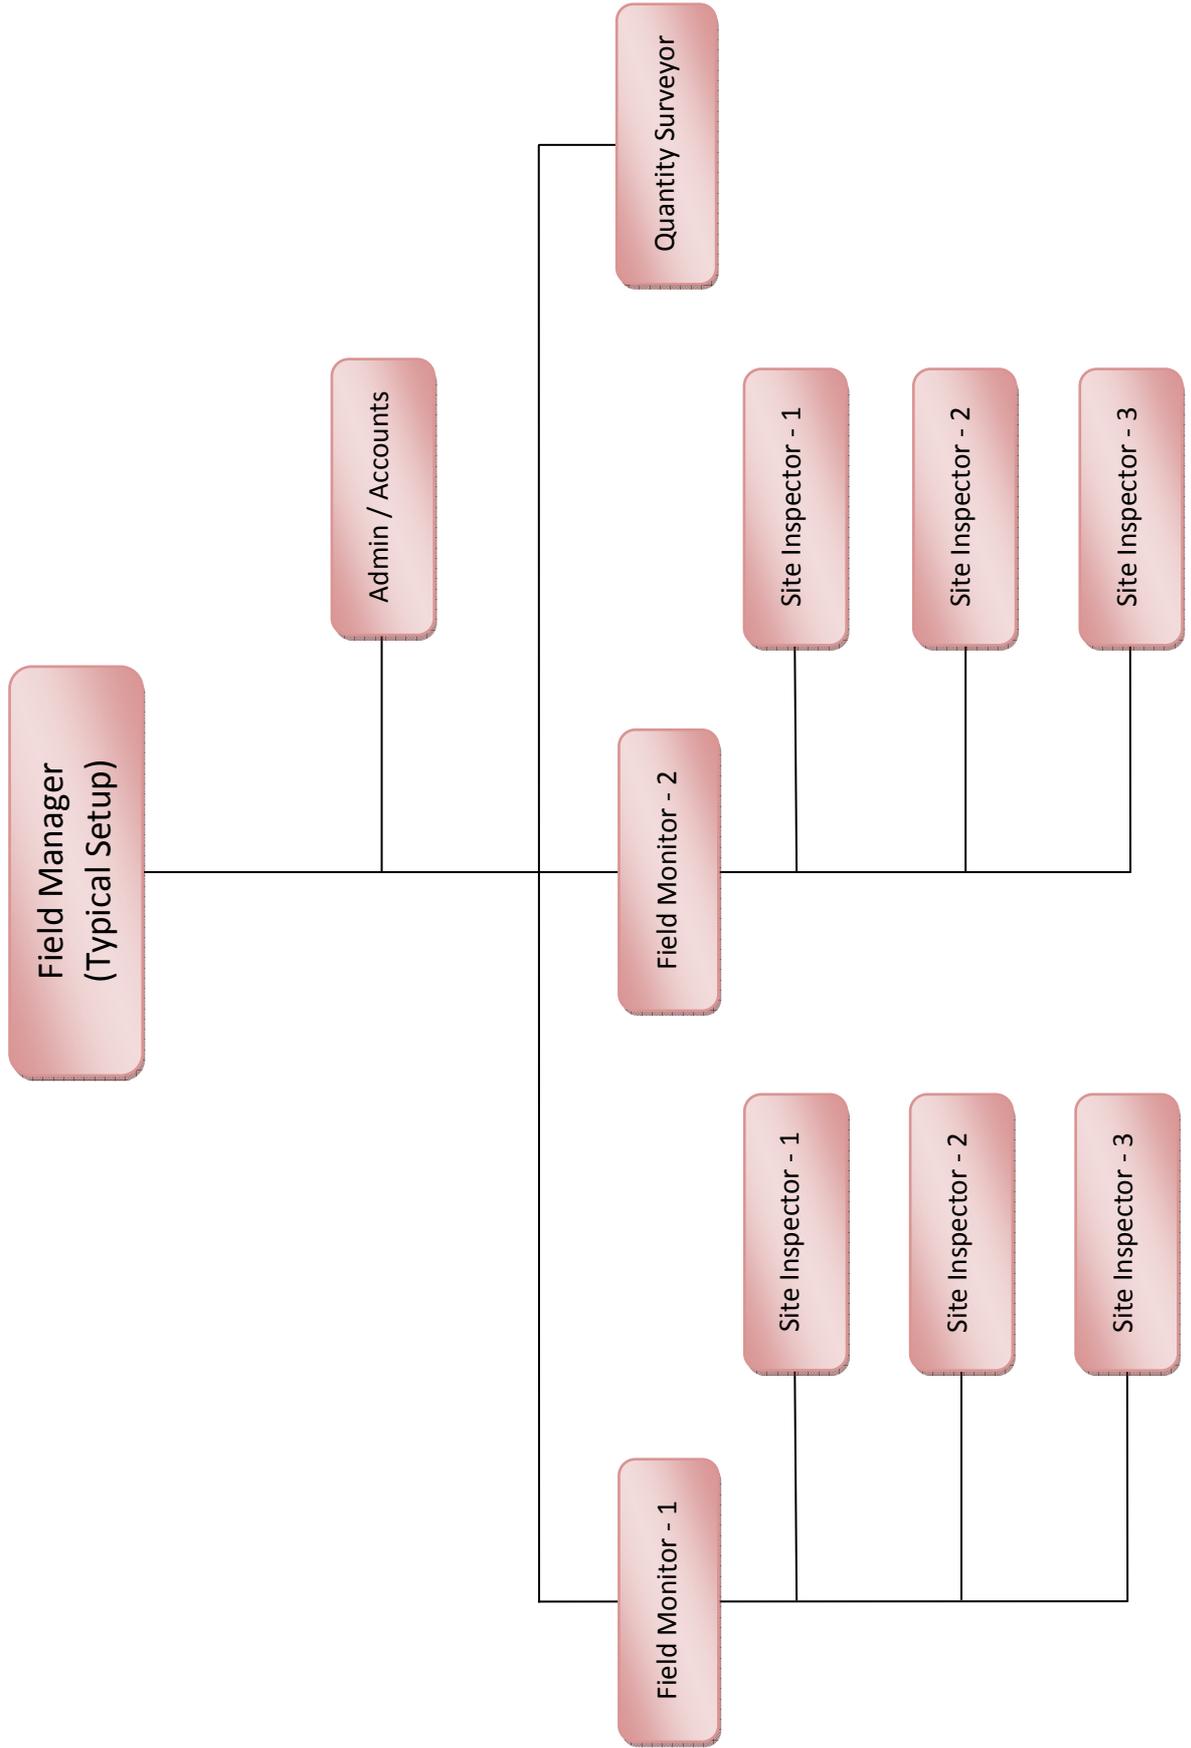

5. ITEMS REQUIRING ACTIONS

As stated in the Executive Summary, urgent action/decision of the concerned forums is required on the following points.

1. Formulation of a strategy for implementation of the schools construction needs to be finalized at the earliest.

ANNEXURES

ANNEXURE-I

(Minutes of Meetings)

**MINUTES OF MEETING HELD ON OCTOBER
28, 2013 IN THE OFFICE OF DEO, DIR UPPER**

MINUTES OF THE PRE-ASSESSMENT MEETING HELD ON OCTOBER 28, 2013
AT THE OFFICE OF DISTRICT EDUCATION OFFICER (E&SE), DIR UPPER

The subject meeting was held prior to the start of physical survey & assessment of flood & militancy damaged schools at District Dir Upper.

The meeting was attended by the following.

- Sub Divisional Officers (M) of Education Department for Dir & Warai Sub Divisions
- Assistant Sub Divisional Officers (M) of Education Department for Sheringle & Warai Sub Divisions
- Infrastructure Coordinator, PaRRSA/C&W, Dir Lower
- Quality Assurance Manager (Buildings), AGES, CMEP

Quality Assurance Manager (Buildings), AGES, CMEP briefed the participants of the meeting that physical survey & assessment of flood & militancy damaged schools provided in the lists by District Education Officer, Dir Upper will be started this week. He further informed that the schools with the following status will not be assessed.

1. Those schools whose lands have been washed away & alternate land has not been arranged for it till date.
2. Partially damaged schools
3. Schools repair/rehabilitated by Pak Army

The concerned sub divisional officers told to the meeting that the following are the schools with the status that its land has been washed away & alternate land has not been arranged for it till date.

S.No	Name of School
1	GHS Bari Kot
2	GMS Bisho
3	GPS Paingas
4	GPS Remin kass

The concerned sub divisional officers told to the meeting the following schools has been repair/rehabilitated by Pak Army.

S.No	Name of School
1	GPS Shaltalo
2	GPS Sunnai
3	GPS Kunai
4	GPS Sro Kalai

The concerned sub divisional officers told to the meeting the following school is partially damaged school.

S.No	Name of School
1	GPS Achar

The meeting agreed that physical survey & assessment of flood & militancy damaged schools at District Dir Upper will be started from Sheringle Sub Division & Assistant Sub Divisional Officer (M) of Education Department for Sheringle will accompany the survey team.

✚ **Compiled by Infrastructure Coordinator, PaRRSA/C&W, Dir Lower**



Meeting in the office of EDO Dir Upper dated: 28 October 2013



Meeting in the office of EDO Dir Upper dated: 28 October 2013

**MINUTES OF THE PRE-AASSESSMENT
MEETING HELD ON OCTOBER 29, 2013
IN THE OFFICE OF DISTRICT EDUCATION
OFFICER, SHANGLA**

MINUTES OF THE PRE-AASSESSMENT MEETING HELD ON OCTOBER 29,
2013

AT THE OFFICE OF DISTRICT EDUCATION OFFICER, SHANGLA

The subject meeting was held prior to the start of physical survey & assessment of flood & militancy damaged schools at District Shangla. The meeting was attended by the following.

- DEO (M/F) Shangla
- ADO P&D (M) Shangla
- ADO P&D (F) Shangla
- Admin Officer (Education) Shangla
- Senior Clerk, DEO office, Shangla
- QAM (Building) AGES CMEP
- Field Manager AGES CMEP
- Junior Architect AGES CMEP
- Ex-MPA Shangla

Quality Assurance Manager (Buildings), AGES, CMEP briefed the participants of the meeting about the criteria of validation process and commencement of physical survey & assessment of flood & militancy damaged schools, will be started this week. He further informed that the schools with the following status will not be assessed.

1. Those schools whose lands have been washed away & alternate land has not been arranged for it till date.
2. Partially damaged schools
3. Schools repair/rehabilitated by other organizations

The participants were informed that the following schools do not fulfill the criteria as their lands have been washed away & no arrangement for alternate land has been made so far.

S.No	Name of School
1	GHS Damorai
2	GGPS Damorai
3	GGMS Damorai

The meeting agreed that physical survey & assessment of flood & militancy damaged schools at

District Shangla will be started & a representative of education department will accompany the AGES field team during the validation process.



Meeting in the office of EDO Shangla dated: 29 October 2013



Meeting in the office of EDO Shangla dated: 29 October 2013

ANNEXURE-II

(E-Mails)

S.No	From	To	Date	Subject
1	QAM (Building) AGES	Chief Infrastructure PaRRSA	October 1, 2013	Final MOM held on Sept. 17, 2013 in CMEP office Peshawar
2	QAM (Building) AGES	Engineer USAID	October 9, 2013	Quarterly Progress Report ending on September 30, 2013 for CMEP Building Component KP.
3	QAM (Building) AGES	Chief Infrastructure PaRRSA	October 12, 2013	Engineer's estimates for 17 No. schools of Districts Peshawar, Charsadda, Nowshera & Dir Lower for expected PIL-2
4	QAM (Building) AGES	Chief Planning Officer PaRRSA	October 23/24, 2013	Tentative visit schedule for physical survey & assessment of schools of District Dir Upper and Shangla, CMEP KP
5	QAM (Building) AGES	Engineer USAID	October 27, 2013	Review of Estimates of 24 schools for PIL-1 CMEP KP
6	QAM (Building) AGES	Engineer USAID	October 31, 2013	Minutes Of The Meeting Held On October 28, 2013 At The Office Of DEO, Dir Upper
7	Engineer USAID	QAM (Building) AGES	October 31, 2013	PIL for 24 flood damaged schools signed by USAID

Email	From	To	Date	Subject
1	QAM (Building) AGES	Chief Infrastructure PaRRSA	October 1, 2013	Final MOM held on Sept. 17, 2013 in CMEP office Peshawar

Subject:	Final MOM held on Sept. 17, 2013 in CMEP office Peshawar
From:	Ruidar ali (ruidarali@hotmail.com)
To:	tahirkamran@pdma.gov.pk; tahirkamran70@yahoo.com;
Cc:	fbanori@usaid.gov; bahrobar@usaid.gov; bahrobar@gmail.com; naseerages@yahoo.com; naseermkhan@hotmail.com; azizages@gmail.com; engineeramjadsaeed@hotmail.com;
Date:	Tuesday, October 1, 2013 3:11 PM

Dear Tahir Kamran sahib,
The final MOM held on Sept. 17, 2013 are attached for your information & record.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Tue, 1 Oct 2013 14:46:17 +0500
Subject: Re: Draft MOM held on Sept. 17, 2013 in CMEP office Peshawar
From: tahirkamran@pdma.gov.pk
To: ruidarali@hotmail.com
CC: tahirkamran70@yahoo.com; azizages@gmail.com;
engineeramjadsaeed@hotmail.com

Kindly download the amended minutes for circulation and official record.

On Tue, Oct 1, 2013 at 10:05 AM, Ruidar ali <ruidarali@hotmail.com> wrote:
Dear Tahir Kamran sahib,
As desired, the draft MOM held on Sept. 17, 2013 are attached for review at your end.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Best Regards

Engr. Tahir Kamran Marwat

Chief Infrastructure,

Provincial Reconstruction, Rehabilitation & Settlement Authority (PaRRSA)

Civil Secretariat, Peshawar.

Mobile#. +92 (0) 333 9152288

Office #. +92 (91) 9213250/ 9213867

Fax #. +92 (91) 9212167

Email	From	To	Date	Subject
2	QAM (Building) AGES	Engineer USAID	October 9, 2013	Quarterly Progress Report ending on September 30, 2013 for CMEP Building Component KP.

Subject:	Quarterly Progress Report ending on September 30, 2013 for CMEP Building Component KP.
From:	Ruidar ali (ruidarali@hotmail.com)
To:	bahrobar@usaid.gov; bahrobar@gmail.com;
Cc:	fbanori@usaid.gov; tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk; naseerages@yahoo.com; naseermkhan@hotmail.com; azizages@gmail.com; engineeramjadsaeed@hotmail.com;
Date:	Wednesday, October 9, 2013 3:37 PM

Dear Bahrobar sahib,

As desired, we are pleased to submit herewith the Quarterly Progress Report ending on September 30, 2013 for CMEP Building Component KP, for review & further appropriate action at your end.

kindly note that we have bifurcated the document into the following two sections in order to be shared on email easily.

- 1, Quarterly Progress Report,
- 2, Annexures (I, II, III & IV).

Hope this will meet your requirements.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Email	From	To	Date	Subject
3	QAM (Building) AGES	Chief Infrastructure PaRRSA	October 12, 2013	Engineer's estimates for 17 No. schools of Districts Peshawar, Charsadda, Nowshera & Dir Lower for expected PIL-2

From: ruidarali@hotmail.com
To: tahirkamran@pdma.gov.pk; tahirkamran70@yahoo.com
CC: naseermkhan@hotmail.com; naseerages@yahoo.com; azizages@gmail.com;
engineeramjadsaeed@hotmail.com
Subject: RE: Engineer's estimates for 17 No.schools of Districts Peshawar, Charsadda,
Nowshera & Dir Lower for expected PIL-2
Date: Sat, 12 Oct 2013 09:54:04 +0500

Dear Tahir Kamran sahib,
As desired, the engineer's estimates based on MRS 2013 of 17 No. schools for the
expected PIL-2 are attached for review & onward submission to the concerned quarter.
District Wise position is given here under;

- District Peshawar----- 05
- District Charsadda----- 03
- District Nowshera----- 02
- District Dir Lower----- 07

kindly note that the final drawings including site/layout plans and modular drawings of all 17
schools are being delivered at your home through special messenger as the same could not be sent
through email due to its large volume.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Thu, 26 Sep 2013 08:33:41 +0500
Subject: Re: Engineer's estimates for 10 No.schools of Districts Peshawar, Charsadda &
Nowshera for expected PIL-2
From: tahirkamran@pdma.gov.pk
To: ruidarali@hotmail.com
CC: tahirkamran70@yahoo.com; naseermkhan@hotmail.com; naseerages@yahoo.com;
azizages@gmail.com; engineeramjadsaeed@hotmail.com

Dear Ruidar Ali sb

Kindly update the estimates as per new market rates approved by Finance department
with nomenclature as "MRS 2013"

On Wed, Sep 25, 2013 at 10:39 AM, Ruidar ali <ruidarali@hotmail.com> wrote:

Dear Tahir Kamran sahib,

As desired, the engineer's estimates of 10 No. schools for the expected PIL-2 are attached for review & onward submission to the concerned quarter. kindly note that the site/layout plans & validation report of all schools(10 No.) have already been discussed & agreed by the stakeholders.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Best Regards

Engr. Tahir Kamran Marwat

Chief Infrastructure,

**Provincial Reconstruction, Rehabilitation & Settlement Authority (PaRRSA)
Civil Secretariat, Peshawar.**

Mobile#. +92 (0) 333 9152288

Office #. +92 (91) 9213250/ 9213867

Fax #. +92 (91) 9212167

Email	From	To	Date	Subject
4	QAM (Building) AGES	Chief Planning Officer PaRRSA	October 23/24, 2013	Tentative visit schedule for physical survey & assessment of schools of District Dir Upper and Shangla, CMEP KP

From: ruidarali@hotmail.com
To: planning_mkd@hotmail.com; parrsa.timergara@yahoo.com;
waseemkundi@gmail.com; pm-parrsa@pdma.gov.pk
CC: azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com;
m.humayun.k@gmail.com; alam.iftikhar@yahoo.com
Subject: RE: Tentative visit schedule for physical survey & assessment of schools of
District Dir Upper and Shangla, CMEP KP.
Date: Thu, 24 Oct 2013 08:53:37 +0500

Dear Said Rahman and Shahid Jan sahib,

Many thanks for continuous cooperation & support.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

From: planning_mkd@hotmail.com
To: parrsa.timergara@yahoo.com; ruidarali@hotmail.com; waseemkundi@gmail.com;
pm-parrsa@pdma.gov.pk
Subject: RE: Tentative visit schedule for physical survey & assessment of schools of
District Dir Upper and Shangla, CMEP KP.
Date: Wed, 23 Oct 2013 10:33:56 +0000

Asalam-o-Alaikum

Dear Shahid Jan,
Infra Coordinator, PaRRSA Dir Lower

This office really appreciates your prompt and timely coordination and facilitation regarding assessment and survey for damaged schools.

SAID RAHMAN,
*SENIOR PLANNING OFFICER,
PMU/PaRRSA, Swat.
Contacts:
Office # 0092+946-725035
Fax: 0092+946-725035
Cell: 0092+0345-9454111*

Date: Wed, 23 Oct 2013 02:21:25 -0700
From: parrsa.timergara@yahoo.com
Subject: Re: Tentative visit schedule for physical survey & assessment of schools of District Dir Upper and Shangla, CMEP KP.
To: ruidarali@hotmail.com; waseemkundi@gmail.com; pm-parrsa@pdma.gov.pk
CC: bahrobar@usaid.gov; bahrobar@gmail.com; azizages@gmail.com; cmep@ages.com.pk; m.humayun.k@gmail.com; alam.iftikhar@yahoo.com; planning_mkd@hotmail.com; planning_cell@hotmail.com; emraan_btk@hotmail.com

Dear Ruidar Saheb,

Salam,

District Education Officer (M), Upper Dir was contacted telephonically today. I briefed him that a meeting will be held at his office on 28-10-2013 prior to the start of physical survey & assessment of schools at District Dir Upper.

He assured me that all the arrangements will be made for the said meeting as desired.

Engr. Shahid Jan

On Wednesday, October 23, 2013 11:51 AM, Ruidar ali <ruidarali@hotmail.com> wrote:

Dear Waseem sahib,

Many thanks for prompt response & continuous cooperation. It would be more appropriate if the list of more schools(if available) of districts Dir upper & Shangla is shared at this stage so that we may go for validation as the AGES teams will be availbale there next week.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Wed, 23 Oct 2013 11:03:50 +0500
Subject: Re: Tentative visit schedule for physical survey & assessment of schools of District Dir Upper and Shangla, CMEP KP.
From: waseemkundi@gmail.com
To: ruidarali@hotmail.com; pm-parrsa@pdma.gov.pk
CC: bahrobar@usaid.gov; bahrobar@gmail.com; azizages@gmail.com; cmep@ages.com.pk; m.humayun.k@gmail.com; alam.iftikhar@yahoo.com; planning_mkd@hotmail.com; planning_cell@hotmail.com; emraan_btk@hotmail.com; parrsa.timergara@yahoo.com

Dear Ruidar Khan

I am glad that AGES has completed validation of schools in 4 districts and we are waiting for the final outcome, which will tell us about the schools to be included in the upcoming PILs. It is to inform that PaRRSA has some more schools to share with AGES, however we are waiting for the final report. I would request PaRRSA staff to facilitate your team as usual.

On Wed, Oct 23, 2013 at 10:39 AM, Ruidar ali<ruidarali@hotmail.com> wrote:

Dear Waseem Kundi sahib,
we are pleased to inform you that we have completed validation of flood/militancy damaged schools of Districts Malakand, Dir Lower, Swat and D.I Khan according to the 3rd list provided by PaRRSA through USAID. The validation report is under preparation & would be shared shortly. The validation of schools in District Dir Upper and District Shangla would be initiated w.e.f Monday, October 28, 2013. Before starting the physical survey & assessment, we would like to have meetings with the respective DEOs/EDOs/ADOs to chalk out the strategy for the way forward. Tentative meeting & visit schedule is planned as below;

- Meeting with EDO District Dir Upper-----> Monday, October 28, 2013 at 02 PM in the office of EDO
Dir Upper at Dir.
- Physical survey/assessment of schools in District Dir Upper by AGES team.....
Tuesday, October 29, 2013 onward.
- Meeting with EDO District Shangla-----> Tuesday, October 29, 2013 at 12 PM in EDO office at Alpuri.
- Physical survey & assessment of schools in District Shangla by AGES
Team.....Wednesday, October 30, 2013 onward.

we would appreciate & welcome if the PaRRSA representatives are accompanied with AGES team during the process of physical survey & assessment.

Dear Shahid Jan sahib, as discussed on telephone, we would appreciate & enjoy your company during the process of validation/physical survey of Dir Upper.

Dear Said Rahman sahib, kindly help in the process of validation/physical survey as usual.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Email	From	To	Date	Subject
5	QAM (Building) AGES	Engineer USAID	October 27, 2013	Review of Estimates of 24 schools for PIL- 1 CMEP KP

Subject:	FW: Review of Estimates of 24 schools for PIL-1 CMEP KP
From:	Ruidar ali (ruidarali@hotmail.com)
To:	bahrobar@usaid.gov; bahrobar@gmail.com;
Cc:	azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com;
Date:	Sunday, October 27, 2013 9:11 PM

Dear Bahrobar sahib,
As desired, the Estimates of 24 schools of PIL-1 have been reviewed and are attached for onward process at your end. The changes made during the review process are tabulated as below;

S.No	School Name	Description	District	Change		Remarks
				From	To	
1	GPS Hisar Baba	Scope of work	Malakand	6 Classrooms	6 Classrooms	Since no Laboratory is proposed in the respective schools therefore the word "Laboratory is deleted from the scope
2	GPS Bazargay			& Labatory +	+ Lav Block	
3	GPS Babagano Sar Agra			Lav Block & Dev: Works	& Dev: Works	
4	GHS Rahatkot	Scope of work	Swat	11 Classrooms, Admin Block, Examination Hall, Library, Laboratory, Lav Block & Dev: Works	10 Classrooms, Admin Block, Examination Hall, Library, Laboratory, Lav Blocks & Dev: Works	The proposed No of CR's are 10. The proposed modules in the school are M3, M6, M11. There are 6 CR's in M3 module, 2 CR's in M6 module & 2 CR's in M11 module, making a total of 10 CR's.
5	GHS Rahatkot	Capital Cost	Swat	Rs. 43.8092 Million	Rs. 43.8521 Million	The cost of mosaic roof treatment was found missing in the abstract of cost of LB only, which has been corrected. The cost of Lavatory Block in the head "LB only" is increased from Rs. 1,678,225/- to Rs. 1,717,735/- and accordingly the capital cost of school is increased from Rs. 43.8092 million to Rs. 43.8521 million. The

						total cost of Swat is increased from Rs. 57.1113 million to Rs. 57.1542 million.
6	GHS Mian Brangola	Scope of work	Dir Lower	13 Classrooms, Admin Block, Examination Hall, Library, Laboratory, Lav Block & Dev: Works	12 Classrooms, Admin Block, Examination Hall, Library, Laboratory, Lav Blocks & Dev: Works	The proposed No of CR's are 12. The proposed modules in the school are M4, M4, M6, M11. There are 8 CR's in two M4 modules, 2 CR's in M6 module & 2 CR's in M11 module, making a total of 12 CR's.
7	GHS Mian Brangola	Capital Cost	Dir Lower	Rs. 50.5641 Million	Rs. 50.6069 Million	The cost of mosaic roof treatment was found missing in the abstract of cost of LB only, which has been corrected. The cost of Lavatory Block in the "LB only" is increased from Rs. 1,678,225/- to Rs. 1,717,735/- and accordingly the capital cost of school is increased from Rs. 50.5641 million to Rs. 50.6069 million. The total cost of Dir Lower is increased from Rs. 69.2383 million to Rs. 69.2811 million
8	Mian Kaley	School Name	Shangla	GPS Mian Kaley	GGPS Mian Kaley	The name of school is corrected.
9	PIL-01	Total Cost	-	Rs. 455.2648 million	Rs. 455.3507 million	Due to increase in capital cost of GHS Rahatkot and GHS Mian Brangola, the total cost of PIL-01 is increased from Rs. 455.2648 million to Rs. 455.3507 million.

looking forward for your comments & advice if any.

Best Regards,

Ruidar Ali

Quality Assurance Manager (Building), AGES

Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745

Date: Wed, 23 Oct 2013 21:44:34 -0700
From: agesswat@yahoo.com
Subject: Fw: Fwd: Flood Schools Estimates and Partially Damaged BHUs
To: ruidarali@hotmail.com
CC: naseerages@yahoo.com; naseermkhan@hotmail.com

Sir,

As directed by Team Leader AGES, Kindly download the Flood Schools Estimates and do the needful.

Regards

AGES CONSULTANTS

M & E Services Malakand
Site Office Swat
Phone No : 0946 722717
Fax No : 0946 724718
Email: agesswat@yahoo.com

----- Forwarded Message -----

From: Naseer Khan <naseerages@yahoo.com>
To: Shamas Ul Wahab <agesswat@yahoo.com>; "agesqs@gmail.com" <agesqs@gmail.com>
Sent: Wednesday, 23 October 2013 9:15 PM
Subject: Fw: Fwd: Flood Schools Estimates and Partially Damaged BHUs

Dear Shamas:

For action at your end.

Regards,

Naseer M Khan
Team Leader
AGES: M&E Consultants KP/FATA-RPs
Cell:- 0333-912-5887 |Phone:-091-5823117-8|Fax:-091-5823145
E-mails: naseer@ages.com.pk \ naseermkhan@hotmail.com

On Wednesday, October 23, 2013 3:22 PM, Bahro Bar <bahrobar@usaid.gov> wrote:
Dear Naseer Sb,
For AGES thorough review and verification.
Thanks

----- Forwarded message -----

From: Tahir Kamran <tahirkamran@pdma.gov.pk>

Date: Wed, Oct 9, 2013 at 1:57 PM

Subject: Fwd: Flood Schools Estimates and Partially Damaged BHUs

To: "Bahrobar (USAID/Pak/FATA)" <Bahrobar@usaid.gov>

Kindly download the attachment as discuss for further processing at your end.

Best Regards

Engr. Tahir Kamran Marwat

Chief Infrastructure,

Provincial Reconstruction, Rehabilitation & Settlement Authority (PaRRSA)

Civil Secretariat, Peshawar.

Mobile#. +92 (0) 333 9152288

Office #. +92 (91) 9213250/ 9213867

Fax #. +92 (91) 9212167

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

Email	From	To	Date	Subject
6	QAM (Building) AGES	Engineer USAID	October 31, 2013	Minutes Of The Meeting Held On October 28, 2013 At The Office Of DEO, Dir Upper

Subject:	FW: MINUTES OF THE MEETING HELD ON OCTOBER 28, 2013 AT THE OFFICE OF DEO, DIR UPPER
From:	Ruidar ali (ruidarali@hotmail.com)
To:	bahrobar@usaid.gov; bahrobar@gmail.com;
Cc:	tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk; azizages@gmail.com; cmep@ages.com.pk; alam.iftikhar@yahoo.com;
Date:	Thursday, October 31, 2013 11:29 AM

fyi, please.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Tue, 29 Oct 2013 19:31:45 +0500

Subject: MINUTES OF THE MEETING HELD ON OCTOBER 28, 2013 AT THE OFFICE OF DEO, DIR UPPER

From: parrsa.timergara@gmail.com

To: tahirkamran70@yahoo.com; planning_mkd@hotmail.com

CC: ruidarali@hotmail.com

Dear Tahir Kamran Saheb / Said Rehman Saheb,

Salam,

Attached please find the subject minutes for information please.

Engr. Shahid Jan

Email	From	To	Date	Subject
7	Engineer USAID	QAM (Building) AGES	October 31, 2013	PIL for 24 flood damaged schools signed by USAID

Subject:	Fwd: PIL for 24 flood damaged schools signed by USAID
From:	bahrobar@usaid.gov
To:	ruidarali@hotmail.com; azizages@gmail.com
Date:	Thu, 31 Oct 2013 14:42:03 +0500

FYI.

----- Forwarded message -----

From: **Bahro Bar** <bahrobar@usaid.gov>

Date: Thu, Oct 31, 2013 at 2:40 PM

Subject: PIL for 24 flood damaged schools signed by USAID

To: pm-parrsa@pdma.gov.pk, Tahir Kamran <tahirkamran@pdma.gov.pk>, "Mr. Tahir Kamran" <tahirkamran70@yahoo.com>

Cc: "Banori, Farhat Ali Shah(USAID/Pak/FATA)" <fbanori@usaid.gov>, Elizabeth Campbell <ecampbell@usaid.gov>, Mohammad Altaf Afridi <mafridi@usaid.gov>

Dear Shakeel Iqbal/Tahir Kamran,

This is to inform you that Project Implementation Letter for 24 flood damaged schools (based on the Revised Schedule of Rates - Market Rate System-2013 of Govt. of KP) have been signed by USAID and dispatched through courier for signature of Director General PaRRSA.

Alongwith, hard copies of Amendment No.3 to Agreement No. 391-MLK-FARA-002 and Amendment No.4 to Agreement No. 391-MLK-FARA-001 duly acknowledged by EAD have been sent for your record.

Please acknowledge the receipt and return all the three original copies of PIL No.28 for EAD acknowledgement accordingly.

Thanks

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov
