



USAID | **PAKISTAN**
FROM THE AMERICAN PEOPLE



CONSTRUCTION MONITORING & EVALUATION PROGRAM

(Reconstruction of Flood Damaged Schools in Khyber Pakhtunkhwa)

MONTHLY PROGRESS REPORT # 11
JANUARY, 2014

Contents

EXECUTIVE SUMMARY	1
1. THE PROJECT	3
1.1. Background	3
1.2. Location	4
1.3. Implementation Arrangements	5
1.4. The M&E Services	5
2. MAJOR ACTIVITIES UNDERTAKEN DURING THE REPORTING MONTH (JANUARY, 2014)	6
2.1. Validation/Revalidation of Schools in District Lakki Marwat	6
2.2. Site & Layout Plans.....	6
2.3. Engineer's Estimates	6
2.4. Submission of Quarterly Progress Report.....	6
2.5. Revision of EDF of PIL-28	6
2.6. Meetings	6
3. OVERALL PROGRESS TILL END OF LAST MONTH (DECEMBER 31, 2013)	8
3.1. Mobilization of Staff & Establishment of Office/Residencies	8
3.2. Submission of Final Quality Assurance Plan (QAP)	8
3.3. Validation/Revalidation of Schools (1 st list)	8
3.4. Validation of Alternate Schools (Subsequent lists)	9
3.5. Validation Report.....	9
3.6. Pre-construction Proforma's	10
3.7. Site/Layout Plans	10
3.8. Revision of Modular Drawings.....	10
3.9. Submission of Modular Drawings	10
3.10. Revision of Modular BOQs	10
3.11. Submission of Modular BOQs.....	10

3.12.	Submission of Quarterly Progress Reports.....	11
3.13.	Meetings	11
3.14.	Organization Chart and Staff Deployment.....	16
4.	ORGANIZATION CHART WITH KEY STAFF DEPLOYMENT.....	17
5.	ITEMS REQUIRING ACTIONS.....	22
 Annexure		23
Annexure I	= Minutes of Meetings	24
Annexure II	= Emails	40

ABBREVIATION

ADP	Annual Development Program
BOQ	Bills of Quantities
CGI	Corrugated Galvanized Iron
C&W	Communication & Works
CO	Contracting Officer
COR	Contracting Officer's Representative
CSR	Composite Schedule Rate
DAE	Diploma of Associate Engineer
EDO	Executive District Officer
EMMP	Environmental Mitigation Measure Protocol
FAR	Fixed Amount Reimbursement
GoP	Government of Pakistan
HCC	Host Country Contracting
ITP	Inspection & Testing Plan
KP	Khyber Pakhtunkhwa
KP-RP	Khyber Pakhtunkhwa Reconstruction Program
LoE	Level of Effort
M&E	Monitoring & Evaluation
PaRRSA	Provincial Reconstruction, Rehabilitation & Settlement Authority
PIL	Project Implementation Letter
PM	Project Manager
PMU	Project Management Unit
QA	Quality Assurance
QAM (Building)	Quality Assurance Manager (Building)
RA	Reimbursement Agreement
RFP	Request for Proposal
SoW	Scope of Work
TSF	Tons per Square Foot
USAID	United States Agency for International Development

EXECUTIVE SUMMARY

The Province of Khyber Pakhtunkhwa suffered heavy infrastructure damages firstly due to terrorism and militancy and thereafter due to the unprecedented floods of July 2010. United States Agency for International Development (USAID) actively supported the rehabilitation and reconstruction activities of damaged schools, health facilities, drinking water supply schemes and other infrastructure components in Malakand Division by initially obligating funds amounting to USD 36 million under an Activity Agreement (No. 391-011) signed in September, 2009 between USAID and PaRRSA on behalf of GoP. Expanding its portfolio, USAID provided funds for rehabilitation / reconstruction of other infrastructure components including irrigation, bridges and roads etc. in the calamity hit areas.

In June 2012, USAID sub-obligated additional funds amounting to USD 25 million for reconstruction of rains / floods damaged and bomb blasted schools in the affected districts of KP under Amended Activity Agreement No. 391-014. M/s AGES Consultants was assigned the task of Monitoring & Evaluation (M&E) services of these reconstruction activities under USAID/Pakistan Construction Monitoring and Evaluation Program (CMEP), for which a formal contract was signed on September 30, 2012.

Initially about 114 damaged schools were identified wherein 42 schools were found suitable/feasible for reconstruction during the revalidation/assessment process. Site/layout plans & validation reports were shared with the stakeholders. In a meeting held on May 17, 2013 in the office of Program Manager PaRRSA, 24 out of the 42 suitable schools were agreed to be included in PIL and accordingly drawings & engineer's estimates of these schools were prepared, reviewed and finalized. Furthermore, designs for all modules were revised / improved and new modules were introduced in light of lessons learnt from KP-RP (Malakand).

USAID issued a signed PIL number 391-014-PIL-28 on October 29, 2013 for the 24 schools to PaRRSA for further appropriate action.

During the reporting month, physical survey and assessment of 56 schools of District Lakki Marwat was carried out by the M&E Consultants. During the validation process, 16 schools were found suitable/feasible while the remaining 40 schools were declared unsuitable for reconstruction due to various reasons.

So far, the M&E Consultants have completed validation/assessment of a total of 356 identified schools, wherein 138 schools were found suitable & 218 schools were declared unsuitable for reconstruction for various reasons. Out of 138 feasible schools, PIL for 24 schools has been already issued, whereas site/layout plans, modular designs and cost estimates etc. for 63 schools have been finalized/reviewed for which a PIL is currently under process at USAID.

Another 21 schools will be included in the subsequent PIL's after finalization of the pre-requisites whereas 30 schools have been kept in 2nd priority.

Physical construction activities will start upon completion of the requisite prequalification, tendering and contracting formalities by PaRRSA. An implementation arrangement in light of the experience gained and lessons learnt from the Malakand model needs to be enacted on priority so as to pursue the project implementation / physical activities without any loss of time.

It is worth noting that PIL for 24 schools has been signed on October 29, 2013, while the requisite prequalification, tendering and construction contracting formalities are yet to be initiated and thus commencement of physical construction activities still seems to be a matter of months. The matter needs to be pursued with the concerned authorities on urgent basis so that the project moves forward to the construction stage.

1. THE PROJECT

1.1. Background

The disaster of 2010 Monsoon Flood in Khyber Pakhtunkhwa (KP) was massive and unprecedented. The flood not only deprived the local communities of their livelihoods but also created an unprotected and challenging environment for the school going children in the flood hit districts of KP.

As per data received from the Education Department of the KP, the numbers of schools either partially or fully damaged ranged in hundreds. The Government of KP was faced with the challenging task of reconstruction and restoration of these lost academic facilities at huge construction costs. Realizing the importance of early resumption of educational activities, the government appealed to national and international donors for funds to rectify and retrieve the situation. In the meantime, the Government of KP, through its concerned line departments, prepared Damage Need Assessments (DNA) of the flood affected districts.


USAID was already working in Malakand Division on the reconstruction and rehabilitation of schools, health facilities and Water & Sanitation (WatSan) infrastructures affected during the militancy period. Contemplating an expansion of its portfolio of projects in KP with regards to flood relief activities, USAID tasked AGES, (the M&E consultants for the USAID funded sub-projects in the Malakand Division) to undertake the additional work of DNA and validation for the partially and fully damaged schools in some of the districts affected by floods.

In September 2012, AGES was assigned the task of monitoring & evaluation services including Quality Assurance and Environmental Monitoring for the reconstruction activities of the damaged schools in the affected districts Khyber Pakhtunkhwa comprising Peshawar, Nowshera, Charsadda, Malakand, Swat, Dir Upper/Lower, Shangla, DI Khan and Tank.

The project has been tasked with the objective to monitor & certify that all the proposed projects are built as per approved designs/drawings, technical specifications and to ensure environmental compliance as per USAID's and Government of Pakistan's (GoP) regulations and requirements.

1.2. Location

The revalidation and subsequent reconstruction activities are presently being pursued in the various districts of Khyber Pakhtunkhwa badly affected due to floods of July 2010 and militancy.

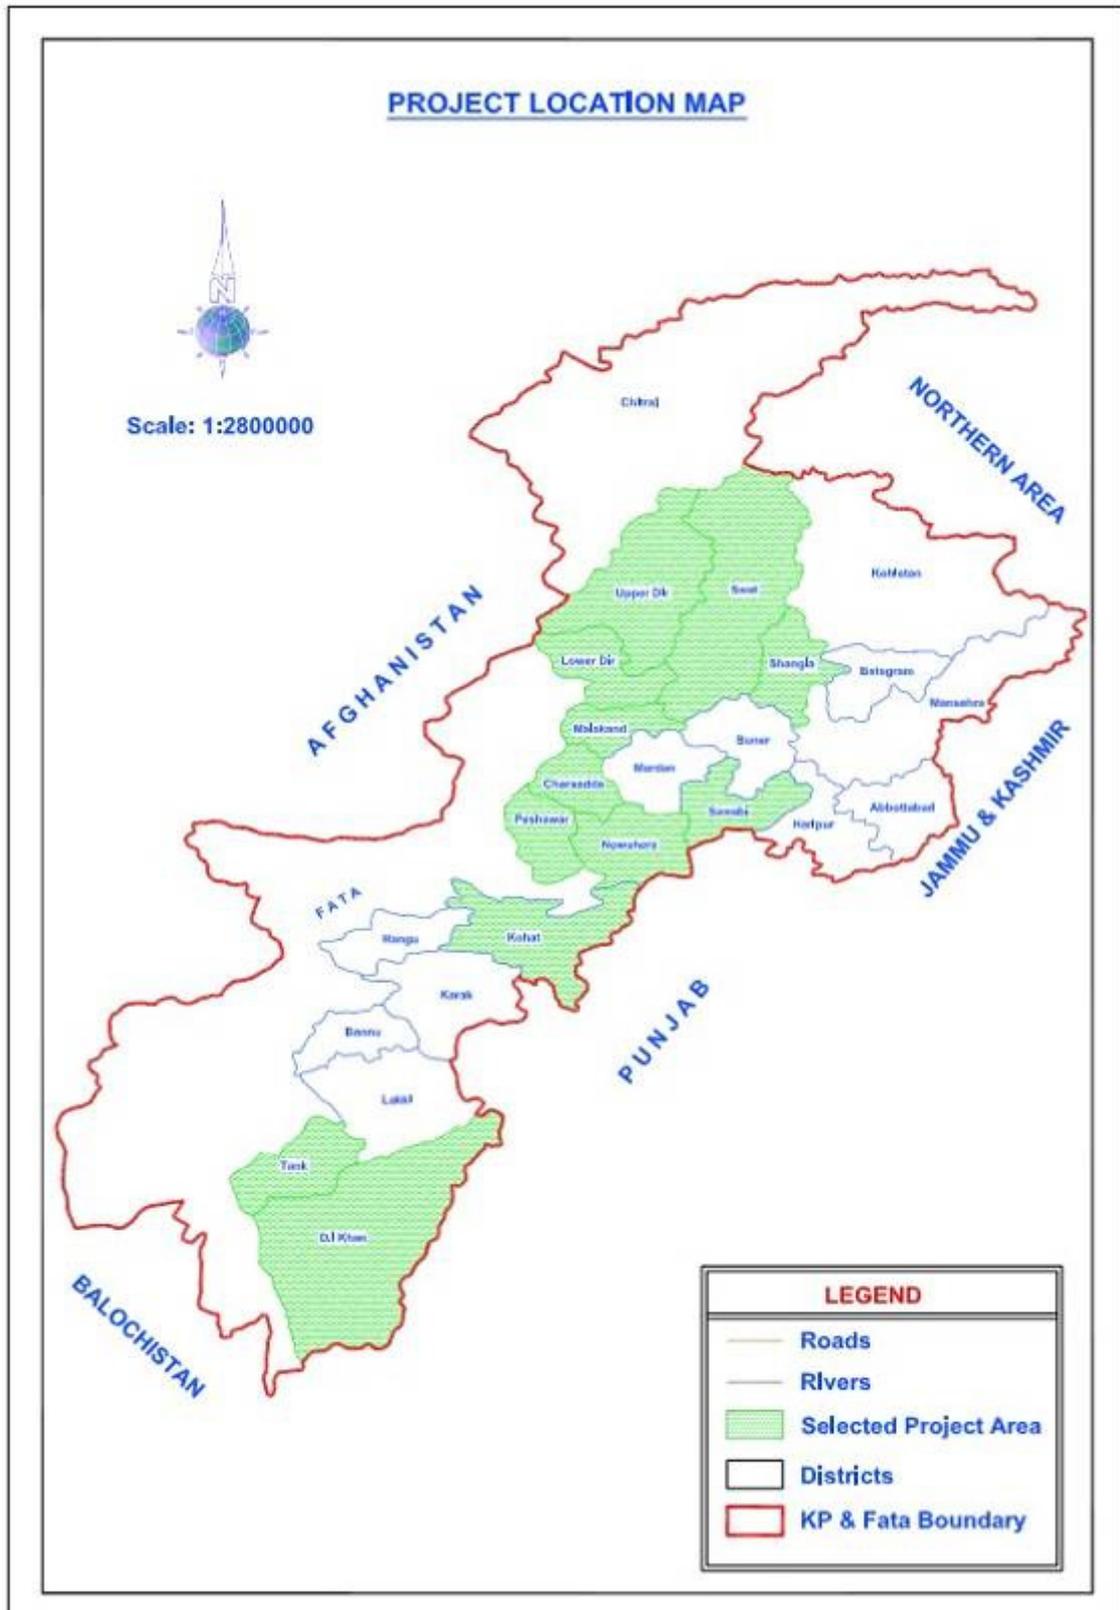

1.3. Implementation Arrangements

The Economic Affairs Division (EAD) designated the Director General (DG) of Provincial Reconstruction, Rehabilitation and Settlement Authority (PaRRSA) as an Additional Representative of the Government of Pakistan (GoP) for the purposes of the implementation of Program Areas. The GoKP has established a Project Steering Committee (PSC) to provide oversight, guidance and approvals required for smooth and timely implementation of the activities. The PSC is chaired by DG PaRRSA, and comprised representatives of USAID Pakistan and relevant provincial departments involved in the planning and execution of the activities. Therefore, PaRRSA has the authority to carry out the works to be financed under a Fixed Amount Reimbursement (FAR) Agreement. Accordingly, PaRRSA is fully responsible for carrying out these works through contracting, supervising the contractor(s) and for ensuring that the contractor(s) diligently undertake the work and provide the necessary equipment, skilled and unskilled labor, and efficient supply of materials to ensure uniform and continuous progress once construction has started. A strategy is presently being debated on and under formulation by the participation of all stakeholders to decide/identify an appropriate executing agency to undertake implementation of this project, on behalf of the government of KP. M/s AGES Consultants of Peshawar have been appointed by USAID as Monitoring & Evaluation Consultants for this project.

1.4. The M&E Services

The Contract for M&E Services for the “Construction Monitoring & Evaluation Program” was signed on September 30, 2012. The M&E services comprise the following.

- Submission of Quality Assurance Plan (QAP).
- Validation / Revalidation of the July 2010 flood damage assessment done through AGES for fully damaged schools to the current status.
- Pre-Construction report of each school site to establish base line condition.
- Preparation of site plan as well as layout plans on the basis of pre-construction survey data obtained as a result of site visits.
- Review and Vetting of Project Design Drawings / Documents.
- Verifying the quality of construction/installation works and ensures conformity to the contract construction drawings, standards, technical specifications & requirements
- Site Monitoring and Inspection Reports
- Assisting, advising & reporting to USAID/PaRRSA with regard to reconstruction activities.
- Field and Laboratory Testing
- Monthly & Quarterly Progress Reports

2. MAJOR ACTIVITIES UNDERTAKEN DURING THE REPORTING MONTH (JANUARY, 2014)

2.1. Validation/Revalidation of Schools in District Lakki Marwat

- Fifty Six (56) schools of District Lakki Marwat have been Validated/Revalidated during the reporting month. Sixteen (16) schools have been found suitable while remaining forty (40) schools were declared unsuitable for reconstruction. The validation report is in the process of preparation and will be shared shortly with the stakeholders.

2.2. Site & Layout Plans

- Preparation of draft site and layout plans of 16 feasible schools of District Lakki Marwat has been initiated & will be shared with the stakeholders shortly for their review & comments.
- Draft site and layout plans of 04 high and higher secondary schools have been shared with the stakeholders for their review and comments on January 10, 2014.

2.3. Engineer's Estimates

- Engineer's estimates of 63 schools of District Peshawar, Nowshera, Charsadda, Dir Lower, D.I Khan, Dir Upper, Malakand, Swat & Shangla have been reviewed in the reporting month. Summary of milestone payments of the modules used in the 63 schools have been prepared and submitted.

2.4. Submission of Quarterly Progress Report

- Fifth Quarterly Progress Report for the quarter October - December, 2013 was shared with USAID/PaRRSA for their review and comments on January 21, 2014.

2.5. Revision of EDF of PIL-28

- Environmental Documentation Form (EDF) of 24 schools of PIL-28 have been revised and submitted on January 31, 2014.

2.6. Meetings

1. A meeting was held on January 07, 2014 in the Project Office of CMEP Peshawar to review the site specific photographs of 32 schools, requiring further clarification. Chief Infrastructure (PaRRSA), with QAM (Building), Mid Level Specialist, Field Manager and Office Engineer CMEP AGES attended the meeting (details attached as Annexure-I).
2. A meeting was held on January 11, 2014 in the Project Office of CMEP Peshawar to review the proposals of GHSS Akbarpura, Site/layout plans & photographs of 13 schools and list of damaged schools of district Lakki Marwat. Chief Infrastructure (PaRRSA), Principal Architect Afkar Associates, while Project Manager, Project Advisor, QAM (Building), Structure Engineer, Mid Level Specialist, Field Manager, Office Engineer and Junior Architect CMEP AGES attended the meeting (details attached as Annexure-I).

3. A meeting was held on January 13, 2014 in the Project Office of CMEP Peshawar to review the proposals of GHSS Akbar Pura, Site photographs of those schools on which further clarification is required and site photographs of high & higher secondary schools. USAID Engineer, Chief Infrastructure (PaRRSA), Team Leader M&E Project Malakand AGES, along with Project Manager, Project Advisor, QAM (Building), Structure Engineer, Mid Level Specialist, Field Manager and Office Engineer CMEP AGES attended the meeting (details attached as Annexure-I).

3. OVERALL PROGRESS TILL END OF LAST MONTH (DECEMBER 31, 2013)

3.1. Mobilization of Staff & Establishment of Office/Residencies

- Key staff of AGES was mobilized in September 2012 and preliminary meetings were conducted with the stakeholders for evolving strategy for the implementation of the project.
- Need based logistics have been provided
- Project Office at Peshawar has been established
- Residencies (02) for office as well as field staff have been established

3.2. Submission of Final Quality Assurance Plan (QAP)

- QAP was reviewed in light of observations/comments made by USAID & final version shared with the stakeholders on March 13, 2013.

3.3. Validation/Revalidation of Schools (1st list)

- One hundred & fourteen (114) schools were Validated/Revalidated till end of December 2012 and revalidation report submitted to the stakeholders during the month of January, 2013.
- Forty two (42) schools out of 114 schools were found suitable during the revalidation process. District wise position is given here under:

S.No	District	Total No. of Schools (No.)	Feasible Schools (No.)	Unfeasible Schools (No.)	PIL-28 (No.)	2 nd Priority (No.)
1	D.I Khan	35	27	08	09	18
2	Tank	02	-	02	-	-
3	Peshawar	17	-	17	-	-
4	Charsadda	06	-	06	-	-
5	Nowshera	01	-	01	-	-
6	Swat	28	02	26	02	-
7	Shangla	12	08	04	08	-
8	Malakand	04	03	01	03	-
9	Dir Upper	07	-	07	-	-
10	Dir Lower	02	02	-	02	-
TOTAL:		114	42	72	24	18

3.4. Validation of Alternate Schools (Subsequent lists)

- Two hundred & forty two (242) schools were Validated/Revalidated till end of December 2013.
- Ninety six (96) schools out of 242 schools were found suitable during the validation/revalidation process. District wise position is given here under:

S.No	District	Total No. of Schools (No.)	Feasible Schools (No.)	Unfeasible Schools (No.)	Expected PIL-29 (No.)	Upcoming PIL's (No.)	2 nd Priority (No.)
1	D.I Khan	11	04	07	04	-	-
2	Peshawar	12	05	07	05	-	-
3	Charsadda	07	05	02	05	-	-
4	Nowshera	05	03	02	02	01	-
5	Swat	33	09	24	06	01	02
6	Shangla	27	15	12	15	-	-
7	Malakand	11	07	04	03	01	03
8	Dir Upper	33	10	23	10	-	-
9	Dir Lower	37	19	18	13	02	04
10	Kohat	07	03	04	-	-	03
11	Swabi	03	-	03	-	-	-
12	Lakki Marwat	56	16	40	-	16	-
TOTAL:		242	96	146	63	21	12

3.5. Validation Report

- Validation/revalidation report of 114 schools of 1st list was prepared and shared with the stakeholders for their review and comments.
- Revision of validation report of 173 schools (subsequent lists) is in the process and will be shared shortly with the stakeholders.
- Preparation of validation report of 13 high and higher secondary schools is in the process and will be shared shortly with the stakeholders.
- Preparation of draft validation report of 56 schools of District Lakki Marwat has been initiated and will be shared with the stakeholders once completed.

3.6. Pre-construction Proforma's

- Pre-construction proforma's of 42 feasible schools (1st list) were shared with the stakeholders.
- Pre-construction proforma's of 63 feasible schools (subsequent lists) are in the process and will be shared shortly with the stakeholders

3.7. Site/Layout Plans

- Site/layout plans along with site specific photographs of all 42 suitable sites (1st list) were shared with the stakeholder for their information, review & comments.
- Site/Layout plans along with site photographs of 63 feasible schools (subsequent lists) were shared with the stakeholders for their information, review & comments.

3.8. Revision of Modular Drawings

- All modules were structurally as well as architecturally revised/modified in accordance with the decisions made in the meetings held on Nov 17, 2012, Dec. 27, 2012, May 17, 2013, May 24, 2013, June 28, 2013 and lessons learnt from M&E Project Malakand and shared with the stakeholders for their comments.
- New modules for M7, M11, M12, M13, LB & LB(H) were also introduced keeping in view the land constraint, site specific condition and requirement of the students etc.
- Double/Triple storey buildings were introduced to provide sufficient accommodation to the students in the limited available area.

3.9. Submission of Modular Drawings

- The modular drawings of 24 schools of PIL-28 were shared with stakeholder for their review & comments.
- The modular drawings of 63 schools of expected PIL-29 were shared with the stakeholders for their review & comments.

3.10. Revision of Modular BOQs

- The BOQ's of all modules duly revised and modified, were prepared and shared with stakeholder for their review & comments.

3.11. Submission of Modular BOQs

- The modular BOQ's of 24 schools of PIL-28 were shared with stakeholder for their review & comments.

- The modular BOQ's of 63 schools of expected PIL-29 were shared with the stakeholders for their review & comments.

3.12. Submission of Quarterly Progress Reports

- First Quarterly Progress report for the quarter ending December 31, 2012 was shared with USAID/PaRRSA for the review and comments.
- Second Quarterly Progress Report for the quarter ending March 31, 2013 was shared with USAID/PaRRSA for their review & comments on April 04, 2013.
- Third Quarterly Progress Report for the quarter ending June 30, 2013 was shared with USAID/PaRRSA for their review & comments on July 08, 2013.
- Fourth Quarterly Progress Report for the quarter ending September 30, 2013 was shared with USID/PARRSA for their review & comments on October 09, 2013

3.13. Meetings

1. A meeting was held in the office of PaRRSA on 24-09-2012. All the stakeholders i.e USAID, PaRRSA and AGES participated in the proceedings. Main purpose of the meeting was to evolve strategy for the way forward for implementation of the reconstruction of flood damaged schools based on the findings of the validation and damaged assessment report prepared by AGES in Year 2010.
2. A meeting was held in the Main office of AGES on 17-11-2012. Chief Infrastructure PaRRSA, Project Manager CMEP AGES, Quality Assurance Manager CMEP AGES, Partners AGES and Field Engineers AGES attended the Meeting. The purpose of meeting was to review the previous minutes of meeting and share the validation/revalidation reports prepared by AGES and to evolve further strategy for the revalidation of schools in the rest of the Districts.
3. A meeting was held in the Main Office of AGES on 27-12-2012. All the Stakeholders i.e USAID, PaRRSA and AGES participated in the meeting. The main purpose of the meeting was to review the previous minutes of meeting and share the validation/revalidation of all Districts covered under the CMEP KP.
4. Meetings were held on 15-10-2012 & 17-10-2012 in the office of EDO District Shangla. EDO & ADO District Shangla, Field Manager AGES & Field Monitor AGES attended the meeting. The purpose of meeting was to chalk out visit program needed for the revalidation of schools in District Shangla.
5. A meeting was held in the office of DTL M&E Malakand at Mingora. The M & E Engineers of M&E Project who were involved in the validation process in Year 2010 participated in the

meeting beside the QAM(B) CMEP AGES, coordinator Swiss Agency for Development and Cooperation and Field Monitor AGES. The purpose of meeting was to identify the suitable and unsuitable sites in light of survey done in year 2010.

6. A meeting was held in the office of M&E Dir at Timergara. Infrastructure Coordinator PaRRSA, Coordination Engineer M&E Dir, M&E Engineer Dir, Site Engineers M&E Dir, QAM Building CMEP AGES and Field Monitor CMEP AGES attended the meeting. The purpose of the meeting was to discuss the validation reports with the respective site engineers of M&E Dir who were involved in the validation process done in Year 2010. The suitable/unsuitable sites were identified in light of their reports.
7. A meeting was held in the Office of EDO District Malakand on 29-11-2012. EDO & ADO District Malakand, QAM(B) CMEP AGES & Field Monitor attended the meeting. The purpose of the meeting was to chalk out program for the visits of the suitable sites as pointed out by EDO Malakand.
8. A meeting was held on 05-12-2012 in the office of EDO D.I.Khan. All DDOs of the respective Tehsils, QAM (B) CMEP AGES, Field Manager and Field Monitor CMEP attended the meeting. The schools having land issues were identified and program was chalked out for the visits of suitable sites. The DDOs of the respective Tehsils were also involved in the revalidation process.
9. Introductory meeting with Country Director USAID Pakistan was held on April 17, 2013 in Islamabad.
10. A meeting was held on 17-05-2013 in the office of Programme Manager PaRRSA. Program Manager PaRRSA, Chief Infrastructure PaRRSA, Programme Manager USAID for KP, Engineer USAID, Team leader M&E AGES, CPO PaRRSA, SPO Education Department, DEO DI Khan, QAM (Building) CMEP AGES, Mid Level Specialist AGES, Field Manager AGES & Office Engineer AGES attended the meeting.

It was decided and agreed in the meeting that 24 out of 42 feasible sites/schools as re-validated & assessed by AGES shall be tagged as priority-1 having comparatively high enrollment & high future potential and will be included in PIL-1. Other issues pertaining to the project were also discussed in the meeting and decisions made accordingly.

11. A meeting was held on 24-05-2013 in the Project office CMEP Peshawar to discuss Layout Plans, modular drawings and cost estimates for PIL No.01. Chief Infrastructure PaRRSA, Partner AGES, QAM (Building) CMEP AGES, Mid Level Specialist AGES, Field Manager AGES & Office Engineer AGES attended the meeting. Some technical modifications/changes were suggested and agreed to be incorporated in the BOQs, Architectural and Structural Drawings keeping in view the lesson learnt from M&E project

12. A meeting with Engineer USAID and Chief Infrastructure PaRRSA was held on 28-06-2013 to review & finalize the BOQ's and drawings of 24 schools selected for PIL-01
13. A meeting was held with USAID & PaRRSA in PaRRSA Secretariat Peshawar on 28-06-2013 and discussed the flood/militancy school implementation strategy and progress of school under KPRP.
14. A meeting was held on July 22, 2013 in the office of Program Manager PaRRSA. Program Manager PaRRSA, Chief Infrastructure PaRRSA, Engineer USAID, Chief Planning Officer PaRRSA, Planning Officer PaRRSA, Senior Engineer PaRRSA, QAM(Building) CMEP AGES, Mid Level Specialist AGES and Field Manager AGES attended the meeting.

Main purpose of the meeting was firstly to review the draft validation report of alternate schools submitted by AGES and secondly to get fresh list of alternate schools for physical survey and assessment.
15. A meeting was held on August 20, 2013 in the office of DEO Swabi. ADO (Male) Swabi, ADO (Female) Swabi, Field Manager (Building) CMEP and Junior Engineer CMEP attended the meeting. The (03) three listed schools were discussed & reviewed in detail before going for physical survey & assessment of the schools. Both ADOs accompanied the survey team during the validation process.
16. A meeting was held on August 26, 2013 in the office of DEO Malakand at Batkhela. Mr. Abdullah DEO(M) Malakand, Mr. Ruidar Ali QAM(Building) CMEP, Mr. Fazal Ahad Dy:DEO(M) Malakand, Mr. Fazli Subhan ADO(P&D) Malakand & Mr. Iftikhar Alam Office Engineer AGES attended the meeting. The list provided by PaRRSA was discussed in detail and all the listed schools were found suitable for physical survey & assessment. A survey team comprising of AGES Engineers & ADO (P&D) were advised to proceed for physical survey & assessment forthwith.
17. A meeting was held on August 26, 2013 in the office of DEO Lower Dir at Timergara. Mr. Shabir Ahmad Dy: DEO (E&SE) Dir Lower, Mr. Muhammad Aslam ADO (P&D) Dir Lower, Mr. Muhammad Tahir ADO(P&D) Dir Upper, Mr. Jehandar Shah ADO(P&D)F Dir Lower, Mr. Shahid Jan Infrastructure Coordinator PaRRSA & Mr. Ruidar Ali QAM(Building) CMEP attended the meeting. The list provided by PaRRSA was discussed in detail and six (06) schools were dropped from the list being Pledged/Reconstructed by other Donor agencies or through Government ADP. AGES was given a green signal to go ahead for the physical survey & assessment of the balance seven (07) listed schools as provided by PaRRSA (Annexure-I).
18. A meeting was held on August 27, 2013 in the office of DTL M&E Swat at Saidu Sharif Swat. Mr. Shakeel Iqbal PM PaRRSA, Mr. Aurang Zeb ADO(P&D) Shangla, Mr. Akhter

Naeem ADO P&D(F) Shangla, Mr. Said Rahman SPO PMU PaRRSA, Mr. Sajjad Ahmad Infrastructure Coordinator PaRRSA, Mr. Ruidar Ali QAM(Building) CMEP, Dilshad Begum DEO(F) Swat, Mr. Abdul Aziz Shaheen ADO P&D(F) Swat, Mr. Sultan Mehmood DEO(M) Swat & Mr. Muhmmad Azim ADO P&D Swat attended the meeting. The list provided by PaRRSA was discussed & reviewed in detail. Some schools were dropped due to inaccessibility, some were not functional for the last 8 to 9 years (according to DEO Female), some were already Pledged/Reconstructed by other donors or through Government ADP, and some have no land being washed away due to floods July, 2010. It was decided that a final list will be submitted to PaRRSA having all informations as discussed in the meeting for physical survey & assessment (Annexure-I).

19. A meeting was held on August 28, 2013 in the office of DEO Dir Upper at Dir. Mr. Shahid Jan Infrastructure Coordinator PaRRSA, Mr. Ruidar Ali QAM(Building) CMEP & Mr. Farmanullah Representative of DEO(M&F) Dir Upper attended the meeting. The list provided by PaRRSA was discussed & reviewed in detail. Five (05) schools mentioned in the list were dropped due to having no land being washed away during the floods July 2010; two (02) schools were already Pledged/Re-constructed by other donor agencies. It was decided that a final list in light of decision made in the meeting held on August 27, 2013 with the Program Manager PaRRSA at Saidu Sharif Swat will be submitted to PaRRSA for physical survey & assessment. AGES survey team will proceed for physical survey & assessment as and when the consolidated list of schools is received from PaRRSA (Annexure-I).
20. A meeting was held on September 17, 2013 in the Project Office of CMEP Peshawar, to discuss validation report of 12 alternate sites of district Nowshera, Swabi & Kohat and actual site specific BOQ's of 24 schools of PIL-01. Chief Infrastructure PaRRSA, QAM(Building) CMEP AGES, Mid Level Specialist AGES, Field Manager AGES, Office Engineer AGES and Quantity Surveyor AGES attended the meeting.
21. A meeting was held on October 28, 2013 in the office of District Education Officer Dir Upper. SDO (M) Dir & Warai Sub Division, ASDO (M) Sheringle & Warai Sub Division, Infrastructure Coordinator PaRRSA Dir Lower & QAM (Building) AGES CMEP attended the meeting. The list provided by PaRRSA was discussed in detail and 09 schools were dropped from the list being repaired/rehabilitated, partially damaged and no arrangement of alternate land. AGES was advised to proceed for physical survey and assessment.
22. A meeting was held on October 29, 2013 in the office of District Education Officer Shangla at Alpura. DEO (M/F) Shangla, ADO P&D (M) Shangla, ADO P&D (F) Shangla, Admin Officer Shangla, Senior Clerk DEO Office Shangla, QAM (Building) AGES CMEP, Field Manager AGES CMEP, Junior Architect AGES CMEP, Ex-MPA Shangla attended the


meeting. The list provided by PaRRSA was discussed in detail and 03 schools were dropped from the list being no arrangement of alternate land. AGES was advised to proceed for physical survey and assessment.

23. A meeting was held on November 06, 2013 in the Project Office of CMEP Peshawar, to revisit the validation reports of 21 schools in Districts Peshawar, Nowshera & Charsadda, 12 schools in District Nowshera, Swabi & Kohat, 8 schools in District Dir Lower and to review the Draft Validation Report of recently assessed, 22 schools in District D.I Khan & 11 schools in District Dir Lower. The sole objective of the above review was to finalize the scope for the upcoming PIL. Chief Infrastructure PaRRSA, Project Manager CMEP AGES, QAM(Building) CMEP AGES, Mid Level Specialist CMEP AGES, Junior Architect CMEP AGES and Junior Engineer CMEP AGES attended the meeting.
24. A meeting was held on November 20, 2013 in the Project Office of CMEP Peshawar, to discuss draft site/layout plans of recently assessed 38 schools of District Dir Lower, Dir Upper, Malakand, Swat & Shangla, to finalize the scope for the upcoming PIL. Chief Infrastructure PaRRSA, Project Manager CMEP AGES, QAM(Building) CMEP AGES, Mid Level Specialist CMEP AGES, Field Manager CMEP AGES and Office Engineer CMEP AGES attended the meeting.
25. A meeting was held at CMEP Project Office Peshawar on December 21, 2013 to review the revised proposals of GHSS Akbarpura. Principal Architect AFKAR Associates presented the proposals to the Chief Infrastructure PaRRSA. AGES CMEP team comprising the Project Manager, Advisor, QAM (Building), Senior Technical Specialist, Structure Engineer / specialist, Mid Level Specialist, Field Manager, Office Engineer and Junior Architect attended the meeting.


3.14. Organization Chart and Staff Deployment

The M&E Consultants organization chart and staff deployment is presented in the next section.

4. ORGANIZATION CHART WITH KEY STAFF DEPLOYMENT

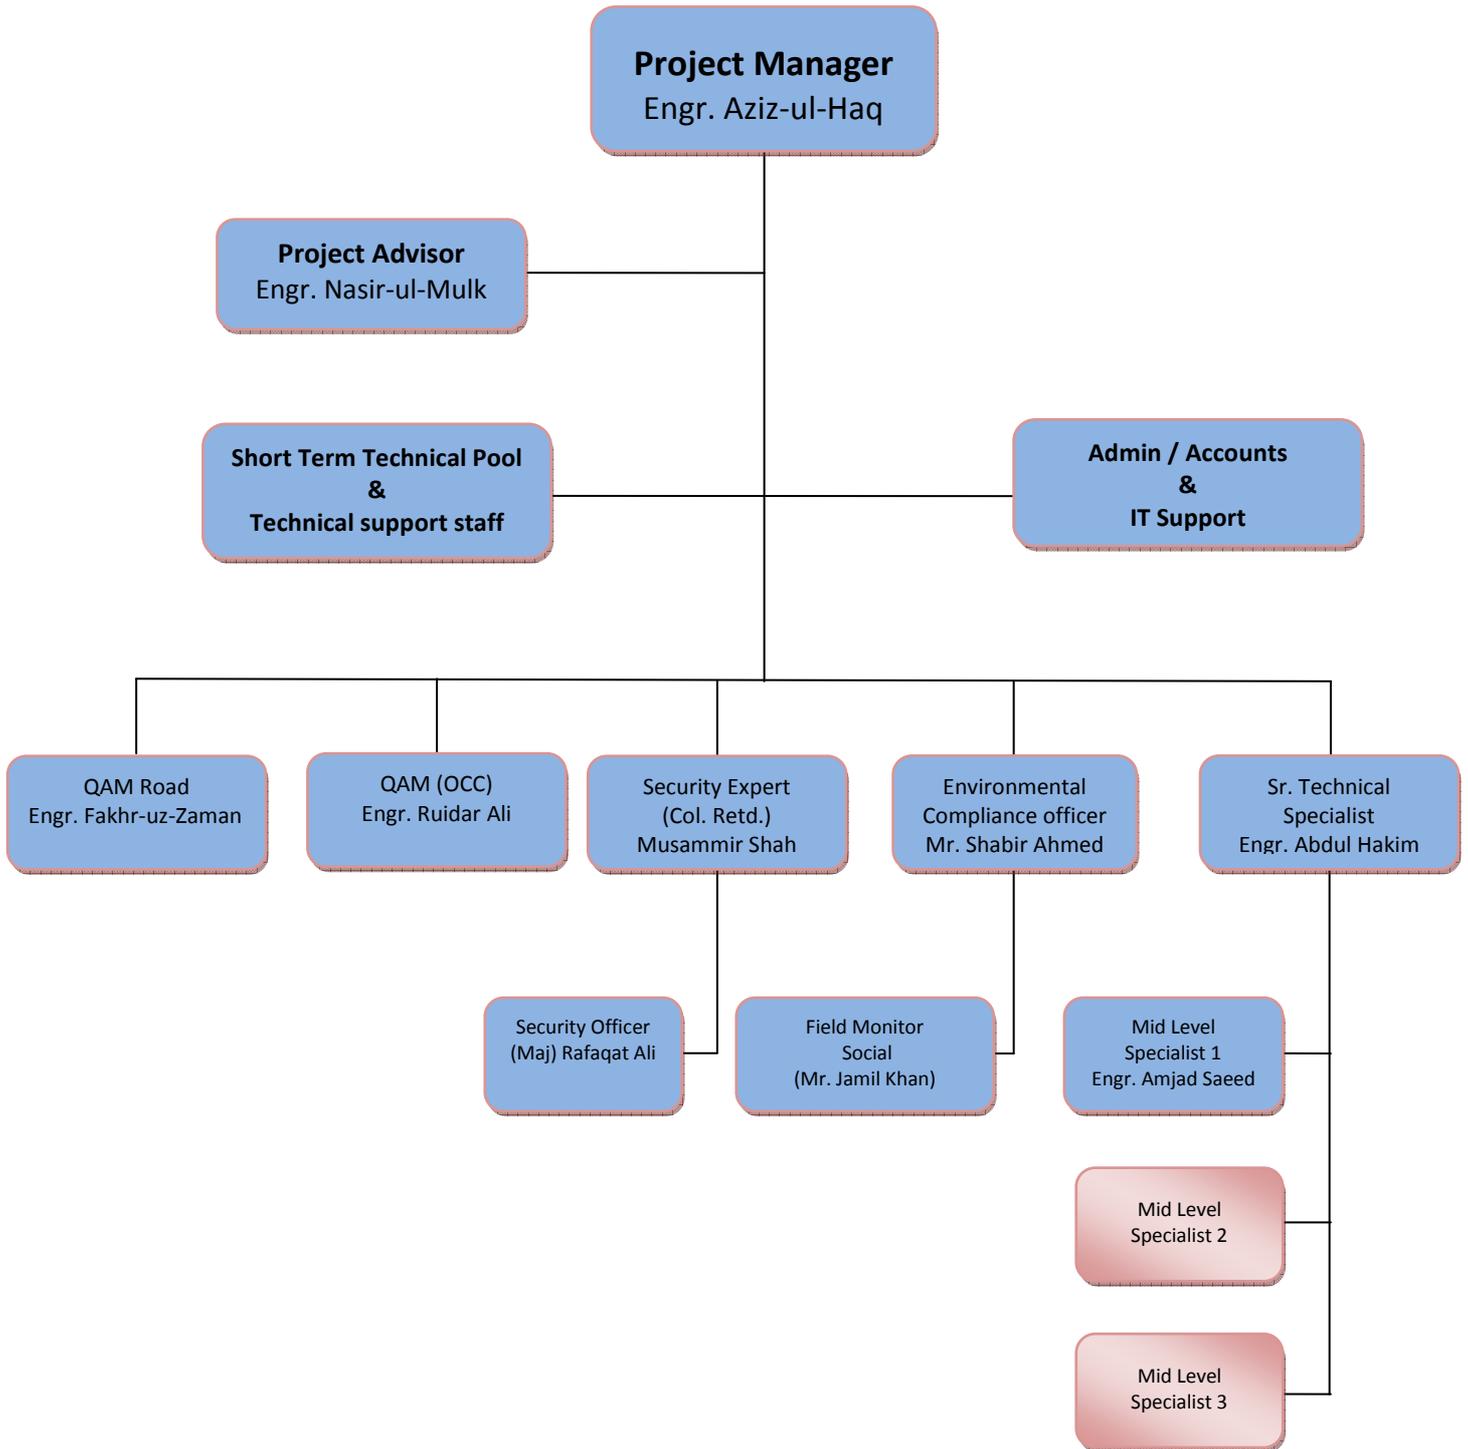

LEGEND:



Mobilized



To be mobilized with expansion of work

PROJECT MANAGER OFFICE – STAFF DEPLOYMENT

S.No.	Name	Designation	
1	Aziz-ul-Haq	Project Manager	ROAD COMPONENT
2	Abdul Hakim	Senior Technical Specialist	
3	Shabir Ahmad Khan	Environmental Compliance Officer	
4	Amjad Saeed	Mid-Level Specialist	
5	Saqib Maqbool	Junior Engineer	
6	Arshad Khan	CAD Operator	
7	Sohail Anjum	Senior Surveyor	
8	Abdul Waheed	Manager Admin/Finance	
9	Amir Habib	IT Officer	
10	Muhammad Bilal	Assistant Accountant	
11	Faizan Khan	Computer Operator	
12	Jamil Khan	Field Monitor Social	OTHER CONSTRUCTION COMPONENT
13	Anwar Dad	Quantity Surveyor	
14	Waqar ul Mulk	Junior Architect	
15	Naeem Jan	Senior Surveyor	
16	Muhammad Waqas	Survey Assistant	
17	Muhammad Ayaz	Survey Assistant	
18	Muhammad Zeeshan Atta	Survey Assistant	
19	Sana ullah	Accountant	

QUALITY ASSURANCE MANAGER OFFICE (Other Construction Component)

S.No.	Name	Designation
1	Ruidar Ali	QAM (OCC)
2	Muhammad Humayun	Field Manager M&E
3	Iftikhar Alam Khan	Office Engineer
4	Fida Ullah	Computer Operator

Figure 4.1: TEAM COMPOSITION-BUILDING COMPONENTS
USAID/PAKISTAN CONSTRUCTION MONITORING AND EVALUATION PROGRAM



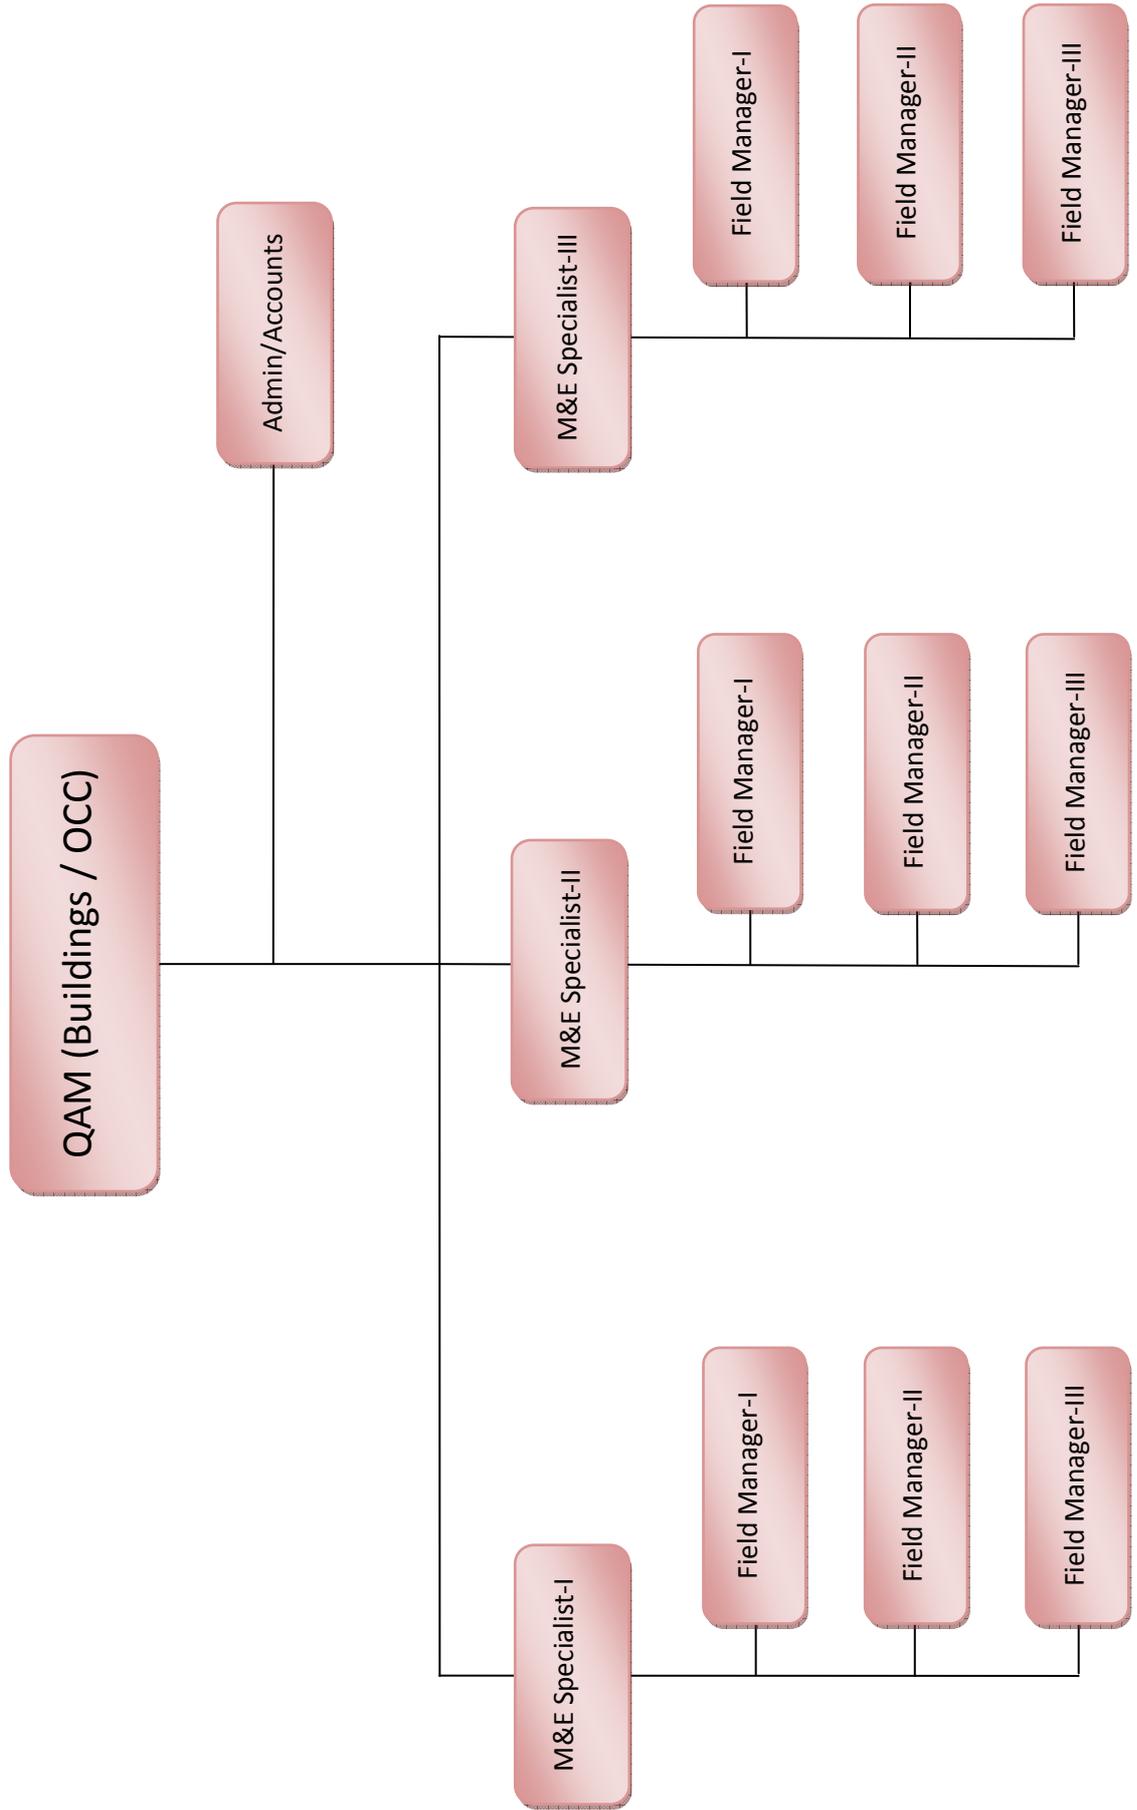


Figure 4.2: TEAM COMPOSITION-BUILDING COMPONENTS
USAID/PAKISTAN CONSTRUCTION MONITORING AND EVALUATION PROGRAM



**Figure 4.3: TYPICAL M&E SETUP –BUILDINGS
USAID/PAKISTAN CONSTRUCTION MONITORING AND EVALUATION PROGRAM**

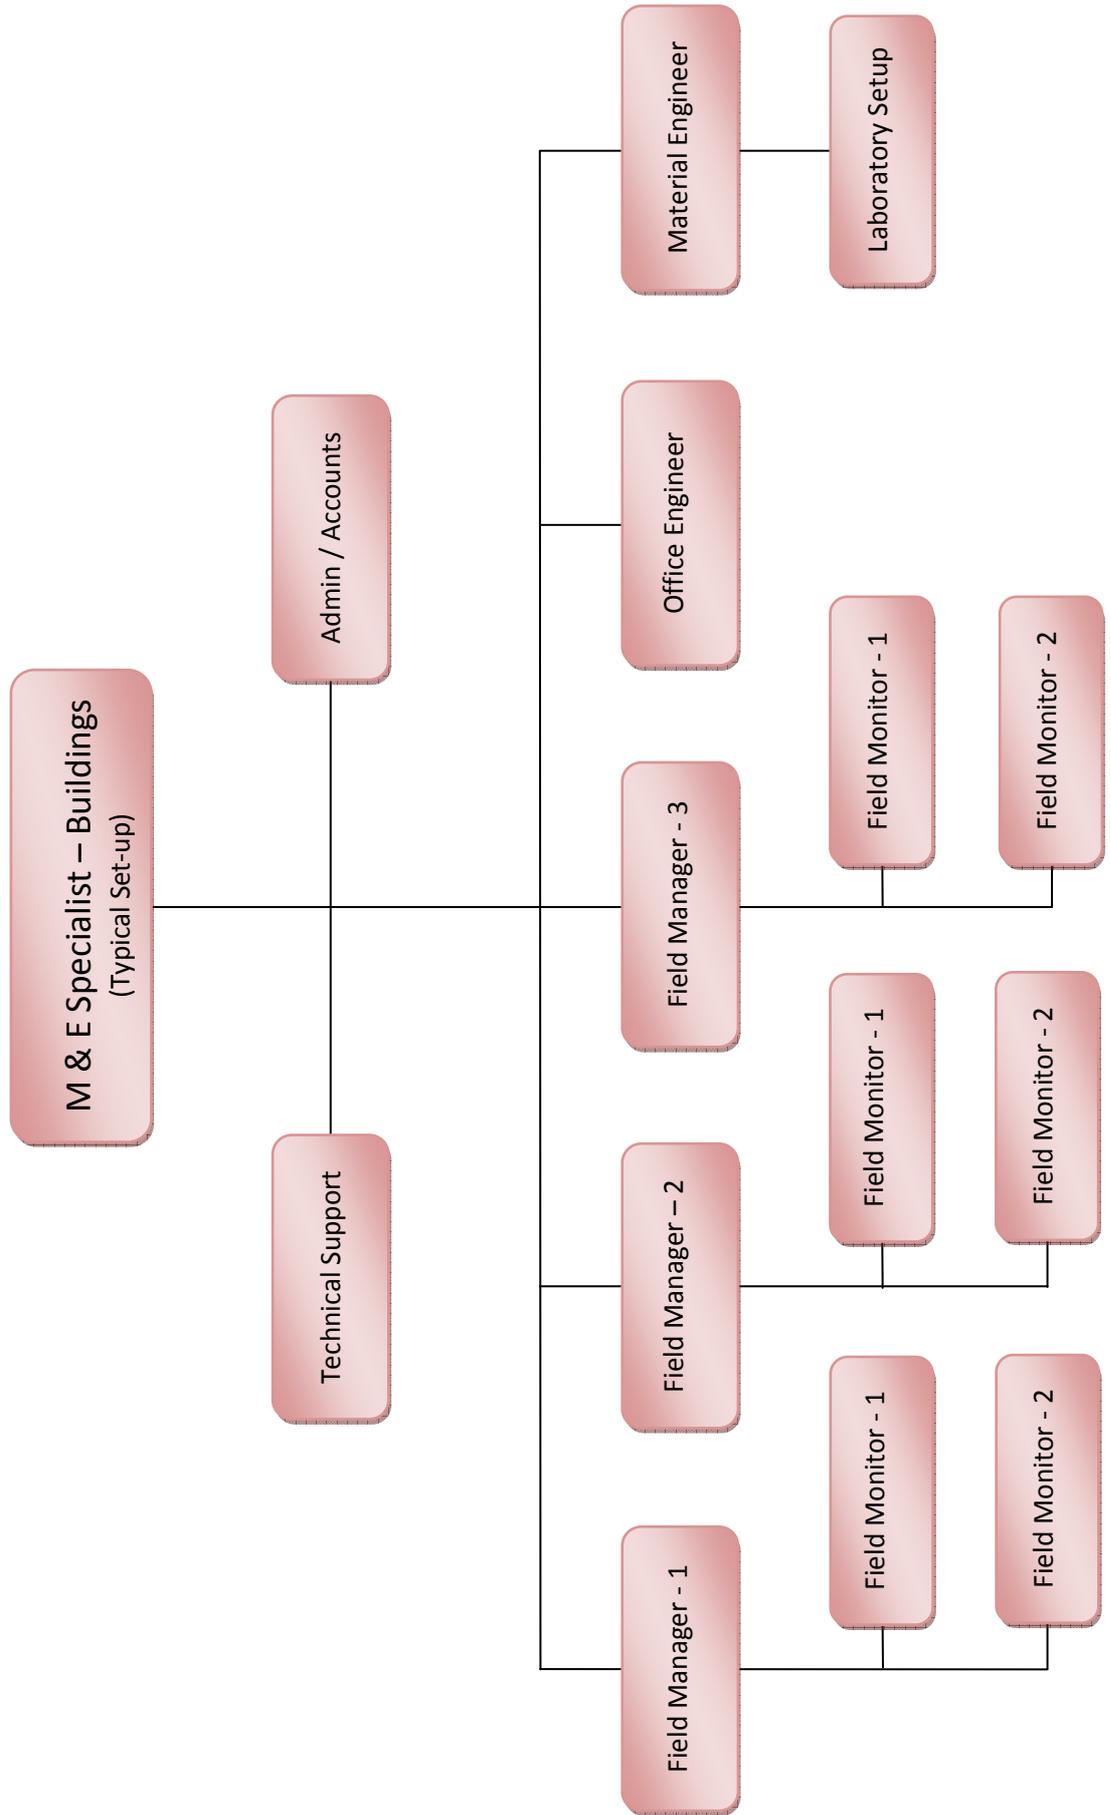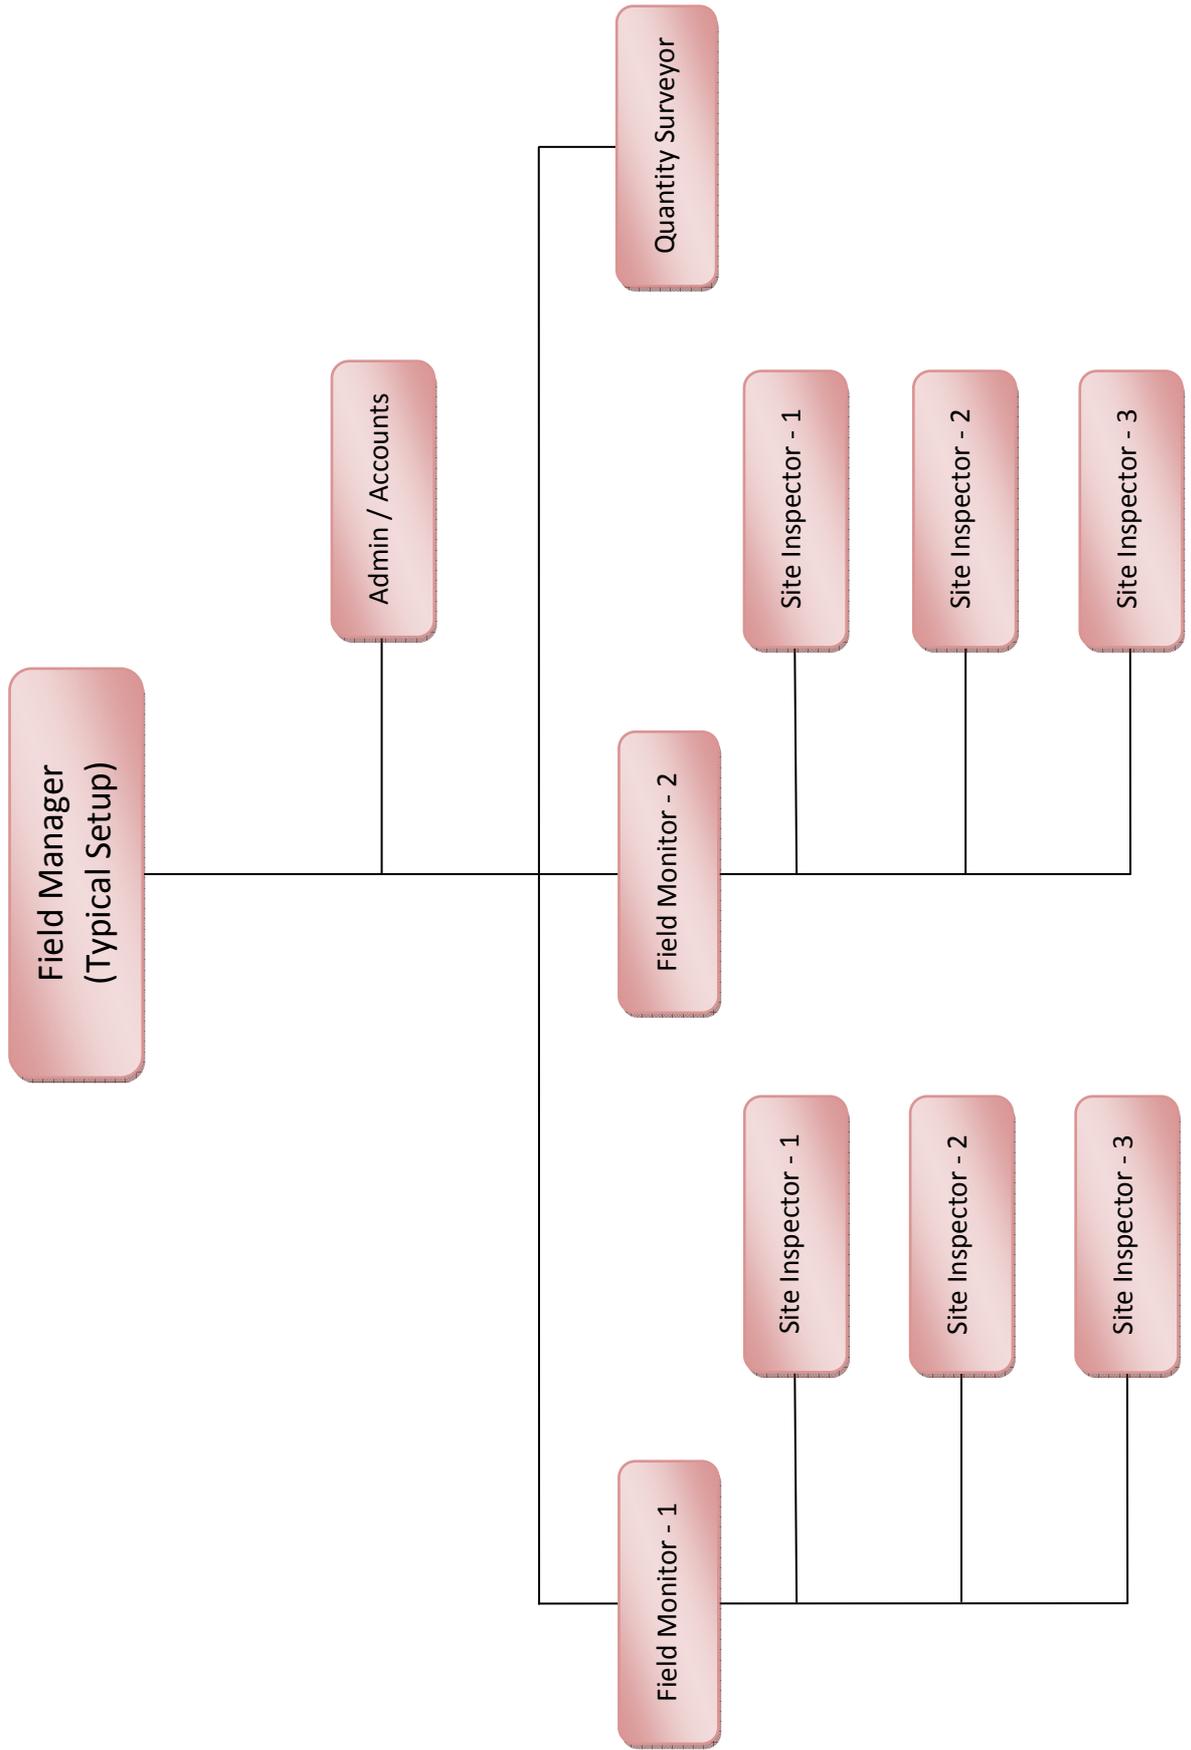

5. ITEMS REQUIRING ACTIONS

As stated in the Executive Summary, urgent action/decision of the concerned forums is required on the following points.

1. Formulation of a strategy for implementation of the schools construction needs to be finalized at the earliest.
2. Completion of requisite prequalification, tendering and construction contracting formalities for the 24 schools under PIL number 391-014-PIL-28 signed on October 29, 2013 so that the project moves forward to the construction stage without further loss of time.

ANNEXURES

ANNEXURE-I

(Minutes of Meetings)

MINUTES OF MEETING HELD ON JANUARY 07, 2014 AT THE CMEP OFFICE PESHAWAR

Construction Monitoring & Evaluation Program (CMEP), KP
(Building Component)
Minutes of Meeting Dated January 07, 2014.

A meeting was held at CMEP Project Office Peshawar on January 07, 2014 to review the pictures of 32 schools on which further clarification is required.

Following personnel participated in the meeting.

PaRRSA

- i. Mr. Tahir Kamran, Chief Infrastructure

AGES

- i. Mr. Ruidar Ali, Quality Assurance Manager
- ii. Mr. Muhammad Humayun, Field Manager
- iii. Mr. Amjad Saeed, Mid Level Specialist
- iv. Mr. Iftikhar Alam, Office Engineer

Following Agenda Points were discussed and decisions made thereon are tabulated as under:-

S.No	Agenda	Discussion and Decision
1	Review of Site Photographs of schools required further clarification	<p>The Site photographs of 32 schools were thoroughly reviewed. The decision made are discussed hereunder;</p> <p>District wise details are as under;</p> <p>1. <u>District Dir Lower</u></p> <p>Eight (08) schools have been thoroughly reviewed.</p> <ol style="list-style-type: none"> 1. GPS Chinar Kot has been agreed. 2. GGMS Kotkay, GGHSS Kumbar and GHS Sadbar Kalay have also been agreed, however PaRRSA will require structure integrity certificate of the existing schools building. 3. GMS Asigi Kalay has been agreed. Further, It has been decided that the name of GPS Asigi Kalay will be deleted from the list and their scope will be added in GMS Asigi Kalay. The Structure Integrity Certificate of existing school buildings will also be required. 4. GGPS Jabagai has been withheld till PaRRSA decide the implementation strategy. 5. GPS Sra Dhera has been agreed, however the remarks in the

		<p>validation report needs to be elaborated. Also the status of mutation of alternate land needs to be updated in the validation report.</p> <p>2. <u>District D.I Khan</u> Two (02) schools have been thoroughly reviewed.</p> <ol style="list-style-type: none"> 1. GPS Roda has been agreed. 2. GPS No. 1 Yarak has also been agreed, however PaRRSA will require structure integrity certificate of the existing school building. <p>3. <u>District Dir Upper</u> All nine (09) schools have been thoroughly reviewed.</p> <ol style="list-style-type: none"> 1. GPS Zakria, GPS Nihag, GPS Sundrai and GPS Sundal have been agreed. 2. GGPS Kotkai has also been agreed, however PaRRSA will require structure integrity certificate of the existing school building. 3. GPS Kass Barikot, GPS Remin Kass, GPS Tagi Sar and GPS Shomai have been agreed, however the remarks in the validation report needs to be elaborated. Also the status of mutation of alternate land needs to be updated in the validation report. <p>4. <u>District Malakand</u> Three (03) schools have been thoroughly reviewed.</p> <ol style="list-style-type: none"> 1. GHS Inzergai and GPS Jalal Kot have been agreed. 2. GPS Landai has been withheld till PaRRSA decide the implementation strategy. <p>5. <u>District Swat</u></p> <ol style="list-style-type: none"> 1. Six (06) schools have been thoroughly reviewed. All six schools including GPS No. 2 Maloach, GPS Chinda Khora, GGPS Kas, GPS Pacha Kalay, GPS Shaheed Baba & GPS Kanjo Chowk and GGPS Godha have been withheld till PaRRSA decide the implementation strategy.
--	--	--

		<p>6. <u>District Shangla</u></p> <p>Four (04) schools have been thoroughly reviewed.</p> <ol style="list-style-type: none"> 1. GPS Faiza and GPS Kandary Kormang have been agreed. 2. GPS Baglosar and GGHS Butyal Besham have been withheld till PaRRSA decide the implementation strategy.
2	Source of Information in Validation Report	<p>It has been decided that the source of information in the validation report also comprise the names of PaRRSA and Education Department officials visited the sites along the AGES team. The source of information column in the validation report needs to be updated.</p>



Meeting in the office of CMEP AGES dated: 07 January 2014



Meeting in the office of CMEP AGES dated: 07 January 2014

MINUTES OF MEETING HELD ON JANUARY 11, 2014 AT THE CMEP OFFICE PESHAWAR

Construction Monitoring & Evaluation Program (CMEP), KP
(Building Component)
Minutes of Meeting Dated January 11, 2014.

A meeting was held at CMEP Project Office Peshawar on January 11, 2014 to review the proposals of GHSS Akbar Pura, site/layout plans & site photographs of remaining 13 schools of 173 validated schools and assessment of damaged schools in District Lakki Marwat.

Following personnel participated in the meeting.

PaRRSA

- i. Mr. Tahir Kamran, Chief Infrastructure

AFKAR ASSOCIATES

- i. Mr. Mansoor, Principal Architect

AGES CONSULTANTS

- i. Mr. Aziz-ul-Haq, Project Manager
- ii. Mr. Nasir-ul-Mulk, Project Advisor
- iii. Mr. Ruidar Ali, Quality Assurance Manager
- iv. Mr. Muhammad Ishaq, Structure Engineer
- v. Mr. Muhammad Humayun, Field Manager
- vi. Mr. Amjad Saeed, Mid Level Specialist
- vii. Mr. Iftikhar Alam, Office Engineer
- viii. Mr. Waqar-ul-Mulk, Junior Architect

Following Agenda Points were discussed and decisions made thereon are tabulated as under:-

S.No	Agenda	Discussion and Decision
1	Review of decisions of last meeting (Dec 21, 2013)	Afkar Associates explain the compliance of decisions in the revised proposals as under; <ul style="list-style-type: none"> 1. Masjid has been excluded from USAID Scope. 2. Level of school building has been reviewed and agreed. 3. All class room sizes have been standardized as 24' x 18'. 4. Ramp has been provided to the first floor of school building. 5. Existing school buildings to be retained have been mentioned in the proposed layout drawing. 6. Offices in the administration block have been revised. 7. Comparative statement of existing and proposed building has

		<p>been prepared and shared.</p> <p>8. Detailed survey of main drain along the boundary of the school has been conducted.</p>
2	Review of revised proposal	<p>Afkar Associates has presented two proposals of the agreed layout plan. The discussion and decision made are given hereunder;</p> <ol style="list-style-type: none"> 1. Two (02) proposals have been presented by Afkar Associates in which proposal 2 has been agreed. 2. It has been decided that one (01) toilet for special students will be provided on each floor of the school building. 3. It has been decided that all those existing buildings will be dismantled which interrupt the proposed plan. According to which Laboratory, Principal office along with staff room and hall will be dismantled whereas two class rooms will be retained. 4. The existing servant quarter will be kept intact. 5. It has been decided that the school building will be designed as frame structure. 6. Grade-60 steel shall be used. 7. Exterior walls in the proposed school building will be 13.5" thick while the inner partition walls will be 9" thick. 8. It has been decided that water sample of the existing water facility will be collected and tested, as the water of the area is badly polluted by the flood 2010. 9. Bearing capacity test will be conducted before structure design of the school. 10. PaRRSA has advised to provide two doors with double leaf in each class room, as practice in modular drawings. The doors will be opened towards outside the class room. A sample modular drawings and BOQ will be shared with Afkar Associates. 11. Maintenance free material will be used in the proposed school building. 12. PaRRSA has advised Afkar Associates to prepare comparative statement of material. 13. PaRRSA has advised AGES Consultant to prepare a detailed technical report of existing facilities in the school. 14. PaRRSA has advised Afkar Associates and AGES Consultant to prepare preliminary design & drawings at the earliest, enabling PaRRSA to submit a proposal to USAID before January 31st, 2014.

3	Site/layout plans & photographs of remaining 13 schools	<p>The site/layout plans along with site photographs of remaining 13 schools of 173 validated schools have been thoroughly reviewed. The discussion and decision made are given here under;</p> <p>District wise details are as under;</p> <p>7. <u>District Charsadda</u></p> <p>Three (03) schools were discussed & agreed. The school wise details are as under;</p> <p>i. <u>GPS Kabali Koroona:</u></p> <p>M4 module (04 class rooms) along with a lavatory block & Development works has been agreed. The existing 02 class rooms were destroyed due to bomb blast. The school has 100 students and 02 teachers.</p> <p>ii. <u>GPS Zarawar Koroona:</u></p> <p>M3 module (06 class rooms) along with two toilets & Development works has been agreed. The existing 02 class rooms were destroyed due to bomb blast. The school has 176 students and 03 teachers.</p> <p>iii. <u>GPS Mansooka:</u></p> <p>M7 module (04 class rooms) along with lavatory block & Development works has been agreed. The existing 02 class rooms were in deplorable condition. The school has 128 students and 02 teachers.</p> <p>8. <u>District Dir Lower</u></p> <p>One (01) school was discussed & agreed. The school wise details are as under;</p> <p>i. <u>GHSS Ouch:</u></p> <p>Two No. M3(H) modules (12 class rooms), M6 module</p>
---	---	---

(Principal Office, Staff Room, 02 Class Rooms & Examination Hall), M11 module (Library, Laboratory & 02 Class Rooms), M12 module (2 x Laboratory & Examination Hall) along with two lavatory blocks & developmental works have been agreed. The school comprises of three buildings. One building has been used by higher secondary section, while the other two buildings were used by high section of the school. The higher secondary building was in good condition and will remain intact. Both the buildings of high section were in deplorable condition and will be dismantled. The school has 758 students & 35 teachers.

9. District Dir Upper

Five (05) schools were discussed & agreed. The school wise details are as under;

i. GHS Barikot:

T4(H) modules (04 Class Rooms), T6 module (Principal Office, Staff Room, 02 Class Rooms & Examination Hall), T11 module (Library, Laboratory & 02 Class Rooms) along with a lavatory block & developmental works have been agreed. The existing school building was washed away by flood 2010. The existing school site is not suitable for reconstruction being located in water way therefore the school will be reconstructed on alternate land. The mutation paper of alternate land will be required. The school has 275 students.

ii. GPS No. 2 Besho:

GPS No. 2 Besho has been withheld till PaRRSA decide the implementation Strategy.

iii. GHS Jan Bathi:

GHS Jan Bathi has been withheld till PaRRSA decide the implementation Strategy.

		<p>iv. <u>GHS Nihag:</u> GHS Nihag has been withheld till PaRRSA decide the implementation Strategy.</p> <p>v. <u>GPS Sperko:</u> GPS Sperko has been withheld till PaRRSA decide the implementation Strategy.</p> <p>10. <u>District Swat</u> One (01) school was discussed & agreed. The school wise details are as under;</p> <p>i. <u>GPS Godha:</u> GPS Godha has been withheld till PaRRSA decide the implementation Strategy.</p> <p>11. <u>District Shangla</u> Three (03) schools were discussed & agreed. The school wise details are as under;</p> <p>i. <u>GHS Shangla:</u> T4(H) module (04 Class Rooms), T6 module (Principal Office, Staff Room, 02 Class Rooms & Examination Hall), T11 module (Library, Laboratory & 02 Class Rooms) along with a lavatory block & developmental works have been agreed. The existing school building was destroyed due to land sliding. The existing school site is not suitable for reconstruction therefore the school will be reconstructed on alternate land. The mutation paper of alternate land will be required. The school has 271 students and 07 teachers.</p>
--	--	---

		<p>ii. <u>GPS Shangla:</u> T3 module (06 Class Rooms) along with a lavatory block & developmental works has been agreed. The existing school building was destroyed due to land sliding. The existing school site is not suitable for reconstruction therefore the school will be reconstructed on alternate land. The mutation paper of alternate land will be required. The school has 238 students and 04 teachers.</p> <p>iii. <u>GGPS Karshat:</u> GGPS Karshat has been withheld till PaRRSA decide the implementation Strategy.</p>
4	Assessment of Damaged Schools in District Lakki Marwat.	PaRRSA has advised AGES Consultant to initiate the assessment and physical survey of damaged schools in District Lakki Marwat.

MINUTES OF MEETING HELD ON JANUARY 13, 2014 AT THE CMEP OFFICE PESHAWAR

Construction Monitoring & Evaluation Program (CMEP), KP
(Building Component)
Minutes of Meeting Dated January 13, 2014.

A meeting was held at CMEP Project Office Peshawar on January 13, 2014 to review the proposal of GHSS Akbar Pura, pictures of those schools on which further clarification is required.

Following personnel participated in the meeting.

USAID

- i. Mr. Bahrobar, Engineer

PaRRSA

- i. Mr. Tahir Kamran, Chief Infrastructure

AGES

- i. Mr. Naseer M Khan, Team Leader, M&E Project Malakand.
- ii. Mr. Aziz-ul-Haq, Project Manager
- iii. Mr. Nasir-ul-Mulk, Project Advisor
- iv. Mr. Ruidar Ali, Quality Assurance Manager
- v. Mr. Muhammad Ishaq, Structure Engineer
- vi. Mr. Muhammad Humayun, Field Manager
- vii. Mr. Amjad Saeed, Mid Level Specialist
- viii. Mr. Iftikhar Alam, Office Engineer

Following Agenda Points were discussed and decisions made thereon are tabulated as under:-

S.No	Agenda	Discussion and Decision
1	GHSS Akbar Pura	Proposals of GHSS Akbar Pura have been shared with USAID. Both the proposals have been reviewed. Proposal No. 2 has been agreed.
2	Review of Site Photographs of schools required further clarification	<p>Site photographs of those schools were thoroughly reviewed which required clarification. The decision made are discussed hereunder;</p> <p>District wise details are as under;</p> <p>12. <u>District Swat</u></p> <p>Seven (07) schools have been thoroughly reviewed.</p> <ul style="list-style-type: none"> 6. GGPS Kas and GPS Godha have been agreed. 7. GPS No. 2 Maloach has been agreed with scope revision from

		<p>T4 module (04 class room), lavatory block and developmental works to M3 module (06 class rooms) and developmental works. The existing toilets will remain intact. PaRRSA will require structure integrity certificate of the existing school building.</p> <p>8. GPS Chinda Khora has been agreed with scope revision from T3 module (06 class room), lavatory block and developmental works to M3 module (06 class rooms), M7 module (04 class rooms), lavatory block and developmental works. PaRRSA will require structure integrity certificate of the existing school building.</p> <p>9. GPS Pacha Kalay has been agreed with scope revision from T4 module (04 class room) and lavatory block to T3 module (06 class rooms) and lavatory block. PaRRSA will require structure integrity certificate of the existing school building.</p> <p>10. GGPS Godha has been agreed. PaRRSA will require structure integrity certificate of the existing school building.</p> <p>11. GPS Shaheed Baba & GPS Kanjo Chowk has been dropped.</p> <p>13. <u>District Shangla</u></p> <p>Two (02) schools have been thoroughly reviewed.</p> <ol style="list-style-type: none"> 1. GPS Baglo Sar has been agreed. 2. GGHS Butyal Besham has been dropped. 3. GGPS Karshat has been withheld till PaRRSA decide the implementation Strategy.
3	Review of Pictures of high and higher secondary schools	<p>USAID has intended to reconstruct some high and higher secondary schools. Fourteen (14) schools have been assessed and physical surveyed, in which the following four (04) schools have been selected for further developmental of proposals through Afkar Associates.</p> <ol style="list-style-type: none"> 1. GHSS Bagh, District Dir Lower 2. GHSS Lal Qila, District Dir Lower 3. GHSS Kabal, District Swat 4. GHSS Kot, District Malakand

ANNEXURE-II

(E-Mails)

S.No.	From	To	Date	Subject
1	QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 10, 2014	Submission of Draft site/layout plans and photographs of 13 remaining schools CMEP KP
2	QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 14, 2014	Scope of remaining 07 schools of 61 listed schools CMEP KP
3	QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 14, 2014	Scope of remaining 07 schools of 173 listed schools CMEP KP
4	QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 15, 2014	List of Flood & Militancy damaged schools in District Lakki Marwat
5	QAM (Building) AGES	Chief Infrastructure PaRRSA & Engineer USAID	Jan 20, 2014	Final MOM dated Jan 07, 11 & 13 2014 (CMEP-Building Component)
6	QAM (Building) AGES	Engineer USAID	Jan 21, 2014	Quarterly Progress Report ending on December 31, 2013 for CMEP Building Component KP

S.No.	From	To	Date	Subject
7	QAM (Building) AGES	Engineer USAID	Jan 28, 2014	Review of Engineer's Estimates of flood PIL having 63 schools, CMEP
8	QAM (Building) AGES	Engineer USAID	Jan 28, 2014	Draft Layout plans of 04 higher secondary schools, CMEP KP
9	QAM (Building) AGES	Engineer USAID	Jan 31, 2014	Corrected EDF of 24 Schools of PIL-28 (Building Component-CMEP)

Email # 01

From	To	Date	Subject
QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 10, 2014	Submission of Draft site/layout plans and photographs of 13 remaining schools CMEP KP

Subject:	Submission of Draft site/layout plans and photographs of 13 remaining schools CMEP KP
From:	Ruidar ali (ruidarali@hotmail.com)
To:	tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk;
Cc:	azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com;
Date:	Friday, January 10, 2014 12:30 PM

Dear Tahir Kamran sahib,

As desired, the CD having draft site/layout plans and photographs of 13 remaining schools are being delivered through special messenger at your home, please.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Email # 02

From	To	Date	Subject
QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 14, 2014	Scope of remaining 07 schools of 61 listed schools CMEP KP

Subject:	Scope of remaining 07 schools of 61 listed schools CMEP KP
From:	Ruidar ali (ruidarali@hotmail.com)
To:	tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk;
Cc:	engineeramjadsaeed@hotmail.com; m.humayun.k@gmail.com; alam.iftikhar@yahoo.com;
Date:	Tuesday, January 14, 2014 12:26 PM

Dear Tahir Kamran sahib,

As discussed & agreed in the meeting held on January 13, 2014 at CMEP project office Peshawar, the list of remaining 07 schools of 61 listed schools having agreed scope is attached for inclusion in the list of upcoming PIL.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Email # 03

From	To	Date	Subject
QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 14, 2014	Scope of remaining 07 schools of 173 listed schools CMEP KP

Subject:	Scope of remaining 07 schools of 173 listed schools CMEP KP
From:	Ruidar ali (ruidarali@hotmail.com)
To:	tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk;
Cc:	engineeramjadsaeed@hotmail.com; m.humayun.k@gmail.com; alam.iftikhar@yahoo.com;
Date:	Tuesday, January 14, 2014 10:51 AM

Dear Tahir Kamran sahib,

As discussed & agreed in the meeting held on January 11, 2014 at CMEP project office Peshawar, the list of 07 schools of 173 listed schools having the agreed scope is attached for inclusion in the list of upcoming PIL.

Kindly ignore the previous emails in this connection. Inconvenience is high regretted.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Email # 04

From	To	Date	Subject
QAM (Building) AGES	Chief Infrastructure PaRRSA	Jan 15, 2014	List of Flood & Militancy damaged schools in District Lakki Marwat

Subject:	RE: List of Flood & Militancy damaged schools in District Lakki Marwat
From:	Ruidar ali (ruidarali@hotmail.com)
To:	tahirkamran@pdma.gov.pk; tahirkamran70@yahoo.com;
Cc:	azizages@gmail.com; cmep@ages.com.pk; m.humayun.k@gmail.com; alam.iftikhar@yahoo.com; engineeramjadsaeed@hotmail.com;
Date:	Wednesday, January 15, 2014 9:05 AM

Dear Tahir Kamran sahib,

Thanks,

We have already deputed the survey team for physical survey & assessment of the subject listed schools.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Wed, 15 Jan 2014 08:53:32 +0500

Subject: Re: FW: List of Flood & Militancy damaged schools in District Lakki Marwat

From: tahirkamran@pdma.gov.pk

To: ruidarali@hotmail.com

Kindly do the needful as discussed.

On Mon, Jan 13, 2014 at 11:59 AM, Ruidar ali <ruidarali@hotmail.com> wrote:

Dear Tahir Kamran sahib,

As desired, the list of damaged schools in District Lakki Marwat is attached for appropriate action at your end, please.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

From: ruidarali@hotmail.com

To: alam.iftikhar@yahoo.com

Subject: FW: List of Flood & Militancy damaged schools in District Lakki Marwat

Date: Sat, 11 Jan 2014 08:50:09 +0500

plz get print

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

From: ruidarali@hotmail.com
To: m.humayun.k@gmail.com
Subject: FW: List of Flood & Militancy damaged schools in District Lakki Marwat
Date: Fri, 23 Aug 2013 10:41:35 +0500

fyi, plz.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

From: ruidarali@hotmail.com
To: tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk
CC: alam.iftikhar@yahoo.com
Subject: List of Flood & Militancy damaged schools in District Lakki Marwat
Date: Fri, 16 Aug 2013 09:50:55 +0500

Dear Tahir Kamran sahib,
As discussed on telephone, the list of Flood & Militancy Damaged schools provided by District Education Officer District Lakki Marwat is attached for information & further appropriate action at your end.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Best Regards

**Engr. Tahir Kamran Marwat
Chief Infrastructure,**

Provincial Reconstruction, Rehabilitation & Settlement Authority (PaRRSA)

Civil Secretariat, Peshawar.

Mobile#. +92 (0) 333 9152288

Office #. +92 (91) 9213250/ 9213867

Fax #. +92 (91) 9212167

Email # 05

From	To	Date	Subject
QAM (Building) AGES	Chief Infrastructure PaRRSA & Engineer USAID	Jan 20, 2014	Final MOM dated Jan 07, 11 & 13 2014 (CMEP-Building Component)

Subject:	Final MOM dated Jan 07, 11 & 13 2014 (CMEP-Building Component)
From:	Ruidar ali (ruidarali@hotmail.com)
To:	tahirkamran@pdma.gov.pk; bahrobar@usaid.gov; bahrobar@gmail.com; azizages@gmail.com; cmep@ages.com.pk;
Cc:	tahirkamran70@yahoo.com; fbanori@usaid.gov; naseer@ages.com.pk; nasir@ages.com.pk; ishaqkhan74@yahoo.com; m.humayun.k@gmail.com; engineeramjadsaeed@hotmail.com; alam.iftikhar@yahoo.com;
Date:	Monday, January 20, 2014 12:07 PM

Dear All,

As desired, the final MOM dated January 07, 11 & 13, 2014 are attached for your information and record please.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Mon, 20 Jan 2014 10:09:13 +0500
Subject: Re: Draft MOM dated Jan 07, 11 & 13 2014 (CMEP-Building Component)
From: tahirkamran@pdma.gov.pk
To: ruidarali@hotmail.com
CC: tahirkamran70@yahoo.com; azizages@gmail.com; cmep@ages.com.pk

Thanks for sharing the minutes of the meeting. Reviewed and found okay for onward circulation to all stake holders for early compliance.

On Fri, Jan 17, 2014 at 10:15 AM, Ruidar ali <ruidarali@hotmail.com> wrote:
Dear Tahir Kamran Sahib,

As desired the draft MOM of January 07, 11 & 13, 2014 are attached for your information and review please.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Best Regards

Engr. Tahir Kamran Marwat

**Chief Infrastructure,
Provincial Reconstruction, Rehabilitation & Settlement Authority (PaRRSA)**

Civil Secretariat, Peshawar.

Mobile#. +92 (0) 333 9152288

Office #. +92 (91) 9213250/ 9213867

Fax #. +92 (91) 9212167

Email # 06

From	To	Date	Subject
QAM (Building) AGES	Engineer USAID	Jan 21, 2014	Quarterly Progress Report ending on December 31, 2013 for CMEP Building Component KP

Subject:	FW: Quarterly Progress Report ending on December 31, 2013 for CMEP Building Component KP.(Part 2)
From:	Ruidar ali (ruidarali@hotmail.com)
To:	bahrobar@gmail.com; bahrobar@usaid.gov;
Cc:	tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk; fbanori@usaid.gov; azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com;
Date:	Tuesday, January 21, 2014 6:56 PM

Dear Bahrobar sahib,

The 2nd part having Annexures III, IV & V is attached as mentioned in the previous email below.

Best Regards,
Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

From: ruidarali@hotmail.com

To: bahrobar@usaid.gov; bahrobar@gmail.com

CC: tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk; fbanori@usaid.gov; azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com

Subject: Quarterly Progress Report ending on December 31, 2013 for CMEP Building Component KP.

Date: Tue, 21 Jan 2014 18:50:38 +0500

Dear Bahrobar sahib,

As desired, we are pleased to submit herewith the Quarterly Progress Report ending on December 31, 2013 for CMEP Building Component KP, for review & further appropriate action at your end. kindly note that we have bifurcated the document into the following two parts as the same couldn't be sent in one email due its large size.

Quarterly Progress Report and Annexures I & II (Part 1, below) are attached, whereas the Annexures III, IV & V

(Part 2, below) will be shared through subsequent email.

Part 1. Quarterly Progress Report and Annexures I & II,
part 2. Annexures (III, IV & V).

Hope this will meet your requirements.

Best Regards,
Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Email # 7

From	To	Date	Subject
QAM (Building) AGES	Engineer USAID	Jan 28, 2014	FW: Review of Engineer's Estimates of flood PIL having 63 schools, CMEP

Subject:	FW: Review of Engineer's Estimates of flood PIL having 63 schools, CMEP
From:	Ruidar ali (ruidarali@hotmail.com)
To:	bahrobar@usaid.gov;
Cc:	azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com; fbanori@usaid.gov
Date:	Tue, 28 Jan 2014 12:34:04 +0500

Dear Bahrobar Sahib,

As desired, the requisite summary is attached.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Tue, 28 Jan 2014 12:26:34 +0500

Subject: Re: Review of Engineer's Estimates of flood PIL having 63 schools, CMEP

From: bahrobar@usaid.gov

To: ruidarali@hotmail.com

CC: azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com; fbanori@usaid.gov

There is some problem in opening the summary sheet, please re-send the summary sheet only. thanks

On Tue, Jan 28, 2014 at 11:50 AM, Ruidar ali <ruidarali@hotmail.com> wrote:

Dear Bahrobar Sahib,

As desired, the requisite documents are attached as winzip.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Tue, 28 Jan 2014 11:07:30 +0500

Subject: Re: Review of Engineer's Estimates of flood PIL having 63 schools, CMEP

From: bahrobar@usaid.gov

To: ruidarali@hotmail.com

CC: azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com; fbanori@usaid.gov

Dear Ruidar Sb,
Please send me the attachment as zipped file. our systems doesn't support rar files.
Regards,

On Mon, Jan 27, 2014 at 3:57 PM, Ruidar ali <ruidarali@hotmail.com> wrote:

Dear Bahrobar Sahib,

As desired, please find attached corrected summary of payment milestone and district wise modular milestones for information and appropriate action at your end.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Fri, 24 Jan 2014 12:34:16 +0500

Subject: Re: Review of Engineer's Estimates of flood PIL having 63 schools, CMEP

From: bahrobar@usaid.gov

To: ruidarali@hotmail.com

CC: azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com; fbanori@usaid.gov

Dear Ruidar Sb,

Subject table contains some mistakes. for example cost of M1 in peshawar is shown 35.8746Million whereas the actual cost in summary is about 11.96M.

I will recommend to please give full reading/attention to PIL No.28 for 24 flood damaged schools and then workout this sheet and rest of the milestones tables as discussed in the morning.

Regards,

On Thu, Jan 23, 2014 at 9:19 AM, Ruidar ali <ruidarali@hotmail.com> wrote:

Dear Bahrobar sahib,

As desired, the estimates shared by USAID vide email below, have been thoroughly checked and reviewed. During the review process, it was observed that the estimated cost of PIL(63 schools) shown in the summary provided by PaRRSA is 15% more than the site specific cost. Main reasons for the increase in cost are given here under;

1. Percentage of steel reinforcement has been increased.
2. Quantity of structural steel(truss) has been increased.
3. Maximum Developmental cost in a specific region has been applied to all schools in that region.

The payment milestones for 63 schools is also attached as desired.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Fri, 17 Jan 2014 09:25:09 +0500
Subject: Fwd: Flood Pil
From: bahrobar@usaid.gov
To: ruidarali@hotmail.com; azizages@gmail.com

Dear Ruidar Sb,
Attached please find detailed cost estimates etc. for the 63 schools for your review and certification. your's earliest response would enable us to initiate the PIL the soonest.
Regards,
Bahrobar

----- Forwarded message -----

From: **Tahir Kamran** <tahirkamran@pdma.gov.pk>
Date: Fri, Jan 17, 2014 at 8:56 AM
Subject: Fwd: Flood Pil
To: "Bahrobar (USAID/Pak/FATA)" <Bahrobar@usaid.gov>, "Banori, Farhat Ali Shah(USAID/Pak/FATA)" <fbanori@usaid.gov>

Kindly download the attachment for further processing at your end.

Best Regards

Engr. Tahir Kamran Marwat
Chief Infrastructure,
Provincial Reconstruction, Rehabilitation & Settlement Authority (PaRRSA)
Civil Secretariat, Peshawar.
Mobile#. +92 (0) 333 9152288
Office #. +92 (91) 9213250/ 9213867
Fax #. +92 (91) 9212167

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

Email # 08

From	To	Date	Subject
QAM (Building) AGES	Engineer USAID	Jan 28, 2014	Draft Layout plans of 04 higher secondary schools, CMEP KP

Subject:	Draft Layout plans of 04 higher secondary schools, CMEP KP
From:	Ruidar ali (ruidarali@hotmail.com)
To:	bahrobar@usaid.gov; bahrobar@gmail.com;
Cc:	tahirkamran70@yahoo.com; tahirkamran@pdma.gov.pk; azizages@gmail.com; cmep@ages.com.pk; engineeramjadsaeed@hotmail.com;
Date:	Tuesday, January 28, 2014 3:25 PM

Dear Bahrobar sahib,

As discussed on telephone, the draft layout plans of 04 higher secondary schools (02 of District Dir Lower, 01 of District Malakand and 01 of District Swat) are attached for your information & review. kindly note that we have applied the modules already in practice, keeping in view the site specific conditions and requirements. The module of GHSS Akbar Pura (Fully or Partially) cannot be accommodated due to site condition, required scope and land constraints.

Keeping in view the time limitation, we would suggest to use the modular arrangement with architectural enhancing/elaborating exterior finishing to give different exterior look to the school buildings. This would further make easier cost estimation and other documentation required for furnishing PIL for these schools.

Best Regards,

Ruidar Ali

Quality Assurance Manager (Building), AGES

Construction, Monitoring & Evaluation Program (CMEP), KPK

Phone # +92-91-5863291-92-93

Mobile # +92-300-5902745

Email # 9

From	To	Date	Subject
QAM (Building) AGES	Engineer USAID	Jan 31, 2014	Corrected EDF of 24 Schools of PIL-28 (Building Component-CMEP))

Subject:	Corrected EDF of 24 Schools of PIL-28 (Building Component-CMEP))
From:	ruidarali@hotmail.com
To:	bahrobar@usaid.gov; bahrobar@gmail.com;
CC:	azizages@gmail.com; cmep@ages.com.pk; sakhan53@gmail.com; engineeramjadsaeed@hotmail.com; guskhanja@student.gu.se
Date:	Fri, 31 Jan 2014 14:32:12 +0500

Dear Bahrobar Sahib,

As desired, the corrected EDF of 24 schools of PIL-28 is attached for information and further appropriate action at your end.

Best Regards,

Ruidar Ali

Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745

Date: Wed, 22 Jan 2014 12:19:22 +0500
Subject: Fwd: EDF of 24 Schools of PIL-1 (Building Component-CMEP)
From: bahrobar@usaid.gov
To: ruidarali@hotmail.com

Dear Ruidar Sb,
Please refer below e-mail for revision of the EDFs as discussed.
Thanks

----- Forwarded message -----

From: **Asim Aziz** <aaziz@usaid.gov>
Date: Tue, Jan 7, 2014 at 3:33 PM
Subject: Re: EDF of 24 Schools of PIL-1 (Building Component-CMEP)
To: Bahro Bar <bahrobar@usaid.gov>

Dear Bahrobar,
As we discussed earlier on that the contents of latest submitted EDF do not address the earlier comments and need an update with a careful review both by USAID contractor and by yourself, I just wanted to know where we are at the moment on this? and when can we expect final submission.

All the very best,

--

Asim Aziz

Deputy MEO / AID Development Program Specialist | **USAID/Pakistan**, Program Office | US
Embassy | Islamabad
Cell: +92 300 832 7110 | Office: +92 51 208 1442 | Fax: +92-51-287-0310 | Email: aaziz@usaid.gov

On Fri, Dec 6, 2013 at 8:46 AM, Bahro Bar <bahrobar@usaid.gov> wrote:

Dear Asim Aziz,
Attached please find revised EDFs for the 24 flood damaged Schools for your review and subsequent clearance. Once you clear it, Will provide the hard version for signature.
Thanks

----- Forwarded message -----

From: **Ruidar ali** <ruidarali@hotmail.com>
Date: Thu, Dec 5, 2013 at 4:44 PM
Subject: RE: EDF of 24 Schools of PIL-1 (Building Component-CMEP)
To: Bahrobar sahib <bahrobar@usaid.gov>, "bahrobar@gmail.com" <bahrobar@gmail.com>
Cc: Farhat Banori <fbanori@usaid.gov>, "azizages@gmail.com" <azizages@gmail.com>, "cmep@ages.com.pk" <cmep@ages.com.pk>, Amjad saeed <engineeramjadsaeed@hotmail.com>, Shabir AGES <sakhan53@gmail.com>

Dear Bahrobar Sahib,

As desired, the revised EDFs for 24 schools of PIL-28 (CMEP-KP) are attached for your information & further appropriate action please.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Wed, 4 Dec 2013 15:58:36 +0500

Subject: Re: EDF of 24 Schools of PIL-1 (Building Component-CMEP)
From: bahrobar@usaid.gov
To: ruidarali@hotmail.com
CC: azizages@gmail.com

OK Thanks.

On Wed, Dec 4, 2013 at 3:34 PM, Ruidar ali <ruidarali@hotmail.com> wrote:
Dear Bahrobar sahib,
Since we were busy in compilation of validation report of 173 schools and engineer's estimate of 61 schools for upcoming PIL-29, therefore, could't sent the EDF as desired. Hopefully, you will get it by tomorrow

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Wed, 4 Dec 2013 15:09:42 +0500

Subject: Re: EDF of 24 Schools of PIL-1 (Building Component-CMEP)
From: bahrobar@usaid.gov
To: ruidarali@hotmail.com; azizages@gmail.com

Dear Ruidar Sb,

Can we have any updates on the revised EDF. USAID can't reimburse a single \$ to PaRRSA until EDF is approved by USAID, for the 24 flood damaged schools PaRRSA is preparing to send us mobilization cost voucher in couple of weeks.

Thanks

On Tue, Nov 19, 2013 at 12:34 PM, Bahro Bar <bahrobar@usaid.gov> wrote:

Dear Ruidar Sb,

Attached please find comments of USAID MEO on the EDF for 24 flood damaged Schools. Sample EDFs are attached as well for revision and modification.

Thanks

----- Forwarded message -----

From: **Asim Aziz** <aaziz@usaid.gov>
Date: Wed, Nov 13, 2013 at 5:02 PM
Subject: Re: EDF of 24 Schools of PIL-1 (Building Component-CMEP)
To: Bahro Bar <bahrobar@usaid.gov>
Cc: "Banori, Farhat Ali Shah(USAID/Pak/FATA)" <fbanori@usaid.gov>

Dear Bahrobar,

Attached file contain my comments (which are applicable to all 24 EDF/EMMP). I hope these can be addressed easily. I have also attached two sample USAID approved EDFs/EMMPs for quick reference to teh identified comments in the submitted file.

After addressing all comments, please submit duly signed (names and official stamp) version for final signatures. Don't hesitate to contact me for further guidance.

All the best,

--

Asim Aziz

Deputy MEO / AID Development Program Specialist | **USAID/Pakistan**, Program Office | US
Embassy | Islamabad

Cell: +92 300 832 7110 | Office: +92 51 208 1442 | Fax: +92-51-287-0310 | Email: aaziz@usaid.gov

On Wed, Nov 13, 2013 at 12:28 PM, Bahro Bar<bahrobar@usaid.gov> wrote:

Dear Asim Aziz,

Can we have any updates on the prescribed EDFs, Govt of KP Requested Reimbursement against certain milestones and we can't process until we have EDF approved.

Regards

On Tue, Sep 10, 2013 at 9:29 AM, Bahro Bar<bahrobar@usaid.gov> wrote:

Dear Asim,

Attached please find EDF for the 24 flood damaged school's reconstruction for your review and comments.
thanks bahrobar

----- Forwarded message -----

From: **Ruidar ali**<ruidarali@hotmail.com>

Date: Fri, Sep 6, 2013 at 3:22 PM

Subject: EDF of 24 Schools of PIL-1 (Building Component-CMEP)

To: Bahrobar sahib <bahrobar@usaid.gov>

Cc: "Aziz-ul-Haq Engr." <azizages@gmail.com>, Farhat Banori <fbanori@usaid.gov>, "Rabbi, Fazal (USAIDPakFATA)" <frabbi@usaid.gov>, Tahirkamran sahib PDMA <tahirkamran@pdma.gov.pk>, Tahir Kamran sahib <tahirkamran70@yahoo.com>, Shabir AGES <sakhan53@gmail.com>, Amjad saeed <engineeramjadsaeed@hotmail.com>

Dear Bahrobar Sahib,

As desired, the EDF of 24 schools of PIL-1 (Building Component-CMEP) is attached for your information and further necessary action please.

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

Date: Wed, 21 Aug 2013 16:13:25 +0500

Subject: Re: Milestone for PIL-1

From: bahrobar@usaid.gov

To: ruidarali@hotmail.com

CC: azizages@gmail.com;fbanori@usaid.gov;FRabbi@usaid.gov;tahirkamran@pdma.gov.pk;naseer@ages.com.pk

Dear Ruidar Sb,

We are in the process of constituting PIL for the 24 flood damaged schools to be signed with PaRRSA, while in the meantime we need to have our Environmental Documentation Form ready for USAID's review and approval.

PaRRSA can't get reimbursed until they have final EDF approved by USAID. Though it's PaRRSA's work but as support being provided by AGES throughout in the M & E for Malakand, here also we need to proceed accordingly.

You may please take help from Naseer Sb on getting the formats etc. as they have already crossed these stages.

Regards,
Bahrobar

On Wed, Aug 21, 2013 at 3:31 PM, Bahro Bar <bahrobar@usaid.gov>wrote:

Thanks Ruidar Sb. Now it works.

On Wed, Aug 21, 2013 at 3:23 PM, Ruidar ali<ruidarali@hotmail.com>wrote:

FYI please

Best Regards,

Ruidar Ali

*Quality Assurance Manager (Building), AGES
Construction, Monitoring & Evaluation Program (CMEP), KPK
Phone # +92-91-5863291-92-93
Mobile # +92-300-5902745*

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov

BAHROBAR | Engineer (Buildings & Roads) | U.S. Embassy, Diplomatic Enclave, Islamabad | Cell : 0300-8505334 | Desk: 051-2081204 | E-mail:bahrobar@usaid.gov
