


4970215/53

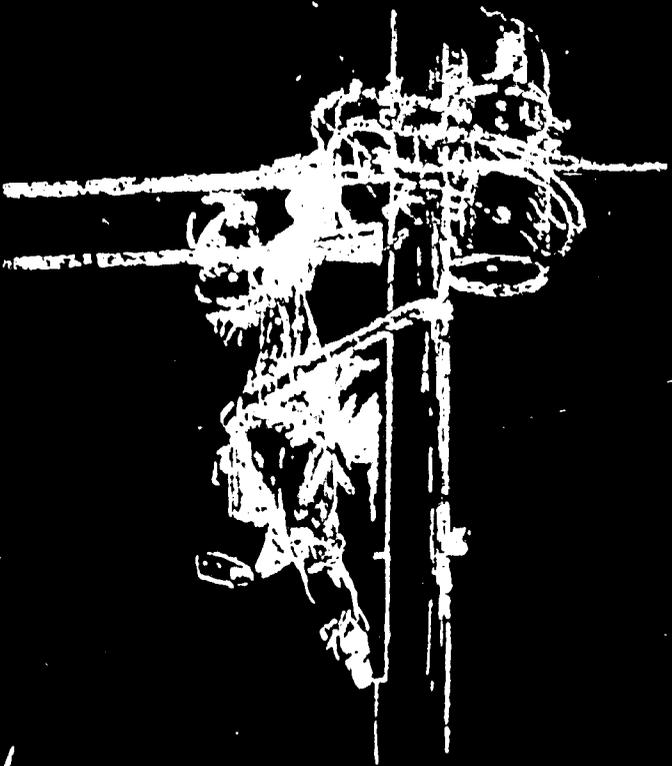

**PERUSAHAAN**

**UMUM**

**LISTRIK**

**NEGARA**

**JAKARTA-INDONESIA**

**MAIN**  
*Engineers*

**CHAS. T. MAIN INTERNATIONAL, INC.**



PERUSAHAAN UMUM LISTRIK NEGARA  
JAKARTA, INDONESIA

WEST JAVA  
ELECTRIC TRANSMISSION AND DISTRIBUTION  
REHABILITATION PROJECT

MONTHLY REPORT

APRIL 1976

WESTJAVA I PROJECT

CONTRACT NO. PJ 013/PST 74

AID LOAN NO. 497-H-028



**CHAS. T. MAIN INTERNATIONAL, INC**

BOSTON, MASSACHUSETTS U. S. A.

BANDUNG, INDONESIA

MAIN  
Engineers

PERUSAHAAN UMUM LISTRIK NEGARA CONSULTANS

CHAS. T. MAIN INTERNATIONAL, INC.

BANDUNG - TROMOLPOS 60. TEL. 78009. JL. CILIWUNG 6  
JAKARTA - P.O. BOX 100. KOT. KED. MORAN TIMUR. TEL. 74041. JL. WIJAYA 1/60  
SEMARANG - P.O. BOX 26. TEL. 27105. JL. SLAMET 5

24 May 1976

Letter No. B - 2278

Ir. Djurzan Hamid  
Perusahaan Umum Listrik Negara  
Proyek Induk Jaringan Jawa Barat & Jakarta Kaya  
Jl. Cililitan Besar 1  
Jakarta

Subject : Contract No. PJ.013/PST/74  
Monthly Report

Dear Ir. Djurzan :

In accordance with article 7.2 of the subject contract, enclosed are six (6) copies of our report for the month of April 1976.

Very truly yours,  
Chas. T. Main International Inc.



Manager of Administration.

CJM/dn.

cc. : DINBANG - PLN Pusat  
AID - Jakarta (encl - 4 copies) ✓  
MAIL - USA (encl)

WEST JAVA PROJECT - PHASE I

MONTHLY REPORT

APRIL - 1976

The following summarizes events and progress made during the month of April 1976.

A. PERSONNEL

1. ENGINEER

a. Mr. W.E. Sebastian, former Projects Director, departed Indonesia 17 April. Mr. T.A. O'Hare will be appointed Projects Coordinator.

b. End of the month strength was as follows :

<u>NAME</u>	<u>TITLE</u>	<u>ARRIVAL DATE</u>
T.A. O'Hare	Projects Coordinator (1)	
F.M. Boxold	Project Manager (2)	1 June 1974
K.A. Smith	Manager of Eng. and Const. (2)	2 Dec. 1975
C.J. Whitby	Manager of Administration (2)	10 Sept. 1974
P.E. Boyd	Transmission Engineer (2)	25 Aug. 1974
R.W. Horlacher	Survey Engineer (3)	5 Apr. 1975
E.H. Knight	Distribution Eng.	3 June 1974
T.J. Plaskota	Substation Eng.	3 Oct. 1974

(1) Performs the same function for the Tuntang, Ketenger, Interim Generation and West Java II Projects.

(2) Performs the same function for the West Java II Project.

(3) Officially assigned to the West Java II Project but temporarily assigned to West Java I.

c. During the month, T.J. Plaskota continued to assist with the Interim Generation Contract work in Jakarta and is now assisting with substation work in Central

Java. These assignments were for short periods of time and did not hinder the work in West Java.

2. PLN

- a. During the month, the position of Transportation Coordinator was filled and the Drafting Room Coordinator from Cirebon was transferred to the Bandung office. Two additional typists were hired.
- b. End of the month strength was as follows :

<u>JOB TITLE</u>	<u>NUMBER</u>	
	<u>Bandung</u>	<u>Cirebon</u>
Transmission Liaison Engineer	1	-
Distribution Liaison Engineer	-	1
Logistics Coordinator	1	1
Transportation Coordinator	1	-
Drafting Room Coordinator	1	-
Survey Liaison Engineer	1	-
Secretary	1	-
Typists	4	-
Clerk/Typist	-	1
Draftsmen	4	10
Distribution Field Personnel	-	35
Distribution Office Personnel	-	5
Survey Crew Personnel	14	-
Construction Estimators	-	4
Equipment Operators	-	4
Drivers	7	4

B. ADMINISTRATION AND GENERAL

1. ADMINISTRATION

- a. During the month, ENGINEER was advised of USAID approval of the loan covering the new Scope of Work

of the Project. ENGINEER is now revising cost estimates, work schedules and manpower requirements.

C. CONFERENCES AND EVENTS

1. During the month, Mr. E. Tierney and Mr. F. Connif, USAID Jakarta, visited the Project. Discussions were held concerning revisions in the Scope of Work and anticipated manpower and financing requirements.
2. During the month, W.E. Sebastian, Projects Director, Jakarta, visited the Project. Discussed were general administrative matters and his planned departure from Indonesia.

D. PROBLEM AREAS

1. PLN Housing. There still has been no well or pump test and there has been no further work on the entrance road.

E. DESIGN PROGRESS

1. DISTRIBUTION

- a. ENGINEER has completed approximately 98% of the field work and expects to complete the entire design phase by 30 June.

2. TRANSMISSION

- a. The Center Line survey from Cirebon to Tegal is complete for 67.1 km and profile complete for 63.6 km. the total line length is 69.728 km. Center Line and profile (including changes) from Cirebon to Ujungberung (Kant - Bandung) are complete.

3. SUBSTATIONS

- a. There were no significant events.

**F. TRAINING ACTIVITIES**

**1. GENERAL**

- a. Training of survey personnel was significantly increased in preparation for doubling the survey forces.**
