

PD-AAQ-037

Library
388-0024



GOVERNMENT OF THE PEOPLE'S REPUBLIC OF BANGLADESH
BANGLADESH AGRICULTURAL DEVELOPMENT CORPORATION



AGENCY FOR INTERNATIONAL DEVELOPMENT

Grant Financed

FERTILIZER DISTRIBUTION IMPROVEMENT - I (388-0024)

ENGINEER CONSULTANT SERVICES FOR CONSTRUCTION
OF BAGGED PRODUCT FERTILIZER WAREHOUSES IN
BANGLADESH-PHASE III

PROGRESS REPORT NO. 14

JANUARY 1984



AMMANN & WHITNEY
CONSULTING ENGINEERS
NEW YORK

in association with



WORLDWIDE ENGINEERS LTD.
ARCHITECT-ENGINEERS
DHAKA



STHAPATI SANGSHAD LTD.
ARCHITECTS, ENGINEERS & PLANNERS
DHAKA

TELEPHONES : 232221
231639 246080
237784
CABLE : AMMWHIT
DHAKA

AMMANN & WHITNEY
CONSULTING ENGINEERS

AMMANN & WHITNEY
95, MOTIJHEEL C. A.
P. O. BOX 348
DHAKA, BANGLADESH

WAREHOUSES PHASE III

Project Director, BADC
USAID Construction Project
20, Outer Circular Road
Rajarbagh, Dhaka-17

724-2.1.1/1110

09 February 1984

Subject: Monthly Report No.14
- January 1984

Dear Sir,

In compliance with paragraph B.2 of Appendix A, Scope of Work, of Agreement for Engineer Consultant Services - Warehouses Phase III, fifteen (15) copies of the Monthly Report No.14 are submitted to BADC and six (6) copies to USAID.

Very truly yours
AMMANN & WHITNEY



George A. Pecht
Project Manager

Encl: Eleven (11) copies

GAP/tr

cc: Chairman, BADC w/encl. (1)
Member-Director (Irri), BADC w/encl. (1)
Manager (Storage) BADC w/encl. (1)
Chief Engineer (C) BADC w/encl. (1)
Mr. David E. Warner, PO, AID/Dhaka w/encl. (6)
File 724-1.4.2 w/encl.

AMMANN & WHITNEY
Consulting Engineers

FERTILIZER WAREHOUSES - PHASE III

Monthly Progress Report No.14
Month of January 1984

TABLE OF CONTENTS

- SITE LOCATION

I. CONSULTANT'S ACTIVITIES

A. PROJECT DESCRIPTION

- . Consultant Financial-Progress Schedule

B. ADMINISTRATION

1. Consultant's Agreement
2. Expatriate Staff
3. Contract Administration
4. Meetings
5. Supporting Bangladeshi Personnel
6. Project Expenditures
7. Billing and Payment
8. Reports

C. TECHNICAL

1. Summary of Consultant's Activities During This Month
2. Status of Sites
3. Railway Sidings
4. Scheduled January Events
 - . Action Check List


II. CONTRACTORS' ACTIVITIES - CONSTRUCTION PHASE

- . Summary of Contractor's Activities During Month
- . B1-Kishoreganj
- . C3-Jamalpur
- . F1-Dohazari
- . F3-Cox's Bazar
- . H2-Chowmuhani
- . H3-Lakshmipur
- . I4-Chandpur
- . L4-Domar
- . O5-Parbatipur

BANGLADESH AGRICULTURAL DEVELOPMENT CORPORATION
FERTILIZER WAREHOUSE - PHASE III
AGENCY FOR INTERNATIONAL DEVELOPMENT - GRANT NO. 388-0024

SITE LOCATION PLAN

- PROPOSED SITE (M.T.)
- △ WITH RAILWAY SIDING

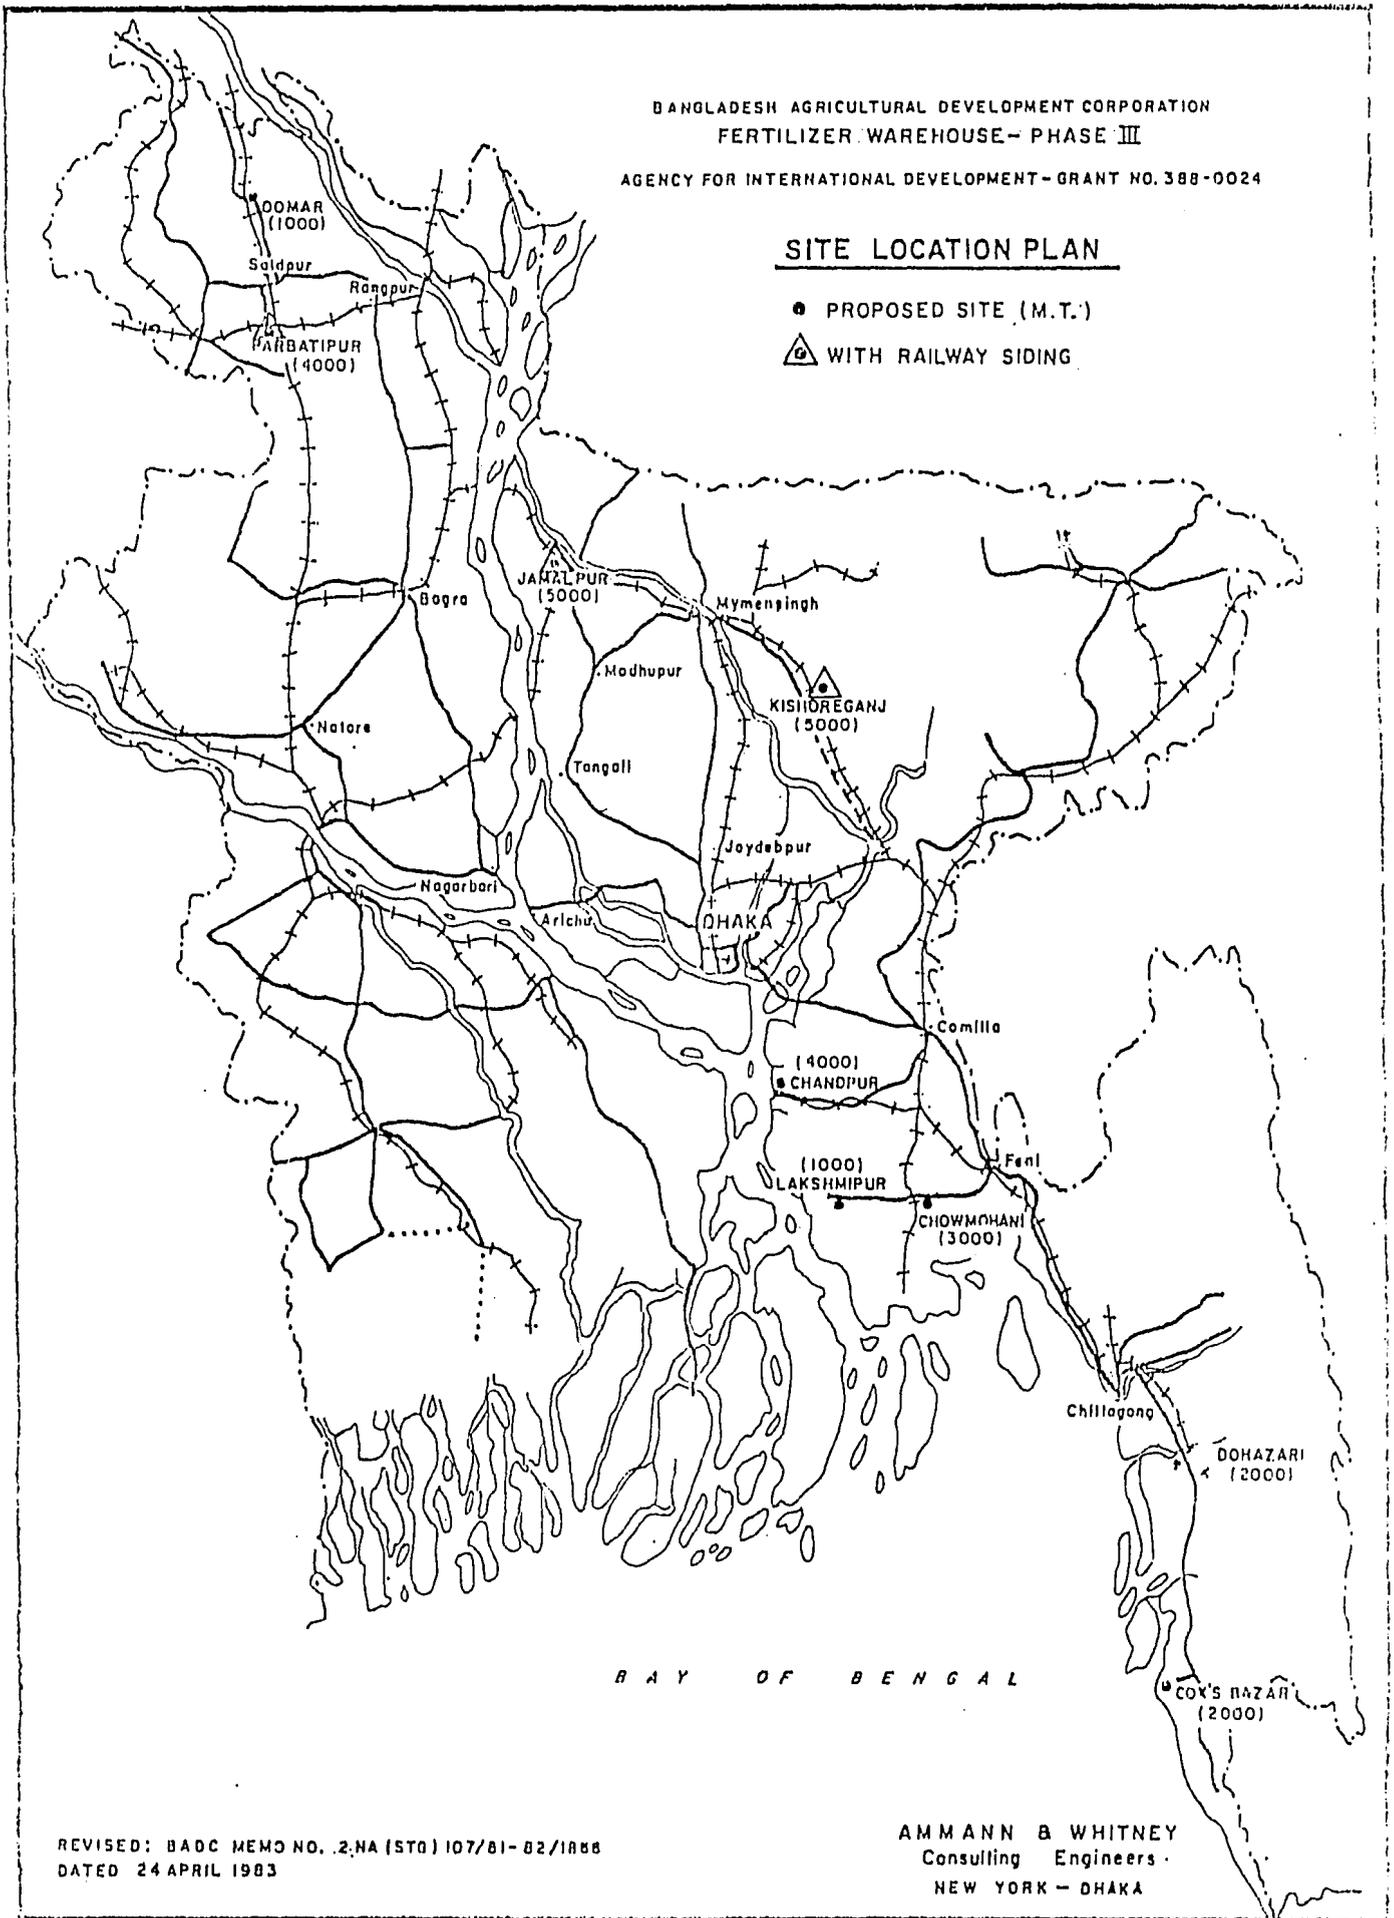

REVISED: BADC MEMO NO. 2/NA (STG) 107/81-82/1888
DATED 24 APRIL 1983

AMMANN & WHITNEY
Consulting Engineers
NEW YORK - DHAKA

I. CONSULTANT'S ACTIVITIES

A.1. PROJECT DESCRIPTION

PROJECT : Construction of Bagged Product Fertilizer Warehouses
in Bangladesh - Phase III

EMPLOYER : Bangladesh Agricultural Development Corporation

FINANCED : United States Agency For International Development
Under Grant
Fertilizer Distribution Improvement-I (388-0024)

ENGINEER : Ammann & Whitney
Consulting Engineers
New York Dhaka

LIST OF SITES AND TONNAGE

<u>NAME OF SITE</u>	<u>TONNAGE</u>	<u>NAME OF DISTRICT</u>	<u>SIZE OF GODOWN</u>
B1 KISHOREGONJ	5000	MYMENSINGH	90'x 300' (27,000 sft)
C3 JAMALPUR	5000 (3500+1500)	JAMALPUR	120'x150'; 90'x90' (26,000 sft)
F1 DOHAZARI	2000	CHITTAGONG	90'x 120' (10,800 sft)
F3 COX'S BAZAR	2000	CHITTAGONG	90'x 120' (10,800 sft)
H2 CHOWMUHANI	3000	NOAKHALI	90'x 180' (16,200 sft)
H3 LAKSHMIPUR	1000	NOAKHALI	60'x 90' (5,400 sft)
I4 CHANDPUR	4000	COMILLA	120'x 180' (21,600 sft)
L4 DOMAR	1000	RANGPUR	60'x 90' (5,400 sft)
O5T PARBATIPUR	4000	DINAJPUR	90'x 240' (21,600 sft)
TOTAL	27,000 M.T.		144,900 sft

I. Consultant's Activities

A.2. FINANCIAL - PROGRESS SCHEDULE

FINANCIAL

Total Procurement Budget	- \$ 2,014,567
Special Project Activity	- \$ 245,498
Total Contract Budget	- \$ 2,260,065
Estimated Expenditures To-date	- \$ 907,476
% Expenditure to Total Procurement Budget	- 40.2%

PROGRESS

Elapsed Contract time	- 418 days
Remaining Contract Time	- 394 days
% Elapsed Time	- 51.5%

B. ADMINISTRATION

1. The Consultant's Agreement

- . Contract Agreement signed - 09 December 1982
- . Effective Date - 09 December 1982
- . Aid Letter of Commitment
No.388-0024-3-30381 - 15 December 1982
- . Duration - 28 February 1985 (26.74 mos.)
- . Months Completed - 13.74 months

2. Expatriate Staff

		<u>Man-Months</u>	
		<u>Allocated</u>	<u>Utilized</u>
George A. Pecht	- Project Manager	27	12.65
Harry S. Allen	- Chief Construction Engr.	25	10.24
	- Foundation Engineer	8	7.72*
	- Structural Engineer	6	4.91*
Y.O. Kim	- Project Engineer	16	-

* Assignment Completed

3. Contract Administration

3.1 For action by BADC:

- . Amendment No.1 to Consultant's Agreement extending duration to 30 June 1985.
- . Obtain T&T approval for wireless licence for radio communication. 724-1.6.1/1035, 29 January 1984;
724-1.1.11/1040, 31 January 1984
- . Approval to procure project vehicles.

4. Meetings

- . Consultant's weekly project review meetings.
- . Pre-construction Conferences.

5. Supporting Bangladeshi Personnel

5.1 WEL and SSL Personnel (Sub-Contract)

<u>Designation</u>	<u>Man-Month</u>	
	<u>Allocated</u>	<u>Utilized</u>
Deputy Project Manager	27	13.0746
S&M Engineer	24	13.2728
Structural Engineer	9*	9.0388
Architect	4	3.8389
Electrical Engineer	6	1.5238
Railway Engineer	24	10.9089
Office Engineer	26	12.8656
Land Procurement Officer	12	10.1366
Surveyor	25	11.7072
Instrument Man	25	11.5664
Rodman	25	5.8222
Chainman	25	11.3191
Draftsman	69*	42.0863
Laboratory Technician	56	14.0649
Laboratory Assistant	56	0.2609
Estimator	48	16.8943
Senior Field Engineer	60	13.0000
Field Engineer	80	0.2174
Inspectors	128	0.7826
Drivers	94	-
Messenger	34	-
Peon	34	-
Guard	68	-
Clerk	34	-
Typist	34	-

5.2 Administrative Personnel

Administrative Manager	27	13.4546
Senior Accountant	27	13.5844
Assistant Accountant	44	12.1108
Secretary	27	13.5368
Printer	27	11.9069
Typist	72	35.6417
Clerk	45	13.1931
Drivers	103	46.7873
Messenger	45	10.8636
Peon	72	32.5433
Guard	90	54.9091
Radio Operator	48	-
Office Superintendent/Asst. Accountant	34	0.3478

* Adjusted

6. Project Expenditures
(Estimated Project Cost Incurred)

<u>Item</u>	<u>Agreement Budget</u>	<u>Adjusted Budget</u>	<u>This Month</u>	<u>Cumulative</u>
Services in Bangladesh	\$ 746,188	\$ 790,172	\$ 20,420	\$ 343,425
Services in Home Office	176,178	176,178	-	133,499
International Travel, etc.	85,740	85,740	215	17,899
Housing Allowances, per diem etc.	91,075	102,775	5,072	50,623
Logistic Costs	223,400	223,400	6,201	64,304
Supporting Staff	382,404	387,842	6,764	93,243
Misc. Direct Costs	43,000	43,000	6	7,779
Fixed Fee	205,460	205,460	7,610	106,540
	<u>\$1,953,445</u>	<u>\$2,014,567</u>	<u>\$ 46,288</u>	<u>\$ 817,312</u>
Percent of Estimated Budget			2.30%	40.57%
Percent Contract Time (To 28.02.85)				51.38%
Special Project Activity	<u>306,620</u>	<u>245,498</u>	<u>343</u>	<u>90,164</u>
	<u>\$2,260,065</u>	<u>\$2,260,065</u>	<u>\$ 46,631</u>	<u>\$ 907,476</u>

7. Billing and Payment

<u>Invoice</u>	<u>Period Ending</u>	<u>Billing</u>	<u>Payment</u>
01 - 10	30 Nov 83	\$ 773,070.57	\$ 771,027.01
11	31 Dec 83	\$ 36,671.56	Under Process

8. Reports

- . Monthly Progress Report No.13 for December 1983 submitted by letter /929,09 January 1984.

C. TECHNICAL

1. Summary of Consultant's Activities During This Month

- . The bid guarantees submitted by Tenderers have been returned between 8-16 January 1984. By Project Implementation Letter (PIL) No.38, dated 22 January 1984 USAID has approved construction contract awards. Refer to Part II of this report.
- . The Contractors informed the Engineer where their payments should be made under Letter of Commitment.
- . Two copies of contract drawings, Technical Specification and supplemental site layout drawings have been distributed to each of the contractors. An action check list prepared by the Engineer has been supplied to all contractors to assist them in the start-up of the project.
- . A preconstruction conference was held at the Engineer's office with the contractor's representatives for each site as follows:
 - Jamalpur, Chowmuhani and Lakshmipur on 15 January 1984, Domar and Parbatipur on 19 January 1984, Cox's Bazar and Chandpur on 24 January 1984 and Kishoreganj and Dohazari on 25 January 1984. Representatives of BADC and USAID also attended most of the conferences.
- . The conferences were held for detailed discussion of contact plans and specifications, contractor's plans for management and scheduling, organization and responsibilities, and clarification were required to promote mutual cooperation and better job understanding.
- . For the Engineer's control of the work and control of materials standard forms were prepared for use of field and laboratory personnel in recording events.
- . To assist the field and laboratory personnel a Material Testing Guide was prepared and distributed.
- . The contractors were requested to arrange test equipment as per technical specification and have available on site for monitoring quality of materials and construction. (/1036, 30.01.84)
- . The Engineer continued to mobilize personnel, hold training sessions, and assign personnel to their post.

2. Status of Sites

B1-Kishoreganj

- . As of 10 January the two telephone lines have not been relocated/raised.
- . On 29 January 1984, Mr. G.R. Rashid, Manager(F), BADC, Kishoreganj handed over the site to the Contractor, National Construction, in presence of the Engineer's Chief Construction Engineer (H.S. Allen) and Field Engineer (A.H. Nazrul Islam).
- . The Contractor started mobilizing his construction material and construction of his site office and labour shed.
- . The handing over of land located parallel to existing line on the east of the site owned by the Railway is being finalized.
- . LAO, BADC has been directed to pursue the T&T Department for obtaining the estimate of cost for shifting the telephone line. Memo No.ADC/S/Sales/3C/3/69/76/788(4) dated 30.1.84.

C3-Jamalpur

- . Representatives of the Engineer inspected the site on 9 January 1984. The site was found clear of obstructions except for 8 to 10 squatters. BADC's District Manager confirmed that the squatters would be removed within a few days notice.
- . The site was turned over to the Contractor, Mostafa Brothers (Pvt) Ltd., on 19 January 84 by A.K.M. Shahjahan, Manager(Storage), K. Altaf Hossain, District Manager in the presence of George A. Pecht, Project Manager and S.A.M. Badruddoja, Soil/Material Engineer.
- . The site was dedicated on 1 February 1984 by the District Commissioner at a ceremony held at the site in presence of BADC's District Manager, Superintendent of Police, Thana Nirbahee Officer, Executive Engineer, PDB, the Engineer's Chief Construction Engineer and Contractor's representative. A brick pedestal monument was constructed at the site on this occasion.
- . BADC has obtained additional land between monument No.1 and No.2 which will be included in land plan drawing after survey.

F1-Dohazari

- . The site was inspected on 20 January 1984 by the Engineer's representative and found clear for construction.
- . The site was handed over to the Contractor, Eastern Engineers Consortium Ltd., by Mr. M.A. Razzaque, District Manager(F), BADC Chittagong in presence of Mr. Jahangir Alam, Senior Field Engineer, on 26 January 1984. The site was demarcated by wooden pillar. The District Manager indicated that the access to river was not finalized.
- . Settlement of 0.28 acres of land for access to river under processing through Upazila Nirbahee Officer (UNO).

F3-Cox's Bazar

- . The site was inspected by the Engineer's representative on 20 January 1984. It was found that the tin shed building has not been removed. The Sub-Divisional Manager (SDM), BADC informed that the building would be removed within 4-5 days. The power line has been relocated but the guy wires near existing entrance gate were not removed. Requisite funds have been placed with PDB for removal. The houses along the proposed river access have not been removed. The Land Acquisition Officer (LAO) and Senior Field Engineer will follow up this case.
- . The site was handed over on 26.01.84 to the Contractor, Builders The Best Ltd., by Mr. Abdur Rashid, Sub-Divisional Manager, BADC, Cox's Bazar, Chittagong in presence of Mr. Jahangir Alam, Senior Field Engineer. The existing tin shed godown will be immediately removed as reported by the SDM. Land for access to the river has not yet been finalized.

H2-Chowmuhani

- . The existing telephone line has not been raised as reported by Chief Construction Engineer on 31 January 1984. The Contractor stated he cannot start filling operations until the line is raised since at its present height he cannot enter the site with trucks and equipment. The DM was informed of this situation and he stated that action was being taken and the line should be raised within two weeks. The estimate of cost for raising T&T line has been obtained by BADC (Memo No./342, dt. 25.1.84).
- . The site was handed over to the Contractor, Technocon Ltd., by Mr. S.K. Sanyal, DM, BADC, Noakhali on 31 January 1984 in presence of Mr. H.S. Allen, Chief Construction Engineer.
- . The Contractor has posted supervisory personnel to the site and has begun mobilizing.

H3-Lakshmipur

- . The site was handed over to the Contractor, Technocon Ltd. by Mr. S.K. Sanyal, DM, BADC, Noakhali on 31 January, 1984 in presence of Mr. H.S. Allen, Chief Construction Engineer. No apparent problem with the site.
- . The Contractor has posted supervisory staff to the site and started mobilizing his materials and equipment.

I4-Chandpur

- . The site was inspected by the Engineer's personnel on 22 January 1984. The tin shed structures have been removed and clearing of surface drain and debris was underway. Two telephone poles and one electric pole were scheduled to be removed shortly as reported by SDM, Chandpur.
- . Temporary accommodation for senior staff of the Engineer can be arranged in Government Dak Bunglow with 2-3 days notice.

I. Consultant's Activities

- . The site was handed over to the Contractor, Fazle Azim Engineers Ltd. by Mr. M.D. Taib Ali, SDM, BADC Chandpur on 30 January 1984 in presence of Mr. H.S. Allen, Chief Construction Engineer. Joint inspection by the above representatives indicated: 1. Approximately 5% of the existing godown foundations have not been removed and 2. Approximately 60 L.F. frontage of shops on Sen Gupta Road at the proposed entrance to the site have not been removed. The SDM stated that he would take action for removal.
- . The Contractor has engaged supervisory staff for the site and started mobilizing.

L4-Domar

- . The site was inspected by the Engineer's staff on 17 January 1984. The site is clear and dry. The available connecting point to PDB power line is about 1½ miles from site. S.M. Farm were to provide the line to the site but the estimated cost of Tk.4 lac was not budgeted. Electricity is provided for 5 hours at night in the S.M. Farm by generator.
- . One vacant house containing two rooms in the S.M. Farm can be arranged for temporary accommodation for the Engineer's office and staff.
- . The site was handed over to the Contractor, M.S. Khan & Heirs Ltd., by Mr. Rakibuddin, Su-Divisional Manager, Nilphamari, BADC in presence of Mr. A. Obayed Khan, Senior Field Engineer on 26 January 1984.
- . The Superintendent of S.M. Farm, BADC was requested to confirm that the existing BADC property line is along the line of R.C.C. pillars located along the District Council Road in the north-south direction and village road in the east and west direction and that the boundary wall should be construction along this line (/1045, 31 January 1984).

05-Parbatipur

- . The site was inspected by the Engineer's staff. The existing access to the site has been cut off by construction of a culvert on the existing road. The site is clear having no apparent problem for starting construction.
- . The site was handed over to the Contractor, The Elite Engineers Ltd., by Mr. Ruhul Amin, Sub-Divisional Manager, Dinajpur, BADC in presence of Mr. Abu Obayed Khan, Senior Field Engineer on 26 January 1984.

3. Railway Sidings

The Project Director/BR has approved the railway siding layout plans for Jamalpur and Parbatipur. The plan of Jamalpur was sent on 15 January 1984 to Chief Engineer/East/BR and that of Parbatipur to Chief Engineer/West/BR for their approval.

The Kishoreganj yard plan has been sent to Project Director/BR's office by DEN/II/BR for approval of Additional Project Director/BR.

4. Materials Testing

The Engineer started mobilizing laboratory testing equipment and establishing a central testing laboratory at Dhaka. The Laboratory was operational at the end of the month and the following tests were performed.

Jamalpur : 6 samples of concrete aggregate, mortar sand, and filling materials were tested. Sample of ordinary fill is approved and all other samples disapproved.

Domar : 5 samples of concrete aggregate, mortar sand, and select fill were tested. Samples of concrete sand and select fill are approved.

Parbatipur : 5 samples of concrete aggregate, mortar sand, and select fill were tested. All were disapproved.

Kishoreganj : 3 samples of bricks received and are being tested.

Lakshmipur

&

Chowmuhani : 3 samples of fine aggregates and fill materials received and are being tested.

5. Scheduled February Events:

1. AID to issue Letter of Commitment
2. Engineer to issue Notice To Proceed after opening of L/C
3. Contractor to nominate key personnel and submit curriculum vitae.
4. Engineer to assist contractors to prepare construction schedule due not later than 21 days after execution of contract.
5. Contractor to commence work within 15 days of date of Notice To Proceed.
6. Engineer and contractor to do setting out of the work.
7. Engineer to mobilize personnel and establish site office and testing facilities.
8. Continue monitoring availability of construction material.
9. Monitor resolution of site possession and use rights and removal of obstructions.
10. Continue construction surveillance.

Serial Number	REFERENCES	ACTION REQUIRED	ACTION BY	ACTION TAKEN										
				B1 Kishoreganj	C3 Jumalpur	F1 Dohazari	F3 Cox's Bazar	H2 Chowmahari	H3 Iakshimpur	I4 Chandpur	I4 Dumar	O5 Turbhatmur		
16.	Sec. 1A.04 D (Spec)	Furnish to Contractor Weekly Report form	Engineer											
17.	Sec. 1A.04 E (Spec)	Furnish to Contractor Monthly Progress Report form	Engineer											
18.	Sec. 1A.05 D (Spec)	Prepare and submit shop drawings for approval	Contractor											
19.	Sec. 1A.05 C (Spec) Sec. 1B.02 (Spec)	Submit samples for approval	Contractor											
20.	Sec. 1A.06 (Spec)	Take and furnish construction photographs	Contractor Contractor											
21.	Sec. 1A.07 (Spec) Clause 14 (Conditions)	Submit plan of temporary facilities and their location	Contractor											
22.	Sec. 1A.07 B (Spec) Clause 34 (Conditions)	Furnish and install tubewell, septic tank and soak well	Contractor											
23.	Sec. 1A.07 D (Spec) Clause 19 (Conditions)	Provide temporary electrical facilities	Contractor											
24.	Clause 53 (Conditions)	Mobilization plant and equipment	Contractor											

II CONTRACTORS' ACTIVITIES
CONSTRUCTION PHASE

1. Summary of Contractors' Activities During Month

- . Contracts for construction of nine godowns were signed during the month.
- . USAID issued PIL No.38, 22.01.84 approving construction awards.
- . Pre-construction conferences held with each of the contractors.
- . BADC handed over sites to the contractors.
- . USAID required to issue Letter of Commitment prior to Engineer issuing Notice To Proceed to the contractors.
- . Contractors began mobilizing.
- . Construction contracts awarded:

Invitation No.	Site	Contractor	Contract Amount (Tks)	Date Contract Signed
1	B1-Kishoreganj	National Construction and Consult Limited	1,98,40,012.82	16.1.84
2	C3-Jamalpur	Mostafa Brothers	1,76,94,451.01	12.1.84
3	F1-Dohazari	Eastern Engineers Consortium Ltd.	1,55,48,978.95	16.1.84
4	F3-Cox's Bazar	Builders The Best	99,64,470.85	12.1.84
5	H2-Chowmuhani	Technocon Ltd.	1,41,20,342.60	12.1.84
6	H3-Lakshmipur	Technocon Ltd.	55,91,275.35	12.1.84
7	I4-Chandpur	Fazle Azim Engineers	1,70,67,822.35	16.1.84
8	L4-Domar	M.S. Khan & Heirs Ltd.	74,99,255.00	12.1.84
9	O5-Parbatipur	Elite Engineers Ltd.	1,70,02,196.40	12.1.84
Total Tk.			12.43,28,805.33 (\$4,999,147.78)	

MONTH ENDING
31 January 1984

INVITATION NO.1 : B1-KISHOREGANJ

CONTRACTOR : National Construction & Consult Ltd.

Total Contract Price : Tk. 1,98,40,012.82 Date of Contract : 16.01.84

Change Orders : Tk. Nil Notice To Proceed:

Revised Contract Price: Tk. 1,98,40,012.82 Scheduled Completion: _____%

Payments To Date : Tk. Nil Elapsed Time : _____ days _____%

	: Tk.	Nil	% Completion			
			Scheduled		Actual	
			<u>This Period</u>	<u>To Date</u>	<u>This Period</u>	<u>To Date</u>
Date of L/Com.	: 31.01.84					
			%	%	%	%

L/Com. No. : 388-002403

Amount of L/Com. : Tk.1,98,40,012.82
(\$797,885.00)

Notice To Proceed pending issuance by USAID of Letter of Commitment.

Site handed over to Contractor by BADC on 29.01.84

14

MONTH ENDING
31 January 1984

INVITATION NO.2 : C3-JAMALPUR

CONTRACTOR : Mostafa Brothers (Pvt) Ltd.

Total Contract Price	: Tk. 1,76,94,451.01	Date of Contract	: 12.01.84
Change Orders	: Tk. Nil	Notice To Proceed:	
Revised Contract Price	: Tk. 1,76,94,451.01	Scheduled Completion:	_____ %
Payments To Date	: Tk. Nil	Elapsed Time	: _____ days _____ %
Retention To Date	: Tk. Nil	% Completion	
Date of L/Com.	: 31.01.84	<u>Scheduled</u>	<u>Actual</u>
L/Com. No.	: 388-002404	<u>This Period</u>	<u>To Date</u>
Amount of L/Com.	: Tk.1,76,94,451.01	<u>This Period</u>	<u>To Date</u>
	(\$711,599.00)	%	%
		%	%

Notice To Proceed pending issuance by USAID of Letter of Commitment

Site handed over to Contractor by BADC on 19.01.84

15

INVITATION NO.3 : F1-DOHAZARI

CONTRACTOR : The Eastern Engineers Consortium Ltd.

Total Contract Price : Tk. 1,55,48,978.95 Date of Contract : 16.01.84
Change Orders : Tk. Nil Notice To Proceed:
Revised Contract Price: Tk. 1,55,48,978.95 Scheduled Completion: _____ %
Payments To Date : Tk. Nil Elapsed Time : _____ days _____ %
Retention To Date : Tk. Nil % Completion
Date of L/Com : 31.01.84

Scheduled		Actual	
This Period	To Date	This Period	To Date
%	%	%	%

L/Com. No. : 388-002405
Amount of L/Com. : Tk.1,55,48,978.95
(\$625,317.00)

Notice To Proceed pending issuance by USAID of Letter of Commitment

Site handed over to Contractor by BADC on 26.01.84

MONTH ENDING
31 January 1984

INVITATION NO.4 : F3-COX'S BAZAR

CONTRACTOR : Builders The Best Ltd.

Total Contract Price : Tk.99,64,470.85

Date of Contract : 12.01.84

Change Orders : Tk. Nil

Notice To Proceed:

Revised Contract Price: Tk.99,64,470.85

Scheduled Completion: _____ %

Payments To Date : Tk. Nil

Elapsed Time : _____ daya _____ %

Retention To Date : Tk. Nil

% Completion

Date of L/Com. :

Scheduled		Actual	
<u>This Period</u>	<u>To Date</u>	<u>This Period</u>	<u>To Date</u>

L/Com. No. :

%	%	%	%
---	---	---	---

Amount of L/Com. :

Notice To Proceed pending issuance by USAID of Letter of Commitment.

Site handed over to Contractor by BADC on 26.01.84

MONTH ENDING
31 January 1984

INVITATION NO.5 : H2-CHOWMUHANI

CONTRACTOR : Technocon Limited

Total Contract Price	: Tk. 1,41,20,342.60	Date of Contract	: 12.01.84
Change Orders	: Tk. Nil	Notice To Proceed:	
Revised Contract Price	: Tk. 1,41,20,342.60	Scheduled Completion	_____ %
Payments To Date	: Tk. Nil	Elapsed Time	: _____ days _____ %
Retention To Date	: Tk. Nil	% Completion	
Date of L/Com.	:	<u>Scheduled</u>	<u>Actual</u>
L/Com. No.	:	<u>This Period</u>	<u>To Date</u>
Amount of L/Com.	: Tk.	<u>This Period</u>	<u>To Date</u>
		%	%
		%	%

Notice To Proceed pending issuance by USAID of Letter of Commitment

Site handed over to Contractor by BADC on 31.01.84

2

MONTH ENDING
31 January 1984

INVITATION NO.6 : H3-LAKSHMIPUR

CONTRACTOR : Technocon Limited

Total Contract Price : Tk.55,91,275.35

Date of Contract : 12.01.84

Change Orders : Tk. Nil

Notice To Proceed:

Revised Contract Price: Tk.55,91,275.35

Scheduled Completion : _____%

Payments To Date : Tk. Nil

Elapsed Time : _____days _____%

Retention To Date : Tk. Nil

% Completion

Date of L/Com. :

Scheduled		Actual	
<u>This Period</u>	<u>To Date</u>	<u>This Period</u>	<u>To Date</u>

L/Com. No. :

%	%	%	%
---	---	---	---

Amount of L/Com. :

Notice To Proceed pending issuance by USAID of Letter of Commitment.

Site handed over to Contractor by BADC on 31.01.84

MONTH ENDING
31 January 1984

INVITATION NO.7 : I4-CHANDPUR

CONTRACTOR : Fazle Azim Engineers Ltd.

Total Contract Price : Tk.1,70,67,822.35

Date of Contract : 16.01.84

Change Orders : Tk. Nil

Notice To Proceed:

Revised Contract Price: Tk.1,70,67,822.35

Scheduled Completion : _____%

Payments To Date : Tk. Nil

Elapsed Time : _____ days _____%

Retention To Date : Tk. Nil

% Completion

Date of L/Com. :

Scheduled		Actual	
<u>This Period</u>	<u>To Date</u>	<u>This Period</u>	<u>To Date</u>

L/Com. No. :

%	%	%	%
---	---	---	---

Amount of L/Com. : Tk.

Notice To Proceed pending issuance by USAID of Letter of Commitment.

Site handed over to Contractor by BADC on 30.01.84

20

MONTH ENDING
31 January 1984

INVITATION NO.8 : L4-DOMAR

CONTRACTOR : M.S. Khan & Heirs Ltd.

Total Contract Price	: Tk.74,99,255.00	Date of Contract	: 12.01.84
Change Orders	: Tk. Nil	Notice To Proceed:	
Revised Contract Price:	Tk.74,99,255.00	Scheduled Completion	: _____ %
Payments To Date	: Tk. Nil	Elapsed Time	: _____ days _____ %
Retention To Date	: Tk. Nil	% Completion	
Date of L/Com.	: 31.01.84	<u>Scheduled</u>	<u>Actual</u>
L/Com. No.	: 388-002410	<u>This Period</u>	<u>To Date</u>
Amount of L/Com.	: Tk.74,99,255.00	%	%
	(\$301,590.00)	%	%

Notice To Proceed pending issuance by USAID of Letter of Commitment.

Site handed over to Contractor by BADC on 25.01.84

21

MONTH ENDING
31 January 1984

INVITATION NO.9 : 05-PARBATIPUR

CONTRACTOR : The Elite Engineers Ltd.

Total Contract Price : Tk.1,70,02,196.40

Date of Contract : 12.01.84

Change Orders : Tk. Nil

Notice To Proceed:

Revised Contract Price: Tk.1,70,02,196.40

Scheduled Completion : _____ %

Payments To Date : Tk. Nil

Elapsed Time : _____ days _____ %

Retention To Date : Tk. Nil

Date of L/Com. :

% Completion			
Scheduled		Actual	
<u>This Period</u>	<u>To Date</u>	<u>This Period</u>	<u>To Date</u>

L/Com. No. :

%	%	%	%
---	---	---	---

Amount of L/Com. :

Notice To Proceed pending issuance by USAID of Letter of Commitment.

Site handed over to Contractor by BADC on 26.01.84

22
