

PVO AND WEST BANK/GAZA LIBRARY

III.C.


III.C.(3)

PDABE892

ISN79836

CR

PDABE 892



III 93

THIRD REPORT

RURAL DEVELOPMENT PROJECT

CRS JWB/4D-006  
USAID 5123

398-0159.14

1 OCTOBER 1986

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL PROJECT PROGRESS REPORT NO. ( 3 )

Date of Last report: 1 April 1986  
Date of This report: 1 October 1986

1. REFERENCE SECTION

CRS-JWB/USAID  
CRS Project No. 4D-006

US \$ 5,842,871.-  
AMOUNT

CATHOLIC RELIEF SERVICES - USCC JERUSALEM AND WEST BANK

Name of Operating Agency

"A partnership Project Assistance Program to promote the development of Rural Agriculture, Health Education and  
Electrification in the Jordan West Bank and Gaza Strip".

Title of Project

ISRAELI ADMINITERED JORDAN WEST BANK AND GAZA STRIP

Area in which Project is located

NEB - 0159 - G - SS - 5123 - 00

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 5,842,871.-

(I) AMOUNT OF GRANT

US \$ 537,853.-

Total Village cash input into sub-projects  
to date

U.S. \$ 746,112.-

(II) Amount received to date

15 AUGUST 1986

(III) Date of last transmittal

US \$ 5,275,324.27

(IV) Balance due under Grant

US \$ 567,546.73

(V) Expenditure to date

The strong willingness of the West Bank villagers to cooperate and work together, and their great efforts to come up  
with their shares and to donate parts of their lands to sub-projects.

(VI) Other inputs which contributed to success of project

- **PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID**
  
- This is the third Semi-Annual Project Progress Report since the AID grant - AID/NEB-0159-G-SS-5123-00- in the amount of \$ 5,842,871 was signed on 24 June 1985 to provide support for a program in the West bank / Gaza, entitled "Rural Development III". This program will support subcomponent activities in the areas of infrastructural development, increased agricultural production, and small business enterprise development. The program's estimated completion date is 2 April 1989.
  
- This report covers the period from 1 April 1986 through 1 October 1986. Excellent progress was made during the reporting period.
  
- During this period, CRS and village partners were engaged in work on sixteen sub-projects. In the following pages we highlight the work of these sub-projects.
  
- Four sub-projects were successfully completed (Table "1"). The four involved constructing two community centers, one for Silet El-Harthieh Village - Jenin District (4D-006-04), and the other for Za'tara Village - Bethlehem District (4D-006-06). The other two-completed sub-projects involved widening, clearing, and leveling an existing agricultural access road including asphaltting about 1.2 kms of its length for Nahhalin Village - Bethlehem District (4D-006-11), and asphaltting an existing access road for Marah Rabah Village - Bethlehem District (4D-006-15). The attached map shows the location of these four sub-projects. In the following pages are to be found final individual reports, including itemizations of expenditures, for each of these four sub-projects. About 12,000 persons directly benefitted from these sub-projects.

- The twelve other sub-projects are ongoing (Table "2"). They involve establishing a drinking water system for each of the following four villages : Kufor Kaddum (4D-006-12) and Jeet (4D-006-13) in Tulkarem District, Beit El-Rush El-Foqa (4D-006-24) and Beit El-Rush El-Tahta (4D-006-25) in Hebron District. Three other ongoing sub-projects call for providing a main internal electrical network for each of the following villages: Raqa' (4D-006-19) and El-Mureq-El-Kom (4D-006-20) in Hebron District, and Zbaidat (4D-006-21) in Jericho District. The other ongoing sub-projects involve constructing additional classrooms for Husan's school - Bethlehem District (4D-006-14), opening, clearing, and leveling agricultural access roads for Beit 'Ummar - Hebron District (4D-006-16), opening, clearing, leveling, and constructing supporting walls and parts of the road foundations of an agricultural access road for Bani N'aim - El-'Idaiseh - Hebron District (4D-006-17), constructing a primary school for Yatmah - Nablus District (4D-006-22), and constructing a community center for Shwaikah - Tulkarem District (4D-006-23). In the following pages are to be found individual reports on each of these twelve sub-projects.
  
- Ten other sub-projects are waiting approvals (Table "3"). Local government authorities are very slow in granting sub-projects approvals . For instance, Beit 'Ummar sub-project (4D-006-16), which involves opening, clearing, and leveling an agricultural access road, was presented to the Social Welfare- Beit-El-West bank, on 10 February 1986 while the approval came six months later. Beir Zeit sub-project (4D-006-09) was submitted to the authorities on 11 April 1985, while up to this date the agreement is still not signed.
  
- Village committees met some difficulties while collecting villages' shares. People in the West Bank and Gaza strip are facing serious financial problems due to drought this year, and the deteriorating economical situation.

- During this reporting period, several villages approached CRS-AID asking for additional sub-projects, in particular agricultural access roads and interior streets, as we are the only voluntary organization in the West Bank and Gaza Strip involved in such sub-projects.
  
- A separate and complete report on the Increased Agricultural Production and the Small Business Management Assistance Program is being sent with this Semi-Annual Project Progress Report.

**ATTACHEMENTS:**

- Budget Expenditure Statement.
- Final reports on Four Completed Sub-Projects.
- Progress Reports on Twelve Ongoing Sub-Projects.
- Tables.
- Map.

**DISTRIBUTION OF REPORT (11 COPIES):**

- USAID / W - NE / RECH / RHPD (3)
- CRS NEW WORK (3)
- US EMBASSY - TEL AVIV , AID LIAISON OFFICER (1)
- US CONSULATE GENERAL - WEST JERUSALEM (1)
- CRS JWB (2)
- CRS JWB RD OFFICE (1)

GA/1b

4

CRS JWB 4D-006 RURAL DEVELOPMENT PROJECT

GRANT NO. NEB - 0159 - G - SS - 5123

BUDGET EXPENDITURE STATEMENT

PROGRAM: JERUSALEM & WEST BANK  
MONTH: SEPTEMBER 1986

G R A N T	APPROVED BUDGET 03/04/1985 03/04/1987 ----- US \$	BUDGET EXPENDITURE TO DATE ----- US \$	BALANCE ----- US \$
1. INFRASTRUCTURAL DEVELOPMENT	1,186,250.-	587,872.21	598,377.79
2. PROJECT SUPERVISION	351,468.-		138,792.31
a. Salaries     \$ 242,968.-		162,998.08	
b. Travel       48,000.-		16,346.67	
c. Non-Expendable 38,000.-		16,973.95	
d. Direct Costs 12,000.-		7,448.52	
e. Office Rent & Utilities   10,500.-		8,306.47	
3. INCREASED AGRICULTURAL PRODUCTIVITY	156,300.-	16,666.10	139,633.90
4. SMALL BUSINESS ENTERPRISE DEVELOPMENT	36,000.-	8,407.68	27,592.32
5. CONSULTATIVE, EVALUATIVE & MONITORING	58,841.-	1,434.16	49,406.84
TOTAL	----- 1,780,859.- =====	----- 827,055.83 =====	----- 953,803.17 =====

5

TABLE "1"

COMPLETED SUB-PROJECTS

<u>NAME OF VILLAGE/ LOCATION/(SUB PROJECT NO.)</u>	<u>KIND OF PROJECT</u>	<u>TOTAL COST \$</u>	<u>CRS SHARE \$</u>	<u>VILLAGE SHARE \$</u>	<u>BENEFICIARIES (PERSONS)</u>
Silet El-Harthieh / Jenin (04)	Community Center	94,109.66	45,498.11 (48%)	48,611.55 (52%)	7500
Za'tara / Bethlehem (06)	Community Center	60,987.95	35,758.65 (58.7%)	25,157.30 (41.3%)	2000
Nahhalin/Bethlehem (11)	Agricultural Road	53,817.43	31,793.86 (60%)	21,223.57 (40%)	1500
Marah Rabah / Bethlehem (15)	Access Road	52,898.86	31,224.49 (60%)	28,873.57 (40%)	1800

TABLE "2"

ONGOING SUB-PROJECTS

<u>NAME OF VILLAGE/LOCATION (SUB-PROJECT NO.)</u>	<u>KIND OF PROJECT</u>	<u>ESTIMATED COST \$</u>	<u>CRS SHARE \$</u>	<u>VILLAGE SHARE \$</u>	<u>BENEF. (PERSONS)</u>
Kufor Kaddum/Tulkarem (12)	Water System	105,628.-	52,814.-	52,814.-	3000
Jeet / Tulkarem (13)	Water System	53,028.-	31,817.-	21,211.-	1500
Husan / Bethlehem (14)	Primary School	39,029.14	19,514.57	19,514.57	3000
Beit 'Ummar / Hebron (16)	Agricultural Roads	81,071.-	40,535.50	40,535.50	8000
Bani N'aim-El-'Idaiseh / Hebron (17)	Agricultural Road	60,629.-	36,377.-	24,252.-	6000
Raq'a / Hebron (19)	Electricity	98,666.-	59,200.-	39,466.-	4000
El-Mureq-El-Kom/Hebron (20)	Electricity	119,500.-	71,700.-	47,800.-	1600
Zbaidat / Jericho (21)	Electricity	34,283.-	22,284.-	11,999.-	1200
Yatmah / Nablus (22)	Primary School	36,000.-	21,600.-	14,400.-	3000
Shwaikeh/Tulkarem (23)	Community Center	81,250.-	40,625.-	40,625.-	5250
Beit El-Rush El-Foqa/Hebron (24)	Water System	43,750.-	26,250.-	17,500.-	800
Beit El-Rush El-Tahta/Hebron (25)	Water System	21,075.-	13,125.-	8,750.-	500

7

TABLE "3"

SUB-PROJECTS WAITING APPROVAL

<u>NAME OF VILLAGE/LOCATION (SUB-PROJECT NO.)</u>	<u>KIND OF PROJECT</u>	<u>ESTIMATED COST \$</u>	<u>CRS SHARE \$</u>	<u>VILLAGE SHARE \$</u>	<u>BENEF. (PERSONS)</u>
Beir Zeit / Ramallah (89)	Agricultural Roads	47,886.-	23,943.-	23,943.-	3000
Wadi Fukkin / Bethlehem (18)	Access Road	56,000.-	33,600.-	22,400.-	1000
'Attil / Tulkarem (26)	Interior Streets	78,766.-	35,445.-	43,321.-	8500
Till / Nablus (27)	Interior Streets	94,725.-	37,890.-	56,835.-	4000
Barta' & Khirbat Barta' / Jenin (28)	Interior Streets	74,588.-	38,786.-	35,802.-	3000
El-Shiyoukh / Hebron (29)	Interior Streets	78,031.-	39,015.50	39,015.50	5000
Surda / Ramallah (30)	Access Roads	74,938.-	44,963.-	29,975.-	600
El-Shawawreh/Bethlehem (31)	Agricultural Road	57,594.-	32,829.-	24,765.-	4500
Zif / Hebron (32)	Primary School	72,188.-	46,922.-	25,266.-	2000
Huwara / Nablus (33)	Out-Patient Clinic	58,437.-	29,218.50	29,218.50	8000

8

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( ) FINAL

Date of Last report: 1 April 1986  
Date of This report: 1 October 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-04

US. \$ 91,000.-

Sub-Project estimated cost

CRS JWB in co-operation with

SILET EL-HARTHIEH VILLAGE

Name of Operating Agency

COMMUNITY CENTER

Title of Sub-Project

JENIN DISTRICT

Area in which Sub-Project is located

NEB-0159-G-SS-5123-00

Funding Agency Code Number

2. EXPENDITURE SECTION

.US \$ 45,500.-

(I) CRS AID cash input

Equivalent to \$ 45,500

Village cash input

. US. \$ 746,112.-

(II) Funds received to date & date of last transmittal

15 August 1986

CRS AID US \$ 45,498.11

(III) Sub-Project expenditure (s) to date

Village US \$ 48,611.55

CRS AID US \$ 1.89

(IV) Balance (s) unused

Village US \$ (3,111.55)

(Overspent)

The strong willingness of the villagers to cooperate with CRS. The donated the piece of land on which the center was constructed. Tax exemption on construction material.

(V) Other inputs which contributed to success of Sub-Project

9

### 3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWC/USAID

- The agreement covering this sub-project was signed with the village leadership on 22 July 1985. Implementation started on 30 August 1985 and was successfully completed on 27 July 1986.
- The sub-project final cost came to U.S. \$ 94,109.66. The village's cash input amounted to \$ 48,611.55 equivalent to 52%, versus CRS/AID cash input of \$ 45,498.11, which is 48% of the total cost. Attached is a detailed final statement of expenditures.
- The two - floor community center consists of 15 rooms, assembly hall, storeroom, corridor, staircase, two kitchens and eight bathrooms. The assembly hall serves as a meeting place for the villagers as well as for social and cultural events.
- The community activities in this center are run and organized by the Village Council. The villagers use the center for weaving and fashion design courses, public library, post office, handicapped center, and sports activities. The center also houses the Village Council which is responsible for all the activities of the Charitable Society. Their activities are a public clinic, kindergarten, knitting and sewing, education, mother and children care, and health education.
- Villagers now have a suitable building where they can carry out all their activities instead of the old scattered rented rooms. They do not have to pay rent anymore. Sick people no longer have to wait hours outside the clinic under the hot sun in summer and heavy rain in winter.
- Villagers donated the piece of land on which the center was built. They also constructed the building wall and asphalted the playground on their own expense.
- Most of the villagers contributed towards the village's share of the sub-project's costs.
- Attached are photos showing the project in its different aspects of implementation.

**EVALUATION:**

- The Community Center contributes to the Overall Goal of the Grant which is development of Rural West Bank Arab Villages.
- Facilities for carrying out community sponsored activities have been improved. This sub-project opened new educational opportunities for the villagers by providing them with a suitable place where they can plan and carry out activities.
- The new center enables the residents to experience a strong sense of participation in their community.

GA/lb


11

1 OCTOBER 1986

LOCATION OF SITES

- \* Four Sub-Projects Completed (04, 06, 11, 15)
- + Twelve Sub-Projects Ongoing (12, 13, 14, 16, 17, 19, 20, 21, 22, 23, 24, 25)
- Y Ten Sub-Projects Waiting Approval (09, 18, 26, 27, 28, 29, 30, 31, 32, 33)

- Silat El-Harthleh (04)
- Y Barta' & Khirbat Barta' (28)
- Y 'Atell (26)
- Shwaleh (23)
- Zbadat (21)
- Y Illi (27)
- Jeet (13)
- Kufor Kaddum (12)
- Y Huwwara (33)
- Yatmah (22)
- Y Beir Zeit (09)
- Y Surda (30)
- Y El-Shawarbeh (31)
- Za'Zara (06)
- Husan (14)
- Marah Rabah (15)
- Y Wadi Fukkin (18)
- Nahhalin (11)
- Beit 'Anwar (16)
- Y El-Shiyakh (29)
- Beit M'aim El-Idlalah (17)
- El-Mureq El-Kom (20)
- Y Zif (32)
- Beit El-Rush El-Qog
- Beit El-Rush El-Tahta (25)
- Raqa' (19)

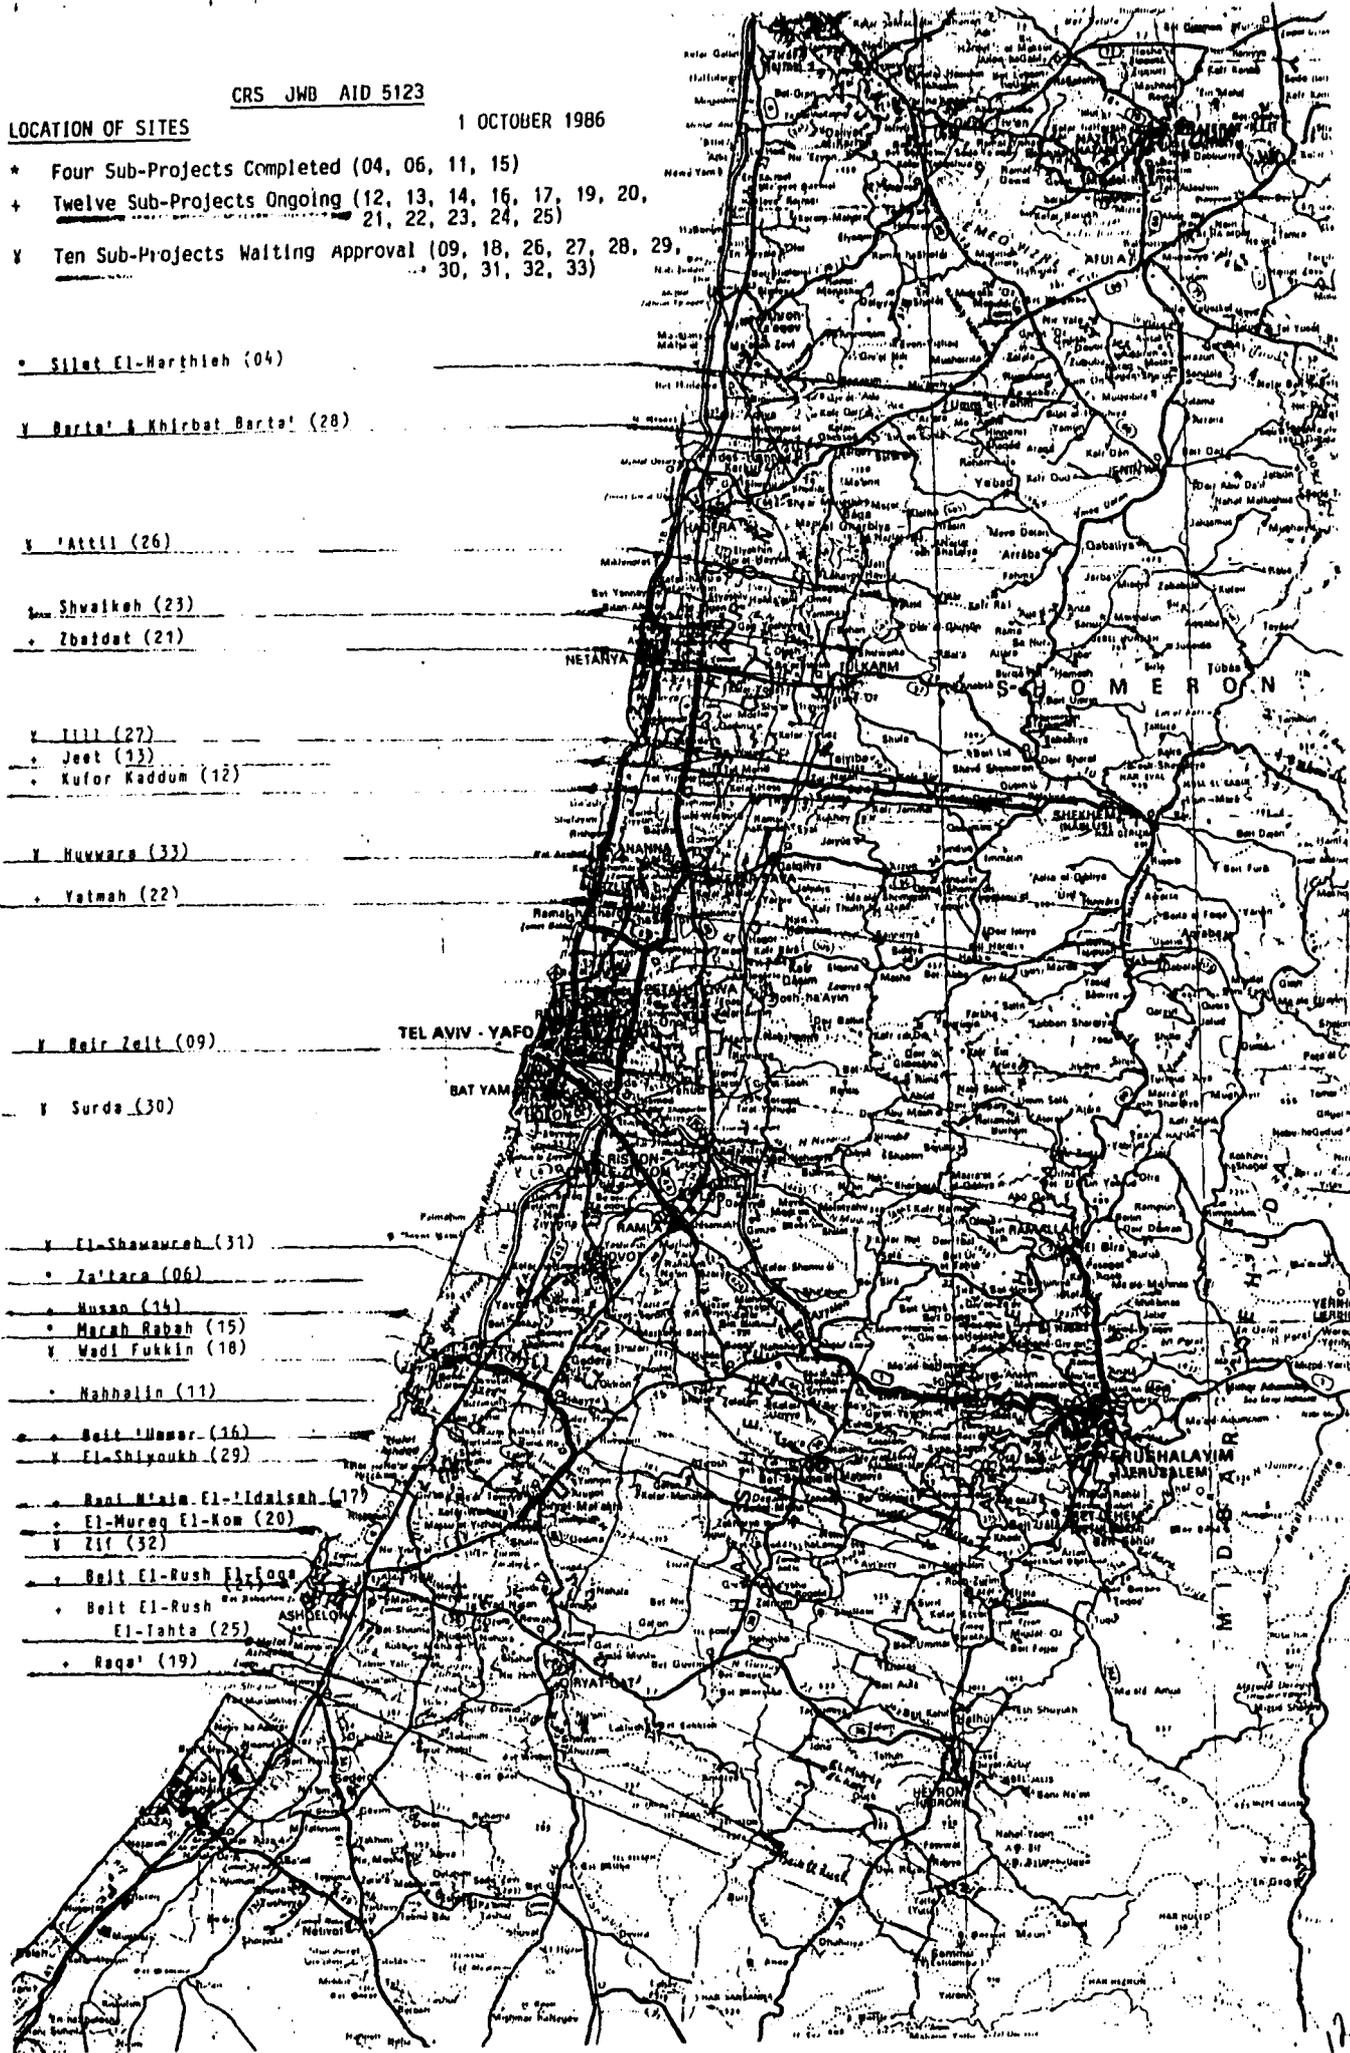

ITEMIZATION OF EXPENDITURES

BILET EL-HARTHIEH COMMUNITY CENTER

4D-006-04

	<u>N. I. S.</u>
1. Cement Blocks (4250 Blocks)	9,614.38
2. Cement (71.25 Tons)	8,351.55
3. Concrete (289 m3)	17,883.51
4. Mixed Gravel (158.83 Tons)	2,240.26
(7 Loads)	1,431.15
5. Sand (148.54 Tons)	1,542.09
(10 Loads)	1,041.98
6. Building Stones (1990 m)	7,968.50
7. Rough Stones (10 Loads)	860.13
8. Limestone (40 bags)	300.-
9. Roofing Iron (21,625 Kgs)	16,719.20
10. Iron doors and windows	4,353.78
11. Asphalt (3 barrels)	.48.96
12. Pipes (73 meters)	114.20
13. Tiles (750 meters)	4,777.50
14. Aluminium Windows (79 m2)	7,775.20
15. Water Tanks (32 Tanks)	401.55
16. Plumbing parts	3,212.52
17. Electrical wires and parts	227.50
18. Bulldozer (44 hrs.)	1,470.86
19. Dumping Truck (18 Loads)	246.20
20. Cementing roof and floor	1,162.80
21. Demolishing old building	1,227.-
22. Sanitary Equipments	2,038.20
23. Date Stone	172.-
24. Mason (768 m2)	26,949.96
25. Electrician	445.50
26. Plumber	445.50
27. Plasterer (2850 m2)	5,127.-
28. Carpenter (36 doors)	5,509.64
29. Tiling (750 m2)	1,743.80
30. Pointing (550 m2)	1,397.76
31. White washing and Painting (by work)	1,737.-
32. Photos	172.-
	-----
TOTAL	N IS 138,709.18
	US \$ 94,109.66

CRS SHARE 48% = US \$ 45,498.11 NIS 67,032.88

VILLAGE SHARE 52% = US \$ 48,611.55 NIS 71,676.30

N.B. Laborers' wages were charged to the village.

13

PHOTOS ILLUSTRATING THE PROJECT

CRS JWB USAID 4D-006-04

TOTAL COST : 94,109.66

CRS SHARE : 48%

VILLAGE SHARE : 52%

SILET EL-HARTHIEH (POP. 7500):

Constructing a two - floor community center consisting of 15 rooms, assembly hall, store-room, corridor, staircase, 2 kitchens & 8 W.C. units, the whole totalling about 736m<sup>3</sup>.


PROJECT STARTED: 30.08.1985

PROJECT COMPLETED: 27.07.1986

- *Silet El-Harthieh village approached CRS/AID for help in constructing a suitable place with improved facilities, to replace the scattered small rented rooms, for carrying out community activities. Here is seen the piece of land bought to construct the community center on.*

- *Photo shows the completed center on the same plot of land shown above. The two - floor building consists of fifteen rooms, assembly hall, storeroom, corridor, staircase, two kitchens, and eight bathrooms. It is large enough to house all the community activities which include a public clinic, a village post office, kindergarten, knitting and sewing , mother and children care, and health education.*



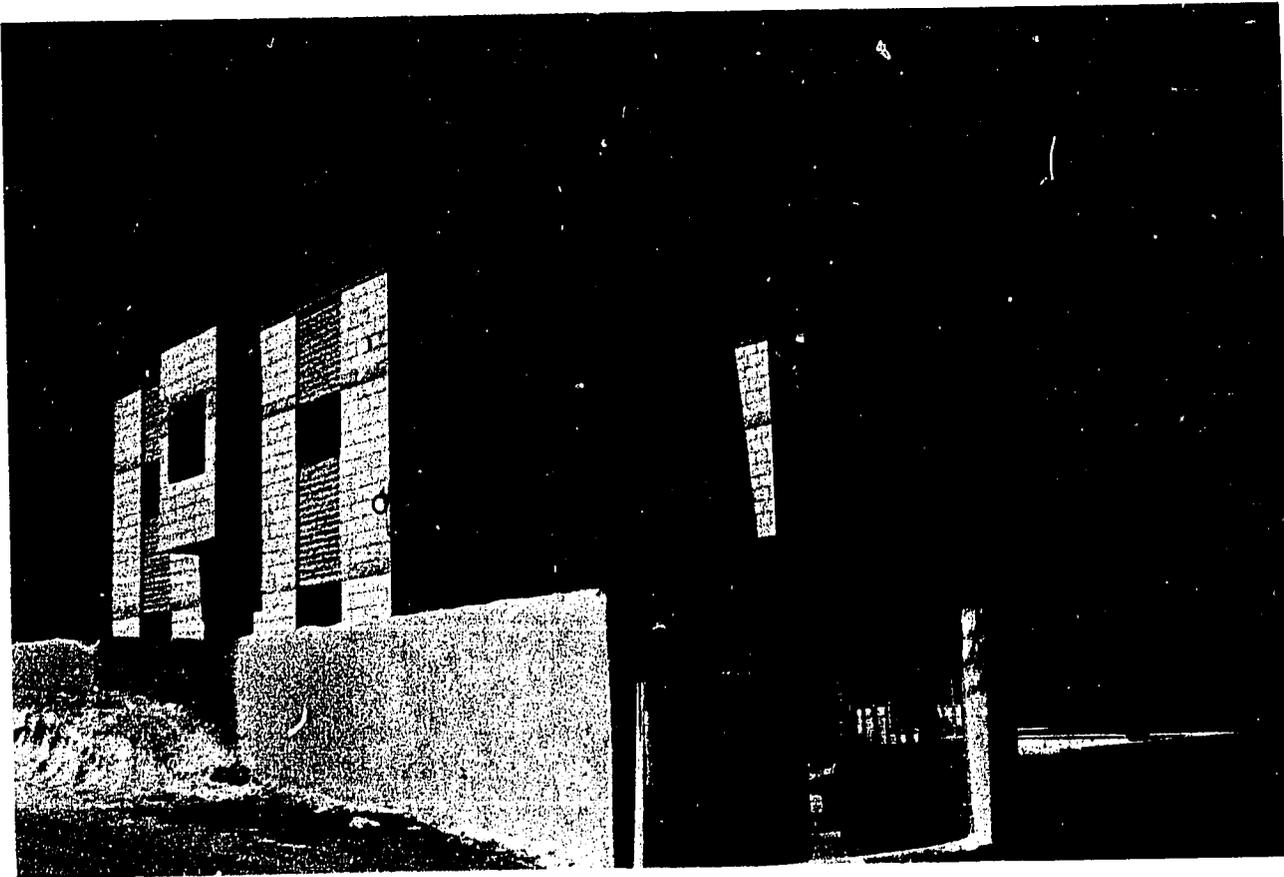

- *Here is seen a kindergarten class, in a good and proper room. 155 child are enrolled in the four kindergarten classes.*

- *Photo shows young and old women from Silet El-Harthieh attending one of the literacy classes, an activity currently ongoing at the new center.*



- *Health Education courses have been already organized at the new center. The photo shows village women weighing a child during one of the Health Education classes under the supervision of CRS Health Education Project-CRS/AID NEB 0159-G-SS-5065-00. 50 women are enrolled in this course.*

- *Photo shows villagers in the waiting room of the public clinic in which a part-time doctor works two days a week. Patients no longer have to wait long hours under the heavy rain in winter or hot sun in summer.*





جريدة يومية سياسية

JERUSALEM - ASHAAB ARABIC DAILY NEWSPAPER

شكر وتقدير

لجمعية الاغاثة الكاثوليكية

زعترة - رئيس واعضاء جمعية زعترة التعاونية الخيرية وعموم  
اهالي القرية يتقدمون بخالص آيات الشكر والتقدير الى رئيس  
واعضاء جمعية الاغاثة الكاثوليكية لتفضلهم مشكورين بالمساهمة  
في بناء مقر للجمعية.  
وتخص بالذكر السيد عيسى بركات مدير الجمعية ومساعدته ابو  
حنا ومهندس الجمعية.  
جزاهم الله كل خير وادامهم ذخرا للانسانية.

THANKS AND APPRECIATION  
FOR THE CATHOLIC RELIEF SERVICES

Za'tara - The head and members of Za'tara - Al-Ta'amreh Charitable Society, and all the village inhabitants, present their deep thanks and appreciation to the Director and Staff of the Catholic Relief Services for their kind participation in constructing the Community Center.

We would like to single out Mr. Issa Barakat, the Rural Development Director, his assistance Abu Hanna, and the association's architect.

May God reward them all the good and keep them a support for humanity.

ITEMIZATION OF EXPENDITURES

ZA'TARA COMMUNITY CENTER

4D-006-06

	<u>N.I.S.</u>
1. Cement (52 Tons) (4000 Blocks)	5,721.38 2,043.30
2. Concrete (149 m3)	8,018.28
3. Rough Stones ( 3 Truck loads)	345.11
4. Mixed gravel (19 Truck loads)	2,277.04
5. Sand (6 Truck loads)	710.20
6. Building Stones (839 m)	4,311.61
7. Limestone (95 kgs)	257.-
8. Tiles (350 m2)	2,229.50
9. Iron (2000 kgs)	2,328.48
10. Electrical Parts and Boards	2,352.62
11. Roofing steel (12 tons)	9,600.-
12. Plumbing Parts	3,318.40
13. Iron Doors and Windows (130 m2)	5,466.-
14. Date Stone	166.-
15. Glass (5.56 m)	250.-
16. Mason (by the job)	16,339.-
17. Chipping Stones (73 Work Days)	1,825.-
18. Connecting Electricity	2,352.90
19. Surveying the building	615.-
20. Sketches	820.-
21. Digging Foundations	1,470.-
22. Leveling Floor	333.60
23. Electrician	625.50
24. Wooden Doors (12 Doors)	1,696.40
25. Digging and Constructing Cesspool (by the job)	1,898.-
26. Plasterer (1303 m2)	4,333.63
27. Aluminium Windows (41 m2)	4,053.60
28. Pointing (157 m2)	251.40
29. Tiling (400 m2)	1,481.82
30. Bulldozer	577.20
31. White Washing and Painting (by the job)	1,352.50
32. Plumber (10 points)	305.-
	-----
TOTAL	N.I.S. 89,725.47 U.S.\$ 60,907.95

CRS SHARE	58.7%	=	US \$ 35,750.65	NIS	52,661.01
VILLAGE SHARE	41.3%	=	US \$ 25,157.30	NIS	37,064.46

- 22 -

- **EVALUATION**

- The Community Center contributes to the Overall Goal of the Grant which is development of Rural West Bank Arab Villages.
  
- Facilities for carrying out community sponsored activities have been improved. The new center provides the villagers with a suitable place where they can plan and perform activities thus increasing their participation in the community.

GA/lb

### 3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The agreement covering this sub-project was signed with the village leadership on 31 July 1985. Implementation started on 28 August 1985 and was successfully completed on 10 September 1986.
- The sub-project's final cost came to U.S. \$ 60,907.95. The village's cash input amounted to \$ 25,157.30 equivalent to 41.3%, versus CRS AID cash input of \$ 35,750.65, which is 58.7% of the total cost. Attached is a detailed final statement of expenditures.
- The two-floor community center consists of eight rooms, assembly hall, corridor, staircase, kitchen, and five bathrooms. The assembly hall is used for sports, social, and cultural events. It also serves as a meeting place for the villagers.
- This sub-project encouraged Za'tara villagers to conduct communal activities and to offer relevant services. They now have more space which allows increased enrollment in the existing activities: kindergarten, literacy classes, karate courses, sports club, and the library. Za'tara villagers also use this center for Health Education, sewing and knitting, and private intensive courses for preparatory and secondary students.
- The center greatly encouraged Za'tara villagers to take part in various activities as they are housed in one building instead of scattered, small rented rooms. Development of Za'tara community will be promoted.
- Proud by their new building, and encouraged in the way work was performed, Za'tara villagers constructed the skeleton of the third floor on their own expense.
- Attached are photos showing the center during and after implementation in addition to some of the activities that are now carried inside it.

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( ) FINAL

Date of Last report: 1 APRIL 1986  
Date of This report: 1 OCTOBER 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-06

US. \$ 59,600.-

Sub-Project estimated cost

CRS JWB in co-operation with ZA'TARA VILLAGE  
Name of Operating Agency

COMMUNITY CENTER  
Title of Sub-Project

BETHLEHEM DISTRICT  
Area in which Sub-Project is located

NEB-0159-0-SS-5123-00  
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 35,760.- Equivalent to \$ 23,840.-  
(I) CRS AID cash input Village cash input

US \$ 746,112.- 15 AUGUST 1986  
(II) Funds received to date & date of last transmittal

CRS AID US \$ 35,750.65 Village US \$ 25,157.30  
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 9.35 Village US \$ (1,317.30)  
(IV) Balance (s) unused (Overspent)

Tax exemption on construction material. The strong willingness of Za'tara villagers to develop their village.

(V) Other inputs which contributed to success of Sub-Project

25

PHOTOS ILLUSTRATING THE PROJECT

CRS JWB / USAID 4D-006-06

TOTAL COST : 60,907.95

CRS SHARE : 58.7%

VILLAGE SHARE : 41.3%

ZA'TARA PROJECT (POP. 2000):


Constructing a two - floor Community Center consisting of 8 rooms, assembly hall, corridor, staircase, kitchen and 5 W.C. units, the whole totalling about 350 m2.

PROJECT STARTED: 28 August 1985

PROJECT COMPLETED: 10 September 1986

1. Za'tara villagers wanted a good and suitable place to hold community activities instead of the scattered, small rooms that were being rented for this purpose. CRS AID helped the village to build a proper community center. The photo shows the piece of land that the villagers bought on their own expense to construct the community center on.

2. Photo shows the completed Community Center on the same plot of land shown above. The building is large enough to house all the community activities which include kindergarten, literacy classes, library, sports activities, health education, sewing and knitting, and private intensive courses.

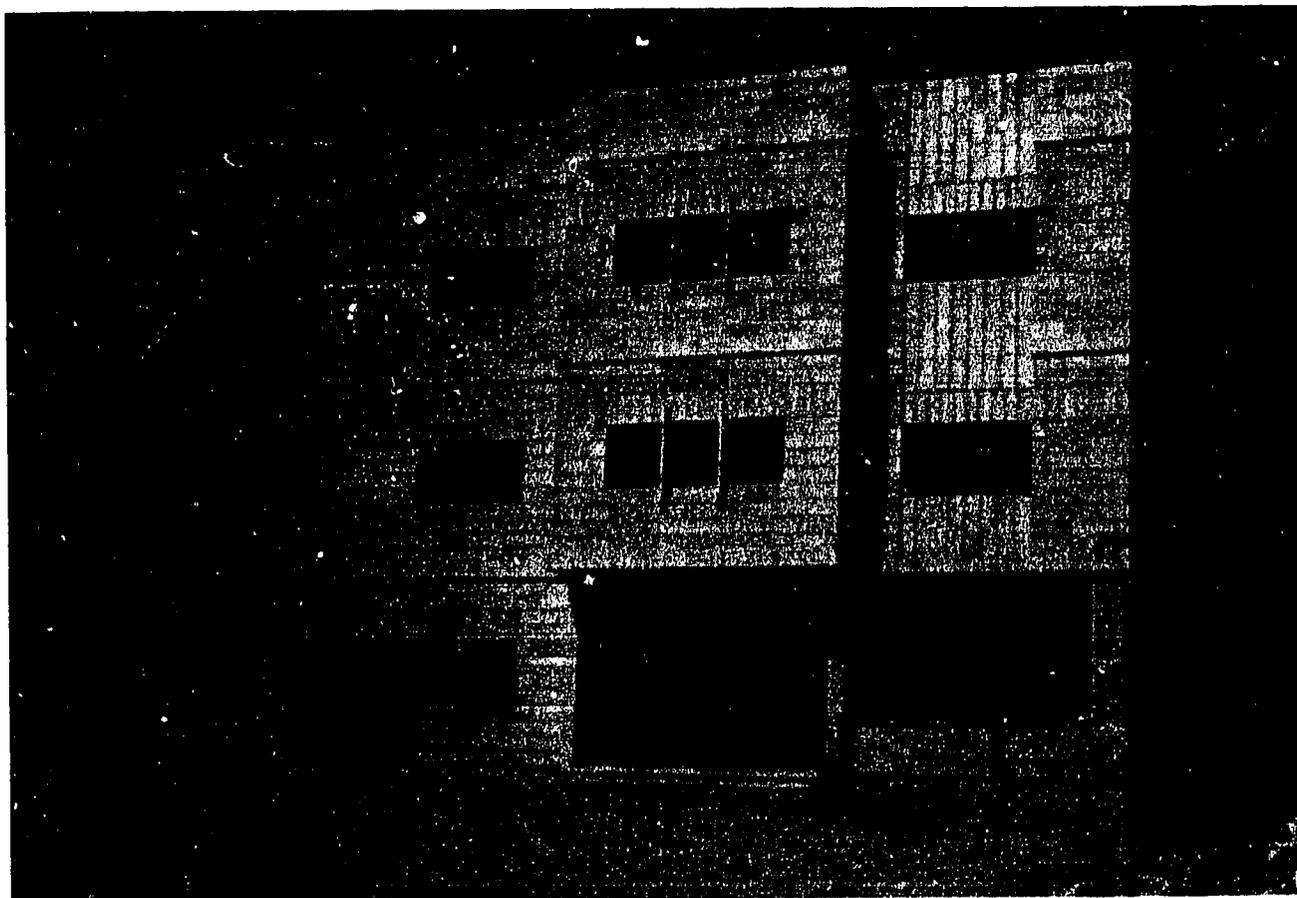


20

3. Photo shows a literacy class in a good and proper room. 22 women from Za'tara are enrolled in this class.



4. Here is a kindergarten class, one of the activities currently ongoing at the new center. 78 children are enrolled in the kindergarten classes.

5. Sports activities are also carried out at the new center. 135 persons are registered in these activities. Photo shows karate students training in one of their sessions.

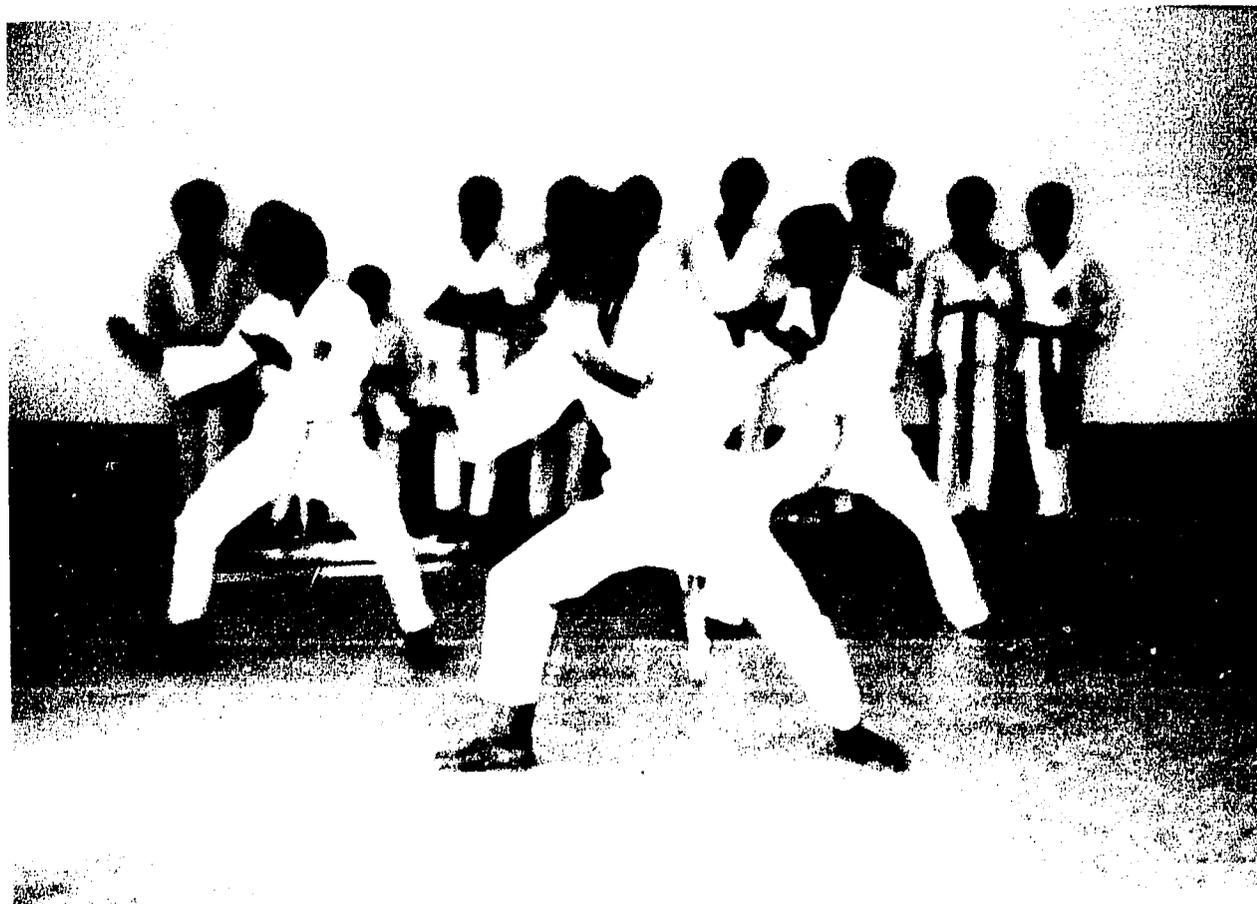

AL - FAJR DAILY  
JERUSALEM  
Tuesday 20  
May 1986  
No - 4087



القدس  
الثلاثاء ٢٠ ايار ١٩٨٦ م  
١٢ رمضان ١٤٠٦ هـ  
السنة الرابعة عشر  
العدد ٤٠٨٧

### شكر وتقدير

نحاليين ، بيت لحم - نتقدم نحن مختار أوأعالي قريسة  
نحاليين قضاء بيت لحم بجزيل الشكر وبمعظيم التقدير اللى  
مدير وموظفي خدمات الاغاثة الكاثوليكية بالقدس على مسا  
تدبره لنا من مساعدات عظيمة بخصوص الشارع الذى يربط  
قريتنا بالشارع الرئيسى « الخليل - القدس » ويبلغ  
طوله ٣ كيلو مترات ونصف الكيلو حيث تم تسوية هذا  
الشارع بومده بطبقة مسن البسكورس وتعبيد حوالى  
كيلو متر منه وقد أصبحنا - بفضل هذا المشروع -  
نستطيع الوصول الى ارضنا بسهولة ونقل انتاج مزرعاتنا  
بيسر . .

جزاهم الله كل خير

عنهم

المختار حسين يوسف  
والسيد محمد ابراهيم احمد

### THANKS AND APPRECIATION

Nakhalin - Bethlehem - We the mukhtar and inhabitants of Nakhalin Village/Bethlehem District present our deep thanks and great appreciation to the director and staff of the Catholic Relief Services in Jerusalem for the great assistance they have offered concerning the street that links our village with the main road (Hatron/Jerusalem). The street which is 3.5 kms long, was levelled and covered with mixed gravel, and 1 km was asphalted. Now, thanks to this project, we can easily reach our land and tranfer our agricultural products.

May God reward them all the good.

The Mukhtar Hassan Youssef and  
Mr. Moh'd Ibrahim Ahmad.

ITEMIZATION OF EXPENDITURES

NAHHALIN SUB-PROJECT

4D-006-11

		<u>N.I.S.</u>
1.	Operation and Rental of dumping Truck (1200 loads)	27,360.-
2.	Operation and Rental of Bulldozer (160 hrs)	7,214.40
3.	Operation and Rental of Excavator (96 hrs)	4,406.-
4.	Operation and Rental of Grader (9 days)	4,131.-
5.	Operation and Rental of Trolley (67 loads)	922.59
6.	Gravel Mixture (941.780 Tons)	9,726.22
7.	Asphalt Mixture (432.120 Tons)	23,799.15
8.	Labourers' Wages (25 Work Days)	421.36
	TOTAL	N.I.S. 77,980.72 U.S.\$ 53,017.43

CRS SHARE 60% = U.S. \$ 31,793.86 = N.I.S. 46,797.57

VILLAGE SHARE 40% = U.S. \$ 21,223.57 = N.I.S. 31,183.15

GA/LB

32'

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- EVALUATION:-

- The road contributes to the Overall Grant Goal which is development of Rural West Bank Arab Villages.
- Farmers have good access to their fields all year Loss and damage of crops is reduced, enabling the farmers to get a higher return on their produce.
- Existing lands and groves will be better cultivated and new fields will be reclaimed for the first time.
- The Agriculture Department can easily visit the village fields for extension work and advice.

### 3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The agreement covering this sub-project was signed with the village leadership on 27 November, 1985. Implementation started on 4 January 1986 and was successfully completed on 21 March 1986.
- The sub-project final cost came to U.S. \$ 53,017,43. The village's cash input amounted to \$ 21,223.57 equivalent to 40%, versus CRS/AID cash input of \$ 31,793.86, which is 60% of the total cost. Attached is a detailed final statement of expenditures.
- Nahhalin villagers have better access to their fields all year round. They are able to get their agricultural produce to Bethlehem and other towns while fresh, to be either sold locally or exported to Arab countries. Prior to this sub-project, farmers used to commute to their fields and groves either on foot or by donkey. This means of transport was not only slow, but meant that only a small amount of produce could be transported at a time. Now, more produce reaches market quickly, enabling the farmers to get a higher return.
- Part of the agricultural road is considered as an interior street as it passes through the village. It is clean, with no dust or mud. Four families, encouraged by this road, started to construct houses along the side of the road.
- This sub-project was completely successful due to the strong willingness of Nahhalin villagers to cooperate and to work together. Under the same costs, we were able to open, clear, and level an additional half-kilometer long access road.
- Beneficiaries of this vital sub-project are the entire Nahhalin villagers (1500 persons).
- The entire village contributed to the village's share of the sub-project's costs.
- Attached are photos showing the project in its different aspects of implementation.

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( ) FINAL

Date of Last report: 1 April, 1986  
Date of This report: 1 October, 1986

REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-11

US. \$ 53,019.-

Sub-Project estimated cost

CRS JWB in co-operation with NAHHALIN VILLAGE  
Name of Operating Agency

AGRICULTURAL ACCESS ROAD  
Title of Sub-Project

HEBRON DISTRICT  
Area in which Sub-Project is located

NEB - 0159 - G - 66 - 5123 - 00  
Funding Agency Code Number

EXPENDITURE SECTION

.US \$ 31,811.- Equivalent to \$ 21,208.-  
CRS AID cash input Village cash input

. U.S. \$ 746,112.- 15 AUGUST, 1986  
) Funds received to date & date of last transmittal

CRS AID US \$ 31,793.86 Village US \$ 21,223.57  
I) Sub-Project expenditure (s) to date

CRS AID US \$ 17.14 Village US \$ (15.57)  
) Balance (s) unused (Overspent)

The strong willingness of Nahhalin villagers to work together. They donated parts of their lands which were in the way of the projected road.

) Other inputs which contributed to success of Sub-Project

35

PHOTOS ILLUSTRATING THE PROJECT

CRS JWB / USAID 4D-006-11

TOTAL COST : 53,017.43

CRS SHARE : 60%

VILLAGE SHARE : 40%

NAHHALIN PROJECT (POP. 1500):

Widening, clearing and leveling an existing agricultural access road about 3.5 Kms long by 5 meters wide including asphaltting 1.2 Kms long stretch by 3 meters wide and constructing a crossing.


PROJECT STARTED: 4 January, 1986

PROJECT COMPLETED: 21 March, 1986

1. Nahhalin agricultural road was in a very bad condition. Farmers used to reach their fields and groves either on foot or donkeys. This means of transport was not only slow, but meant that only a small amount of produce could be transported at a time. CRS/AID agreed to help the village in widening, clearing, and leveling the agricultural access road.



2. Photo shows another section of the agricultural road in the process of being paved.
3. Here is a view of the very same section of the road shown above now converted into a proper road. Loss and damage of crops is now reduced, enabling the farmers to get a higher return.

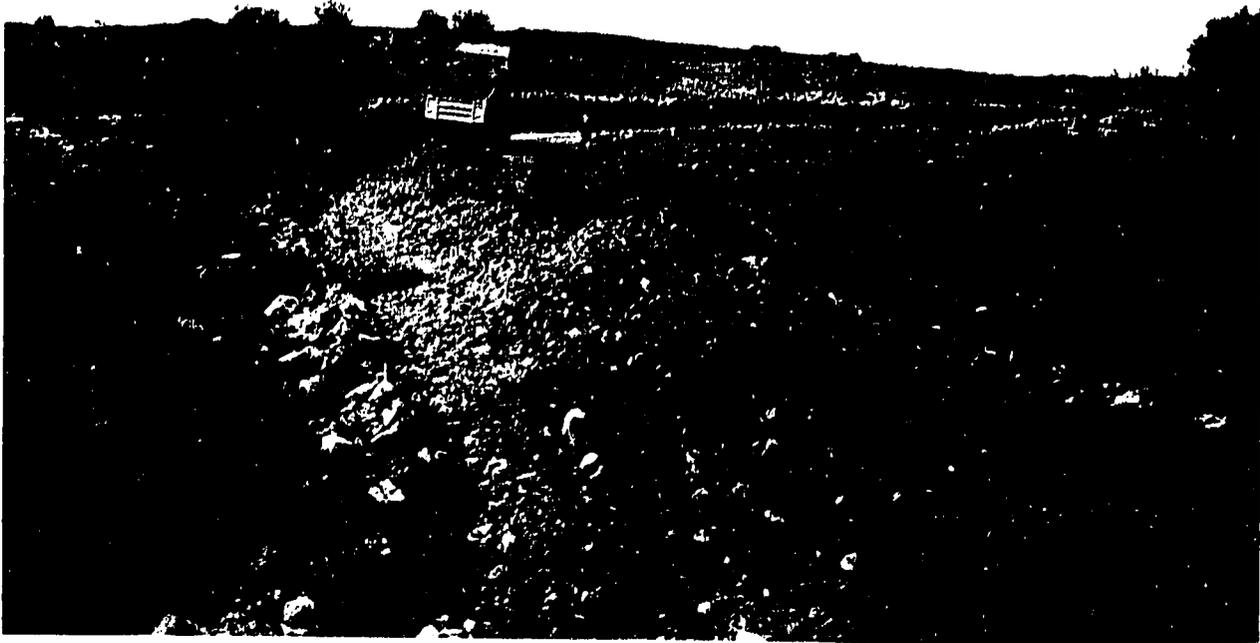

170



RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 2 )

Date of Last reports: 1 April, 1986  
Date of This report: 1 October, 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-12

US, \$ 105,628.-

Sub-Project estimated cost

CRS JWB in co-operation with

KUFOR KADDUM VILLAGE

Name of Operating Agency

DRINKING WATER SYSTEM

Title of Sub-Project

TULKAREM DISTRICT

Area in which Sub-Project is located

NEB - 0159 - G - SS - 5123 - 00

Funding Agency Code Number

2. EXPENDITURE SECTION

.US \$ 52,814.-

Equivalent to \$ 52,814.-

(I) CRS AID cash input

Village cash input

. U.S. \$ 746,112.-

15 AUGUST, 1986

(II) Funds received to date & date of last transmittal

CRS AID US \$ 20,160.86

Village US \$ 35,156.88

(III) Sub-Project expenditure (s) to date

CRS AID US \$ 32,653.14

Village US \$ 17,657.12

(IV) Balance (s) unused

(V) Other inputs which contributed to success of Sub-Project

40

**3 PROGRESS OF (SUB) PROJECT SECTION CRS--JWB/USAID**

- This sub-project calls for establishing a drinking water system throughout the village, linking it with the main line of the West Bank Water Authority.
- A tender for installing the water net was held on 21/5/1986 and a sub-contractor was chosen. Attached is the Tender Notice and its translation.
- 80% of the net is completed. A strike in the Water Pipes Factory delayed the work. We are now waiting for the Water Department to connect the village with the main line.
- This sub-project is expected to be completed by the end of October 1986.

GA/1b

# القدس

٢٥  
اغورة

١٢  
صفحة

جريدة يومية سياسية

"AL-QUDS" Jerusalem Wednesday 14 May 1986 No. 6003

الاربعاء ١٤ ايار ١٩٨٦ - ٦ رمضان ١٤٠٦ هـ العدد ٦٠٠٣

## Tender Notice

Nablus- Kufor Kaddum- The Water Committee of Kufor Kaddum Village in cooperation with CRS invite bids in sealed envelopes for carrying out the internal water net for the village. Those who wish to participate in this tender can obtain a copy of the specifications and layouts from the mukhtar Mr. Saleh Youssef Saleh in exchange for 10 J.D. unrefundable.

Bids should be submitted to the mukhtar Saleh Youssef accompanied with an insurance of 5% of the total value, cash, or endorsed check, or bank guarantee not later than 11 a.m., Wednesday 21/5/1986.

Remarks: Awardee is to pay the cost of the advertisements in the papers.

2. The committee does not undertake to accept the lowest offer or any other offer and without explaining the reasons.

3. Any bid not according to the instructions will not be considered-especially the condition of enclosing an insurance as it is mentioned above.

## اعلان مناقصه

نابلس - كفر قدوم - تعلن لجنة مياه قرية كفر قدوم بالتعاون مع خدمات الاغاثة الكاثوليكية عن طرح عطاء تنفيذ شبكة المياه الداخلية في القرية للمناقصة عن طريق الظرف المختوم - كل متعهد يرغب في الاشتراك بهذه المناقصة يمكنه الحصول على نسخة من المواصفات والمخططات من منزل المختار صالح يوسف صالح مقابل مبلغ عشرة دنانير اردنية غير مستردة.

تعاد العطاءات بعد تعبئتها الى منزل المختار صالح يوسف مرفقه بتأمين مقداره ٥٪ من قيمة العطاء نقدا او شيك مصدق او كفالة بنكية غير متأخرة عن الساعة الحادي عشرة من صباح يوم الاربعاء الموافق ١٩٨٦/٥/٢١

ملاحظات : ١- اجور الاعلان في الصحف على المتعهد الذي يحال عليه العطاء

٢- اللجنة غير مقيدة بقبول ارضى العروض او اي عرض اخر دون ابداء الاسباب

٣- لن ينظر في اي عطاء مخالف لاي شرط من شروط العطاء وخاصة شرط ارفاق التأمين كما هو مذكور اعلاه .

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 2 )

Date of Last report: 1 April, 1986  
Date of This report: 1 October, 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-13

US. \$ 53,020.-

Sub-Project estimated cost

CRS JWB in co-operation with

JEET VILLAGE

Name of Operating Agency

DRINKING WATER SYSTEM

Title of Sub-Project

TULKAREH DISTRICT

Area in which Sub-Project is located

NEB-0159-G-SS-5123-00

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 31,817.-

(I) CRS AID cash input

Equivalent to \$ 21,211.-

Village cash input

U.S. \$ 746,112.-

(II) Funds received to date & date of last transmittal

15 August, 1986

CRS AID US \$ 18,658.55

(III) Sub-Project expenditure (s) to date

Village US \$ 19,814.88

CRS AID US \$ 13,158.45

(IV) Balance (s) unused

Village US \$ 1,396.92

(V) Other inputs which contributed to success of Sub-Project

43

### 3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for establishing a potable drinking water system throughout the village, linking it with the main line of the West Bank Water Authority.
- A tender for installing the water net was held on 22/5/1986 and a sub-contractor was chosen. Attached is the Tender Notice and its translation.
- Work was delayed due to a strike in the Water Pipes Factory. We are now waiting for the Water Department to connect the village with the main line.
- 90% of the net is completed and the sub-project is expected to be successfully completed by the end of October 1986.

GA/1b

44

# القُدس

٢٥  
اغورة

١٢  
صفحة

جريدة يومية سياسية

"AL-QUDS" Jerusalem Wednesday 14 May 1986 No. 6003

الأربعاء ١٤ ايار ١٩٨٦ - ٦ رمضان ١٤٠٦ هـ - العدد ٦٠٠٣

## TENDER NOTICE

**NABLUS - JEET :** The Water Committee of Jeet village in cooperation with CRS invite bids in sealed envelopes for carrying out the internal water net for the village. Those who wish to participate in this tender can obtain a copy of the specifications and layouts from Mr. Ma'zouz Issa Hasan khader in exchange for 10 J.D. unrefundable. Bids should be submitted to Mr. Ma'zouz Issa Khader, accompanied with an insurance of 5% of the total value, cash, or endorsed check, or bank guarantee not later than 11 a.m., Thursday 22/5/1986.

- REMARKS:**
1. Awardee is to pay the cost of the advertisements in the papers.
  2. The committee does not undertake to accept the lowest offer or any other offer and without explaining the reasons.
  3. Any bid not according to the instructions will not be considered - especially the condition of enclosing an insurance as it is mentioned above

## اعلان مناقصه

نابلس - جيت - تعلن لجنة مياه قرية جيت بالتعاون مع خدمات الاغاثة الكاثوليكية عن طرح عطاء تنفيذ شبكة المياه الداخلية في القرية للمناقصة عن طريق الخرف المختوم . كل من يرغب الاشتراك في هذه المناقصة يمكنه الحصول على نسخة من المواصفات والمخططات من منزل السيد معزوز عيسى حسن خضر مقابل دفع مبلغ عشرة دنانير اردنية غير مستردة .

تعاد العطاءات بعد تعيينتها الى السيد معزوز عيسى خضر مرفقة بتامين بمقدار ٥٪ من قيمة العطاء اما نقدا واما شيك مصدق او كفالة بنكية غير متاخرة عن الساعة الحادية عشرة من صباح يوم الخميس الموافق ١٩٨٦/٥/٢٢ .

ملاحظات : ١- اجور الاعلان في الصحف على المتعهد الذي يحال عليه العطاء .

٢- اللجنة غير مقيدة بقول اخص العروض او اي عرض اخر دون ابداء الاسباب .

٣- لن ينظر في اي عطاء مخالف لاي شرط من شروط العطاء وخاصة شرط ارفاق التامين كما هو مذكور اعلاه .

P.O. BOX 19447  
East Jerusalem

CATHOLIC RELIEF SERVICES - USCC  
JERUSALEM AND WEST BANK

PAGE OF

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last report:

Date of This report: 1 October, 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-14

US, \$ 39,029.14

Sub-Project estimated cost

CRS JWB in co-operation with HUSAN VILLAGE  
Name of Operating Agency

PRIMARY SCHOOL  
Title of Sub-Project

BETHLEHEM DISTRICT  
Area in which Sub-Project is located

NEB-0159-C-88-5123-00  
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 19,514.57 Equivalent to \$ 19,514.57  
(I) CRS AID cash input Village cash input

US \$ 746,112.- 15 AUGUST, 1986  
(II) Funds received to date & date of last transmittal

CRS AID US \$ 12,667.83 Village US \$ 28,836.18  
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 6,846.74 Village US \$ (1,321.61)  
(IV) Balance (s) unused (OVERSPENT)

(V) Other inputs which contributed to success of Sub-Project

46

### 3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for the construction of additional classrooms for Husan's School.
- The agreement covering this sub-project was signed with the village leadership on 9 April 1986. Implementation started on 2 May 1986 and work is expected to be completed by the end of October 1986.
- This sub-project is a very successful one. The school skeleton is completed. The doors and windows frames were placed. A plasterer and a mason were chosen and started work. All the tiles are on the spot.
- After obtaining the approval of the Education Department and CRS, the villagers decided to roof the basement to be used as additional classrooms in case of any future need. This increased the village's share in the sub-project's costs.

GA/1b

CATHOLIC RELIEF SERVICES - USCC  
JERUSALEM AND WEST BANK

Sub-Project Proposal Within Package  
Project No. CRS JWB 4D-006

Sub-project Number : CRS JWB - 4D-006-14

Sub-project Location : Husan village, Bethlehem District, West Bank

Operating Agency : CRS JWB together with Husan village.

Sub-project proposal : Constructing the second floor of the primary school (five rooms, balcony and an external staircase) the whole totalling about 246 m<sup>2</sup>.

Objective : To improve primary level education facilities (for boys) in a rural area of Bethlehem District.

Expected Results : Primary level education for boys in rural Husan village will become more suitable. The five new rooms will replace current inadequate and inappropriate quarters. It will also serve the boys of the two neighbouring villages of Wadi Fukkin and Nahhalin.

Time Needed to complete sub-project : Construction of the building should take about 4 months. The additional school floor will be put to use immediately after completion of construction. The education Department will furnish the school and provide the necessary teaching staff and text-books.

Supporting Local Authorities : Husan village committee, Department of Labour and Social Welfare, Department of Education, and West Bank Military Government.

Estimate of costs : \$ 39,029.14 equivalent to J.D. 13,660.20 at exchange rate of J.D. 0.35 = \$1.--.

Participants in costs : CRS JWB up to a maximum of 50% equivalent to \$ 19,514.57 = J.D. 6,830.10

Husan village at least 50% equivalent to \$ 19,514.57 = J.D. 6,830.10

48

**Construction Plan prepared by** : **Private Architect approved by Bethlehem District Education Department and CRS JWB.**

**Responsibility for sub-project Upkeep/operation** : **Husan village committee.**

**Number of Beneficiaries** : **About 3000 persons.**

#### HUSAN

- Husan is a small old village located 10 Kms West of Bethlehem with a population of 3000 inhabitants. Most of the villagers' lands were lost during the 1948 war. The villagers' depend upon agriculture, especially the cultivation of vegetables and grapes. The village has no community center, no charitable organization and no cooperative association.

- Husan villagers are very eager to improve their living standards. One important way to achieve this goal is through improving education in the village. Education for boys in Husan is currently up to the ninth grade. The Bethlehem District Education Department is running the educational establishment which not only serves the Husan students but also the students of the two neighbouring villages of Wadi Fukkin and Nahhalin. The number of boys studying at the school is 470. The school's classrooms are crowded and stuffy with students sitting there to a small bench in most of the classrooms. There is an average of fifty students in each classroom. Some of the classes are going to be divided into two sections to make it easier for students to comprehend and understand their studies. Two elementary classes are held in rented rooms in a very old private home. Teachers have to run the distance between these rented classrooms and the main school building. Another class is located in the basement. Students that study in this class suffer badly from the cold and from the water that runs into the class during the winter season.

- The proposed second floor addition will consist of five classrooms. The whole area of the construction will be 246 sq. meters. The second floor will bring together the two classes now in rented rooms, the class in the basement, and the new sections of two crowded classes. Construction costs are estimated at \$ 39,029.14. The village will own the new building while the Education Department will run the school and provide it with the necessary furniture.

- The addition of a new second floor will mean more opportunity for Husan and neighbouring villages boys to go to school, and an opportunity for a higher level of education. Proper classrooms will be available. Money paid by the village for renting the old "school classes" would be saved. Ninety five percent of the villagers in Husan will contribute toward the village's share of the costs of the sub-project.

IMPLEMENTATION: Can start as soon as AID/W and CRS/NY approval is obtained and agreement is signed by Husan village, the West Bank Military Government and the Department of Labour and Social Welfare.

50

**SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT**

**UNDER PROJECT NO. CRS JWB 4D-006**

**COVERING**

**SUB PROJECT CRS JWB - 4D-006-14**

**This Agreement is between Husan village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-**

**A. SUB PROJECT DESCRIPTION**

**Constructing the second floor of the primary school (five rooms, balcony and an external staircase) the whole totalling about 246 m2.**

**B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-**

- 1. At least 50% of the total estimated sub-project's cost of US \$ 39,029.14 equivalent to \$ 19,514.57.**
- 2. A committee to supervise daily all work on the project and keep records of labour and material used.**

**C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-**

- 1. Up to 50% of the total estimated sub-project's cost of US \$ 39,029.14 equivalent to \$ 19,514.57.**
- 2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of allonies spent and to assure interalia fair prices for material.**

**D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 120 (One hunderd & Twenty days) from the first work day of the project.**

**E. The village will be responsible for the project maintenance and upkeep.**

**F. The implementation of the project will begin with the total village share which should be available before the starting date.**

**G. The village agrees to comply with all standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.**

**H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local<sup>o</sup> otherwise, due on wages or salaries or the sale of goods, material or otherwise.**

51





RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( ) FINAL

Date of Last report: 1 April, 1986  
Date of This report: 1 October, 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-15

US. \$ 52,057.-

Sub-Project estimated cost

CRS JWB in co-operation with

MARAH RABAH VILLAGE

Name of Operating Agency

ACCESS ROAD

Title of Sub-Project

BETHLEHEM DISTRICT

Area in which Sub-Project is located

NEB-0159-G-89-5123-00

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 31,234.-

Equivalent to \$ 20,823.-

(I) CRS AID cash input

Village cash input

U.S. \$ 746,112.-

15 August, 1986

(II) Funds received to date & date of last transmittal

CRS AID US \$ 31,224.49

Village US \$ 20,873.57

(III) Sub-Project expenditure (s) to date

CRS AID US \$ 9.51

Village US \$ (50.57)

(IV) Balance (s) unused

(Overspent)

Marah Rabah villagers had great willingness to cooperate and work together. They donated parts of their lands which were in the way of the projected road.

(V) Other inputs which contributed to success of Sub-Project

54

### 3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The agreement covering this sub-project was signed with the village leadership on 9 April 1986. Implementation started on 14 April 1986 and was successfully completed in a very short period not exceeding two weeks.
- The sub-project final cost came to U.S.\$ 52,098.06. The village's cash input amounted to \$ 20,873.57 equivalent to 40%, versus CRS/AID cash input of \$ 31,224.49, which is 60% of the total cost. Attached is a detailed final statement of expenditures.
- The completed paved access road connects Marah Rabah with the main road. Villagers are now able to get their agricultural produce to Bethlehem and Hebron while fresh, to be sold locally or exported to Arab countries. Farmers have better access to their fields all year round.
- Vehicles including ambulances, taxis, and trucks are now coming easily in and out of the village. Marah Rabah is now linked with the outside world. The villagers are extremely happy. They report that the new road is giving life back to their village.
- Beneficiaries of this vital sub-project are the entire Marah Rabah villagers (1000 persons).
- The entire village contributed to the village's share of the sub-project's costs.
- Attached are photos showing the project during implementation.

#### EVALUATION:-

- The new access road definitely contributes to the Overall Goal of the Grant which is development of Rural West Bank Arab Villages.
- This sub-project has met the specific objective of facilitating access to the outside modern world.

55

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- Excellent results have been achieved. Taxis, ambulances, and ordinary passenger cars are easily reaching the village for the first time. Marketing of agricultural produce has been greatly facilitated. Sick people are transported from the village to the hospital by ambulance. These people would normally have had to walk, or be carried on donkey back, to the main road to await passing transportation to take them to the hospital.
  
- The Health Department, the Education Department, and other authorities can easily visit the village to discuss the possibilities of developing it.
  
- The opening of the road encouraged some families to return and stay in their village. Three families were encouraged by the road and started to construct houses.

GA/1b

- 56 -

ITEMIZATION OF EXPENDITURES

MARAH RABAH SUB-PROJECT

4D-006-15

			<u>N.I.S.</u>
1.	Mixed Gravel	(632.450 Tons)	6,531.42
2.	Asphalt Mixture	(1271.84 Tons)	70,052.58
			-----
	TOTAL		N.I.S. 76,584.-
			U.S.\$ 52,098.06

CRS SHARE      60% = U.S. \$ 31,224.49    N.I.S. 45,900.-

VILLAGE SHARE 40% = U.S. \$ 20,873.57    N.I.S. 30,684.-

GA/1b

51

٣٥  
أغسورة

بوتية مياينة ملقزة

٨  
صفحات

AL - FAJR DAILY  
JERUSALEM  
Wednesday 28  
May 1986  
NO - 4095



المنسى  
الاربعاء ٢٨ أيار ١٩٨٦ م  
٢٠ رمضان ١٤٠٦ هـ  
السنة الرابعة عشر  
العدد ٤٠٩٥

### شكر وتقدير

● نحن مختار وأهالي قرية مراح رباح / بيت لحم . نتقدم  
بشكرنا وتقديرنا الجزيل الى مدير جمعية الخدمات للاغاثة  
الكاثوليكية بالقدس . على ما أبداه من مساعدة لنا بتعبيد  
الشارع الذي يربط تربتنا بالشارع العام .  
جزاه الله خيرا وأكثر من أمثاله لخدمه الانسانية .  
عن القرية  
مختار القرية / خليل نعمان محمد الشيخ

### THANKS AND APPRECIATION

We the mukhtar and inhabitants of Marah Rabah village/Bethlehem, present our deep thanks and appreciation to the Director of the Catholic Relief Services in Jerusalem for the assistance offered to us in asphatling the street that links our village with the main road.

May God reward him good and increase his alike for the benefit of humanity

For the village  
The village mukhtar  
Khalil No'man Moh'd El-Shaikh

PHOTOS ILLUSTRATING THE PROJECT

CRS JWB / USAID 4D-006-15

TOTAL COST : 52,098.06

CRS SHARE : 60%

VILLAGE SHARE : 40%

MARAH RABAH VILLAGE (POP. 1000)

Asphalting an existing village access road 2.7 Kms long by 3 meters wide, (8100 sq. meters) thus linking Marah Rabah village with the main road.

PROJECT STARTED: 14 April 1986

PROJECT COMPLETED: 30 April 1986


59

1. Marah Rabah villagers were suffering from the very bad and difficult access road. Vehicles could not use it. The village was isolated from the outside world and from its fields. CRS AID agreed to help them in asphaltting the access road. Photo shows the asphaltting stage while the village committee and villagers are happily watching the work.



2. Photo shows CRS Field Supervisor (wearing a hat) inspecting work during the process of paving the road.

3. Here is a view of the very same section of the road shown above, converted into a very good paved access road. Now ambulances and public transportation can easily use it.

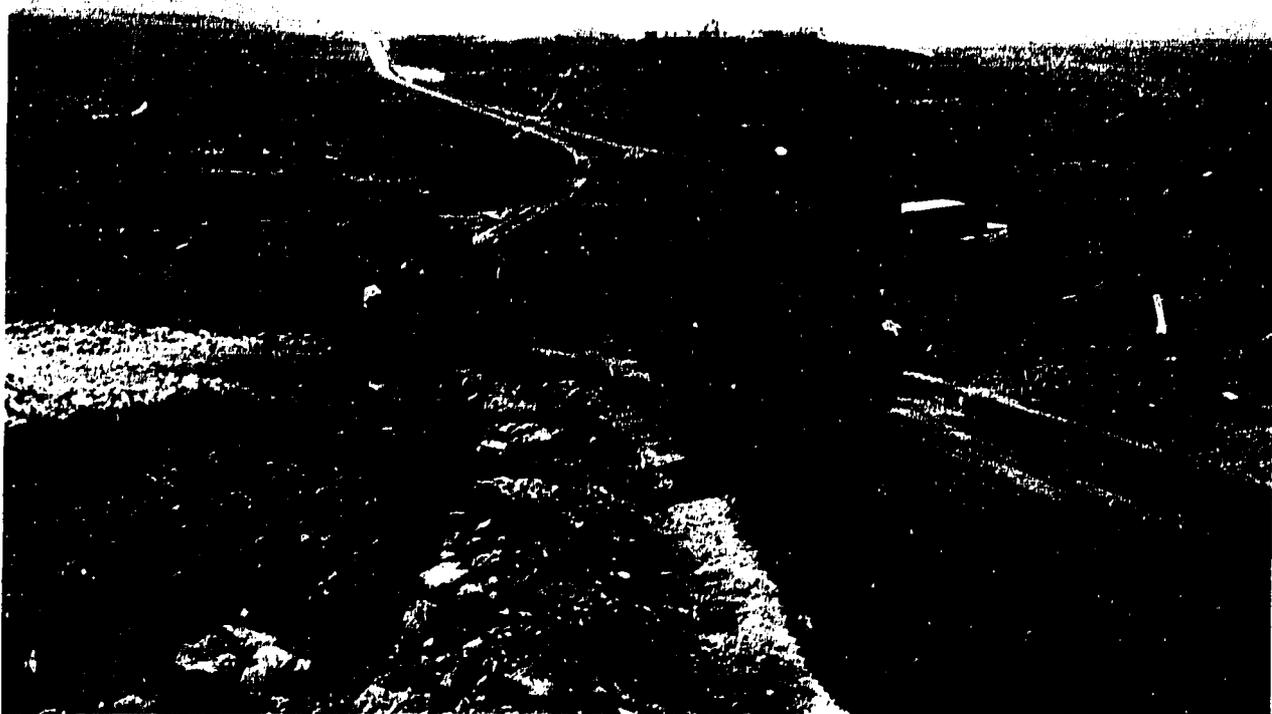

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last reports  
Date of This report: 1 OCTOBER 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-16

US. \$ 81,871.-

Sub-Project estimated cost

CRS JWB in co-operation with

BEIT 'UMHAR VILLAGE

Name of Operating Agency

AGRICULTURAL ROADS

Title of Sub-Project

HEBRON DISTRICT

Area in which Sub-Project is located

NEB-0159-G-SS-5123-00

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 40,535.50

(I) CRS AID cash input

Equivalent to \$ 40,535.50

Village cash input

US \$ 746,112.-

15 AUGUST 1986

(II) Funds received to date & date of last transmittal

CRS AID US \$ -----

(III) Sub-Project expenditure (s) to date

Village US \$ ----

CRS AID US \$ 40,535.50

(IV) Balance (s) unused

Village US \$ 40,535.50

(V) Other inputs which contributed to success of Sub-Project

62'

### 3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project involves opening, clearing, and leveling an agricultural access road about 8 kms long by 5 meters wide.
- The agreement concerning this sub-project was signed with the village leadership on 25 August 1986. Implementation is expected to start within the first two weeks of October 1986.
- This sub-project was requested from the Social Welfare Department-Beit-El-West Bank, on 10 February 1986 and the agreement was signed after more than six months from the request date.
- Implementation was delayed due to the fact that the Village Council was very busy in solving some problems related with the Academic Year. The Council is now working on the surveying plan for these agricultural roads.
- The Final Report on this sub-project will be submitted as part of our next Semi-Annual Report.

GA/1b

63'

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-16

Sub-Project Location : Beit 'Ummar village, Hebron District, West Bank.

Operating Agency : CRS JWB with Beit 'Ummar Village Council

Sub-Project Proposal : Opening, clearing and levelling an agricultural access road, about 8 kms long by 5 meters wide.

Objective : To improve Beit 'Ummar villagers connection with their agricultural land, some of which is already being cultivated and some of which, though cultivable, is unused. Transportation of produce to the village or markets will be facilitated.

Time needed to complete sub-project : Opening, widening, clearing and levelling agricultural access road will take approximately 3 months.

Supporting Local Authorities : Beit 'Ummar village council, Department of Labour and Social Welfare, and the West Bank District Authorities.

Cost Estimate : \$ 81,071.- = J.D. 28,375.-

Participants in cost : CRS JWB up to a maximum of 50% equivalent to \$ 40,535.50 = JD 14,187.50.  
Beit 'Ummar village minimum of 50% equivalent to \$ 40,535.50 = JD 14,187.50.

Responsibility for sub-Project upkeep/Maintenance : Beit 'Ummar village.

Expected Number of Beneficiaries : About 8000 persons.

- 64 -

**Brief Narrative:**

Beit 'Ummar is approximately 15 kms Northwest of Hebron, with about 8,000 inhabitants, who depend upon agriculture, for their livelihood, mainly vegetables, fruit trees, and olive cultivation. Village affairs are run by the village council. The villagers have improved their village in many ways and this is why they decided to open, clear and level an agricultural access road.

The villagers of Beit 'Ummar reach their fields either by foot or donkey. Villagers have to carry bags of seeds on their heads or on donkey backs, together with their simple agricultural tools. Agricultural machinery cannot reach their fields. They must carry out their produce on their backs and heads or by hired donkeys. In this way, the produce reaches markets in bad condition, with high costs and loss. Some farmers leave their barren fields to work as unskilled labours outside the village. The villagers badly need an agricultural road giving them access to their fields. They cannot afford all the money the needed for such an important and vital project. They approached CRS/AID for help.

This proposed sub-project will convert the donkey paths leading to the agricultural lands, into a road giving the villagers access to their vital agricultural area. The income of the farmers and the food production will increase due to this road construction. Lands will be brought under cultivation for the first time. The Agricultural Department will be able to visit village fields for agricultural extension work. Agricultural machinery would reach the fields facilitating ploughing and harvesting. Trucks, tractors and pickups would also reach the fields and be able to transport produce in good shape to reach market. 80% of the Beit 'Ummar inhabitants will contribute towards the cost of this sub-project.

**PROJECT  
IMPLEMENTATION :**

Implementation can start as soon as CRS/New York approval is given and agreement is signed by Beit 'Ummar village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

65

**SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT**

**UNDER PROJECT NO., CRS JWB 4D-006**

**COVERING**

**SUB PROJECT CRS JWB - 4D-006-16**

This Agreement is between Beit 'Ummar Village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

**A. SUB-PROJECT DESCRIPTION:-**

Opening, clearing and leveling agricultural access roads about 8 kms long by 5 meters wide.

**B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-**

1. At least 50% of the total estimated sub-project's cost of US \$ 81,071.- (JD 28,375.-) equivalent to \$ 49,535.50 (JD 14,187.50).
2. A committee to supervise daily all work on the project and keep records of labour and material used.

**C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-**

1. Up to 50% of the total estimated sub-project's cost of US \$ 81,071.- (JD 28,375.-) equivalent to US \$ 40,535.50 (JD 14,187.50). This amount is provided by AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within (90) (Ninety Days from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The villlage will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government Authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

65a


- I. The village herewith agrees to hold the Catholic Relief services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

الإدارة المدنية لمنطقة يهودا والسامرة  
 مديرة مكتب المشاريع القروية  
 فرهاد دودزه

*[Handwritten signature]*

DEPARTMENT OF LABOUR & SOCIAL WELFARE



CATHOLIC RELIEF SERVICES

عبد محمد الحمد  
*[Handwritten signature]*  
 V I L L A G E

DATE: - 25/8/1986

c 66

CATHOLIC RELIEF SERVICES - USCC

-----  
JERUSALEM WEST BANK & GAZA  
-----

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006  
-----

Sub-project Number : CRS JWB - 4D-006-20

Sub-project Location : El-Murq - El-Kom and Beit Maqdoum villages, Hebron District, West Bank.

Operating Agency : CRS JWB with El-Mureq - El-Kom and Beit Maqdoum villages

Sub-project Proposal : Providing El-Mureq El-Kom and Beit Maqdoum with a transformer, an electrical distribution board, an electrical transmission tower and an internal electrical network throughout the village.

Objective : To make electrical power available in these villages for the first time in its history

Time needed to complete sub-project : Approximately 3 months

Supporting local Authorities : El-Mureq El-Kom and Beit Maqdoum's committees, Department of Labour and Social Welfare, and the District Authorities.

Cost Estimate : \$ 119,500.- = JD 41,825.-.

Participants in cost : CRS JWB up to a maximum of 60% equivalent to \$ 71,700.- = JD 25,095.-.

El-Mureq El-Kom and Beit Maqdoum villages minimum of 40% equivalent to \$ 47,800.- = JD 16,730.-.

Sub-project Blue-Prints Prepared by : An electrical engineer in consultation with El-Mureq El-Kom and Beit Maqdoum villages and subject to the approval of CRS JWB and the West Bank Power Officer.

Responsibility for sub-project Upkeep Maintenance : El-Mureq El-Kom and Beit Maqdoum Villages will be responsible for maintaining the electrical net and the transformer.

Expected Number of Beneficiaries : 1600 people (i.e. the entire population of the three villages.)

ESTIMATED COST LIST

Sub-Project No. : 4D-006-16  
 Name of Village : Beit 'Ummar  
 Location : Hebron District  
 Project Description : Opening, clearing and leveling agricultural access roads, about 8 kms long by 5 meters wide.

			TOTAL JD'S
			-----
1. Excavator	10 Days	100 JD per day	1000
2. Bulldozer	10 Days	80 JD per day	800
3. Grader	5 Days	100 JD per day	500
4. Rolling machine	5 Days	40 JD per day	200
5. Cement	10 Tons	35 JD per ton	350
6. Sand	2 Truck loads	50 JD per load	100
7. Rough stone	5 Truck loads	25 JD per load	125
8. Cement pipes	(by work)	-----	400
9. Gravel mixed	8500 Tons	2.50 JD per ton	21250
10. Asphalt mixed	190 Tons	17 JD per ton	3230
11. Mason	10 Days	7 JD per day	70
12. Labourers	50 Days	3 JD per day	150
13. Miscellaneous	--		200
			-----
			28375

GRAND TOTAL US \$ = 81,071.- (At an exchange rate of \$1.- = JD 0.35)

CRS JWB 50% = US \$ 40,535.50 = JD 14,187.50

BEIT 'UMMAR VILLAGE 50% = US \$ 40,535.50 = JD 14,187.50

P.O. BOX 19447  
East Jerusalem

CATHOLIC RELIEF SERVICES - USCC  
JERUSALEM AND WEST BANK

PAGE OF

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last reports  
Date of This reports 1 OCTOBER 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-17

US. \$ 68,629.-

Sub-Project estimated cost

CRS JWB in co-operation with

BANI N'AIM-EL-'IDAISEH VILLAGES

Name of Operating Agency

AGRICULTURAL ROAD

Title of Sub-Project

HEBRON DISTRICT

Area in which Sub-Project is located

NEB-0159-G-85-5123-00

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 36,377.-

(I) CRS AID cash input

Equivalent to \$ 24,252.-

Village cash input

US \$ 746,112.-

(II) Funds received to date & date of last transmittal

15 AUGUST 1986

CRS AID US \$ 9,912.33

(III) Sub-Project expenditure (s) to date

Village US \$ 24,186.07

CRS AID US \$ 26,464.67

(IV) Balance (s) unused

Village US \$ 65.93

(V) Other inputs which contributed to success of Sub-Project

69

### 3 PROGRESS OF (SUB)PROJECT SECTION CRS-JWB USAID

- This sub-project calls for opening, clearing, leveling, and constructing supporting walls and parts of the road foundations of an agricultural access road about 5 kms long by 5.5 meters wide linking El-'Idaiseh with Bani N'aim.
- The agreement covering this sub-project was signed with the village leadership on 18 June 1986. Work began on 7 July 1986.
- This very successful sub-project is expected to be completed before the end of October 1986. The agricultural road was completely opened, widened, and leveled. Supporting walls were constructed on both sides. The necessary mixed gravel was ordered for the road foundation.
- The village committee cooperated very well with CRS. Some problems arose while widening the road. Finally, the land owners were persuaded to donate parts of their lands for the project.
- The Final Report on this sub-project will be submitted as part of our next Semi-Annual Report.

GA/1b

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-17

Sub-project Location : Bani N'aim - El-'Idaiseh villages, Hebron District West Bank.

Operating Agency : CRS JWB together with Yatmah village.

Sub-project Proposal : Constructing additional classrooms for the girls' primary school, (Four rooms, veranda, W.C. units and staircase) the whole totalling about 225 m2.

Objective : To improve primary level education facilities (for girls) in a rural area of Nablus District..

Expected Results : Primary level education for girls in rural Yatmah village will become more suitable. The four new rooms will replace current inadequate and inappropriate quarters.

Time needed to complete sub-project : Construction of the building will take about 3 months. The additional classrooms will be put to use immediately after completion of construction. The education Department will furnish the additional classrooms and provide the necessary teaching staff and text-books.

Supporting local Authorities : Yatmah village committee, Department of Labour and Social Welfare, Department of Education, and West Bank Military Government.

Cost Estimate : \$ 36,000.- = JD 12,600.- at exchange rate of J.D. 0.35 = \$ 1.-.

Participants in cost : CRS JWB up to a maximum of 60% equivalent to \$ 21,600.- = JD 7,560.-.  
Yatmah village minimum of 40% equivalent to \$ 14,400.- = JD 5,040.-.

Construction Plan Prepared by : Private Architect approved by Nablus District Education Department and CRS JWB

Responsibility for sub-project Upkeep Maintenance : Yatmah Village Committee.

Expected Number of Beneficiaries : 3000 people (i.e. the entire population of the village.)

Brief Narrative : Bani N'aim and El 'Idaiseh are neighbouring village located 9 kms from Hebron. The total population of the two villages is 20,000 people (Bani Na'im 15,000, El 'Idaiseh 5,000). Six thousand villagers will benefit directly from this proposed sub-project. The village inhabitants depend upon agriculture for their daily livelihood. El'Idaiseh is without electricity, a drinking water system, postal services, telephones, an out-patient health clinic, paved access roads public transportation and cooperative associations, while Bani N'aim is in far better shape. The affairs of El 'Idaiseh are run by village leaders and Mukhtars (headmen) while affairs of Bani N'aim are run by an elected village council.

Bani N'aim and El'Idaiseh villagers find great difficulty in reaching certain parts of their fields because of the narrow rocky twisting paths. In winter, especially when it rains heavily, Bani N'aim and El 'Idaiseh fields become isolated due to the muddy and sloppy donkey paths. These paths are full of holes and ditches. They become totally muddy as a result of the winter rains. In other times of the year, it takes more than one hour to reach certain parts of the fields. Farm machinery and vehicles cannot get out to the fields and groves thus holding back, even discouraging, agricultural production. The agricultural produce is carried either on the villagers backs and heads or on animals. The produce reaches the villages in very bad condition.

The agricultural access road is badly needed. This road will link Bani N'aim with El 'Idaiseh and will lead to the quarry. So, it will then become possible for the villagers to make and sell stones to other villages. The construction of this road will increase the income of the villages and improve their living standards. Existing land and groves will be more intensively worked, and some new fields will be opened to cultivation for the first time. New groves will be planted. All the villagers concerned will contribute the villages' share of the cost.

PROJECT  
IMPLEMENTATION :

Implementation can start as soon as CRS/New York approval is given and agreement is signed by Beit 'Ummar village, the Ministry of Labour and Social Affairs and the West Bank District Authorities

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-17

This Agreement is between Bani N'aim village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB PROJECT DESCRIPTION

Opening, clearing, leveling and constructing supporting walls and parts of the road foundations of and Agricultural access road about 5 kms long by 5.5 meters wide linking El-I'daiseh with Bani N'aim.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 40% of the total estimated sub-project's cost of US \$ 60,629.- equivalent to \$ 24,252.- (JD 8,488.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 60% of the total estimated sub-project's cost of US \$ 60,629.- equivalent to \$ 36,377.- (JD 12,732.-)  
This amount is provided by AID
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 90 (Ninty days only) from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

73

- I. The village herewith agrees to hold the Catholic Relief Services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

**SIGNATORIES**


המנהל האזורי לאזור יהודה ושומרון  
 וועד הפועלים  
 משרד העבודה  
 וזרע  
 יחידת המעורבות  
 מכתב המשרד

DEPARTMENT OF LABOUR & SOCIAL WELFARE

DISTRICT AUTHORITIES



CATHOLIC RELIEF SERVICES



V I L L A G E

ע"מ דרדסה עמא  
 אבא נחמא  
 ברנד פטר

DATE: 18/6/1986

Handwritten signature

Handwritten signature

Handwritten signature

ESTIMATED COST LIST

Name of village : Bani N'aim - El 'Idaiseh

Location : Hebron District

Sub-Project No. : 4D-006-17

Project Description: Opening, clearing leveling and constructing supporting walls and parts of the road foundations of and Agricultural access road about 5 kms long by 5.5 meters wide linking El-'Idaiseh with Bani N'aim.

				TOTAL JD'S
				-----
1.	Bulldozer	15 Days	80 JD per day	1200
2.	Rolling Machine	6 Days	70 JD per day	420
3.	Grader	4 Days	100 JD per day	400
4.	Mixed Gravel	7500 tons	2.5 JD per load	18750
5.	Water	30 Tanks	15 JD per tank	5400
				-----
				JD 21,220
				=====

GRAND TOTAL US \$ = 60,629 = JD 21,220 (At an exchange rate of \$1.- = JD 0.35)

CRS JWB 60% US \$ = 36,377.- = JD 12,732.-

VILLAGE SHARE 40% US \$ = 24,252.- = JD 8,488.-

15

P.O. BOX 19447  
East Jerusalem

CATHOLIC RELIEF SERVICES - UBCC  
JERUSALEM AND WEST BANK

PAGE 1 OF 3

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last reports:  
Date of This reports: 1 October 1986

1. REFERENCE SECTION

CRS-JWB/USAID US. \$ 98,666.-  
Sub-Project No. 4D-886-19 Sub-Project estimated cost

CRS JWB in co-operation with RAQ'A VILLAGE  
Name of Operating Agency

ELECTRICITY  
Title of Sub-Project

HEBRON DISTRICT  
Area in which Sub-Project is located

NEB-8159-0-88-5123-88  
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 59,200.- Equivalent to \$ 39,466.-  
(I) CRS AID cash input Village cash input

US. \$ 746,112.- 15 August 1986  
(II) Funds received to date & date of last transmittal

CRS AID US \$ 44,833.83 Village US \$ 45,168.78  
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 15,166.17 Village US \$ (5,694.78)  
(IV) Balance (s) unused (Overspent)

(V) Other inputs which contributed to success of Sub-Project

76

### 3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for providing Raqa' village with a main internal electrical network including an electrical distribution board and an electrical transmission tower.
  
- This sub-project was requested from the Social Welfare Department-Beit-El-West Bank on 10 February 1986, while the agreement was signed on 18 June 1986, after more than four months from the request date.
  
- Tenders were held and a sub-contractor was chosen to provide the electrical materials. Another sub-contractor for installing the electrical net was selected. The tender notice and its translation are attached.
  
- 80% of the materials are on the spot and 50% of the electrical poles were installed.
  
- The village committee faced great difficulties while collecting the village's share from the inhabitants. The committee is functioning very well and cooperates completely with CRS.

GA/1b

11

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-19

Sub-project Location : Raqa' village, Hebron District, West Bank

Operating Agency : CRS JWB with Raqa' village.

Sub-project Proposal : Providing Raqa' with a transformer, an electrical distribution board, an electrical transmission tower and an internal electrical network throughout the village.

Objective : To make electrical power available in this village for the first time in its history

Time needed to complete sub-project : Approximately 3 months

Supporting local Authorities : Raqa' village committee , Department of Labour and Social Welfare, and the District Authorities.

Cost Estimate : \$ 98,666.- = JD 34,533.--

Participants in cost : CRS JWB up to a maximum of 60% equivalent to \$ 59,200.- = JD 20,720.--

: Raqa' Village a minimum of 40% equivalent to \$ 39,466.- = JD 13,813.--

Sub-project Blue-Prints Prepared by : An electrical engineer in consultation with Raqa' village and subject to the approval of CRS JWB and the West Bank Power Officer.

Responsibility for sub-project Upkeep Maintenance : The village will be responsible for maintaining the electrical net and the transformer.

Expected Number of Beneficiaries : 4000 people i.e. the entire population of the village.

77a

**BRIEF NARRATIVE :**

Raqa' is a very poor village located 10 kms west of Hebron. The 4000 inhabitants depend upon cereal farming, which is a very bad crop this year. They raise sheep and goats. They provide unskilled hand labour to Hebron.

Raqa' villagers are very eager to develop their poor village. They find development impossible without electricity. They have decided to provide their village with an internal electrical network. As they cannot do this project by themselves, they approached CRS/AID and requested help.

The village is still without paved interior roads, out-patient health clinic, postal services, a community center, public transportation, or a potable water delivery system. Raqa' only has two small primary schools; one for boys and the other for girls. The girls school was built in 1982 with the help of CRS/AID, which participated in 65% of the total cost. Five villages including Raqa' contributed to the remaining 35% of the sub-project total cost.

Now Raqa' village alone will contribute in 40% of the total cost of the suggested sub-project. This is a clear proof that villagers are giving tremendous efforts, despite their limited resources, to help and develop themselves.

Once the proposed sub-project is implemented, electric machines could replace manual ones. This will increase productivity and raise the standard of living in the village. In addition to that, school children will be able to study in well-lighted rooms, rather than on the dim light of kerosene lanterns. Household electrical appliances mainly refrigerators for long term food storage, may then be used in some houses. All the villagers will contribute in the village share.

**PROJECT**

**IMPLEMENTATION :**

Implementation can start as soon as CRS/New York approval is given and agreement is signed by Raqa' village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

13

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-19

This Agreement is between Raqa' village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB PROJECT DESCRIPTION

Providing Raqa' with transformer, an electrical distribution board, an electrical transmission tower, and a main internal electrical network throughout the village.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 40% of the total estimated sub-project's cost of US \$ 98,666.- equivalent to \$ 39,466.- (JD 13,813.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 60% of the total estimated sub-project's cost of US \$ 98,666.- equivalent to \$ 59,200.- (JD 20,720.-)  
This amount is provided by AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 90 (Ninty days only) from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

- I. The village herewith agrees to hold the Catholic Relief Services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

**SIGNATORIES**

-----

*[Handwritten signature]*


DEPARTMENT OF LABOUR & SOCIAL WELFARE

*[Handwritten signature]*

DISTRICT AUTHORITIES



CATHOLIC RELIEF SERVICES



V I L L A G E

DATE: 18/6/1986

*[Handwritten signature]*

*[Handwritten signature]*

*[Handwritten signature]*

ESTIMATED COST LIST

Name of village : Raqa' village

Location : Hebron District

Sub-project No. : 4D-006-19

Project Description: Providing Raqa' with a transformer, an electrical distribution board, an electrical transmission tower, and a main internal electrical network throughout the village.

MATERIAL	QUANTITY	PRICE JD	TOTAL JD
1. Iron Tower	1	500	500
2. Wooden Poles (7m)	80	45	3600
3. Wooden Poles (8.5m)	70	33	2310
4. Distribution Cables	--	---	500
5. Aluminum Rods (95 ml)	3000 KG	1.10	3300
6. Aluminum Rods (50 ml)	3200 KG	1.10	3520
7. Aluminum Rods (25 ml)	750 KG	1.10	825
8. Cup-shaped Rods with screws	1200	.60	720
9. Accessories including conductors, screws, etc.	--	---	5033
10. Lamps (125 watt)	120	15	1800
11. Distribution Board	1	2500	2500
12. Tranformer	1	7500	7500
13. Electrical Transmission Tower	1	2425	2425
		JD	34533

GRAND TOTA US \$ = 98,666.- (At an exchange rate of \$ 1.- = JD 0.35)

CRS SHARE 60% = \$ 59,200.- = JD 20,720.-

VILLAGE SHARE 40% = \$ 39,466.- = JD 13,813.-

# القدس

صفحة ١٤  
عورة

"AL-QUDS" Jerusalem Thursday 14 August 1986 No. 6094

**إعلان مناقصة**

بطا / أرقعةم لتفك اللجنة كهرباء رقةم بالتمان مع كذا لا  
الكاثوليكية عن طرح مناقصة بالطرف المختوم للقيام بأعمال شبكة  
منقط منقطع لقرية رقةم . على الراغبين الدخول بل بكون الكاد  
مراجعة رئيس اللجنة بل القرية بجانب مسجد الصادق الأمين للحد  
على نسخ المخطط (٢٠٨) ديكران من فير منقولة  
يوم الأربعاء ١٢ / ٨ الساعة ١٠ / ١٠  
ملاحظة اللجنة غير مقيدة بأقل الامتياز بل  
أجور الاعلان على من يرغب عليه العطاء

## Tender Notice

Yatta-Raq'a-Raq'a's electrical committee in cooperation with CRS invite bids in sealed envelopes for carrying out a low voltage power grid for the village. Those who are interested to participate in this tender can obtain bid forms from the head of the village committee near Al-Sadiq Al-Amin Mosque in exchange for 20 JD unrefundable. Deadline for submitting bids is 1 p.m., Wed. 20 Aug. 1986.

N.B. The committee does not undertake to accept the lowest price. The awardee is to pay the cost of this advertisement.

82

P.O. BOX 19447  
East Jerusalem

CATHOLIC RELIEF SERVICES - USCC  
JERUSALEM AND WEST BANK

PAGE OF

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last reports:

Date of This report: 1 October 1986

1. REFERENCE SECTION

CRS-JWB/USAID

Sub-Project No. 4D-006-20

US \$ 119,500.-

Sub-Project estimated cost

CRS JWB in co-operation with

EL-MUREQ EL-KOM VILLAGES

Name of Operating Agency

ELECTRICITY

Title of Sub-Project

HEBRON DISTRICT

Area in which Sub-Project is located

NEB-0159-G-SB-5123-00

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 71,700.-

(I) CRS AID cash input

Equivalent to \$ 47,800.-

Village cash input

\$ 746,112.-

15 August, 1986

(II) Funds received to date & date of last transmittal

CRS AID US \$ 35,810.82

(III) Sub-Project expenditure (s) to Gate

Village US \$ 38,647.15

CRS AID US \$ 35,889.18

(IV) Balance (s) unused

Village US \$ 9,152.85

(V) Other inputs which contributed to success of Sub-Project

43

### 3 PROGRESS OF (SUB)PROJECT SECTION CRS-JWB USAID

- This sub-project calls for providing El-Mureq, El-Kom and Beit Magdoun with a transformer, an electrical distribution board, an electrical transmission tower, and an internal electrical network throughout the village.
- This sub-project was requested from the Social Welfare Department-Beit-El-West Bank, on 10 February 1986 while the agreement was signed on 18.6.1986, four months from the request date.
- Due to the drought and the very difficult economic situation prevailing in the West Bank, the village committee met great difficulties while trying to collect the village's share from the inhabitants.
- Tenders were held and a sub-contractor was chosen to provide the electrical materials. Another sub-contractor for installing the electrical net was selected. The foundations of the room in which the distribution board is going to be placed are completed.
- 50% of the electrical poles were installed and most of the materials are on the spot.
- The Final Report on this sub-project will be part of our next Semi-Annual Report.

GA/1b

84

**BRIEF NARRATIVE:**

*El-Mureq, El-Kom and Beit Maqdoum are poor villages located about 33 kms southwest of Hebron. Their population is 1600 people. The inhabitants grow wheat, barley, lentils, which are bad crops this year due to the drought, vegetables, olive, grapes and water-melons. The villages have no telephone, health clinics, running water, postal services, or community center. Part of their lands were lost in the 1948 war.*

*The villages are still without electricity. The villagers live, work and study without one of the most important needs of life - electricity.*

*El-Mureq, El-Kom and Beit Maqdoum approached CRS/AID for help in installing an internal electrical network. Despite their difficult situation, the villagers were able to collect some money as part of their share in this suggested sub-project. They have elected a committee to collect the rest of money and to supervise work, and to run the electrical system after installation. The availability of electricity will open new opportunities for the villagers; to start small workshops such as carpentry and metal work. Their living standards will be improved.*

**PROJECT**

**IMPLEMENTATION:**

*Implementation can start as soon as CRS/New York approval is given and agreement is signed by El-Mureq, El-Kom and Beit Maqdoum villages, the Ministry of Labour and Social Affairs and the West Bank District Authorities.*

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-20

This Agreement is between El-Mureq, El-Kom and Beit Maqdom village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

- A. SUB PROJECT DESCRIPTION  
Providing El-Mureq, El-Kom and Beit Maqdom with a transformer, an electrical transmission tower, and a main internal electrical network throughout the village.
- B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-
1. At least 40% of the total estimated sub-project's cost of US \$ 119,500.- equivalent to \$ 47,800.- (JD 16,730.-)
  2. A committee to supervise daily all work on the project and keep records of labour and material used.
- C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-
1. Up to 60% of the total estimated sub-project's cost of US \$ 119,500.- equivalent to \$ 71,700.- (JD 25,095.-)  
This amount is provided by AID.
  2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.
- D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 90 (Ninty days only) from the first work day of the project.
- E. The village will be responsible for the project maintenance and upkeep.
- F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.
- G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.
- H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

- I. The village herewith agrees to hold the Catholic Relief Services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

הממונה על המשרד לרווחה ולעבודה

*[Handwritten signature]*


DEPARTMENT OF LABOUR & SOCIAL WELFARE



DISTRICT AUTHORITIES



CATHOLIC RELIEF SERVICES



V I L L A G E

قرية بيارنة كمالعوب

محمد طاهر العواد

عبد السلام الرقيب

DATE: 18/6/1986

ESTIMATED COST LIST

Name of village : El-Mureq El-Kom and Beit Maqdoum

Location : Hebron District

Sub-project No. : 4D-006-20

Project Description: Providing El-Mureq El-Kom and Beit Maqdoum with a transformer, an electrical distribution board, an electrical transmission tower, and a main internal electrical network throughout the village.

MATERIAL -----	QUANTITY -----	PRICE JD -----	TOTAL JD -----
1. Electrical Transmission tower	1	1500	1500
2. Distribution Board	1	12000	12000
3. Central earth			500
4. Wooden Poles (10m)	80	50	4000
5. Wooden Poles (8.5 m)	100	35	3500
6. Aluminum Rods (95 ml2)	3000 kg	1.10	3300
7. Aluminum Rods (50ml2)	2200 kg	1.10	2200
8. Aluminum Rods (25 ml2)	1000 kg	1.10	1100
9. Cup-shaped Rods	1200	1	1200
10. Wooden screws (16-22 cm)	800	.80	640
11. Accessories including screwsm conductors, etc.			2685
12. Lamps	120	20	2400
13. Full Earth sets	30	20	600
14. Electrician			5400
GRAND TOTAL US \$ = 119,500 (At an exchange rate of \$1.- = JD 0.35)		JD	41825 =====

CRS SHARE            60% = \$ 71,700 = JD 25,095.-

VILLAGE SHARE        40% = \$ 47,800 = JD 16,730.-

22

P.O. BOX 19447  
East Jerusalem

CATHOLIC RELIEF SERVICES - UBCC  
JERUSALEM AND WEST BANK

PAGE OF

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last reports:  
Date of This report: 1 October 1986

1. REFERENCE SECTION

CRS-JWB/USAID US \$ 34,283  
Sub-Project No. 4D-006-21 Sub-Project estimated cost

CRS JWB in co-operation with ZBAIDAT VILLAGE  
Name of Operating Agency

ELECTRICITY  
Title of Sub-Project

JERICHO DISTRICT  
Area in which Sub-Project is located

NEB-0159-0-68-5123-00  
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 22,284.- Equivalent to \$ 11,999.-  
(I) CRS AID cash input Village cash input

US \$ 746,112.- 15 AUGUST 1986  
(II) Funds received to date & date of last transmittal

CRS AID US \$ ----- Village US \$ -----  
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 22,284.- Village US \$ 11,999.-  
(IV) Balance (s) unused

(V) Other inputs which contributed to success of Sub-Project

51

### 3 PROGRESS OF (SUB)PROJECT SECTION CRS-JWB USAID

- This sub-project calls for providing Zbaidat village with a transformer, an electrical distribution board, an electrical transmission tower, and an internal electrical network throughout the village.
  
- The agreement covering this sub-project was signed with the village leadership on 23 June 1986.
  
- A tender was held and a sub-contractor for the material was chosen. All the materials will be on the spot during October 1986.
  
- The drought and the very difficult economic situation prevailing in the West Bank, formed a very heavy task on the village committee while trying to provide the village's share of the sub-project's costs.

GA/1b

90

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-21

Sub-project Location : Zbaidat village, Jericho District, West Bank.

Operating Agency : CRS JWB with Zbaidat village.

Sub-project Proposal : Providing Zbaidat with a transformer, an electrical distribution board, an electrical transmission tower and an internal electrical network throughout the village.

Objective : To make electrical power available in this village for the first time in its history

Time needed to complete sub-project : Approximately 3 months

Supporting local Authorities : Zbaidat committee, Department of Labour and Social Welfare, and the District Authorities.

Cost Estimate : \$ 34,283.- = JD 11,999.-.

Participants in cost : CRS JWB up to a maximum of 65% equivalent to \$ 22,284.- = JD 7,799.-.

Zbaidat village minimum of 35% equivalent to \$ 11,999.- = JD 4,200.-.

Sub-Project Blue-Prints Prepared by : An electrical engineer in consultation with Zbaidat village and subject to the approval of CRS JWB and the West Bank Power Officer.

Responsibility for sub-project Upkeep Maintenance : Zbaidat Village will be responsible for maintaining the electrical net and the transformer.

Expected Number of Beneficiaries : 1200 people (i.e. the entire population of the village.)

**BRIEF NARRATIVE :**        *Zbaidat is a very poor village situated forty kms north of Jericho. Its 1200 inhabitants, originally beduins, emigrated there from Beir El-Sabe' during the 1948 war. Villagers depend on vegetable raising mainly tomatoes and eggplants, and on live-stock raising with about 120 sheep and cows.*

*The fifty-two dunums of land in the village used to belong to the Jordanian Government. After the 1967 war, the Israeli Authorities confiscated these lands. Villagers are now using the lands by special permission.*

*The village has no school, clinic, agricultural road, paved interior roads, charitable society, public transportation or community center. It also lacks electricity and a drinking water system.*

*Zbaidat has a very old diesel pump used for irrigation. The pump so often becomes out of order, as a result of which great amounts of vegetables are usually damaged and lost.*

*The villagers hope that after the installment of electricity their major problem will be solved. Instead of the old pump, electricity will then be used for irrigation. Productivity will increase and the living standards will improve. the villagers are very anxious to develop their poor village. They have all expressed willingness to participate to the village share of the total cost.*

**PROJECT  
IMPLEMENTATION :**

*Implementation can start as soon as CRS/New York approval is given and agreement is signed by Zbaidat village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.*

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-21


This Agreement is between Zbaidat village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

- A. SUB PROJECT DESCRIPTION  
Providing Zbaidat with a transformer, an electrical transmission tower, and a main internal electrical network throughout the village. If, after the completion of project implementation, the village is not connected with the main line of the West Bank electricity, the villagers will then have to provide their own generator.
- B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-
1. At least 35% of the total estimated sub-project's cost of US \$ 34,283.- equivalent to \$ 11,999.- (JD 4,200.-)
  2. A committee to supervise daily all work on the project and keep records of labour and material used.
- C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-
1. Up to 55% of the total estimated sub-project's cost of US \$ 34,283.- equivalent to \$ 22,284.- (JD 7,799.-)
  2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.
- D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 60 (Sixty days only) from the first work day of the project.
- E. The village will be responsible for the project maintenance and upkeep.
- F. The implementation of the project will begin with the total village share which should be available before the starting date.
- G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.
- H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.
- 97

- I. The village herewith agrees to hold the Catholic Relief Services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

המנהל האזורי לאזור יהודה ושומרון  
 الادارة المدنية لقطاع يهودا والسامرة  
 משרד העבודה והרווחה  
 وزارة الرفاه الاجتماعي  
 מוקד מפעלי פיתוח  
 مكتب المشاريع القروية



DEPARTMENT OF LABOUR & SOCIAL WELFARE

DISTRICT AUTHORITIES



Handwritten signature in Arabic script.

زبدات	زبدات
مختار	مختار
١٠٤٨	١٩٤٨
عدد محمد علي زبدات	

CATHOLIC RELIEF SERVICES

V I L L A G E

DATE: 23/6/1986

ESTIMATED COST LIST

Name of village : Zbaidat village

Location : Jericho District

Sub-project No. : 4D-006-21

Project Description: Providing Zbaidat with a transformer, an electrical distribution board, an electrical transmission tower, and a main internal electrical network throughout the village.

MATERIAL	QUANTITY	PRICE JD	TOTAL JD
-----	-----	-----	-----
1. Wooden Poles (10 m)	20	45	900
2. Aluminum Rods	1260	1.15	1449
3. Electrical Transmission Tower	2	500	1000
4. Distribution Board	1	4700	4700
5. Electrician			900
6. Installing the network			750
7. Labourers			750
8. Accessories including U-shaped, iron, screws, conductors, etc.			1550
			-----
		JD	11999
			=====

GRAND TOTAL US \$ = 34,283 (At an exchange rate of \$ 1.- = JD 0.35)

CRS SHARE 65% = \$ 22,284.- = JD 7,799.-

VILLAGE SHARE 35% = \$ 11,999.- = JD 4,200

95

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last report:  
Date of This report: 1 October, 1986

1. REFERENCE SECTION

CRS-JWB/USAID US. \$ 36,000.-  
Sub-Project No. 4D-006-22 Sub-Project estimated cost

CRS JWB in co-operation with YATMAH VILLAGE  
Name of Operating Agency

PRIMARY SCHOOL  
Title of Sub-Project

NABLUS DISTRICT  
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00  
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 21,600.- Equivalent to \$ 14,400.-  
(I) CRS AID cash input Village cash input

US \$ 746,112.- 15 AUGUST 1986  
(II) Funds received to date & date of last transmittal

CRS AID US \$ 20,970.38 Village US \$ 15,496.89  
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 629.62 Village US \$ (1,896.89)  
(IV) Balance (s) unused (Overspent)

Other inputs which contributed to success of Sub-Project  
(V)

96

### 3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for the construction of additional classrooms for the girls' primary school-four rooms, veranda, W.C. units, and staircase - the whole totalling about 225 m2.
  
- The approval for this sub-project came from the Social Welfare Department - Beit-El-West bank, four months from the date the sub-project was presented. Approval was requested on 10 February 1986, while the agreement was signed with the village leadership on 11 June 1986.
  
- It is a very successful sub-project. Although work started only on 14 June 1986, 95% of the sub-project is completed.
  
- All the work concerning foundations, walls, roofing, plastering, tiling, white washing, and bathrooms was completed. Pointing is the only thing left.
  
- The village committee faced some difficulties while collecting the village's share due to the bad economic situation in the West Bank.
  
- This sub-project is expected to be completed by the end of October 1986, and the Final Report on this sub-project will be submitted as part of our next Semi-Annual Report.

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package

Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-22

Sub-project Location : Yatmah village, Nablus District, West Bank.

Operating Agency : CRS JWB together with Yatmah village.

Sub-project Proposal : Constructing additional classrooms for the girls' primary school, (Four rooms, veranda, W.C. units and staircase) the whole totalling about 225 m2.

Objective : To improve primary level education facilities (for girls) in a rural area of Nablus District..

Expected Results : Primary level education for girls in rural Yatmah village will become more suitable. The four new rooms will replace current inadequate and inappropriate quarters.

Time needed to complete sub-project : Construction of the building will take about 3 months. The additional classrooms will be put to use immediately after completion of construction. The education Department will furnish the additional classrooms and provide the necessary teaching staff and text-books.

Supporting local Authorities : Yatmah village committee, Department of Labour and Social Welfare, Department of Education, and West Bank Military Government.

Cost Estimate : \$ 36,000.- = JD 12,600.- at exchange rate of J.D. 0.35 = \$ 1.-.

Participants in cost : CRS JWB up to a maximum of 60% equivalent to \$ 21,600.- = JD 7,560.-.  
Yatmah village minimum of 40% equivalent to \$ 14,400.- = JD 5,040.-.

Construction Plan Prepared by : Private Architect approved by Nablus District Education Department and CRS JWB

Responsibility for sub-project Upkeep Maintenance : Yatmah Village Committee.

Expected Number of Beneficiaries : 3000 people (i.e. the entire population of the village.)

Breif Narrative : Yatmah is a village located 17 kms south of Nablus with a population of 3000 people. The villagers depend upon agriculture for a livelihood. They also provide unskilled hand labour to Nablus. They grow olives, wheat, barley, and lentils. Yatmah is without a water delivery system, an out-patient health clinic, a community center, telephones, postal services, public transportation an agricultural cooperative and a charitable society. Village affairs are run by mukhtars (headmen), elders and notables.

The village had two primary schools one for boys and the other for girls. The girls' school is jammed and cannot accept new students. Students of two different grades study in the same room. The third and fourth grades are located in one room. The fifth and sixth grades are located in another room. This situation leaves some girls at home without education. The villagers appealed for help from the Nablus District Education Department, which suggested to them to construct four additional classrooms and promised to provide the necessary teaching staff, textbooks, and furniture. The villagers cannot afford this expense to complete this sub-project. They approached CRS-AID and asked for help.

The land surrounding the school is too small. The proposed new school building will be separated from the old one by staircase making it possible for the villagers to build a second floor in the future. Yatmah would own the new building.

The additional classrooms will mean more students, more teachers, and a better standard of education. A first preparatory class will be added, and each grade will study in a separate room. The villagers are ready to contribute toward the village's share of the costs of this sub-project.

**PROJECT  
IMPLEMENTATION:**

Implementation can start as soon as CRS / New York approval is given and agreement is signed by Yatmah village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-22

This Agreement is between Yatmah village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB PROJECT DESCRIPTION

Constructing additional classrooms for the girls' primary school. (Four rooms, veranda. W.C. units and staircase) the whole totalling about 225 m2.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 40% of the total estimated sub-project's cost of US \$ 36,000.- equivalent to \$ 14,400.- (JD 5,040.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 60% of the total estimated sub-project's cost of US \$ 36,000.- equivalent to \$ 21,600.- (JD 7,560.-)
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of allonies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 90 (Ninty days only) from the first work day of the project.

E. The village will be responsible for the project maintenance and unkeep.

F. The implementation of the project will begin with the total village share which should be available before the starting date.

G. The village agrees to comply with all standard Provisions requirement of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

- I. The village herewith agrees to hold the Catholic Relief Services harmless from any and all liability, claims, suits all law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.


SIGNATORIES

*[Handwritten signature]*

DEPARTMENT OF LABOUR & SOCIAL WELFARE



CATHOLIC RELIEF SERVICES



V I L L A G E

*[Handwritten signature]*

DATE: 11/6/1986

**ESTIMATED COST LIST**

Sub-project No. (22)

CRS—JWB (


NAME OF VILLAGE : Yatmah LOCATION : Nablus District

PROJECT DESCRIPTION : Constructing additional classrooms for the girls' primary school

(Four rooms, veranda, W.C. Units and staircase) the whole totalling about 225 m2.

MATERIAL	Quantity	Price JD	Total JD	WAGES	Quantity	Price JD	Total JD
Black Cement	60 tons	32	1,920.-	Mason	225 m2	8	1,800.-
White Cement	10 bags	5.5	55.-	Plasterer	1685 m2	.60	1,011.-
Steel	5.7 tons	225	1,282.5	Tiling	275 m2	.80	220.-
Doors	14.20 m2	24	340.80	Pointing	31 m2	0.85	26.3
Windows	34.7 m2	16	555.20	Painting	128 m2	0.60	76.8
Window Fence	47.6 m2	6	285.60	White Washing	675 m2	0.40	270.-
Building Stone	110 m	1.60	176.-	Miscellaneous	-	-	36.4
Cement Blocks	7860	.18	1,414.80	Labourers	35 days	4	140.-
Rough Stone	-	-	-	Skilled Labour	7 days	5	35.-
Gravel, Mixed	170 m3	3.40	578.-	Bulldozer	2 days	80	160.-
Fine	50 m3	4.50	225.-				
Powder	60 m3	5.40	324.-	Compressor	3 days	25	75
Sand	85 m3	2.70	229.50	Rolling machine			
Tiles	220 m2	1.80	396.-	Total of Wages			3,850.6
Glass	35.50 m2	4.50	159.75	Total of Material Cost			8,749.4
Water	15 tanks	6	90.-	Grand Total JD			12,600.-
Window Sill	34.5 m2	8	276.-	Grand Total US \$			36,000.-
Asphalt	-	-	-	CRS—JWB—EX— 60%			
Asphalt Mixed	-	-	-	US \$ 21,600.- = JD 7,560.-			
Solar	-	-	-	VILLAGE SHARE 40%			
Wood	-	-	-	US \$ 14,400.- = JD 5,040.-			
Pipes	35 m	1.15	40.25				
4 W.C. seats	-	-	-				
Lavatories etc.	-	-	276.-				
Fitting parts	-	-	125.-				
<b>Total of Material Cost</b>			<b>8,749.40</b>				

SIGNATURE :



Name :

Signature :

Village Responsible Representative

102

P.O. BOX 19447  
East Jerusalem

CATHOLIC RELIEF SERVICES - USCC  
JERUSALEM AND WEST BANK

PAGE OF

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last report:  
Date of This report: 1 OCTOBER 1986

1. REFERENCE SECTION

CRS-JWB/USAID Sub-Project No. 4D-006-23 US. \$ 81,250.-  
Sub-Project estimated cost

CRS JWB in co-operation with SHWAIKEH VILLAGE  
Name of Operating Agency

COMMUNITY CENTER  
Title of Sub-Project

TULKAREM DISTRICT  
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00  
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 40,625.- Equivalent to \$ 40,625.-  
(I) CRS AID cash input Village cash input

US \$ 746,112.- 15 AUGUST, 1986  
(II) Funds received to date & date of last transmittal

CRS AID US \$ ----- Village US \$ -----  
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 40,625.- Village US \$ 40,625.-  
(IV) Balance (s) unused

(V) Other inputs which contributed to success of Sub-Project

103

### 3      PROGRESS OF (SUB)PROJECT SECTION CRS-JWB USAID

- This sub-project calls for the construction of a community center consisting of ten rooms, corridor, entrance, staircase, W.C. units, and a kitchen the whole totalling about 345 m2, to house the village and the charitable society activities such as the typing and weaving courses, the out-patient clinic, the kindergartens, the health education, and the sports activities.
  
- The agreement covering this sub-project was signed with the village leadership on 21 August 1986, although this sub-project was requested from the Social Welfare Department on 27 May 1986.
  
- Work is proceeding very well despite the short period of time. A tender was held and a mason was chosen who started digging the foundations. Parts of the gravel, cement, cement blocks, and reinforcing steel are on the spot.

GA/1b

104

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-23

Sub-project Location : Shwaikheh village, Tulkarem District, West Bank

Operating Agency : CRS JWB with Shwaikheh village.

Sub-project Proposal : Constructing a community center consisting of 10 rooms, entrance, corridor, staircase, kitchen & W.C. units the whole totalling about 345 m2.

Objective : Improving facilities for carrying out community sponsored and - oriented activities.

Expected Results : The villagers intend to use the community center for typing and weaving courses, out-patient clinic, kindergarten, health education and sports activities. Some of these services and activities are still lacking due to the fact that there is no building to house them. The rest are carried in rented rooms.

Time needed to complete sub-project : Approximately 6 months , following which the new center will be put into use immediately.

Supporting local Authorities : Shwaikheh village committee, Department of Labour and Social Welfare, and the West Bank District Authorities.

Cost Estimate : \$ 81,250.- = JD 26,000.- at exchange rate of U.S. \$ 1.- = JD 0.32

Participants in cost : CRS JWB up to a maximum of 50% equivalent to \$ 40,625.- = JD 13,000.-.  
: Shwaikheh Village a minimum of 50% equivalent to \$ 40,625.- = JD 13,000.-.

Construction Lay-outs Prepared by : Private architect in consultation with the local council and subject to the approval of CRS-JWB.

Responsibility for sub-project Upkeep Maintenance : The local Committee.

Expected Number of Beneficiaries : 5250 persons (the entire population).

**Brief Narrative:**

Shwaikeh lies 3 kms north of Tulkarem. The majority of its 5250 inhabitants are farmers who grow olives, wheat, barley and vegetables, mostly potatoes and grapes. Some of the villagers work as labourers in the West Bank. A few villagers have emigrated to the Arab Countries and they remit money to their families in the village. The village has water, electricity, some paved interior roads, a post office and two schools. It lacks a village council, a charitable society, and an agricultural cooperative. Parts of the village lands were lost during the 1948 war.

This sub-project will provide new educational opportunities for the villagers with a suitable place where they can plan and carry out village activities. In addition to new activities and services, the building will house the current activities which are ongoing in scattered rented rooms, such as the typing knitting and sewing courses, the out-patient clinic, the kindergarten and the health education class. The villagers also intend to use the center for literacy classes and for private intensive courses. The community center building will promote dignity and self-reliance by enabling the villagers to make more productive use of their time.

**PROJECT  
IMPLEMENTATION:**

Implementation can start as soon as CRS/New York approval is given and agreement is signed by Shwaikeh village, the ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-23

This Agreement is between Shwaikah village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

- A. SUB PROJECT DESCRIPTION  
Constructing a community center consisting of 10 rooms, entrance, corridor, staircase, kitchen & W.C. units the whole totalling about 345 m2
- B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-
1. At least 50% of the total estimated sub-project's cost of US \$ 81,250.-- equivalent to \$ 40,625.-0 (JD 13,000.-)
  2. A committee to supervise daily all work on the project and keep records of labour and material used.
- C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-
1. At least 50% of the total estimated sub-project's cost of US \$ 81,250.-- equivalent to \$ 40,625.- (JD 13,000.-)  
This amount is provided by AID.
  2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.
- D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 180 (One Hundred Eighty days) from the first work day of the project.
- E. The village will be responsible for the project maintenance and upkeep.
- F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.
- G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.
- H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

- I. The village herewith agrees to hold the Catholic Relief services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

**SIGNATURES**


الإدارة المدنية لمحافظة يهودا والسامرة  
 مديرية مكتب المشاريع القروية  
 قرية صيوزة

*[Handwritten signature]*

2051110/7  
 717

DEPARTMENT OF LABOUR & SOCIAL WELFARE

DISTRICT AUTHORITIES



*[Handwritten signature]*

CATHOLIC RELIEF SERVICES



*[Handwritten signature]*

DATE: - 2/18/1986

**ESTIMATED COST LIST**

Sub-project No. 23

CRS-JWB/USAID ( )

NAME OF VILLAGE : Shwakkh LOCATION : Tulkarem District

PROJECT DESCRIPTION : Constructing a community center consisting of ten rooms, corridor, entrance, staircase, W.C. Units and a kitchen the whole totalling about 345 m<sup>2</sup>.

MATERIAL	Quantity	Price JD	Total JD	WAGES	Quantity	Price JD	Total JD
Black Cement	120 tons	35	4,200.-	Mason	357 m <sup>2</sup>	10.5	3,748.5
White Cement	18 bags	5	90.-	Plasterer	1270 m <sup>2</sup>	0.80	1,016.-
Scdel	12.4 tons	235	2,914.-	Tiling	485 m <sup>2</sup>	0.80	388.-
Doors	46 m <sup>2</sup>	36	1,656.-	Pointing	270 m <sup>2</sup>	0.90	243.-
Windows	32.6 m <sup>2</sup>	28	912.80	Painting	260 m <sup>2</sup>	0.90	234.-
Window Fence	32.6 m <sup>2</sup>	7	228.20	White Washing	940 m <sup>2</sup>	0.70	658.-
Building Stone	985 m.r.	1.65	1,625.25	Miscellaneous	-	-	262.-
Cement Blocks	4875	21	1,023.75	Labourers	80 days	4	320.-
Rough Stone	85 m <sup>3</sup>	2.3	195.5	Skilled Labour	20 days	5	100.-
Gravel, Mixed	218 m <sup>3</sup>	3.50	763.-	Bulldozer	7 days	80	560.-
Fine	60 m <sup>3</sup>	4.60	276.-	Cess Pool	90 m <sup>2</sup>	9	810.-
Powder	55 m <sup>3</sup>	5.40	297.-	Compressor	6 days	35	210.-
Sand	130 m <sup>3</sup>	2.80	364.-	Rolling machine			
Files	360 m <sup>2</sup>	1.60	576	Total of Wages			8,549.50
Glass	46 m <sup>2</sup>	4.5	207.-	Total of Material Cost			
Water	17 Tanks	6	102.-	Grand Total JD			26,000.-
Window Sill	38.5 m <sup>2</sup>	8	308.-	Grand Total US \$			81,250.-
Porcelain tiles	1120	.12	134.40				
Asphalt				CRS-JWB-EX- 50%			
Asphalt Mixed	120 m <sup>2</sup>	5	600	US \$ 40,625.- = JD 13,000.-			
Solar				VILLAGE SHARE 50%			
Wood				US \$ 40,625.- = JD 13,000.-			
Pipes	48 m.r.	1.20	57.60	At an exchange rate of US \$ 1 = JD 0.32			
Fitting Parts	-	-	340.-				
& W.C. seats							
Materials			580				
Total of Material Cost			17,450.50				

SIGNATURE :



Name :

Signature :



Village Representative

109

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last report:  
Date of This report: 1 OCTOBER 1986

1. REFERENCE SECTION

CRS-JMB/USAID

Sub-Project No. 4D-006-24

US. \$ 43,750.-

Sub-Project estimated cost

CRS JMB in co-operation with

BEIT EL-RUSH EL-FOQA

Name of Operating Agency

WATER SYSTEM

Title of Sub-Project

HEBRON DISTRICT

Area in which Sub-Project is located

NEB-0159-0-SS-5123-00

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 26,250.-

(I) CRS AID cash input

Equivalent to \$ 17,500.-

Village cash input

US \$ 746,112.-

(II) Funds received to date & date of last transmittal

15 AUGUST 1986

CRS AID US \$ ----

(III) Sub-Project expenditure (s) to date

Village US \$ ---

CRS AID US \$ 26,250.-

(IV) Balance (s) unused

Village US \$ 17,500.-

(V) Other inputs which contributed to success of Sub-Project

### 3      PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The aim of this sub-project is to establish a drinking water system for Beit El-Rush El-Foqa village, according to the West Bank Water Authority plans.
  
- This sub-project was requested from the Social Welfare Department-Beit-El-West bank, on 27 may 1986 while the agreement was signed with the village leadership on 25 August 1986 (three months period).
  
- The villagers are still collecting their share. The drought year and the very bad economic situtation in the West bank formed a very heavy burden on the villagers. Despite this, the village committee is doing all its best to collect all the village's share in the near future.

GA/1b

111

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-24

Sub-Project Location : Beit El-Rush El-Foqa village, hebron District,  
West Bank

Operating Agency : CRS JWB together with Beit El-Rush El-Foqa village

Sub-Project Proposal : Establishment of a potable drinking water system  
by laying 1100 m of 2" and 1900 m of 1" water  
pipes throughout the village linking it with the  
main line of the West Bank Water Authority.

Expected Results : Villagers will have an ample supply of clean,  
unpolluted, potable running water to meet their  
various needs - drinking, washing clothes and  
dishes, bathing, mopping floors etc. all the year  
round. It follows that the health status of the  
population should improve significantly.

Time needed to  
complete sub-  
project : Construction of the main pipe line throughout the  
village will take about 3 months.

Supporting Local  
Authorities : Beit El-Rush El-Foqa village committee, Department  
of Labour and Social Welfare, West Bank Water  
Authority and the District Authorities.

Cost Estimate : \$ 43,750.- equivalent to J.D. 14,000.- at exchange  
rate of approximately J.D. 0.32 = \$1.-

Participants in cost : CRS JWB 60% equivalent to \$ 26,250.- = J.D.  
8,400.-  
Village 40% equivalent to \$ 17,500.- = J.D.  
5,600.-

Sub-project plan  
prepared by : The West Bank Water Authority, subject to the  
concurrence of CRS JWB

Responsibility for  
sub-Project upkeep/  
Maintenance : The village will be responsible for the routine  
maintenance of the pipe line, while back - up for  
major problems will be provided by the West Bank  
Water Authority.

Expected Number of  
Beneficiaries : The entire population of the village (i.e. 800)

**Brief Narrative :**

Beit El-Rush El-Foqa is a small village located 32 kms south west of Hebron. It has about 800 inhabitants. Most of the villagers earn their living by cultivating wheat, barley, crops, legumes, and olives.

Beit El-Rush El-Foqa has no paved interior streets, agricultural roads, agricultural cooperative, charitable society, electricity, community center, postal services, telephones, or water system. It only has a primary co-educational school and a rented out-patient clinic. Villagers are still dependent on rain water accumulated in hand-dug cisterns.

The water which is carried to the cisterns by open channels through unclean courtyards and animal compounds, is polluted. To get the polluted water to their homes, village women have to walk several times daily to the cisterns, fill their buckets, and carry them on their heads or on donkey's backs. By the time the water reaches their houses, it will be even more polluted and loaded with germs. So often, in drought years such as this year, villagers will have to buy water. This situation forms a heavy burden on the villagers and hinders the development in the village.

The implementation of this vital sub-project will provide Beit El-Rush with clean, running, drinking water throughout the village linking it with the main line of the West Bank Water Authority. This will likely improve the hygiene conditions of the villagers. It will also encourage some villagers to return and to develop their village. It is expected that all the villagers will contribute towards their village's share of the costs.

**PROJECT  
IMPLEMENTATION:**

Implementation can start as soon as CRS/New York approval is given and agreement is signed by Beit El-Rush El-Foqa village, the ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-24

This Agreement is between Beit El-Rush El-Foqa village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB PROJECT DESCRIPTION

Establishing a drinking water system according to the West Bank Water Authority plans, and connecting it with the main line.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 40% of the total estimated sub-project's cost of US \$ 43,750.- equivalent to \$ 17,500.- (JD 5,600.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 60% of the total estimated sub-project's cost of US \$ 43,750.- equivalent to \$ 26,250.- (JD 8,400.-)
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 90 (Ninty days only) from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.


- I. The village herewith agrees to hold the Catholic Relief Services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

الإدارة المدنية لتعمير مدائن اسكندرية  
 مديرة مكتب التوزيع القروي  
 فريال ديوزنه

*[Handwritten signature]*

DEPARTMENT OF LABOUR & SOCIAL WELFARE



DISTRICT AUTHORITIES

*[Handwritten signature]*

*[Handwritten signature]*



*[Handwritten signature]*

CATHOLIC RELIEF SERVICES

V I L L A G E

DATE: 25/8/86

115

**ESTIMATED COST LIST**

Name of village : Beit El-Rush El-Foqa

Location : Hebron District

Sub-Project No. : 4D-006-24

Project Description : Establishing a drinking water system according to the West bank Water Authority plans, and connecting it with the Main Line.

<u>MATERIAL</u>	<u>QUANTITY</u>	<u>UNIT COST (J.D)</u>	<u>TOTAL COST (J.D.)</u>
1. 2" Water Pipes	1100 m	5	5500
2. 1" Water Pipes	1900 m	3	5700
3. Installing the Water System	(by work)		2800
	GRANT TOTAL (J.D.)		14000

TOTAL COST ESTIMATE: U.S. \$ 43,750.- = J.D. 14,000.-  
At an exchange rate of U.S. \$ 1.- = JD 0.32

CRS SHARE 60% = U.S. \$ 26,250.- = JD 8,400.-

VILLAGE SHARE 40% = U.S. \$ 17,500.- = JD 5,600.-

P.O. BOX 19447  
East Jerusalem

CATHOLIC RELIEF SERVICES - USCC  
JERUSALEM AND WEST BANK

PAGE OF

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM  
SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT NO. ( 1 )

Date of Last report:  
Date of This report: 1 October 1986

1. REFERENCE SECTION

CRS-JWB/USAID  
Sub-Project No. 4D-086-25

US. \$ 21,875.-  
Sub-Project estimated cost

CRS JWB in co-operation with BEIT EL-RUSH EL-TAHTA  
Name of Operating Agency

WATER SYSTEM  
Title of Sub-Project

HEBRON DISTRICT  
Area in which Sub-Project is located

NEB-0159-G-SB-5123-00  
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 13,125.- Equivalent to \$ 8,750.-  
(I) CRS AID cash input Village cash input

US \$ 746,112.- 15 AUGUST 1986  
(II) Funds received to date & date of last transmittal

CRS AID US \$ --- Village US \$ ---  
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 13,125.- Village US \$ 8,750.-  
(IV) Balance (s) unused

(V) Other inputs which contributed to success of Sub-Project

117

### 3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for establishing a drinking water system for Beit El-Rush El-Tahta village, according to the West bank Water Authority plans.
  
- This sub-project was requested from the Social Welfare Department-Beit-El-West bank, on 27 May 1986 while the agreement was signed with the village leadership on 25 August 1986.
  
- Due to the drought year and the very bad economic situation prevailing in the West Bank, villagers met great difficulties in collecting the village's share, but the village committee is doing its best to make the village's share available in the near future.

GA/1b

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

Sub-Project Proposal Within Package  
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-25

Sub-Project Location : Beit El-Rush El-Tahta village, hebron District,  
West Bank

Operating Agency : CRS JWB together with Beit El-Rush El-Tahta village

Sub-Project Proposal : Establishment of a potable drinking water system  
by laying 800 m of 2" and 500 m of 1" water  
pipes throughout the village linking it with the  
main line of the West Bank Water Authority.

Expected Results : Villagers will have an ample supply of clean,  
unpolluted, potable running water to meet their  
various needs - drinking, washing clothes and  
dishes, bathing, mopping floors etc. all the year  
round. It follows that the health status of the  
population should improve significantly.

Time needed to  
complete sub-  
project : Constrution of the main pipe line throughout the  
village will take about 3 months.

Supporting Local  
Authorities : Beit El-Rush El-Tahta village committee, Department  
of Labour and Social Welfare, West Bank Water  
Authority and the District Authorities.

Cost Estimate : \$ 21,875.- equivalent to J.D. 7,000.- at exchange  
rate of approximately J.D. 0.32 = \$1.-

Participants in cost : CRS JWB 60% equivalent to \$ 13,125.- = J.D.  
4,200.-  
Village 40% equivalent to \$ 8,750.- = J.D.  
2,800.-

Sub-project plan  
prepared by : The West Bank Water Authority, subject to the  
concurrence of CRS JWB

Responsibility for  
sub-Project upkeep/  
Maintenance : The village will be responsible for the routine  
maintenance of the pipe line, while back - up for  
major problems will be provided by the West Bank  
Water Authority.

Expected Number of  
Beneficiaries : The entire population of the village (i.e. 500)

**Brief Narrative :** Beit El-Rush el-Tahta is a small village located about 31 kms south west of Hebron. It has about 500 inhabitants. Most of the villagers earn their living by cultivating wheat, barley, crops, legumes and olives.

Beit El-Rush El-Tahta has no paved interior streets, agricultural roads, agricultural cooperative, charitable society, health clinic, community center, postal services, telephone, or water system. It only has a primary co-educational school.

Beit El-Rush El-Tahta has always depended on the winter rains (October - April) for its water needs year-round. Villagers depend on cisterns to capture the run-off from the rains, fed by open chamels. This water can scarcely be considered hygienic, as it passes through unclean courtyards and animal compounds. It reaches the houses in open buckets either on women's heads or on donkeys' backs thus becoming more polluted. In drought years such as this year, villagers will have to buy water. This is a heavy burden on them and hinders the village development.

The implementation of this vital sub-project will provide Beit El-Rush El-Tahta with clean, running, drinking water throughout the village linking it with the main line of the West Bank Water Authority. This will likely improve the hygiene conditions of the villagers. It will also encourage some villagers to return and to develop their village. It is expected that all the villagers will contribute towards their village's share of the costs.

**PROJECT**

**IMPLEMENTATION:**

Implementation can start as soon as CRS/New York approval is given and agreement is signed by Beit El-Rush El-Tahta village, the ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-25

This Agreement is between Beit El-Rush El-Tahta village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB PROJECT DESCRIPTION

Establishing a drinking water system according to the West Bank Water Authority plans, and connecting it with the main line.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 40% of the total estimated sub-project's cost of US \$ 21,875.- equivalent to \$ 8,750.- (JD 2,800.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 60% of the total estimated sub-project's cost of US \$ 21,875.- equivalent to \$ 13,125.- (JD 4,200.-) . This amount is provided by AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 90 (Ninty days only) from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

121

- I. The village herewith agrees to hold the Catholic Relief services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

الإدارة المدنية لمنطقة يهودا والسامرة  
 مديرة مكتب المشاريع القروية  
 فريال دووזה

*[Handwritten signature]*

DEPARTMENT OF LABOUR & SOCIAL WELFARE


*[Handwritten signature]*

DISTRICT AUTHORITIES



*[Handwritten signature]*

CATHOLIC RELIEF SERVICES



*[Handwritten signature]*

V I L L A G E

*[Handwritten signature]*

DATE: - 25/8/1986

ESTIMATED COST LIST

Name of village : Beit El-Rush El-Tahta

Location : Hebron District

Sub-Project No. : 4D-006-25

Project Description : Establishing a drinking water system according to the West Bank Water Authority plans, and connecting it with the main line.

MATERIAL -----	QUANTITY -----	UNIT COST (J.D) -----	TOTAL COST (J.D.) -----
1. 2" Water Pipes	300 m	5	4000
2. 1" Water Pipes	500 m	3	1500
3. Installing the Water System	(by work)		1500
	GRAND TOTAL (J.D.)		7000

TOTAL COST ESTIMATE : U.S. \$ 21,875.- = J.D. 7,000.- (At an exchange rate of U.S. \$ 1.- = J.D. 0.32)

CRS SHARE 60% = U.S. \$ 13,125.- = J.D. 4,200.-

VILLAGE SHARE 40% = U.S. \$ 8,750.- = J.D. 2,800.-

123
