

PD CAVOTT



CATHOLIC RELIEF SERVICES

Near East

FILE

COUNTRY <u>Korea</u> ^(CRS) <u>Rural Area III</u>	
PROJ. # <u>398-0159.14</u>	BIR CODE <u>82</u>



World Headquarters
Catholic Relief Services
1011 First Avenue
New York, NY 10022
Telephone: (212) 838-4700
Cable: CATHWEL New York

PDC44077

Washington Office
2010 Massachusetts Ave., N.W.
Washington, D.C. 20036
Telephone: (202) 466-4578

May 22, 1987

Ms. Carla Barbiero
Project Officer
ANE/NE/TR/HR
Agency for International Development
Washington, DC 20523

RE: SEMI-ANNUAL PROGRESS REPORT NO. 4
ON THE INFRASTRUCTURAL DEVELOPMENT
COMPONENT OF THE JWB RURAL DEVELOPMENT
GRANT -AID/NEB-0159-G-SS-5123-00

398-0159.14

Dear Carla:

Please find enclosed four (4) copies of the above report for the period October 1, 1986 to April 1, 1987.

Reports on the small business and agricultural mechanization components of this grant will be submitted USAID/W within another week.

As noted in the report, 19 sub-projects have now been completed under this grant. During this six-month period, nine of these sub-projects benefiting 26,000 people were completed.

Your comments on this report would be welcomed.

With kind regards.

Sincerely,

Pauline L. Wilson
Resource Administrator

PLW/vb
enc.

FILE

2

RECEIVED
MAY 19 1987

CATHOLIC RELIEF SERVICES
EURASIA REGION
MENA


FOURTH REPORT
RURAL DEVELOPMENT PROJECT

CRS JWB / 4D - 006

USAID 5123

398-0159.14

01 April 1987

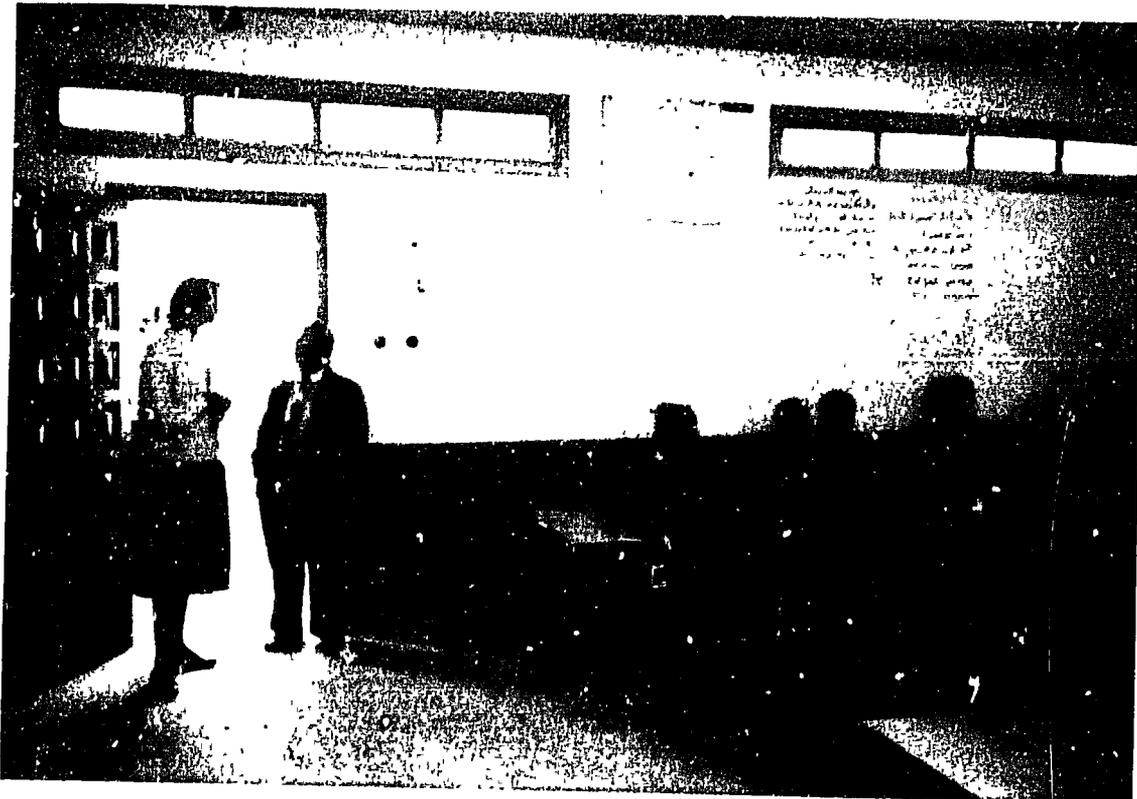

Ms. Carla ilaged - AID/Washington, accompanied by CRS - JWB Rural Development Supervisor, visiting a CRS - AID school sub-project in Gaza Strip.

3X



Mr. Abraham Grayson - AID/W Chief Engineer, Mr. Douglas Broderick - CRS / JWB Assistant Country Representative, and Mr. Issa Barakat - CRS / JWB Rural Development Supervisor, visiting one of CRS / AID Sub-Projects in the West Bank. Also appearing in the photo, members of the village committee.

P.O. BOX 19447
EAST JERUSALEM

CATHOLIC RELIEF SERVICES-USCC
JERUSALEM AND WEST BANK

PAGE 1 OF .

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
SEMI-ANNUAL PROJECT PROGRESS REPORT NO. (4)

Date of Last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

CRS-JWB/USAID

CRS Project No. 4D-886

US. \$ 5,842,871.-
AMOUNT

CATHOLIC RELIEF SERVICES - USCC JERUSALEM AND WEST BANK

Name of Operating Agency

"A partnership Project Assistance Program to promote the development of Rural Agriculture, Health Education and
Electrification in the Jordan West Bank and Gaza Strip".

Title of Project

ISRAELI ADMINISTERED JORDAN WEST BANK AND GAZA STRIP

Area in which Project is located

NEB - 8159 - G - 26 - 5123 - 08

Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 5,842,871.-

(I) AMOUNT OF GRANT

US \$ 763,594.43

Total Village cash input into sub-projects
to date

U.S. \$ 1,157,598.84

(II) Amount received to date

28 January 1987

(III) Date of last transmittal

US \$ 4,697,716.72

(IV) Balance due under Grant

US \$ 1,145,154.28

(V) Expenditure to date

The strong willingness of the West Bank villagers to cooperate and work together, and their great efforts to come up with their shares and to donate parts of their lands to sub-projects.

Other inputs which contributed to success of Project.

PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This is the fourth Semi-Annual Project Progress Report for the AID Grant - AID/NEB-0159-G-SS-5123-00 entitled "Rural Development III", to provide support for a program in the West Bank and Gaza Strip. This program supports subcomponent activities in the areas of infrastructural development, increased agricultural production, and small business enterprise development.
- This report covers the period from 1 October 1986 through 1 April 1987. Excellent progress was made during the reporting period, despite the very bad weather and heavy rain.
- During this reporting period, we were honored by the visits of Mr. Abraham Grayson - AID/W Chief Engineer, Ms. Carla Maged, Mr. Robert Bell, and Mr. Steve Grant from AID/Washington, Ms Paula Brumbaugh - American Vice Consul Jerusalem, and Ms. Molly Williamson - Political Officer U.S. Embassy Tel Aviv. They all expressed their satisfaction and admiration in the level of accuracy and tactfulness with which work is being achieved.
- CRS and village partners were engaged in work on twenty sub-projects during this reporting period. In the following pages we highlight the work of these sub-projects.
- Nine sub-projects were successfully completed benefitting more than 26,000 persons and bringing the number of completed sub-projects since the beginning of this Grant to nineteen (table "1").
- The nine involved constructing two primary schools, one for Husan Village - Bethlhem District (4D-006-14) and the other for Yatmah Village - Nablus District (4D-006-22). Two other completed sub-projects involved establishing a drinking water system for two villages in Tulkarem District. Kufor Kaddum (4D-006-12) and Jeet (4D-006-13). Three electrification sub-projects were completed, two in Hebron District; Raqa' (4D-006-19) and El-Mureq-El-Kom (4D-006-20), and the third in Jericho District - Zbaidat Village (4D-006-21).

- Another completed sub-project involved opening, clearing and leveling an agricultural access road about 5 kms long by 5.5 meters wide linking El-Idaiseh with Bani N'aim Village in Hebron District (4D-006-17). The ninth completed sub-project involved widening, clearing, leveling, and asphaltting existing interior streets in Barta' Village - Jenin District (4D-006-28). The attached map shows the location of these nine sub-projects.
- In the following pages are to be found individual reports, including itemizations of expenditures, photos captions, and thanks letters or notes for each of the nine completed sub-projects.
- The other eleven sub-projects are on-going (Table "2"). They involve establishing water systems for Beit El Rush El Foqa Village (4D-006-24) and Beit El Rush El Tahta Village (4D-006-25) in Hebron District, widening clearing, leveling, and asphaltting interior streets in Attil Village - Tulkarem District (4D-006-26) and in El Shiyoukh Village - Hebron District (4D-006-29). Three other sub-projects involve opening, clearing, leveling and asphaltting portions of agricultural access roads for Beit Ummar Village - Hebron District (4D-006-16), Surda-Raddana - Ramallah District (4D-006-30a) and for El-Shawawreh Village - Bethlehem District (4D-006-31).

The three other on-going sub-projects involve constructing a community center for Shwaikeh Village - Tulkarem District (4D-006-23), a primary school for Zif Village - Hebron District (4D-006-32) and an out-patient health clinic for Huwwara village - Nablus District (4D-006-33).

In the following pages are to be found individual reports on each of these eleven sub-projects.

- Seven other sub-projects are waiting the approval of the local government authorities (Table "3"). Of these, two were submitted to the authorities long ago, while up to this date the agreements are still not signed. Bir Zeit sub-project was presented on 11 April 1985 and Wadi Fukkin sub-project was presented on 10 February 1986. Both sub-projects involve opening, clearing, and leveling agricultural roads.

- People in the West Bank and Gaza Strip are facing serious financial problems. Village committees have difficulties while raising villages' shares.
- During this reporting period, villagers continued to approach CRS-AID asking for sub-projects, in particular agricultural access roads, interior streets, and electrification, as we are the only voluntary organization in the West Bank and Gaza Strip involved in such sub-projects. Attached is a list in the requested sub-projects.
- A separate and complete report on the Increased Agricultural Production and the Small Business Management Assistance Program is being sent with this Semi-Annual Progress Report.

ATTACHEMENTS:

- Budget Expenditure Statement
- Final reports on Nine Completed Sub-Projects.
- Progress Reports on Eleven Ongoing Sub-Projects.
- Tables.
- Map.

DISTRIBUTION OF REPORT (11 COPIES):

- USAID / W - NE / RECH - RHPD (3)
- CRS NEW WORK (3)
- US EMBASSY - TEL AVIV , AID LIAISON OFFICER (1)
- US CONSULATE GENERAL - WEST JERUSALEM (1)
- CRS JWB (2)
- CRS JWB RD OFFICE (1)

CRS JWB 4D-006 RURAL DEVELOPMENT PROJECT

GRANT NO. NEB - 0159 - G - SS - 5123

BUDGET EXPENDITURE STATEMENT

PROGRAM: JERUSALEM & WEST BANK
MONTH: MARCH 1987

GRANT	APPROVED BUDGET 03/04/1985 03/04/1987 ----- US \$	BUDGET EXPENDITURE TO DATE ----- US \$	BALANCE ----- US \$
1. INFRASTRUCTURAL DEVELOPMENT	1,186,250.-	819,409.29	366,840.72
2. PROJECT SUPERVISION	351,468.-		62,860.43
a. Salaries \$	242,968.-	214,517.65	
b. Travel	48,000.-	25,684.19	
c. Non-Expendable	38,000.-	23,761.06	
d. Direct Costs	12,000.-	13,451.89	
e. Office Rent & Utilities	10,500.-	11,192.78	
		27,230.59	129,069.41
3. INCREASED AGRICULTURAL PRODUCTIVITY	156,300.-	8,472.68	27,527.32
4. SMALL BUSINESS ENTER- PRISE DEVELOPMENT	36,000.-	1,434.16	49,406.84
5. CONSULTATIVE, EVALUATIVE & MONITORING	50,841.-	1,145,154.28	635,704.72
	-----	-----	-----
TOTAL	1,780,859.- -----		

GA/sk.

9

TABLE "1"

BEST AVAILABLE DOCUMENT

COMPLETED SUB-PROJECTS
(APRIL 1985 - APRIL 1987)

NAME OF VILLAGE/ LOCATION/(SUB PROJECT NO.)	KIND OF PROJECT	TOTAL COST \$	CRS SHARE \$	VILLAGE SHARE \$	BENEFICIARIES (PERSONS)
Kufor Malik / Ramallah (01)	Interior Streets	63,709.42	34,644.61 (54%)	29,064.81 (46%)	2000
Taybeh / Ramallah (02)	Interior Streets	62,738.43	35,846.71 (57%)	26,891.72 (43%)	800
Silet El-Harthieh / Jenin (04)	Community Center	94,109.66	45,498.11 (48%)	48,611.55 (52%)	7500
Sinjel / Ramallah (05)	Water System	116,707.13	57,526.27 (49.3%)	59,180.86 (50.7%)	3500
Za'tara / Bethlehem (06)	Community Center	60,907.95	35,750.65 (58.7%)	25,157.30 (41.3%)	2000
Kfairet / Jenin (07)	Electrifica- tion	91,820.-	45,446.- (49.5%)	46,374.- (50.5%)	1000
El-Hashimieh / Jenin (08)	Access Road	76,286.43	44,112.43 (57.8%)	32,174.- (42.2%)	700
Ta'nik / Jenin (10)	Electrifica- tion	72,493.-	43,489.- (60%)	29,004.- (40%)	700
Nahhalin/Bethlehem (11)	Agricultural Road	53,017.43	31,793.86 (60%)	21,223.57 (40%)	1500
Kufor Kaddum / Tulkarem (12)	Water System	106,253.94	52,796.23 (50%)	53,457.71 (50%)	3000
Jeet / Tulkarem (13)	Water System	55,391.85	31,916.25 (57.4%)	23,575.60 (42.6%)	1500

10

TABLE "1" (CONT.)

NAME OF VILLAGE/ LOCATION/(SUB PROJECT NO.)	KIND OF PROJECT	TOTAL COST \$	CRS SHARE \$	VILLAGE SHARE \$	BENEFICIARIES (PERSONS)
Husan / Bethlehem (14)	Primary School	42,647.85	19,501.41 (45.7%)	23,146.44 (54.3%)	3000
Marah Rabah / Bethlehem (15)	Access Road	52,098.06	31,224.49 (60%)	20,873.57 (40%)	1000
Bani N'aim El-'Idaiseh / Hebron (17)	Agricultural Road	60,763.77	36,342.70 (60%)	24,421.07 (40%)	6000
Raqa' / Hebron (19)	Electrifica- tion	98,751.74	59,179.37 (60%)	39,572.37 (40%)	4000
El-Mureq El-Kom / Hebron (20)	Electrifica- tion	120,790.45	71,667.79 (59%)	49,122.66 (41%)	1600
Zbaidat / Jericho (21)	Electrifica- tion	34,415.41	22,278.12 (65%)	12,137.29 (35%)	1200
Yatmah / Nablus (22)	Primary School	40,707.38	24,525.14 (60.2%)	16,182.24 (39.8%)	3000
Barta' & Khirbat Barta' / Jenin (28)	Interior Streets	74,945.-	38,763.75 (52%)	36,181.25 (48%)	3000

BEST AVAILABLE DOCUMENT

11

TABLE "2"

ONGOING SUB-PROJECTS

<u>NAME OF VILLAGE/LOCATION (SUB-PROJECT NO.)</u>	<u>KIND OF PROJECT</u>	<u>ESTIMATED COST \$</u>	<u>CRS SHARE \$</u>	<u>VILLAGE SHARE \$</u>	<u>BENEF. (PERSONS)</u>
Beit 'Ummar / Hebron (16)	Agricultural Roads	81,071.-	40,535.50	40,535.50	8000
Shwaikeh/Tulkarem (23)	Community Center	81,250.-	40,625.-	40,625.-	5250
Beit El-Rush El-Foqa/Hebron (24)	Water System	43,750.-	26,250.-	17,500.-	800
Beit El-Rush El-Tahta/Hebron (25)	Water System	21,875.-	13,125.-	8,750.-	500
'Attil/Tulkarem (26)	Interior Streets	78,766.-	35,445.-	34,321.-	8500
El-Shiyoukh/Hebron (29)	Interior Streets	87,031.-	39,015.50	39,015.50	5000
Surda-Raddana/Ramallah (30a)	Access Road	40,375.-	29,025.-	19,350.-	370
El-Shawawreh/Bethlehem (31)	Agricultural Road	57,594.-	32,829.-	24,765.-	4500
Zif/Hebron (32)	Primary School	72,188.-	46,922.-	25,266.-	2000
Huwara/Nablus (33)	Out-patient Clinic	58,437.-	29,218.50	29,218.50	8000
Shu'ab Musmar and Others/ Hebron (34)	Electricity	126,742.-	72,243.-	54,499.-	2700

BEST AVAILABLE DOCUMENT

12


TABLE "3"

SUB-PROJECTS WAITING APPROVAL

<u>NAME OF VILLAGE/LOCATION (SUB-PROJECT NO.)</u>	<u>KIND OF PROJECT</u>	<u>ESTIMATED COST \$</u>	<u>CRS SHARE \$</u>	<u>VILLAGE SHARE \$</u>	<u>BENEF. (PERSONS)</u>
Beir Zeit / Ramallah (89)	Agricultural Roads	47,886.-	23,943.-	23,943.-	3000
Wadi Fukkin / Bethlehem (18)	Access Road	56,000.-	33,600.-	22,400.-	1000
Till / Nablus (27)	Interior Streets	94,725.-	37,890.-	56,835.-	4000
Surda-El-Salamiyyeh/ Ramallah (30b)	Access Road	26,563.-	15,938.-	10,625.-	230
Khirbat 'Irzaikiyyeh/ Hebron (35)	Access Road	71,382.-	46,398.-	24,984.-	900
Burqin/Jenin (36)	Interior Streets	86,073.-	38,734.-	47,339.-	6000
Kasra/Nablus (37)	Electricity	100,750.-	50,379.-	50,379.-	4000

THE RELIEF SERVICES ASSOCIATION
COMPLETED THE OPENING OF AN
AGRICULTURAL ROAD

الطبعة المحلي



خدمة خدمات الإغاثة

القسيس - صرح عيسى بركات مدير
التنمية الريفية في جمعية خدمات الإغاثة
الكاثوليكية في القدس بان الجمعية
فرغت من شق طريق زراعي بطول خمسة
كيلومترات يربط قرية بني نعيم مع قرى
سعين والعبسة والقرى المجاورة شرق
مدينة الخليل

واضلل بركات بان العمل يجري
حاليا في بناء مدرسة مختلطة في قرية
زيف ومحالفة الخليل مؤلفة من خمسة
غرف للتدريس وملحقاتها تقام بمساهمة
خدمات جمعية الإغاثة الكاثوليكية

Jerusalem - Issa Barakat, the supervisor of the Rural Development at the Catholic Relief Services in Jerusalem, declared that the association has completed the opening of an agricultural road 5 kms-long linking Bani N'aim village with Sa'ir, Fl-Idaiseh, and the surrounding villages east of Hebron.

Barakat added that work is ongoing in constructing a co-educational school in Zif village, Hebron District, consisting of five classrooms, with the assistance of the Catholic Relief Services.



الجمعة ١٣ شباط ١٩٨٧، ١٤ جمادى ثاني ١٤٠٧ هـ - العدد ٥٠ - القدس

"AN-NAHAR" Jerusalem Friday 13 February 1987 NO.50

Some of The Catholic Relief Services Activities

Following is a summary of CRS latest activities in the West Bank:

من نشاطات خدمات الإغاثة الكاثوليكية

● فيما يلي مجمل النشاطات مؤسسة خدمات الإغاثة الكاثوليكية في الضفة
مؤخرا:

● في بيت أومر بإشراف المجلس القروي
بشؤون طرق زراعية في القرية بالتعاون مع
مؤسسة خدمات الإغاثة.

● وفي الشيوخ بإشراف لجنة القرية
بتوسيع الطرق الداخلية بالتعاون مع
المؤسسة وتقدر التكاليف بـ ٢٥ آلاف
دينار.

● والمفدى لجنة المعارف للقرية زيف
بأنه قد بوشر العمل في بناء مدرسة
مختلطة بإشراف مهندس المؤسسة داود
أبو جفم

● وفي حواراه بإشراف المجلس القروي
ببناء عيادة صحية للقرية

- In Beit 'Ummar, the village council started opening agricultural roads in cooperation with the Relief Services Association.
- In El-Shiyoukh, the village committee started widening the interior streets in cooperation with the association. The costs are estimated by 25,000 Dinars.
- The educational committee in Zif village informed us that work has started in constructing a co-educational school under the supervision of the association's engineer Da'oud Abu Judom.
- In Huwwara, the village council started building a health clinic for the village.


AL — FAJR DAILY

JERUSALEM

NOVEMBER 1986

Friday 28

No. 4276



السنة الرابعة عشر

الجمعة ٢٨ من الشهر الثاني ١٩٨٦

العدد ٤٢٧٦

الصفحة ٨

تنفيذ مشاريع تطويرية

في عدد من قرى محافظة الخليل

الخليل - ارسلنا الخاص - تم امس توقيع اتفاقتين لتنفيذ مشاريع تطويرية في قرى زيف والشيوخ في محافظة الخليل بمساهمة من خدمات الاغاثة الكاثوليكية في القليل في بناء مدرسة ابتدائية مختلطة في قرية زيف مكونة من ست غرف دراسية مع ملحقاتها

تقدر تكاليفها بحوالي ٢٠ الف دولار سنويًا. خدمات الاغاثة الكاثوليكية تسيّر ١٠ سيارات من مشروع تكاليف المشروع الميزنة. وتم توقيع هذه الاتفاقية بحضور عدد من المسؤولين والمسؤولين في مديرية المشاريع القروية في خدمات الاغاثة وتمكين سكان قرى زيف والشيوخ وتساهم خدمات الاغاثة في تنفيذ عدد من المشاريع الحيوية في عدد من قرى محافظة الخليل حيث يجري العمل حاليا في تنفيذ مشاريع للكهرباء في قرى الكوم وبيت مقوم والموق ورفقة وشرق طريق يربط ما بين قرى زيف والشيوخ في تنفيذ

وبمساحة قدرها ٢٢٠ مترا مربعا وتبلغ تكاليفها حوالي ١٢ الف دولار سنويًا. تساهم خدمات الاغاثة ببنائها ١٠ غرف دراسية من مشروع تكاليف المشروع. اما قرية الشيوخ فسوف تساهم خدمات الاغاثة في توسيع وتعمير القرية الداخلية وتعمل طولها ١٠ كم وتزيد من طولها ١٠ كم

Implementing Development Projects in a number of Hebron District Villages

Hebron - Our Special Correspondent - Two agreements were signed yesterday to implement development projects in Zif and El-Shiyoukh villages - Hebron District with the participation of the Catholic Relief Services in Jerusalem. In Zif village, it was agreed to construct a primary co-educational school consisting of six classrooms with an area totalling 320 m2. The sub-project's total cost is about J.D. 23,000 of which CRS will participate in 65%.

In El-Shiyoukh village, the Catholic Relief Services will participate in widening and leveling the 3.5 kms long interior streets and in asphaltting a portion of 2 kms long. The costs are estimated by about J.D. 24,000. The Catholic Relief Services will share in 50% of the sub-project's total estimated cost.

This agreement was signed in the presence of some officials, the supervisor of rural projects at CRS, and representatives of Zif and El-Shiyoukh villages.

The Catholic Relief Services is also participating in implementing a number of vital projects in Hebron District. Work is now ongoing in implementing electrification projects in El-Kom, Beit Maqdom, El-Mureq, and Raqa' villages, and in opening a road linking El-'Idaiseh with Bani N'aim villages.

16

LOCATION OF SITES

01 APRIL 1987

* Nine Sub-Projects Completed (12, 13, 14, 17, 19, 20, 21, 22, 28)

+ Eleven Sub-Projects Ongoing (16, 23, 24, 25, 26, 29, 30a, 31, 32, 33, 34)

* Barta' & Khirbat Barta' (28)

+ 'Attil (26)

+ Shwaikah (23)

* Zbaidat (21)

* Jeet (13)


* Kufor Kaddum (12)

+ Huwara (33)

* Yatmah (22)

TEL AVIV - YAFO

BAT YAM

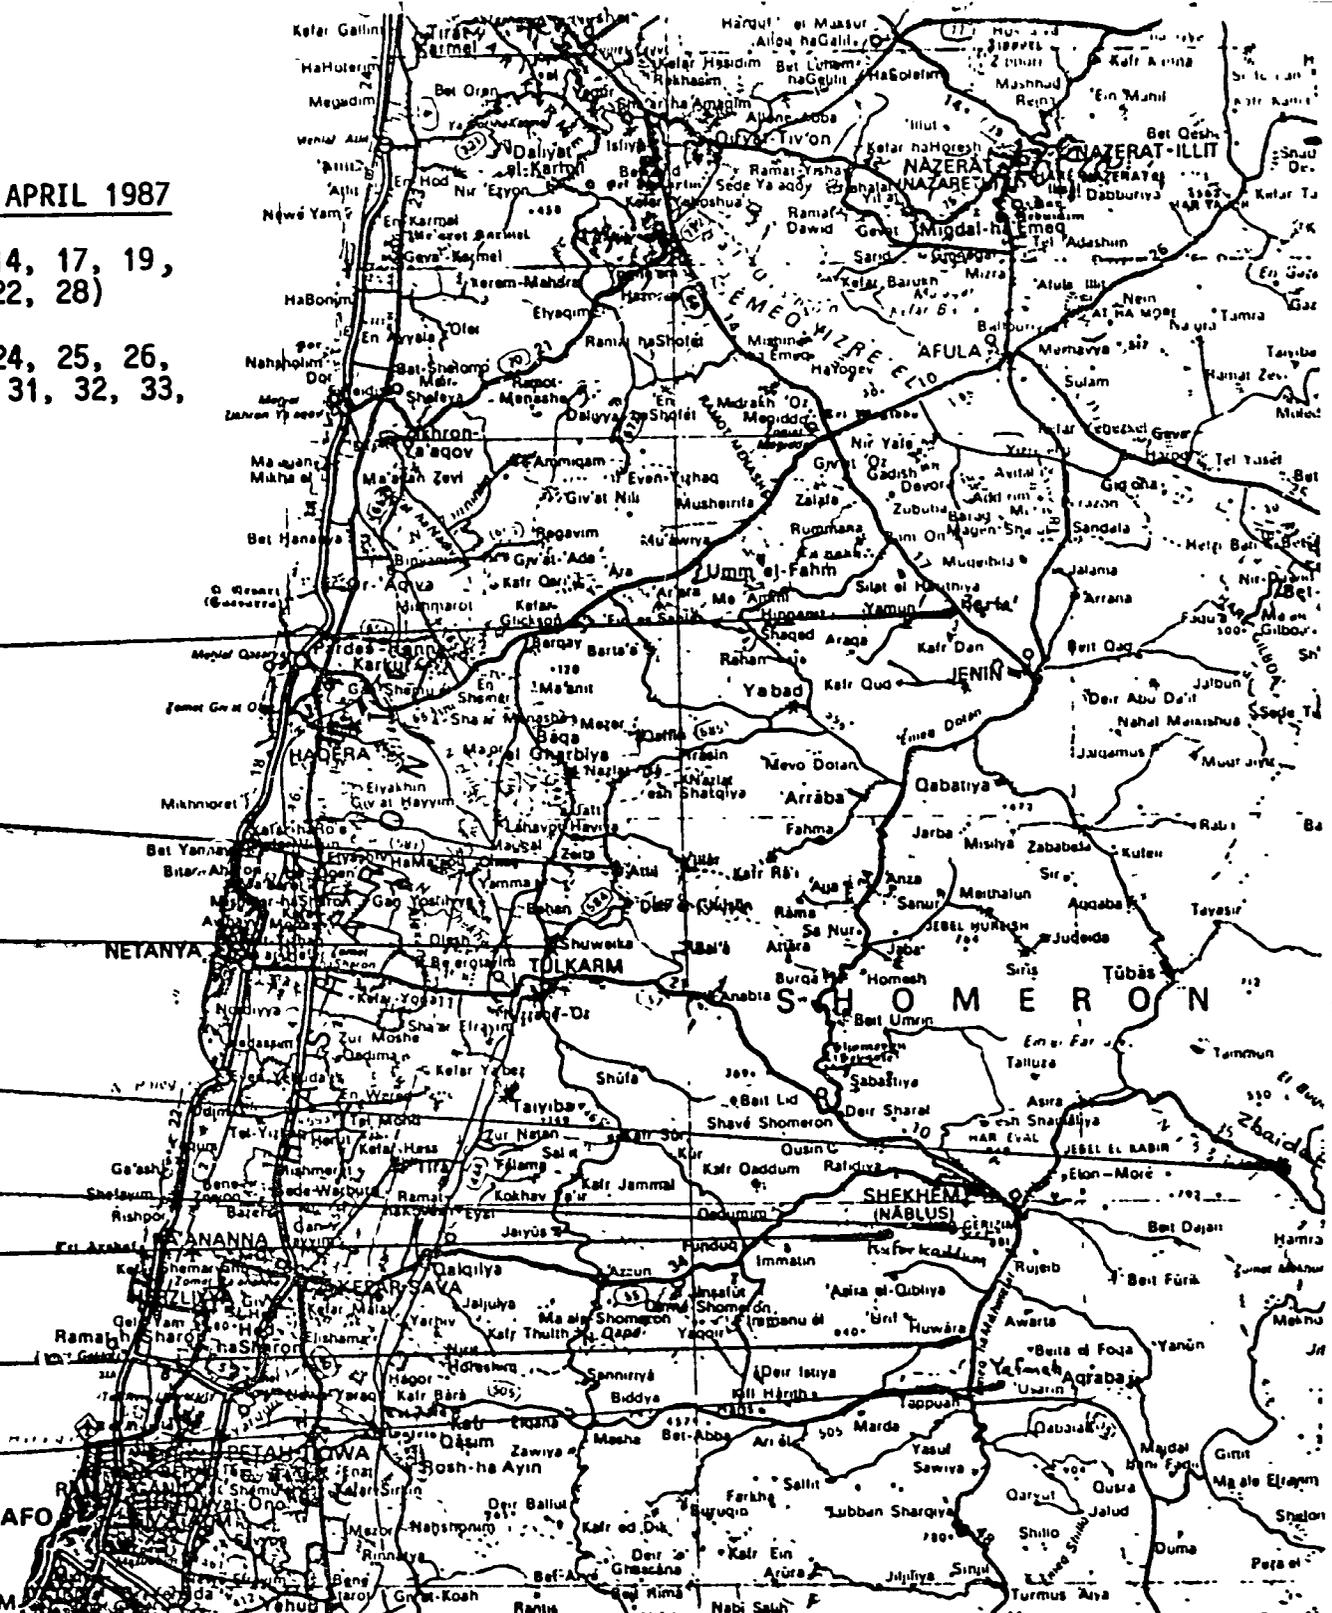

* Yatmah (22)

+ Surda (30a)

+ El-Shawawreh (31)

* Husan (14)

+ Beit 'Ummar (16)

+ El-Shiyoukh (29)

* Bani N'aim El-'Idaiseh (17)

* El-Mureq El-Kom (20)

+ Zif (32)


+ Beit Ei-Rush El-Foqa (24)

+ Beit El-Rush El-Tanta (25)

* Raqa' (19)

+ Shu' ab

Mu'smar (34)

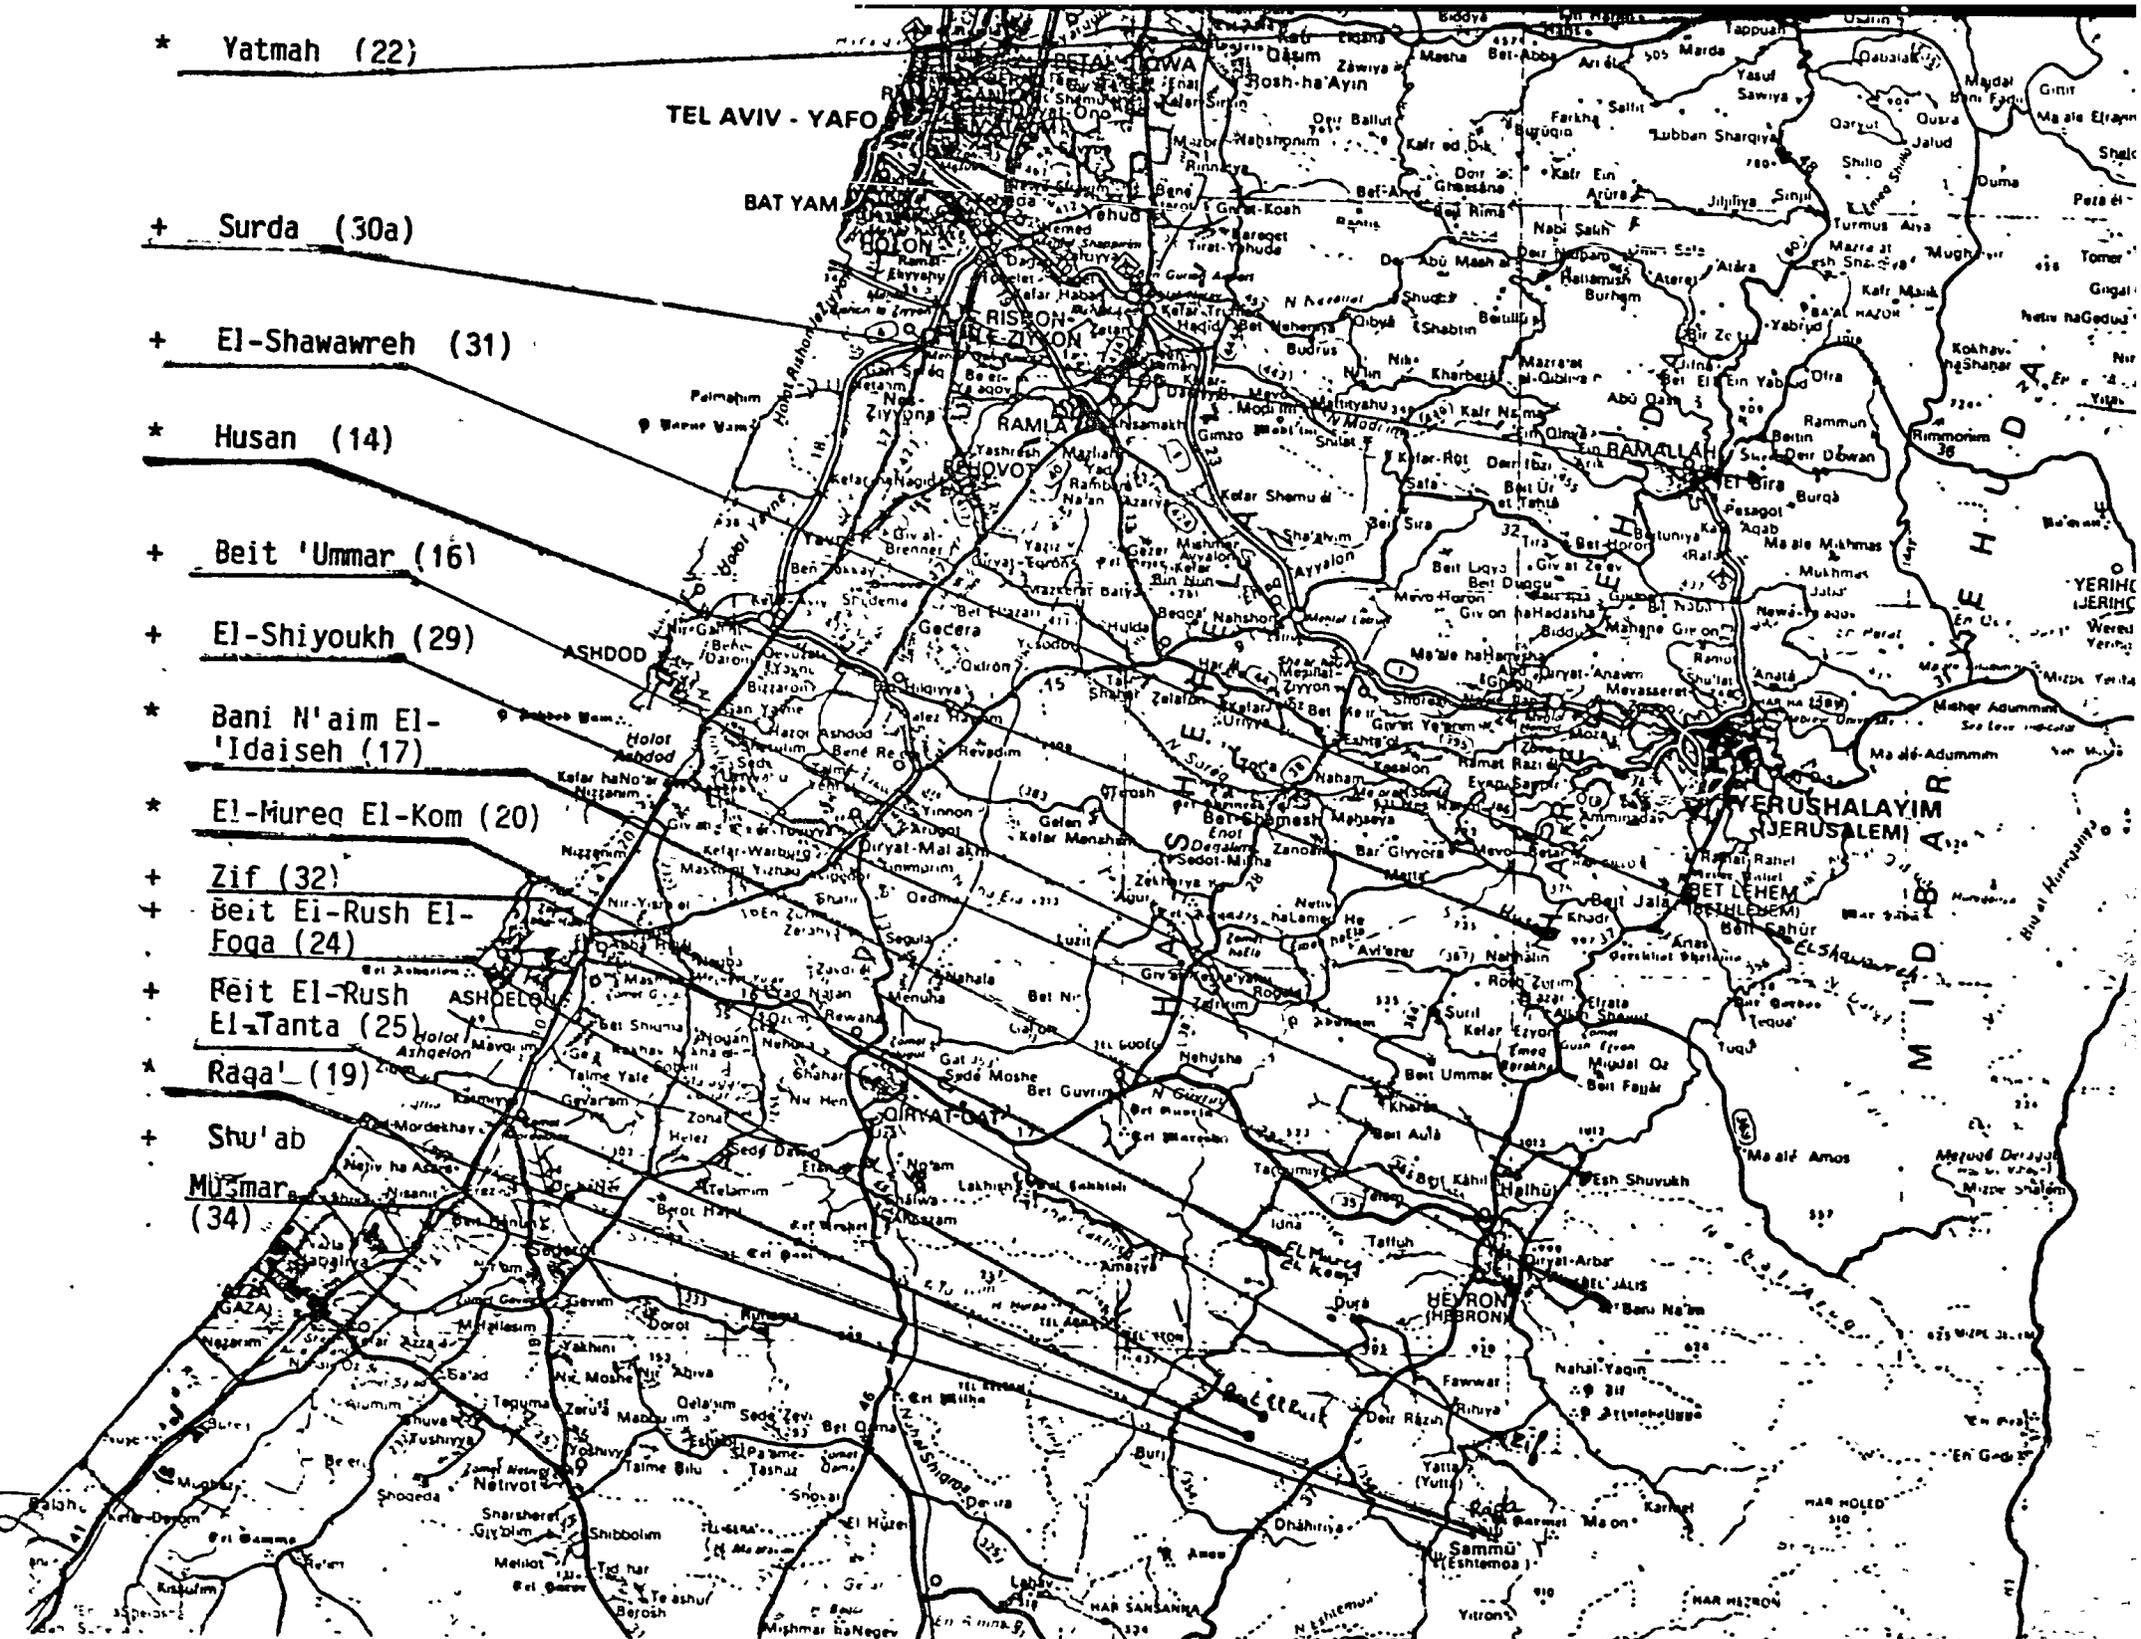

TEL AVIV - YAFO

BAT YAM

HOLON

RISHON LE-ZION

RAMLA

BE'ER SHEVA

ASHDOD

NETIV

BE'ER SHEVA

ASHDOD

YERUSHALAYIM (JERUSALEM)

BET LEHEM

HEBRON

HEBRON

HEBRON

HEBRON

HEBRON

MIDBAR

MIDBAR

MIDBAR

KUFOR KADDUM SUB-PROJECT

WATER SYSTEM

4D - 006 - 12

WORK BEGAN : 28 MAY 1986

COMPLETED : 27 MARCH 1987

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The agreement covering this sub-project was signed with the village leadership on 11 February 1986. Implementation started on 28 May 1986 and was successfully completed on 27 March 1987.
- The sub-project's final cost came to US \$ 106,253.94. The village's cash input amounted to \$ 53,457.71, equivalent to 50%, versus CRS/AID cash input of 52,796.23 which is also 50% of the total cost. Attached is a detailed and final statement of expenditures.
- This sub-project is a complete success. We were able to install a water system not only in the main streets as planned before, but also in the village alleys thus serving the entire population. This was made possible by saving on the implementation cost. We also had a Value Added Tax refund.
- The completed water system brought in sufficient potable water for all the villagers. They no longer have to cover long distances on foot to haul a small amount of polluted water on their heads and shoulders. Villagers no longer need to keep water standing in open containers where it could become contaminated. The general health should improve.
- The village will be responsible for the maintenance of the pipe line, backed-up by the West Bank Water Authority for major problems.
- Attached are photos showing the sub-project in its different phases of implementation.

EVALUATION

- Villagers now have an ample supply of clean, unpolluted potable running water to meet their various needs all the year round. The easy availability of water is the greatest factor encouraging higher standards of cleanliness.
- Women could now spend more time working in their houses and fields.
- Water projects are valuable investments in safe-guarding the quality of life.

GA/mf

22

ITEMIZATION OF EXPENDITURES

KUFOR KADDUM SUB-PROJECT 4D-006-12

DRINKING WATER SYSTEM

<u>ITEM</u>	<u>QUANTITY</u>	<u>TOTAL</u>
1. Galvanized 1/2" water pipes	3320m.	2,934.92
2. Galvanized 1" water pipes	5000m.	12,038.97
3. Galvanized 2" water pipes	2400m.	10,943.40
4. Galvanized 3" water pipes	1036m.	10,883.53
5. Galvanized 4" water pipes	1700m.	20,940.72
6. Stop Valves	35	261.95
7. Water Meters	235	13,418.87
8. Manholes	46	3,817.75
9. Digging & refilling trenches	-----	11,484.-
10. Washing the interior of the pipelines	-----	180.-
11. Reasphalting road crossings	-----	648.-
12. Connecting pipes with the main line	-----	433.22
13. Cement	10m3	1,110.-
14. Plumber	-----	10,823.44
15. Fitting Parts	-----	6,222.67
16. Photos	-----	112.50
Grand Total		\$ 106,253.94
		NIS 159,537.93
CRS SHARE 50%	=	\$ 52,796.23 = 79,581.97
VILLAGE SHARE 50%	=	\$ 53,457.71 = 955.96



جريدة يومية سياسية

JERUSALEM - ASHA'AB ARABIC DAILY NEWSPAPER

Sunday, 19 April 1987 No. 4676 Vol. 15

الاحد ١٩ نيسان ١٩٨٧م الموافق ٢١ شعبان ١٤٠٧هـ - العدد ٤٦٧٦

Thanks and Appreciation

to the Catholic Relief Services - Jerusalem

شكر وتقدير

الى خدمات الاغاثة الكاثوليكية في القدس

نابلس - كفر قدوم - نحن رئيس واعضاء مجلس كفر قدوم القروي وجميع اهالي القرية نتقدم بالشكر والتقدير الجزيلين الى السيد مدير خدمات الاغاثة الكاثوليكية ولجميع المسؤولين وخاصة الاخوة عيسى بركات وابراهيم سعادة والمهندس داود ابو جظم لما قاموا به تجاه القرية من مساعدات وتمديد شبكة مياه للقرية مما ادى الى تطور القرية وتقديمها من الناحيتين الاقتصادية والصحية.
جزاهم الله كل خير

مجلس كفر قدوم القروي

Nabius - Kufor Yaddum - we, the head and members of Kufor Yaddum village council and all the village inhabitants present our deep thanks and appreciation to the director of the Catholic Relief Services and to all the responsible persons and in particular the brothers Issa Barakat, Ibrahim Galaden, and the architect Galoud Abu Joudom, for the help they presented to the village, in installing an internal water net.

This lead to a development and progress in the village economical and hygienic fields.

May God reward them all the good.

Kufor Yaddum Village Council

gef

PHOTOS ILLUSTRATING SUB-PROJECT

KUFOR KADDUM - WATER SYSTEM

4D - 006-12

Total Cost : \$ 106,253.94
CRS Share : \$ 52,796.23 (50%)
Village Share : \$ 53,457.71 (50%)
Project Completed : 27 March 1987

25X




Kufor Kaddum villagers get their water from cisterns. This water reaches the cisterns through man-made ridges from courtyards along donkey and foot paths to be used for drinking, cooking, clearing, and washing. This is a major health hazard. Kufor Kaddum villagers were anxious to solve their problem.

(Above) A tractor filling-in the trenches with sand after the installation of the internal water net throughout the village.

(Below) All the members of a Kufor Kaddum family watching happily the clean, sufficient, potable, running water for the first time in their house. With this new system, the health status of the population will improve. →

24

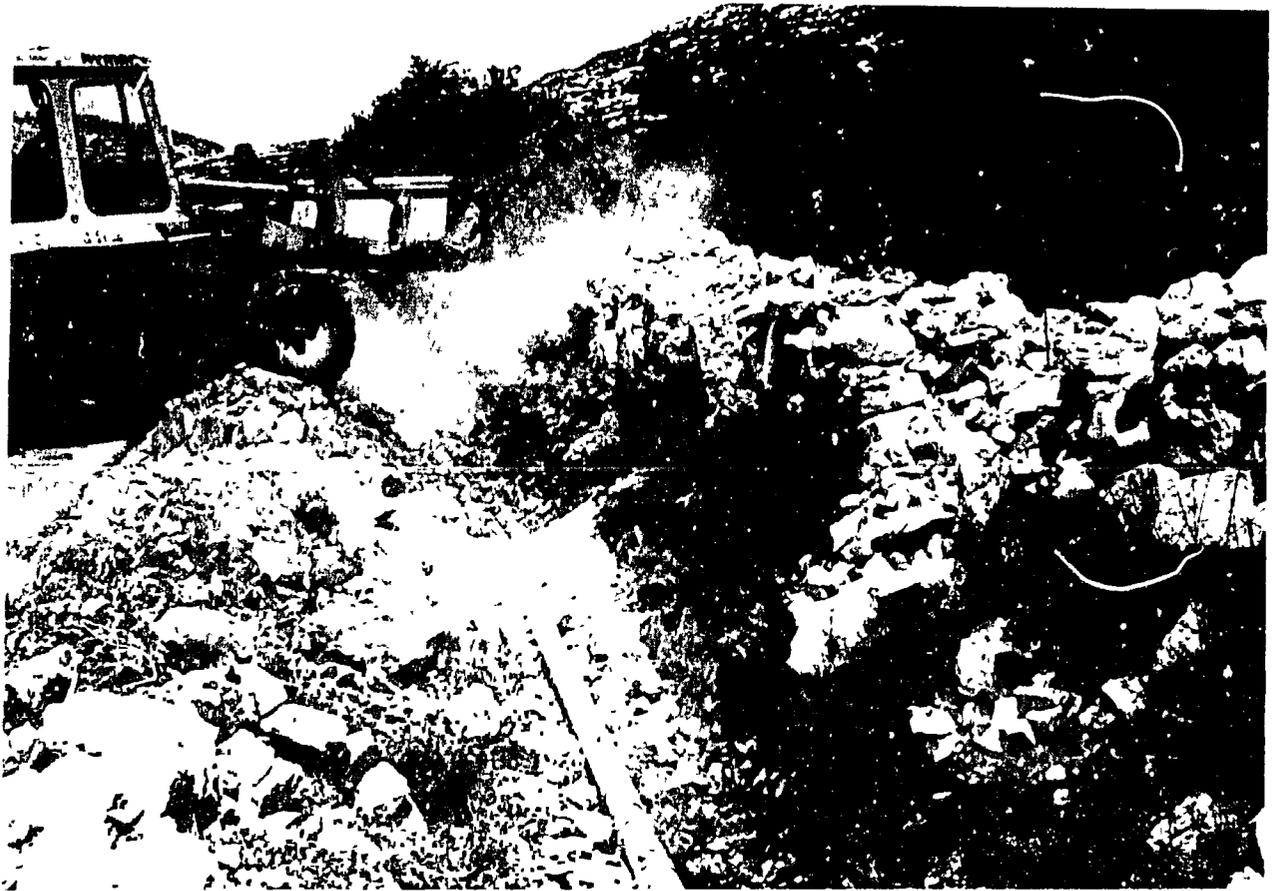

JEET SUB-PROJECT

WATER SYSTEM

4D - 006 - 13

WORK BEGAN : 02 JUNE 1986

COMPLETED : 18 DECEMBER 1986

JK

**CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK**

**RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FINAL SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT**

Date of Last report: 1 October 1986
Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-13
CRS-JWB/USAID Sub-Project No.

US \$ 53,028.-
Sub-Project estimated cost

CRS JWB in co-operation with JEET VILLAGE
Name of Operating Agency

DRINKING WATER SYSTEM
Title of Sub-Project

TULKAREM DISTRICT
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

(I) US \$ 31,817.- Equivalent to \$ 21,211.-
CRS AID cash input Village cash input

(II) US \$ 1,157,598.04 20 January 1987
Funds received to date Date of last transmittal

(III) CRS AID US \$ 31,816.25 Village US \$ 23,575.61
Sub-Project expenditure (s) to date

(IV) CRS AID US \$ 0 75 Village US \$ (2,364.61)
Balance (s) unused (Overspent)

Cooperation of the West Bank Water Authority in rendering technical services free of charge, Tax exemption on pipes, Villages expressed a good sense of cooperation.

(V) Other inputs which contributed to success of Sub-Project

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project involved establishing a potable drinking water system throughout Jeet village, linking it with the main line of the West Bank Water Authority.
- The agreement was signed with the village leadership on 11 February 1986. Work started on 2 June 1986 and the sub-project was successfully completed on 18 December 1986. Implementation was delayed due to a strike in the Water Pipes Factory.
- The sub-project's final cost came to U.S. \$ 55,391.86. The village's cash input amounted to \$ 23,575.61 equivalent to 43%, versus CRS/AID cash input of \$ 31,816.25, which is 57% of the total cost. Attached is a detailed final statement of expenditures.
- The completed water system brought in sufficient potable water for all the villagers. They no longer have to cover long distances to haul small amounts of polluted water on their heads and shoulders. Now they can get water at any time they want and in whatever amount they need. With running water in the houses, the general health of the population should improve.
- Beneficiaries of this sub-project are the entire Jeet villagers (1500 persons).
- All the village inhabitants contributed to the village's share of the sub-project's costs.
- Attached are photos showing the sub-project in its different aspects of implementation.

EVALUATION

- Jeet water problem is solved. Instead of having to use the non-potable cistern water, villagers now have piped in sufficient potable water. There are no longer any water shortages in the village.
- The easy availability of water is the greatest factor encouraging higher standards of cleanliness.
- Village women spend more time taking care of their houses and children, and working in the fields.
- Water projects are valuable investments in safe-guarding the quality of life.

GA/mf

ITEMIZATION OF EXPENDITURES
JEET SUB-PROJECT 4D - 006 -13

DRINKING WATER SYSTEM

<u>I T E M</u>	<u>QUANTITY</u>	<u>TOTAL (\$)</u>
1. Galvanized 3" water pipes	800 m	8,022.10
2. Galvanized 2" water pipes	1660 m	9,775.53
3. Galvanized 1" water pipes	2348 m	5,546.62
4. Galvanized 1/2" water pipes	2498 m	3,112.83
5. Water Meters	145	9,682.82
6. Digging and refilling trenches		9,775.-
7. Reasphalting Road Crossings		156.-
8. Washing the interior of the pipelines		90.-
9. Plumber		2,564.03
10. Manholes	33	1,267.50
11. Cement	15 m3	2,493.-
12. Fitting Parts		2,735.-
13. Photos		171.43
Grand Total		\$ 55,391.86 NIS 81,535.23

CRS SHARE 57% = \$ 31,816.25 = NIS 46,887.17

VILLAGE SHARE 43% = \$ 23,575.61 = NIS 34,648.06

Translation

Jeet 04 December 1987

The respectable director of The Catholic Relief Services and his respectable assistances - Jerusalem

Thanks and appreciation

We, the mukhtars, representatives, and villagers of Jeet village - Tulkarem District, present the deep thanks and appreciation to the Catholic Relief Services in Jerusalem represented in its director and in Mr. Issa Barakat and his respectable assistances for the precious help that the association presented for the water project in our village. Without their help, this great sub-project would have never been achieved.

No one can deny the importance of water in human life. It is of the first requirements of any city, village, or community, for it is used in the various household requirements, and in irrigating the gardens and decorating the streets, and in the cattle and animals watering.

Our village has suffered from water insufficiency especially during summer season. For this, the sub-project will help in solving the village's water problem and in developing and embellishing our village. People will care more in cleanliness, which raises the inhabitants hygiene standards.

For this, we reassure our thanks to the Catholic Relief Services represented in its director, and in Mr. Issa Barakat and his assistances for their vital participation in implementing this sub-project and in achieving this dream which we have been longing for several years. We used to watch the signs of development and progress invading the surrounding villages, while we were deprived from this great rejoice.

To this association and those who operate it, we present many thanks and appreciation .

Please accept our deepest regards.

GA/lb

PHOTOS ILLUSTRATING SUB-PROJECT

JEET - WATER SYSTEM

4D - 006 - 13

Total Cost :	\$ 55,391.86	
CRS Share :	\$ 31,816.25	(57%)
Village Share :	\$ 23,575.61	(43%)
Project Completed :	18 December 1986	

The unavailability of clean, running water was a major problem hindering the development of Jeet village - Tulkarem District.

Village women had to walk several times to the nearest cistern to haul small amounts of polluted water on their heads or on donkey backs. Jeet villagers decided to solve their water problem with the help of CRS-AID. →



Photo shows workers installing water pipes in the village after the digging of the trenches.

These two girls and all of Jeet villagers now enjoy for the first time having piped-in, clean, potable water in their houses.

They will use water in sufficient quantities to bath, and to properly clean their food, clothes, and houses. Thus the health status of the population should improve. →



HUSAN SUB-PROJECT

PRIMARY SCHOOL

4D - 006 - 14

WORK BEGAN : 02 MAY 1986

COMPLETED : 25 NOVEMBER 1986

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FINAL SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of Last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-14
CPS-JWB/USAID Sub-Project No.

US. \$ 39,029.14
Sub-Project estimated cost

CRS JWB in co-operation with HUSAN VILLAGE
Name of Operating Agency

PRIMARY SCHOOL
Title of Sub-Project

BETHLEHEM DISTRICT
Area in which Sub-Project is located

NER-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 19,514.57 Equivalent to \$ 19,514.57
(I) CRS AID cash input Village cash input

US \$ 1,157,598.04 20 January 1987
(II) Funds received to date Date of last transmittal

CPS AID US \$ 19,501.41 Village US \$ 23,146.44
(III) Sub-Project expenditure (€) to date

CPS AID US \$ 13.16 Village US \$ (3,631.87)
(IV) Balance (s) unused (Overspent)

The strong willingness of the villagers to cooperate with CRS. Tiling and pointing were done by village volunteers, Tax exemption on construction materials.

Other inputs which contributed to success of Sub-Project.

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The agreement covering this sub-project was signed with the village leadership on 9 April 1986. Implementation started on 2 May 1986 and was successfully completed on 25 November 1986. The internal part of the building was completed by the end of September 1986 and put into use immediately.
- The sub-project final cost came to U.S. \$ 42,647.85. The village's cash input amounted to \$ 23,146.44, equivalent to 54% versus CRS/AID cash input of \$ 19,501.41, which is 46% of the total cost. Attached is a detailed final statement of expenditures.
- This sub-project involved the construction of additional classrooms for Husan's School. After obtaining the approval of the Education Department and CRS, villagers decided to roof the basement to be used as additional classrooms in case of any future need. This increased the village's share in the costs.
- Villagers expressed a good sense of responsibility. They worked together and cooperated with CRS in achieving this vital sub-project despite the difficulties they met while collecting village's share. All the tiling (262 m²) and pointing (175 m²) were done by village volunteers, who were so much encouraged and proud by this sub-project.
- This sub-project improved Husan's level of education. Proper classrooms are now available replacing the inadequate and inappropriate quarters. Husan and the neighbouring villages students will have more opportunity to go to school. Money paid by the village for renting the old classes would be saved. Students are much satisfied with the new, healthy, well ventilated classrooms.
- The Education Department furnished the new classrooms and provided the necessary teaching staff and text-books.
- Attached are photos showing different aspects of sub-project implementation.

EVALUATION

- This sub-project contributes to the Overall Goal of the Grant which is development of Rural West Bank Arab Villages.
- The educational facilities in a rural area of Bethlehem District have been improved.
- The new rooms replaced inadequate and inappropriate quarters. The school will also serve the boys of the two neighbouring villages of Wadi Fukkin and Nahhalin.

GA/mf

ITEMIZATION OF EXPENDITURES

HUSAN SUB-PROJECT 4D - 006 - 14

PRIMARY SCHOOL

<u>I T E M</u>	<u>QUANTITY</u>	<u>TOTAL \$</u>
1. Cement	27 Tons	2,310.43
2. Cement Blocks	116 m3	6,462.17
3. Gravel, Powdered	75 Bags	975.-
Mixed	21 Loads	1,680.63
Fine	7 Loads	736.55
4. Sand	12 Loads	1,227.02
5. Concrete	73 m3	3,057.95
6. Limestone	7 Bags	204.08
7. Building Stones	1171 m	5,041.42
8. Water	300 m3	228.04
9. Roofing Iron	12 Tons	7,931.01
10. Tiles	250 m	1,262.84
11. Iron Doors	5	545.-
12. Aluminium Windows	21 m	1,090.73
13. Excavator	(by job)	2,310.50
14. Mason	312 m2	6,032.16
15. Electrician	35 pts	119.05
16. Plasterer	834 m2	1,147.16
17. Miscellaneous		286.11
Grand Total		----- \$ 42,647.85
		NIS 63,093.83

CRS SHARE 46% - \$ 19,501.41 - NIS 28,838.27

VILLAGE SHARE 54% - \$ 23,146.44 - NIS 34,255.56

GA/1b

PHOTOS ILLUSTRATING SUB-PROJECT

HUSAN - PRIMARY SCHOOL

4D - 006 - 14

TOTAL COST : \$ 42,647.85
CRS SHARE : \$ 19,501.41 (46%)
VILLAGE SHARE: \$ 23,146.44 (54%)
PROJECT COMPLETED : 25 November 1986



Representatives of CRS - JWB, Bethlehem Education Department, and Husan village, in a meeting discussing the sub-project.


413x

The boys' school in Husan village was jammed. Students have to study in rented, scattered rooms away from the school. CRS-AID agreed to help the village in constructing additional classrooms. Photo shows the process of constructing the foundations. →



Photo shows students attending a class in one of the newly constructed rooms. The new classrooms are well lit, ventilated, and beautifully constructed.

Here is seen the completed new building. After obtaining the approval of CRS and the Education Department, villagers roofed the basement on their own expense, to be used as additional classrooms. →

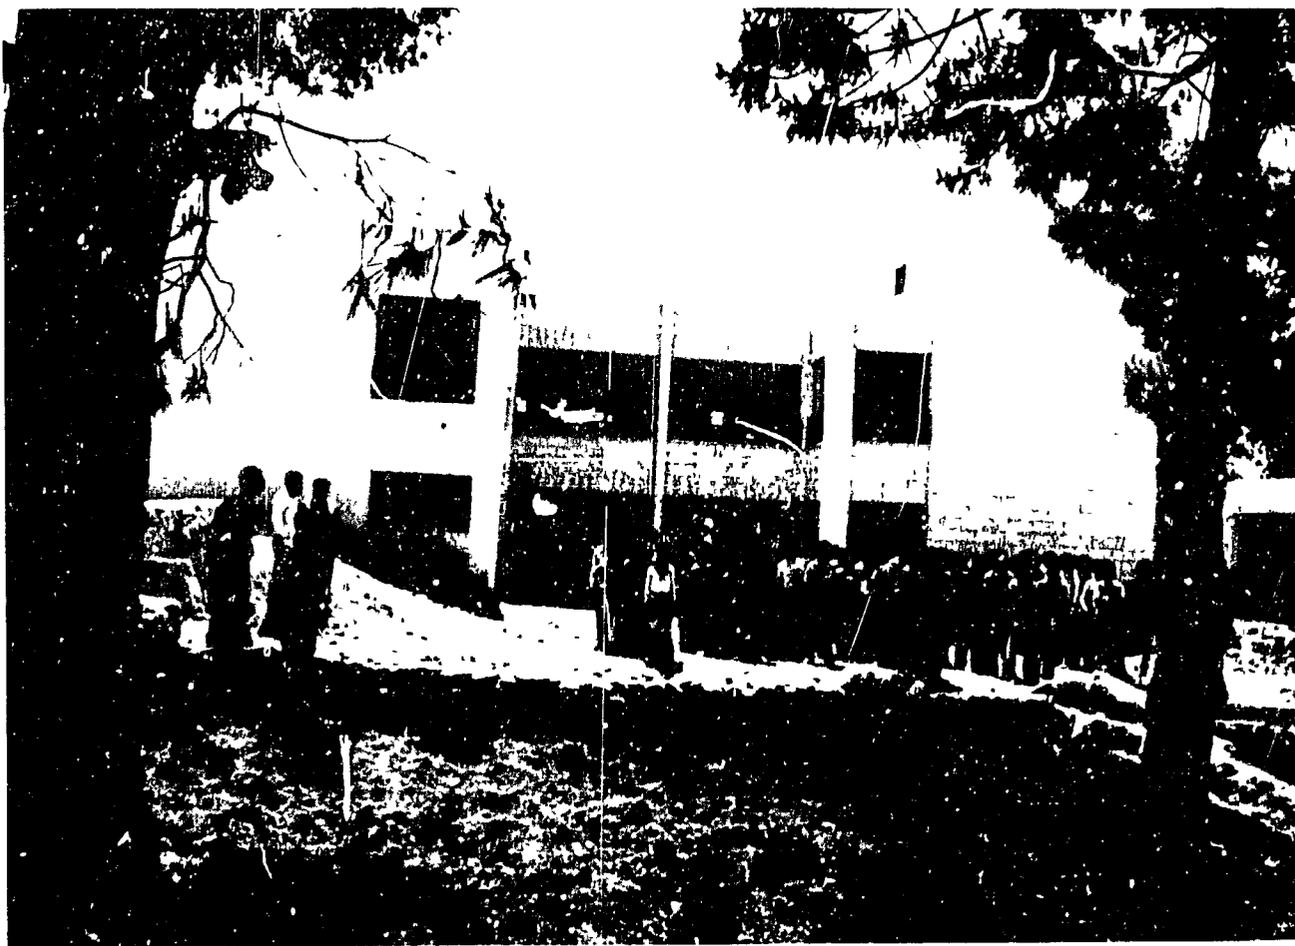

BEIT 'UMMAR SUB-PROJECT

AGRICULTURAL ROADS

4D - 006 -16

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
SECOND SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of Last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-16 . US. \$ 81,071 .
CRS-JWR/USAID Sub-Project No. Sub-Project estimated cost

CRS JWB in co-operation with BEIT 'UNMAR VILLAGE .
Name of Operating Agency

AGRICULTURAL ROADS .
Title of Sub-Project

HEBRON DISTRICT .
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00 .
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 40,535.50 . Equivalent to \$ 40,535.50 .
(I) CRS AID cash input Village cash input

US \$ 1,157,598.84 20 January 1987 .
(II) Funds received to date Date of last transmittal

CRS AID US \$ - Village US \$ 27,502.49 .
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 40,535.50 Village US \$ 13,033.01 .
(IV) Balance (s) unused (Overspent)

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project involves opening, clearing, and leveling an agricultural access road about 8 kms. long by 5 meters wide.
- Implementation was delayed due to the fact that the Village Council was very busy in solving some financial problems and other problems related with the Academic Year. CRS staff and village committee convinced with difficulty some villagers to give part of their lands to the projected road.
- The road is now completely opened. The villagers are reconstructing the retaining walls on their own expense. The road foundations are expected to be constructed soon.
- The village committee is working very hard and its members are very cooperative with CRS / JWB.
- The sub-project is expected to be completed by the end of May 1987.

GA/sk.

**BANI N'AIM EL-IDAISEH SUB-PROJECT
AGRICULTURAL ROAD**

4D - 006 -17

WORK BEAGN : 07 JULY 1986

COMPLETED : 11 FEBRUARY 1987

**CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK**

**RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FINAL SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT**

Date of Last reports: 1 October 1986
Date of This reports: 1 April 1987

1. REFERENCE SECTION

4D-886-17
CRB-JWB/USAID Sub-Project No.

US. \$ 60,629.-
Sub-Project estimated cost

CRS JWB in co-operation with BANI N'AIM - EL-'IDAISEH
Name of Operating Agency

AGRICULTURAL ROAD
Title of Sub-Project

HEBRON DISTRICT
Area in which Sub-Project is located

NEB-0159-C-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 36,377.- Equivalent to \$ 24,252.-
(I) CRS AID cash input Village cash input

US \$ 1,157,598.04 20 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ 36,342.70 Village US \$ 24,421.07
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 34.30 Village US \$ (169.07)
(IV) Balance (s) unused (Overspent)

Villagers donated parts of their lands which were in the way of the projected road.

Other inputs which contributed to success of Sub-Project.

50

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The agreement covering this sub-project was signed with the villag leadership on 18 June 1986. Implementation started on 7 July 1986 and was successfully completed on 11 February 1987.

- The sub-project's final cost came to U.S. \$ 60,763.77. The village's cash input amounted to \$ 24,421.07 equivalent to 40%, versus CRS/AID cash input of \$ 36,342.70, which is 60% of the total cost. Attached is a detailed final statement of expenditures.

- The village committee cooperated very well with CRS. Some problems arose while widening the road. Finally, the land owners were persuaded to donate parts of their lands for the project.

- The agricultural access road links Bani N'aim with El Idaiseh and leads to the quarry. It is now possible for the villagers to make and sell stones to other villages as well as to Jordan. This will increase the villagers income and improve their living standards.

- Existing lands and groves will be more intensively worked, and some new fields will be opened to cultivation for the first time. New groves will be planted.

- Bani N'aim and El 'Idaiseh villagers have better access to their fields. They are able to get their agricultural produce to Hebron and other towns while fresh, to be either sold locally or exported to Arab countries. Prior to this sub-project, farmers used to commute to their fields and groves either on foot or by donkey. Now, more produce reaches market quickly, enabling the farmers to get a higher return.

- Attached is a thanks & appreciation note to CRS published in one of the local newspapers in addition to some photos showing the sub-project in its different aspects of implementation.

51

Evaluation

- The road contributes to the overall Grant Goal which is development of Rural West Bank Arab Villages.
- Farmers have access to their fields all year round. Loss and damage of crops is reduced, enabling the farmers to get a higher return on their produce.
- As the road leads to the quarry, villagers will be able to make and sell stones thus increasing their income.
- Existing lands and groves will be better cultivated, and new fields will be reclaimed for the first time.
- The Agriculture Department can easily visit the village fields for extension work and advice.

GA/sk.

ITEMIZATION OF EXPENDITURES

BAIN N'AIM - EL-'IDAISEH SUB-PROJECT (4D - 006 - 17)

AGRICULTURAL ROAD

<u>I T E M</u>	<u>QUANTITY</u>	<u>TOTAL (\$)</u>
1. Bulldozer	285 hrs.	10,091.11
2. Grader	14 days	5,972.97
3. Rolling Machine	6 days	1,050.94
4. Excavator	228 hrs.	9,619.13
5. Compressor	10 days	751.70
6. Dumping Truck	14 days 120 Loads	3,085.81 2,485.95
7. Assorted Gravel	4987 cubes	11,459.01
8. Mixed Gravel	462 Loads	8,083.-
9. Water	8 Tanks	1,508.07
10. Skilled & unskilled Labourers' wages	459 work days	6,521.08
11. Photos		135.-
Grand Total		----- \$ 60,763.77 NIS 91,785.62

CRS SHARE 60% = \$ 36,342.70 NIS 55,686.94

VILLAGE SHARE 40% = \$ 24,421.07 NIS 36,098.68

N.B. Labourers wages were charged to the village.

THANKS AND APPRECIATION
TO THE
CATHOLIC RELIEF SERVICES
JERUSALEM



El'Idaiseh, Sa'ir, Bani N'aim
Hebron.

We the Mukhtar, villagers,
Farmers, and quarries owners
in El-Idaiseh and Bani Na'im
villages, present our deep
thanks to the director of the
Catholic Relief Services for
the great assistance that he
offered to the 5 kms long
agricultural road sub-project
that links El-'Idaiseh and
Bani N'aim with surrounding
villages. Without this
assistance the sub-project
would have never been achieved.

We are now able with the help of
this vital agricultural road to
reach our houses and fields
easily after that walking and
transporting on this road was
difficult.

شكر وتقدير
إلى خدمات الإغاثة الكاثوليكية في القدس
العديسة، سعيدة، بني نعيم - الخليل - نحن مختار وإهالي قرية
العديسة وبزازعي وأصحاب المحاجر فيها وفي بني نعيم نتقدم بالشكر
إلى السيد مدير خدمات الإغاثة للمساعدة الكبيرة التي قدمها لمشروع
الخط الزراعي الذي يربط العديسة وبني نعيم وبالقري من حولنا بطول
وكم الإزاهم بدون هذه المساعدة ما كان للمشروع أن يتم من حولنا بطول
لقد أصبحنا بفضل هذا الخط الزراعي والخوض نصل إلى بيوتنا
وحقولنا بكل يسر بعد أن كان السير والتنقل على هذا الخط عسيراً
كما ساعدتنا هذه الطريق في نقل متعلقاتنا الزراعية إلى الأسواق دون
صعوبة الأمر الذي يعود على المزارعين بالخير بعد أن كانت تنقلاتنا
تذهب هدراً.
كما نتقدم بالشكر إلى جميع المسؤولين في لسم المشاريع ونخص بالذكر
الإخ ابراهيم سعادة (أبو حنا) على ما قام به أثناء التنفيذ من جهد
وتضحية دون أن ننساها.
حفظ الله السيد المدير وأبناؤه دخرنا لكل عمل خير.

عن العشيرتين

مختار قرية العديسة والخرب المجاورة
محمد دعدوش جرادات و ابراهيم خليل الخضور

34

The road also helped in transporting our agricultural products to the markets without difficulty, the thing that has good effects on the farmers, while previously all our efforts were worthless.

We present our thanks also to all the responsible people at the Project Section and we single out Mr. Ibrahim Sa'adeh (Abu Hanna) for the unforgettable efforts and sacrifices that he expressed during implementation.

May God protect the director and keep him a support for every good deed.

For the two tribes,

The Mukhtar of El-Idaiseh village and the surrounding Khirabs.

Mohammad Da'doush Jaradat
and Ibrahim Khalil El-Khdour.

GA/mf

PHOTOS ILLUSTRATING SUB-PROJECT
BANI N'AIM - EL 'IDAISEH - AGRICULTURAL ROAD
4D - 006 - 17


Total Cost :	\$ 60,763.77	
CRS Share :	\$ 36,342.70	(60%)
Village Share :	\$ 24,421.07	(40%)
Project Completed :	11 February 1987	


Bani N'aim - El 'Idaiseh agricultural road was in a very bad condition. Farmers used to reach their fields and groves either on foot or donkeys. This meant that only a small amount of produce could be transported at a time. CRS-AID agreed to help the village in widening, clearing, and leveling the agricultural access road. →

Photo shows a section of the agricultural road in the process of constructing the road foundations.


Here is a view of the very same section of the road shown above now converted into a proper road (a highway as referred to by the villagers). Loss and damage of crops is now reduced enabling the farmers to get a higher return. →

57

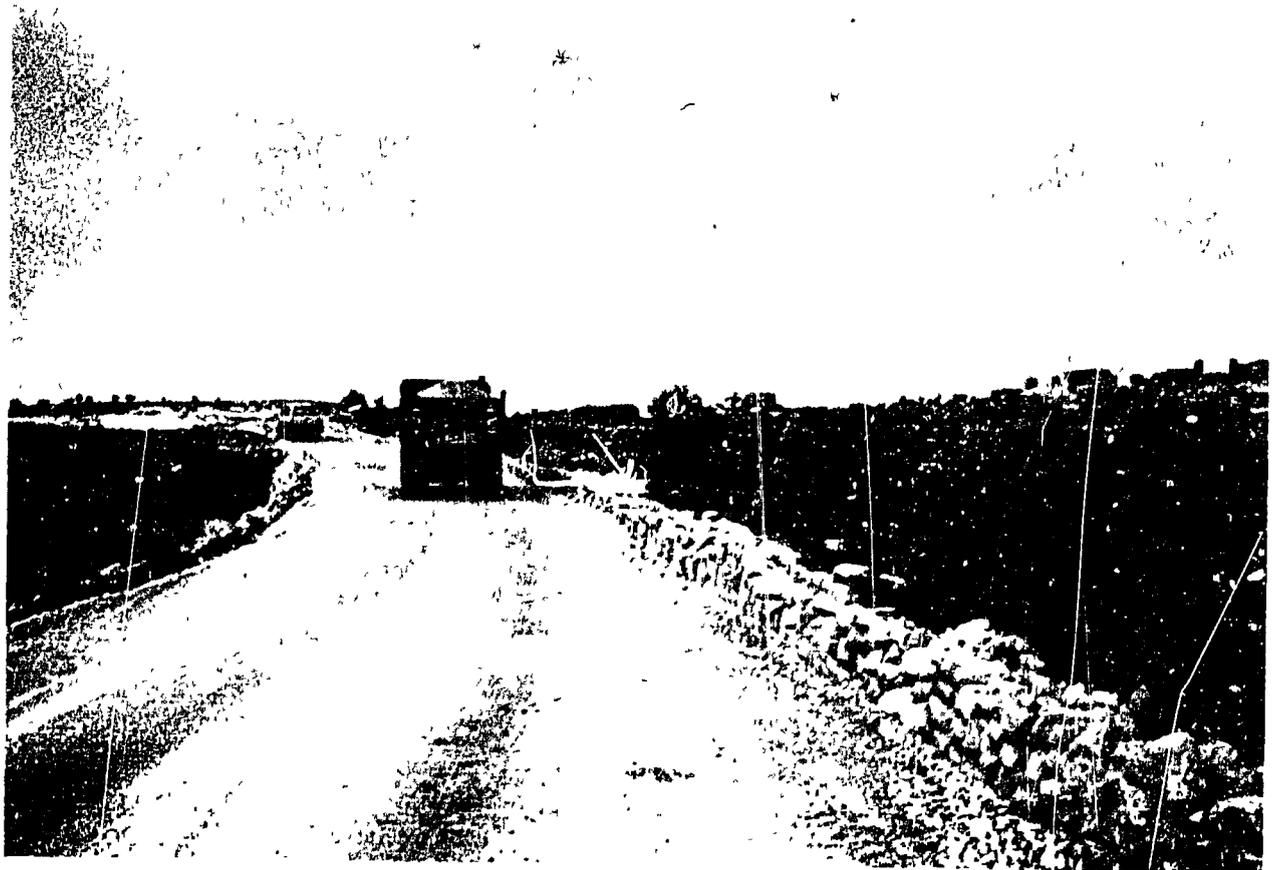

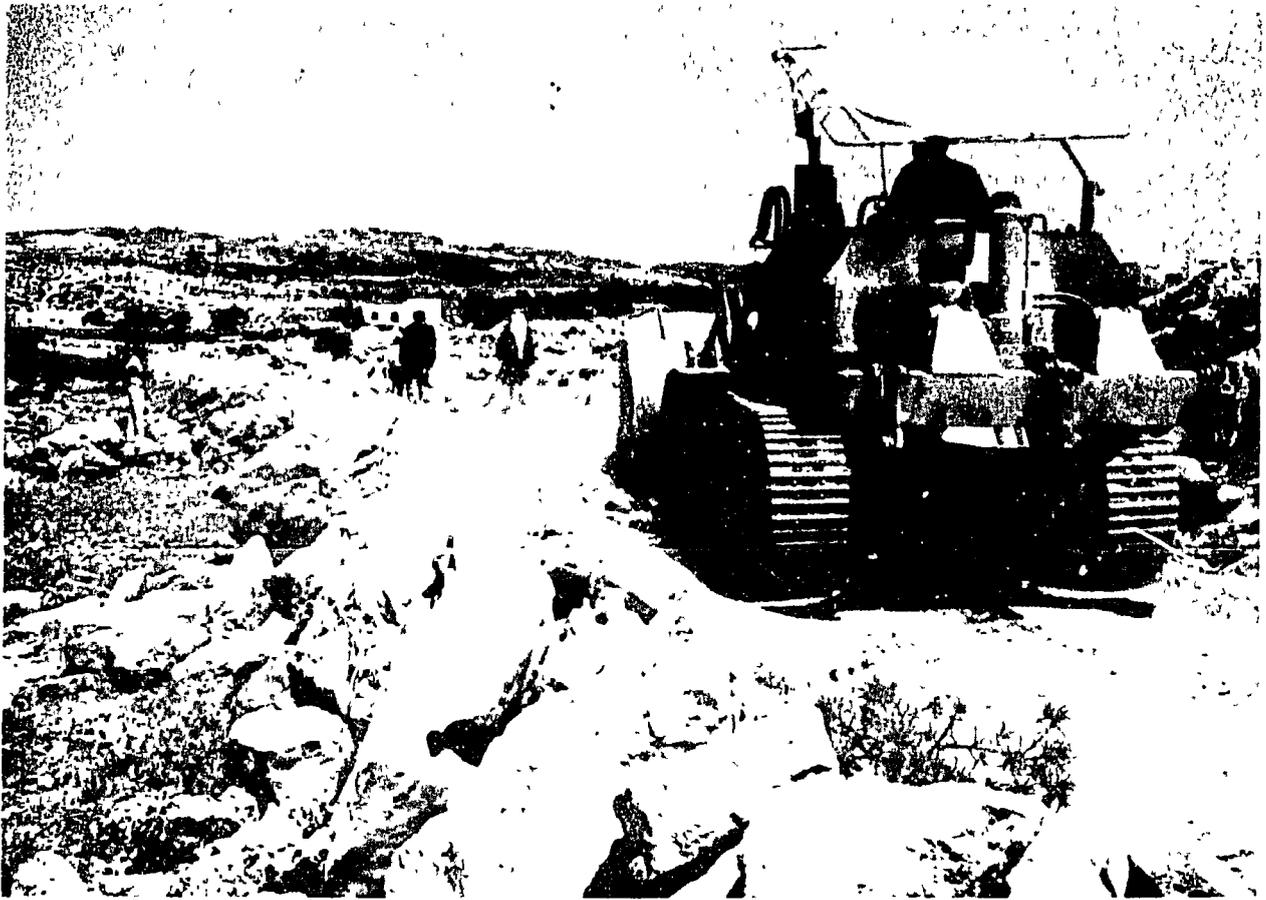

Members of Bani N'aim village committee inspecting work during the widening and leveling stages.

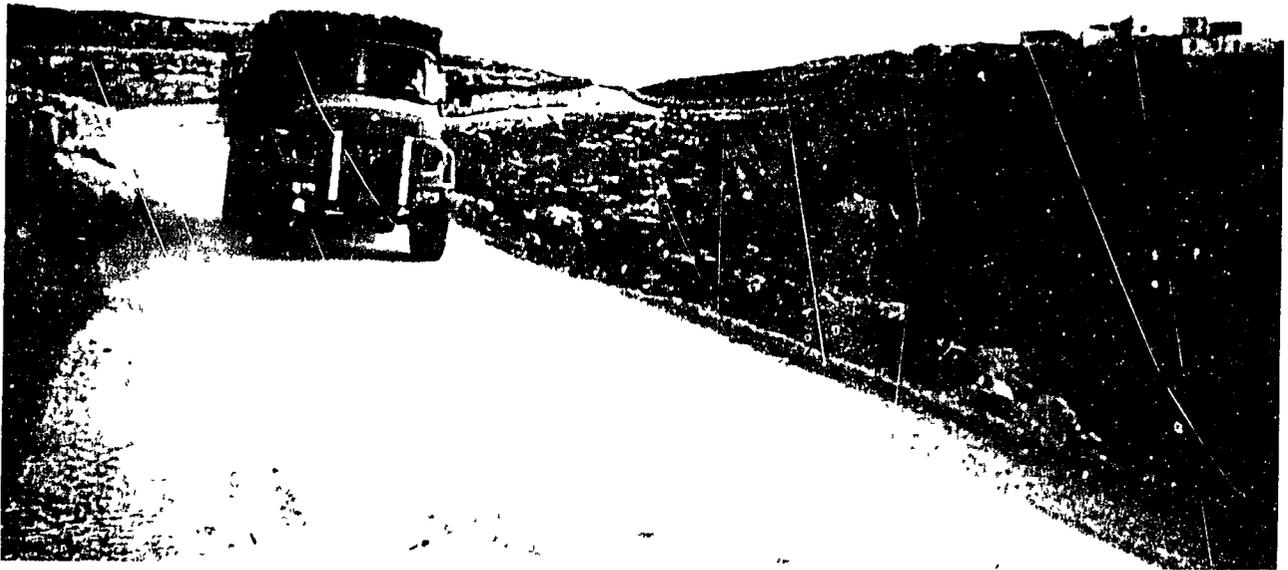

The same section of the road seen on opposite page, after the completion of implementation.

The agricultural road links Bani N'aim with El 'Idaiseh and leads to the quarry. It is now possible for the villagers to make and sell stones to other villages as well as to Jordan. This will increase the villagers income and improve their living standards.

RAQA' SUB-PROJECT

ELECTRIFICATION

4D - 006 -19

WORK BEGAN : 01 AUGUST 1986

COMPLETED : 12 FEBRUARY 1987

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FIRST SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of Last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-886-19
CRS-JWB/USAID Sub-Project No.

US. \$ 98,666.-
Sub-Project estimated cost

CRS JWB in co-operation with RAQ'A VILLAGE
Name of Operating Agency

ELECTRIFICATION
Title of Sub-Project

HEBRON DISTRICT
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 59,200.-
(I) CRS AID cash input Equivalent to \$ 39,466.-
Village cash input

US \$ 1,157,598.04
(II) Funds received to date 20 January 1987
Date of last transmittal

CRS AID US \$ 59,179.37
(III) Sub-Project expenditure (to) to date Village US \$ 39,572.37

CRS AID US \$ 20.63
(IV) Balance (s) unused Village US \$ (106.37)
(Overspent)

The strong willingness of Raq'a villagers to work together and to cooperate with CRS in achieving this vital Sub-Project. Tax exemption on electrical parts.

(V) Other inputs which contributed to success of Sub-Project.

62

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- The agreement covering this sub-project was signed with the village leadership on 18 June 1986. Implementation started on 1 August 1986, and was successfully completed on 12 February 1987.
- This sub-project involved providing Raq'a village - Hebron District with an internal electrical network plus its facilities and accessories.
- The final cost amounted to \$ 98,751.74. The village's share came at \$ 39,572.37, equivalent to 40% of the total costs. CRS-AID share came at \$ 59,179.37, which is 60% of the total costs. The attached statement of final expenditures gives a clear idea of the final cost.
- Raq'a villagers are waiting for the District Authorities to connect the village with the main line of the West Bank Electrical Power. The West Bank Power Officer insisted that the villagers should pay \$ 30,000 in order to extend the main line to their village. The village committee started collecting money from the inhabitants.
- All of Raq'a villagers contributed toward their share of the sub-project's costs.
- Beneficiaries of this sub-project are the entire village population i.e. 4,000 people.
- The attached photos show some of the aspects of this sub-project.

EVALUATION

=====

- Providing Raq'a village with an electricity system contributes to the Overall Goal of the Grant which is the development of underdeveloped rural Arab West Bank villages.

- When Raq'a is connected with the main line, villagers will enjoy the benefit of having refrigerators for long-term food storage. School children will be able to study in well-lighted rooms and houses, rather than the light of kerosene lanterns, which is dim and can be detrimental to sight. Household electrical appliances may then be used in each house. Electric machines could replace manual ones. This will increase productivity and raise the standard of living. Villagers hope that the improved facilities will prompt young people to stay in or return to the village.

GA/mf

6f

ITEMIZATION OF EXPENDITURES

RAQ'A SUB-PROJECT 4D - 006 -19

ELECTRIFICATION

<u>ITEM</u>	<u>QUANTITY</u>	<u>TOTAL</u>
1. Distribution Tower	1	3182.39
2. Aluminium Rods	10780 kgs.	30872.69
3. Wooden Poles (8.5m)	101	9,874.51
4. Wooden Poles (10m)	88	12,427.24
5. Electrical Bridges	240	3,000.-
6. Screws (4.5cm)	900	1,074.06
7. Screws (8cm)	1360	2,164.03
8. Brackets	25	2,023.44
9. Earth Sets	50	1,790.10
10. Street Lamps	100	7,160.38
11. Conductors		1,717.50
12. Isolators	1800	1,406.25
13. Line Tape	1720m	3,170.63
14. Accessories including U. Shapped holders, iron rods and bars, etc...		3,998.52
15. Digging holes for Poles	(by Job)	6,312.16
16. Electrician	(by Job)	6,937.57
17. Engineer		1,520.27
18. Photos		120.-
Grand Total	\$	98,751.74
	NIS	146,995.14

CRS share 60% = \$ 59,179.37 NIS. 88,550.09

Village Share 40% = \$ 39,572.37 NIS. 58,445.05

GA/sk.


65

PHOTOS ILLUSTRATING SUB - PROJECT
RAQ'A - ELECTRIFICATION
4D - 006 - 19

Total Cost :	\$ 98,751.74	
CRS Share :	\$ 59,179.37	(60%)
Village Share :	\$ 39,572.37	(40%)
Project Completed :	12 February 1987	

66X

Raq'a villagers were living in darkness. Lack of electricity hindered village development. Photos show different parts of the village after the installation of the internal electrical network. The village could never be able to do this vital sub-project without CRS-AID help. →

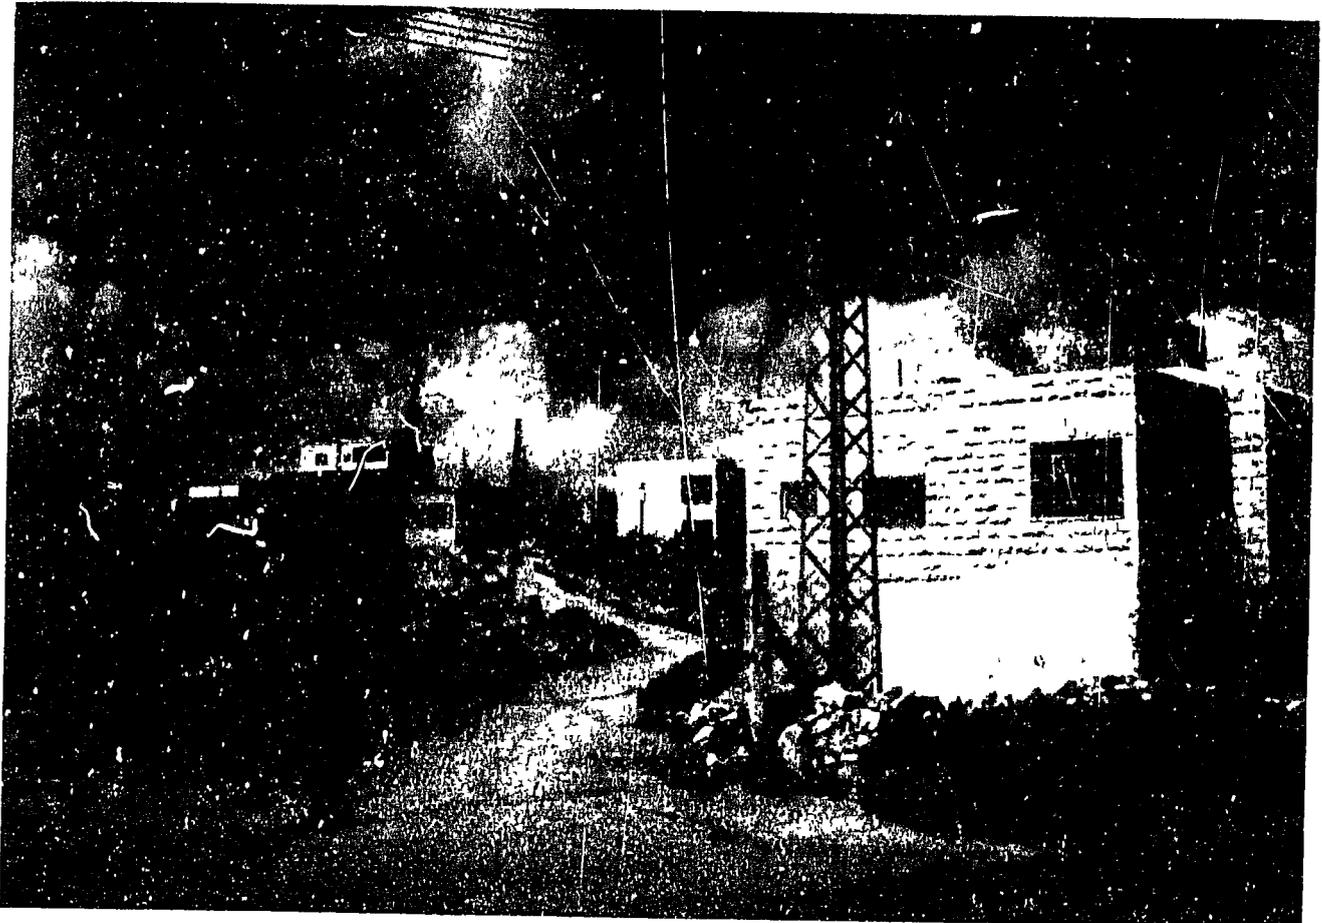

Raq'a's main electrical transmission tower after being installed.

67



EL MUREQ EL-KOM SUB-PROJECT
ELECTRIFICATION

4D - 006 -20

WORK BEGAN : 20 AUGUST 1986

COMPLETED : 27 MARCH 1987

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FINAL SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of Last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-20
CRS-JWB/USAID Sub-Project No.

US, \$ 119,500
Sub-Project estimated cost

CRS JWB in co-operation with EL-MUREQ - EL KOM VILLAGES
Name of Operating Agency

ELECTRIFICATION
Title of Sub-Project

HEBRON DISTRICT
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

.US \$ 71,700 Equivalent to \$ 47,000
(I) CRS AID cash input Village cash input

. US \$ 1,157,598.04 20 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ 71,667.79 Village US \$ 49,122.66
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 32.21 Village US \$ (1322.66)
(IV) Balance (s) unused (Overspent)

Tax Exemption on Electrical Parts. The villagers strong willingness to help themselves and work together. They donated the piece of land on which the distribution board's room was constructed.

Other inputs which contributed to success of Sub-Project.

70

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project involved providing El-Mureq, El-Kom, and Beit Maqdoum villages with an internal electrical network plus its facilities and accessories.
- The agreement was signed with the village leadership on 18 June 1986. Work started on 20 August 1986 and the sub-project was successfully completed on 27 March 1987.
- The final cost amounted to \$ 120,790.45. The village's share came to \$ 49,122.66 equivalent 41% of the total costs, versus CRS/AID cash input of \$ 71,667.79 which is 59% of the total cost. Attached is a detailed final statement of expenditures.
- In order to connect the village with the main line of the West Bank Electrical Power, the West Bank Power Officer asked the villagers to pay \$ 30,000. Eager to have electricity for the first time in their villages, the inhabitants started to raise the required sum despite their difficult financial situation. El-Mureq El-Kom and Beit Maqdoum committees will then run the system and will be responsible for its upkeep and maintenance.
- Villagers are extremely happy. They are confident that electricity will give life to their village.
- All the villagers have contributed toward their share of the costs, and all of them will benefit of this sub-project.
- The attached photos show some of the aspects of this sub-project.

EVALUATION

=====

- Providing El-Mureq, El-Kom and Beit Maqdoum with an internal electrical network contributes to the overall goal of the Grant which is the development of underdeveloped rural Arab West Bank villages.
- When the three villages are connected with the main line, villagers will enjoy an excellent electricity system. Students will be able to study in well-lighted rooms. Food and goods will be stored in refrigerators. Electrical machines will replace manual ones. Economic activities will increase in the village.

GA/mf

72

ITEMIZATION of EXPENDITURES

EL MUPEQ - EL KOM SUB-PROJECT 4D-006-20

ELECTRIFICATION

<u>I T E M</u>	<u>QUANTITY</u>	<u>TOTAL (\$)</u>
1. Electric Transmission Tower	1	1,571.43
2. Distribution Board	1	2,803.13
3. Transformer	1	3,548.12
4. Central Earth	-	1,175.--
5. Wooden Poles (10m)	150	20,860.73
6. Wooden Poles (8.5m)	80	779.44
7. Isolators	1500	3,214.29
8. Aluminium Wires	2765 kgs	6,843.12
9. Aluminium Rods (25&95ml)	5250 kgs	14,850.--
10. Aluminium Rods (50ml)	1000 kgs	2,828.58
11. U - Shaped	1500	3,107.15
12. Screws (8cm)	1000	1571.43
13. Screws (4.5cm)	1500	1767.86
14. Conductors	1130	10,835.72
15. Brackets	15	1,339.29
16. Electric Bridges	250	3,571.43
17. Full Earth Sets	60	2,121.43
18. Street Lamps	100	7,071.43
19. Mixed Gravel	2 Loads	300.71
20. Cement	8 Bags	493.50
21. Iron	450 Kgs	276.13
22. Iron Door	1	234.04
23. Accessories	---	5,985.45
24. Electrician	---	7,284.61
25. Engineer	---	1,920.36
26. Layouts	---	1,023.92
27. Digging holes	430 holes	8,693.48
28. Constructing Tower	(by Job)	722.05
29. Constructing Distribution Board Room	(by Job)	936.15
30. License Fees	---	2,925.47
31. Photos	---	135.--

Grand Total

\$ 120,790.45

NIS 188,149.26

CRS SHARE 59% = \$ 71,667.79 = NIS 111,939.54

VILLAGE SHARE 41% = \$ 49,122.66 = NIS 76,209.72

73

PHOTOS ILLUSTRATING SUB-PROJECT
EL-MUREQ EL-KOM - ELECTRIFICATION
4D - 006 - 20

TOTAL COST : \$ 120,790.45
CRS SHARE : \$ 71,667.79 (59%)
VILLAGE SHARE : \$ 49,122.66 (41%)
PROJECT COMPLETED : 27 March 1987

74/7

El-Mureq`El-Kom and Beit Maqdoum villagers were living in darkness.lack of electricity hindered development. Villagers were eager to improve their living conditions. →

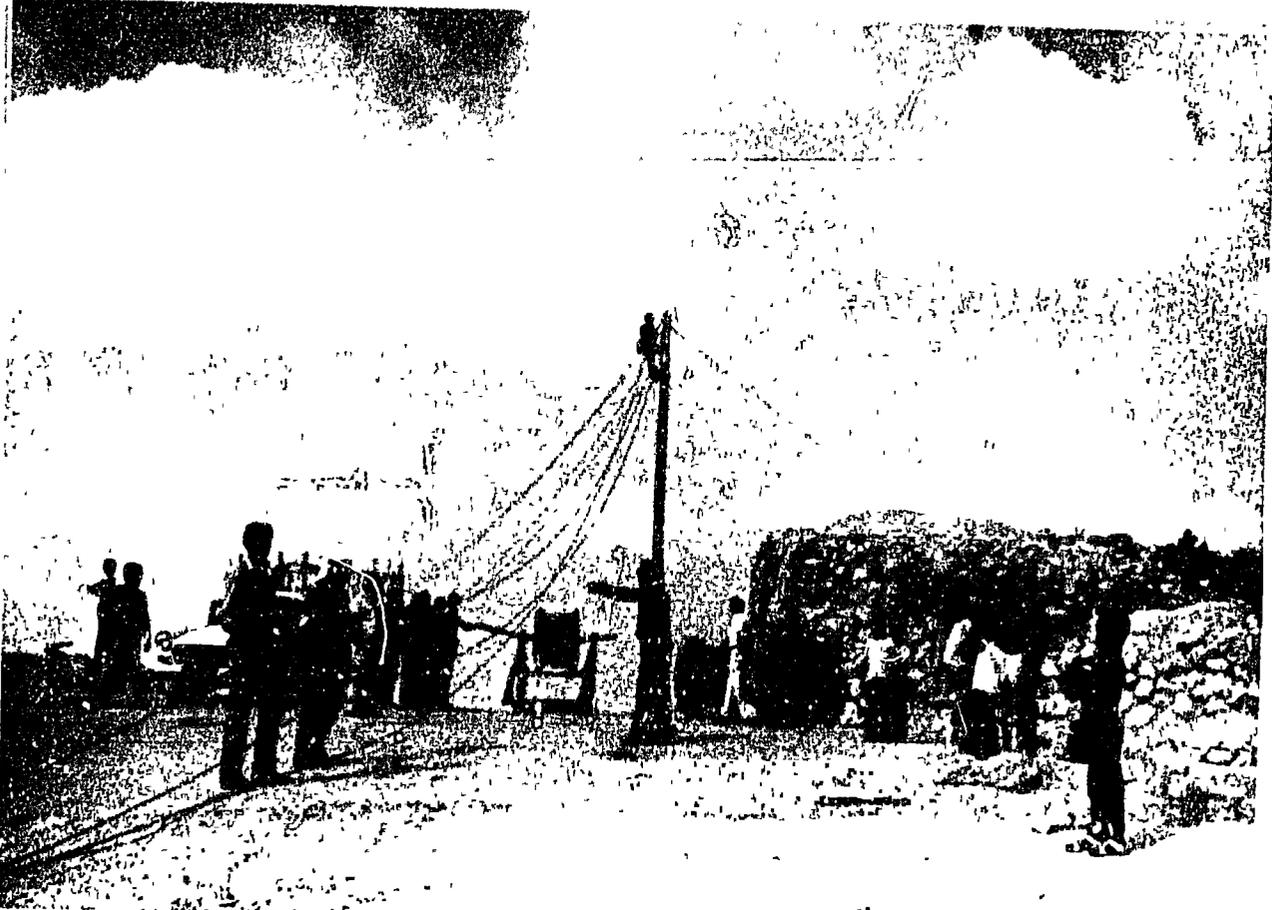



Photo shows work during the installation of the internal electrical network

The same part of the village seen in photo above, after installing the network. When the villages are connected with the main line, villagers will enjoy an excellent electricity system. →

75




10

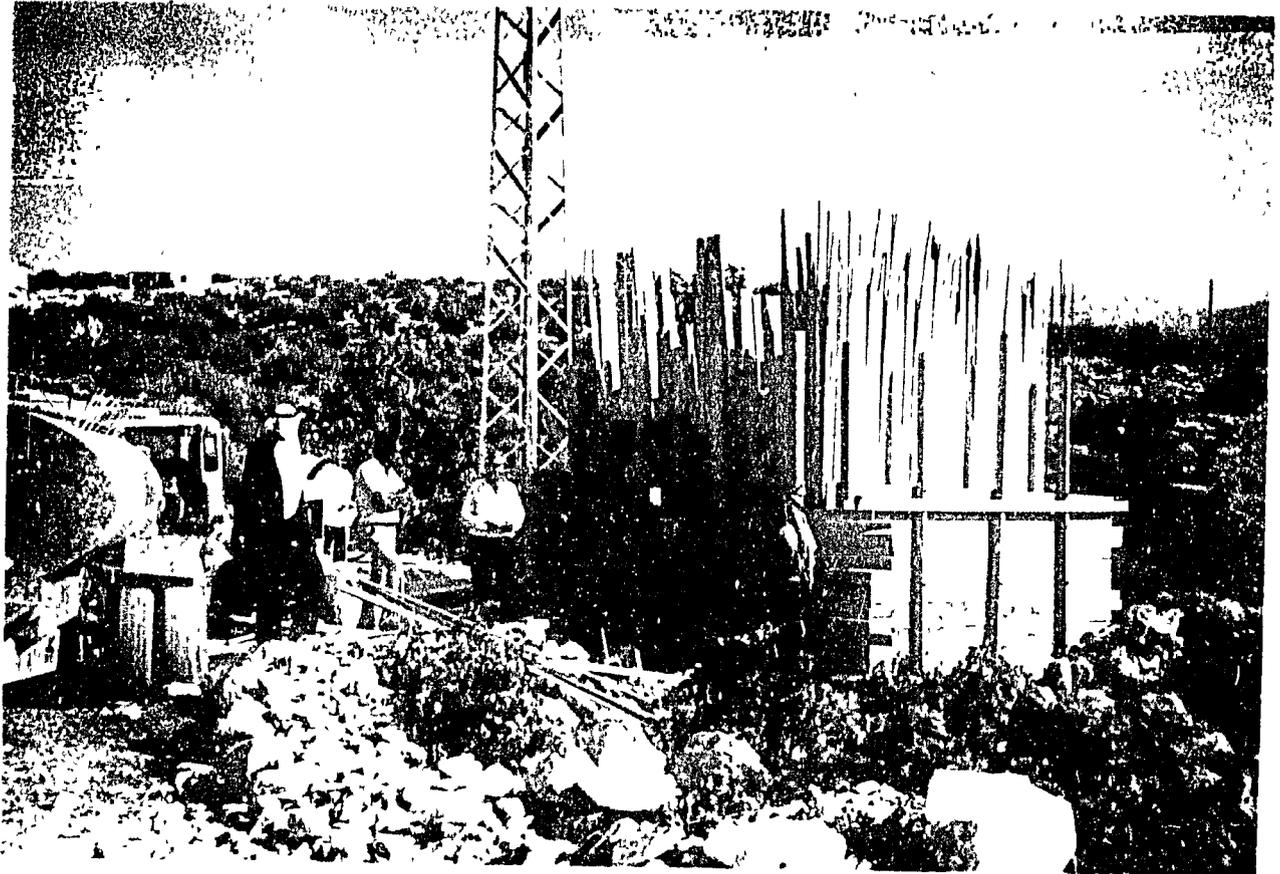

CRS JWB Field Supervisor inspecting work during the construction of the distribution board's room.

71

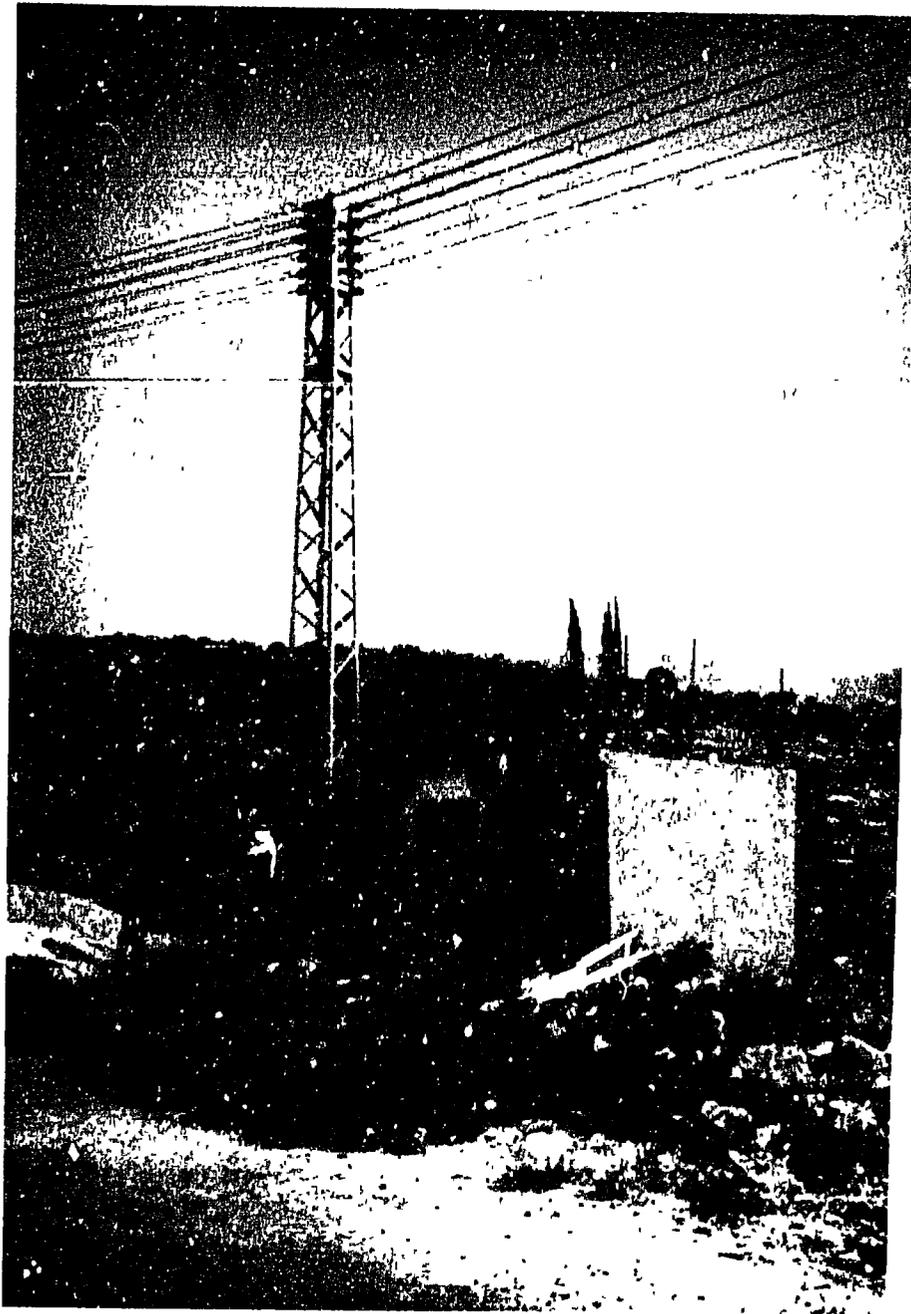

El-Mureq, El-Kom, and Beit Maqdoum's main transmission tower and the completed distribution board's room.

ZBAIDAT SUB-PROJECT

ELECTRIFICATION

4D - 006 -21

WORK BEAGN : 08 OCTOBER 1986

COMPLETED : 20 JANUARY 1987

**CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK**

**RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FINAL SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT**

Date of Last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

<u>4D-006-21</u> CRS-JWB/USAID Sub-Project No.	<u>US \$ 34,283.-</u> Sub-Project estimated cost
CRS JWB in co-operation with	<u>ZBAIGAT VILLAGE</u> Name of Operating Agency
	<u>ELECTRIFICATION</u> Title of Sub-Project
	<u>JERICO DISTRICT</u> Area in which Sub-Project is located
	<u>NEB-0159-G-SS-5123-00</u> Funding Agency Code Number

2. EXPENDITURE SECTION

<u>US \$ 22,284.-</u> (I) CRS AID cash input	<u>Equivalent to \$ 11,999.-</u> Village cash input
<u>US \$ 1,157,598.84</u> (II) Funds received to date	<u>20 January 1987</u> Date of last transmittal
<u>CRS AID US \$ 22,270.12</u> (III) Sub-Project expenditure (s) to date	<u>Village US \$ 12,137.29</u>
<u>CRS AID US \$ 5.88</u> (IV) Balance (s) unused	<u>Village US \$ (138.29)</u> (Overspent)

Villagers cooperated with CRS and raised their share despite the village's difficult economic situation.

Other inputs which contributed to success of Sub-Project.

80

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project involved providing Zbaidat village - Jericho District - with a transformer, an electrical distribution board, an electrical transmission tower, and an internal electrical network throughout the village.
- The agreement was signed with the village leadership on 23 June 1986. Work started on 8 October 1986 and the sub-project was successfully completed on 20 January 1987.
- The final cost amounted to \$ 34,415.41. The village's share came to \$ 12,137.29 equivalent to 35% of the total costs, versus CRS/AID cash input of \$ 22,278.12 which is 65% of the total cost. Attached is a detailed final statement of expenditures.
- The West Bank Power Officer asked the villagers to pay \$ 12,000 in order to connect their village with the main line of the West Bank. This was a very heavy burden on the village committee as the village is facing a very difficult financial situation.
- All the villagers contributed toward their share of the costs.
- Beneficiaries of this sub-project are all the villagers (1200 persons).
- The attached photos show some of the aspects of this sub-project.

EVALUATION

=====

- This sub-project contributes to the Overall Goal of the Grant which is development of rural West Bank Arab Villages.
- The specific objective of this sub-project to provide Zbaidat with an internal electrical network has been achieved.
- Electricity, when available, will certainly develop the village and raise the standard of living. Electrical appliances and machines will be introduced. All the inhabitants and in particular students and housewives will enjoy a more promising and encouraging life.
- Electricity will then be used for irrigation, instead of the old diesel pump which so often becomes out of order, as a result of which great amounts of vegetables are usually damaged and lost.

GA/mf

82

ITEMIZATION OF EXPENDITURES

ZBAIDAT SUB-PROJECT (4D - 006 - 21)

ELECTRIFICATION

<u>I T E M</u>	<u>QUANTITY</u>	<u>TOTAL (\$)</u>
1. Wooden Poles (10m)	25	2,756.22
2. Wooden Poles (8.5m)	35	2,673.92
3. Aluminium Rods	1650	3,689.44
4. Electrical Transmis- sion Tower	1	1,242.24
5. Electrical Distribu- tion Board	1	4,350.93
6. Street Lamps	35	1,956.53
7. Accessories including U-Shapped, Iron, Screws Conductors, etc..		13,168.83
8. Electrician Installing Network		2,599.37
9. Engineer		1,880.43
10. Photos		97.50
Grand Total		<u>34,415.41</u>
		NIS 54,052.30

CRS SHARE 65% = \$ 22,278.12 NIS 35,339.80
VILLAGE SHARE 35% = \$ 12,137.29 NIS 18,712.50

GA/1b

83

PHOTOS ILLUSTRATING SUB-PROJECT

ZBAIDAT - ELECTRIFICATION

4D - 006 - 21

Total Cost : \$ 34,415.41
CRS Share : \$ 22,278.12 (65%)
Village Share : \$ 12,137.29 (35%)
Project Completed : 20 January 1987



CRS-JWB Rural Development Supervisor, Social Welfare representative, and Zbaidat village committee signing the agreement at the Military Governor's office.

if X


The poor village of Zbaidat never had electricity in its history. Villagers were living in darkness. They badly needed an electricity system as the lack of electricity hindered their village development. The village could never do this vital sub-project alone without CRS-AID help.



Photo shows work during the installation of the internal electrical network, after that the wooden poles were placed.

The same part of the village seen in photo above, after installing the network. Electricity, when available, will develop the village and raise the standard of living.



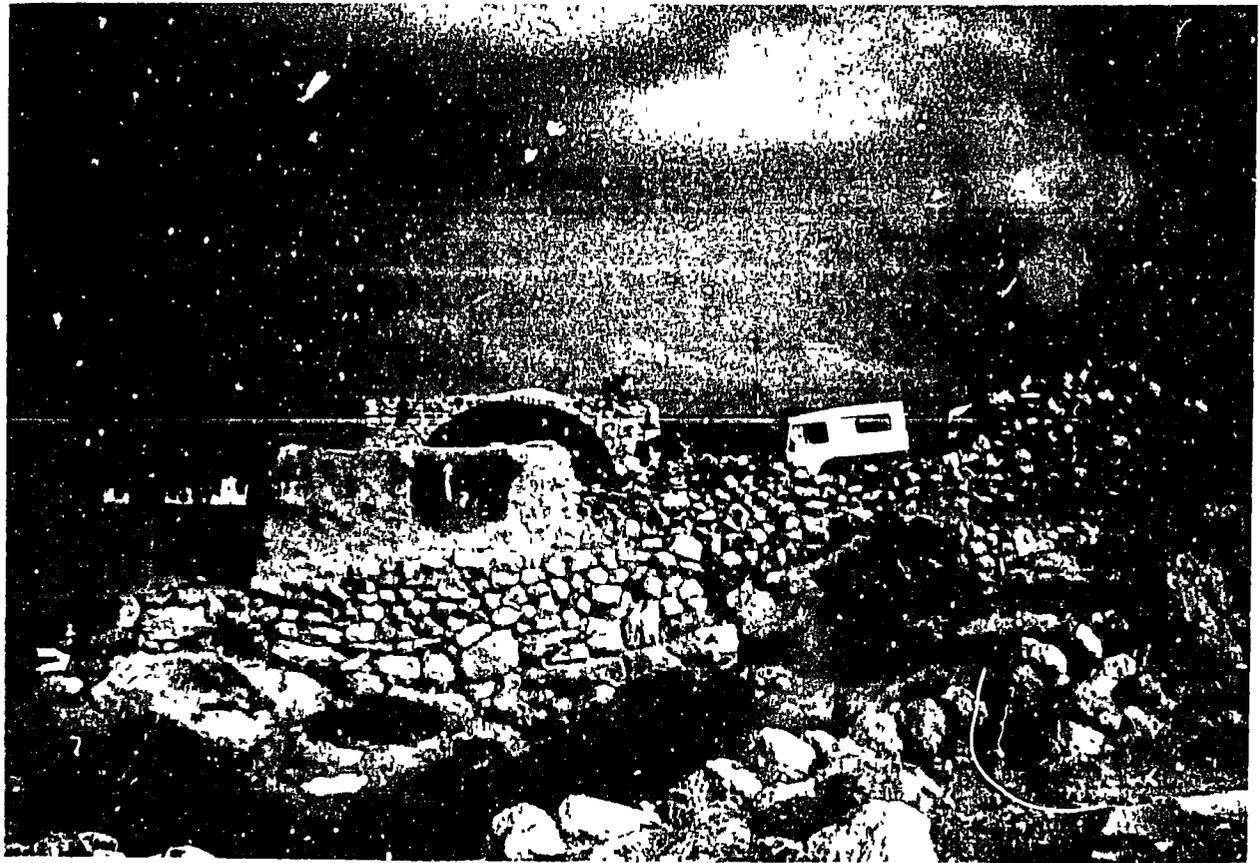

YATMAH SUB-PROJECT

PRIMARY SCHOOL

4D - 006 -22

WORK BEGAN : 14 JUNE 1986

COMPLETED : 04 NOVEMBER 1986

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FINAL SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-22
CRS-JWB/USAID Sub-Project No.

US \$ 40,895
Sub-Project estimated cost

CRS JWP in co-operation with YATMAH VILLAGE
Name of Operating Agency

PPINARY SCHOOL
Title of Sub-Project

NARLUS DISTRICT
Area in which Sub-Project is located

NER-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 24,537
(I) CRS AID cash input

Equivalent to \$ 16,358
Village cash input

US \$ 1,157,598.04
(II) Funds received to date

20 January 1987
Date of last transmittal

CRS AID US \$ 24,525.14
(III) Sub-Project expenditure (s) to date

Village US \$ 16,182.24

CRS AID US \$ 11,86
(IV) Balance (s) unused

Village US \$ 175.76

The cooperation of the villagers and the Education Department with CRS. Villagers donated the piece of land on which the school was constructed.

Other inputs which contributed to success of Sub-Project

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project involved the construction of additional classrooms for the girls' primary school, four rooms, veranda, W.C. units, and staircase - totalling 225 m2.
- The agreement was signed with the village leadership on 11 June 1986. Work started on 14 June 1986, and the sub-project was successfully completed on 4 November 1986, and immediately put into use.
- The village committee faced some difficulties while collecting the village's share due to the bad economic situation in the West Bank.
- The final cost amounted to \$ 40,707.38. The village's share came at \$ 16,182.24, equivalent to 40% of the total costs. CRS-AID share came at \$ 24,525.14, which is 60% of the total costs. The attached statement of expenditures gives a clear idea of the final cost.
- The additional classrooms increased the number of students and teachers, and improved the standard of education. A first preparatory class will be added in the next academic year (Sept. 87). Each grade has now a separate room.
- The Education Department furnished the new classrooms and provided the necessary teaching staff and textbooks.
- Attached are photos showing different aspects of the sub-project's implementation, and a letter of thanks sent by Yatmah villagers.

EVALUATION

- The educational facilities in a rural area of Nablus District has been much improved. This contributes to the Grant Goal which is development of underdeveloped rural West Bank Arab Villages.
- The new rooms replaced inadequate and inappropriate quarters. The girls' school is no longer jammed and can accept new students. Each grade has now a separate room and every girl will have the opportunity for primary education.

GA/mf

ITEMIZATION OF EXPENDITURES

YATMAH SUB-PROJECT 4D - 006 - 22

PRIMARY SCHOOL.

<u>ITEM</u>	<u>QUANTITY</u>	<u>TOTAL</u>
1. Cement	53 Tons	4,269.02
2. Cement Blocks	2200	611.64
3. Roofing Iron	11.5 Tons	7,280.73
4. Iron Bars	200	382.70
5. Wires and Nails	395 kgs.	585.13
6. Building Stones	771 m.	4,505.48
7. Concrete	83 m3	4,043.61
8. Gravel-Powdered	4 m3	101.69
Mixed	7 loads	625.75
Fine	2 loads	178.79
9. Rough stones	20 loads	304.05
10. Sand	1 load	119.17
11. Asphalt	3 tins	60.81
12. Fiber Boards	50	67.57
13. Wooden Doors	6	1,058.10
14. Iron Doors	4	335.81
15. Sanitary Equipments		2,543.36
16. Water	30 tanks	475.81
17. Aluminium Windows	20 m2	889.90
18. Window Sills	11 m	156.75
19. Tiles	250	1,097.98
20. Compressor	10 days	809.80
21. Bulldozer	3 days	608.10
22. Dumping and leveling foundations	(by Job)	243.24
23. Roofing water Reservoir	(by Job)	142.23
24. Painting rear wall	(by Job)	236.73
25. Clearing school site	(by Job)	207.48
26. White washing & Painting	(by Job)	557.82
27. Pointing	100 m2	173.47
28. Tiling	315 m2	780.05
29. Plastering	1014 m2	1,203.-
30. Mason	270 m2	5,338.10
31. Labourers' wages	6	713.51
Grand Total:		-----
	\$	40,707.38
	NIS	60,182.51
CRS Share 60% = \$ 24,525.14	NIS.	36,232.76
Village share 40% = \$ 16,182.24	NIS.	23,949.75

N.B. Labourers' wages were charged to the village.

GA/sk.

بسم الله الرحمن الرحيم

١٤/٤/١٩٨٧

السادة: خيرات جمعية الاعاثة الاثولية المحترمين

بعد التحية نحن نخاطب واهالي بلدة تهما قضاء نابلس، نشكر السادة مدير الجمعية ونائبه والمهندس وجميع العاملين فيها، لا بد لوه من خدماتهم في بلدنا وسناعتهم في بناء مدرسة البنات الاعلادية وما قدسوه من جهود تنفان واخلاص، حيث اطمعنا ساهموا مشكورين في تخفيف العبء والمشيقة عن بناتنا حيث كنت يدرسن في اماكن بعيدة عن القرية.

ادانكم الله لنا وللانسنة ذخرا ومعينا، ولا زالتتم اهلا للخير ولازال المحتاجين. وفقكم الله دوماً. واسألوا للجميع

عن
عن
عن
عن

~~عن~~ ~~عن~~ ~~عن~~ ~~عن~~

TRANSLATION

In the name of the merciful and compassionate God

14.4.1987

Sirs: The respected Catholic Relief Services

We, the mukhtars and inhabitants of Yatmah Village - Nablus District, present our thanks to the association's director, to his deputy, to the architect, and to all the staff, for the services they rendered to our village, and their participation in constructing the girls' primary school, and for the efforts they presented in perfectness and faithfulness.

They participated - thanks to them - in decreasing the pain and trouble on our girls who used to study in places far from the village.

May God keep you a pride and a support for us and for the humanity.

You are entitled to charity, and you are a shelter for the needy.

May God always grant success to your efforts and keep you.

GB/ms.

PHOTOS ILLUSTRATING SUB-PROJECT

YATMAH - PRIMARY SCHOOL

4D - 006 - 22

Total Cost : \$ 40,707.38

CRS Share : \$ 24,525.14 (60%)

Village Share : \$ 16,182.24 (40%)

Project Completed : 04 November 1986

7/9/86

The girls' school in Yatmah Village was jammed. Students of two different grades have to study in the same room. In an attempt to solve their problem, villagers approached CRS-AID. Photo shows the construction of the foundations for the new building.


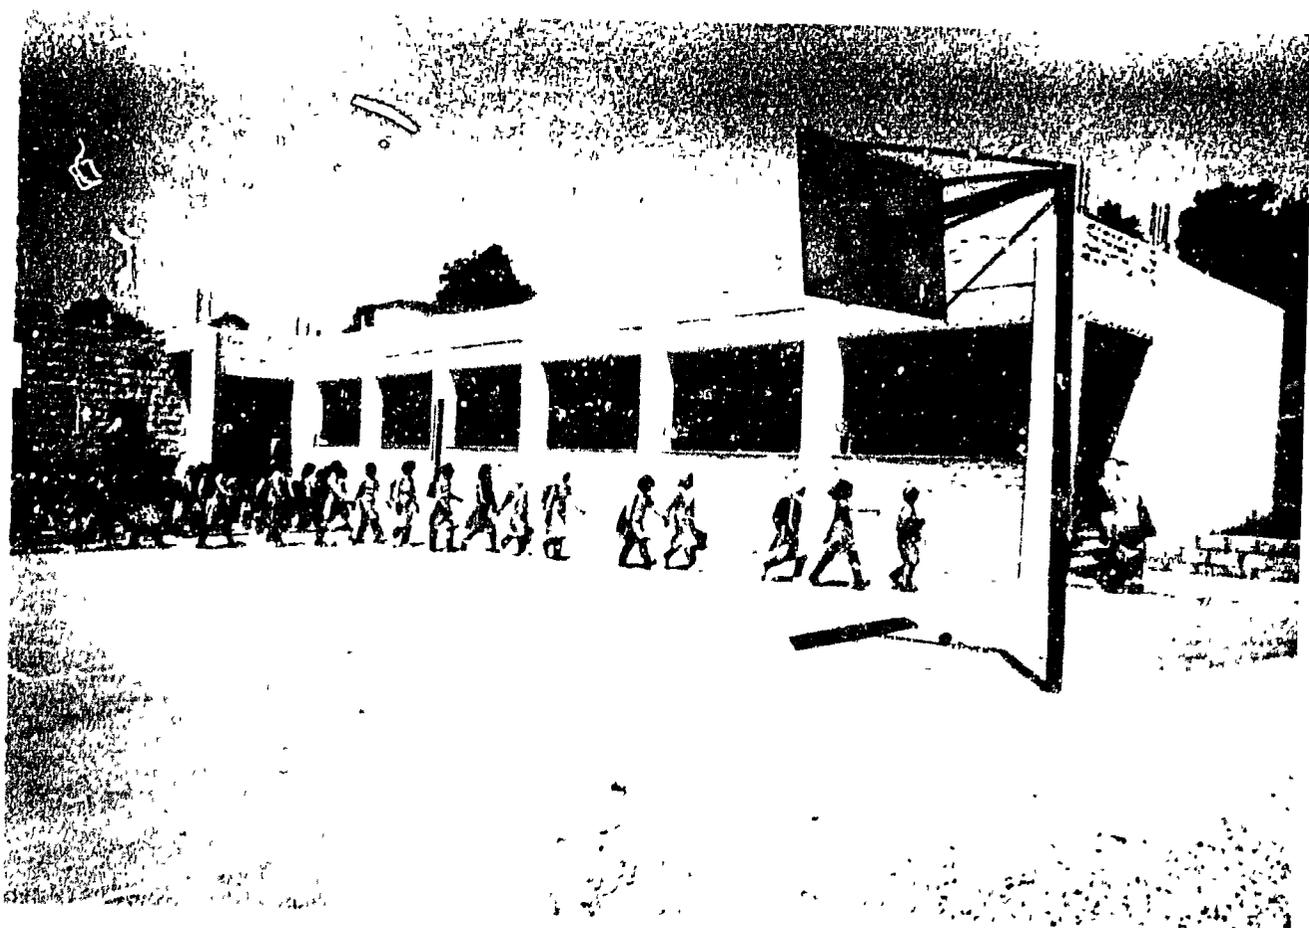


Photo shows girls from Yatmah attending a class in their new building. Villagers are happy and proud of the new, well-lit, ventilated, and beautifully constructed classrooms.

Here is seen the completed new building. It consists of four additional classrooms, veranda, W.C. units, and staircase. The girls' school is no longer jammed and can accept new students. Each grade has a separate room. The level of education is expected to be improved.



95

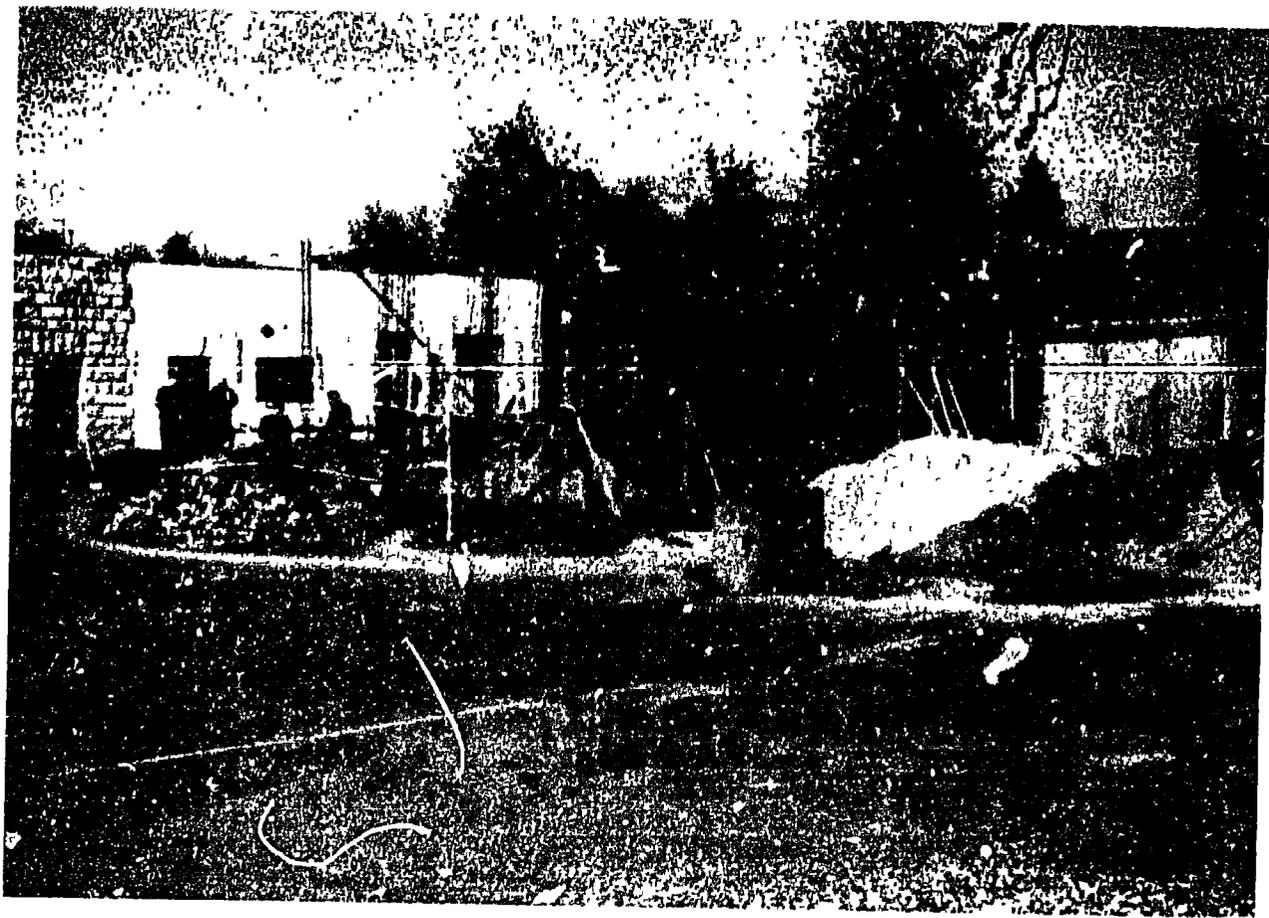

11

SHWAIKEH SUB-PROJECT

COMMUNITY CENTER

4D - 006 - 23

3. PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for the construction of a community center consisting of ten rooms, corridor, entrance, staircase, W.C. units, and a kitchen, the whole totalling about 345 m², to house the village and the charitable society activities.
- The unavailability of cement and heavy rain delayed work. Foundations, partitions, walls, and roofing were successfully completed.
- Tenders will be held soon for selecting a plasterer, a blacksmith, and a carpenter.
- The very cooperative village committee faced some difficulties while collecting funds for the sub-project.
- The center is expected to be completed within sixty days. Villagers are planning to use the building as soon as it is completed.

GA/lb

BEIT EL-RUSH EL-FOQA SUB-PROJECT

WATER SYSTEM

4D - 006 - 24

100

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
SECOND SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-24
CRS-JWB/USAID Sub-Project No.

US \$ 43,750.-
Sub-Project estimated cost

CRS JWB in co-operation with

BEIT EL RUSH EL FOQA
Name of Operating Agency

WATER SYSTEM
Title of Sub-Project

HEBRON DISTRICT
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 26,250.-
(I) CRS AID cash input

Equivalent to \$ 17,500.-
Village cash input

US \$ 1,157,598.04
(II) Funds received to date

20 January 1987
Date of last transmittal

CRS AID US \$ -
(III) Sub-Project expenditure (s) to date

Village US \$ 1,422.27

CRS AID US \$ 26,250.-
(IV) Balance (s) unused

Village US \$ 16,077.73

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for establishing a drinking water system for Beit El Rush El Foqa Village, according to the West Bank Water Authority plans.
- The agreement was signed with the village leadership on 25 August 1986. Implementation started on 31 March 1987.
- The village committee succeeded in collecting only part of the village's share despite all the financial difficulties facing the village, due to which sub-project implementation was delayed.
- All the pipes were ordered. A tender was held on 30 March 1987 and a sub-contractor was chosen for installing the internal net.
- A Final Report including Itemization of Expenditures will be submitted as part of the next Semi-Annual Report.

GA/sk.

الطبعة المحلية

القدس

٤٠
أغشيرة

٨
صفحات

جريدة يومية سياسية

AL-QUDS

Jerusalem - Monday, 23 March 1987 No. 6311

الانثين ٢٣ آذار ١٩٨٧ - ٢٣ رجب ١٤٠٧ هـ العدد ٦٣١١

TENDER NOTICE

اعلان مناقصة

الخليل / بيت الروش الفوقا / تعلن لجنة مياه قرية بيت الروش الفوقا بالتعاون مع خدمات الاغاثة الكاثوليكية عن طرح عطاء تنفيذ شبكة المياه الداخلية في القرية للمناقصة عن طريق الظرف المختوم . كل متعهد يرغب في الاشتراك بهذه المناقصة يمكنه الحصول على نسخة من المواصفات والمخططات من منزل مختار القرية مقابل مبلغ عشرة دنانير اردنية غير مستردة . تعاد العطاءات بعد تعبئتها الى لجنة القرية مرفقة بتأمين مقداره ١٠٪ من قيمة العطاء نقدا او شيك مصدق او كفالة بنكية غير متأخرة عن الساعة العاشرة من صباح يوم الانثين ١٩٨٧/٣/٣٠ .

ملاحظات

- اجور الاعلان في الصحف على المتعهد الذي يحال عليه العطاء .
- اللجنة غير مقيدة بقبول ارضخ العروض او اي عرض اخر ودون ابداء الاسباب
- لن ينظر في اي عطاء مخالف لاي شرط من شروط العطاء وخاصة شرط ارفاق التأمين كما هو مذكور اعلاه .

لجنة مياه بيت الروش الفوقا

Hebron-Beit El-Rush El-Foqa - Beit El-Rush El-Foqa water committee in cooperation with the Catholic Relief Services invite bids in sealed envelopes for carrying out the internal water net for the village . The contractor who wishes to participate in this tender can obtain a copy of the specifications and layouts from the village mukhtar in exchange for ten J.D. unrefundable.

Bids should be handed to the village committee with an insurance of 10% of the total value in cash, or endorsed check, or bank guarantee not later than 10 a.m., Monday 30 March 1987.

Remarks:

1. Awardee is to pay the cost of the advertisements in the papers.
2. The committee does not undertake to accept the lowest offer or any other offer and without explaining the reasons.
3. Any bid not according to the instructions will not be considered especially the condition of enclosing an insurance as it is mentioned above.

Beit El-Rush El-Foqa Water committee

AL - FAJR DAILY

Jerusalem

Wednesday 27

August 1986

No. 4179



« القدس »

الاربعاء ٢٧ اب ١٩٨٦ م

٢٢ ذو الحجة ١٤٠٦ هـ

العدد ٤١٧٩

السنة الرابعة عشرة

اتفاق لتنفيذ مشاريع

في قرى الخليل

الخليل - لمرأينا الخاص من احتفل صباح امس الاول بالتوقيع على ثلاث اتفاقيات لتنفيذ مشاريع تطويريه في عدد من قرى محافظة الخليل من ضمنها خدمات الاغاثية الكاثوليكية بالقدس. تمهيداً لتنفيذ شبكات مياه داخلية في قرى بيت الروش النوقساو بيت الروش التحتا وشق طرق زراعية في قرية بيت ام بطلان لثانية كيلومترًا .

وقد وقع على هذه الاتفاقيات عيسى بركات مدير قسم المشاريع في خدمات الاغاثية الكاثوليكية وفريمال دروزه منتسب المشاريع القروية منسبي الضفة الغربية وسكان القرى المذكوره .

An agreement to implement projects in Hebron villages

Hebron - Our special correspondent - Three agreements to implement development projects in a number of Hebron District Villages in participation with the Catholic Relief Services Jerusalem, were signed the day before yesterday.

These agreements include implementing internal water networks in Beit El-Rush El-Tahta and Beit El-Rush El-Foqa villages, and opening 8 kms long agricultural roads in Beit 'Ummar village.

The agreements were signed by Issa Barakat the Projects Supervisor at CRS, Ferial Darwazeh the inspector of Rural Projects in the West Bank, and the inhabitants of the mentioned villages.

BEIT EL-RUSH EL-TAHTA SUB-PROJECT

WATER SYSTEM

4D - 006 - 25

105

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
SECOND SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of Last report: 1 October 1986

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-25 .. US. \$ 21,875 .
CRS-JWB/USAID Sub-Project No. Sub-Project estimated cost

CRS JWB in co-operation with BEIT EL-RUSH EL TAHTA .
Name of Operating Agency

WATER SYSTEM .
Title of Sub-Project

HEBRON DISTRICT .
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00 .
Funding Agency Code Number

2. EXPENDITURE SECTION

.US \$ 13,125 . Equivalent to \$ 8,750 .
(I) CRS AID cash input Village cash input

. US \$ 1,157,598.04 20 January 1987 .
(II) Funds received to date Date of last transmittal

CRS AID US \$ 5,700.- Village US \$ 5,328.24 .
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 7,425.- Village US \$ 3,421.76 .
(IV) Balance (s) unused

106

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for establishing a drinking water system for Beit El Rush El Tahta Village, according to the West Bank Water Authority plans.
- The agreement was signed on 25 August 1986 while implementation started only on 29 January 1987. The delay was due to the difficulties that the village committee faced in collecting money due to the very difficult economic situation prevailing in the West Bank. The committee collected only part of their share and they promised to raise the rest in a short period.
- CRS-JWB faced some difficulties with the village committee and mukhtar but were successfully solved. Work is going very well. 80% of the water net has been completed.
- The next Semi Annual Report will include a Final Report on this sub-project.

GA/sk.

القدس

اعتورة

صفحات

جريدة يومية سياسية

AL-GUDS - Jerusalem - Monday, 9 February 1987 No. 6270 - العدد ٦٢٧٠ - الاثنين ٩ شباط ١٩٨٧

Tender Notice

Beit El Rush El Tahta - Beit El
sh El Tahta water committee in coopera-
on with the Catholic Relief Services
invite bids in sealed envelopes for carry-
ing out the internal water net for the
village. The sub-contractor who wishes to
participate in this tender can obtain a
copy of the specifications and layouts from
the village mukhtar in exchange for ten
D. unrefundable.

Bids should be handed to the village
committee with an insurance of 10% of the
total value in cash, or endorsed check, or
bank guarantee not later than 10 a.m.
Friday 17 February 1987.

Remarks:

Awardee is to pay the cost of the
advertisements in the papers.

The committee does not undertake to
accept the lowest offer or any other
offer and without explaining the
reasons.

Any bid not according to the instruc-
tions will not be considered especially
the condition of enclosing an
insurance as it is mentioned above.

Beit El Rush El Tahta Water
Committee

اعلان مناقصة

الخليل / بيت الروش التحتا / تعلن لجنة مياه قرية بيت الروش التحتا بالتعاون مع خدمات الاغاثة الكاثوليكية عن طرح عطاء تنفيذ شبكة المياه الداخلية في القرية للمناقصة عن طريق الطرح المختوم ، كل عتهد يرغب في الاشتراك بهذه المناقصة يمكنه الحصول على نسخة من المواصفات والمخططات من منزل مفتاح القرية مقابل مبلغ عشرة لنانيز اردنية غير مستردة ، تعاد العطاءات بعد تعبئتها الى لجنة القرية مرافقة بتأمين مقداره 10% من قيمة العطاء نقدا او شيك مصدق او كفالة بنكية وغير متأخرة عن الساعة العاشرة من صباح يوم الثلاثاء ١٧ شباط ١٩٨٧ ملاحظات :

١/ اجور الاعلان في الصحف على المتعهد الذي يحال عليه العطاء .
٢/ اللجنة غير مقيدة بقبول ارضى العروض او اي عرض اخر ودون ابداء الاسباب .

٣/ لمن ينظر في اي عطاء مخالفا لاي شرط من شروط العطاء وخاصة شرط ارفاق التأمين كما هو مذكور اعلاه .
لجنة مياه بيت الروش التحتا

108

'ATTIL SUB-PROJECT
INTERIOR STREETS
4D - 006 -26

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FIRST SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-26
 CRS-JWB/USAID Sub-Project No.

US \$ 78,766.-
 Sub-Project estimated cost

CRS JWB in co-operation with 'ATTIL VILLAGE
 Name of Operating Agency

INTERIOR STREETS
 Title of Sub-Project

TULKAREH DISTRICT
 Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
 Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 35,445.- Equivalent to \$ 43,321
 (I) CRS AID cash input Village cash input

US \$ 1,157,598.04 20 January 1987
 (II) Funds received to date Date of last transmittal

CRS AID US \$ - Village US \$ -
 (III) Sub-Project expenditure (s) to date

CRS AID US \$ 35,445 Village US \$ (43,321.-)
 (IV) Balance (s) unused (Overspent)

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project involves widening, clearing, and leveling interior streets about 5 Kms long by 4.5 meters wide, including asphaltting a portion of 2 kms. of the length by 3.2 meters of the width of the streets.
- The sub-project was presented to the Social Welfare - Beit-El, West Bank on 27 May 1986. The agreement was signed about six months later. Desperately waiting, the village invested its share in other badly needed projects. Sub-project implementation is expected to start by the beginning of May, as the village committee started to recollect money from the villagers.
- A Final Report including itemization of expenditures covering this sub-project will be submitted as part of the next Semi Annual Report.

GA/bk.

111

CATHOLIC RELIEF SERVICES - USCC

JERUSALEM WEST BANK & GAZA

**Sub-Project Proposal Within Package
Project No. CRS JWB - 4D-006**

Sub-project Number : CRS JWB - 4D-006-26

Sub-Project Location : 'Attil village , Tulkarem District, West Bank.

Operating Agency : CRS JWB with 'Attil Village

Sub-Project Proposal : Opening, clearing and leveling interior streets, about 4.7 kms long by 3 meters wide, including asphaltting a portion of 2 kms of the streets.

Purpose/Objective : To improve the extend sanitary environment in parts of this village due to the fact that a smooth hard surface allows the removal of accumulated garbage and animal droppings which are breeding grounds of disease - carrying insects.

Expected Results : Bad smells, germs, mud and dust will be reduced . Vehicles including ambulances will have better access to the heart of the village.

Time needed to complete sub-project : Approximately 2 months.

Supporting Local Authorities : 'Attil Village Committee, Department of Labour and Social Welfare, and the West Bank Water District Authority.

Cost Estimate : \$ 78,766.- = J.D. 25,205.- at exchange rate of approximately JD 0.32 = \$ 1.-.

Participants in cost : CRS JWB up to a maximum of 45% equivalent to \$ 35,445.- = JD 11,342.-.
'Attil village minimum of 55% equivalent to \$ 43,321.- = JD 13,863.-.

Responsibility for sub-Project upkeep/Maintenance : 'Attil village.

Expected Number of Beneficiaries : All the village inhabitants (i.e. 8500 persons)

BRIEF NARRATIVE:

'Attil lies 9 kms north west of Tulkarem. It has a population of about 8500 persons. The bulk of its residents are farmers who grow vegetables, citrus and olives. A great number of its young people work abroad, mostly in the Gulf States, and constitute a considerable source of income to their village. Having lost about 50,000.- dumums of their arable land during the 1948 war, 'Attil villagers were left with almost no land for growing wheat. The village affairs are run by a Village Council.

'Attil has running water, a post office with telephone services, electricity (from generators supervised by a cooperative) a primary and secondary schools for boys and girls' and a charitable society comprising 400 members. It also has a community center constructed with the help of CRS/AID (48%), while in this sub-project CRS AID is sharing in 45% of the sub-project's costs. But the village still lacks paved interior streets and agricultural roads.

The interior streets are important and essential to 'Attil inhabitants. Cars, pick-ups, taxis and ambulances cannot circulate easily in the important parts of the village. Even 'Attil villagers find great difficulty in reaching their homes and businesses. Garbage and animal droppings are difficult to remove thus threatening the healths of the villagers. Providing 'Attil with smooth hard surfaced streets will clean the village and reduce health hazards. Bad smells and germs will be reduced. Villagers will be able to move conveniently in their village. 90% of 'Attil's inhabitants will contribute toward the village's share of the costs of this sub-project.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-26

This Agreement is between 'Attil village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB PROJECT DESCRIPTION

Widening, clearing and leveling interior streets about 5 kms long by 4.5 meters wide, including asphaltting a portion of 2 kms of the length by 3.2 meters of the width of the streets.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 55% of the total estimated sub-project's cost of US \$ 78,766.- equivalent to \$ 43,321.- (JD 13,863.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 45% of the total estimated sub-project's cost of US \$ 78,766.- equivalent to \$ 35,445.- (JD 11,342.-)
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within 60 (Sixty days only) from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The implementation of the project will begin with the total village share which should be available before the starting date.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

114

- I. The village herewith agrees to hold the Catholic Relief Services harmless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

الإدارة المدنية لمنطقة يهودا والسامرة
مديرة مكتب التوزيع القروي
فريال دووזה

ת"ד י"כ"י - 2044
של נפת טול-כרם

[Handwritten signature]

[Handwritten signature]

DEPARTMENT OF LABOUR & SOCIAL WELFARE

DISTRICT AUTHORITIES



السيد محمد وديع عيسى
السيد حافظ بركات

مجلس عقيل القروي
الرقم
التاريخ

CATHOLIC RELIEF SERVICES

V I L L A G E

فخرا - عقيل
المنطقة
قوز محمد بركات

DATE: 11/11/1986

ESTIMATED COST LIST

Name of village : 'Attil village

Location : Tulkarem District

Sub-Project No. : 4D-006-26

Project Description: Opening, clearing and leveling interior streets about 4.7 kms long by 3 meters wide, including asphaltting a portion of 2 kms of the streets.

				TOTAL (J.D.)

1. Excavator	15 days	X	100 JD per day	1,500.--
2. Bulldozer	6 days	X	80 JD per day	480.--
3. Mixed Gravel	3300 tons	X	2.5 JD per ton	8,250.--
4. Asphalt Mixture	985 tons	X	15 JD per ton	14,775.--
5. Miscellaneous				200

GRAND TOTAL (J.D.)				25,205.--

TOTAL COST ESTIMATE : \$ 78,766.-- = JD 25,205.--
(At an exchange rate of U.S. \$ 1.-- = JD 0.32)

CRS SHARE 45% = \$ 35,445.-- = JD 11,342.--

VILLAGE SHARE 55% = \$ 43,321.-- = JD 13,863.--

السيد
 التاريخ
 السيد
 التاريخ

فتحنا عند
 السيد



**BARTA' & KHIRBAT BARTA' SUB-PROJECT
INTERIOR STREETS**

4D - 006 - 28

WORK BEGAN: 10 FEBRUARY 1987

COMPLETED : 28 MARCH 1987

117

**CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK**

**RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FINAL SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT**

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-28
CRS-JWB/USAID Sub-Project No.

US. \$ 74,588.-
Sub-Project estimated cost

CRS JWB in co-operation with BARTA' & KHIRBAT BARTA'
Name of Operating Agency

INTERIOR STREETS
Title of Sub-Project

JENIN DISTRICT
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 38,786.- Equivalent to \$ 35,882.-
(I) CRS AID cash input Village cash input

US \$ 1,157,598.04 28 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ 38,763.75 Village US \$ 36,181.25
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 22.25 Village US \$ (379.25)
(IV) Balance (s) unused (Overspent)

The strong willingness of the villagers to work together and to cooperate with CRS. They donated parts of their lands which were in the way of the projected streets.

Other inputs which contributed to success of Sub-Project.

118

3 **PROGRESS OF (SUB) PROJECT SECTION CRS/JWB-USAID**

- This sub-project calls for widening, clearing, leveling, and asphaltting existing interior streets about 2.2 kms. long by 5 meters wide. Asphaltting covered only 3.2 meters of the width.

- The agreement was signed with the village leadership on 20 November 1986. The heavy rain and bad weather delayed implementation which started on 10 February 1987. The sub-project was successfully completed on 28 March 1987.

- The sub-project's final cost came to U.S. \$ 74,945.-. The village's cash input amounted to \$ 36,181.25 equivalent to 48%, versus CRS/AID cash input of \$ 38,763.75, which is 52% of the total cost. Attached is a detailed final statement of expenditures.

- The new streets replaced very rough and rocky roads which were dusty in summer and muddy in winter. Vehicles including ambulances have better access to the heart of the village.

- Realizing the great benefits of good interior village streets, villagers donated walls and pieces of lands which were in the way of the projected streets. The village is very happy with its new clean streets. Attached is a letter of thanks sent to CRS.

- The entire village contributed to village's share of the sub-project's costs.

- Attached are photos showing the sub-project in its different aspects of implementation.

Evaluation:

- Construction of the new streets with the many benefits contributes to the overall goal of the Grant which is the development of under-developed rural West Bank villages.
- Excellent results have been achieved. The new streets replaced rough, rocky, and narrow roads. Garbage and animal droppings are being removed. The village is much cleaner with a completely new appearance. Ambulances and other vehicles are able to use the streets.
- The sanitary environment in parts of the village has been much improved. Villagers no longer suffer from mud, dust, or germs.

GA/1b

ITEMIZATION OF EXPENDITURES

BARTA' & KHIRBAT BARTA' (4D - 006 - 28)

INTERIOR STREETS

<u>I T E M</u>	<u>Q U A N T I T Y</u>	<u>T O T A L (\$)</u>
1. Mixed Gravel	3416 Tons	30,300.-
2. Asphalt Mixture	760 Tons	32,775.-
3. Widening, clearing, and leveling the streets	(by job)	4,406.25
4. Constructing a traverse	(by job)	7,343.75
5. Photos		120.-
Grand Total		<u>\$ 74,945.-</u>
		NIS 119,912.-

CRS SHARE 52% = \$ 38,763.75 = NIS 62,022.-

VILLAGE SAHRE 48% = \$ 36,181.25 = NIS 57,890.-

٣١٩٨٧/٤١٥

مدرسة السيد مير الافغانه الكاثوليكه المحترم / القدس

صديق واعد:

بلن ذواتي سرورنا، وانشرح صبورنا ان نكتب لك ولزلائك في مدينت
 الله هذه الرسائل، ليعبر عن ما نحس به صبورنا حول من هب وولاد
 ندر لصور كل الوصف، للاسما وانتم الذين انقذتم فرسنا واولادنا
 امراضنا به ومحققه ههنا فتحتم وعيدتم الشوارع في فرسنا
 في كانت في الماضي مليئة بالحفر والاورساج والمياه العادمه والى طاب
 ردا للعوطن والامراض، وعلاوه على ذلك كانت قعر ضالحه للبدليل
 طاب ان مما سبب لنا مشاكل عديده بالنسبه للشيوخ والبيات الحوامل،
 اليوم ويفضل الله وفضلتم اصوت شوارع فرسنا معبده وهي مفتحه لنا
 والى نحى مدي اللحم الانسانى الى قدموه ولقد صوب لنا وللقرى اللسه
 شرم في هذه الارض المباركه والى ياتى الله في جميع كنهه السماويه،
 مدي مدرجتم الافغانه. لقد قالت الملائكه عندما ولد المسيح عيسى عليه
 سلام دو المجد في الاعالي وعلى الارض المسره، قلقت لانتون مرم
 انشاع المسيح تنشرون العدل والفرح والسرور على الارض وفي سنى
 العالم وذلك بانما انتم للمنتوبين والمصنوعين من بني الانسان في اسما
 لقرى وهى اورونا، تحققون عن المصاب مصابه وتنشرون النور والعدل
 مدي الافغانه، لقد فخرنا بكم وعطفكم وسببتم في فرسنا بوضع
 اصنعته نحى للاهمال من مدي ما هتمتم لنا وسببتم السننا بالبر
 لكم ومحبتكم وفقتم الله لما فيه الخد والانسانية والسلام عليكم

مختار برطه
 19 19

مدرسة

عضو
 محمود روح
 محمد
 احمد سالم خليل

لجنة مدارس قرية برطه
 محمد يوسف
 خليل محمد
 احمد محمد
 شمس محمد
 محمود محمد
 19

TRANSLATION

05.04.1987

The respected director of the Catholic Relief
Services - Jerusalem

It is a cause of pleasure and delight to write this letter to you and to your colleagues at the Relief Office, to explain the deep feelings of love, loyalty, and appreciation that we admire to you, and which are beyond any description.

You are the ones who have saved our village and children from actual and prevailing diseases when you opened and asphalted the interior streets which were in the past full of holes, dirt, and polluted water, and a cause for gnats and diseases. In addition to that, the streets were unfit for travelling on by cars, the thing that created several problems for the old and for the pregnant women.

Today, by God's efforts and by yours, our village streets became asphalted; a reason of pride for us and for you. The streets relate the extent of the human support that you offered and still offer to us and to the many villages scattered in this blessed land, that God blessed in all His Holy Books.

Sir, the director of the Relief Association,
The angels said, when Jesus Christ-may peace be upon him-was born: "Glory in heaven, and delight on earth." So how there won't be delight, while you, the followers of Christ, spread justice, joy, and pleasure on the land and in all the world's spots, by relieving the disastared and distressed of human beings, in Asia, Africa, and even Europe. You release pain from the affected and spread light and justice.

Sir, the Relief Director,
You have overwhelmed us with your generosity and affection. We will always, in our humbled village Barta', relate to the generations about the extent of your assistance. Our tongues will remain excited to mention you and your affection. May God grant success to your efforts, for the benefit of humanity.

May peace be upon you.

PHOTOS ILLUSTRATING SUB - PROJECT
BARTA' AND KHIRBAT BARTA' - INTERIOR STREETS
4D - 006 - 28

Total Cost :	\$ 74,945.00	
CRS Share :	\$ 38,763.75	(52%)
Village Share :	\$ 36,181.25	(48%)
Project Completed :	28 March 1987	

12/11

Barta' and Khirbat Barta' interior streets are narrow, rough, dirty and rocky, full of dust, animal droppings, mud, and germs.

CRS - AID agreed to assist the village in widening, clearing, leveling, and asphaltting the main interior streets.

The same view of the section seen in photo above, after the street was completed. The general sanitary environment has been improved, as a smooth hard surface allows the removal of accumulated garbage and animal droppings. Now, vehicles have good access to the heart of the village.



106

The valley seen in the picture overflows during the winter season and separates the village. A small bridge, whose foundations are seen, had to be constructed, to connect both parts of the village. →



Photo shows the traverse-small bridge-after being successfully constructed.

Here is a view of the very same section seen in photo above. It is converted into a quite wide, hard surfaced, cleanable paved street. Children are seen sitting on the edge of the traverse. Now, as it is obvious from the picture, trucks and public transportation can easily use it. →



128

EL-SHIYOUKH SUB-PROJECT
INTERIOR STREETS
4D - 006 -29

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FIRST SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-886-29
CRS-JWB/USAID Sub-Project No.

US. \$ 78,831.-
Sub-Project estimated cost

CRS JWB in co-operation with EL SHIYOUKH VILLAGE
Name of Operating Agency

INTERIOR STREETS
Title of Sub-Project

HEBRON DISTRICT
Area in which Sub-Project is located

NEB-8159-G-SS-5123-88
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 39,815.50 Equivalent to \$ 39,815.50
(I) CRS AID cash input Village cash input

US \$ 1,157,598.84 20 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ - Village US \$ 8,518.75
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 39,815.50 Village US \$ 38,496.75
(IV) Balance (s) unused (Overspent)

PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for widening, clearing and leveling existing interior streets 3.5 kms. long by 5 meters wide and asphaltting a portion of 2 kms. long by 3 meters wide of the streets.
- The agreement was signed with the village leadership on 26 November 1986. Work was interrupted several times by the heavy rain. The sub-project is expected to be completed by the end of May 1987.
- 90% of the roads are now opened, and they will be soon leveled and asphalted.
- CRS-JWB met several difficulties before convincing some villagers to give up parts of their lands and walls to the projected streets, as a result of which the very narrow "donkey paths" were converted into decent, wide interior streets. The village committee greatly appreciated CRS-JWB efforts in overcoming these difficulties.
- Villagers are now installing on their own expense part of the water network which had to be removed while constructing the streets. When this is completed, the asphaltting stage will start.
- The Final Report on this sub-project will be submitted as part of the next Semi-Annual Progress Report.

GA/mf

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM WEST BANK & GAZA

Sub-project Proposal Within Package
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-29

Sub-project Location: El-Shiyoukh village, Hebron District,
West Bank.

Operating Agency : CRS JWB together with El-Shiyoukh village.

Sub-project Proposal: Widening, clearing, leveling and asphaltting
existing interior streets, about 3.5 kms long
by 5 meters wide. Asphaltting will cover only
2 kms of the length and 3 meters of the width
of the streets.

Purpose/Objective : To improve the extend sanitary environment
in parts of the village due to the fact that
a smooth hard surface allows the removal of
accumulated garbage and animal excrement
which are breeding grounds of disease
carrying insects.

Expected Results : Vehicles including ambulances will have better
access to the heart of the village. Mud in winter
and dust in summer will be reduced.

Time needed to
complete the sub-
project : Approximately 2 months

Supporting Local
Authorities : El-Shiyoukh Village Committee, Department of
Labour and Social Welfare, and the West Bank
District Authority.

Cost Estimate : \$ 78,031.- equivalent to J.D. 24,970.- at
exchange rate of approximately J.D. 0.32
= \$ 1.-.

Participants
Costs : CRS JWB 50% equivalent to \$ 39,015.50 =
J.D. 12,485.-

El-Shiyoukh village 50% equivalent to \$
39,015.50 = J.D. 12,485.-

Responsibility
for sub-project
keep/maintenance : El-Shiyoukh village.

Expected Number
Beneficiaries : 5000 persons (the entire village
population).

BRIEF NARRATIVE:-

El-Shiyoukh is located 12 kms north east of Hebron. It has a population of 5000 people who depend upon olives, wheat and barley cultivation, with some live-stock raising. Some of the villagers work as labourers in the Hebron area. The village has no paved interior streets. Parts of the village still lack water and electricity.

El-Shiyoukh has a girls' preparatory school and a boys' secondary school. It also has an out-patient health clinic and a charitable association. It has no village council. The village affairs are run by a mukhtar (headman).

The present interior streets are very rough, rocky, narrow, and dirt donkey-paths. These streets are extremely important and essential to El-Shiyoukh villagers. Garbage and animal droppings thrown into these streets are difficult to remove. The lack of vehicular movement is an impediment to the village's development.

El-Shiyoukh villagers are very eager to widen, clear, level, and asphalt their existing interior streets. They approached CRS-AID for help to solve their problem.

Providing El-Shiyoukh with clean, smooth hard surfaced streets will clean-up the village and will reduce health hazards. The village will look nicer. Vehicles including ambulances will have better access to the heart of the village. This will encourage the villagers to develop their village. All the villagers will contribute towards their village's share of the costs of this sub-project.

PROJECT IMPLEMENTATION:

Implementation can start as soon as CRS NEW YORK approval is given and agreement is signed by El-Shiyoukh village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-29

This Agreement is between El-Shiyoukh village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB-PROJECT DESCRIPTION:-

Widening, clearing, leveling, and asphaltting existing interior streets about 3.5 kms long by 5 meters wide. Asphaltting will cover only 2 kms the of the length and 3 meters of the width of the streets.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 50% of the total estimated sub-project's cost of US \$ 78,031.- (JD 24,970.-) equivalent to \$ 39,015.50 (JD 12,485.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 50% of the total estimated sub-project's cost of US \$ 78,031.- (JD 24,970.-) equivalent to US \$ 39,015.50 (JD 12,485.-).
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within (60) Sixty days from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The villiage will have collected and have at its disposal at least 90% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government Authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

134

- I. The village herewith agrees to hold the Catholic Relief services blameless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES


الإدارة المدنية لمنطقة بهودا والسامرة
مديرة مكتب الشاريع القرويه
فريال دروزه

[Handwritten signature]

DEPARTMENT OF LABOUR & SOCIAL WELFARE

DISTRICT AUTHORITIES

[Handwritten signature]



[Handwritten signature]

CATHOLIC RELIEF SERVICES

[Handwritten signature]
عبد الحادق

[Handwritten signature]
رؤسه عبد الكريم بنك

[Handwritten signature]

V I L L A G E

DATE: - 26/11/1986

ESTIMATED COST LIST

SUB-PROJECT NO. CRS JWB 4D-006-29

El-Shiyoukh Village - Hebron District - West Bank

Sub-project Description: Widening, clearing, leveling and asphaltting existing interior streets about 3.5 kms long by 5 meters wide. Asphaltting will cover only 2 kms of the length and 3 meters of the width of the streets.

	<u>QUANTITY</u>	<u>PRICE</u>	<u>TOTAL JD</u>
1. Mixed Gravel	3000 (tons)	3 JD per ton	9,000.-
2. Asphalt	985 (tons)	14 JD per ton	13,790.-
3. Excavator	17 days	100 JD per day	1,700.-
4. Bulldozer	6 days	80 JD per day	480.-
		TOTAL (J.D.)	24,970.-
			=====

TOTAL COST ESTIMATE : \$ 78,031.- = JD 24,970.-
at an exchange rate of \$ 1.- = JD 0.32

CRS SHARE 50% : \$ 39,015.50 = JD 12,485.-

VILLAGE SHARE 50% : \$ 39,015.50 = JD 12,485.-

136

SURDA-RADDANA SUB-PROJECT

ACCESS ROAD

4D - 006-30A

(15)

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FIRST SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-006-30 a
CRS-JWB/USAID Sub-Project No.

US \$ 48,375.-
Sub-Project estimated cost

CRS JWB in co-operation with RADDANA HOUSING PROJECT
Name of Operating Agency

ACCESS ROAD
Title of Sub-Project

RAMALLAH DISTRICT
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 29,025.- Equivalent to \$ 19,350.-

(I) CRS AID cash input Village cash input

US \$ 1,157,598.04 20 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ - Village US \$ -
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 29,025.- Village US \$ 19,350.-
(IV) Balance (s) unused

138

PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project was supposed to serve two Housing Projects - Raddana and Al Salamiyyeh - in Surda Village Rammallah District.
- The sub-project was divided into two separate sub-projects after receiving a rejection from the Military Governor concerning Al Salamiyyeh access road. Al Salamiyyeh sub-project was referred to the Planning Department, and we are working to obtain their consent.
- Raddana sub-project calls for opening, clearing, and leveling an access road about 1100 meters long by 6 meters wide and asphaltting it by only 4 meters of the width.
- The agreement covering Raddana sub-project was signed on 24 November 1986. The road is expected to be completed by the end of May 87.
- The road is now completely opened. Leveling, constructing road foundations, and asphaltting will start soon.
- The Final Report on Raddana's access road will be submitted in the next Semi-Annual Progress Report.

GA/mf

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM WEST BANK & GAZA

Sub-project Proposal Within Package
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-30

Sub-project Location: Surda - Al-Salamiyyeh and Al-Raddana Housing Projects - Ramallah - West Bank.

Operating Agency : CRS JWB together with Al-Raddana and Al-Salamiyyeh Committees

Sub-project Proposal: Opening, clearing, leveling and asphaltting access roads about 2 kms long by 6 meters wide. Asphaltting will cover only 3.5 meters of the width of the roads.

Purpose/Objective : To connect Al-Salameyeh and Al-Raddana Housing Projects with the main streets, thus improving the sanitary environment.

Expected Results : Vehicles including ambulances will have better access to these Housing Projects

Time needed to complete the sub-project : Approximately 7 months

Supporting Local Authorities : Al-Salamiyyeh and Al-Raddana Committees, Department of Labour and Social Welfare, and the West Bank District Authority.

Cost Estimate : \$ 74,938.- equivalent to J.D. 23,980.- at exchange rate of approximately J.D. 0.32 = \$ 1.-.

Participants in costs : CRS JWB 60% equivalent to \$ 44,963.- = J.D. 14,388.-
El-Salamiyyeh and Al-Raddana Housing Project 40% equivalent to \$ 29,975.- = J.D. 9,592.-

Responsibility for sub-project upkeep/maintenance : El-Salamiyyeh and Al-Raddana Housing Projects

Expected Number of Beneficiaries : 600 persons (the entire village population).

REF NARRATIVE:-

In the West Bank, people are facing housing problems. Vacant houses are rarely available; those that are available have extremely high rents. Most people are not in a good financial position to build private houses. So they became much interested in forming Housing Cooperatives.

Al-Raddana and Al-Salamiyyeh are two Housing Projects formed in Surda area - Ramallah District. Al-Raddana has 28 families while Al-Salamiyyeh has 17 families. Most of these families are from the middle class or low-income people. They purchased land with their earnings and divided it into lots. Then they started to build their houses with the help of loans obtained from Banks or Agencies.

Al-Raddana and Al-Salamiyyeh families got their houses as skeletons only. They had to complete them on their own, whenever money will be available. They also had to pay monthly installments to cover the loans.

Due to their critical financial position, families cannot achieve any other project. They have deposited all their life earnings in the housing project. They will have to live a very simple life without the essential requirements and facilities such as water system, electricity, and roads. This life might last long unless help is offered to them.

Al-Raddana and Al-Salamiyyeh approached CRS-AID to help to connect both Housing Projects with the main street. Constructing the access roads will bring all sorts of benefits to the Housing Projects. Public transportations and ambulances will reach these cooperatives easily. Families will be encouraged to continue their houses as the road will reduce the cost of materials and of transportation. Ten other families from Surda will directly benefit from these roads. The sanitary environment will be much improved. These Housing Projects will become a more bearable place to live in. All the member families will contribute towards the Housing Projects' share of the sub-project's costs.

OBJECT IMPLEMENTATION:

Implementation can start as soon as CRS NEW YORK approval is given and agreement is signed by Al-Raddana and Al-Salamiyyeh Housing Projects, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

141

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-30

This Agreement is between Raddana Housing Project and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB-PROJECT DESCRIPTION:-

Opening, clearing, leveling and asphaltting access road about 1100 ms long by 6 meters wide. Asphaltting will cover only 4 meters of the width of the road.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 40% of the total estimated sub-project's cost of US \$ 48,375.- (JD 15,480.-) equivalent to \$ 19,350.- (JD 6,192.)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 60% of the total estimated sub-project's cost of US \$ 48,375.- (JD 15,480.) equivalent to US \$ 29,025.- (JD 9,288.-) This amount is provided by US/AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within (60) Sixty days from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The villlage will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government Authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

KJ

- I. The village herewith agrees to hold the Catholic Relief services blameless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

الإدارة المدنية لدمشق
 مديرية مكتب العمل
 لدمشق

ל. ח. מ.
 סאניל-שלמה חסון
 מושל נפת רמאללה

[Signature]

 DEPARTMENT OF LABOUR & SOCIAL WELFARE

[Signature]

 DISTRICT AUTHORITIES



 CATHOLIC RELIEF SERVICES

[Signature]
[Signature]

 V I L L A G E

DATE: - 24/11/1986

143

ESTIMATED COST LIST

SUB-PROJECT NO. CRS JWB 4D-006-30

RADDANA - Ramallah District.

Sub-project Description:- Opening, clearing, leveling and asphaltting access roads about 1100 ms long by 6 meters wide. Asphaltting will cover only 4 meters of the width of the road.

	<u>QUANTITY</u>	<u>PRICE</u>	<u>TOTAL JD</u>
1. Excavator	6 Days	100 J.D. per day	600.-
2. Bulldozer	4 Days	80 J.D. per day	320.-
3. Dumping Truck	3 Days	70 J.D. per day	210.-
4. Mixed Gravel	2000 Tons	2.70 J.D. per day	5,400.-
5. Asphalt	630 Tons	14 J.D. per day	8,820.-
6. Miscellaneous			130

		TOTAL (J.D.)	15,480.-
			=====

TOTAL COST ESTIMATE : \$ 48,375.- J.D. 15,480.- (At an exchange rate of \$ 1.- = J.D. 0.32)

CRS SHARE 60% : \$ 29,025.- = J.D. 9,288.-

RADDANA SHARE 40% : \$ 19,350.- = J.D. 6,192.-

EL-SHAWAWREH SUB-PROJECT
AGRICULTURAL ROAD
4D - 006 - 31

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for opening, clearing, and leveling 3.8 kms. of a 5 kms. long by 5 meters wide agricultural access road, including asphaltting a portion of 1.2 kms. by 3 meters of the road.
- The agreement was signed with the village leadership on 30 December 1986. Implementation started on 10 February 1987.
- Work was interrupted by the heavy rain and bad weather. The very narrow "donkey paths" were opened, widened, and converted into decent roads. The foundations were completed and three small bridges constructed.
- The road is expected to be asphalted during April. The sub-project will be soon completed.

GA/sk.

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM WEST BANK & GAZA

Sub-project Proposal Within Package
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-31

Sub-project Location: El-Shawawreh village, Bethlehem District, West Bank.

Operating Agency : CRS JWB together with El-Shawawreh village.

Sub-project Proposal: Opening, clearing and leveling 3.8 kms of a 5 kms long by 5 meters wide agricultural access road, including asphaltting a portion of 1.2 kms by 3 meters of the road.

Purpose/Objective : To improve El-Shawawreh villagers connection with their agricultural land, some of which is already being cultivated and some of which, though cultivable, is unused. Transportation of produce to the village or markets will be facilitated.

Time needed to complete the sub-project : Approximately 3 months

Supporting Local Authorities : El-Shawawreh Village Committee, Department of Labour and Social Welfare, and the West Bank District Authority.

Cost Estimate : \$ 57,594.- equivalent to J.D. 18,430.- at exchange rate of approximately J.D. 0.32 = \$ 1.-.

Participants in costs : CRS JWB 57% equivalent to \$ 32,829.- = J.D. 10,505.-.
El-Shawawreh village 43% equivalent to \$ 24,765.- = J.D. 7,925.-.

Responsibility for sub-project upkeep/maintenance : El-Shawawreh village.

Expected Number of Beneficiaries : 4500 persons (the entire village population).

BRIEF NARRATIVE:-

El-Shawawreh village is located 9 kms east of Bethlehem. It has a population of 4500 people. The inhabitants of this poor village depend upon agriculture and the provision of unskilled labour to the neighbouring towns of Bethlehem, Beit Sahhour, and Beit Jala. In their fields, villagers grow wheat, barley, and lentils. The village has no electricity, postal services, public transportation, community center, out-patient health clinic, or charitable association. It has two primary schools, one for boys consisting of five rooms, and the other for girls consisting of three rented rooms. The village affairs are run by a village headman (mukhtar) supported and helped by village elders and notables.

The villagers of El-Shawawreh reach their fields either by foot or donkey. They have to carry their simple agricultural tools with their bags of seeds on their heads or on donkey backs. The agricultural produce reaches markets in bad condition with high costs and loss. Agricultural machinery cannot reach the fields. The villagers badly need an agricultural road giving them access to their fields. They cannot afford all the money needed for such an important and vital project. They approached CRS-AID for help.

Constructing the agricultural access road will undoubtedly improve the villagers connection with their lands. It will also provide speedy means of transport for the agricultural produce. Villagers will be able to get this produce to the markets while fresh, to be either sold locally or exported to the Arab countries. Loss and damage of crops will be reduced, enabling the farmers to get a higher return, and raising the standard of living. 95% of the villagers will contribute towards the village's share of the sub-project costs.

PROJECT IMPLEMENTATION:

Implementation can start as soon as CRS NEW YORK approval is given and agreement is signed by El-Shawawreh Village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-31

This Agreement is between El-Shawawreh village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB-PROJECT DESCRIPTION:-

Opening, clearing and leveling 3.8 kms of a 5 kms long by 5 meters wide agricultural access road, including asphaltting a portion of 1.2 kms by 3 meters of the road.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 43% of the total estimated sub-project's cost of US \$ 57,594.- (JD 18,430.-) equivalent to \$ 24,765.- (JD 7,925.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 57% of the total estimated sub-project's cost of US \$ 57,594.- (JD 18,430.-) equivalent to US \$ 32,829.- (JD 10,505.-). This amount is provided by US/AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure inter alia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within (90) Ninety days from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government Authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

- I. The village herewith agrees to hold the Catholic Relief services blameless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.


SIGNATORIES

המינהל האזורי לאזור יהודה ושומון
 الادارة المدنية لمنطقة يهودا والسامرة
 משרד העבודה והרווחה
 وزارة الرفاه الاجتماعي
 יחידת מסעדות ומסעדות
 مكتب الخدمات الاجتماعية



DEPARTMENT OF LABOUR & SOCIAL WELFARE

ק"ט/טו
 סגן מושל נפת בית לחם
 סגן מושל שמואל

DISTRICT AUTHORITIES



CATHOLIC RELIEF SERVICES



V I L L A G E

DATE: - 20 - 12 - 1986

ESTIMATED COST LIST

SUB-PROJECT NO. CRS JWB 4D-006-31

El-Shawawreh Village - Bethlehem District - West Bank

Sub-Project Description: Opening, clearing, and leveling
3.8 kms of a 5 kms long by 5 meters wide
agricultural access road, including
asphalting a portion of 1.2 kms by
3 meters of the road.

	<u>QUANTITY</u>	<u>PRICE</u>	<u>TOTAL JD</u>
1. Excavator	14 Days	100 J.D. per day	1,400
2. Bulldozer	9 Days	80 J.D. per day	720
3. Mixed Gravel	3000 Tons	2.35 J.D. per ton	7,050
4. Asphalt	640 Tons	14 J.D. per ton	8,960
5. Miscellaneous			300

		TOTAL J.D.	18,430

TOTAL COST ESTIMATE : \$ 57,594.- = J.D. 18,430.- (At an exchange
rate of \$ 1.- = J.D. 0.32)

CRS SHARE 57% : \$ 32,829.- = J.D. 10,505.-

VILLAGE SHARE 43% : \$ 24,765.- = J.D. 7,925.-

ZIF SUB-PROJECT

PRIMARY SCHOOL

4D - 006 - 32

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FIRST SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-886-32
CRS-JWB/USAID Sub-Project No.

US. \$ 46,922,-
Sub-Project estimated cost

CRS JWB in co-operation with ZIF VILLAGE
Name of Operating Agency

PRIMARY SCHOOL
Title of Sub-Project

HEBRON DISTRICT
Area in which Sub-Project is located

NEB-8159-G-SS-5123-88
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 72,188,- Equivalent to \$ 25,266,-
(I) CRS AID cash input Village cash input

US \$ 1,157,559.84 28 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ 9,289.89 Village US \$ 14,826.51
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 62,898.11 Village US \$ 18,439.49
(IV) Balance (s) unused

GA/1b

154

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This sub-project calls for the construction of a primary co-educational school consisting of five classrooms, veranda, and W.C. units totalling 320 m2.
- The agreement covering this sub-project was signed with the village leadership on 26.11.1986. Implementation started on 16.1.1987.
- The foundations, walls, partitions, and roofing were successfully completed in a short time despite a shortage in cement and the very bad weather and heavy rain that affected the West Bank during the winter season. The digging of the cesspool and the water cistern was successfully completed.
- Bids will soon be held for choosing a plasterer, a blacksmith, and a carpenter. The tiles were ordered.
- The Final Report on this sub-project will be submitted as part of the next Semi-Annual Report.

GA/sk.

القدس

٣٥
صورة

AL QUDS Jerusalem Friday 28 November 1986 No: 6197

The Catholic Services Shares in two Sub-Projects in Zif and El Shiyoukh Villages

Hebron - Two agreements were signed between the Catholic Relief Services in Jerusalem and the inhabitants of Zif and El Shiyoukh villages - Hebron district. The first agreement states for the construction of a primary co-educational school consisting of six classrooms with an estimated cost of about 23,000 Jordanian Dinars. The Catholic Relief Services will share in about 65%.

In El Shiyoukh, a number of the village interior streets will be opened and asphalted. The costs are estimated by about 25,000 Jordanian Dinars, of which the CRS will share in 50%.

الخدمات الكاثوليكية تساهم في مشروعين بقرية زيف والشيوخ

الخليل / تم التوقيع على الاتفاقية
بين خدمات الاغاثة الكاثوليكية في القدس
وسكان قرية زيف والشيوخ لقيام
الخليل الاولى لبناء مدرسة ابتدائية
مختلطة مؤلفة من ست غرف دراسية مع
ملحقاتها بتكاليف تقدر بحوالي ٢٣ الف
دينار اردني تساهم الاغاثة بحوالي ٦٥
بالمائة منها .

اما في قرية الشيوخ فسيتم شق
وتعميد عدد من الشوارع الداخلية في
القرية وتقدر تكاليفها بحوالي ٢٥ الف
دينار اردني تساهم فيها الاغاثة
الكاثوليكية بخمسين في المائة .

GA/sk.

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM WEST BANK & GAZA

Sub-project Proposal Within Package
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-32

Sub-project Location: Zif village, Hebron District, West Bank.

Operating Agency : CRS JWB together with Zif and other villages.

Sub-project Proposal: Constructing a primary co-educational school consisting of six classrooms, veranda, and W.C. units the whole totalling about 320 m2.

Purpose/Objective : To improve primary level education facilities for girls and boys in a rural area of Hebron District.

Expected Results : Primary level education for boys and girls will become more suitable. This new school will also serve the students of three neighbouring villages of Al-Buwaib - Hraiz & Al-Dwair in addition to some bedouins living in the area. The education Department will furnish the school and provide the necessary teaching staff and text-books.

Time needed to complete the sub-project : Construction of the building should take about 4 months. The school will be put to use immediately after completion of construction.

Supporting Local Authorities : Zif Village Committee, Department of Labour and Social Welfare, and the West Bank District Authority.

Cost Estimate : \$ 72,188.- equivalent to J.D. 23,100.- at exchange rate of approximately J.D. 0.32 = \$ 1.-.

Participants in costs : CRS JWB 65% equivalent to \$ 46,922.- J.D. 15,015.-.
Zif village 35% equivalent to \$ 25,266.- = J.D. 8,085.-.

Construction Plan prepared by : Private Architect approved by Hebron District Education Department and CRS JWB.

Responsibility for sub-project upkeep/maintenance : Zif village.

Expected Number of Beneficiaries : 2000 persons.

BRIEF NARRATIVE:

The poor villagers of Zif, Al-Buwaib, Hraiz, and Al-Dwair are located 12 kms East of Hebron. The total population of these four villages is 2000 people. Their daily livelihood is farming, the raising of sheep and goats, and providing unskilled labour to Hebron. These villages have no interior paved streets, no electricity, no postal services, no community center, no out-patient health clinic, no public transportation, and no clean water system. Affairs of these villages are run by the elders and notables.

These villages have no schools. Students walk five to seven kilometers daily to reach the jammed and overcrowded Yatta or Raq'a schools. Due to the lack of space, not every student has the opportunity of attending these schools. This situation increases the percentage of illiteracy among the villages' population.

Zif and the neighbouring villages want to improve their living conditions. They concluded that one important way to achieve this aim is through education. They bought a piece of land for the school. They got the Hebron District Education Department approval and encouragement for such a vital project. Then they approached CRS-AID asking help for solving their problem.

In addition to the four mentioned villages, some bedouins living in the area will benefit from the school. The Department of Education will provide school text-books, furniture, and teachers. The villagers would own the building. The construction of this school building will mean more opportunity for the village students. Proper classrooms will become available. 90% of the village's inhabitants will contribute towards their share of this sub-project's costs.

PROJECT IMPLEMENTATION:

Implementation can start as soon as CRS NEW YORK approval is given and agreement is signed by Zif village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-32

This Agreement is between Zif Village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB-PROJECT DESCRIPTION:-

Constructing a primary co-educational school consisting of six classrooms, veranda, and W.C. units the whole totalling about 320 m2.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 35% of the total estimated sub-project's cost of US \$ 72,188.- (JD 23,100.-) equivalent to \$ 25,266.- (JD 8,085.-)
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 65% of the total estimated sub-project's cost of US \$ 72,188.- (JD 23,100.-) equivalent to US \$ 46,922.- (JD 15,015.-). This amount is provided by US/AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within (120) One Hundred Twenty days from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The villlage will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assummes all liability for the assessment, collection and deposit with appropriate Government Authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.


- I. The village herewith agrees to hold the Catholic Relief services blameless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

للادارة المدنية لمنطقة يهودا والسامرة
 مديرة مكتب الشرايع القرويه
 فريال دوزوه

DEPARTMENT OF LABOUR & SOCIAL WELFARE

DISTRICT AUTHORITIES



HOB

بطا	١١٠٤
١١٠٤	١١٠٤

محمد عبد الله
 محمد عبد الله

CATHOLIC RELIEF SERVICES

V I L L A G E

بسم حكومة اتحادة شان



محمد عبد الله

DATE: - 26/11/1986

ESTIMATED COST LIST

Sub-project No. 40-006-32

CRS-JWB

(32)

NAME OF VILLAGE : Zif and Others

LOCATION : Hebron District

PROJECT DESCRIPTION : Constructing a primary co-educational school consisting of six classrooms, veranda, and W.C. units, the whole totalling about 320 m2.

MATERIAL	Quantity	Price JD	Total JD	WAGES	Quantity	Price JD	Total JD
Black Cement	110 Tons	31	3410	Mason	460 m2	10	4600
White Cement	18 Bags	6	108	Plasterer	2650 m2	0.60	1590
Steel	11.6 Tons	230	2668	Tiling	345 m2	0.80	276
Doors	26.5 m2	28	742	Pointing	130 m2	0.90	117
Windows	36.5 m2	22	803	Painting	146 m2	0.60	87.6
Window Fence	56.7 m2	7	396.90	White Washing	1120 m2	0.40	448
Building Stone	245 m2	1.40	343	Miscellaneous	-	-	44.7
Cement Blocks	8870	18	1596.60	Labourers	60 days	4	240
Rough Stone	60 m3	2.50	150	Skilled Labour	10 days	5	50
Gravel, Mixed	230 m3	3.50	805	Bulldozer	5 days	80	400
Fine	70 m3	4.70	329	Cess Pool	70 m2	15	1050
Powder	80 m3	5.50	440				
Sand	110 m3	2.80	308	Compressor	5 days	25	150
Tiles	300 m2	2.60	780	Rolling machine			
Glass	36 m2	4.5	162	Total of Wages			9053.3
Water	19 Tanks	6	114	Total of Material Cost			
Window Sill	46 m2	8	368	Grand Total JD			23,100.-
Asphalt	-	-	-	Grand Total US \$			72,188.-
Asphalt Mixed	-	-	-				
Solar	-	-	-				
Wood	-	-	-				
Pipes	36 m.r.	1.20	43.2				
Fitting Parts	-	-	110				
4 W.C. seats	-	-	370				
Lavatories	-	-	-				
Total of Material Cost			14,046.70				

CRS-JWB-EX-


US \$ 65% \$ 46,922.- = JD 15,015

VILLAGE SHARE

US \$ 35% \$ 25,266.- = JD 8,085.-

At an exchange rate of \$ 1.- = JD 0.32


SIGNATURE :



 RELIEF, DEVELOPMENT
 & REHABILITATION
 Projects & The World Bank
 CRS Supervisor S.E.D. Projects

Name :

Signature :



 Village Responsible Representative

161

HUWWARA SUB-PROJECT
OUT-PATIENT CLINIC
4D - 006 - 33

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FIRST SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of This report: 1 April 1987

A1. REFERENCE SECTION

4D-006-33
CRS-JWB/USAID Sub-Project No.

US. \$ 58,437.-
Sub-Project estimated cost

CRS JWB in co-operation with HUWARA VILLAGE
Name of Operating Agency

OUT-PATIENT CLINIC
Title of Sub-Project

NABLUS DISTRICT
Area in which Sub-Project is located

NEB-0159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 29,218.50 Equivalent to \$ 29,218.50
(I) CRS AID cash input Village cash input

US \$ 1,157,598.04 20 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ 12,958.35 Village US \$ 17,899.89
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 16,260.15 Village US \$ 11,318.61
(IV) Balance (s) unused (Overspent)

3 **PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID**

- This sub-project involves the construction of an out-patient clinic consisting of five rooms (two rooms to be used by the village council), kitchen, W.C. units, corridor, and a waiting room, the whole totalling about 262m².
- The agreement was signed with the village leadership on 2 Dec. 1986, and work started on 23 January 1987.
- Big progress in work was achieved despite the short period of time, the bad weather and heavy rain, and the shortage of cement. The foundations, walls, partitions, and roofing were successfully completed. Tenders were held selecting a blacksmith and a carpenter.
- The very cooperative village committee is facing some difficulties in raising the rest of the village's share.
- Huwwara villagers are planning to use the building as soon as it is completed. The next Semi-Annual Report will include a Final Report on this Sub-Project.

GA/sk.

164

HUWWARA VILLAGE COUNCIL

TENDER OPENING

=====



QJDS, Jerusalem Tuesday 11 December 1986 No. 0210

الرقم 11 كانون الأول 1986 - 11 كانون الأول 1986 - 11 كانون الأول 1986

Huwwara Village Council in cooperation with the Catholic Relief Services declares the opening of a tender for constructing a health clinic and an abode for the Council, on Monday December 15th, 1986 at 12 noon.

The committee does not undertake to accept the lowest offer.

The Council Head
Jihad El-Hawary

Awardee is to pay the cost of the advertisement in the papers.

GA/mf

مجلس قروي حوارة
فتح مناقصة
يعلن مجلس قروي حوارة وبالتعاون مع خدمات الاغاثة الكاثوليكية
فتح مناقصة ببناء عيادة صحية ومقر للمجلس يوم الاثنين الموافق
15/12/86 الساعة الثانية عشرة ظهرا
اللجنة غير مقيدة بالمال الاسعار
رئيس المجلس
جهاد الحواري
أجود الاعلان في الصحف على من يهتم عليه العطاء

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM WEST BANK & GAZA

Sub-project Proposal Within Package
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-33

Sub-project Location: Huwwara Village - Nablus District - West Bank

Operating Agency : CRS JWB together with Huwwara Village

Sub-project Proposal: Constructing an out-patient health clinic consisting of five rooms (two rooms to be used by the Village Council), kitchen, W.C. units, corridor, and a waiting room, the whole totalling about 262 m2.

Purpose/Objective : To provide Huwwara village with a suitable and improved out-patient health facility.

Expected Results : A suitable out-patient health clinic will be built to serve Huwwara and the surrounding villages. This clinic will replace an existing inadequate and impractical place consisting of a rented room in a private house.

Time needed to complete the sub-project : The clinic will take five months to construct, and will start functioning upon completion of construction.

Supporting Local Authorities : Huwwara Village Council, Nablus District Health Department, Department of Labour and Social Welfare, and the West Bank District Authority.

Cost Estimate : \$ 58,437.- equivalent to J.D. 18,700.- at an exchange rate of approximately J.D. 0.32 = \$ 1.-.

Participants in costs : CRS JWB 50% equivalent to \$ 29,218.50 = J.D. 9,350.-.

Huwwara village 50% equivalent to
\$ 29,218.50 = J.D. 9,350.-.

Construction Plan prepared by : A private architect in consultation with village and CRS JWB and with the approval of the Nablus District Health Department.

Responsibility for sub-project upkeep/maintenance : The clinic will be staffed by Health Department Personnel. The Village Council will assume maintenance and upkeep of the building.

Expected Number of Beneficiaries : Huwwara villagers (8000 persons) in addition to the inhabitants of the surrounding villages (23,500 persons). 166

Brief Narrative:

Huwwara is situated 58 kms. north of Jerusalem and 8 kms. south of Nablus. It has 8000 inhabitants who depend upon agriculture. They grow olives, wheat, barley, cereals, onions, and vegetables. Huwwara has two schools; one for boys and the other for girls. Students from the surrounding villages of Burin, 'Einabous, 'Orif, Jamma`yin, Awarda, Odala, Baita, and Kufor Qallil study in these schools. The village has electricity but still lacks a water system. Villagers still depend on rain water gathered in cisterns through unclean courtyards. The village has no paved interior streets or agricultural roads. It has a Charitable Association and a Village Council.

Huwwara villagers are very active. They exert much effort to improve village conditions. Huwwara has a temporary out-patient health clinic consisting of one rented room. The current clinic is inadequate, impractical, and in bad condition. Villagers from seven surrounding villages are usually treated in this clinic. The clinic is always crowded and many patients are forced to wait outside the room under the hot sun in summer and heavy rain in winter.

Huwwara villagers collected money in order to put-up a new building to house a proper out-patient clinic. They cannot afford the total cost so they approached CRS- AID.

Providing Huwwara with a suitable health clinic will encourage the Health Department, which strongly supports this project, to improve its services. The clinic will be staffed by Health Department Personnel while the Village Council will take care of the building maintenance. Medical equipments and medicines will be provided by the Health Department while the furniture will be provided by the village. The following surrounding villages have no medical services at all and will directly benefit from this proposed sub-project: Einabous (1500 villagers), 'Orif (3000 villagers), Awarta (5000 villagers), 'Odala (2500 villagers), Baita (6000 villagers), Kufor Qallil (2500 villagers) and Yatmah (3000 villagers). At least 95% of Huwwara villagers will contribute towards financing their village's share of the costs.

**PROJECT
IMPLEMENTATION:**

Implementation can start as soon as CRS NEW YORK approval is given and agreement is signed by Huwwara village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-33

This Agreement is between Huwara Village and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB-PROJECT DESCRIPTION:-

Constructing an out-patient health clinic consisting of five rooms (two rooms to be used by the village council), kitchen, W.C. units, corridor, and a waiting room, the whole totalling about 262 m².

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 50% of the total estimated sub-project's cost of US \$ 58,437.- (JD 18,700.-) equivalent to \$ 29,218.50 (JD 9,350.-).
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 50% of the total estimated sub-project's cost of US \$ 58,437.- (JD 18,700.-) equivalent to US \$ 29,218.50 (JD 9,350.-). This amount is provided by US/AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure inter alia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within (150) One Hundred Fifty Days from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The village will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government Authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

1108

- I. The village herewith agrees to hold the Catholic Relief services blameless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

המינהל האזרחי לאזור יהודה ושומון
 الادارة المدنية لمطقة يهودا والسامرة
 משרד העבודה והרווחה
 وزارة الرفاه الاجتماعي
 יחידת מפעלי פיתוח
 مكتب المشاريع القروية

 DEPARTMENT OF LABOUR & SOCIAL WELFARE



 DISTRICT AUTHORITIES



 CATHOLIC RELIEF SERVICES

(Handwritten signature)

 V I L L A G E

DATE: - 2/12/1986

ESTIMATED COST LIST

Sub-project No. 4D-006-33

CRS—JWB/USAID

NAME OF VILLAGE : Huwwara

LOCATION : Nablus

PROJECT DESCRIPTION : Constructing an out-patient health clinic consisting of five rooms (two rooms to be used by the Village Council), kitchen, W.C. units, corridor, and a waiting room, the whole totalling about 262 m².

MATERIAL	Quantity	Price JD	Total JD	WAGES	Quantity	Price JD	Total JD
Black Cement	90 Tons	27	2430	Mason	262 m ²	10	2620
White Cement	18 Bags	6	108	Plasterer	1870 m ²	.60	1122
Steel	7.6 tons	220	1672	Tiling	366 m ²	.70	256.20
Doors	48.5 m ²	24	1164	Pointing	140 m ²	.80	112
Windows	42.5 m ²	22	935	Painting	110.75 m ²	0.80	88.60
Window Fence	43 m ²	6	258	White Washing	870 m ²	.65	565.50
Building Stone	418 m ³	2	836	Miscellaneous	-	-	120
Cement Blocks	9760	16	1561.60	Labourers	45 days	4.5	202.50
Rough Stone	-	-	-	Skilled Labour	28 days	6	168
Gravel, Mixed	110 m ³	3.50	385	Bulldozer	4 days	80	320
Fine	90 m ³	4.20	378				
Powder	60 m ³	4.5	270				
Sand	120 m ³	3.70	444	Compressor	5 days	25	125
Tiles	275 m ²	2.50	687.5	Rolling machine			
Glass	49 m ²	6	294	Total of Wages			5699.80
Water	18 Tank	8	144	Total of Material Cost			13000.
Window Sill	31.5 m ²	7	220.50	Grand Total JD			18,700
Some Furniture	-	-	300	Grand Total US \$			58437.
Asphalt							
Asphalt Mixed							
Solar							
Wood							
Pipes	42 m.r.	1.35	56.70				
4 W.C. Units	-	-	470				
Fitting parts	-	-	110				
Porsalain tiles	46 m ²	6	276				
Total of Material Cost			13,000.30				

CRS—JWB—EX—


US \$ 50% JD 9,350 = U.S. 29,2

VILLAGE SHARE

US \$ 50% JD 9,350 = U.S. 29,2

At an Exchange rate of \$ 0.32 = JD 1.

SIGNATURE :



Name :

Signature :

Village Responsible Representative

Name :

SHU'AB MUSMAR & OTHERS SUB-PROJECT

ELECTRIFICATION

4D - 006 - 34

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM AND WEST BANK

RURAL VILLAGE COMMUNITY DEVELOPMENT PROGRAM
FIRST SEMI-ANNUAL SUB-PROJECT PROGRESS REPORT

Date of This report: 1 April 1987

1. REFERENCE SECTION

4D-886-34
CRS-JWB/USAID Sub-Project No.

US. \$ 126,742
Sub-Project estimated cost

CRS JWB in co-operation with SHU'AB MUSMAR AND OTHER VILLAGES
Name of Operating Agency

ELECTRIFICATION
Title of Sub-Project

HEBRON DISTRICT
Area in which Sub-Project is located

NEB-8159-G-SS-5123-00
Funding Agency Code Number

2. EXPENDITURE SECTION

US \$ 72,243 Equivalent to \$ 54,499
(I) CRS AID cash input Village cash input

US \$ 1,157,598.04 20 January 1987
(II) Funds received to date Date of last transmittal

CRS AID US \$ 15,225.17 Village US \$ 23,533.10
(III) Sub-Project expenditure (s) to date

CRS AID US \$ 57,017.83 Village US \$ 30,965.90
(IV) Balance (s) unused

3 PROGRESS OF (SUB) PROJECT SECTION CRS-JWB/USAID

- This Sub-Project calls for providing Shu'ab Musmar and five other surrounding Khirabs (small villages) with an internal electrical network throughout the villages. These villages belong to Raq'a Area and their line is going to be connected with Raq'a's transformer.
- The agreement covering this sub-project was signed with the village leadership on 3 March 1987. Work started on 16 March 1987 and is expected to be completed by June 1987.
- Much work has been achieved despite the very short period of time. Most of the poles, wires, rods, and electrical parts are on the site. 30% of the holes were dug for installing the poles.
- An electrician was chosen and will soon start working.
- The next Semi-Annual Report will include the final Report on this Sub-Project.

GA/sk.

CATHOLIC RELIEF SERVICES - USCC
JERUSALEM WEST BANK & GAZA

Sub-project Proposal Within Package
Project No. CRS JWB - 4D-006

Sub-project Number : CRS JWB - 4D-006-34

Sub-project Location: Shu'ab Musmar & other Villages - Hebron District - West Bank

Operating Agency : CRS JWB together with Shu'ab Musmar and other Villages

Sub-project Proposal: Providing Shu'ab Musmar and five other surrounding Khirabs (villages) with an electrical distribution board, an electrical transmission tower and an internal electrical network throughout the villages. The five other Khirabs (villages) are El-Dwair, 'Ihraiz, Zif, El-Fahjeh, and Khillat Ghnaim. These villages belong to Raqa' Area and their line is going to be connected with Raqa's transformer.

Purpose/Objective : To make electrical power available in these villages for the first time.

Time needed to complete the sub-project : Approximately 3 months.

Supporting Local Authorities : The villages committee, Department of Labour and Social Welfare, and the District Authorities

Cost Estimate : \$ 126,742.- = J.D. 41,825.- at an exchange rate of approximately = \$ 1.- J.D. 0.33

Participants in costs : CRS JWB 57% equivalent to \$ 72,243.- = J.D. 23,840.-
The villages 43% equivalent to \$ 54,499.- = J.D. 17,985.-.

Plan prepared by : An electrical engineer in consultation with the villages and subject to the approval of CRS JWB and the West Bank Power Officer.

Responsibility for sub-project upkeep/maintenance : The villages will be responsible for maintaining the electrical net.

Expected Number of Beneficiaries : 2700 persons.

Brief Narratives:-

Shu'ab Musmar and the five surrounding khirabs (villages) are located about 13 kms south east of Hebron. They are very poor villages and some inhabitants still live in caves.

These villages have a population of 2700 persons distributed as the following: Shu'ab Musmar 400, El-Dwair 500, 'Ihraiz 600, Zif 500, El-Fahjeh 500, and Khillat Ghnaim 200. Most of the villagers are small farmers. They grow wheat, barley, tomatoes and olives in their fields. The others work as labourers in Hebron area.

These villages are still without paved interior streets, out-patient health clinics, postal services, community centers, public transportation, water systems, electricity, and even schools (they go to Raqa' and Yatta schools, 6 and 8 kms away consequently). The villagers are very eager to develop their villages. They find development impossible without electricity. They approached CRS/AID for help.

This sub-project calls for providing Shu'ab Musmar and the five surrounding villages with an electrical distribution board, an electrical transmission tower, and an internal electrical network throughout the villages. These villages belong to Raqa' Area and their line is going to be connected with Raqa's transformer.

Once this sub-project is implemented, the standard of living in these villages will be much improved. School children will be able to study in well lighted rooms rather than on the dim light of kerosene lanterns. Electrical appliances mainly refrigerators may then be used and electrical machines could replace manual ones.

**PROJECT
IMPLEMENTATION:**

Implementation can start as soon as CRS NEW YORK approval is given and agreement is signed by Shu'ab Musmar village, the Ministry of Labour and Social Affairs and the West Bank District Authorities.

175

SELF HELP COMMUNITY DEVELOPMENT SUB PROJECT AGREEMENT

UNDER PROJECT NO. CRS JWB 4D-006

COVERING

SUB PROJECT CRS JWB - 4D-006-34

This Agreement is between Shu'ab Musmar & other villages and the Catholic Relief Services. According to the conditions of this Agreement as stated below, the Catholic Relief Services has offered to assist in the following project:-

A. SUB-PROJECT DESCRIPTION:-

Providing Shu'ab Musmar and five other surrounding Khirabs (villages) with an electrical distribution board, an electrical transmission tower and an internal electrical network throughout the villages. The five other Khirabs (villages) are : El-Dwair, 'Ihraiz, Zif, El-Fahjeh, and Khiilat Ghnaim. These villages belong to Raqa' Area and their line is going to be connected with Raqa's transformer.

B. THE VILLAGE WILL PROVIDE AND ABIDE BY THE FOLLOWING:-

1. At least 43% of the total estimated sub-project's cost of US \$ 126,742.- (JD 41,825.-) equivalent to \$ 54,499.- (JD 17,985.-).
2. A committee to supervise daily all work on the project and keep records of labour and material used.

C. THE CATHOLIC RELIEF SERVICES WILL PROVIDE THE FOLLOWING:-

1. Up to 57% of the total estimated sub-project's cost of US \$ 126,742.- (JD 41,825.-) equivalent to US \$ 72,243.- (JD 23,840.-). This amount is provided by US/AID.
2. The Field Project Supervisor with overall responsibility for the supervision of the project's implementation, proper use of all monies spent and to assure interalia fair prices for material.

D. The project should be started within (2) two weeks of the signing of the Agreement and completed within (90) Ninety days from the first work day of the project.

E. The village will be responsible for the project maintenance and upkeep.

F. The villlage will have collected and have at its disposal at least 80% of its share before starting the implementation of the project which will start with its share in full.

G. The village agrees to comply with all Standard Provisions requirements of the AID Grant applicable to sub-agreements under such Grant.

H. The village assumes all liability for the assessment, collection and deposit with appropriate Government Authorities of any and all sums required for taxes, local or otherwise, due on wages or salaries or the sale of goods, materials or otherwise.

176

- I. The village herewith agrees to hold the Catholic Relief services blameless from any and all liability, claims, suits at law in equity or otherwise arising out of demands to either persons or property except those arising out of the negligence of the Catholic Relief Services.
- J. The Catholic Relief Services will comply with this Agreement unless the village does not fulfill the stated terms of the Agreement in which case, the Catholic Relief Services is released completely from all commitments and obligations of the Agreement.

SIGNATORIES

الإدارة المدنية لمنطقة يهودا والسامرة
 مديرية مكتب المشاريع القروية
 فرمياش دودزه

[Handwritten signature]


DEPARTMENT OF LABOUR & SOCIAL WELFARE

[Handwritten signature]

DISTRICT AUTHORITIES



CATHOLIC RELIEF SERVICES



V I L L A G E

[Handwritten signature]

[Handwritten signature]

[Handwritten signature]

DATE:- 3/2/1987

ESTIMATED COST LIST

4D-886-34

Sub-project Description: Providing Shu'ab Musmar and five other surrounding Khirabs (village) with an electrical distribution board, an electrical transmission tower and an internal electrical network throughout the villages.

	<u>QUANTITY</u>	<u>UNIT COST</u> <u>J.D.</u>	<u>TOTAL COST</u> <u>J.D.</u>
Distribution Board	1	1200	1,200
Iron tower 12 meters long	1	500	500
Distribution cables	-	-	750
Wooden Poles (10 meters)	80	45	3,600
Wooden Poles (8.5 meters)	74	33	2,442
Aluminum Wires (90 m12)	7000 KG.	1.10	7,700
Aluminum Wires (95 m13)	8500 meters	0.80	6,800
Wooden screws	1000	0.80	800
Screws (4.5 cm)	1500	0.40	600
Screws (9.5 cms)	1000	0.50	500
Lamps	100	25	2,500
Electric Supplies including conductors, rods etc.			1,000
Electrician			5,643
TOTAL (J.D.)			----- 41,825

Total cost estimate = \$ 126,742.- = J.D. 41,825.- At an exchange rate of \$ 1 = J.D. 8.33

CRS SHARE 57% = \$ 72,243.- = J.D. 23,840.-

VILLAGE SHARE 43% = \$ 54,499.- = J.D. 17,985.-

178
