

PD-AAI-084

388-0030
3880030005302

BANGLADESH AGRICULTURAL DEVELOPMENT CORPORATION

বাংলাদেশ কৃষি উন্নয়ন কর্পোরেশন

②

FERTILIZER STORAGE CONSTRUCTION PROJECT

U.S. AID LOAN NO. 388 - T - 011

সার গুদাম নির্মাণ প্রকল্প

যুক্তরাষ্ট্র আন্তর্জাতিক উন্নয়ন সংস্থা ঋণ নং ৩৮৮-টি-০১১

PROGRESS REPORT NO : FSCP - 003 - 33

FOR THE MONTH OF
JANUARY, 1980

AMMANN & WHITNEY
CONSULTING ENGINEERS
NEW YORK DACCA

IN ASSOCIATION WITH
PROKAUSHALI SANGSAD LTD.

আসমান এন্ড হুইটনি
উপদেষ্টা প্রকৌশলী
নিউ ইয়র্ক ঢাকা

সহযোগী
প্রকৌশলী সংসদ লিঃ

BANGLADESH AGRICULTURAL DEVELOPMENT CORPORATION
 FERTILIZER STORAGE CONSTRUCTION PROJECT
 U.S. AID LOAN 388-T-011

AMMANN & WHITNEY
 CONSULTING ENGINEERS

Monthly Progress Report No.33
 January 1980

1. General Project Assessment:

	Last Month	This Month
- Project Completion: Work Item Assessment	74.99%	78.33%
Based on Payment	69.53%	71.00%

Percentage Completion as of 31 January 1980:

M.T.	Total Items	Withdrawn or Cancelled	Less 50%	50-60%	61-70%	71-80%	81-90%	91-99%	100%
500	20	4	-	3	-	2	2	2	7
1000	6	1	-	1	-	-	2	1	1
2000	5	1	-	1	-	2	-	1	-
3000	3	1	-	-	1	-	1	-	-
Total	34	7	0	5	1	4	5	4	8
Last Month	34	6	2	4	3	6	3	3	7

- Sites for which FAR withdrawn: Ullapara, Chowmuhani, Munshiganj, Dhamoirhat.
- Site Cancelled : Narail; Sirajganj, Lohajang.
- A total of eight sites have been handed over to BADC.

- Consultant's prediction on project completion:

February	March	April	May
Santahar	Lakshmipur	Rupganj	Taltala
Gabtali	Feni	Kalkini	Manikganj
Gaibandha	Shibpur		Tepakhola
	Jhinaidah		Madaripur
			Shahjadpur
			Adamdighi
			Saghata
			Rangpur
			Akkelpur
			Kurigram

- Adamdighi: Due to slow progress and neglect of work the site is under observation for taking action as per contract. Contractor informed in writing of the consequences to follow for his failure to demonstrate initiative and drive to complete the work.

- Madaripur: Contractor given fifteen days time to accelerate work and meet the Engineer on the 18 February 1980 with a definitive program to complete the work. His failure to show sufficient progress in the meantime will be cause for recommending termination of Contract.
- Rugganj: The Engineer has recommended to BADC to take up the remaining works by force account. Contractor allowed 15 days time by BADC to accelerate work or face action.
- Taltala: Contractor's field activity is under observation by the Engineer and action to be taken will be decided after visit to the site by the Engineer on 8 February 1980.
- Shahjadpur and Kurigram : Following a meeting between the Engineer and the Contractor regarding progress at both the sites the Contractor has engaged sufficient labours and procured materials to expedite work. Progress of work is under continuing observation.

2. Meetings:

- 07.01.80 CE(C) Progress of Work

3. Soils & Materials Testing:

The testing laboratories of Ammann & Whitney at Dacca, Bogra and Faridpur areas continued their operations during the month of January 1980 to keep a constant check over the qualities of materials incorporated in works at site. Due to completion of most of the sites at Jessore area, the testing laboratory at Jessore shifted to Faridpur area from January 1980. The Soils and Materials Engineer continued touring sites for spot checks and verification. Laboratory personnel were attending field tests and concrete pouring as required.

Following tests were performed during the month:

	<u>Dacca</u>	<u>Bogra</u>	<u>Jessore</u>
Compressive Strength of Concrete	36	188	56
Field Density Tests	23	39	12
Sieve Analysis of Sand	3	11	-
Gradation Test of Brick Chips	-	2	9
Moisture-Density Relationship	5	2	1

4. Consultant Staff Status:

	Personnel Engaged	Man-Month To 31 December 1979		Personnel Engaged	Man-Month 1 Jan 80 to 30 June 80	
		Allocated	Utilized		Allocated	Utilized
Consultant	1	5	3.9384	-	-	-
Structural Engineer	1	2	2.0000	-	-	-
Senior Engineer	-	-	-	1	6	1.0487
Office Engineer	1	12	10.6385	1	4	1.0487
S/M Engineer	1	10	10.5308	1	3	1.0487
Technician	5	48	48.2077	5	25	3.5949
Laboratory Assistant	5	48	45.0154	4	4	1.9846
Draftsman	2	18	22.8641	2	9	2.0974
Senior Accountant	1	12	11.5513	1	6	1.0487
Accountant	1	12	11.2949	1	6	1.0487
Senior Field Engineer	3	32	34.7923	3	18	2.7462
Field Engineer	7	56	55.2128	4	12	3.2077
Senior Inspector	4	33	30.8461	4	20	3.7949
Inspector	31	138	304.3821	21	76	17.4359
Administrative Officer	1	12	8.8718	1	6	1.0487
Others	-	535	454.8745	-	179	35.7256
		<u>973</u>	<u>1,055.0207</u>		<u>374</u>	<u>76.8794</u>
		====	=====		====	=====

5. Engineers Cost Incurred: (In U.S. Dollar)

<u>Line Item</u>	<u>Budget Amount</u> */	<u>Cumulative to 31 December 79</u>	<u>Month of January 80</u>	<u>Cumulative to 31 January 80</u>
Services in Home Office	16,389	16,389	-	16,389
Services in Bangladesh	409,725	402,806	10,892	413,698
International Travel	54,752	39,718	-	39,718
Housing, Allowances, Per Diem, etc.	113,882	107,012	1,650	108,662
Logistic Costs	146,975	140,066	5,180	145,246
Supporting Staff	320,977	275,328	14,667	289,995
Misc. Direct Expenses	52,637	45,834	-	45,834
Fixed Fee	99,304	99,304	3,537	102,841
Reimbursable Cost Items	51,374	62,918	-	62,918
	<u>U.S. \$ 1,266,515</u>	<u>1,189,375</u>	<u>35,926</u>	<u>1,225,301</u>
	=====	=====	=====	=====

*/ Contract Amount to 31 December 1979. Amendment No.2 extending Contract beyond 31 December 1979 to 30 June 1980 pending action with BADC.

6. <u>Project FAR Amount:</u> Funding	\$ 5,250,000
Original FAR approved for Construction	Tk. 5,43,14,437
Cost of deleted sites: (Chowmuhani, Munshiganj, Lohajang, Dhamoirhat, Narail, Sirajganj and Ullapara). Refer AID Implementation Letter No.21.	1,23,34,359
	<u>Tk. 4,19,80,078</u>
	@ 15 \$ 2,798,672
Engineering	\$ 1,266,515
	<u>Total \$ 4,065,187</u>

7. Project Expenditures: (U.S. Dollar)

	<u>Previous Month</u>	<u>Current Month</u>	<u>Cumulative</u>
Engineering	\$ 1,189,375	\$ 35,926	\$ 1,225,301
FAR Financing*	(Tk.53,26,049.29)	-	350,855.01
			<u>\$ 1,576,156.01</u>

*Reference AID letter 29 June 1979. Payments made to be adjusted against 100% completed sites (Joydebpur, Araihasar, Srinagar, Monirampur, Naidigram, Kaliganj, Jessore(Sadar), Ghoraghat total Tk.90,11,675). Balance to be invoiced for reimbursement Tk.36,85,625.80.

8. Outstanding Issue:

Finalizing contract amendment with Consultant for extension to 30 June 1980.

Attachments: Monthly Statements
 Sitewise Weighted Percentage Completion
 Total Weighted Project Completion
 Sites Completed and Possession Handed Over to BADC(Storage)
 Site Reports and Critical Construction Items **Outstanding**
 Construction Progress Bar Diagram
 Site wise Overall Progress

Submitted by: _____

George A. Pecht
 PROJECT MANAGER
 ANMANN & WHITNEY

Distribution:

Chairman, BADC	-	1
CE(C), BADC	-	20
USAID/Dacca	-	5
Prokaushali Sangsad Ltd.	-	1
Project Engineer/Dacca	-	1
Project Engineer/Bogra	-	1
Sr. Field Engineers/Field Engineers	-	8
Office Engineer/S&M Engineer/Adm. Officer	-	3
New York	-	1
File	-	7

MONTHLY STATEMENT SHOWING THE AMOUNT PAID TO THE
CONTRACTORS AGAINST CONSTRUCTION WORKS UNDER FSCP USAID

Name of the Month: January 1980

Sl. No.	Description of Work	MT	Cost of Work As per W/O (Tk)	Amount Paid to the Contractor up to previous month (Tk)	Amount Paid to Contractor during the month (Tk)	Total Amount paid to the Contractor (Tk) (Col. 4&5) ^{2/}	Financial Progress % _{6/3x100}
1	2		3	4	5	6	7
1.	Lakshampur (1000)		20,98,656.19	1/ 14,47,208.41	-	14,47,208.41	68.9
2.	Feni (3000)		43,60,703.77	29,56,257.04	-	29,56,257.04	67.8
3.	Lohajang (500)		16,11,086.97	4,11,768.01	-	4,11,768.01	Cancelled
4.	Taltala (1000)		26,15,002.05	18,05,933.00	-	18,05,933.00	69.1
5.	Srinagar (500)		16,74,677.50	1/ 14,29,065.80	1,63,069.50	15,92,135.75	95.0 5/
6.	Manikganj (1000)		24,96,994.07	1/ 13,63,337.00	-	13,63,337.00	54.6
7.	Rupganj (500)		13,69,074.51	10,60,048.00	-	10,60,048.00	77.4
8.	Araihazar (500)		15,81,348.14	15,66,069.72	-	15,66,069.72	99.0 4/
9.	Joydebpur (500)		16,36,433.17	16,27,518.00	-	16,27,518.00	99.5
10.	Shibpur (500)		14,59,391.50	12,11,295.00	-	12,11,295.00	83.0
11.	Monirampur (500)		15,33,989.61	15,12,653.39	-	15,12,653.39	98.0 5/
12.	Narail (500)		15,22,548.41	1,65,349.00	-	1,65,349.00	Cancelled
13.	Jessore(S) (500)		13,43,140.90	12,80,798.70	-	12,80,798.70	95.4 5/
14.	Kaliganj (1000)		20,63,506.20	19,33,291.73	-	19,33,291.73	93.7 5/
15.	Jhinaidah (500)		15,23,477.89	10,71,350.20	1,02,599.64	11,73,949.84	77.0
16.	Tepakhola (2000)		37,93,339.20	1/ 18,25,130.00	-	18,25,130.00	48.1
17.	Madaripur (500)		15,92,215.90	7,28,100.00	-	7,28,100.00	45.7
18.	Kalkini (500)		16,04,294.44	1/ 9,16,644.11	-	9,16,644.11	57.1
19.	Shahjadpur (2000)		31,16,613.90	21,51,095.30	-	21,51,095.30	69.0
20.	Ullapara (2000)		33,88,671.05	4,38,280.00	-	4,38,280.00	12.9
21.	Sirajganj (500)		12,77,645.04	70,701.64	3/ -	70,701.64	Cancelled
22.	Nandigram (500)		16,66,607.52	1/ 16,57,290.67	-	16,57,290.67	99.4 4/
23.	Santahar (1000)		26,73,126.02	23,79,224.30	-	23,79,224.30	89.0
24.	Akkelpur (500)		15,25,518.90	7,11,895.10	1,36,493.93	8,48,389.03	55.6
25.	Adamdighi (500)		15,60,263.56	1/ 8,63,548.74	-	8,63,548.74	55.3
26.	Gabali (500)		15,81,529.96	1/ 14,30,864.92	-	14,30,864.92	90.5
27.	Saghata (500)		13,98,095.64	8,57,138.01	1,82,000.00	10,39,138.01	74.3
28.	Ghoraghat (500)		14,72,971.34	12,70,510.52	78,908.90	13,49,419.42	91.6
29.	Gaiband' (2000)		38,36,477.54	1/ 33,43,900.62	3,06,587.31	36,50,487.93	95.2
30.	Rangpur(S) (3000)		41,27,435.50	1/ 23,22,190.43	2,41,000.00	25,63,190.43	62.1
31.	Kurigram (2000)		33,20,106.50	19,11,709.80	3,01,000.00	22,12,409.80	66.0
Total (Exclude Cancelled Contracts)			6,67,88,964.89	4,37,20,167.16	15,11,659.28	4,52,31,526.58	68.0
			6,23,77,684.47			4,45,83,707.93	71.0%

1/ Change Order Amount

2/ Includes 10% Retention

3/ Recommended to BADC for Payment

4/ Payment made as per actual work done

5/ Final Bill not yet paid

FERTILIZER STORAGE CONSTRUCTION PROJECT
CONSTRUCTION PROJECT CHART
WEIGHTED PERCENTAGE COMPLETION

Sl. No.	Site	Site Development		Godown		Storekeeper Quarter		Inspection Building		Darwan Quarter		Sanitary		Percent Total
		Wt	%	Wt	%	Wt	%	Wt	%	Wt	%	Wt	%	
1.	Lakshmipur	2.19	24	47.44	85	17.46	96	4.99	99	8.69	98	2.47	83	83.24
2.	Feni	2.66	23	62.27	88	8.68	95	2.24	96	3.83	96	1.35	67	81.03
3.	Lohajang	Cancelled												
4.	Taltala	3.33	44	46.88	80	17.22	95	4.59	96	7.59	95	1.70	53	81.32
5.	Srinagar	Complete												
6.	Manikganj	7.67	68	30.36	52	8.52	53	3.56	80	5.16	71	0.70	29	55.97
7.	Rupganj	2.51	35	37.35	74	24.42	89	-	-	11.07	91	1.74	59	77.10
8.	Araihazar	Complete												
9.	Joydebpur	Complete												
10.	Shibpur	9.16	93	44.51	91	25.04	99	-	-	11.13	99	4.28	95	94.12
11.	Monirampur	Complete												
12.	Narail	Cancelled												
13.	Jessore (S)	Complete												
14.	Kaliganj	Complete												
15.	Jhinaidah	5.41	39	41.10	90	24.32	100	-	-	10.56	99	5.33	100	86.72
16.	Tepakhola	8.36	53	34.43	55	8.92	82	2.53	87	4.10	85	-	-	58.36
17.	Madaripur	4.11	32	22.83	49	16.74	66	-	-	8.41	75	-	-	52.09
18.	Kalkini	3.55	35	36.58	75	23.76	92	-	-	11.10	96	-	-	74.99
19.	Shahjadpur	2.46	23	50.90	77	10.31	85	2.80	88	4.57	87	0.68	25	71.72
20.	Ullapara	2.35	17	16.66	26	0.36	3	0.16	6	0.25	5	-	-	19.78
21.	Sirajganj	Cancelled												
22.	Nandigram	Complete												
23.	Santahar	5.77	97	59.34	100	17.96	99	4.71	99	7.80	99	3.64	96	99.22
24.	Akkelpur	2.88	25	27.01	57	19.56	76	-	-	8.70	76	-	-	58.15
25.	Adamdighi	1.34	31	25.76	50	15.70	56	-	-	11.08	92	2.53	64	56.41
26.	Gabali	4.51	45	47.08	100	26.99	99	-	-	11.91	99	3.23	95	93.72
27.	Saghata	3.82	69	38.34	79	27.07	94	-	-	12.30	97	1.35	33	82.88
28.	Ghoraghat	9.07	100	46.53	100	27.75	100	-	-	12.05	100	4.60	100	Complete
29.	Gaibandha	11.37	99	67.03	100	11.52	100	2.98	100	4.96	100	1.53	90	99.39
30.	Rangpur(S)	5.12	64	50.64	68	7.85	88	2.24	95	3.58	91	0.65	33	70.08
31.	Kurigram	3.43	64	56.52	78	9.52	81	3.26	100	4.54	90	0.44	18	77.81

Fertilizer Storage Construction Project
Total Weighted Project Completion

For Month January 1980

S1. No.	DESCRIPTION OF WORK MT	COST OF WORK AS PER W/O (TK)	FAR AMOUNT	WEIGHTED PERCENT	PERCENT COMPLETE TO DATE	WEIGHTED PERCENT COMPLETE
1.	Lakshmipur (1000)	19,51,361.46	16,05,453	3.04	83.24	2.53
2.	Feni (3000)	43,60,703.77	31,67,985	6.81	81.03	5.52
3.	Lohajang (500)	16,11,086.97	Cancelled	2.51	Cancelled	-
4.	Taltala (1000)	24,97,758.51	17,03,440	3.89	81.32	3.16
5.	Srinagar (500)	15,67,092.66	11,67,469	2.44	100.00	2.44
6.	Manikganj (1000)	21,79,612.87	19,21,136	3.40	55.97	1.90
7.	Rupganj (500)	13,69,074.51	10,94,123	2.13	77.10	1.65
8.	Araihazar (500)	14,77,221.56	10,77,300	2.30	100.00	2.30
9.	Joydebpur (500)	13,97,470.80	10,72,079	2.18	100.00	2.18
10.	Shibpur (500)	14,59,391.50	11,50,145	2.28	94.12	2.15
11.	Monirampur (500)	15,33,989.61	11,22,470	2.39	100.00	2.39
12.	Narail (500)	15,22,548.41	Cancelled	2.37	Cancelled	-
13.	Jessore (Sadar) (500)	13,43,140.90	9,85,258	2.09	100.00	2.09
14.	Kaliganj (1000)	20,63,506.20	15,36,953	3.22	100.00	3.22
15.	Jhinaidah (500)	15,23,477.89	11,05,120	2.37	86.72	2.06
16.	Tepakhola (2000)	36,24,851.20	28,98,527	5.65	58.36	3.30
17.	Madaripur (500)	15,92,215.90	11,30,843	2.48	52.09	1.29
18.	Kalkini (500)	15,25,001.00	11,06,893	2.38	74.99	1.78
19.	Shahjadpur (2000)	31,16,613.90	24,54,563	4.86	71.72	3.49
20.	Ullapara (2000)	33,88,671.05	27,29,189	5.28	19.78	1.04
21.	Sirajganj (500)	12,77,645.04	Cancelled	1.99	Cancelled	-
22.	Nandigram (500)	14,09,585.07	10,13,600	2.20	100.00	2.20
23.	Santahar (1000)	23,87,136.02	15,59,452	3.72	99.22	3.69
24.	Akkelpur (500)	15,25,518.90	11,12,864	2.38	58.15	1.38
25.	Adamdighi (500)	14,37,024.62	10,31,552	2.24	56.41	1.26
26.	Gabtali (500)	14,38,518.78	10,40,720	2.24	93.72	2.10
27.	Saghata (500)	13,98,095.64	10,02,544	2.18	82.88	1.81
28.	Ghoraghat (500)	14,72,971.34	10,36,546	2.30	100.00	2.29
29.	Gaibandha (2000)	35,77,040.54	23,81,801	5.58	99.39	5.55
30.	Rangpur (Sadar) (3000)	37,99,528.50	30,01,208	5.92	70.08	4.15
31.	Kurigram (2000)	33,20,106.50	25,00,034	5.18	77.81	4.03

6,41,47,961.62	4,47,09,267	100.00	Total %	72.95
U.S. \$	29,80,618		Adjusted %	78.33

Deletion:

Sirajganj, Narail & Lohajang 6.87

93.13

Sites completed and possession handed over to BADC(Storage)

1. Site: Joydebpur

Contract No.	: DAC5NBIIB9	Date Work Commenced	:12-02-78
Contractor	: M.S. Khan	Contract Completion	:10-08-78
Contract Price	: Tk.13,97,470.80	1st Revised Completion	:15-12-78
Change Order No.1	: Tk. 2,50,444.50	Actual Completion	:16-04-79
Revised Contract Price:	Tk.16,36,433.17	Handed Over Possession	:05-05-79
F.A.R. Amount	Tk.10,72,079.00		

2. Site: Araihasar

Contract No.	: DAC5NBIIB8	Work Commenced	:02-03-78
Contractor	: Taleb Ali Bhuiyan	Contract Completion	:28-08-78
Contract Price	: Tk.14,77,221.56	3rd Revised Completion	:30-07-79
Change Order No.1	: Approved	Actual Completion	:27-07-79
Revised Contract Price:	Tk.15,81,348.74	Handed Over Possession	:30-07-79
F.A.R. Amount	: Tk.10,77,300.00		

3. Site: Nandigram

Contract No.	: BCC5NBIIB5	Work Commenced	:05-05-78
Contractor	: Fragati Builders	Contract Completion	:31-10-78
Contract Price	: Tk.14,09,585.07	4th Revised Completion	:22-08-79
Change Order No.1	: Approved	Actual Completion	:13-08-79
Revised Contract Price:	Tk.16,66,607.52	Handed Over Possession	:22-08-79
F.A.R. Amount	: Tk.10,13,600.00		

Note: Godown was used for
storage of Fertilizer
from 26-06-79

4. Site: Srinagar

Contract No.	: DAO5NBIIB4	Date Work Commenced	:02-03-78
Contractor	: Taleb Ali Bhuiyan	Contract Completion	:28-08-78
Contract Price	: Tk.15,67,092.66	3rd Revised Completion	:04-09-79
Change Order No.1	: Approved	Actual Completion	:04-09-79
Revised Contract Price:	Tk.16,74,677.50	Handed Over Possession	:04-09-79
F.A.R. Amount	: Tk.11,67,469.00		

5. Site: Monirampur

Contract No.	: JEO5NBIIC1	Date Work Commenced	:04-05-78
Contractor	: National Constn.	Contract Completion	:31-10-78
Contract Price	: Tk.15,33,989.61	2nd Revised Completion	:31-08-79
Change Order No.1	:	Actual Completion	:15-10-79
Revised Contract Price:		Handed Over Possession	:15-10-79
F.A.R. Amount	: Tk.11,22,470.00		

6. Site: Kaliganj

Contract No.	: JE10NBIIC4	Date Work Commenced	:22-06-78
Contractor	: National Constn.	Contract Completion	:18-03-79
Contract Price	: Tk.20,63,506.20	2nd Revised Completion	:31-10-79
Change Order No.1	:	Actual Completion	:20-11-79
Revised Contract Price:		Handed Over Possession	:22-11-79
F.A.R. Amount	: Tk.15,36,953.00		

7. Site: Jessore(Radar)

Contract No.	: JEC5NCIIC3	Date Work Commenced	:01-06-78
Contractor	: Allied Cons- truction & Co.	Contract Completion	:28-11-78
Contract Price	: Tk.13,43,140.00	3rd Revised Completion	:30-11-79
Change Order No.1	:	Actual Completion	:28-11-79
F.A.R. Amount	: Tk. 9,85,258.00	Handed Over Possession	:28-11-79

8. Site: Ghoraghat

Contract No.	: D105NCIIC2	Date Work Commenced	:23-05-78
Contractor	: Waheed & Co.Ltd.	Contract Completion	:19-11-78
Contract Price	: Tk.14,72,971.34	4th Revised Completion	:31-12-79
Change Order No.1	:	Actual Completion	:30-01-80
F.A.R. Amount	: Tk.10,36,546.00	Handed Over Possession	:30-01-80

Monthly Progress Report
January 1980

Site: #1 Lakshmipur

Contractor: Feni Ideal Construction

Contract Price	: Tk.19,51,361.46	Date Work Commenced	: 23.06.1978
FAR Amount	: Tk.16,05,456.00	Scheduled Completion Date	: 19.03.1979
Revised Contract Price	: Tk.20,98,656.19	3rd Revised Completion Date	: 31.12.1979
Payments To Date	: Tk.14,47,208.41	Estimated Completion Date	: 31.03.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development		Access Road & Parking Area. Boundary Wall. Final clean-up & grading.
Godown	25% floor cast, 100% apron, preparation of remaining floor.	50% floor, doors, ventilators, lime concrete, white washing.
Storekeeper's Quarter	No activity.	doors/windows (G.F.). doors/windows (F.F.).
Darwan's Quarter	No activity.	doors/windows.
Inspection Building	No activity.	doors/windows.
Sanitary Work	Installed W.C. pan in Darwan's Qtr. Installed W.C. pan in Storekeeper's Qtr. Installed W.C. pan in Inspection Building.	20% work for Darwan's Qtr. 20% work for Storekeeper's Qtr. (Ground Floor). 20% work for Storekeeper's Qtr. (1st Floor). 20% work for Inspection Building. Tubewells & platform.

Percentage Completion This Period : 9.09% To Date: 83.24

Remarks: Contractor should start installation of tubewells and take more initiative to complete the remaining work. Estimated completion date has been revised from 29 February to 31 March due to Contractor's slow progress.

Monthly Progress Report
January 1980

Site: #2 Feni

Contractor: Siddique & Co. Ltd.

Contract Price	: Tk.43,60,703.77	Date Work Commenced	: 23.06.1978
FAR Amount	: Tk.31,67,985.00	Scheduled Completion Date	: 23.09.1979
Revised Contract Price:	Tk. -	2nd Revised Completion Date:	31.12.1979
Payments To Date	: Tk.29,56,257.04	Estimated Completion Date	: 31.03.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	400 rft. boundary wall done in west side.	Part of site filling, boundary wall, access road, etc.
Godown	50% floor cast and preparation for the remaining portion in progress. Continued brickwork.	50% floor, L.C. on roof, installation of doors, white wash etc.
Storekeeper's Quarter	Started white wash and applied one coat.	Part of door/window installation.
Darwan's Quarter	Started white wash and applied 1st coat.	Part of door/window installation.
Inspection Building	Started white wash and applied 1st coat.	Part of door/window installation.
<u>Sanitary:</u>		
Storekeeper's Quarter	No activity.	Sanitary installation in 1st floor.
Darwan's Quarter	No activity.	25% sanitary installation.
Inspection Building	No activity.	25% sanitary installation. 50% work of septic tanks & soak wells. Installation of tube wells and platform.

Percentage Completion This Period: 8.38% To Date: 81.03%

Remarks: Contractor allotted 30 MT of cement. Site can be handed over end of March 1980.

Monthly Progress Report
January 1980

Site: #4 Taltala

Contractor: M/s. M. Omar Meah & Sons

Contract Price	: Tk.24,97,758.51	Date Work Commenced	: 02.03.1978
FAR Amount	: Tk.17,03,440.00	Scheduled Completion Date	: 26.11.1978
Revised Contract Price	: Tk.26,15,002.55	3rd Revised Completion Date	: 31.12.1979
Payments To Date	: Tk.18,05,933.00	Estimated Completion Date	: 31.05.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity.	56% work is pending.
Godown	Remaining 25% roof slab cast. Plastering was in progress.	R.C.C. floor, wall plaster, door fixing L.C. etc.
Storekeeper's Quarter	No activity.	Part of woodwork and sanitary fittings.
Inspection Building	No activity.	Part of woodwork and sanitary fittings.

Percentage Completion This Period: 4.7% To Date: 81.32%

Remarks: Contractor allowed 15 days time to expedite work or face as per Contract.

Monthly Progress Report
January 1980

Site: #6 Manikganj

Contractor: Md. Siddique Khan

Contract Price	: Tk.21,79,612.87	Date Work Commenced	: 25.06.1978
FAR Amount	: Tk.19,91,136.00	Scheduled Completion Date	: 21.03.1979
Revised Contract Price	: Tk.24,96,994.07	2nd Revised Completion Date	: 31.12.1979
Payments To Date	: Tk.13,63,337.00	Estimated Completion Date	: 31.01.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity.	About 30% site development work is pending.
Godown	32 columns cast up to canopy level including brickwork.	All work above canopy level including canopy casting.
Storekeeper's Quarter	Complete brickwork up to 1st floor lintel and shuttering for the lintels was in progress.	All work above 1st floor lintel including woodwork and sanitary fittings.
Darwan's Quarter	Complete roof casting.	L.C. woodwork and sanitary fittings.
Inspection Building	No activity.	L.C. woodwork and sanitary fittings.

Percentage Completion This Period: 4.06% To Date: 55.97%

Remarks: Progress not satisfactory due to shortage of materials. Contractor allotted 30 MT of cement by BAOC.

Monthly Progress Report
January 1980

Site: #7 Rugganj

Contractor: M/s. Hossain Builders

Contract Price	: Tk. 13,69,074.51	Date Work Commenced	: 30.06.1978
FAR Amount	: Tk. 10,94,193.00	Scheduled Completion Date:	11.12.1978
Revised Contract Price:	Tk. -	Revised Completion Date	: 31.12.1979
Payment To Date	: Tk. 10,60,048.00	Estimated Completion Date:	30.05.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity.	Site filling, part of boundary wall and some other finishing work.
Godown	Lime concrete mortar mixing started and continued.	R.C.C. floor, plaster, L.C. and various finishing work including door fixing.
Storekeeper's Quarter	Minor work for window shutter.	Woodwork in door windows and sanitary fittings.
Darwan's Quarter	No activity	Woodwork in door windows and sanitary fittings.

Percentage Completion This Period: 0.11%

To Date: 77.10%

Remarks: Progress of work during next 15 days is under review by BADC. Action follows after expiry of review period.

Monthly Progress Report
January 1980

Site: # 10 Shibpur

Contractor: M/s. Moniruzzaman

Contract Price	: Tk.14,59,391.50	Date Work Commenced	: 17.06.1978
FAR Amount	: Tk.11,50,145.00	Scheduled Completion Date	: 10.12.1978
Revised Contract Price	: Tk. -	3rd Revised Completion Date	: 30.11.1979
Payments To Date	: Tk.12,11,295.00	Estimated Completion Date	: 31.03.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Work continued for access road.	Access Road, parking area and final clean-up.
Godown	Complete sand filling and rebar placing in floor and made it ready for casting.	Floor casting, finishing, door installation, window glass fitting etc.
Storekeeper's Quarter	Continued shutter fitting to door/window, painting white wash etc.	Painting, glass fitting to window shutter and final coat of white wash etc.
Darwan's Quarter	Continued shutter fitting to doors/windows, painting white wash etc.	Painting, glass fitting to window shutter, final coat of white wash etc.

Percentage Completion This Period: 4.17% To Date: 34.12%

Remarks: Finishing work continuing. Site may be handed over end of March 1980.

Monthly Progress Report
January 1980

Site: # 15 Jhinaidah

Contractor: M/s. Asiatic Builders Ltd.

Contract Price	: Tk.15,23,477.89	Date Work Commenced	: 01.06.1978
FAR Amount	: Tk.11,05,120.00	Scheduled Completion Date	: 28.11.1978
Revised Contract Price	: Tk. -	3rd Revised Completion Date	: 31.12.1979
Payments To Date	: Tk.11,73,949.84	Estimated Completion Date	: 31.03.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity.	Access Road, Apron and Walkways.
Godown	Continued lime terracing. Sand filling and compaction in floor.	Floor casting, door installation, L.C. and white wash.
Storekeeper's Quarter	Surface drain construction.	White wash.
Darwan's Quarter	Surface drain construction.	Part of lime terracing and white wash. Tube wells installation.

Percentage Completion This Period: 4.65% To Date: 81.72%

Remarks: Contractor allotted 10 MT of cement. Progress under review.

Monthly Progress Report
January 1980

Site: #16 Tepakhola

Contractor: M/s. Mir Akhtar Hossain & Co.

Contract Price	: Tk.36,24,851.20	Date Work Commenced	: 26.06.1978
FAR Amount	: Tk.28,98,527.00	Scheduled Completion Date	: 07.06.1979
Revised Contract Price	: Tk.37,93,339.20	1st Revised Completion Date	: 30.11.1979
Payments To Date	: Tk.18,25,130.00	Estimated Completion Date	: 30.05.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Top slab of septic tank and soak well completed.	20% work of site development.
Godown	Completed all columns and brickwork up to roof level including fixing of louvers.	Godown roof & floor including doors, plaster and various finishing work.
Storekeeper's Quarter	Pent house roof slab cast and plastered brickwork. Stair slab with railing cast. Door/window frame 25% complete.	Door/window installation and sanitary fittings.
Darwan's Quarter	No activity.	Door/window installation and sanitary fittings.
Inspection Building	Floor C.C. work complete. Woodwork started.	Door/Window installation and sanitary fittings.

Percentage Completion This Period: 4.21% To Date: 58.36%

Remarks: Contractor allotted 45 MT of cement. Progress under review.

Monthly Progress Report
January 1980

Site: #17 Madaripur

Contractor: M/s. M. Kamal & Co.

Contract Price	: Tk.15,92,215.90	Date Work Commenced	: 18.05.1978
FAR Amount	: Tk.11,30,843.00	Scheduled Completion Date	: 14.11.1978
Revised Contract Price	: Tk. -	3rd Revised Completion Date	: 31.12.1979
Payments To Date	: Tk. 7,28,100.00	Estimated Completion Date	: 31.5.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Complete casting septic tank & soak wells cover slab.	5% work of the site development items.
Godown	Cast both canopy slab. Continued columns casting.	Roof slab, floor slab, lime terracing etc. More than 50% work is pending.
Storekeeper's Quarter	1st floor roof slab casting complete and continued plastering.	Pent house, L.C. woodwork sanitary fitting etc.
Darwan's Quarter	No activity.	C.C. floor, door/window and sanitary installation.

Percentage Completion This Period: 3.07%

To Date: 52.09%

Remarks: Slow progress due to Contractor's neglect of work. Contractor allowed 15 days time to expedite work or face action as per Contract.

Monthly Progress Report
January 1980

Site: #18 Kalkini

Contractor: M/s. Abdul Barek Khan

Contract Price	: Tk.15,25,001.00	Date Work Commenced	: 01.06.1978
FAR Amount	: Tk.11,06,893.00	Scheduled Completion Date	: 28.11.1978
Revised Contract Price	: Tk.16,04,294.44	3rd Revised Completion Date	: 31.12.1979
Payments To Date	: Tk. 9,16,644.11	Estimated Completion Date	: 30.01.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity	10% work is pending.
Godown	Roof slab casting complete. Plastering in progress. Fixing of louvers complete.	Floor slab, steel doors, plastering L.C. etc.
Storekeeper's Quarter	Floor C.C. and patent stone complete. Door & window frame installation in progress.	Installation of door/windows, sanitary fittings etc.
Darwan's Quarter	Rectification of rejected lintels is complete.	Installation of door/windows, sanitary fittings etc.

Percentage Completion This Period: 12.72%

To Date: 74.99%

Remarks: With the change of site management satisfactory progress achieved during the month.

MONTHLY PROGRESS REPORT
January 1980

Site : No.19 Shahjadpur	Contractor : M/s H. Rahman & Co.
Contract Price : Tk.31,16,613.90	Date Work Commenced : 07.06.1978
FAR Amount : Tk.24,54,563.00	Scheduled Completion Date: 03.06.1979
Revised Contract Price:	2nd Revised Completion Date: 31.12.1979
Payments To Date: Tk.21,51,095.30	Estimated Completion Date : 31.05.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity	10% site filling, access road, septic tank and soak well cover etc.
Godown	Plastering to ceiling complete. East side louvers installed. Preparation for floor casting in progress.	Floor slab, L.C., Doors, windows installation and various finishing works.
Storekeeper's Quarter	Fabrication of door window shutters in progress.	L.C., door window shutters, sanitary fittings, whitewash and painting etc.
Darwan's Quarter	Lime terracing in progress.	Door window shutters, sanitary fittings, whitewash and painting etc.
Inspection Building	Fabrication of door window shutters in progress.	L.C. door window shutters, sanitary fittings, white wash and painting etc.

Percentage Completion This Period : 1.81% To Date : 71.72%

Remarks: Slow progress due to shortage of materials. Contractor allotted 30 MT of cement by BADC. Contractor informed of actions to be taken as per contract if satisfactory progress not achieved during next 15 days.

MONTHLY PROGRESS REPORT
January 1980

Site : No.20 Ullapara	Contractor : Bangladesh Construction Co.
Contract Price : Tk.33,88,671.05	Date Work Commenced : 10.07.1978
FAR Amount : Tk.27,29,189.00	Scheduled Completion Date: 04.07.1979
Revised Contract Price: -	___ Revised Completion Date: 31.12.1979
Payments To Date : Tk. 4,38,280.00	Estimated Completion Date: 31.12.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity	50% work pending.
Godown	West side grade beam, 35 Nos. cols. 5'-0" in line A, D & E and 19 pedestals in line B & C cast. Sand filling in plinth continued.	About 75% work is pending Some work below plinth and all work above plinth to be done.
Storekeeper's Quarter.	No activity	Foundation has not yet cast.
Darwan's Quarter	No activity	Foundation has not yet cast.
Inspection Building	No activity	Foundation has not yet cast.

Percentage Completion This Period : 3.96% To Date : 19.78%

Remarks : Progress is slow due to contractor's negligence and shortage of materials. Contractor allotted 60 MT of cement.

Monthly Progress Report
January 1980

Site: # 23 Santahar	Contractor: Frachi Constn.Co.Ltd.
Contract Price: Tk.23,87,136.02	Date Work Commenced: 02-03-78
FAR Amount: Tk.15,59,452.00	Scheduled Completion Date: 26-11-78
Revised Contract Price: Tk.26,73,126.02	4th Revised Completion Date: 31-12-79
Payments To Date: Tk.23,79,224.30	Estimated Completion Date: 29-02-80

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Work continued in parking area, walkways and final grading	Sodding & Final Cleanup.
Godown	Remaining 50% floor cast, installed steel doors, white wash and other finishing works in progress.	Final coat of white wash and cleaning.
Storekeepers Quarter	Glass panes fixed and finishing continued.	Final coat of paints and fixing of hardwares .
Darwan's Quarter	Glass panes fixed and finishing continued.	Final coat of paint, and fixing of hardwares.
Inspection Building	Glass panes fixed and finishing continued.	Final coat of paint and fixing of hardware.
Percentage Completion This Period: 4.59%		To Date: 99.22%

Remarks: All works substantially completed. Finishing going on. Site can be handed over to BADC by end of February 1980.

Monthly Progress Report
January 1980

Site: #24 Akkelpur

Contractor: M/s. M.R. Khan & Co.

Contract Price:	Tk. 15,25,518.00	Date Work Commenced:	17-06-78
FAR Amount:	Tk. 11,12,864.00	Scheduled Completion Date:	13-12-78
Revised Contract Price:	Tk. -	2nd Revised Completion Date:	31-12-79
Payments To Date:	Tk. 7,11,985.10	Estimated Completion Date:	30-05-80

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No Activity	25% work is pending
Godown	Form work for roof slab in progress. Complete brickwork and sand filling.	Roof slab and floor slab yet to be done.
Storekeepers Quarter	1st floor lintel cast. Plastering in ground floor in progress.	All work pending above 1st floor lintel.
Darwan's Quarter	Complete plastering	Wood work, sanitary fittings and white wash etc.
Percentage Completion This Period: 7.09%		To Date: 58.15%

Remarks: Slow progress for shortage of cement and other materials.
Contractor allotted 35 MT of cement by BADC in January 1980.

Monthly Progress Report
January 1980

Site: #25 Adamdighi

Contractor: M/s. Star Enterprise Ltd.

Contract Price: Tk. 14,37,024.62
 FAR Amount: Tk. 10,31,552.00
 Revised Contract
 Price(C.O.#1): Tk. 15,60,263.56
 Payments To Date: Tk. 8,63,548.74

Date Work Commenced: 05-05-78
 Scheduled Completion Date: 31-10-78
 3rd Revised Completion Date: 31-12-79
 Estimated Completion Date: ~~30-05-80~~

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity	25% work is pending
Godown	Formwork for roof beams and slab in progress.	Roof slab, floor, L.C. etc. are pending. In all about 50% work to be done.
Storekeepers Quarter	Installation of door/window frames in progress. Rebar, placing in 1st floor roof slab in progress.	1st floor roof slab, Penthouse, L.C. etc.
Darwan's Quarter	No Activity	Door/Window shutter installation, painting and 25% sanitary fittings.

Percentage Completion This Period: 0.69%

To Date: 56.41%

Remarks: Practically no progress due to Contractor's neglect of work. Contractor given 7 days notice to show progress or face termination of Contract.

Monthly Progress Report
January 1980

Site: #26 Gabtali

Contractor: The Elegant Builders

Contract Price:	Tk.14,38,518.78	Date Work Commenced:	20-05-78
FAR Amount:	Tk.10,40,720.00	Scheduled Completion Date:	16-11-79
Revised Contract Price(C.C.1):	Tk.15,81,529.96	4th Revised Completion Date:	31-12-79
Payments To Date:	Tk.14,30,864.92	Estimated Completion Date:	29-02-80

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Access road, parking area and walkways complete. Final cleanup and grading in progress.	Codding and final clean up.
Godown	Platform complete. Wiremesh were fixed to the vent. White/colour wash continued.	Fixing of glass panes to windows, final coat of white/colour wash and over all cleaning.
Storekeepers Quarter	Glass panes were fixed and white/colour wash continued.	Fainting, fixing hard wares & final coat of white/colour wash.
Darwan's Quarter	Glass panes were fixed and white/ and colour wash continued.	Fainting, fixing hard wares & final coat of white/colour wash.

Percentage Completion This Period: 3.52% To Date: 93.72%

Remarks: All works complete. Punch list prepared for rectification of unacceptable works. Site can be handed over to BADC by the end of February 1980.

Monthly Progress Report
January 1980

Site: #27 Saghata

Contractor: M/s. Waheed & Co. Ltd.

Contract Price: Tk.13,98,095.64
 FAR Amount: Tk.10,02,544.00
 Revised
 Contract Price: Tk. -
 Payments To Date: Tk.10,39,138.01

Date Work Commenced: 23-05-78
 Scheduled Completion Date: 19-11-78
 3rd Revised Completion Date: 31-12-79
 Estimated Completion Date: 31-05-80

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity	Sodding, surface drains, septic tanks & soakwell cover
Godown	Outside plastering complete and plastering to ceiling continued	RCC Floor Slab, part of ceiling plaster L.C., door installation etc.
Storekeepers Quarter	Continued installation of window shutters.	Floor Slab, wood work in doors windows, sanitary fitting etc.
Darwan's Quarter	Continued installation of window shutters	Wood work in door windows, sanitary fittings white wash, painting etc.

Percentage Completion This Period: 4.60% To Date: 82.88%

Remarks: This Contractor has two sites. Handed over Ghoraghat on 30-1-80. May handover this site by end of April 1980.

Monthly Progress Report
January 1980

Site: #29 Gaibanda

Contractor: M/s. Fakub Engg. Ltd.

Contract Price:	Tk. 35,77,040.54	Date Work Commenced:	02-03-78
FAR Amount:	Tk. 23,81,801.00	Scheduled Completion Date:	24-02-79
Revised Contract Price:	Tk. 38,36,477.54	3rd Revised Completion Date:	31-12-79
Payments To Date:	Tk. 36,50,487.93	Estimated Completion Date:	29-02-80

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Apron and walkway complete. Final grading and clean up in progress	Grading and final cleanup.
Godown	Platform, louvers, wiremesh screen fixing complete.	Complete
Storekeepers Quarter	Door window shutter fixing complete including painting.	Complete.
Darwan's Quarter	Door window shutter fixing and painting complete.	Complete
Inspection Building	Final coat of paint.	Complete
Percentage Completion This Period:	2.10%	To Date: 99.39%

Remarks: All works complete. Site may be handed over by third week of February 1980.

Monthly Progress Report
January 1980

Site: # 30 Rangpur(Sadar)

Contractor: M/s. A.M. Ishaque

Contract Price	: Tk.37,99,529.50	Date Work Commenced	: 07.06.1978
FAR Amount	: Tk.30,10,208.00	Scheduled Completion Date	: 01.09.1979
Revised Contract Price	: Tk.41,27,435.50	2nd Revised Completion Date	: 31.12.1979
Payments To Date	: Tk.25,63,190.43	Estimated Completion Date	: 31.05.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	No activity.	Access Road, parking area, boundary wall etc. about 25% work pending.
Godown	L.C. 20%, complete plaster to ceiling 50%, shuttering for another 25% roof slab in progress.	50% roof slab, floor L.C. etc. about 32% work pending.
Storekeeper's Quarter	No activity	Installation of door windows, sanitary fittings and white wash.
Darwan's Quarter	Remaining door and window frame fixing complete.	-do-
Inspection Building	No activity.	-do-

Percentage Completion This Period: 1.58% To Date: 70.08%

Remarks: Contractor allotted 60 MT of cement by BADC. Progress of work under view.

MONTHLY PROGRESS REPORT
January 1980

Site : No.31 Kurigram Contractor : M/s H. Rahman & Co.
Contract Price : Tk.33,20,106.50 Date Work Commenced : 07.06.1978
FAR Amount : Tk.25,00,034.00 Scheduled Completion Date : 03.06.1979
Revised Contract Price: Tk.33,20,106.50 2nd Revised Completion Date: 31.12.1979
Payments To Date : Tk.22,12,709.80 Estimated Completion Date : 31.05.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Work for the parking area & apron in progress.	Access road, sodding Surface drain etc.
Godown	Preparation for plastering and floor dressing in progress	RCC floor, L.C., plaster, Door installation etc.
Storekeeper's Quarter.	Worked for the pent house roof slab casting and plaster to walls.	Pent house roof, wood work for the doors & windows and sanitary fittings.
Darwan's Quarter	Complete lime terracing.	Door window installation and sanitary fittings.
Inspection Building	L.C. in progress, whitewash started. Windows shutter building in progress.	Door window installation, sanitary fittings and part of whitewash.

Percentage Completion This Period: 2.21% To Date : 77.81%

Remarks: Slow progress due to shortage of materials. Contractor allotted 30 MT of cement by BADC. Contractor informed of actions to be taken if satisfactory progress not achieved during next 15 days.

MONTHLY PROGRESS REPORT
January 1980

Site : No.31 Kurigram Contractor : M/s H. Rahman & Co.
Contract Price : Tk.33,20,106.50 Date Work Commenced : 07.06.1978
FAR Amount : Tk.25,00,034.00 Scheduled Completion Date : 03.06.1979
Revised Contract Price: Tk.33,20,106.50 2nd Revised Completion Date: 31.12.1979
Payments To Date : Tk.22,12,709.80 Estimated Completion Date : 31.05.1980

<u>Activity</u>	<u>Work Performed This Report Period</u>	<u>Work Outstanding</u>
Site Development	Work for the parking area & apron in progress.	Access road, sodding Surface drain etc.
Godown	Preparation for plastering and floor dressing in progress	RCC floor, L.C., plaster, Door installation etc.
Storekeeper's Quarter.	Worked for the pent house roof slab casting and plaster to walls.	Pent house roof, wood work for the doors & windows and sanitary fittings.
Darwan's Quarter	Complete lime terracing.	Door window installation and sanitary fittings.
Inspection Building	L.C. in progress, whitewash started. Windows shutter building in progress.	Door window installation, sanitary fittings and part of whitewash.

Percentage Completion This Period: 2.21%


To Date : 77.81%

Remarks: Slow progress due to shortage of materials. Contractor allotted 30 MT of cement by DADC. Contractor informed of actions to be taken if satisfactory progress not achieved during next 15 days.


SITewise OVERALL PROGRESS

AS OF 31 JAN, 1980


BEST AVAILABLE DOCUMENT

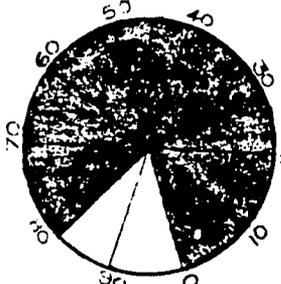


LAKSHMIPUR

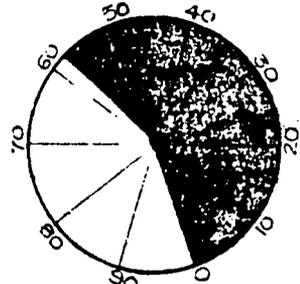


TEPAKHOLA

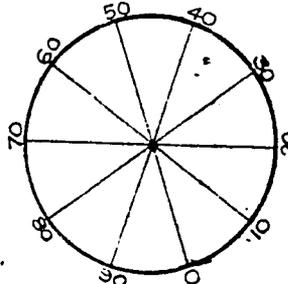


CHOWMUHANI

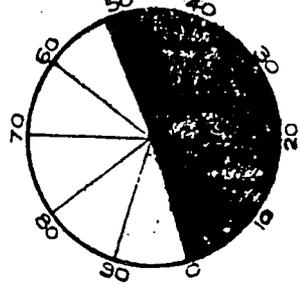


MADANPUR

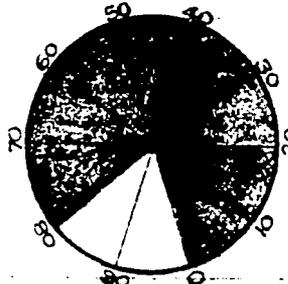


FENI

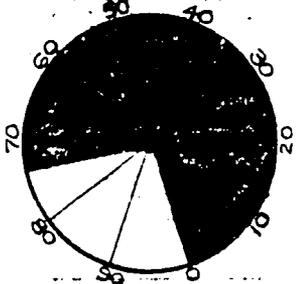


KALKINI

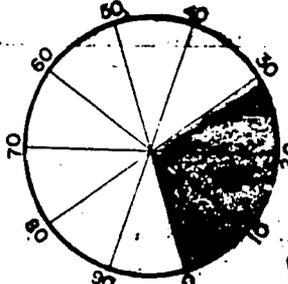


LOHAJANG (Cancelled)

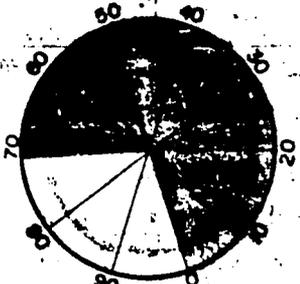



SHAHJADPUR

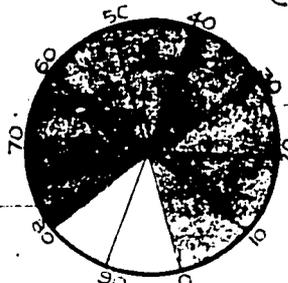

TALTALA

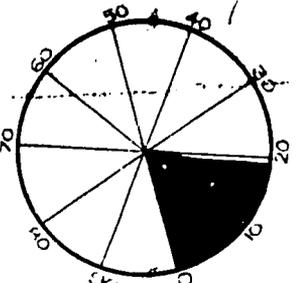


ULLAPARA




BEST AVAILABLE DOCUMENT


TALTALA

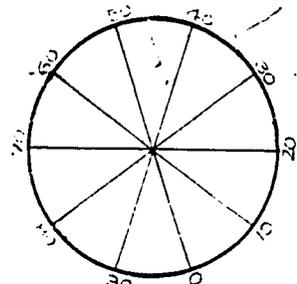


MUNSHIGANJ

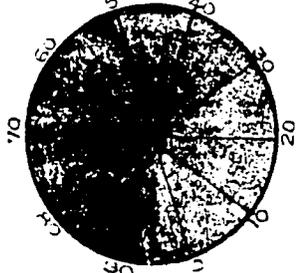


SRINAGAR

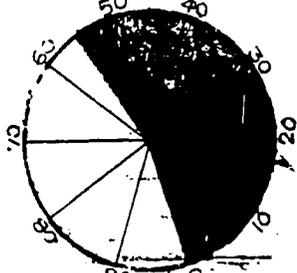


MANIKGANJ

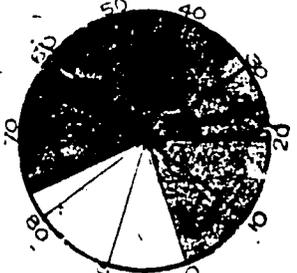


RUPGANJ




ARAIHAZAR

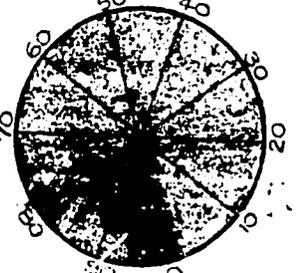


JOYDEBPUR




ULLAPARA

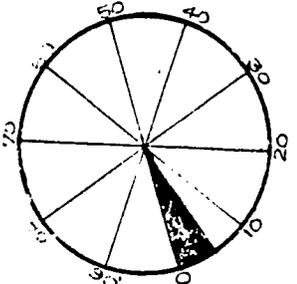


SIRAJGANJ (Cancelled)

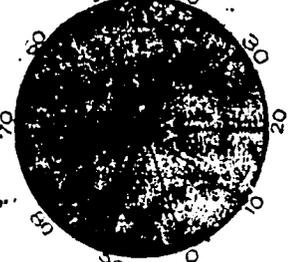


NANDIGRAM

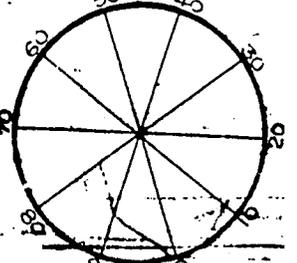


DHAIKIRHAT




BANTAHAR

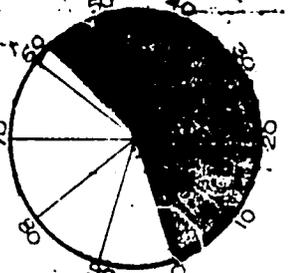

AKKELPUR




ADAMDIGHI




BESI AVAILABLE DOCUMENTS


JOYDEBPUR

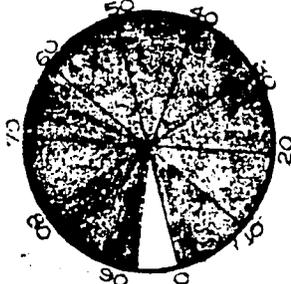


ADAMDIGHI

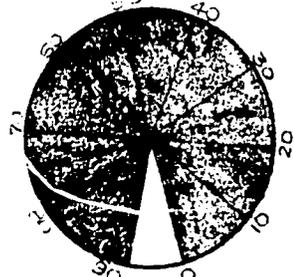


SHIBPUR




GABALI

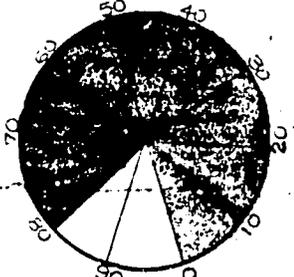


MONIRAMPUR

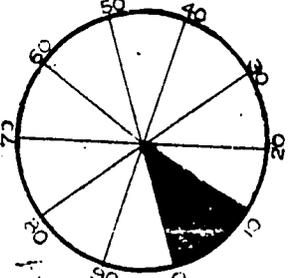

SHAGHATA




NARAIL (Cancelled)




GHORAGHAT




JESSORE




GAIBANDA

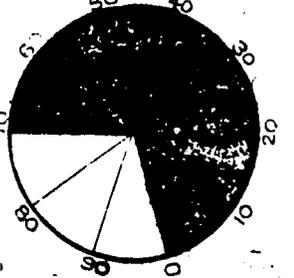

KALIGANJ

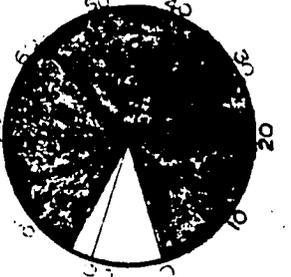

RANGPUR

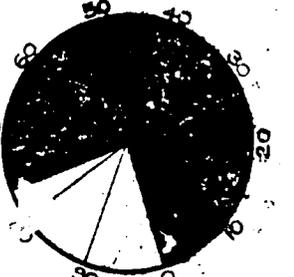

JHINAIDAH

KURIGRAM

**BANGLADESH AGRICULTURAL DEVELOPMENT CORPORATION
FERTILIZER STORAGE CONSTRUCTION PROJECT**

US AID LOAN 388-T011

SL NO.	CONTRACT NO.	LOCATION	CONTRACTOR	CONTRACT AMOUNT(TK)	Weighted %
IIA-2	NO 10 NC IIA 2	Lakshmipur	Feni Ideal Construction	19,51,361.46	3.04
4	NO 30 NC IIA 4	Feni	Siddique & Co Ltd.	43,60,703.77	6.81
II B-1	DA05 NB II B 1	Lohajang	The Starlight Ltd.	16,11,086.97	2.51
2	DA10 NB II B 2	Taltala	M. Omar Meah & Sons	24,97,758.51	3.89
4	DA05 NB II B 4	Srinagar	Taleb Ali Bhuiyan	15,67,092.66	2.44
6	DA10 NB II B 6	Manikganj	Siddique Khan	21,79,612.87	3.40
7	DA05 NB II B 7	Rupganj	Hossain Builders	13,69,074.51	2.13
8	DA05 NB II B 8	Araihazar	Taleb Ali Bhuiyan	14,77,221.56	2.30
9	DA05 NB II B 9	Joydebpur	M. S. Khan	13,97,470.80	2.18
10	DA05 NB II B 10	Shibpur	Moniruzzaman	14,59,391.50	2.28
II C-1	JE 05 NB IIC 1	Monirampur	National Construction	15,33,989.61	2.39
2	JE 05 NB IIC 2	Narail	Lucky Traders & Co.	15,22,548.41	2.37
3	JE 05 NC IIC 3	Jessore (Sadar)	Allied Construction & Co.	13,43,140.90	2.09
4	JE 10 NB IIC 4	Kaliganj	National Construction	20,63,506.20	3.22
5	JE 05 NB IIC 5	Jhinaldha	Asiatic Builders Ltd.	15,23,477.89	2.37
6	FA20 NB IIC 6	Tepakhola	Mir Akhtar Hossain & Co.	36,24,851.20	5.65
7	FA05 NB IIC 7	Madaripur	Karnal & Co.	15,92,215.90	2.48
8	FA05 NB IIC 8	Kalkini	Abdul Berek Khan	15,25,001.00	2.38
III B-1	PB 20 NC III B 1	Shahjadpur	H. Rahman & Co.	31,16,613.90	4.86
2	PB 20 NB III B 2	Uliapara	Bangladesh Construction Co.	33,88,671.05	5.28
3	PB 05 NC III B 3	Sirajganj	Agrani Banijja Sangstha	12,77,645.04	1.99
5	BO 05 NB III B 5	Nandigram	Pragati Builders.	14,09,585.07	2.20
8	BO 10 NB III B 8	Santahar	Prachi Construction Co.	23,87,136.02	3.72
9	BO 05 NB III B 9	Akkelpur	M. R. Khan & Co.	15,25,518.90	2.38
10	BO 05 NB III B 10	Adamdighi	Star Enterprise Ltd.	14,37,024.62	2.24
11	BO 05 NC III B 11	Gabfali	The Elegant Builders	14,38,518.78	2.24
III C-1	RN 05 NC III C 1	Saghata	Waheed & Co.	13,98,095.64	2.18
2	RN 05 NC III C 2	Ghoraghat	Waheed & Co.	14,72,971.34	2.30
3	RN 20 NC III C 3	Gaibanda	Eokub Engineering Ltd	35,77,040.54	5.58
4	RN 30 NC III C 4	Rangpur (Sadar)	A. M. Ishaque	37,99,528.50	5.92
5	RN 20 NB III C 5	Kurigram	M. Rahman & Co.	33,20,106.50	5.18

M

1979					1980					%
					FEB	MAR	APR	MAY	JUN	COMP.
[REDACTED]										83.24
[REDACTED]										81.03
[REDACTED]										
[REDACTED]										81.32
[REDACTED]										100
[REDACTED]										55.97
[REDACTED]										77.10
[REDACTED]										100
[REDACTED]										100
[REDACTED]										94.12
[REDACTED]										
[REDACTED]										100
[REDACTED]										
[REDACTED]										100
[REDACTED]										86.72
[REDACTED]										58.36
[REDACTED]										52.09
[REDACTED]										74.99
[REDACTED]										
[REDACTED]										71.72
[REDACTED]										31.12.84
[REDACTED]										19.78
[REDACTED]										
[REDACTED]										100
[REDACTED]										99.22
[REDACTED]										58.15
[REDACTED]										56.41
[REDACTED]										93.72
[REDACTED]										
[REDACTED]										82.86
[REDACTED]										100
[REDACTED]										99.39
[REDACTED]										70.08
[REDACTED]										77.81
[REDACTED]										

N
AM
C
DRG. M

