

Cooperative Housing Foundation
Quarterly Performance Report

110366

Programa Hondureño de Gestión de Actividades de Reconstrucción (HOGAR)
Honduras

Grantee: Cooperative Housing Foundation
Cooperative Agreement: 522-A-00-00-00207-00
Reporting Period: April 1, 2001 to June 30, 2001
Submission Date: July 31, 2001

A. Background

CHF was awarded a Cooperative Agreement by USAID for the Management of the Housing Reconstruction Program in Honduras pursuant to Hurricane Mitch in late October 1998. The Cooperative Agreement was effective October 29, 1999, and the Project Assistance Completion Date (PACD) is scheduled for December 31, 2001. The HOGAR program will make recognizable, significant and measurable contributions to the achievement of USAID/Honduras' Hurricane Reconstruction Special Objective, and will directly contribute to the Intermediate Result, "Permanent Housing Developed for Dislocated Families." CHF will coordinate the building efforts through NGO sub-awards to permanently house more than 3,000 dislocated families on land with access to basic services and away from potential natural disasters.

The program is funded with a \$7,808,057 grant from USAID. CHF anticipates matching funds and counterpart contributions to exceed 32% of the total program budget, or a minimum of \$3,700,000.

B. Expected Results

As with other CHF projects, the goal for this program will follow a comprehensive approach to housing that includes not only sound and appropriate house construction, but also, community involvement, community strengthening, economic stimulation, risk mitigation, environmental protection, infrastructure development and the provision of education and health facilities. Using this approach, CHF will ensure that all projects funded under this program address each community's basic needs and go beyond that to strengthen the community's capacity ensuring sustainable long-term development. Specific objectives of HOGAR include:

- More than 3,000 families with upgraded or constructed permanent homes on titled and serviced land.
- Broad geographic coverage to meet the housing needs of un-served families in hurricane affected regions of the country.
- Newly resettled communities with sound urban planning and access to comprehensive community development services including schools, health services and economic opportunity.
- At least five NGOs, implementing housing credit-programs with reflows committed to future housing needs in the communities.
- Fifteen NGOs and municipalities with improved capacity to address housing and other community development needs on a significant scale.

Now, more than two years after *Mitch*, thousands of families in Honduras remain without access to shelter that meets minimum standards. These families are living in emergency shelters, temporary shelters provided by donor agencies and, in many cases, marginal houses reconstructed from debris and salvaged materials. CHF expects this program to construct an average of 125 homes a month in an effort to meet the goals of HOGAR and provide relief to the current housing needs in the most affected areas of Honduras.

To respond to the enormous need for housing in post-Hurricane Honduras, the CHF HOGAR Program has been designed to include the following key elements:

- Grants to Honduran and international NGOs/PVOs to directly assist families and communities to construct basic core houses.
- A technical guidance and assistance program using CHF technical staff, materials and part-time consultations by Honduran housing professionals.
- Management of HOGAR with the advice of a working group that includes USAID staff.
- The issuance of RFAs with clear and transparent criteria to allow the maximum number of NGOs/PVOs to access the housing funds.
- Technical supervision to ensure proper management of U.S. Government finances by all sub-awardees.
- Training in the management of housing lending programs to enable NGOs to recover and reinvest reflow funds into future housing efforts.
- Internal monitoring to ensure proper progress using a management by measurable objectives format reported on a monthly basis to CHF/HQ.

C. Current Core Activities

Twenty-three sub-awards/contracts have been signed, of which thirteen (13) have been completed in their entirety. These twenty-three projects are being implemented by twelve (12) national and international NGO's / PVO's and two (2) Construction Companies. Eight (8) of them have established fund recovery mechanisms to continue working in the housing sector and/or in other community development activities.

1. Closed Projects from Previous Quarters

- NPH/Morocelí, El Paraíso-Nueva Esperanza Project
- GOAL/San Jerónimo, Comayagua-Colonia Irlanda Project
- APAN/CI La Guacamaya, Yoro-Niños Felices Project
- Cooperativa Getsemaní/Land purchase, El Progreso Agua Blanca Project

2. Projects Completed this Quarter

Nine additional projects were completed this quarter for a total of thirteen (13) fully completed projects. The majority of the remaining projects in construction will be completed next quarter.

The official administrative project closeout for these nine projects is in process. The HOGAR Program team, however, will continue following up on these projects as well as the other closed projects through the PACD ensuring that all the activities required under the Program and in the sub-award documents have been completed.

The following are individual summaries of the nine (9) projects completed this quarter:

APAN/CI Renacer, La Guacamaya, El Progreso, Yoro

This 3-month sub-award was signed November 1, 2000.

The project was completed in the first days of May. The project included: 110 houses, streets, and the potable water and drainage systems.

In the month of April, CHF approved a complementary fund of \$6,200 to improve the wastewater drainage system for the Renacer project. CHF approved a second time extension request of 45 days, from April 16th to May 31st, to finish the complementary works and to put together the financial and technical reports needed for the project closeout.

Habitat for Humanity Honduras/Amarateca, Francisco Morazán - Residential Project

This sub-award was signed June 28, 2000.

In this quarter HABITAT continued to move families into their new homes and 145 houses are inhabited. Although the majority of construction activities are finished, HABITAT still has to install the toilets, sinks, doors and windows as each family occupies its home.

The project will be officially received by CHF in the month of July at which time 100% of the houses should be occupied. Considering the issues surrounding delayed construction of the infrastructure to be provided by USAID/FHIS, the less than 100% occupancy rate is considered acceptable for the time being.

HABITAT has requested approval to use excess project funds to improve the roofs of some houses and to continue community development in the area. This request is under consideration by CHF.

AIEH/Choloma, Cortés-Colonia Japón Project

This project was finalized during the last quarter; however, additional funds were approved to connect 180 more families to the sewer system, for a total of 260 families. Follow up activities will continue during the next period.

ADRA/Villa El Porvenir, Amarateca-Streets Grading Project

This contract was signed February 12, 2001 for the grading work and the removal of the rock mantle complementing the ADRA housing project previously signed with CHF.

In light of the low load bearing capacity of the soil and its composition, CHF decided to bid for a contractor that would do all site grading and street conformation. The bid was held in early January and activities were partially concluded in March. Problems were encountered with two streets where a rock

mantle made it impossible to continue via conventional methods. A backhoe with a power drill was unable to break through the rock so CHF decided in late May to use dynamite. To date all dynamite work has been completed and the rock is being removed from the streets to finish the contract.

GOAL / Rehabilitation Las Liconas, Comayagua Project

This sub-award was signed October 18, 2000 to rehabilitate 28 houses of which 100% are completed.

The first stage of the rehabilitation project in Comayagua concluded with the inauguration of 28 homes in Las Liconas on April 19, 2001. Based on the good results achieved with this project, a second phase is taking place in the surrounding urban area of Comayagua focusing on families with extremely damaged homes.

Hermanos maristas / Choluteca- Colonia Marcelino Champagnat

This 6-month sub-award was signed December 1, 2000.

On May 19, 2001 the Marcelino Champagnat water system was inaugurated having reached its goal of providing potable water to this community. The system consists of a pump, 15,000 meters of pipeline, a metal elevated 50,000-gallon tank and 620 house connections providing potable water to every home through a scheduled and zoned operation to maximize the efficiency of the system with minimal water and energy waste. This was considered a very important gap-filling project for CHF as the 620 families living in this community had purchased their own land, received houses from various NGOs, but did not have access to potable water.

The ambitious development scheme programmed by Hermanos Maristas for the Marcelino Champagnat community includes a sewage system currently in the final stages of construction with Spanish Cooperation funding. Other complementary projects include road improvements and a bridge.

Atlas Logistique/ Choluteca- Hato Nuevo Project I Phase

This 6-month sub-award was signed December 1, 2000.

During this period the Hato Nuevo project consisting of 87 new houses and 22 rehabilitations was successfully completed with high quality standards. All houses have washbasins, latrines and bathing facilities. Additionally the project included two drilled wells with manual pumps with a 60-gpm and 70-gpm productions, which can supply the entire community.

Atlas Logistique has identified some solid waste disposal problems and CHF-HOGAR technical staff has recommended the implementation of a cleaning campaign, awareness training and garbage collection/disposal facilities. Protection of the water source, chlorination and further training in health related issues are being implemented to ensure the quality of the water.

The wastewater disposal is being addressed by Atlas Logistique technicians with the implementation of an innovative system, which recycles the previously treated waters, which are then dispersed below surface to existing crops.

Even though the project includes two wells with very good production the Hato Nuevo community covers a very extended territory, which makes recollection of the water difficult. Hato Nuevo is

considering an electrically generated pump, tank and a public connection distribution as a more adequate solution for the water problem. CHF-HOGAR is awaiting a formal proposal for such a project. Rainwater harvesting is also being implemented in Hato Nuevo giving the community yet another water solution.

GOAL / Mata de Caña, Comayagua- Lazos de Amistad Project

This 4-month sub-award for a water system benefiting 89 families was signed December 12, 2000.

This project was successfully completed and tested during this period. Pressures in the main distribution lines were tested proving well within established limits.

SANAA personnel have been monitoring the establishment of the "Junta de Agua", operation and maintenance procedures, quality of the water and chlorination and other health issues.

To avoid erosion of the terrain surrounding the tank site CHF-HOGAR has recommended the construction of a containment wall, elongation of the scour pipe and fencing.

Other necessities identified in the follow-up visits are improved wastewater drainage, a storm drainage system, improvement of the existing latrines and washbasins for water storage to limit squandering of water. A proposal for these complementary works is currently under discussion.

CRWRC/Amarateca, Francisco Morazán- Construyendo Sobre Roca Project

This 3-month sub-award was signed December 15, 2000.

CRWRC has completed the 47 contracted houses in this period. During the past month, CHF verified housing occupancy and reviewed a request by CRWC for an increase in the project budget. The request was rejected by CHF as it did not meet the sub-donation criteria. CRWRC has, however, received financing from another organization to complete some details of the project.

Due to the lack of coordination with the NGO social promoter and the beneficiaries, the final reception will take place until July.

3. Projects in Implementation

The following is a summary of the main community development activities that are included in each project as well as a general summary of progress to date:

a. GOAL Morazán/Yoro -Flor del Campo Project

This sub-award was signed June 16, 2000 and was originally expected to be completed June 16, 2001.

During the month of April the housing portion of the project was 100 % concluded and inaugurated on May 08. All houses were satisfactorily received by CHF, including the sanitary facilities. The completion of the water system is the only part of the Morazán project still pending and it currently presents an overall advancement of 75%. On June 13, GOAL requested a no-cost time extension in order to complete work on the potable water supply system. Since the month of May this part of the

project has been subject to a number of delays, mainly cause by a lack of construction materials, bad weather and poor beneficiary participation. This situation was analyzed by CHF and a new completion date was set for the 28th of July.

In April, CHF approved a request of additional funds for the water and sanitation system. This amount will serve to cover complementary works that include an improved sanitary solution consisting of a latrine/washbasin/shower design instead of a simple pit latrine, road improvements and amplification of the water system due to changes in the original design.

b. ADRA/Amarateca F.M. -Villa El Porvenir Project

This 8-month sub-award was signed September 1, 2000.

Activities for this quarter have been significant, including both programmed and unforeseen activities. All housing has shown considerable progress and improvement quality.

Of the 150 houses contemplated in the original proposal 127 are currently under construction and a progress rate of 70% can be observed. CHF is accepting houses as they are being completed and to date, 60 houses have been accepted by CHF.

CHF's rejection of the first 23 houses due to poor quality construction means that additional funds are available under the award. ADRA and CHF are considering the option of building a school. However, this offer is still under review pending documentation that has not yet been provided by ADRA.

Due to various situations presented in the implementation of this project, including site grading and labor competition in the area, the construction progress has been delayed. ADRA has requested an extension of time, and CHF has analyzed the request approving an additional 40 days extending the project through August 15, 2001.

c. Catholic Relief Services (CRS) / Choluteca- Colonias Unidas Iztoca

This 12-months sub-award was signed September 26, 2000.

During this quarter, the Colonias Unidas Project has finally caught up with their pre-established schedule having completed 164 new houses. Formal reception of the houses has been set for mid-July. During this time, it is expected that the rest of the 208 houses will be completed. Overall progress in the housing project is 96%, and the construction of the water system has reached 90% of completion. Leaving pending are 30% of the house connections, installation of valves and final testing of the system, which has been set for July 30th. Still delayed due to technical difficulties is the construction of sanitary facilities, which should have started three months ago.

The construction of a 3000-meter drainage system as well as other risk mitigation measures commenced during this quarter. Drainage ditches and small containment walls are among the activities undertaken by the new homeowners to ensure their own safety.

Pre-cast washing basins will be installed as scheduled, once a suitable wastewater disposal system has been established. Absorption testing of the terrain has been carried out to determine the most convenient wastewater disposal as well as sanitary units to be completed next quarter.

d. GOAL / Rehabilitation Casco Urbano, Comayagua Project

This sub-award was signed October 18, 2000 to rehabilitate 28 houses of which 100% are completed.

With an extension of the second stage of this rehabilitation project, 72 additional houses are contemplated. Even though this project was approved last year, it was initially presented as the second phase of the Liconas project and officially started with 24 houses on April 21, 2001 in different neighborhoods of the surrounding area of Comayagua.

The quality shown in this project has been excellent. GOAL's ever-present involvement is paying off again. Ten more houses will be built in the second site and a third site is being contemplated in 1 de Mayo. Total progress to date is 30%.

Having identified additional need in the area, GOAL submitted a proposal to include 60 more rehabilitations houses to the most recent 72. In light of their excellent performance and the positive impact shown in the community, CHF approved the new proposal and extended the contract. Activities are currently underway.

e. Atlas Logistique / Choluteca- Hato Nuevo II phase Project

This sub- award was signed May 16, 2001 and the completion deadline is August 16, 2001.

This second phase of the Hato Nuevo project, approved by CHF-HOGAR for additional funding, consists of 26 new houses, rehabilitation of a communal center and the construction of a health center.

The project is currently 25% completed with 12 houses in different stages of completion. The health center is almost completed and preliminary works are taking place on the communal center. Progress is as scheduled and quality continues to be outstanding.

f. AIEH Azacualpa, Santa Bárbara

This 4-month sub-award was signed February 9, 2001.

At this moment, all 41 houses are under construction with 17 houses completed reflecting an overall progress rate of 80%. The project was initially divided in two stages, the first being of 17 houses and the second of 24 houses. Initially work was delayed on the second stage due to problems with the beneficiary list provided by the Major, whose beneficiaries did not have the capacity to pay for the houses. This required AIEH to review the situation, and a reduction of the size of the house and thus the cost was presented to and accepted by the beneficiaries. With the savings from the smaller houses, AIEH is proposing to provide the project with all the site's public electric installation. A request for redirection of funds has been made by AIEH and is under review by CHF.

SANAA has completed a 25,000 gallon-water tank and the main piping for the first stage of the system. Also in the first stage, the drainage canal is 95% complete. The start of the rainy season has brought about unforeseen problems and activities. On the lower area erosion has occurred, which could endanger the houses. AIEH installed a provisional plastic tarp over the slope to prevent further erosion and is currently building a retaining wall and additional drainage canals. To complement these solutions AIEH is encouraging the beneficiaries to start a reforestation campaign directed specifically to this area.

g. AIEH/ La Lima, Cortés

This 5-month sub-award was signed February 9, 2001.

All 83 houses are currently under construction with 40 houses 100% completed and the rest with a 50% completion rate for an overall progress rate of 85%. The quality of the houses is up to code and beneficiary participation has been exceptional. A small delay was experienced in the month of April because the main suppliers for the steel structures were out of stock. The problem, however, was solved quickly and activities were accelerated to make up for the lost time.

The excavation and installation of piping for the sewage system is complete and only the pump station is pending for an overall progress rate of 80%. The main piping for the water system has been installed and only the domiciliary connections are pending for a progress rate of 80%.

h. Project Teamwork/Pimienta, Cortés- Santiago de Umaña Project

This 6-month sub-award was signed February 28, 2001.

To date 28 houses are under construction and show good progress for an overall completion rate of 30%. Quality shown on the first 12 houses was adequate but not as expected due to problems with the cement blocks. Substantial improvement with the subsequent houses has been observed since changing block suppliers.

The sewage system is 70% complete, and the water system is 85% complete with only the treatment plants and the well water pending. Both systems depend on the electrical system which is still 50% complete. The quality in workmanship and materials for these systems has been excellent.

A concern was raised by CHF and USAID about the stability of some of the slopes in the project. Mitigation measures were requested for these areas and a cost breakdown and design analysis was to be presented by Project Teamwork. The use of geo textile matting in addition to the gavions is being implemented to address erosion and soil stability problems.

All expenses for the mitigation measures are expected to be covered by savings made in the rest of the project.

i. APAN/La Sabana, Cortés- El Milagro Project

This 3.5-month sub-award was signed June 18, 2001 after several months of negotiations, and a site change.

The "El Milagro" project contemplates the construction of 200 homes, a complete domiciliary potable water system and full electrification of the site. The work plan and organization of this project will need to be exceptional in order to finish in the short timeframe. A clause was written into this sub-award stating that if the project were behind at 30 days, the total number of houses to be built would be reduced. Based on initial start-up and the number of laborers and supervisors hired for this project, CHF does not anticipate any delays. A crew of 100 skilled masons, 200 helpers, 5 contractors and 1 site engineer have all been contracted and APAN guarantees a 45% progress rate by July 15.

During the first 15 days of this project, APAN concentrated on preparing the construction site, grading streets and lots and finalizing material purchases. The identification of staff and initial steps for purchasing materials, such as obtaining quotes, were completed before the contract was signed in order to save time.

j. Patronato Pro-Mejoramiento Villa Linda Miller

This 5-month sub-award was signed May 02, 2001.

The CHF-HOGAR program will support this community with the execution of several contracts to complete the sewer system. During this quarter CHF contracted a private company to drill a well to assure the permanent provision of water for the sustainability of the sanitation project. The perforation was successful and water was found at 500 feet with a capacity of 64 gallons per minute.

Once the permanent water source was confirmed, CHF proceeded with the bidding process for the construction of the second phase of the sewer system. The first phase was completed with funding from IOM/USAID. A construction company has been selected and is expected to begin construction the second week of July.

k. CAM/Municipality of Puerto Cortés

This 3-month sub-award was signed Mayo 9, 2001.

During this quarter CHF contracted a private company, "Consultores Asociados Metropolitanos," to develop an urban development plan (master plan) in an area of 30 hectares in Puerto Cortés. CAM has almost completed the first phase of the contract representing 33% progress, which includes the urban design of an area of 3.5 manzanas of the whole area.

Although CHF contracted directly with CAM, an agreement of understanding was signed with the mayor of Puerto Cortes, who originally requested HOGAR's support for this project.

4. Follow-up on Previously Finished Projects

a. Colonia Irlanda, San Jerónimo , GOAL

CHF has made several trips to the San Jerónimo project to review the use of the latrines and to provide additional technical assistance. Due to the fact that all efforts made to date, by the NGO and the beneficiaries have not produced the desired with the correct use and acceptance of the sanitation facilities, GOAL will propose a new alternative to improve this situation. This proposal is expected to need additional funding which will be analyzed by GOAL and CHF.

5. Accepted Proposals to be signed

a. "Purchase of Land", Amarateca, ADRA

This project has been approved, and all contract negotiations have taken place. During this last quarter, the legal ownership of the land and the area needed for the treatment lagoon were confirmed. Unfortunately, the Director of ADRA had to leave the country in late June and is not expected to return until mid-July to sign the contract.

D. Performance

General progress on basic and complementary solutions for each project is shown in the attached Table 1. This table clearly shows that there is only one sub-donation still pending, the ADRA land purchase for the wastewater lagoon in Amarateca. The program goal for number of solutions to be completed will be surpassed by more than 1,500 homes with the contracts already signed. The small amount of still available funds will be invested in complementary works of existing projects. The status of each project is presented in Table 2.

In addition to surpassing the goal of 3,000 solutions, 8 NGOs are working with credit, and 14 different organizations and NGOs are participating in the program, one short of the goal of 15. Although the number of organizations participating is one short, the intention of this indicator was to ensure broad geographic coverage and participation by many. This objective has been met.

Tables 3 and 4 illustrate the housing occupancy rates and property title status for the applicable finished projects.

Table 5 shows the status of the environmental license for each of the HOGAR projects including those projects that have already received their license. Although an approved license was not required before work began in each project, all approved projects meet USAID and GOH environmental standards. Annex A shows a summary of the environmental and risk mitigation measures applied to each project.

Tables 6, 7 and 8 show the quarterly counterpart, the accumulated counterpart and the disbursement of funds to NGOs. It is important to mention that even though the deadline for the HOGAR program is December 31, 2001 all projects are expected to complete construction on or before September 30, 2001. To date 98 % of the funds have been fully committed. Furthermore 63 % of the fully committed funds have been disbursed.

It is important to mention that the counterpart reported to date represents more than 51% of the approved funds and 81% of the funds disbursed to date. This is much higher than the proposed 32%. All projects have been approved with a minimum of 32% counterpart and many have reached percentages of 50%. This additional counterpart will allow the program to surpass the 3,000-solution goal by more than 1,500. To date, \$3,103,198 of counterpart has been reported, or 84% of the goal.

As per the original HOGAR proposal, an external engineer was hired this quarter to inspect all HOGAR projects to assure the quality in all phases of the construction process. This engineer will provide an objective external opinion of all projects.

Annex B highlights pictures and descriptions of the HOGAR projects.

Annex C reviews the most relevant news articles published about the HOGAR Program during this period.

E. Lessons Learned

- Both the NOG's as well as CHF must follow up on all the compromises established in the Environmental Guidelines and Environmental Licenses. Special follow-up should be carried out by the social and technical staff to guarantee that all commitments are met as promised.
- It is very important that the technical staff with the NGOs understands and complies with the clauses of the sub-award/contract agreement, especially those that refers to budget modification. Also any technical or community development change should be reported to CHF prior their implementation. Although CHF took great pains to make the contracts clear and to review the highlights with each NGO, it appears that the commitments and requirements in the contracts are rarely shared with field personnel.
- In order to assure the legal clean title of land, a thorough investigation must be carried out. CHF recommends that as part of the investigation, an intent to purchase the land should be published in the local paper as well as installing a sign at the site before the land is purchased. These two steps will help to identify any additional "owners" before money changes hand. CHF is pleased to state that none of its projects have had land tenure issues, but issues have arisen on potential site locations.
- Follow-up visits after projects have been closed are important to ensure the success of the HOGAR program. Key areas to review are the proper use of sanitation facilities, the quality of construction and efficiency of infrastructure systems built. Social issues and community development are also key areas that are not easily evaluated immediately following the completion of construction activities, but they are key to the sustainability of any project.

F. Key Future Activities

- Sign the last HOGAR sub-award for the purchase of land in Amaratoca with ADRA
- Hold an environmental workshop with SERNA and USAID in October or November 2001
- Create a database with the complete information of the program beneficiaries
- Continue with the collection of statistical data of the technical and final cost of the solutions as well as the assurance of the occupancy of the houses.
- Continue providing technical assistance in the areas of construction, accounting, credit, social and community development issues for the projects currently in execution.

Annex A
Mitigation Measures Follow-up

Reported to June 30, 2001

Table 1
Program HOGAR
General Project Information

No	NGO	Location	Amount Requested US\$	Cost per Solution US\$	Execution Period (months)	Number of Houses	Number of New Solutions	Constructed Solutions per month
1	APAN "Niños Felices"	La Guacamaya, El Progreso/Yoro	80,575.00	2,369.85	1	34	34	34
2	NPH, Nueva Esperanza	Morocel/El Paraíso	140,773.00	977.59	6	30	144	5
3	GOAL, San Jerónimo	San Jerónimo/Comayagua	202,350.00	2,698.00	7	75	75	11
4	GOAL, Morazán II	Morazán/Yoro	393,312.00	3,933.12	13	100	100	8
5	HABITAT, Resid. Habitat Honduras	Amarateca, Km 16/Fco Morazán	500,000.00	2,857.14	8	175	175	22
6	AIEH, Col. Japon	Choloma/Cortés	354,518.70	1,363.53	6	80	260	13
7	ADRA, Villa El Porvenir	Amarateca, Km 16/Fco Morazán	320,350.36	2,135.67	13	150	150	12
8	ADRA/Streets Grading	Amarateca, Km 16/Fco Morazán	18,773.58	-	1.5	0	0	0
9	CRS, Colonias Unidas, Iztoca	Choluteca/Choluteca	793,468.07	1,194.98	10.5	208	664	20
10	GOAL Comayagua Phase I & II	Zona Urbana, Comayagua	290,400.00	2,200.00	6	132	132	6
11	GOAL Las Liconas	Zona Rural, Comayagua	67,915.80	2,425.56	8	28	28	9
12	APAN "Renacer"	La Guacamaya, El Progreso/Yoro	334,540.00	3,041.27	3	110	110	37
13	Hermanos Maristas	Col. Marcelino Champagnat, Choluteca	166,979.67	269.32	6	0	620	103
14	Atlas Logistique, Hato Nuevo I Etapa	Hato Nuevo, Choluteca	275,342.00	2,526.07	6	109	109	18
15	Atlas Logistique, Hato Nuevo II Etapa	Hato Nuevo, Choluteca	93,399.00	3,592.27	2	26	26	13
16	GOAL "Lazos de Amistad"	Mata de Caña, Comayagua	84,865.00	953.54	4	0	89	22
17	CRWRC (Comité de Ayuda Mundial)	Constuyendo sobre Roca, Amarateca	131,712.79	2,802.40	3	47	47	16
18	AIEH, Azacualpa	Azacualpa/ Sta. Bárbara	128,370.72	3,130.99	4	41	41	10
19	AIEH, La Lima	La Lima, Cortés	333,348.29	4,016.24	5	83	83	17
20	Project Team Work	"Umaña de Santiago" Pimienta, Cortés	268,000.00	4,466.67	6	60	60	10
21	APAN "El Milagro"	La Sábana, Cortés	725,903.00	3,629.52	3.5	200	200	57
22	Patronato Pro-Mejoramiento - Linda Miller	Villa Linda Miller, Km. 10 Salida a Olancho	180,000.00	1,097.56	5	0	164	33
23	ADRA, Land, Villa El Porvenir	Amarateca, Km 16/Fco Morazán	120,000.00	240.00	1	0	500	0
24	Land, Yoro	Agua Blanca Sur, Carretera al Progreso	50,000.00	-	1	0	450	0
25	CAM, Municipalidad de Cortés	Cortés	48,122.88	-	3	-	300	-
26	Complementary Work in all Projects	Mitigation Measures, Desings, Audits, etc.	96,980.14	-	-	-	-	-
TOTAL			6,200,000.00			1,688.00	4,561.00	
			Under or (Over) Budget	-100,000.00				# of solutions
			CHF counterpart	100,000.00				above the
			Available Funds	0.00				3000 goal
								1,561.00

Finalized Projects	\$2,408,345.54	38.84%
Projects in execution	\$3,671,654.46	59.22%
Accepted Projects, Contract not Signed	\$120,000.00	1.94%
Available Funds		0.00%



Table 2
HOGAR Program
Approved Project Status

Reported to June 30, 2001

No	NGO/Project	Start	End	Number Of Solutions	Approved Solutions					Project Advancement					
					Core Solutions				Complementary Solutions	Core Solutions				Complementary Solutions	
					Housing Rehabilitation	Potable Water	Sanitation Infrastructure	Land Purchases		Housing Rehabilitation	Potable Water	Sanitation Infrastructure	Land Purchases		Other Infrastructure
1	APAN, La Guacamaya/Yoro	May 30, 2000	Aug. 05, 2000	34	34						100%				
2	NPH, Mompel/El Paraiso	May 05, 2000	Oct. 05, 2000	144	30					144*	100%				100%
3	GOAL, San Jerónimo/Comayagua	June 16, 2000	Jan. 16, 2001	75	75	75	75				100%	100%	100%		
4	GOAL, Morazán II/Yoro	June 16, 2000	July 28, 2001	100	100	100	100	100			100%	65%	100%	100%	
5	HABITAT, Amarateca/Francisco Morazán	June 28, 2000	Apr. 15, 2001	175	175						100%				100%
6	AIEH, Col. Japon, Choloma/Cortés	June 29, 2000	March 30, 2001	260	80		260			260	100%		100%		
7	ADRA, Villa El Porvenir/Francisco Morazán	Sept. 01, 2000	Aug. 15, 2001	150	150										100%
8	ADRA, Streets Grading-Removal of Rock Mantle	Feb. 12, 2001	Jun. 08, 2001	-							99%	91%	0%		
9	CRS, Colonias Unidas/Choluteca	Sept. 26, 2000	Aug. 10, 2001	664	208	664	664				30%				
10	GOAL, Casco Urbano/Comayagua	April 01, 2001	Sept. 30, 2001	132	132						100%				
11	GOAL, Las Leonas/Comayagua	Oct. 23, 2000	Apr. 01, 2001	28	28						100%				
12	APAN, Renacer de Guacamaya/Yoro	Nov. 06, 2000	Apr. 15, 2001	110	110										
13	Hermanos Maristas, Col. Champagna/Choluteca	Nov. 20, 2000	Apr. 20, 2000	620		620						100%			
14	Atlas Logístico, Hato Nuevo Choluteca	Dec. 04, 2000	June 04, 2001	109	109						100%				
15	Atlas Logístico, Hato Nuevo II Etapa	June 05, 2001	Aug. 05, 2001	26	26						25%				
16	GOAL "Lazos de Amistad", Comayagua	Feb. 01, 2001	July 01, 2001	89		89						100%			
17	CRWRC, Amarateca/Fco Moraz	Dec. 15, 2000	March 15, 2001	47	47						80%				
18	AIEH, Azacualpa	Feb. 09, 2001	July 30, 2001	41	41	41					85%	80%	80%		
19	AIEH, La Lima	Feb. 09, 2001	Aug 09, 2001	83	83		83				30%	85%	70%		
20	Project Teamwork, Plinilla/Cortés	Feb. 28, 2001	Aug. 28, 2001	60	60	60	60				0%	0%	0%		
21	APAN "El Milagro"	June 18, 2001	Sept. 30, 2001	200	200	200	200					70%	10%		
22	Patronato Pro-Mejoramiento, Linda Miller	May 02, 2001	Sept. 30, 2001	164		164	164								
23	ADRA, Land, Villa El Porvenir			500				878							
24	Land, Agua Blanca Sur, Yoro	April 17, 2001	May 17, 2001	450				450							100%
25	CAM, Municipalidad de Cortés	May 09, 2001	Aug. 09, 2001	300					300						30%
26	Complementary Work in all Projects														50%
					1,688	1,165	1,144	500	1,144						
Total Solutions = Core and Complementary solutions					4,561	4,147			414						

Notes:

* This includes electrical installations and lot grading

** Preliminary activities

This value has been included in order to compare it with the total Number of Solutions

Complementary Solutions include: Electrical Systems, Schools, Health Centers, Community Centers, Recreational Areas and other communal facilities.

Key:

Finalized Projects
Projects in execution
Each solution has been counted only once
Assigned projects, but Council Pending

14



Table 3
HOGAR Program
Housing Occupancy for the Period of April - June, 2001

NGO	Project	Location	Project Completion Date	Number of houses	No. of Houses Occupied	%
CRS	Colonias Unidas/Iztoca	Choluteca	8/10/01	208	105.00	50.48
ATLAS	Hato Nuevo I PHASE	Choluteca	6/4/01	109	106.00	97.25
CRWRC	Construyendo Sobre La Roca	Amarateca, F.M.	3/15/01	47	41.00	87.23
HABITAT	Residencial Hábitat Honduras	Amarateca, F.M.	4/15/01	175	145.00	82.86
APAN	Niños Felices	Guacamaya, El Progreso	8/5/00	34	34.00	100.00
APAN	Renacer	Guacamaya, El Progreso	5/31/01	110	99.00	90.00
GOAL	San Jerónimo	Colonia Irlanda	1/16/01	75	54.00	72.00
GOAL	Flor del Campo	Morazán, Yoro	4/28/01	100	25.00	25.00
AIEH	Colonia Japón	Choloma, Cortés	3/30/01	80	80.00	100.00
GOAL	Las Liconas	Comayagua	4/1/01	28	28.00	100.00
				966	717.00	74.22



Table 4
STATUS ON HOUSES LEGALIZATION
HOGAR PROGRAM

Report to: June 30, 2001

NGO/PROJECT	STATUS
APAN/Niños Felices	Titles will be delivered to each beneficiary between July 02-06, 2001.
NPH/Proyecto Nueva Esperanza	The beneficiaries pay a monthly fee. At the end of the payment term each family will receive their property title.
GOAL/San Jerónimo	The beneficiaries receive a municipal certificate which allows them to register directly at the municipal register office.
GOAL/Morazán II	The Municipal Office is processing the titles for each beneficiary.
HPH/Residencial Honduras	85 delivered Registered Titles, 27 Titles in process at the Register's Office, the rest are at the Lawyer's office.
AIEH/Colonia Japón	37 delivered registered titles, while 43 are in process to be delivered at the municipal register's office.
GOAL/Liconas	Program joining with the Municipal Office (P.A.A.R) and are processing the Titles for each beneficiary.
APAN/Renacer	Titles will be delivered the first week of August '01.
Hermanos Maristas/Marcelino C.	120 delivered titles to the date. After the beneficiaries finish their land payment they will received the title.
Atlas/Hato Nuevo I PHASE	Each beneficiary is processing the Title, through donation documents delivered by Atlas, which indicates that the house cannot be sold or rented during a period of 10 years.
CRWRC/Construyendo Sobre la Roca	Beneficiaries pay a monthly fee and at the end they receive the property title.

Table 5
HOGAR Program
Environmental Licenses Status

June 30, 2001

No.	NGO & Project Site	Status of the Environmental License
1	Children International/APAN – Aldea La Guacamaya, El Progreso, Yoro	Approved
2	Nuestros Pequeños Hermanos – Morocelí, El Paraíso	Approved
3	GOAL – San Jerónimo, Comayagua	Pending signature of Mitigation Measures Contract.
4	GOAL – Morazán II, Yoro	Pending signature of Mitigation Measures Contract.
5	HABITAT – Amarateca, Francisco Morazán	Approved
6	AIEH – Colonia Japón, Choloma, Cortés	Pending signature of Mitigation Measures Contract.
7	ADRA – Villa El Porvenir, Amarateca, Francisco Morazán	After changing the location of the treatment plant, IOM informed that the license has been approved.
8	CRS – Colonias Unidas, Choluteca	The file was given back to the General Secretariat of Environment for additional information.
C 9	GOAL – Casco Urbano, Comayagua	It does not apply because there are dispersed rehabilitations.
C 10	GOAL – Las Liconas, Comayagua	It does not apply because there are dispersed rehabilitations.
C 11	Children International/APAN- Renacer, Yoro	Approved
C 12	Hermanos Maristas – Marcelino Champagnat, Choluteca	Approved
13	Atlas Logistique – Hato Nuevo, Choluteca	Approved
14	GOAL – Lazos de Amistad, Comayagua	Pending signature of Mitigation Measures Contract.
15	CRWRC – Construyendo Sobre la Roca, Amarateca, Francisco Morazán	Pending signature of Mitigation Measures Contract.
16	AIEH – La Lima, Cortés	Pending signature of Mitigation Measures Contract.
17	AIEH – Azacualpa, Santa Bárbara	Pending signature of Mitigation Measures Contract.
18	Project Teamwork – Pimienta, Cortés	The process has been initiated by the Municipality of Pimienta, Cortés.



Table 6
 QUARTERLY COUNTERPART REPORT
 From April to June 2001 Only

NGO	Voluntary Services	Services and Property	Beneficiary Counterpart	Materials and Supplies	Economic Resources	GRAND-TOTAL	US\$ EQUIVALENT BY NGO	US\$ EQUIVALENT BY CHF
Hábitat - Amarateca	-	-	1,890.00	-	139,639.01	141,529.01	9,286.86	9,265.42
ADRA - Amarateca	15,899.88	309,595.04	19,972.57	863,695.75	-	589,973.16	38,851.29	38,643.05
CRS - Colonias Unidas	-	10,500.00	774,495.00	1,000.00	3,476,399.56	4,262,394.56	281,346.18	278,805.30
GOAL - Casco Urbano	107,370.00	916,100.00	101,260.00	18,768.96	-	1,143,498.96	75,032.74	74,805.35
GOAL - Las Liconas	-	-	18,600.00	-	-	18,600.00	1,220.47	1,219.99
APAN - Renacer	154,000.00	521,215.80	-	364,031.96	-	1,039,247.76	69,888.89	68,165.27
ATLAS - Hato Nuevo	1,278.00	-	173,354.04	443,304.50	354,560.00	972,496.54	63,404.98	63,666.49
GOAL - Lazos de Amistad	-	-	482,000.00	-	-	482,000.00	31,627.30	31,536.53
AIEH - La Lima	11,703.13	37,800.00	143,683.75	45,000.00	-	238,186.88	15,317.48	15,589.64
AIEH - Azacualpa	4,025.00	-	92,610.00	-	-	96,635.00	6,214.47	6,312.44
PTW - Umaña de Santiago	-	-	-	722,236.28	657,713.75	1,379,950.03	90,112.99	90,112.99
TOTALS	\$294,276.01	\$1,176,020.76	\$1,807,865.36	\$2,458,037.45	\$4,628,312.32	\$10,364,511.90	\$682,303.65	\$678,122.47

Differences between NGO and CHF amounts are due to exchange rate differences.

Table 7
ACCUMULATED COUNTERPART REPORT
Reported to June 2001

NGO	Voluntary Services	Services and Property	Beneficiary Counterpart	Materials and Supplies	Economic Resources	GRAND-TOTAL	US\$ EQUIVALENT BY NGO	US\$ EQUIVALENT BY CHF
APAN - Niños Felices	-	123,420.15	165,370.62	69,364.08	58,617.42	416,772.27	28,902.38	28,086.31
NPH - Proy. Nueva Esperanza	-	30,000.00	1,639,832.04	4,068,469.68	609,921.00	6,348,222.72	430,758.87	428,369.09
GOAL - San Jerónimo	-	808,500.00	1,398,700.00	294,205.00	1,707,654.90	4,209,059.90	285,560.08	284,649.82
GOAL - Morazán	59,352.90	-	1,182,300.00	267,535.00	-	1,509,187.90	99,972.07	99,840.13
Hábitat - Amarateca	141,260.00	775,924.48	253,060.00	741,598.91	2,529,248.35	4,441,091.74	298,106.57	297,338.07
AIEH - Col. Japón	147,181.94	4,782,196.15	121,037.00	210,386.40	166,000.00	5,426,801.49	364,508.33	366,729.40
ADRA - Amarateca	32,309.83	1,383,553.05	80,759.91	1,795,760.71	-	3,292,383.50	217,945.81	218,408.65
CRS - Colonias Unidas	-	29,000.00	1,571,505.94	3,052.00	4,077,381.24	5,680,939.18	374,979.48	372,380.00
GOAL - Casco Urbano	107,370.00	916,100.00	101,260.00	18,768.96	-	1,143,498.96	75,032.74	74,805.35
GOAL - Las Liconas	55,744.00	255,376.32	227,472.00	35,825.16	-	574,417.48	37,973.70	37,954.14
APAN - RENACER	8,800.00	670,988.00	425,760.00	47,836.56	-	1,153,384.56	77,564.53	76,260.21
Hermanos Maristas	85,275.00	678,229.00	450,053.56	69,498.90	165,604.84	1,448,661.30	96,033.23	95,905.45
ATLAS - Hato Nuevo	472,756.00	1,281,176.00	382,612.48	67,170.00	-	2,203,714.48	145,149.78	145,335.65
GOAL - Lazos de Amistad	-	5,056,340.87	911,249.76	55,012.68	-	6,022,603.31	396,337.44	396,183.66
CRWRC - Const. sobre Roca	102,364.00	327,140.00	83,696.33	666,548.52	100,347.00	1,280,095.85	84,260.93	84,398.40
PTW - Umaña de Santiago	-	-	-	722,236.28	657,713.74	1,379,950.03	90,112.99	90,112.99
TOTALS	\$1,212,413.67	\$17,117,944.02	\$8,994,669.64	\$9,133,268.84	\$10,072,488.49	\$46,530,784.67	\$3,103,198.94	\$3,096,757.31

Differences between NGO and CHF amounts are due to exchange rate differences.

Table 8
HOGAR PROGRAM
Disbursement Management Plan for the Quarter of April - June 2001

No.	NGO	Approved Amount	DISBURSEMENTS			
			Date	No.	Quarterly Amount	Accumulated
1	Children International/APAN - Niños Felices	\$ 80,575.00				\$ 80,549.49
2	Nuestros Pequeños Hermanos - Morocelí	\$ 140,773.00				\$ 140,773.00
3	GOAL - San Jerónimo/Comayagua	\$ 202,350.00	05/16/01	3	\$ 13,697.50	\$ 185,695.00
4	GOAL - Morazán/Yoro	\$ 393,312.00	7/5/01	6	\$ 31,557.95	\$ 334,315.20
5	Hábitat - Amaratéca/Fco. Morazán	\$ 500,000.00				\$ 430,275.58
6	AIEH - Col. Japón/Choloma - Cortés ⁽¹⁾	\$ 354,518.70				\$ 345,674.57
7	ADRA - Villa El Porvenir	\$ 320,350.36				\$ 217,901.99
8	CRS - Colonias Unidas	\$ 793,468.07	10/4/01	2	\$ 292,837.00	\$ 682,837.00
			06/28/01	3	\$ 200,000.00	
C 9	GOAL - Casco Urbano	\$ 290,400.00	06/25/01	1	\$ 20,880.28	\$ 20,880.28
C 10	GOAL - Las Liconas	\$ 67,915.80	7/5/01	4	\$ 19,578.72	\$ 67,915.80
C 11	Children International/APAN - RENACER	\$ 334,540.00	6/6/01	3	\$ 6,200.00	\$ 334,540.00
C 12	Hermanos Maristas - Marcelino Champagnat	\$ 166,979.67				\$ 166,976.71
13	Atlas Logistique - Hato Nuevo	\$ 275,342.00	04/23/01	4	\$ 46,271.38	\$ 224,528.06
			05/21/01	5	\$ 25,794.51	
14	GOAL - Lazos de Amistad	\$ 84,865.00	7/5/01	1	\$ 9,816.78	\$ 58,298.61
			05/16/01	2	\$ 32,689.43	
			06/26/01	3	\$ 15,492.40	
15	CRWRC - Construyendo sobre la Roca ⁽²⁾	\$ 131,712.79				\$ 113,348.67
16	AIEH - La Lima ⁽³⁾	\$ 333,348.29	05/16/01	2	\$ 65,821.95	\$ 138,004.70
17	AIEH - Azacualpa ⁽⁴⁾	\$ 128,370.72	05/16/01	2	\$ 46,075.37	\$ 85,447.77
18	Project Teamwork - Umaña de Santiago	\$ 268,000.00	7/5/01	2	\$ 60,000.00	\$ 120,000.00
C 19	ADRA - Landscaping (INTEGRAL)	\$ 18,773.58	2/4/01	2	\$ 9,925.30	\$ 18,773.58
			06/22/01	3	\$ 1,094.61	
C 20	Cooperativa de Vivienda Getsemaní	\$ 50,000.00	04/17/01	1	\$ 50,000.00	\$ 50,000.00
C 21	CAM	\$ 48,122.88	05/18/01	1	\$ 14,436.86	\$ 14,436.86
C 22	Inversiones Diversas	\$ 17,844.62	05/14/01	1	\$ 7,153.22	\$ 17,844.62
			6/6/01	2	\$ 10,691.41	
23	Atlas Logistique - Ampliación Hato Nuevo	\$ 93,399.00				\$ -
C 24	INTEGRAL	\$ 3,466.60				
25	Children International/APAN - El Milagro	\$ 725,903.00				
26	Ingeniería Ortega S. de R.L.	\$ 93,691.70				
GRAND-TOTAL		\$ 5,918,022.78			\$ 980,014.67	\$ 3,849,017.49

(1) This sub-grant was awarded in Lempiras (L. 5,250,069.72), using an Exchange Rate of 1US\$ = L. 14.7342

(2) This sub-grant was awarded in Lempiras (L. 1,982,936.00), using an Exchange Rate of 1US\$ = L. 15.055

(3) This sub-grant was awarded in Lempiras (L. 5,044,392.99), using an Exchange Rate of 1US\$ = L. 15.1325

(4) This sub-grant was awarded in Lempiras (L. 1,942,569.86), using an Exchange Rate of 1US\$ = L. 15.1325

NOTE: This table indicates a total approved amount lower than values showed in table 1, including the Finalized Projects and Projects in execution. This difference is due to the fact that the amount assigned for the complementary works are reserved funds to assure the execution of these works, most of them already requested.

**Annex B:
Photograph Descriptions**

Photographs Description

Page 1 La Lima Project. NGO: AIEH

Picture 1: Floor slab installation

Picture 2: Beneficiaries curing wood bean

Picture 3: Conduction line for the water system

Picture 4: Houses in their final stage of construction

Page 2 Azacualpa Project. NGO: AIEH

Picture 1: Duplex home under construction

Picture 2: Permanent houses replacing temporary shelters

Picture 3: Beneficiary installing block

Page 3 Renacer Project. NGO: APAN/CI

Picture 1: Lisa Pacholek, CHF Country Director, explains to Honduras President Mr. Carlos Flores and US Ambassador, Mr. Frank Almaguer, the construction method use by APAN in the Renacer Project.

Picture 2: Street grading before project inauguration

Picture 3: Installation of main distribution pipelines

Picture 4: President Flores and the US Ambassador during the inauguration ceremony

Page 4 Umaña de Santiago Project. NGO: Project Teamwork

Picture 1: New cut and fill activities in block G. All slopes will be stabilized with geo-textile as part of the mitigation measures for the project.

Picture 2: Construction of a block wall showing precision and good quality materials

Picture 3: Initial slope preparation for gabion wall installation

Picture 4: Peter Hearne (USAID) and CHF technical personal with PTW Project Manager inspecting mitigation measures

Page 5 El Milagro Project, Villanueva Cortés. NGO: APAN/CI

Picture 1: Street grading prior to house construction

Page 6 Flor del Campo Project, Morazán Yoro. NGO: GOAL

Picture 1: Inauguration day at the Morazán project

Picture 2: Vice-President of Honduras, Mr. Billy Handal, presiding over the inauguration acts with USAID, GOAL and CHF representatives.

Picture 3: General view of the site on inauguration day, May 8th, 2001

Picture 4: Panorama of the housing project

Page 7 Lazos de Amistad Project, Comayagua. NGO: GOAL

Picture 1: Installation of main distribution pipelines

Picture 2: Scour valve installation and concrete supports of conduction line

Page 8 Housing Rehabilitation Project, Comayagua City. NGO: GOAL

Picture 1: Adobe home being rehabilitated

Picture 2: Monolithic pour of ring beam and columns in a new house

Page 9 Villa El Porvenir, Amaratéca. NGO: ADRA

Picture 1: Rock after dynamite was used as part of the definition of internal streets. The rock is used by ADRA as the main material for the house foundation.

Picture 2: Beneficiary laying block in his future house

**Page 10 Col. Marcelino Champagnat Project, Choluteca. NGO: Hermanos Maristas
Colonias Unidas Project, Choluteca. NGO: CRS**

Picture 1: CHF, Hermanos Maristas, and Municipal representatives in the Inauguration Ceremony, May 19, 2001.

Picture 2: Satisfied beneficiary comments on benefits of water system.

Picture 3: Rainwater drainage system in construction, pump station and 60,000 gallon-tank.


Picture 4: Completed House.

Page 11 Hato Nuevo Project, Choluteca. NGO: Atlas Logistique

Picture 1: Healthcare center in final stages of construction. Phase II of the Hato Nuevo Project

Picture 2: Occupied home showing beneficiary improvements and personal details

Projects in the North of
Honduras
Cortés, Yoro and Santa Bárbara

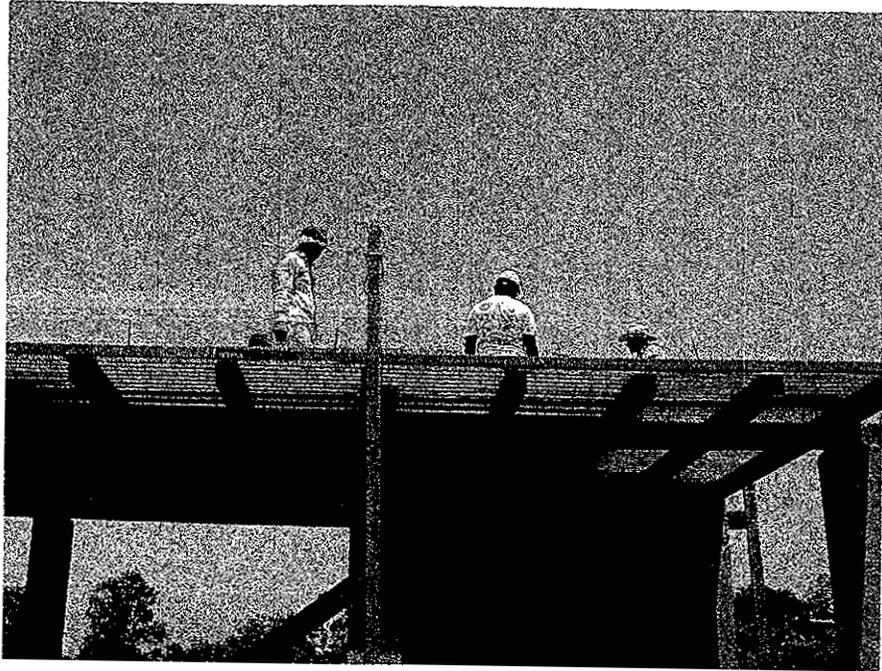

Picture 1




Picture 2

La Lima Project, NGO: AIEH



Picture 3

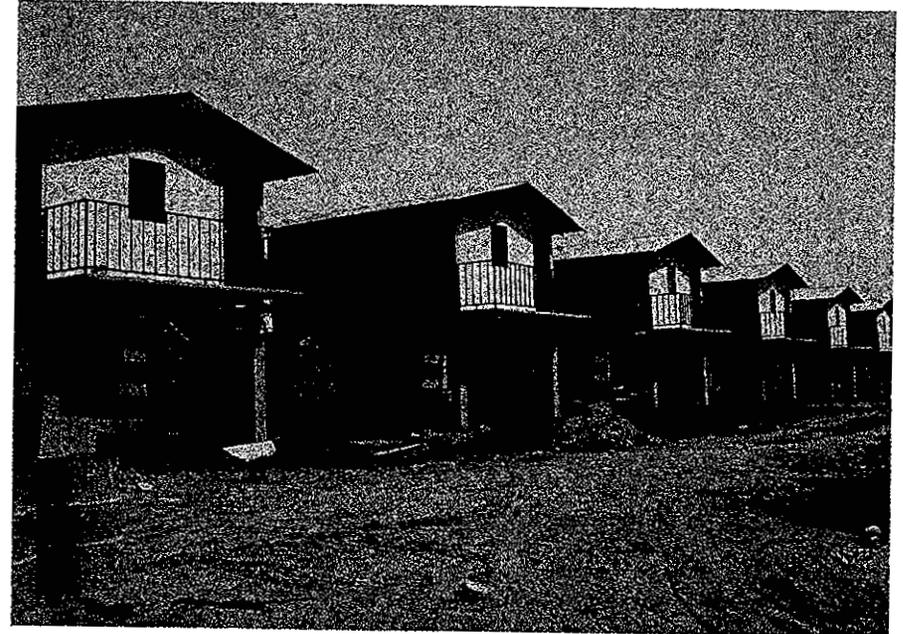


Picture 4

25



Picture 1

Azacualpa Project, NGO: AIEH

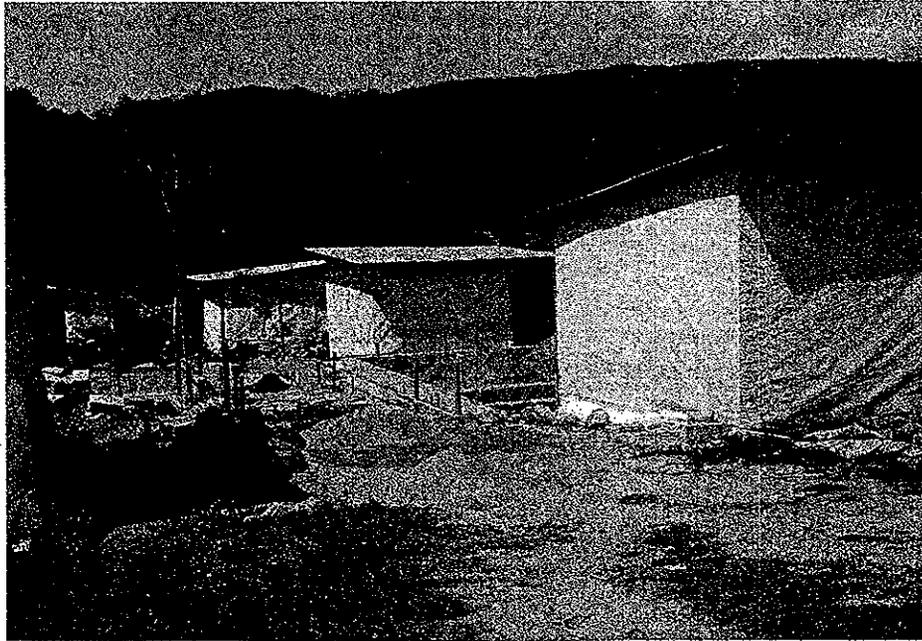

Picture 2



Picture 3



Picture 1

Picture 2

Renacer Project, NGO: APAN-CI




CHF-Honduras

Picture 3

Picture 4

27

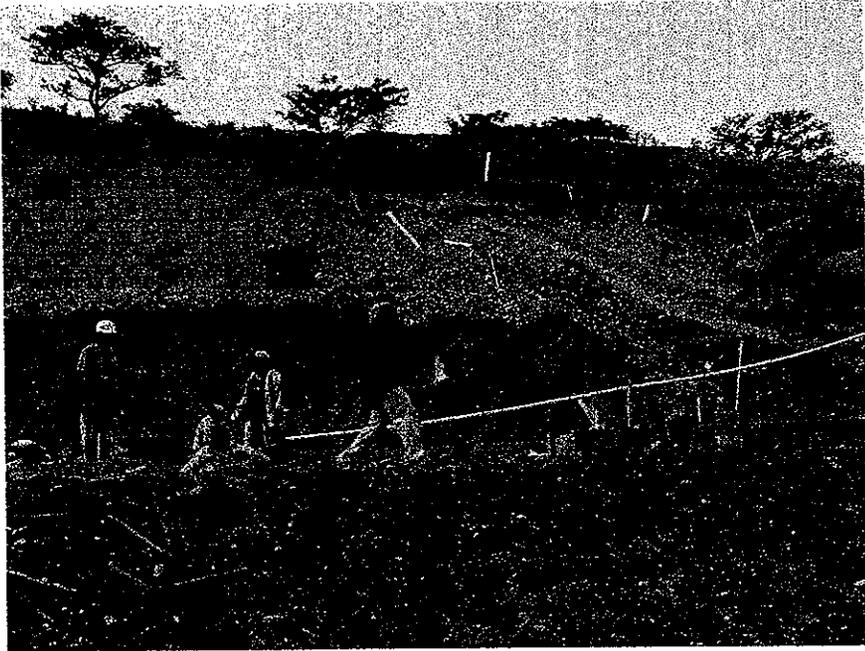

Picture 1

Umaña de Santiago Project. Pimienta, Cortés. NGO: Project Teamwork




CHF-Honduras

Picture 3

Picture 4

28

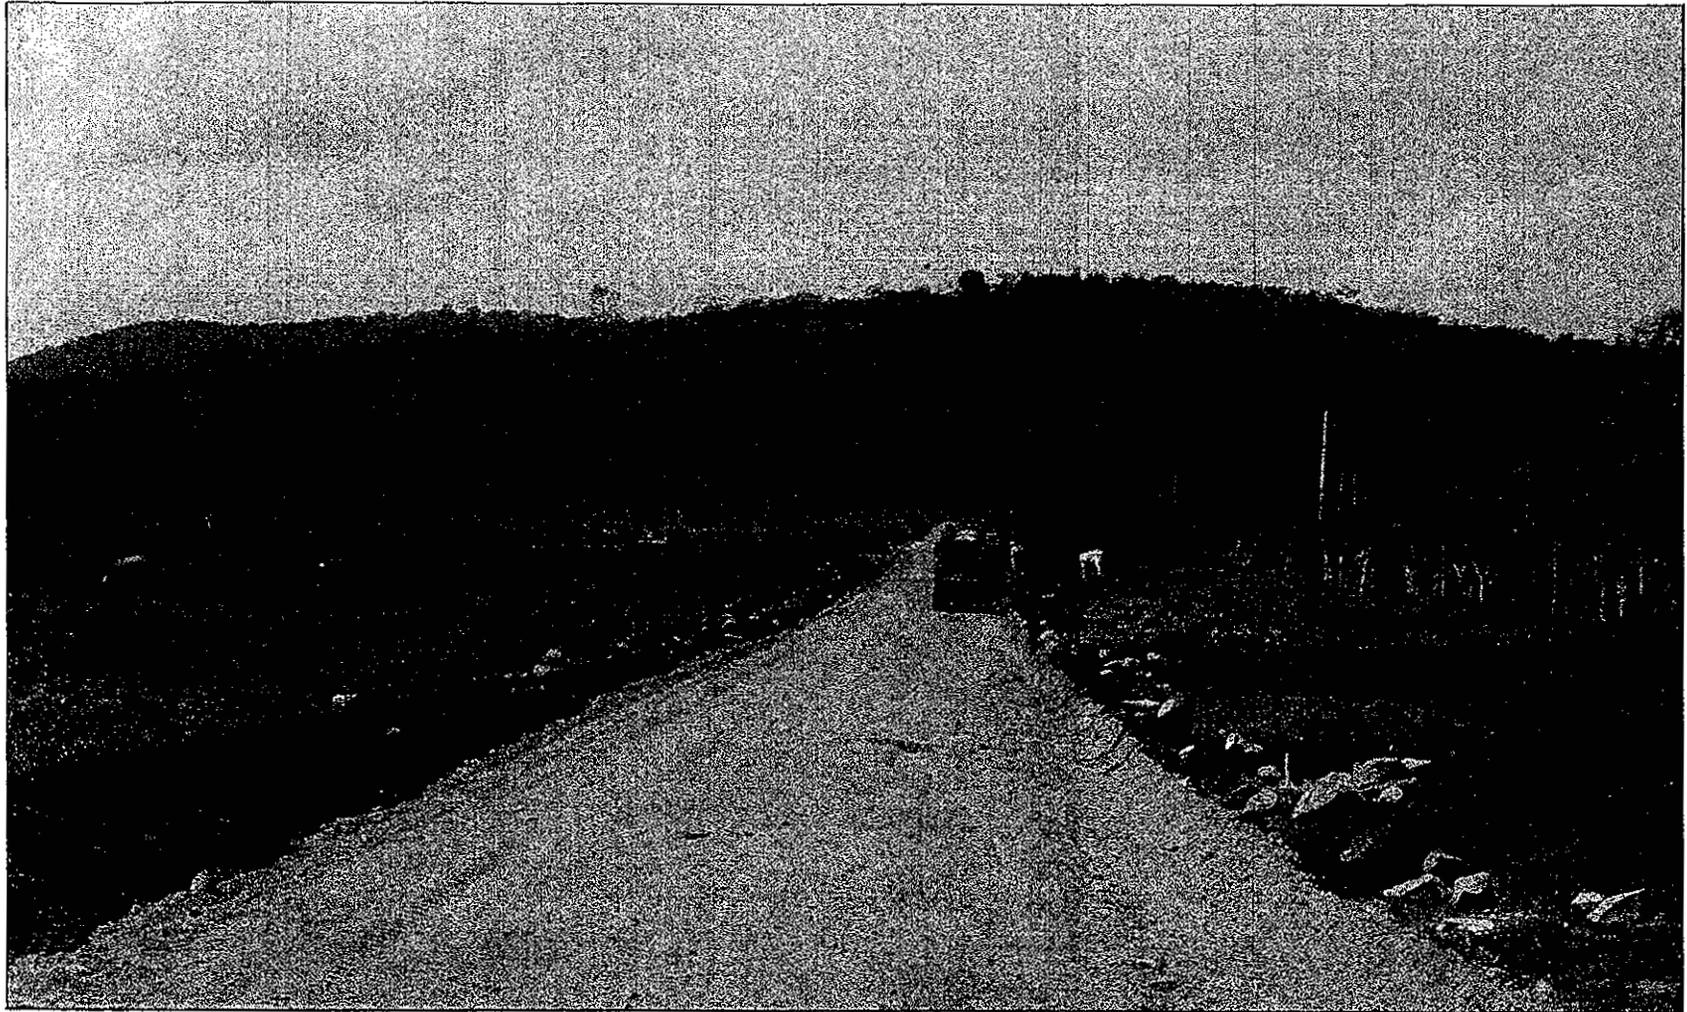

Picture 1

El Milagro Project, NGO: APAN-CI

BEST AVAILABLE COPY

CHF-Honduras

Page 5

29




Picture 1



Picture 2

Flor del Campo Project. Morazán, Yoro. NGO: GOAL

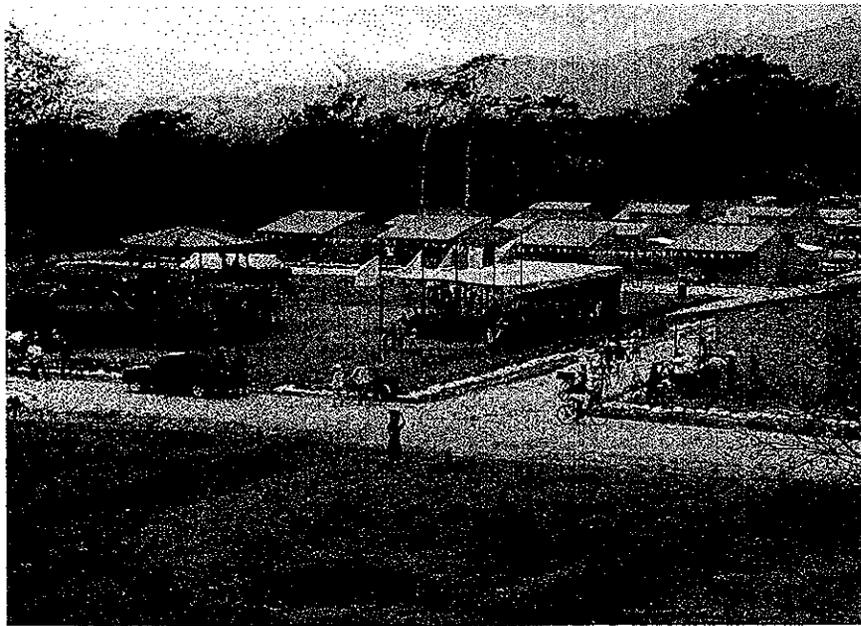

Picture 3



Picture 4

Projects in the Central
Region of Honduras
Comayagua



Picture 1



Picture 2

Lazos de Amistad Project, Comayagua
NGO: GOAL

BEST AVAILABLE COPY



Picture 1




Picture 2

Housing Rehabilitation Project
Casco Urbano, Comayagua
NGO: GOAL


BEST AVAILABLE COPY

Projects in Amaratéca Sector, Francisco Morazán

BEST AVAILABLE COPY

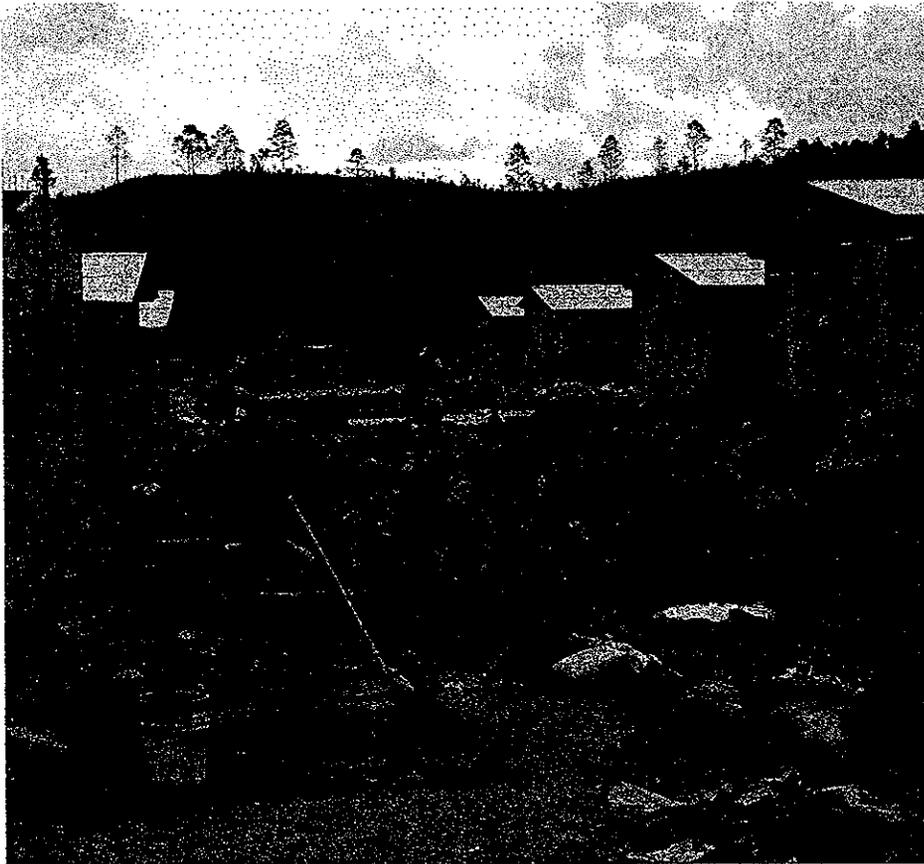

Picture 1

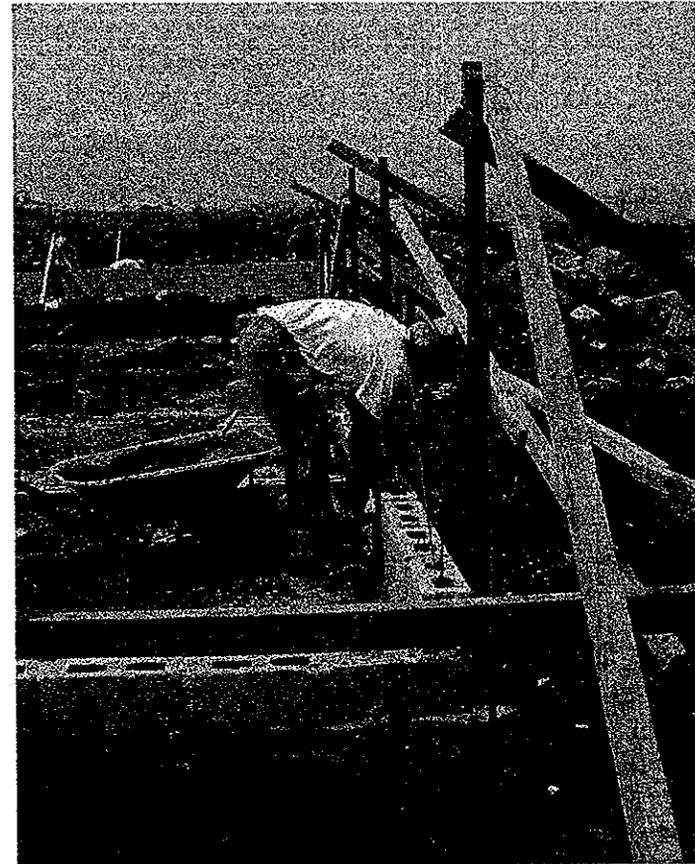

Picture 2


**Villa El Porvenir, Amaratéca
NGO: ADRA**

BEST AVAILABLE COPY

Projects in the South of Honduras, Choluteca




Picture 1

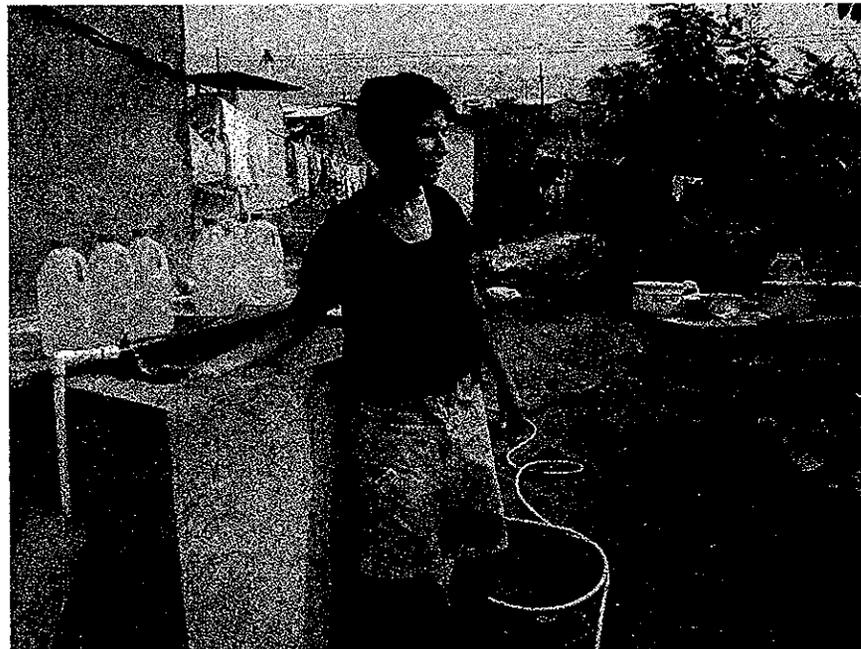


Picture 2

Col. Marcelino Champagnat Project, NGO: Hermanos Maristas

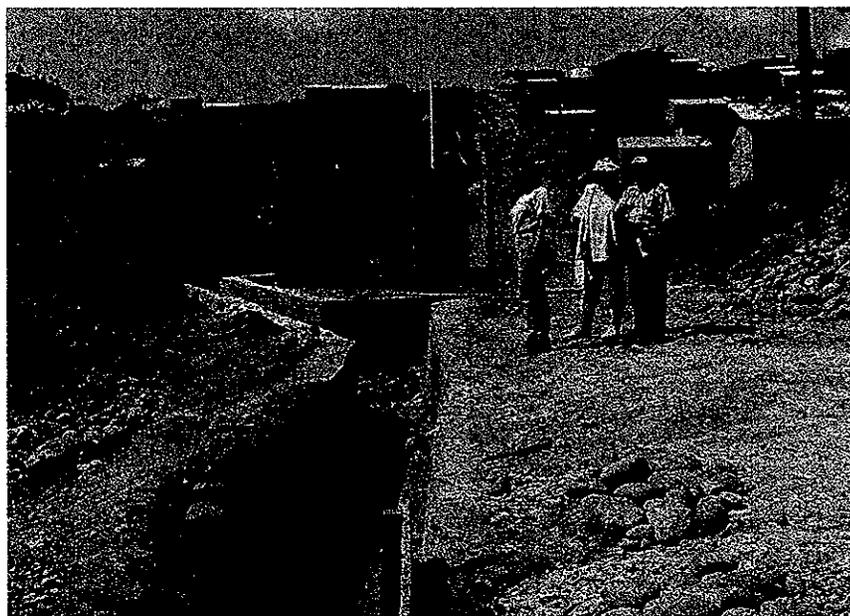

Picture 3

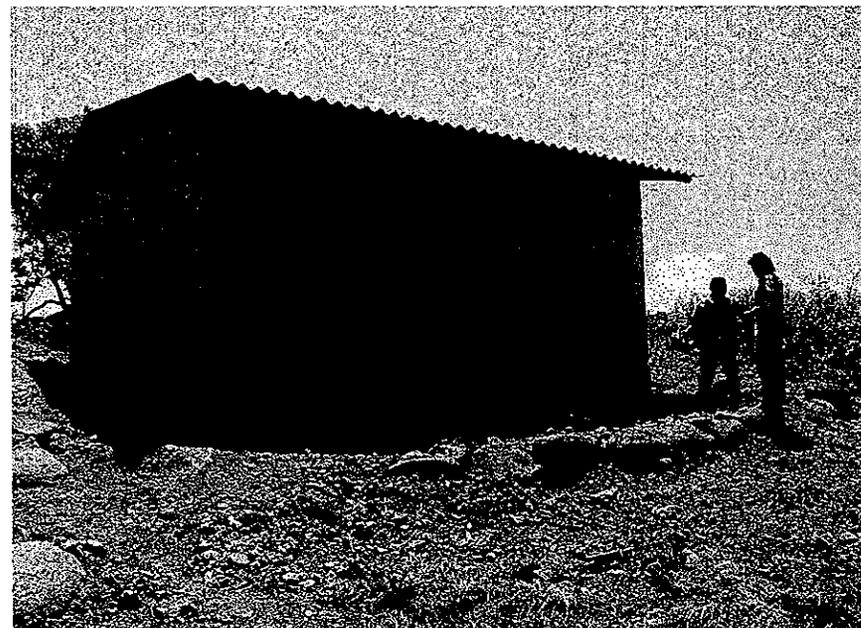

Picture 4

Colonias Unidas Project, NGO: CRS



Picture 1



Picture 2

Hato Nuevo Project, NGO: Atlas Logistique
Hato Nuevo, Choluteca

BEST AVAILABLE COPY

ANNEX C
HOGAR in the News

HOGAR ACTIVITIES IN THE NEWS
April-June 2001

**H
O
G
A
R

I
N

T
H
E

N
E
W
S**

May 10, 2001

With pride, CHF carried out the inauguration of three housing projects, two Starter Home projects and one HOGAR project.

In two of the inaugurations, Starter Home Project, Colonia La Esperanza in Guaymitas, El Progreso, Yoro; and Project Renacer, La Guacamaya, El Progreso, Yoro, of the Program HOGAR, CHF was pleased with the presence of the President of the Republic of Honduras, Ing. Carlos Flores Facussé, who in one of his speeches expressed: "Here is a symbol of what reconstruction is, and one more example of the transformation of the country."

In addition to the President of Honduras, the US Ambassador to Honduras, Frank Almaguer, officials from USAID and other representatives of the local Government attended the ceremonies.

The inaugurations were covered by almost all the mass media at the national level. Some of the publications are as follows:

Friday – May 11, 2001
Newspaper: La Prensa

Ambassador Frank Almaguer affirms when inaugurating two housing projects: "These projects represent the type of integral development that my government supports with the Honduran national reconstruction effort."

Friday – May 11, 2001
Newspaper: El Heraldo

President Flores inaugurates two housing projects: Colonia Renacer, in La Guacamaya, which consists of 110 houses, and Colonia La Esperanza, in Guaymitas, with 71 housing solutions, both in El Progreso, Yoro

Friday – May 11, 2001
Newspaper: La Tribuna

President Flores shared the words of the Director of CHF in Honduras, Lisa Pacholek, expressing: "There is a true feeling of confidence and faith in which it is possible to be done, when we arrange to do them and when we put will in what we want to do."

Monday – May 21, 2001
Newspaper: La Tribuna
Section Reconstructing Honduras

The President of the Hondurans inaugurated 181 houses built with funds donated by the Government of the United States and that will benefit thousands of people in the Department of Yoro who were affected by Hurricane Mitch.

Other media representatives attending this ceremony were:

Week from the 7 to the 11 of May, 2001

RADIO: Radio América Morning Newsreel

TV – CHANNEL 7 – ABRIENDO BRECHA NEWSREEL

EVENING NEWS: 7:00 to 8:00 PM

TV – CHANNEL 6 – EVENING NEWS: 5:00 to 7:00 PM

Directed by: RUBÉN QUIRÓZ, VANESA BOGRÁN Y GERMAN MIRANDA

HOGAR Program – Dedication Ceremony for the Colonia Japón Project

CHF through the HOGAR Program inaugurates another housing project. In this occasion with NGO AIEH.

News reporting the dedication ceremony of the Colonia Japón development in Choloma, Cortés, where 260 families victims of hurricane Mitch where benefited with 80 homes, one school, one day care center, one health center and sanitary sewage system.

HOGAR Program – Dedications Ceremonies for: GOAL Colonia Flor del Campo and Barrio Las Liconas

CHF celebrated the inaugurations of the GOAL Projects, Colonia Flor del Campo y Barrio Las Liconas.

Colonia Flor del Campo, Morazán, Yoro

On May 8, 2001, one hundred families of the Municipality of Morazán, Yoro, received the keys of their houses.

It is important to mention that the houses have potable water provision, latrines, washbasins, showers and improved stoves. An area for obtaining firewood has been created (daily energy source), like part of a sustainable development of the project.

The inauguration ceremony was presided by the main representatives of GOAL and CHF NGOs, as well as Officials of USAID and the Vice-president of the Republic, Mr. Billy Handal.
