



# Biweekly Report

## September 16-30, 2006

ALTERNATIVE LIVELIHOODS  
PROGRAM - EASTERN REGION



Completed reservoir (above) and completed flood protection wall (below) in Durbaba, Nangarhar





## EXECUTIVE SUMMARY

Highlights of ALP/E activities and achievements during this reporting period:

- ALP/E's efforts supporting small fruit producers continue to yield positive results; fruit sales have reached 80MT and increased revenue derived from improved grading and packaging are still approximately 15%, despite substantial increases in local supply. Field technicians and senior management of the Fruit Marketing Program have engaged in the implementation of an aggressive training plan, preparing citrus and apple producers for the upcoming harvest.
- ALP/E is starting its fall 2006 vegetable programs; vegetables together with fruit and nuts are competitive sub-sectors that can serve as engines of growth for the regional economy.
- The Commercial Livestock Production Program supports emerging commercial operations working with beef and dairy. As part of the capacity building component, the first 12-day training course was held with sessions in identification and treatment of common diseases, nutrition and other management topics. ALP/E successfully registered the Eastern Region Commercial Livestock Producers Association, a building block for the development of the regional livestock industry.
- The Small Livestock Development Program that works mainly with women farmers and complement ALP/E's other activities in support of the development of the livestock sub-sector continues to be one of ALP/E's most popular programs. The program led by a team of women paravets has trained over 800 rural women in the last 4 months.
- ALP/E concluded beneficiary selection in Nangarhar for the 2006 Fall Wheat Seed and Fertilizer Distribution. Voucher distribution is occurring among selected beneficiaries in Nangarhar, coordinating with government officials from the Ministry of Agriculture, Provincial and District Governors, District Shuras and representatives of the rural communities.
- Proposals for the Kama Road rehabilitation project of Kama District, Nangarhar were received and assessed. A final decision on an implementing partner will be completed in the next reporting period.
- Rehabilitation work on Mashina Road in Qarghai District by HADF is progressing satisfactorily including an acceptable level of material supplies used in the project. The overall progress has been estimated at 10% completion during the reporting period, with an expected completion date of November 15, 2006.
- The first engineer's training course for cobblestone roads was held at the CTTC, with 11 supervisory engineers from IRD Kabul, and seven site engineers from ALP/E who will be working on cobblestone roads. Courses for skilled cobblestone road workers continued and a total of 204 skilled workers have been trained to date. Another group of six local engineers from cash-for-work (CFW) projects are attending two weeks of training to improve their technical skills.
- Work continued on the concrete structures at the Jalalabad Wholesale Market. Columns were completed for the second half of the market and on the concrete roof. Efforts also continued on the cobblestone road behind the market, and the new toilet block. Work is behind schedule due to the extra work which had to be carried out on foundations, and also a shortage of skilled carpenters in the city willing to work on a daily wage. The CTO of USAID made a visit to the market to see progress on September 20, and a six day work week has been initiated to increase efforts.
- **Nangarhar Province:** Nineteen CFW projects underway with a cumulative total of 472,522 employment days generated.
- **Laghman Province:** Fifteen CFW projects underway with a cumulative total of 465,253 employment days generated.
- **Kunar Province:** Seven CFW projects in Kunar underway with a cumulative total of 132,047 employment days generated.
- **Nuristan Province:** Work has started on the first cobblestone road to be built in Nuristan Province.
- The PSD Unit finalized two business plans that were requested by CNFA for two food processing factories. The business plans were sent to CNFA along with photos of the specific locations of each project. The two projects- a dehydration factory and a food factory- were approved by CNFA last week for funding and the contracts will be signed in October 2006.
- The PSD Unit performed an assessment of local dried fruit and nuts and found an interested buyer in the United States. Two suppliers were requested to provide one container of dried fruit and nuts including packaging.
- The Micro-Enterprise Program scheduled the first radio program to air Saturday, October 1, 2006. Self Help Groups (SHGs) will be informed about the weekly radio schedule and members will be encouraged to listen and discuss topics of interest during their weekly meetings. The main objectives of the radio program are to introduce the GME program, motivate women to achieve economic access and inform women about existing business support programs.
- Led by three female paravets, 717 women from Laghman and Nangarhar have been trained in the areas of livestock nutrition and management, identification and treatment of common diseases, and practices to improve productivity.

## SECTOR ACTIVITIES

A description of the activities and achievements of the Economic Development and Infrastructure programs:

### I. AGRIBUSINESS

#### I.1 Fruit Marketing Program

The Fruit Marketing Program is one key elements of ALP/E's short-term strategy for the development of perennial horticulture in Eastern Afghanistan. This program is currently supporting over 4,000 farmers organized into 98 community-level fruit production and marketing groups by providing training and technical assistance in fruit and nut production, post-harvest handling, including grading and packaging, and facilitating market linkages.

This program helps smallholder farmers to rehabilitate the existing fruit and nut orchards, and allows them to experience—first hand—the benefits of improved grading and packaging, as well as collective marketing. The latter enables smallholder farmers to reduce transaction costs, gain bargaining power and reach economies of scale in marketing. From a program standpoint these groups constitute an ideal vehicle for the dissemination of improved technologies and other program services.



**ALP/E Fruit Marketing Specialist shows Mulberry Dealers new packaging**

ALP/E provides hands-on training to group leaders, who are in turn delivering training to their fellow fruit producers, with the assistance of a very aggressive team of 15 field technicians. This team consists of young agronomists, each one assigned to a district; they reside with the communities they serve and mobilize using the same means available to their clientele, thereby creating the conditions for an indigenous and cost-effective extension system.

During the reporting period, the Fruit Marketing Program—launched in June 2006—has facilitated fruit sales for over 80MT and derived increased revenue from improved grading and packaging at approximately 15%, despite substantial increases in local supply, which have seriously affected non-beneficiaries. Field technicians and senior management of the Fruit Marketing Program have engaged in the implementation of an aggressive training plan, preparing citrus and apple producers for the upcoming harvest. ALP/E will provide short-term technical advice during the October-November period.



**Graded and well packaged pomegranates in the field**



Smallholder farmer's graded produce being delivered to the collection center

### 1.2 Eastern Region Annual Crops Initiative

ALP/E's activities include three complementary programs in support of vegetable production and marketing; a) the Vegetable Production and Marketing Support Program serving subsistence farmers by enabling them to increase productivity and quality as mechanisms to produce marketable surpluses; b) the Regional Vegetable Marketing Program (REVAMP) targeting surplus farmers, supporting them to increase productivity, quality and facilitating the establishment of collective marketing mechanisms to increase market efficiency and establish strong market linkages, and c) the Commercial Vegetable Demonstration Farms Program, assisting commercial farmers in the production of high-value vegetables for export. This program is also building the capacity of farmer associations, in collaboration with Nangarhar University and the Departments of Agriculture, to support 22,000 surplus and commercial horticulture farmers.

ALP/E's plans for the fall of 2006 were affected by the procurement of seeds and fertilizers, resulting in delays and a reduction in area planted to high-value crops under the Commercial Vegetable Demonstration Farms Program for the current season.

Despite these constraints, ALP/E will launch its plug seedling nurseries program, consisting of three to five women-operated enterprises that will produce some 150,000 vegetable seedlings. Similarly, ALP/E will launch its Commercial Demonstration Farms Program, which will result in the production of commercial quantities of high-value crops to supply the high-end markets in Kabul and Western Pakistan, with trial shipments to Dubai programmed for mid January. ALP/E will bring a short-term technical advisor for the period October-December. This specialist will train ALP/E and Ministry of Agriculture staff, as well as male and female entrepreneurs in intensive vegetable production practices.



Some of the high-value fruit and vegetables in the Eastern Region Annual Crops Initiative


### **I.3 Smallholder Livestock Development Program**

Administering anti-diarrhoeal suppositories and parenteral medications and monitoring estrus in livestock were just some of the challenging activities previously reserved for men. ALP/E recognizes the role that women play as primary care-takers of household livestock, providing the ideal channel to disseminate improved husbandry practices.

ALP/E's Smallholder Livestock Development Program launched in June 2006, provides rural women with basic training in management, nutrition, as well as identification and treatment of common livestock diseases. In just over three months the program- facilitated by three female paravets hired and trained by ALP/E- has trained over 800 women from 25 villages in Laghman and Nangarhar provinces. The program works in coordination with self-help groups (SHGs) organized through ALP/E's Gender and Micro-Enterprise Unit; whose members take a four-day practical course in animal husbandry.

These training courses, which do not include direct economic rewards for participants, have become extremely popular- to the extent that women paravets often have to conduct three to four training sessions in a single village, as a way to accommodate dozens of women interested in enhancing their knowledge.

The main objective of this program is to enable rural households to increase productivity in the form of milk production and feed-to-meat conversion, and reducing livestock mortality and morbidity. Women beneficiaries have shown particular interest in learning about animal diseases communicable to humans, especially important considering the high prevalence of foot and mouth disease, Brucellosis and Toxoplasmosis in the region.

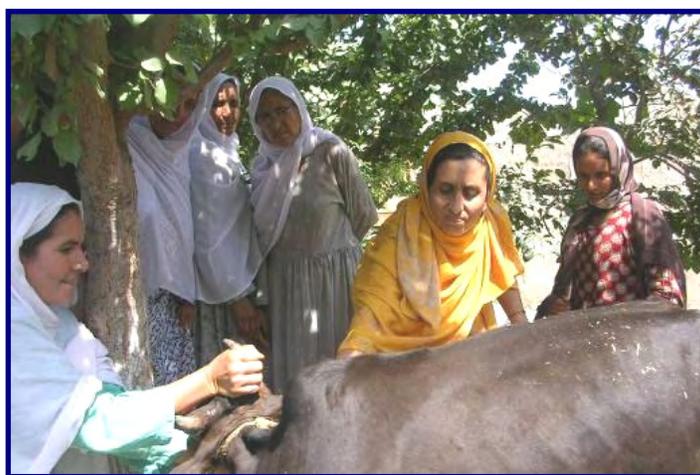

**Practical training of small-scale livestock producers, implemented by ALP/E's team of women paravets**

*"I am amazed by the reception that this program has had in the rural communities, women are eager to learn about trades that were part of the domain of men. We are slowly making a difference!"*

*Najeeba Ishaq Zai  
ALP/E women paravet*

### **I.4 Commercial Livestock Production Program**

The Commercial Livestock Production Program supports the efforts of emerging commercial operations, especially those working with beef and dairy cattle. This is a coordinated effort between ALP/E's Agribusiness and Institutional Capacity Building teams which support this group of business leaders through assistance for the establishment of trade associations, while building their capacity in aspects related to modern production practices, and marketing.



**Practical training of commercial livestock farmers**

The training incorporates professors from Nangarhar University and staff from the Livestock Directorate of the Provincial Department of Agriculture. The program carried out its first 12-day training course with sessions in identification and treatment of common diseases, nutrition and management aspects.

ALP/E, in collaboration with commercial farmers have recently established 11 demonstration farms that will constitute centers for the dissemination of improved practices, including recordkeeping, improved livestock management and nutrition.

Field days to these demonstration farms will begin in early October, with the participation of small livestock farmers, professors from Nangarhar University and students from the Agriculture High School.

This program complements ALP/E's activities in support of smallholder livestock producers, mainly geared towards building the capacity of rural women, with over 800 graduates in 4 months. Future activities include the establishment of 200 female-owned semi-commercial broiler operations, which will be launched at the end of the winter.

### **1.5 Fall Wheat Seed and Fertilizer Distribution Program**

This is a high profile program to increase self-food reliance, while providing an alternative to poppy production during the winter, providing 80,000 farmers in Kunar, Laghman, Nangarhar and Nuristan with certified seed and fertilizer to plant one Jerib of high-yielding wheat varieties.

During the reporting period ALP/E concluded the selection of beneficiaries in Nangarhar Province. Currently, voucher distribution amongst selected beneficiaries is being conducted in Nangarhar. The program is being implemented in close coordination with the Government officials from the Ministry of Agriculture, Provincial and District Governors, District Shuras and representatives of the rural communities.

The distribution of inputs is expected to begin in October, giving priority to communities located in high elevations.



**Manual marking of fertilizer bags with an anti-poppy message**

## Agribusiness Activities:

Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
			Design	Execution				
Eastern Region Orchards Development Program (ERODP)	8 districts/2 districts	Nangarhar/Laghman	100%	30%	IF Hope	5-Jul-05	July-08	Ongoing
Radio Program-Farmers Interviews	All districts	Nangarhar/Laghman /Kunar	100%	50%	ALP/E	12-Feb-06	June-07	Ongoing
Smallholder Livestock Management Program	Village based Self Help Groups	Nangarhar/Laghman /Kunar	100%	12%	ALP/E	1-May-05	May-07	Ongoing
Training for Commercial Nursery Owners	Behsud, Asadabad, Mehtarlam	Nangarhar/Laghman	100%	20%	ALP/E	1-May-06	Dec-06	Ongoing
Training for Female Nursery Owners	Behsud, Surkh Rod, Qarghayi	Nangarhar/Laghman	100%	30%	ALP/E with RI	1-Apr-06	Dec-06	Ongoing
Forest Incentives for Livelihoods Diversification	TBD	Nangarhar/Laghman /Kunar	80%	5%	ALP/E	1-May-06	Dec-07	Ongoing
Adaptive Research Technology Dissemination and Development of Seed Supply Systems	17 districts of Eastern Region	Nangarhar/Laghman /Kunar	100%	2%	ICARDA	Oct 06	Dec 08	Subcontract signed
Input Supply Support Program	20 districts of Eastern Region	Nangarhar/Laghman /Kunar	100%	97%	ALP/E	Sep 05	Oct 06	On going
Market Information System	Throughout Eastern Region	Nangarhar/Laghman /Kunar	100%	30%	ALP/E&DoA	Mar 06	Dec 08	Ongoing
Fruit Marketing Program	15 districts of Eastern Region	Nangarhar/Laghman /Kunar	100%	20%	ALP/E	May 06	Dec 08	Ongoing
Eastern Region Annual Crops Initiative	Eastern Region	Nangarhar/Laghman /Kunar	100%	0%	ALP/E	Jul 06	Dec 08	Design completed
Eastern Region Livestock Development Initiative	Eastern Region	Nangarhar/Laghman /Kunar	90%	2%	ALP/E	Jun 06	Dec 08	Ongoing
Fall Wheat Program (2006)	Selected villages in all four Provinces	Nangarhar/Laghman /Kunar/Nuristan	100%	10%	ALP/E&DoA	1-Jul	Nov-08	Ongoing

## 2. INFRASTRUCTURE DEVELOPMENT

### 2.1. PRODUCTIVE INFRASTRUCTURE PROJECTS (PIP)

The Infrastructure Unit completed the following activities during the reporting period:

**Kama Main Road:** Proposals for the Kama Road rehabilitation project of Kama District, Nangarhar were received and assessed. A final decision on an implementing partner will be completed in the next reporting period.

**Mashina Road:** Rehabilitation work on Mashina Road in Qarghai District by HADF is progressing satisfactorily including an acceptable level of material supplies used in the project. The overall progress has been estimated at 10% completion during the reporting period, with an expected completion date of November 15, 2006. Progress to date:

- Completed construction of three box culverts and three pipe culverts
- Completed repairs to two existing culverts
- Started construction of retaining walls
- Started stripping and scarification of the existing road surface

**Abuzai Bridge:** The design of Abuzai Bridge was finalized and the technical feasibility report will be completed in October.

**Qasimabad Road:** The technical feasibility report for Qasim Abad road was completed and submitted to the COP for obtaining USAID approval for implementation through competitive bidding.

**Construction Trades Training Center (CTTC) Training:** Another batch of six local engineers from CFW projects will receive two weeks training starting September 20, 2006 and will end beginning in early October. The training will improve their technical skills in their field. Another group of 28 Tradesmen started a 30-day course in trades skills at the CTTC on September 28, 2006.

**Wholesale Vegetable Market:** Work continued on the concrete structure at the Jalalabad Wholesale Market. Columns were completed for the second half of the market and on the concrete roof. Efforts also continued on the cobblestone road behind the market, and the new toilet block. Work is behind schedule due to the extra work which had to be carried out on foundations, and also a shortage of skilled carpenters in the city willing to work on a daily wage. The CTO of USAID made a visit to the market to see progress on September 20, and a six day work week has been initiated to increase efforts.

**Improving access to Markets:** Improvements to existing farm to market roads connecting priority production areas to the district centers are planned. Surveys and designs in progress are as follows:

- a) Alignment and X-sections of Zaisar cobblestone Road in Nazian District is completed.  
Total length of the road is 7+739 km
- b) Alignment and X-sections of Omarzai cobblestone road in Mihtarlam district is completed:  
Total length of the road is 9+500 km
- c) Alignment and cross sections of the Barabad to Mangwal road in Khas Kunar district of Kunar is ongoing.
- d) Design and cost estimate for the Sherzad to Hisarak road Section I (15.2 km) have been prepared.

**Cobblestone Road Training Center.** The first engineer's training course for cobblestone roads was held at the CTTC, with 11 supervisory engineers from IRD Kabul, and seven site engineers from ALP/E who will be working on cobblestone roads. Courses continued and a total of 204 skilled workers have been trained to date, while another group of six local engineers from CFW projects are attending two weeks of training to improve technical skills. Training materials including technical specifications, the Cobblestone Road Construction Manual, and sample cost estimates were distributed to all the trainees, and they visited both Shamshapur and Darunta Cobblestone road construction sites to observe the ongoing projects. A sixth group of skilled cobblestone workers was trained for constructing the cobblestone roads, consisting of 20 workers from Pachir wa Agam and 20 from Kot district. To date a total of 204 skilled workers, 10 Site supervisors and 18 Engineers have been trained in cobblestone roads at the CTTC.



The first group of 18 Engineers graduating from the CTTC Cobblestone Road Training Center



**Graduating Skilled Cobblestone Workers with visitors Betsy Marcotte of DAI and Guy Jones of HMM.**

**Nangarhar Road Inventory:** During the reporting period, the NRIT completed GPS surveys of the following districts:

#	District surveyed	Length
1	Deh Bala	63 km
2	Pachir wa Agam	51 km
3	Chaparhar	159 km
<b>Total length</b>		<b>273 km</b>

To date the NRIT Team has completed inventories for 1,664 km of roads in 19 Districts of Nangarhar Province.

The number of projects currently being designed and implemented under PIP and the status is below:

Province	Technical Feasibility Completed	Engineering Survey and Design Completed	Projects Under Tender Process	Contracts Awarded
Nangarhar	2	7	1	0
Laghman	1	2	0	1
Kunar	0	0	0	0
<b>Total</b>	<b>3</b>	<b>9</b>	<b>1</b>	<b>1</b>

### PRODUCTIVE INFRASTRUCTURE PROJECTS (PIP)

Project Name	District	Province	% Design Completed	% Implementation Completed	Implementer	Activity Start Date	Activity Completion Date	Comments
Darunta by-pass Road	Qarghai	Laghman	100%	ongoing	DAI	February 2006	December 2006	Work being carried out under CFW
Mashina Road Improvement – 7.5 km	Qarghai	Laghman	100%	10%	Contract	2-Sep-06	15-Nov-06	Work started on 2 <sup>nd</sup> Sep.
Abuzai Bridge	Mehtarlam	Laghman	100 %	0%	Contract	Nov-06	June-07	Awaiting finalization of Technical Feasibility Report
Shamshapur Road – 11.5 km	Surkhrud	Nangarhar	100%	ongoing	DAI	Feb.06	Feb.07	Work being carried out under CFW
Wazir Tatang Causeway	Surkhrud	Nangarhar	100%	0%	Contract	TBD	TBD	Pending
Wholesale Market	Jalalabad City	Danaher	100%	ongoing	DAI	Jun-06	Oct-06	Work being carried out under CFW

## PRODUCTIVE INFRASTRUCTURE PROJECTS (PIP)

Project Name	District	Province	% Design Completed	% Implementation Completed	Implementer	Activity Start Date	Activity Completion Date	Comments
Kama DBST Road - 14.6 km	Kama	Nangarhar	100%	RFP received	Contract	Nov-06	May-07	22 bids received
Qasim Abad Road – 5.7 km	Behsud	Nangarhar	100%	0%	Contract	Dec-06	May-07	Awaiting USAID approval for implementation
Rodat Road - 12.3 km	Rodat	Nangarhar	100%	0%	Contract	TBD	TBD	Design and BOQ completed.
Sherzad to Hesarak Road - 28 km	Sherzad & Hesarak	Nangarhar	60%	0%	Contract	Dec-06	Mar-07	Survey completed and design ongoing.
Lal Pur to Goshta Road- 15km	Lal Pur	Nangarhar	30%	0%	Contract	Dec-06	May-07	Engineering survey completed.
Chardy-Ghaziabad road 12.6 km	Kot	Nangarhar	10%	0%	DAI	TBD	TBD	Engineering survey has been completed. To be implemented under CFW
Dudarak Road,6.2km	Dari-Nur	Nangarhar	10%	0%	Contract	Jan-07	Apr-07	Engineering survey has been completed.
Barabad to Mangwal road 24 km	Khas Kunar	Kunar	3%	0%	Contract	TBD	TBD	Started engineering surveys.

### 2.2. CASH-FOR-WORK PROJECTS (CFW)

Five CFW projects were completed while work on four new projects started during the reporting period, making a total of 42 ongoing projects in Laghman, Nangarhar and Kunar provinces. Approval was received from USAID for the first 5 cobblestone roads under AWP-2. **Work was started on the first cobblestone road in Nuristan province.**

The daily employment rate was 4,388 workers per day, while 19,698 individual workers have been employed from June 2005 through September 30, 2006. Total employment days during the period were recorded as 49,958 and the cumulative total reached 1,069,862 employment days from June 2005 through September 30, 2006.

Status of each Province is below:

- **Nangarhar Province:** Nineteen CFW projects underway with a cumulative total of 472,522 employment days generated.
- **Laghman Province:** Fifteen CFW projects underway with a cumulative total of 465,253 employment days generated.
- **Kunar Province:** Seven CFW projects in Kunar underway with a cumulative total of 132,047 employment days generated.
- **Nuristan Province:** Work has started on the first cobblestone road to be built in Nuristan Province.

#### SUMMARY OF CFW PROJECTS BY PROVINCE

SN	Province	Active	Completed	Other approved
1	Nangarhar	19	30	8
2	Laghman	15	20	2
3	Kunar	7	6	3
4	Nuristan	1	0	0
Total		<b>42</b>	<b>56</b>	<b>13</b>

### i. Nuristan Province

Work started this period on CFW-300801, the Dakor to Mashfa cobblestone road in Nogram District, the first ALP/E CFW project in Nuristan Province. A joint Infrastructure and Procurement Team visited the site on September 27, and signed contracts for renting a site office and supplying local vehicles. Daily labor was arranged with the shura, a local engineer was appointed (already trained at CTTC), and collection of cobblestones started on September 28, with 20 laborers. Tools, machinery and materials were ordered from the Procurement Team in Jalalabad.

**ii. Laghman Province:** Under the supervision of ALP/E, Relief International (RI) continued to work on 15 CFW projects during the reporting period in Laghman. One new project CFW-090214 was started by RI during this reporting period. Work also continued on the Darunta By-pass Cobblestone road project in Qarghai district under the direct supervision of ALP/E. The daily worker rate in Laghman reached an increased 1,861 workers per day, with a cumulative total of 9,098 individual workers employed from June 2005 through September 30, 2006. Employment days during the reporting period were 21,264 and the cumulative total reached 454,142 through September 30, 2006.

## CFW PROJECTS: LAGHMAN

Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Daronta Bypass Cobblestone Road, Second Reach	CFW-090209	Qarghai	Laghman	100%	86%	DAI	13-May-06	31-Oct-06	Ongoing
Deh-Ziarat Protection wall	CFW-090101	Mihtarlam	Laghman	100%	100%	RI	28-Sep-05 22-July-06	15-Mar-06 10-Sep-06	Completed this period including backfilling.
Tergari Protection wall	CFW-090103	Mihtarlam	Laghman	100%	100%	RI	20-Oct-05 23-July-06	30-Mar-06 14-Sep-06	Completed this period including backfilling.
Pacha Joie Canal	CFW-090107	Mihtarlam	Laghman	100%	50%	RI	26-Aug-06	30-Nov-06	Ongoing
Abizai Flood Protection	CFW-090108	Mihtarlam	Laghman	100%	15%	RI	12-Sep-06	20-Dec-06	Ongoing. Work held up due to flood on 19 Sept.
Gundy Baba Sahib Flood Protection	CFW-090112	Mihtarlam	Laghman	100%	20%	RI	10-Sep-06	20-Dec-06	Ongoing. Work delayed by flood on 19 Sept.
Qala Shagee Flood Protection	CFW-090118	Mihtarlam	Laghman	100%	20%	RI	10-Sep-06	20-Dec-06	Ongoing. Work delayed by flood on 19 Sept.
Baba Sahib Canal	CFW-090120	Mihtarlam	Laghman	100%	35%	RI	30-Aug-06	25-Nov-06	Ongoing
Dehziarat-Omerzai cobblestone road	CFW-090121	Mihtarlam	Laghman	100%	0%	DAI	TBD	TBD	Project approved on 19 Sept 06
Dopai and Langalam Protection wall	CFW-090201	Qarghai	Laghman	100%	100%	RI	24-Nov-05 01-Aug-06	30-Mar-06 05-Oct-06	Backfilling, 55% complete. Community dispute resolved, backfilling restarted.
Kakas Canal Rehabilitation	CFW-090207	Qarghai	Laghman	100%	0%	RI	TBD	TBD	Pending due to community problem, still not resolved.
Kanda Canal Rehabilitation	CFW-090208	Qarghai	Laghman	100%	100%	RI	26-Apr-06	14-Sep-06	Completed this period.
Kac Aziz Khan Canal	CFW-090210	Qarghai	Laghman	100%	30%	RI	5-Sep-06	10-Jan-07	Ongoing
Qardy Kac Canal	CFW-090214	Qarghai	Laghman	100%	10%	RI	25-Sep-06	30-Dec-06	Community labor supply problem resolved, work restarted
Bara Kandy and Kuza Kandy Canal Rehabilitation	CFW-090304	Alingar	Laghman	100%	85%	RI	27-May-06	30-Oct-06	Work restarted on 16 Aug with lower river level.
Purwaie Flood Protection	CFW-090305	Alingar	Laghman	100%	10%	RI	10-Sep-06	20-Nov-06	Ongoing

## CFW PROJECTS: LAGHMAN

% Complete									
Project Name	Project Code	District	Province	Design	Execution	Firm	Activity Start Date	Activity Completion Date	Remarks
works									
Mundal Flood Protection works	CFW-090306	Alingar	Laghman	100%	25%	RI	2-Sep-06	10-Nov-06	Ongoing, but community problem is affecting work.
Kandi Sahib Canal	CFW-090705	Alishang	Laghman	100%	75%	RI	14-Aug-06	15-Nov-06	Ongoing
Qardi Salab Canal	CFW-090708	Alishang	Laghman	100%	60%	RI	17-Aug-06	20-Nov-06	Ongoing
Kalay Baya Canal	CFW-090709	Alishang	Laghman	100%	25%	RI	30-Aug-06	30-Nov-06	Ongoing. Work stopped for remedial work on masonry.

**iii. Kunar Province:** Two projects were completed this reporting period, CFW-101501 Daag Canal, and CFW-101504 Khas Kunar Middle Road, both in Khas Kunar district. Work continued on seven active projects in Kunar during the reporting period. To date, 1,972 people have been employed with a cumulative total of 132,047 employment days through September 30, 2006.

## CFW PROJECTS: KUNAR

% Complete									
Project Name	Project Code	District	Province	Design	Execution	Firm	Activity Start Date	Activity Completion Date	Remarks
Dandono Kotgi Canal Intake	CFW-101201	Narang	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
Bar Narang Road Improvement	CFW-101203	Narang	Kunar	100%	100%	DAI	16-Apr-06	15-Aug-06	Completed
Sharalo-Badil Road Improvement	CFW-101204	Narang	Kunar	100%	100%	DAI	16-Apr-06	15-Aug-06	Completed
Badil Khovar Flood Protection	CFW-101205	Narang	Kunar	100%	74%	DAI	11-Jul-06	11-Oct-06	Ongoing
Seend Wala Chawkay Intake	CFW-101301	Chawkay	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
Dewagal Road Improvement	CFW-101303	Chawkay	Kunar	100%	85%	DAI	16-Apr-06	15-Oct-06	Ongoing
Zarmandai Flood Protection	CFW-101304	Chawkay	Kunar	100%	80%	DAI	27-Jun-06	10-Oct-06	Ongoing
Chawkay Khower Flood Protection	CFW-101306	Chawkay	Kunar	100%	75%	DAI	10-Jul-06	10-Oct-06	Ongoing
Noorgal Seend Wala Intake	CFW-101401	Noorgal	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
Seend Wala Canal Rehabilitation	CFW-101402	Noorgal	Kunar	100%	100%	DAI	20-Feb-06	15-Aug-06	Completed, including additional work
Nurgal-Aret Road	CFW-101403	Noorgal	Kunar	100%	62%	DAI	18-Jun-06	25-Oct-06	Ongoing
Tora Tega Road	CFW-101404	Noorgal	Kunar	100%	50%	DAI	11-Jul-06	11-Oct-06	Ongoing
Daag Canal Repair	CFW-101501	Khas Kunar	Kunar	100%	100%	DAI	21-Feb-06	18-Sep-06	Additional works completed.
Tanar Road Rehabilitation	CFW-101502	Khas Kunar	Kunar	100%	100%	DAI	21-Feb-06	12-Jun-06	Completed
Khas Kunar Clinic to Hakimabad Road	CFW-101503	Khas Kunar	Kunar	100%	28%	DAI	28-Aug-06	28-Nov-06	Ongoing

Khas Kunar Middle Road	CFW-101504	Khas Kunar	Kunar	100%	100%	DAI	14-Jun-06	18-Sep-06	Completed this period.
------------------------	------------	------------	-------	------	------	-----	-----------	-----------	------------------------

**iv. Nangarhar Province:** During the reporting period, work was completed on three projects and continued on 19 active projects, while two new projects started during this reporting period. The daily workers employed in Nangarhar Province during the period were 1,793 workers per day with a cumulative total of 8,608 workers. Total employment days were 19,612 while total employment days reached 472,522 through September 30, 2006.

A ground-breaking ceremony was held for the Hojoom Kal Chelgazi Canal intakes project in Spinghar district, which started this period. The ceremony was attended by the Spinghar Sub-Governor and a large number of community elders.



A completion ceremony was held on 18<sup>th</sup> September for CFW-082202, the Binigah emergency flood protection project on the bank of the Kunar river downstream of Kama bridge, in Behsud district. The acting Director of RRD in Nangarhar Province attended, and district and community leaders made speeches, all thanking ALP/E for the excellent work done on the project. At the same ceremony the start of work was officially opened for the next phase of the Binigah flood protection work, CFW-082206.




**Commemorative plaque at completed Binigah Emergency Flood Protection**

A similar completion ceremony was held on 20<sup>th</sup> September for CFW-081601, CFW-081602 and CFW-081603, the Koz and Bar Bela flood protection works in Goshta District. These three projects were originally started by AINP in December 2005, and were completed by ALP/E in September 2006. The community leaders congratulated the site staff on their efforts, and the positive tangible results of the project. The project was inaugurated by the District Head and Security Chief from Goshta.

Work continued on the concrete structure at the Jalalabad Wholesale Market. Columns have been completed for the second quarter portion of the market. Work is also in progress on the cobblestone road at the back of the market, the drainage improvements and the toilet block. Work is behind schedule due to the extra work which had to be carried out on foundations, and also a shortage of skilled carpenters in the city willing to work on a daily wage. The CTO of USAID made a visit to the market to see progress on 20 September.



**The existing old part of the market, with sagging roof and unsanitary conditions.**

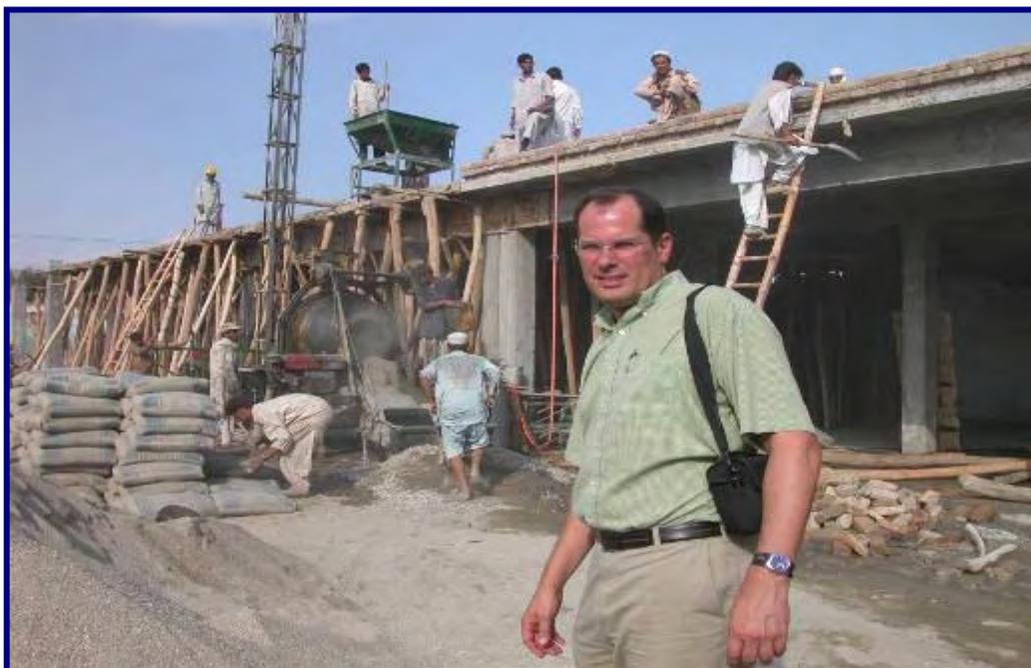


**CTO Brian Bacon inspecting work at the Wholesale Market**

## CFW PROJECTS: NANGARHAR


Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Jalalabad City Main Drain	CFW-080101	Jalalabad	Nangarhar	100%	100%	DAI	2005	29-Mar-06	Completed, Project closed.
Wholesale Market Rehabilitation	CFW-080103	Jalalabad	Nangarhar	100%	50%	DAI	5-Jun-06	5-Oct-06	Ongoing
Kakrak Road Improvement	CFW-080202	Surkhrud	Nangarhar	100%	90%	DAI	29-May-06	15-Oct-06	Ongoing
Tatang Nawab Jabar Canal Rehabilitation	CFW-080203	Surkhrud	Nangarhar	100%	100%	DAI	6-Jun-06	20-Sep-06	Completed this period.
Sarband and Jalawanano Canal Intakes Construction	CFW-080204	Surkhrud	Nangarhar	100%	100%	DAI	6-Jun-06	7-Sep-06	Completed this period.
Shamshapoor-Daronta Road Improvement	CFW-080205	Surkhrud	Nangarhar	100%	88%	DAI	8-May-06	31-Oct-06	Ongoing
Shamshapur Cobble Stone Road second reach	CFW-080206	Surkhrud	Nangarhar	100%	85%	DAI	14-May-06	20-Oct-06	Ongoing
Ghauchak cobblestone road	CFW-080207	Surkhrud	Nangarhar	100%	0%	DAI	TBD	TBD	Project approved on 19 Sept 06
Sanzai Road	CFW-080305	Hisarak	Nangarhar	100%	95%	DAI	2-Jul-06	10-Oct-06	Ongoing
Petlaw Road Rehabilitation	CFW-080405	Sherzad	Nangarhar	100%	100%	DAI	8-Jun-06	28-Sep-06	Completed this period.
Nemla Irrigation	CFW-080504	Khogyani	Nangarhar	100%	6%	DAI	17-Sep-06	30-Dec-06	Ongoing.
Nemla Flood Protection	CFW-080507	Khogyani	Nangarhar	100%	86%	DAI	28-Jun-06	30-Oct-06	Ongoing
Dawlat Zai Canal Intake	CFW-080601	Chaparhar	Nangarhar	100%	118%	DAI	6-May-06	5-Oct-06	Ongoing for additional work
Garatak Flood Protection Wall	CFW-080603	Chaparhar	Nangarhar	100%	96%	DAI	30-May-06	10-Oct-06	Ongoing
Chardahi Flood Protection Wall	CFW-080604	Chaparhar	Nangarhar	100%	90%	DAI	30-May-06	10-Oct-06	Ongoing
Sholana Flood Protection Wall	CFW-080605	Chaparhar	Nangarhar	100%	98%	DAI	30-May-06	5-Oct-06	Ongoing
Lawangapoor cobblestone road	CFW-080606	Chaparhar	Nangarhar	100%	0%	DAI	TBD	TBD	Project approved on 19 Sept 06
Deh Sarak Canal Intake	CFW-081001	Achin	Nangarhar	100%	10%	DAI	9-Sep-06	17-Nov-06	Ongoing
Terkhy Intake and Flood Protection	CFW-081101	Nazyan	Nangarhar	100%	66%	DAI	5-Jul-06	30-Oct-06	Ongoing. Flood again disrupted works on 19 September.
Zysar cobblestone road	CFW-081102	Nazyan	Nangarhar	100%	0%	DAI	TBD	TBD	Project approved on 19 Sept 06
Torlala Kaly Irrigation Reservoir & Flood Protection	CFW-081203	Dur Baba	Nangarhar	100%	80%	DAI	27-Jun-06	30-Oct-06	Ongoing. Work affected by flood on 19 September.
Zakhil Irrigation Canal	CFW-081301	Shinwar	Nangarhar	100%	95%	DAI	25-Jun-06	15-Oct-06	Ongoing
Zara Sultankhil Protection Wall	CFW-081402	Momandara	Nangarhar	100%	100%	DAI	21-Mar-06 15-July-06	28-May-06 22-Sep-06	Additional work completed.
Basawal Banbaba Flood Protection	CFW-081404	Momandara	Nangarhar	100%	8%	DAI	4-Aug-06	30-Nov-06	Ongoing. Flood again disrupted works on 19 September.
Koz & Bar Bela F. Protection Wall I	CFW-081601	Goshta	Nangarhar	100%	122%	DAI	11-Dec-05	7-Sep-06	Completed including additional work.
Spin Jumat Embankment	CFW-082204	Behsud	Nangarhar	100%	99%	DAI	25-Apr-06	15-Oct-06	Ongoing
Binigah II Flood Protection	CFW-082206	Behsud	Nangarhar	100%	0%	DAI	TBD	TBD	Materials ordered, work will start next week.
Inzari Khola Intakes	CFW-082302	Spinghar	Nangarhar	100%	0%	DAI	TBD	TBD	Project approved 30 August.

## CFW PROJECTS: NANGARHAR

Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Hojoom, Kal Chelgazi Intakes	CFW-082303	Spinghar	Nangarhar	100%	3%	DAI	25-Sep-06	31-Dec-06	Work started
Lokhi Canal Intake	CFW-082304	Spinghar	Nangarhar	100%	0%	DAI	TBD	TBD	Project approved 30 August.
Girdi Nawagai Road	CFW-082305	Spinghar	Nangarhar	100%	58%	DAI	13-Jun-06	30-Oct-06	Ongoing
Shangina Yousaf Kas Canal Rehabilitation	CFW-082401	Tor Ghar	Nangarhar	100%	0%	DAI	TBD	TBD	Suspended due to security problem.
Gachawy Mirano Road Improvement	CFW-082402	Tor Ghar	Nangarhar	100%	2%	DAI	19-Jul-06	TBD	Suspended due to security problem.

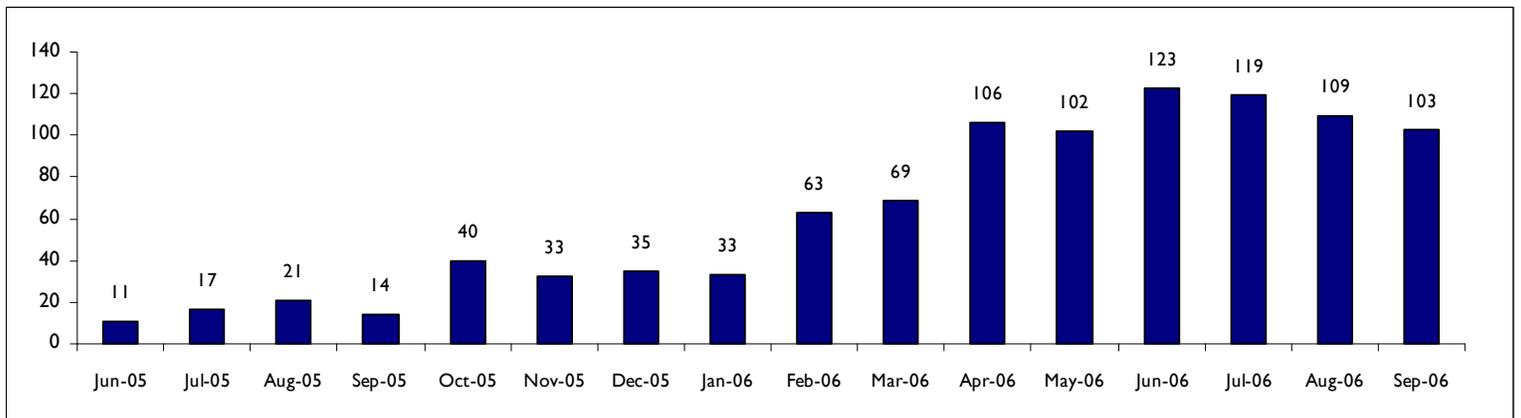

**Monthly Employment Days (in 1,000s) in CFW Projects**

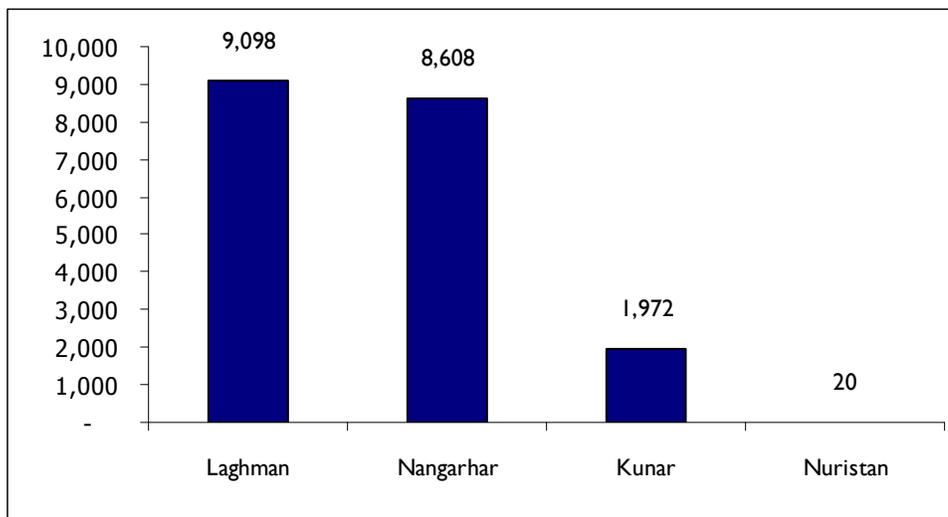

**Persons Hired on CFW projects since June 2005**

### 3. PRIVATE SECTOR DEVELOPMENT

The Private Sector Development Unit completed the following activities during the reporting period:

- Finalized two business plans which were requested by CNFA for food processing factories. The business plans were sent to CNFA along with photos of the specific locations. These two projects were approved by CNFA last week for funding and the contracts will be signed in October 2006 between CNFA and the grantees. The two approved projects are shown below:

#### Businesses supported by CNFA with the collaboration of ALP/E in this reporting period

Company Name	New or Existing	Product	New Labor		Contribution at the start-up Period of the business		Total	Status
			Male	Female	Owner Contribution	Proposed CNF A Contribution		
			Hamisha Bahar Vegetable and Fruit Dehydration Factory	New	Dried vegetables and fruit	5		
Azizi Food Factory	Existing	Fried pulse, roasted peanuts, (snack)	15	8	\$34,100	\$13,000	\$47,100	The application has been submitted to CNFA and was approved last week. The contract between the CNFA and the grantee will be signed in the near future.

- Performed a quick assessment of dried fruit and nuts and provided a pricing list for a US buyer. Two suppliers were identified to provide a container of dried fruit and nuts as requested by the buyer, they are preparing the samples including packaging.
- Facilitated efforts, in collaboration with the ALP/E Institutional Development Team, to finalize the creation of the Nangarhar Carpet Association. Additional efforts focused on developing the business plan with the newly formed association for carpet cutting and washing. Currently the team is researching quotations for the machinery of the proposed project.
- Coordinated with the UK venture capital firm ACAP re 1) Sabawoon Flour Mill and 2) Ahmadzai Rickshaw Company. The two investors were sent to Kabul to attend an initial interview with the ACAP Kabul office, and ACAP reported the information was sent to the UK for final review. In addition, ACAP interviewed another investor who wants to invest in marble processing.
- The PSD Unit is coordinating the Business Skills Training Programs (TARAQI). Last week the team worked with the STTA consultant on preparation activities including: implementation models, curriculum, workshop, and trainings.
- Signed a memorandum of understanding (MoU) with the University of Nangarhar's chancellor. The MoU commits ALP/E and the University to: 1) share mutual expertise to support the development of the University, as well as ALP/E's programs; 2) provide paid internships to university students selected and endorsed by the Office of the Chancellor based on academic merit; 3) assist the University in the development of a Business Administration course available to students in all fields; 4) arrange study tours for students of Nangarhar University to enhance their practical knowledge; 5) implement TARAQI –SABA, a youth entrepreneurship capacity building program to be administered by the University, in collaboration with male and female high schools in Jalalabad; 6) support the veterinary research team in the development of the regional livestock industry.

PRIVATE SECTOR DEVELOPMENT PROJECTS					
Project Name	Location	Province	Activity Start Date	Activity Completion Date	Comments
Business Development Center	Jalalabad	Nangarhar	04-Apr-06	07-Feb-09	Ongoing
MIS (Market Information System)	Nangarhar	Nangarhar	01-May-06	In planning	Managed in time by the BDC.
Establishing Women Handicraft Center	Nangarhar	Nangarhar	TBD	TBD	Fielding an STTA to do a study of designs for the handicraft industry in ER.
Policy Reform	Nangarhar	Nangarhar	05-Nov-06	In planning	Further research and implementation of policy reform activities.

PRIVATE SECTOR DEVELOPMENT PROJECTS					
Training and Internship Program with Nangarhar University	Jalalabad	Nangarhar	ongoing	Ongoing	Formal agreement expected by end of September 2006
Regional Representative for CNFA (operating under an MOU)	Nangarhar	Nangarhar	01-Aug-05	On going	CNFA is implementing the AADP program and ALP/E represents CNFA..
Support the capacity building of Nangarhar Industrial Assn (NIA).	Nangarhar	Nangarhar	05-Apr-05	On going	Working on supporting their sub-groups and investment promotion activities
Support to Afghanistan Investment Support Agency (AISA).	Nangarhar	Nangarhar	01-Jan-06	On going	Supporting the establishment of a office at the BDC, and on ER focused investment promotion
Support to Afghanistan Women's Business Association (AWBA).	Nangarhar	Nangarhar	01-Jan-06	On going	Approval for supporting a Jalalabad office
Support to Afghanistan Finance Company (AFC).	Nangarhar	Nangarhar	01-Jan-06	On going	Support with establishment of office at the BDC, and with referrals for leasing/funding
Support and Collaboration with Afghan International Chamber of Commerce (AICC).	Nangarhar	Nangarhar	18-Jul-05	In planning	Seeking ways for greater collaboration between AICC and BDC (ALP/E)
Internet Cafes with Afghan Telecoms/PRT	Nangarhar	Nangarhar	01-Feb-06	In planning	Still determining the role for the private sector in the District Comm. Network.
Hygiene Program for food processors	Nangarhar	Nangarhar	01-Apr-06	In planning	1) assessment, 2) awareness, 3) training to targeted sub sectors

### Business Development Center Activities

- A local industrialist requested assistance from the BDC in establishing a cola and juice production plant in Kunar. The businessman had problems importing raw materials (chemicals) for cola from Pakistan, and the BDC referred him to AISA who promised to lobby the Ministry of Finance to resolve the issue.
- The BDC identified an olive oil buyer in Karachi Pakistan. The buyer is interested in buying the 80 MT of stored oil in the local oil factory, but he insists that NVDA should facilitate transporting the oil to Peshawar. The BDC spoke with the head of NVDA who agreed to send the oil, and quotations were solicited by the BDC for drums to transport the oil.
- The Afghanistan Finance Company (AFC) with offices at the BDC finalized negotiations for leasing equipment to five local companies in the eastern region. Ideally, the equipment will arrive in October after AFC reopens its Kabul office, which was closed for one month due to security problems.
- A local woman investor interested in establishing a thread making factory in the eastern region visited the BDC to develop a business plan for her proposed business. The BDC will complete the plan in October.
- The BDC committed to collaborate in future endeavors with the National Traders Association of Nangarhar Province.
- The BDC held a Basic Internet Training on September 19, and will continue the training through October 2 for 12 attendees. In addition, local businesses requested marketing training. The materials have been finalized and translated to Pashto and the training will take place in October. The BDC held an internal meeting with partners to discuss the future vision of the BDC and expanding services. The BDC will hold a strategic planning workshop on October 7 facilitated by ALP/E's STTA.
- The Provincial Coordinator of GTZ-PAL for Laghman Province visited the BDC and requested assistance coordinating with the carpet weaving project. GTZ wants to train carpet weavers in Laghman. The BDC Director invited the Head of the Carpet Association for a joint meeting in early October between PAL, the Nangarhar Carpet Association, ALP/E, and the BDC.



The BDC Director (right) discussing marketing with a representative of Nangarhar TV

Some of the businesses in ALP/E operating area looking for support from CNFA

#	Company Name	New or Existing	Product	New Labor		Owner Contribution	CNFA Contribution	Total	Status
				Male	Female				
1	A haj Said Rahmanullah Cotton seed Factory	Existing	Refining Cotton and Cotton Seed	14		\$16,666	\$15,000	\$31,666	Submitted to CNFA and under study
2	Yousafi Qazi Zada Tomato Paste Factory	New	Tomato Paste	20		\$149,746	\$35,000	\$184,746	The grantee has been interviewed by CNFA and the application is still under study
3	Nawab Mal k Cotton Seeds Oil Production Company	New	Cotton Seed Oil	25		\$50,400	\$30,000	\$80,400	Submitted to CNFA and under study
4	Afghan Juice Production Company	Existing	Lemon and Orange Juice	4		\$12,000	\$5,000	\$17,000	Submitted to CNFA and currently exploring ways of linking to a big juice factory.
5	Ezat Gul Cotton Seed and Cotton Production Company	Existing	Refining Cotton and Cotton Seed	10	0	\$26,000	\$5,000	\$31,000	Submitted to CNFA and currently under revision
6	Nangarhar Women Tomato Paste and Pickle Producing Factory	New	Tomato Paste and Pickle	1	9	\$17,500	\$5,000	\$22,500	Rejected by CNFA because of the pickle and tomato not compatible.
7	Riyaz Carton Making Factory	New	Vegetable and Fruit Cartons	19	2	\$40,000	\$36,450	\$76,450	Submitted to CNFA
8	Shakir Sihami Shirkat	Existing	Soap and Pulp	10	5	\$157,200	\$72,000	\$229,200	Submitted to CNFA and currently under revision.
9	Wahid Oil Production Company	Existing	Pulp, and Cotton Seed	3	0	\$36,000	\$5,000	\$41,000	Submitted to CNFA and currently under revision
0	Mirwais Lalpuri Soap and Oil Factory	Existing	Soap, Pulp, unrefined oil and refine cotton	13	4	\$73,000	\$61,100	\$134,100	Submitted to CNFA
11	Mansoor Helmand Ed ble Oil Factory	Existing	Pulp, Soap and Edible oil	16	4	\$166,200	\$50,000	\$116,200	The grantee has been interviewed and CNFA requested for analysis of the oil.
12	Zar Mohammad Popcorn and poprice factory	Existing	Popcorn and pop rice	6	2	\$11,400	\$5,000	\$16,400	Approved and the contract has been signed between CNFA and the grantee.
13	Hamisha Bahar Vegetable and Fruit Dehydration Factory	New	Dried vegetables and fruit	5	3	\$21,600	\$9,500	\$31,100	The application has been submitted to CNFA. CNFA has approved the project and the contract will be signed between the grantee and CNFA in the near future.
14	Azizi Food Factory	Existing	Fried pulse, roasted peanuts,	15	8	\$34,100	\$13,000	\$47,100	The application has been submitted to CNFA. CNFA has approved the project and the contract will be signed between the grantee and CNFA in the near future.

Note: The figures above indicate only capital expenditures and do not include operating expenses, which will be paid by the owner.

#### 4. GENDER AND MICRO-ENTERPRISE DEVELOPMENT

The Gender and Micro-Enterprise (GME) Unit completed the following activities during the reporting period:

- **The Micro-Enterprise Program:** The weekly gender radio program was scheduled and the first program will air Saturday, October 1, 2006. Self Help Groups (SHGs) will be informed about the weekly radio schedule and members will be encouraged to listen and discuss topics of interest during their weekly meetings. The main objectives of the radio program are to introduce the GME program; motivate women to achieve economic access; and inform women about existing business support programs. The radio programs will introduce women and business topics to radio in the eastern region. The topics for this month include: business for women according to Islam (Bibi Khadija – the Prophet's wife); overview of SHGs and success stories; interview with business women; women in business role models; and credit opportunities.
- All SHG will start a literacy program in early October. RI has received 14 proposals for Capacity Building Training for SHGs and a bidding selection is scheduled for next week.

- **Smallholder Livestock Management Program:** 717 women from Laghman and Nangarhar have been trained in the areas of livestock nutrition and management, identification and treatment of common diseases, and practices to improve productivity led by three female paravets.
- **The Women's Forestry Nursery Program:** Three day trainings are scheduled for October. The saplings will be ready for re-planting in early January 2007. GME will be working with CFW regarding site selection and landscaping.



**Nursery established by one of the beneficiaries of the Forest Nursery Program**

- **Handicraft:** A Rural Handicraft Exhibit is scheduled for November 14-27, 2006 in New Delhi, India sponsored by Global Network & India Trade Promotion Organization. ALP/E will assist four local firms participating in the exhibition, and will provide technical assistance in handicraft design to improve the competitiveness of Afghan handicrafts by enhancing the quality and selection of products, and provide financial assistance for travel, accommodation and exhibition costs, as well as assistance in the design and set-up of the exhibition. This will constitute the first step towards the promotion of handicrafts from Eastern Afghanistan in the international marketplace.
- **Capacity Building:** A six month (October 06 – March 07) Capacity Building Plan was developed in collaboration with the Director of Women's Affairs of Nangarhar, Laghman and Kunar. The plan will be implemented in collaboration with the Institutional Development Department. An introductory meeting is scheduled with the Director of Women's Affairs and the Institutional Development Department early next week and implementation begins in October.
- **Vegetable Production:** The GME is working closely with the Natural Resource Management (NRM) Specialist to develop a vegetable seedling production work plan. Three sites have already been identified in Kama and Dare- Noor Districts. Three groups, each consisting of 15 women have been formed. An STTA will provide additional assistance in November.
- **Women's Private Sector Initiative:** The Kaweyan Business Development Services team is in the process of data entry and compiling a final report expected in mid October 2006. In addition, AWBA conducted a four-day market access training for 20 women at the BDC.
- **Mainstreaming Gender:** CFW – GME staff attended the opening ceremony of the Benagha, Behsud project. GME staff also selected female cooks for the new sites and are currently in the process of recruiting female laborers for construction of the Jalalabad Wholesale Market through the Labor Association and DoWA. Female laborers will be trained in steel bending and cobble stone road construction.



**ALP/E GME Coordinator monitoring payment of female cooks at the Binigah CFW site in Behsud, Nangarhar**

## GENDER AND MICRO-ENTERPRISES

#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
	Business Training of Trainers	Kunar	Kunar	100%	100%	RI	2-Jul-06	13-Jul-06	Planned
	Establishment of 4 women-owned nurseries	ER	Nangarhar, Laghman	100%	15%	ALP/E	1-Apr-06	15-Jan-07	On-Going
	Monitoring of Infrastructure Projects	ER	ER	100%		ALP/E	1-May-06	31-Jan-09	On-Going
	Selection of women for Food Service	ER	ER	100%		ALP/E	1-May-06	31-Jan-09	On-going
	Smallholder Livestock Management Program	Village based Self Help Groups	Nangarhar/Laghman/Kunar	100%	10%	ALP/E	1-May-05	1-May-07	On-going
	Women in Business Survey	ER	ER	95%	0%	Kaweyan	11-Jun-06	30-Sep-06	Planned
	AWBA at the BDC	Nangarhar	Jalalabad	100%	10%	AWBA	13-Jun-06	30-Jun-08	On-going
	Data Base collection on Businesses	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100%	20%	RI	06-Jul-06	05-Sep-06	On going
	Call for proposal (Follow up & Capacity Building for SHG)	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100%	50%	RI	14-Aug-06	01-Sep-06	On going
	Livestock Vet Service and Vaccination	Laghman	Laghman	100%	70%	RI	08-Aug-06	05-Sep-06	On going

## 5. INSTITUTIONAL CAPACITY DEVELOPMENT

The following activities were undertaken during the reporting period:

### I. Support to Associations:

#### a. Existing association:

- The Fresh Fruit and Vegetable Wholesale Market Association has been operating since 2002, however the management and members had little knowledge of either the guiding principles or the usual functions of an association. ALP/E is committed to strengthening the organization by offering association members and management information regarding their responsibilities and basic organizational operations. An initial meeting was held on September 24, with an emphasis on association management, selection of a board of directors, and changes that can be made if members are not satisfied with current management. Over thirty members participated and learned that they are able to make changes to the management team if they are dissatisfied with their performance.

#### b. Newly established:

- Meetings took place with the Livestock Development Association to finalize their charter document, with the full agreement of all members and the management group. With the final version in hand, the association leader, secretary and ALP/E staff traveled to Kabul to submit the document to the Justice Ministry. The secretary and the treasurer will soon start computer and language training. Once trained, they will be able to prepare proper reports, communicate with members and keep track of funds.
- The Carpet Producers Association has submitted a charter document to the Justice Ministry in Kabul. ALP/E staff assisted in finalizing the document, with a consensus reached by all members.


#### c. To be established:

- Road User Association meetings were held with the ALP/E Infrastructure team to prioritize needs for establishing the association. Shamsapur cobblestone road was selected as the first to set up a user association, and an agreement was reached to go into the field to speak to the village shuras located along the road.

- The Handicrafts Association, with the cooperation of the GME Unit, will be created to support women and women-owned businesses.
- The Computer and English language training for association staff, delivered by RANA Institute, is being monitored on an ongoing basis and students continue to make impressive progress.



**Livestock Development Association during discussions on their charter document**

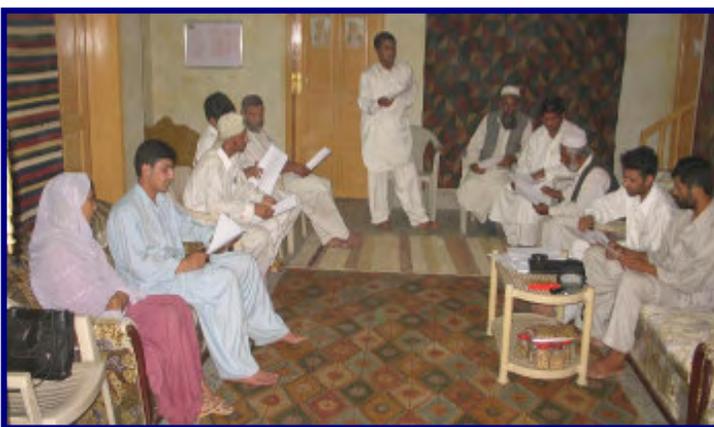

**ALP/E Capacity Building specialist finalizing charter document with members of the Carpet Producer Association**

## **II. Support to Ministry of Agriculture:**

- Together with the ALP/E M&E team, a meeting was held with the head of the Agricultural Directorate discussing possible involvement in a province wide data gathering survey. The M&E member suggested methodologies for implementing such a survey, and other donors will be included in the data collection and results analysis.
- The director of Agriculture in Laghman requested project planning and management training. ALP/E identified a suitable training institution and contract documents are being finalized.
- Two visits to Kunar Province were completed to identify computer and language training institutions. A suitable institution was selected and required documents prepared. The computer and language training started on September 19. with twenty-five staff from the Agricultural Directorate participating.
- ALP/E staff conducted weekly monitoring of the computer and English language training delivered by RANA Institute; the training is for the Nangarhar Agricultural Directorate and for association support staff.



**Laghman Agriculture Directorate staff during computer training**

## INSTITUTIONAL CAPACITY DEVELOPMENT Support to Ministry of Agriculture

#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Internet Use Training for the directors of Agriculture Directorate	Jalalabad	Nangarhar/Laghman/Kunar	100%	100%	BDC	27 Aug-06	29-Aug-06	Completed
2	Computer and English language training for staff of Nangarhar Agricultural Directorate	Jalalabad	Nangarhar	100%	10%	RANA Institute	5-Jul-05	16-Feb-08	Ongoing
3	Computer and English language training for staff of Laghman Agricultural Directorate	Mihtarlam	Laghman	100%	05%	Laghman Educational Training Center	12-Sept-06	12-Apr-08	Ongoing
4	Computer and English language training for staff of Kunar Agricultural Directorate	Asadabad	Kunar	80%	0%	Kunar Community Educational Center	12-Oct-06		Ongoing
5	Survey and sampling - Nangarhar Agricultural Directorate	Jalalabad	Nangarhar	20%	0%				Ongoing
6	Project Planning and Management Training for selected staff of Laghman Agricultural Directorate	Mihtarlam	Laghman	20%	0%	AITM	29-Sept-206	06-Oct-06	Ongoing
7	Project Planning and Management Training for selected staff of Kunar Agricultural Directorate	Asadabad	Kunar	20%	0%		19-Oct-06	02-Nov-06	Ongoing
8	Survey and sampling - Nangarhar Agricultural Directorate	Jalalabad							

## INSTITUTIONAL CAPACITY DEVELOPMENT Support to Associations

#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
9	Computer and English language training for support staff of selected local associations	Jalalabad	Nangarhar	100%	10%	RANA	11-Aug-06	12-April-07	Ongoing
10	Establishment of Livestock Producers Association	Jalalabad	Nangarhar	100%	80%	ALP/E	24-Aug-06	01-Oct-06	Ongoing
11	Establishment of Carpet Producers Association	Jalalabad	Nangarhar	100%	20%	ALP/E	27-Aug-06	15-Oct-06	Ongoing
12	Support to Fresh Fruits and Vegetable Wholesalers Association	Jalalabad	Nangarhar	70%	05%	ALP/E	20-Aug-06		Ongoing

## 6. COORDINATION WITH THE GOVERNMENT

ALP/E continued to work towards improving already effective efforts with government bodies and other organizations during this reporting period:

- The ALP/E's liaison officer attended the fourth Poppy Elimination Program (PEP) meeting held at the Governor of Nangarhar's Office. The meeting was attended by government officials, community representatives, religious leaders, and NGO representatives. The Provincial Governor of Nangarhar, Mr. Gul Agha Sherzai welcomed the participants and thanked the communities for effectively ending poppy cultivation during 2005. The Governor also stressed closely monitoring and evaluating all the projects being implemented in the region.

# ADDITIONAL INFORMATION

## I. SECURITY

- The security situation in the eastern region was tense during the reporting period. A total of 15 security related incidents took place. The AGEs/ Insurgents are increasing their activities throughout the region, specifically in Kunar (Nari, Marawara and Pech districts and in Laghman (Alingar, Alishing and Dawlat Shah District). The risk of VBIED/BBIED attacks is increasing particularly in Nangarhar and Kunar Provinces, with reports of attackers targeting government and security positions. Additionally, a special warning was received for Jalalabad city, the Jalalabad –Torkham highway and the Jalalabad - Asadabad highway.
- The security situation in the Province of Nangarhar was relatively calm with seven incidents noted during the reporting period in Jalalabad. The infiltration of a new group of 25 AGEs/ Insurgents reportedly crossed the Pakistani border through the eastern districts to conduct attacks against governmental installations the Province. The infiltration of a group of 100 AGEs through Rodat district was also reported. This group has been tasked to conduct attacks against governmental structures in the area, the nationality of the group members is not clear yet.
- The security situation in Laghman was calm with four incidents reported during the period. ALP/E could not send its international staff to Dawlat Shah, Alingar and Alishang Districts of Laghman province. However, elsewhere operations are going smoothly without interruption by the subcontractor Relief International (RI). Situations in Alishang, Alingar and Dawlat Shah Districts of Laghman province are uncertain with the report of insurgents' movements and infiltration.
- The security situation in Kunar continues to be tense with four incidents reported. The province is assessed as being a high risk area for the aid community due to the presence of AGEs, and regular IED, RCIED and rocket attacks against government and Coalition Forces. It is widely believed that Insurgents have almost complete freedom of movement in the border areas and reports indicate a group of suicide attackers entered to Kunar province to target CF, ANSF and International aid workers. ALP/E operations continue in the four districts of Narang, Nurgal, Khas Kunar and Chawkay.
- The CF operation in Eastern and Central Nuristan continued, reportedly to destroy AGE hideouts in the remote areas of Nuristan and clear the area from AGEs. There is little accurate information about ongoing insurgent activities in Nuristan available, as there are almost no international NGOs present there.

## 2. MONITORING AND EVALUATION

M&E completed the following activities during the reporting period:

- The ALP/E M&E Team conducted a monitoring mission to eight ongoing and three completed CFW projects in the region. The findings and recommendations were shared with concerned technical units for action. The monitoring missions focused on; 1) physical progress, assessing whether planned physical progress was achieved in terms of length, width, and quantities provided, 2) financial disbursements, laborers working on CFW projects were directly interviewed to determine whether they have been paid for hours worked. Project financial data submitted to the ALP/E finance section was cross checked with laborers attendance sheets and pay roll, and 3) persons employed and employment days; individual laborers from each group were counted in spot checks to cross check their physical attendance with the reports. In addition, a monitoring visit was conducted to the Business Development Center (BDC) to monitor activities.
- The USAID GeoBase database was updated for 80 active and completed CFW, Agribusiness, and GME projects.
- The M&E GIS component continued supporting the Nangarhar Road Inventory Team to track standard data collection, downloading, and cleaning field GPS data and sharing the information. In addition, numerous maps on program, security, administration, and other topics were produced during the reporting period.
- The M&E Team has been tracking the process of selecting the farmers under the ALP/E Fall 2006 Wheat Seed and Fertilizer Distribution Program. The team completed the process of selecting beneficiaries in Nangarhar, and is currently distributing vouchers among the selected beneficiaries in Nangarhar.



**M&E Field Monitor holds meeting with Shura Representatives**

## Short term Technical Assistance

#	Name	Title	Activity	Status
1	Conrado Camacho	Cobblestone Training Advisor	Training for cobblestone roads	ongoing
2	Anne Williams	Business Training Advisor	Business skills training and Private Sector Development assistance	ongoing

### ALP/E CONTACT INFORMATION

Organization: Development Alternatives, Inc. (Nangarhar Office)  
Address: Jalalabad, Nangarhar, Afghanistan  
Name: Jonathan Greenham, COP  
Afghanistan cell: 0798-039432  
[jonathan\\_greenham@dai.com](mailto:jonathan_greenham@dai.com)

Organization: Development Alternatives, Inc. (Home Office)  
Address: 7250 Woodmont Avenue, Suite 200  
Telephone: (301) 718-8699  
Fax : (301) 718-7968  
Web site : [www.dai.com](http://www.dai.com)



### Annex-II: Summary Table of APMS Activities

District/Province	Beneficiary Selection		Fertilizer Distributed		Seed Distributed in Kgs				
	No of Farmers Supported	Land supported in Hectares	Urea in MT	DAP in MT	Tomato	Okra	Eggplant	Cucumber	Watermelon
Khogyani	3,958	475	118.75	59.38	475	7,125	475	0	0
Sherzad	3,958	475	118.75	59.38	475	7,125	475	0	0
Hisarak	3,958	475	118.75	59.38	475	7,125	475	0	0
Pachir Wa Agam	3,958	475	118.75	59.38	475	7,125	475	0	0
Behsud	3,958	475	118.75	59.38	475	7,125	475	0	0
Surkh Rod	3,958	475	118.75	59.38	475	7,125	475	0	0
Kama	3,958	475	118.75	59.38	475	7,125	475	0	0
Rodat	4,750	475	118.75	59.38	475	7,125	475	0	0
Kuz Kunar	4,750	475	118.75	59.38	475	7,125	475	0	0
Shinwar	4,750	475	118.75	59.38	475	7,125	475	0	0
Bati Lot	6,250	775	193.75	96.88	475	7,125	475	0	750
Chaparhar	4,750	475	118.75	59.38	475	7,125	475	0	0
<b>Nangarhar Sub-total</b>	<b>52,956</b>	<b>6,000</b>	<b>1,500</b>	<b>750</b>	<b>5,700</b>	<b>85,500</b>	<b>5,700</b>	<b>0</b>	<b>750</b>
Qarghai	12,500	1,250	312.50	156.25	350	7,500	0	500	375
Mehtarlam	12,500	1,250	312.50	156.25	350	7,500	0	500	375
<b>Laghman Sub-total</b>	<b>25,000</b>	<b>2,500</b>	<b>625.00</b>	<b>312.50</b>	<b>700</b>	<b>15,000</b>	<b>0</b>	<b>1,000</b>	<b>750</b>
Asad Abad	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Khas Kunar	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Chawkay	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Narang	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Nurgal	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Sirkanay	2,500	250	62.50	31.25	100	1,249	66.66	0	0
<b>Kunar Sub-total</b>	<b>15,000</b>	<b>1,500</b>	<b>375.00</b>	<b>187.5</b>	<b>600</b>	<b>7,494</b>	<b>399.96</b>	<b>0</b>	<b>0</b>
<b>Grand-Total</b>	<b>92,956</b>	<b>10,000</b>	<b>2,500</b>	<b>1,250</b>	<b>7,000</b>	<b>107,994</b>	<b>6,100</b>	<b>1,000</b>	<b>1,500</b>

### Annex –III: Person Employed, Employment Days, and Wages Paid on ALP/E CFW Projects through September 30<sup>th</sup>, 2006

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Kunar	Chawkey	CFW101303	Dewagal Road Improvement	177	14	191	17,016	1,304	18,320	68,066	5,216	73,282
Kunar	Chawkey	CFW101304	Zarmandai and Kulmani Flood Protection Wall	160	14	174	11,259	916	12,175	45,036	3,664	48,700
Kunar	Chawkey	CFW101306	Chawkey Khower Flood Protection Wall	160	14	174	8,415	667	9,082	33,664	2,668	36,332
Kunar	Khas Kunar	CFW101501	Daag Canal Repair	235	17	252	13,359	801	14,160	51,780	3,204	54,984
Kunar	Khas Kunar	CFW101502	Tanar Road Rehabilitation	84	6	90	4,682	328	5,010	17,886	1,312	19,198
Kunar	Khas Kunar	CFW101503	Clinic To Hakim Abad Road	63	4	67	1,546	85	1,631	6,184	340	6,524
Kunar	Khas Kunar	CFW101504	Khas Kunar Middle Road	77	5	82	4,711	300	5,011	18,844	1,200	20,044
Kunar	Narang	CFW101203	Bar Narang Road Improvement	216	16	232	17,845	1,422	19,267	71,380	5,688	77,068
Kunar	Narang	CFW101204	Sharalo Badil Road Improvement	200	14	214	15,924	1,216	17,140	63,696	4,864	68,560
Kunar	Narang	CFW101205	Badil Khawar Flood Protection Walls and Irrigation Intake	103	8	111	5,120	312	5,432	20,480	1,248	21,728
Kunar	Nurgal	CFW101402	Seenda Wala Canal Rehabilitation	105	8	113	8,843	539	9,382	33,976	2,156	36,132
Kunar	Nurgal	CFW101403	Nurgal Aret Road	178	14	192	11,297	855	12,152	45,188	3,420	48,608
Kunar	Nurgal	CFW101404	Kuz Nurgal Tora Tega Road Improvement	74	6	80	3,061	224	3,285	12,244	896	13,140
<b>Kunar Province Sub-total</b>				<b>1,832</b>	<b>140</b>	<b>1,972</b>	<b>123,078</b>	<b>8,969</b>	<b>132,047</b>	<b>488,424</b>	<b>35,876</b>	<b>524,300</b>
Laghman	Alingar	CFW090301	Khoja Khil Sofla Canal Rehabilitation	1,329	38	1,367	11,100	408	11,508	52,597	1,596	54,193
Laghman	Alingar	CFW090302	Ghundai Nazar Khil Protection	211	8	219	19,327	2,651	21,978	71,823	9,762	81,585
Laghman	Alingar	CFW090303	Qasaba Protection Wall	201	7	208	15,437	2,405	17,842	59,090	10,061	69,151
Laghman	Alingar	CFW090304	Bar Kanday and Kuz Kanday Canal Rehabilitation	108	4	112	6,780	262	7,042	25,468	1,048	26,516
Laghman	Alingar	CFW090305	Purai Protection Wall	96	4	100	1,352	34	1,386	4,586	136	4,722
Laghman	Alingar	CFW090306	Mandol Protection Wall	92	4	96	1,674	51	1,725	5,585	204	5,789
Laghman	Alingar	CFW090705	Kandi Sah b Canal Rehabilitation	126	5	131	4,103	133	4,236	15,789	532	16,321
Laghman	Alishing	CFW090701	Nolo Protection Wall	399	7	406	24,345	381	24,726	90,552	1,524	92,076
Laghman	Alishing	CFW090702A	Jamshidabad Protection Wall	450	4	454	21,566	164	21,730	75,883	656	76,539
Laghman	Alishing	CFW090702B	Jamshidabad Flood Protection Wall Additional Work	186	5	191	12,636	324	12,960	49,228	1,296	50,524
Laghman	Alishing	CFW090703	Mustafa Kalay Protection Wall	500	18	518	17,082	565	17,647	60,917	2,260	63,177
Laghman	Alishing	CFW090704	Akhund Sahib Protection Wall	360	9	369	24,352	482	24,834	95,600	1,928	97,528

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Laghman	Alishing	CFW090708	Qardi Salab Canal Rehabilitation	158	6	164	5,024	158	5,182	18,742	632	19,374
Laghman	Alishing	CFW090709	Kalay Baya Canal Rehabilitation	88	4	92	1,790	55	1,845	6,513	200	6,713
Laghman	Mihtarlam	CFW090101	Deh Zairat Protectin Wall	525	10	535	43,484	923	44,407	160,625	3,693	164,318
Laghman	Mihtarlam	CFW090102	Karaho Protection Wall	209	4	213	13,744	155	13,899	115,181	1,557	116,738
Laghman	Mihtarlam	CFW090103	Tergari Protection Wall	331	8	339	33,494	927	34,421	126,773	3,692	130,465
Laghman	Mihtarlam	CFW090104	Mulayan Protection Wall	369	12	381	27,892	933	28,825	102,319	3,600	105,919
Laghman	Mihtarlam	CFW090105	Shamangal Canal Reconstruction	168	7	175	14,319	563	14,882	56,453	2,222	58,675
Laghman	Mihtarlam	CFW090106	Hayadarkhani Canal Reconstruction	219	4	223	5,390	173	5,563	22,922	692	23,614
Laghman	Mihtarlam	CFW090107	Pacha Joie Canal Rehabilitation	143	7	150	3,612	109	3,721	13,619	436	14,055
Laghman	Mihtarlam	CFW090108	Abi Zai Flood Protection Wall	155	7	162	2,362	50	2,412	7,677	200	7,877
Laghman	Mihtarlam	CFW090112	Ghundy Baba Flood Protection Wall	126	6	132	2,112	46	2,158	7,219	184	7,403
Laghman	Mihtarlam	CFW090118	Qala Shagee Protection Wall	177	8	185	3,222	90	3,312	10,754	360	11,114
Laghman	Mihtarlam	CFW090120	Baba Sahib Canal Rehabilitation	84	3	87	2,035	57	2,092	7,828	228	8,056
Laghman	Qarghayi	CFW090201	Dopi and Longalam Protection Wall	301	13	314	22,542	860	23,402	81,684	3,272	84,956
Laghman	Qarghayi	CFW090202	Char Bagh Canal Reconstruction	157	5	162	11,607	446	12,053	44,063	1,768	45,831
Laghman	Qarghayi	CFW090203	Kalakot and Longalam Canal Reconstruction	186	6	192	15,903	532	16,435	59,107	2,084	61,191
Laghman	Qarghayi	CFW090204	Daronata Road Repair (Daronta Bypass)	226	2	228	11,346	86	11,432	42,404	344	42,748
Laghman	Qarghayi	CFW090205	Shamsherabad Flood Protection	412	14	426	27,294	1,151	28,445	102,280	4,140	106,420
Laghman	Qarghayi	CFW090208	Kanda Canal Rehabilitation	149	6	155	9,856	387	10,243	38,449	1,548	39,997
Laghman	Qarghayi	CFW090209	Daronta Bypass Cobble Stone Road Second Reach	303	2	305	27,704	242	27,946	110,816	968	111,784
Laghman	Qarghayi	CFW090210	Kac Aziz khan Canal	101	4	105	1,892	47	1,939	7,209	188	7,397
Laghman	Qarghayi	CFW090212	Farman Khil and Jue Daman Canal	96	-	96	2,599	-	2,599	10,396	-	10,396
Laghman	Qarghayi	CFW090214	Qardi Kac Canal Rehabilitation	106	-	106	426	-	426	1,434	-	1,434
<b>Laghman Province Sub-total</b>				<b>8,847</b>	<b>251</b>	<b>9,098</b>	<b>449,403</b>	<b>15,850</b>	<b>465,253</b>	<b>1,761,585</b>	<b>63,011</b>	<b>1,824,596</b>
Nangarhar	Achin	CFW081001	Deh Sarak Canal Intake Improvement	71	6	77	1,013	52	1,065	4,052	208	4,260
Nangarhar	Achin	CFW081002	Pekha Protection Flood Protection Wall	461	-	461	29,769	-	29,769	110,600	-	110,600
Nangarhar	Behsud	CFW082201	Abdian Road Rehabilitation	185	-	185	7,952	-	7,952	30,833	-	30,833
Nangarhar	Behsud	CFW082202	Biniga Flood Protection Wall	78	6	84	5,093	285	5,378	20,213	1,140	21,353
Nangarhar	Behsud	CFW082203	Sammarkhil Erosion Protection	207	17	224	6,312	561	6,873	24,863	2,244	27,107

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Nangarhar	Behsud	CFW082204	Spin Jumat Embankement	65	5	70	5,481	355	5,836	21,924	1,420	23,344
Nangarhar	Chaparhar	CFW080601	Daulat Zai Canal Intake	133	10	143	12,015	872	12,887	48,060	3,488	51,548
Nangarhar	Chaparhar	CFW080602	Garatic and Chardahi Canal Intakes	159	13	172	7,498	563	8,061	29,992	2,252	32,244
Nangarhar	Chaparhar	CFW080603	Garatic Flood Protection Wall	142	11	153	9,866	706	10,572	39,464	2,824	42,288
Nangarhar	Chaparhar	CFW080604	Chardahi Flood Protection Wall	108	9	117	9,140	600	9,740	36,560	2,400	38,960
Nangarhar	Chaparhar	CFW080605	Sholana Flood Protection Wall	127	9	136	10,170	701	10,871	40,680	2,804	43,484
Nangarhar	Dur Baba	CFW081201	Mahsil and Qasaba Kalay Irrigation Reservoir and Erosion Protection	188	2	190	7,010	8	7,018	28,040	32	28,072
Nangarhar	Dur Baba	CFW081202	Sasobi Irrigation Reservoir and Flood Protection Wall	186	8	194	10,692	24	10,716	42,768	96	42,864
Nangarhar	Dur Baba	CFW081203	Torlala Kalay Irrigation Reservoir and Flood Protection	153	4	157	8,262	172	8,434	33,048	688	33,736
Nangarhar	Goshta	CFW081601	Kuz and Bar Billa Flood Protection Wall 1	244	18	262	13,384	1,147	14,531	50,917	4,588	55,505
Nangarhar	Goshta	CFW081602	Kuz and Bar Billa Flood Protection Wall 2	90	8	98	2,549	197	2,746	15,736	788	16,524
Nangarhar	Goshta	CFW081603	Kuz and Bar Billa Flood Protection Wall 3	89	6	95	5,301	382	5,683	19,811	1,528	21,339
Nangarhar	Hisarak	CFW080301	Mana Road Rehabilitation	288	26	314	20,876	1,894	22,770	82,332	7,576	89,908
Nangarhar	Hisarak	CFW080302	Shana Zawara Road Rehabilitation	116	10	126	8,454	652	9,106	33,408	2,608	36,016
Nangarhar	Hisarak	CFW080305	Sanzai Road Improvement	65	4	69	4,190	300	4,490	16,760	1,200	17,960
Nangarhar	Jalalabad	CFW080101	Jalalabad city Main Drain	63	-	63	2,622	-	2,622	9,363	-	9,363
Nangarhar	Jalalabad	CFW080102	Jalalabad city Road Side Drains	540	-	540	22,174	-	22,174	82,200	-	82,200
Nangarhar	Jalalabad	CFW080103	Whole Sale Market Rehabilitation	160	-	160	11,934	-	11,934	47,736	-	47,736
Nangarhar	Khogyani	CFW080501	Khawaran Road Rehabilitation	146	14	160	9,153	741	9,894	36,080	2,964	39,044
Nangarhar	Khogyani	CFW080502	Kalagho Road Rehabilitation	181	16	197	9,103	781	9,884	35,991	3,124	39,115
Nangarhar	Khogyani	CFW080504	Nemla Irrigation Intakes and Canal Repair	50	4	54	302	16	318	1,208	64	1,272
Nangarhar	Khogyani	CFW080506	Khawaza khil and Malam Khil Road	48	3	51	2,718	179	2,897	10,872	716	11,588
Nangarhar	Khogyani	CFW080507	Nemla Flood Protection Works	110	7	117	7,204	424	7,628	28,816	1,696	30,512
Nangarhar	Kuz Kunar	CFW081902	Bodiali and soraj Irrigation Rehabilitation	128	9	137	6,346	484	6,830	25,384	1,936	27,320
Nangarhar	Lal Pur	CFW081502	Guldag Flood Protection Wall	163	13	176	3,094	199	3,293	12,376	796	13,172
Nangarhar	Muhmand Dara	CFW081402	Zara Sultankhil Protection Wall	67	1	68	3,477	33	3,510	13,772	132	13,904
Nangarhar	Muhmand Dara	CFW081403	Girdi Ghos Protection Wall	82	3	85	2,637	112	2,749	10,948	448	11,396
Nangarhar	Muhmand	CFW081404	Basawal Banbaba Flood Protection Wall	73	6	79	1,496	118	1,614	5,984	472	6,456

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
	Dara											
Nangarhar	Nazyan	CFW081101	Tarkhy Flood Protection Works and Irrigation Intake	99	8	107	6,153	494	6,647	24,612	1,976	26,588
Nangarhar	Sherzad	CFW080401	Gandomak Road Rehabilitation	180	16	196	10,924	936	11,860	43,468	3,744	47,212
Nangarhar	Sherzad	CFW080402	Toto Road Rehabilitation	129	8	137	8,970	631	9,601	35,408	2,524	37,932
Nangarhar	Sherzad	CFW080403	Ashpan Flood Protection	203	18	221	10,764	971	11,735	42,629	3,884	46,513
Nangarhar	Sherzad	CFW080405	Patlaw Road Rehabilitation	109	7	116	7,053	507	7,560	28,140	2,028	30,168
Nangarhar	Shinwar	CFW081301	Zakhil Wash Irrigation Canal	71	-	71	3,578	-	3,578	14,312	-	14,312
Nangarhar	Spin Ghar	CFW082301	Maidanak Road Rehabilitaion	465	-	465	16,857	-	16,857	61,271	-	61,271
Nangarhar	Spin Ghar	CFW082303	Hajoom Kal Chelgazi Canal Intakes	72	-	72	347	-	347	1,388	-	1,388
Nangarhar	Spin Ghar	CFW082305	Girdi Nawagai Road Repair	156	13	169	12,453	976	13,429	49,812	3,904	53,716
Nangarhar	Surkh Rod	CFW080201	Shamshapur Cobble Stone Road Pilot	393	16	409	18,773	851	19,624	71,332	3,404	74,736
Nangarhar	Surkh Rod	CFW080202	Kakrak Road Improvement	258	20	278	15,389	567	15,956	61,556	2,268	63,824
Nangarhar	Surkh Rod	CFW080203	Tatang Nawab Jabar Canal Rehabilitation	158	11	169	8,084	217	8,301	32,336	868	33,204
Nangarhar	Surkh Rod	CFW080204	Sarband and Jalawanano Canal Intake	87	7	94	5,218	308	5,526	20,872	1,232	22,104
Nangarhar	Surkh Rod	CFW080205	Shamshapur Daronta Road Improvement	283	6	289	23,326	336	23,662	93,304	1,344	94,648
Nangarhar	Surkh Rod	CFW080206	Shamshapur Cobble Stone Road Second Reach	390	16	406	35,699	1,391	37,090	142,796	5,564	148,360
Nangarhar	Tor Ghar	CFW082401	Shangina Yousaf Kas Canal Rehabilitation	153	-	153	840	-	840	3,360	-	3,360
Nangarhar	Tor Ghar	CFW082402	Gachway Mirano Road Improvement	42	-	42	64	-	64	256	-	256
<b>Nangarhar Province Sub-total</b>				<b>8,214</b>	<b>394</b>	<b>8,608</b>	<b>451,779</b>	<b>20,743</b>	<b>472,522</b>	<b>1,777,642</b>	<b>82,972</b>	<b>1,860,614</b>
Nuristan	Nur Gram	CFW300801	Dakor Mashafa Cobblestone Road	20	-	20	40	-	40	160	-	160
<b>Nuristan Province Sub-total</b>				<b>20</b>	<b>-</b>	<b>20</b>	<b>40</b>	<b>-</b>	<b>40</b>	<b>160</b>	<b>-</b>	<b>160</b>
<b>Grand Total</b>				<b>18,913</b>	<b>785</b>	<b>19,698</b>	<b>1,024,300</b>	<b>45,562</b>	<b>1,069,862</b>	<b>4,027,811</b>	<b>181,859</b>	<b>4,209,670</b>

**Note: USAID/AINP Performance Data:** i. Work Days Generated (#): 2,967,708 ii. Salaries Paid to Workers: \$9,842,363 iii. People Employed (#): 134,000 iv. Irrigation Canals, drainage, ditches, and Karezes repaired or cleaned (Km): 2,281 v. Land Benefiting from Improved Irrigation (Ha): 113,060 vi. Roads Repaired (Km): 148
