



USAID
FROM THE AMERICAN PEOPLE

AFGHANISTAN

**ALTERNATIVE LIVELIHOODS PROGRAM
- EASTERN REGION (ALP/E)**



ALP/E: Deputy Governor of Laghman Province is inaugurating the first ever Cobblestone Road in Qarghai District

Biweekly Report
May 1-15, 2006

ALP/E General Information	
Project	Alternative Livelihoods Program – Eastern Region
Start Date	15 February, 2005 (contract signing)
End Date	14 February, 2009
Contract Number	Contract Number GS-10F-0359M
Order Number	Order Number 306-M-00-05-00515-00
Cognizant Technical Officer	Brian Bacon
Contracting Officer	Margaret Kline
Geographic Coverage	Nangarhar, Laghman, and Kunar Provinces

ALP/E'S MISSION STATEMENT

The overall objective of ALP/E is to accelerate broad-based, sustainable regional economic development in the Eastern Region, providing the population with licit livelihood options, and contributing to the elimination of poppy production as an economic element. This will be accomplished by working with the public and private sectors to increase the competitiveness and diversity of regional agricultural and non- agricultural sub-sectors; improving access to markets, inputs and business services; consolidating the presence of supportive public and productive infrastructure; building public and private sector capacity to function in a competitive and transparent economy; and addressing the needs of populations that are heavily reliant on the poppy economy.



1. EXECUTIVE SUMMARY

Snapshots of ALP/E activities and achievements during this reporting time are as follow:

- A Fresh Fruit and Vegetable Exhibition was held at Serena Hotel Kabul, attended by ALP/E Agribusiness Specialists and Wholesalers of the Eastern Region.
- Preparations for the Eastern Region Agricultural Trade Fair were underway. The fair will provide opportunities for research centers, input suppliers, fruit, vegetable and livestock producers, and traders to learn about the latest agricultural technologies, observe products currently being produced by farmers in the region, and establish market contacts.
- The Fruit Marketing Program consultant identified and selected more than 40 groups representing 1,500 farmers as part of the development of production and marketing clusters.
- Work continued on finalizing and approving long term infrastructure projects including Kama irrigation system, Kama main road, Goshta Bridge, Abuzai Bridge, Qasam Abad road, and Wholesale Market.
- Three CFW projects were completed and work continued on 39 ongoing projects. The daily employment rate was 4,766 workers per day while total employment days were recorded as 48,719 during the reporting period.
- The PSD Unit facilitated the participation of traders and investors of the region in AISA's International Investment Conference in Kabul. Several discussions and meetings were held with government, INGOs, and business communities to promote investment in the region.
- 33 Self Help Groups (SHG) were established including 500 women who began their vocational trainings. The GPS survey is being conducted for SHGs in Laghman and will soon be started in Kunar.
- Three EMS workbooks were cleared for CFW and the Wholesale market. Efforts are underway to deal with solid waste issue and composting toilets and vegetable wastes.
- The first part of a series of five training sessions on commercial production of trees saplings was completed. Thirty male and ten female nursery operators were trained and will be contracted for tree production.
- The first part of a series of five trainings on commercial trees sapling was completed. Thirty men and ten women were trained and will be contracted for tree production.

2. PERFORMANCE DATA

The basic tools for monitoring and for this report are the agreed indicators for ALP/E. The following table specifies the basic M&E results, showing the progress and degree of achievement of the targets.

Indicator	Unit of Measure	Added Bi-weekly)	Total (Life of Project)	Target (FY 06)	Target (FY 07)	Target (FY 08)	By Province (Life of Project)			By Gender (Life of Project)	
							Nangarhar	Laghman	Kunar	Male	Female
Kms. of irrigation and drainage canals and karezes	Km	2.83	137	TBD	TBD	TBD	97.5	26	13.5	0	0
Kms. of rural roads repaired in poppy regions	Km	4	102	TBD	TBD	TBD	70	6	30	0	0
# of hectares of improved irrigation as a result of ALP infrastructure	Km	475	53,126	TBD	TBD	TBD	21,395	28,331	3,400	0	0
\$ paid in cash for work (CFW) in AL programs	USD	194,673	2,185,077	TBD	TBD	TBD	712,478	1,361,933	110,666	2,097,056	88,021
# of labor days for CFW in AL programs	#	49,233	558,011	TBD	TBD	TBD	185,570	343,801	28,640	535,915	22,096
# of Afghans paid through CFW salaries	#	4,766	13,039	TBD	TBD	TBD	5,297	6,843	899	12,571	468
# Afghans trained in business skills	#	1,342	4,000	700	1,900	0	2,500	1,000	500	0	4,000
# of farmers receiving seed and fertilizer	#	0	92,956	0	0	0	52,956	25,000	15,000	92,956	
# of farmers trained in agricultural practices in targeted poppy provinces under ALP	#	0	80,106	0	0	0	54,794	25,312	0	80,106	0

Data Source: ALP/E Program only

3. SECTOR ACTIVITIES

A brief description of the activities and achievements of the technical sectors is presented as follow.

1. AGRIBUSINESS

- i. **AMPS:** The Agribusiness team assisted beneficiaries of the Agricultural Marketing and Production Support (AMPS) Program in a trade promotion activity organized by the Peace Dividend Trust. The activity consisted in a produce exhibition and a workshop on food safety and quality requirements for fruit and vegetable, by the Serena Hotel in Kabul. The Eastern Region was represented by 10 produce wholesalers, all members of the Jalalabad Wholesalers Association, who exhibited their products and learned about the requirements of institutional customers. This activity is expected to result in concrete negotiations over the next few weeks, which will constitute a significant leap for local producers and traders, as their produce will compete with imports from Dubai and European countries. In the last six months ALP/E has been engaged in a robust training program to enable producers, district assemblers and wholesalers to meet stricter grades and standards, especially those concerned with quality, food safety and packaging, which is reflected in the success in this first promotional activity.



ALP/E: Wholesalers of the Eastern Region display their fresh produce in Serena Hotel, Kabul



ALP/E: Serena Hotel Management is checking fresh produce from the Eastern Region

- ii. **Agriculture Trade Fair:** ALP/E will be sponsoring the first edition of the Eastern Region Agricultural Trade Fair “Jalalabad 2006”. The preparations are underway with an aggressive promotional campaign, the renovation of the facilities provided by Nangarhar Valley Development Authority, at Hada Farm. Representatives from a broad range of actors including research centers, input suppliers, individual farmers and farmer organizations, District-level produce assemblers, fruit and vegetable wholesalers, processors, and exporters will participate in the fair. Visitors will have the opportunity to observe and learn about the latest agricultural technologies, fresh and processed commodities produced in the region, and establish market contacts. The event aims to promote regional agricultural production, including fruit, vegetables and livestock, facilitate the interaction among the different actors in the supply chains, and catalyze the establishment of market linkages with wholesalers and retailers from the main regional markets. The format of the event will enable private sector actors to identify business opportunities, especially in agro-industry.
- iii. **Perennial Horticulture:** The Fruit Marketing Program is progressing rapidly. The consultant and Agribusiness team identified and selected more than 40 groups representing 1,500 farmers. The next steps of the activity will be of the recruitment and training of field technicians to provide technical assistance to farmer groups and facilitate linkages with wholesalers; train farmer groups in post-harvest handling, grades and standards, and in the procurement of packaging materials.




ALP/E short term technical adviser discusses Fruit Marketing situation with Head of Agriculture Faculty, Nangarhar University

- iv. **ERODP:** The Eastern Region Orchards Development Program (ERODP) GPS survey was finalized for 11 districts of Nangarhar and Laghman. Currently, M&E Unit is extracting Orchard polygons and crosschecking them with poppy distribution shown in satellite imagery of 2004. In addition, technical follow-up and assistance was underway during the reporting period. The follow-up focused: a) irrigation, b) pruning, c) branch training, d) weeding and earthing-up, and e) pest control. The later is especially relevant considering the increased risk of aphid infestation due to the onset of the spring.

During the currently planting season, the program achieved the target of 2,156 fruit and nut orchards on 1,517 hectares of land in 11 districts of Nangarhar and Laghman provinces.

ERODP SUMMARY STATISTICS: NUMBER OF BENEFICIARIES, HECTARES OF LAND AND TOTAL NUMBER OF TREES PLANTED BY DISTRICT

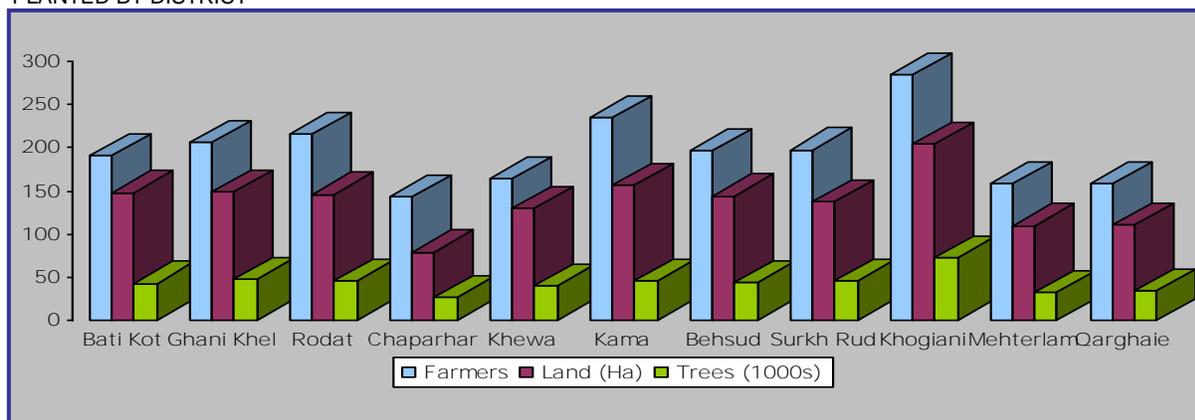

District	Farmers	Land (Ha)	Trees (1000s)
Bati Kot	191	148	43
Ghani Khel	207	149	48
Rodat	216	146	45
Chaparhar	144	79	26
Khewa	165	131	40
Kama	235	156	46
Behsud	197	144	44
Surkh Rud	198	138	45
Khogiani	285	204	72
Mehterlam	159	110	32
Qarghaie	159	112	34
Total	2,156	1,517	475

- v. **Market Information System:** The Agribusiness Team complemented the Market Information System (MIS) by incorporating price information on agricultural inputs (seeds, fertilizers and crop protection products), in addition fruit, vegetables and meats. Data collection began in Nangarhar and will soon extend to Kunar and Laghman, in collaboration with interns from Nangarhar University. The regional MIS is expected to be fully operational in the three provinces by the end of June 2006. ALP/E is currently in discussions with the Eastern Region Business Development Center, so that the latter could become the institutional home of the MIS. *Please refer to the annex-II for the latest market report.*

Other Relevant Activities:

The concept note for the Forestry Incentives for Livelihood Diversification (FieLD) Program was finalized which includes a comprehensive set of activities in support of nursery operators and farmers for establishment of high-density woodlots in the Eastern Region.

Finalized a draft strategy and action plan for annual crops which integrated 3 major programs to provide assistance to survival, surplus and commercial farmers. The drafted document is currently being analyzed by ALP/E senior staff.

Table: ALP/E Infrastructure Projects

AGRIBUSINESS									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	NVDA Olive Pruning	Behsud	Nangarhar	100	100	ALP/E	2/21/2006	3/13/2006	
2	Eastern Region Orchards Development Program	Nangarhar/Laghman	Nangarhar/Laghman	100	100	IF Hope	7/05/2005	2/16/2009	
3	Farmers Training (TOT)	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100	100	ALP/E	1/28/2006	2/9/2006	
4	Traders (Assemblers) Training	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100	100	ALP/E	2/20/2006	2/23/2006	
5	Wholesalers training	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100	100	ALP/E	2/11/2006	2/12/2006	
6	Influenza Training(TOT)	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100	100	ALP/E	3/27/2006	3/28/2006	
7	Radio Program-Farmers Interview	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100	25	ALP/E	2/12/2006	6/15/2006	
8	Establishment of Vegetable Wholesalers Association	Jalalabad	Nangarhar	100	100	ALP/E	2/16/2006	3/12/2006	
9	Orchard Survey	Nangarhar/Laghman	Nangarhar/Laghman	100	100	ALP/E	4/3/2006	4/18/2006	
10	Vegetable Seed and Fertilizer distribution	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100	100	ALP/E	2/23/2006	3/21/2006	

2. INFRASTRUCTURE DEVELOPMENT

The Infrastructure section completed the following activities during the reporting period:

- **Kama Main Road:** Further comments were received from USAID on the Technical Feasibility Reports submitted for clearance. The Technical Feasibility Report and designs are revised considering the comments and traffic count, and will be resubmitted to USAID for clearance.
- **Kama Irrigation System:** A draft overall program for studies, surveys, designs, and construction was prepared. A response to the first Deputy Minister's letter was also drafted for discussion.
- **Goshta Bridge:** The cost for all options for Goshta and Lal Pur bridge construction is being reviewed.
- **Mashina Road:** The Technical Feasibility Report was prepared and submitted with EMS workbook to USAID for approval.
- **Qasam Abad Road Design:** Work continued on detailed design of the road including designing of big washes and would be finished soon.
- **Abuzai Bridge:** Search for a suitable company is ongoing to carry out the geotechnical investigation to confirm the site condition of the proposed project.
- **Engineering Survey Team:** Survey of Sherzad to Hisarak road was successfully completed. Alignment and X-Sections of the road from 19+550 to 24+000 km have been completed. The team returned back to the site to survey the Gandomak Bridge at the start of the road.
- **CTTC Training:** Twenty new trainees were sent to CTTC training during the reporting period. A time table for the training of the next group of students was received by ALP/E for the following dates:

SN	Class	Date
1	Trade classes	May 11, 2006
2	Site engineers class	May 16, 2006
3	Foremen class	May 25, 2006

- **Wholesale Vegetable Market:** Detailed design for the wholesale Market was completed and discussed with the Mayor of Jalalabad. The decision has been made to carry out the construction work under CFW program. The project documents were submitted to USAID for approval.
- **Nangarhar Road Inventory:** The Nangarhar Road Inventory Team collected GPS tracks for the following primary, secondary, tertiary road in the Surkhrud District, Nangarhar Province.

SN	Type of Road tracked	No. of Roads Tracked Coordinates
1	Primary Roads	4
2	Secondary Roads	4
3	Tertiary Roads	67

Table: ALP/E Infrastructure Projects

Infrastructure Projects									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Kama Road	Kama	Nangarhar	90	0	ALP/E	TBD	TBD	
2	Kama Irrigation System	Kama	Nangarhar	0	0	ALP/E	TBD	TBD	
3	Goshta Bridge Scoping Study	Goshta & Lalpur	Nangarhar	100	90	ALP/E	TBD	TBD	
4	Mashina Road	Qargai	Laghman	100	0	ALP/E	TBD	TBD	
5	Alternative Energy	Various	Nangarhar, Laghman, Kunar	50	0	ALP/E	TBD	TBD	
6	Qasam Abad Road Rehabilitation	Behsud	Nangarhar	70	0	ALP/E	TBD	TBD	
7	Under graduate Training	Nangarhar	Nangarhar	100	100	ALP/E	01/21/2006	04/30/2006	
8	CTTC Training	Nangarhar	Nangarhar	100	100	ARD	ongoing	Ongoing	
9	Wholesale vegetable Market	Jalalabad	Nangarhar	100	0	ALP/E	Transferred to CFW	Ongoing	
10	Nangarhar Road Inventory	All Districts	Nangarhar	100	5	GoA	4/15/2006	10/31/2006	

Cash-for-work Projects (CFW):

- Three CFW projects were completed during this period, and work continued on 39 ongoing projects in Laghman, Nangarhar, and Kunar provinces. The daily employment rate was 4,766 workers per day, and 13,039 individual laborers have been employed from June 2005 through May 15th, 2006. Total employment days were recorded as 49,233 and the cumulative total reached 558,011 employment days from June 2005 through May 15th, 2006.

SUMMARY OF CFW PROJECTS BY PROVINCE

SN	Province	Active	Completed
1	Nangarhar	24	5
2	Laghman	9	12
3	Kunar	6	0
Total		39	17

- Laghman Province:** Under the supervision of ALP/E, Relief International (RI) continued to work on eight CFW projects during the reporting period in Laghman. The daily laborers rate in Laghman reached 1,047 workers per day, with a cumulative total of 6,843 individual laborers employed from June 2005 through May 15th, 2006. Employment days during the reporting period were 11,585 and the cumulative total reached 343,801 through May 15th, 2006. Four new projects were approved and will be starting during next reporting period and five new projects are under preparation for USAID approval. During the reporting period, the first 2 km length of Darunta Cobblestone Road was formally inaugurated and opened for public use.

Table: ALP/E CFW Project in Laghman

Cash For Work Projects									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Deh Ziarat Protection Wall	Mehtarlam	Laghman	100	100	RI	09/28/2005	3/15/2006	Completed
2	Karaho Protection Wall	Mehtarlam	Laghman	100	100	RI	12/20/2005	2/23/2006	Completed
3	Terghari Protection Wall	Mehtarlam	Laghman	100	100	RI	10/20/2005	3/29/2006	Completed
4	Mulayan Protection Wall	Mehtarlam	Laghman	100	95	RI	12/28/2005	05/30/2006	
5	Shamngal Canal Rehabilitation	Mehtarlam	Laghman	100	68	RI	2/15/2006	06/28/2006	

Cash For Work Projects									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
6	Hayadarkhani Canal Reconstruction	Mehtarlam	Laghman	100	95	RI	2/8/2006	5/30/2006	
7	Dopi and Longalam Protection Wall	Qarghayi	Laghman	100	100	RI	11/24/2005	2/24/2006	Completed
8	Char Bagh Canal Rehabilitation	Qarghayi	Laghman	100	57	RI	2/23/2006	8/23/2006	
9	Kalakot Canal Rehabilitation	Qarghayi	Laghman	100	52	RI	2/16/2006	8/6/2006	
10	Daronata Road Repair-Section 1, Cobblestone (Daronata Bypass)	Qarghayi	Laghman	100	100	ALP/E	1/25/2006	4/10/2006	Completed
11	Darunta Road Repair (Second Part)	Qarghai	Laghman	100	2	ALP/E	5/13/2006	8/25/2006	
12	Shamshirabad Flood Protection Wall	Qarghayi	Laghman	100	75	RI	3/8/2006	6/8/2006	
13	Khoja Khil Sofla Canal Rehabilitation	Alingar	Laghman	100	100	RI	7/19/2005	11/15/2005	Completed
14	Ghundai Nazar Khil Protection Wall	Alingar	Laghman	100	93	RI	12/19/2005	3/19/2006	
15	Qasaba Protection Wall	Alingar	Laghman	100	100	RI	12/10/2005	3/10/2006	Completed
16	Nolo Protection Wall	Alishing	Laghman	100	100	RI	8/3/2005	11/3/2005	Completed
17	Akhund Sahib protection Wall	Alishang	Laghman	100	100	RI	9/30/2005	12/3/2005	Completed
18	Mustafa Kalay Protection wall	Alishang	Laghman	100	100	RI	6/1/2005	8/31/2005	Completed
19	Jamshidabad Protection Wall	Alishing	Laghman	100	100	RI	6/4/2005	8/31/2005	Completed
20	Jamshidabad Additional Work	Alishing	Laghman	100	100	RI	10/2/2005	1/2/2006	Completed
21	Kanda Canal Rehabilitation	Qarghai	Laghman	100	13	RI	4/26/2006	7/26/2006	

- ii. **Kunar Province:** Work continued on five CFW projects in Kunar province during the reporting period. Work remained suspended on the Dewagal Road in Chawkay District due to security concerns. To date, 899 people are employed with a cumulative total of 28,640 employment days through the 15th of May, 2006..

Table: ALP/E CFW Project in Kunar

Cash For Work Projects									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Seenda Wala Canal Rehabilitation	Nurgal	Kunar	100	87	ALP/E	2/20/2006	5/20/2006	
2	Daag Canal Repair	Khas Kunar	Kunar	100	74	ALP/E	2/21/2006	5/21/2006	
3	Tanar Road Rehabilitation	Khas Kunar	Kunar	100	69	ALP/E	2/21/2006	5/21/2006	
4	Barnarang Road Repair	Narang	Kunar	100	19	ALP/E	4/17/2006	7/17/2006	
5	Sharalow-Badil Road Repair	Narang	Kunar	100	20	ALP/E	4/17/2006	7/17/2006	
6	Dewagal Road Repair	Chawki	Kunar	100	6	ALP/E	4/18/2006	7/18/2006	Suspended

- iii. **Nangarhar Province:** During this period, work started on five new projects, making up a total of 24 CFW projects in progress in Nangarhar during this reporting period. The daily laborers employed during this period were 3,148 workers per day with a cumulative total of 31,206 employment days during the reporting period. Total employment days reached 185,570 through May 15th, 2006. Three new projects


are waiting for USAID approval in Surkhrud and Torghar districts, upgrading the Wholesale Market in Jalalabad is submitted and Rehabilitation of Shahi Canal which flows in Jalalabad city is ready to submit for USAID approval.

Table: ALP/E CFW Project in Nangarhar

Cash For Work Projects									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Jalalabad city Side ditches Cleaning	Jalalabad	Nangarhar	100	100	ALP/E	1/23/2006	3/23/2006	Completed
2	Jalalabad city Side ditches Rehabilitation	Jalalabad	Nangarhar	100	90	ALP/E	12/1/2005	4/1/2006	
3	Shamshapur Road Construction-Section 1, Cobblestone Road	Surkh Rod	Nangarhar	100	100	ALP/E	1/25/2006	4/25/2006	Completed
4	Mana Road Repair	Hisarak	Nangarhar	100	57	ALP/E	3/12/2006	6/30/2006	
5	Shana Zawara Road Repair	Hisarak	Nangarhar	100	45	ALP/E	3/12/2006	6/30/2006	
6	Gandomak Road Repair	Sherzad	Nangarhar	100	55	ALP/E	3/13/2006	6/30/2006	
7	Ashpan Protection Wall	Sherzad	Nangarhar	100	60	ALP/E	3/12/2006	6/30/2006	
8	Toto Road Rehabilitation	Sherzad	Nangarhar	100	48	ALP/E	3/20/2006	6/20/2006	
9	Khawaran Road Rehabilitation	Khoghyiani	Nangarhar	100	44	ALP/E	3/12/2006	6/30/2006	
10	Kalagho Road Rehabilitation	Khoghyiani	Nangarhar	100	40	ALP/E	3/12/2006	6/30/2006	
11	Pekha Protection Wall & Groynes	Achin	Nangarhar	100	100	ALP/E	1/9/2006	3/9/2006	Completed
12	Zara Sultankhil Protection Wall	Muhmandara	Nangarhar	100	95	ALP/E	3/21/2006	4/30/2006	
13	Bar & Kuz Bela Protection wall-I	Goshta	Nangarhar	100	91	ALP/E	12/11/2005	2/11/2006	
14	Bar Bila Flood Protection wall-II	Goshta	Nangarhar	100	100	ALP/E	12/29/2005	3/15/2006	Completed
15	Bela Flood Protection wall(Dikes)	Goshta	Nangarhar	100	100	ALP/E	12/20/2005	4/15/2006	Completed
16	Abdian Road Rehabilitation	Behsud	Nangarhar	100	44	ALP/E	3/12/2006	6/30/2006	
17	Binigah Flood Protection wall	Behsud	Nangarhar	100	45	ALP/E	3/21/2006	4/30/2006	
18	Summerkhil Flood Protection wall	Behsud	Nangarhar	100	100	ALP/E	3/20/2006	5/01/2006	Completed
19	Spin Jumat Flood Protection Wall	Behsud	Nangarhar	100	10	ALP/E	5/1/2006	8/1/2006	
20	Maidanak Road Rehabilitation	Spin Ghar	Nangarhar	100	100	ALP/E	12/18/2005	3/30/2006	Completed
21	Guldaag Emergency protection wall	Lal Pur	Nangarhar	100	85	ALP/E	4/4/2006	7/4/2006	
22	Girdi Ghous Emergency Protection Wall	Lal Pur	Nangarhar	100	30	ALP/E	4/4/2006	7/4/2006	
23	Mahsil and Qasaba Kalay protection wall	Durbaba	Nangarhar	100	20	ALP/E	4/18/2006	5/20/2006	
24	Sasobi Flood protection wall	Durbaba	Nangarhar	100	20	ALP/E	4/19/2006	7/15/2006	
25	Bodiali Reservoir	Kuz Kunar	Nangarhar	100	10	ALP/E	4/26/2006	7/26/2006	
26	Dawlat Zai Canal Rehabilitation	Chaparhar	Nangarhar	100	3	ALP/E	5/6/2006	8/30/2006	
27	Garatak canal Rehabilitation	Chaparhar	Nangarhar	100	5	ALP/E	5/6/2006	7/10/2006	
28	Shamshapor-Daronta Road Repair	Surkhrud	Nangarhar	100	5	ALP/E	5/8/2006	8/8/2006	
29	Shamshapur Cobblestone (Part 2)	Surkhrud	Nangarhar	100	2	ALP/E	5/14/2006	8/14/2006	



A view of Darunta Cobblestone Road Opening Ceremony

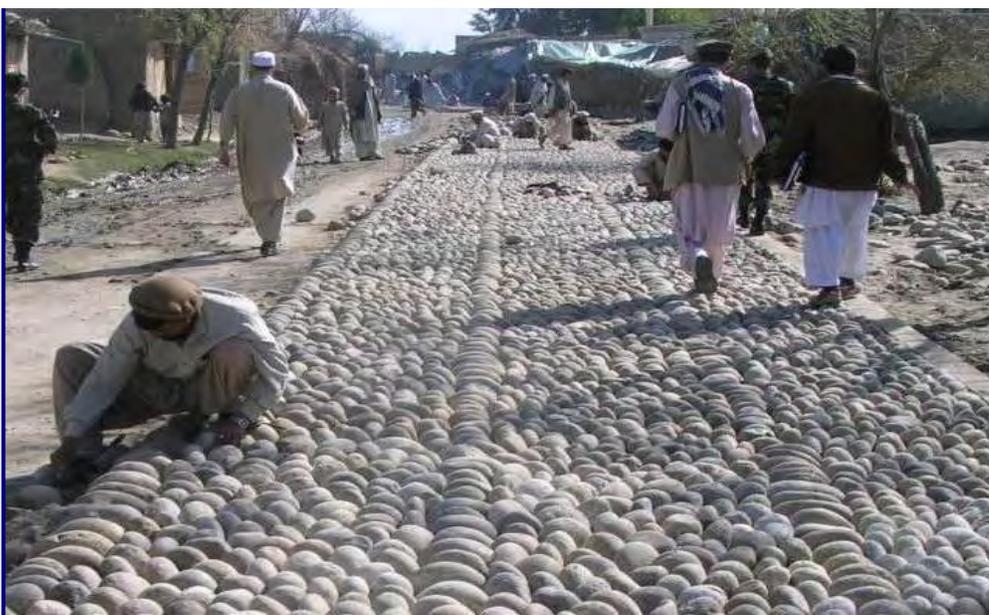

.....After.....



.....Before.....

The ALP/E's innovative cobblestone roads provide public and government with relatively low cost, reduced maintenance, and an effective alternative to the current dirt roads in an exercise that promotes economic development and grassroots democracy in the Eastern Region. With this technology, USAID and ALP/E are putting efforts together to open up economic markets, create improved access to social services, and in the end provide a deeper sense of citizen security toward licit economic development.




Gabion Box Weaving – A part of capacity building on ALP/E CFW project



An ongoing CFW project in Nangarhar

MONTHLY EMPLOYMENT DAYS (IN 1,000s) IN CFW PROJECTS SINCE JUNE 2005

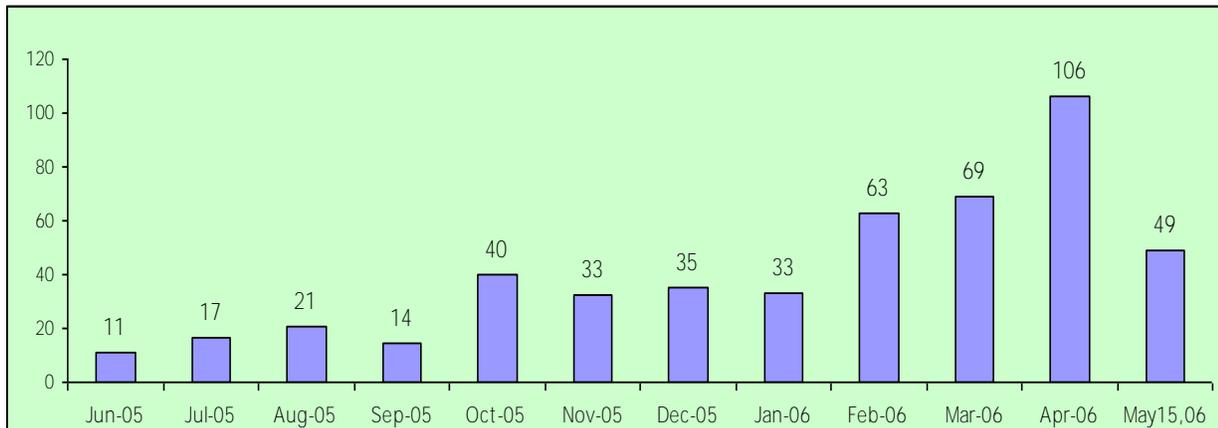

.....Before ALP/E started its work in our district, we had our main road in a very bad condition since decades. I hardly realize anyone including government and NGOs ever tried to repair this road. We have been facing problems in traveling and transporting agricultural produce to the nearest market. With ALP/E road project, I hope we will be able to repair the road ensuring proper and easy traveling and transportation to other parts in and outside the province. I personally thank ALP/E for having a tremendous project road project in our area.

Abdul Marten, 58-years old, Resident of Khas Kunar.

3. PRIVATE SECTOR DEVELOPMENT

- The PSD Unit coordinated with Afghan Women Business Association (AWBA) to assist them in establishing their office in Jalalabad. All required information and documents were shared to proceed with the support. Meanwhile, the PSD Unit prepared a Scope of Work (SOW) for the operation of AWBA.
- Revised the Nangarhar Textile Factories' feasibility report. The report delineates vital information about the history of textile business in Nangarhar. The information presented would be of great importance for the SAFI garment factory in their start up investment and activities in Nangarhar.
- The PSD Unit facilitated the participation of eight potential investors of the Eastern Region in Afghanistan's Investment Support Agency's (AISA) International Investment conference in Kabul. The visit endowed the participating with the opportunity to discuss and coordinate with potential investors and companies, resulting in business development in the region.



ALP/E facilitated the participation of traders and investors from Nangarhar Province in AISA International Investment Conference in Kabul

The PSD Unit held several meetings and discussions with Government, INGOS, potential investors, which are briefed as follow:

- Met with the Director of Nangarhar Olive Oil Factory and discussed the pre-existing problem of olive oil marketing for the factory
- Met with Nangarhar University, Dean of Faculty of Economics to reach on the conclusion of possible cooperation between ALP/E and the University.
- Held meetings with traders of Sabawoon Export and Import Trade Company and discussed the issue of cool storage project. The current status of cold storage project with RAMP is being finalized. Out of 12 entrepreneurs, 6 applications were approved by RAMP project as cost sharing scheme.
- Met with Jerry Turnbull of CNFA to discuss the possibility of their support for some of our planned initiatives in flour mills, dairy, carpets and fruit juice
- Met with Mustafa Kazem of AFC to discuss areas of potential collaboration. AFC is interested in exploring the possibility of assisting PSD priority businesses including SAFI garments.
- Met with Zach Lee of Roots of Peace to discuss their final report with a strong conclusion
- Held discussion with David Frey, COP of GIA to proceed on flour mills planning in the region



ALP/E PSD Unit representative (first from right) in AISA Conference in Kabul

Table: ALP/E Private Sector Development Projects

Private Sector Development									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Business Development Center	Jalalabad	Nangarhar	100	100	ALP/E	4/4/2006	2/7/2009	
2	Training and Internship Program	Jalalabad	Nangarhar	100	100	ALP/E	ongoing	Ongoing	
3	Formation of Business Development Board	Nangarhar	Nangarhar	100	100	ALP/E	4/15/2006	5/15/2006	
4	Edible Oil Sub sector study	Nangarhar	Nangarhar	100	100	ALP/E	12/20/2005	12/31/2005	
5	Technical Machinery Sub sector study	Nangarhar	Nangarhar	100	100	ALP/E	6/1/2006	7/1/2006	
6	Carpet Study	Nangarhar	Nangarhar	100	100	ALP/E	11/3/2005	11/15/2005	
7	Marble Study	Nangarhar	Nangarhar	100	100	ALP/E	10/11/2005	10/20/2005	
8	Feasibility Study for Flour Mills	Nangarhar	Nangarhar	100	100	ALP/E	12/15/2005	11/30/2005	
9	Tomato value chain Analysis	Nangarhar	Nangarhar	100	100	ALP/E	8/2/2005	8/20/2005	
10	Establishing Women Handicraft Center	Nangarhar	Nangarhar	40	0	ALP/E	TBD	TBD	
11	Dry fruits and Nuts Study	Nangarhar	Nangarhar	100	100	ALP/E	11/15/2005	11/30/2005	
12	Dairy Sub sector assessment	Nangarhar	Nangarhar	100	0	ALP/E	01/20/2006	02/10/2005	
13	Poultry sub sector assessment	Nangarhar	Nangarhar	100	100	ALP/E	02/15/2006	02/27/2005	

4. GENDER AND MICRO-ENTERPRISE DEVELOPMENT

- During the reporting period, Gender and Micro-Enterprise Development (GME) Unit completed the formation of 33 Self Help Groups (SHG) in Laghman including approximately 500 women, who have begun their vocational training. The ongoing trainings are effective and greatly appreciated by the participants. The GME Unit continued monitoring the training sessions and provided technical assistance and support as needed. As a result of the ALP/E Micro-enterprise program, the women of the province will be able to promote their home-based businesses enhancing their family incomes.
- The GME Unit finalized collecting GPS data for the Self Help Groups in Laghman while data for the remaining sites in Kunar will be collected soon. In addition, the possibility of conducting value chain studies using GIS was also explored.
- Drafted a SOW for women in Business Survey for the Eastern Region. This survey aims to identify constraints to women in business; develop an approach to address those constraints; and define opportunities to offer support to those businesses. The Unit in close collaboration with Natural Resource Management Unit finalized SOW and contracts for the women-owned forestry nurseries. The procurement of expendable inputs will begin during the next reporting period.
- The GME Unit assisted the implementation of Female Cooks Monitoring on ALP/E's CFW projects in the region. With support from M&E, GME female monitors will interview the female cooks currently working on all ALP/E ongoing projects. As a result of this monitoring effort, the female laborers will have the opportunities to discuss and share their problems with ALP/E personnel.

Table: ALP/E Gender and Micro-Enterprise Projects

GENDER AND MICRO-INTERPRISES									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Training Of Trainers	ER	ER	100	100	ALP/E	2/01/2006	2/28/2006	
2	Establishment of Self Help Groups	Laghman	Laghman	100	100	RI	3/15/2006	3/31/2006	
3	Establishment of Self Help Groups	Kunar	Kunar	100	25	RI	3/15/2006	3/31/2006	



ALP/E: Women are being trained in embroiderya woman receives sheep as of part of her livestock option in Micro-Enterprises Program

4. ADDITIONAL INFORMATION

1. NRM/ENVIRONMENTAL COMPLIANCE

- During the reporting period, NRM/EC cleared 3 EMS workbooks for CFW projects and the Jalalabad Wholesale Vegetable and Fruit Market. Efforts were also undertaken to discuss the arrangements of dealing with solid waste issue and composting toilets and vegetable waste to find a culturally appropriate, commercially viable and environmentally sound solution.
- In coordination with Infrastructure Unit, Shahee Canal (one of the key canal's running through Jalalabad city) was visited and a public health awareness action plan was finalized to encourage people not to dump their rubbish in canal. The plan focuses on public participation in the long-term canal maintenance and the promotion of health and hygiene amongst the citizens living adjacent to the canal. In addition, efforts are underway to collaborate with Environmental Protection Agency on this public awareness campaign along with NGOs or health care providers to assist with community based health education training.
- The first part of a series of five trainings on commercial trees sapling production was completed. Thirty men were trained who will be contracted for tree production. The series will end in November/December and conclude with preparation for out planting and sales.
- Followed up with women trained in nursery establishment to provide additional one-on-one technical assistance on site including. In addition, various aspects of contracts with women including governance, procedure of work, and payment were discussed.
- Completed the concept note for the Forest Incentives for Livelihood Diversification (FleLD) program. Activities will target medium sized landholders to establish on-farm woodlots for firewood, house timbers and pole wood for sale at a commercial level. This is a 3 year program and will target 1,000 landholders. An RFP is being drafted to solicit bids from third parties to implement the program.
- Completed the design for the Smallholder Livestock Management Program. ALP/E are working with professors from Nangarhar University to design a training of trainers manual and a field manual for a site based training program on improving livestock productivity. ALP/E is posting a job announcement to hire four female trainers based in ALP/E provinces to lead this training targeting women who own and/or care for 1-5 head of livestock. Training will focus on health care and management to increase productivity.



ALP/E's Nursery trainer provides technical assistance in grafting practices



ALP/E's NRM Specialist provides hands on technical training in nursery management

Table: ALP/E NRM Projects

NATURAL RESOURCES MANAGEMENT									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
1	Smallholder Livestock Management Program	Village based Self Help Groups	Nangarhar, Laghman, Kunar	100	10	ALP/E	5/1/2005	5/1/2007	NRM assists Ag Unit to implement
2	Training for Commercial Nursery Owners	Besud, Assadabad, Meterlahm	Nangarhar, Laghman	100	20%	ALP/E	5/1/2006	12/30/2006	
3	Training for Female Nursery Owners	Behsud, Surkh Road, Qarghai	Nangarhar, Laghman	100	30%	ALP/E with RI	4/1/2006	12/30/2006	
4	Forest Incentives for Livelihoods Diversification (FieLD)	TBD	Nangarhar, Laghman, Kunar	80	5%	ALP/E	5/1/2006	12/30/2007	

2. SECURITY

- The security situations in the Eastern Region throughout the reporting period remained relatively tense with some incidents in Nangarhar, Kunar, and Laghman provinces. Situation is assessed volatile in some parts of Kunar province while a massive CF air and ground operation started in Kunar province by the name of Mountain Lion. ALP/E suspended three projects in Khas Kunar and Chowkai districts of Kunar province, due to the security concerns, information and latest incidents. The ALP/E Security Unit is monitoring closely the situation in the region to advise the senior management accordingly.
- With the ongoing summer season, more insurgents' infiltration and attacks within region are expected. Credible reports suggest that Taliban/Al Qaeda networks are orchestrating and planning to increase insurgent activities in the Eastern Region. These groups have been tasked to conduct violent acts including: abductions of internationals, robbery of civilian homes, attacks against newly appointed governmental officials and IED/Suicide Attacks within the city. As a result of current situation in the region, ALP/E International Staff are reduced to urgent needs only

3. MONITORING AND EVALUATION

- The ALP/E M&E Unit continued to monitor active and completed CFW projects in the region. The findings and recommendations were shared and followed-up with Infrastructure Unit. The Unit also facilitated monitoring female cooks on all ongoing CFW projects in collaboration with GME. The monitoring missions focused on; 1) Physical progress, assessing whether planned physical progress was achieved in term of length, width. 2) Financial disbursements, laborers working on Cash-for-Work projects were directly interviewed to know whether they have paid for what they have worked. Project financial data submitted to ALP finance section were cross checked with laborers attendance sheets and pay rolls and 3) Persons Employed and Employment Days, individual laborers on each group were counted on spot to cross check their physical attendance with the reported one.
- GeoBase Update: The GeoBase was updated for 35 active and completed Cash-for-work, orchards, pruning, and agricultural training projects. Due to problem in database, M&E section couldn't fill in the required fields directly, but prepared the sets of data in MS Excel and sent out to Kabul for entry.
- M&E GIS component continued working on identifying ALP/E intervention sites and possible buffer zones for village monitoring. Significant progress was made to download, clean, integrate, analyze ERODP GPS Survey data. Work also continued with Nangarhar Road Inventory Team to keep track of standard data collection, downloading, and cleaning field GPS data.

4. ADMINISTRATION

- The Administration Unit provided training to the local drivers of rules and regulation in ALP/E. The training focused on safe driving, IED check for the vehicles, parking rules within the office, city and project sites, driving speed limit within and outside cities, convoy procedures, response to accidents and incidents, reporting incidents, and dealing and behaving with the local authorities (particularly traffic police).
- Two new positions for Survey Engineers and one post of Marketing Development Specialist were announced. In addition, two new trainees were introduced to CTTC training program in different fields of construction. The administration also facilitated the construction of three rooms in Public Works Department as part of collaboration with government in the field of infrastructure and surveys.

Table - Short term Technical Assistance

No	Name	Title	Activity	Status
1	Cliff Barton	Advisor – Business Development Center	Preparatory Work on Formation of Business Services Center	Completed
2	Gary Baltzer	Activity Manager -APMS	Design and Implementation of APMS Program	Ongoing
3	Kirsten Spainhower	NRM Manager	Environmental Assessments and compliance	Ongoing
4	Jan Chromecek Peter Nehasil Mark Brett	Goshta Bridge Advisors	Survey of Goshta Bridge	Ongoing
5	Danilo Benavides	Technical Advisor (perennial Horticulture)	Identifying Production Centers for 6 target crops	ongoing
6.	Alia Afshar	Project Associate	Providing Support in operations and finance	Ongoing

ALP/E CONTACT INFORMATION

Organization: Development Alternatives, Inc. (Nangarhar Office)
Address: Jalalabad, Nangarhar, Afghanistan
Name: Jonathan Greenham, COP
Afghanistan cell: 0798-039432
"jonathan_greenham@dai.com"

Organization: Development Alternatives, Inc. (Home Office)
Address: 7250 Woodmont Avenue, Suite 200
Telephone: (301) 718-8699
Fax : (301) 718-7968
Web site : www.dai.com

Annex-I: Summary Table of APMS Activities

District/Province	Beneficiary Selection		Fertilizer Distributed		Seed Distributed in Kgs				
	No of Farmers Supported	Land supported in Hectares	Urea in MT	DAP in MT	Tomato	Okra	Eggplant	Cucumber	Watermelon
Khogyani	3,958	475	118.75	59.38	475	7,125	475	0	0
Shirzad	3,958	475	118.75	59.38	475	7,125	475	0	0
Hisarak	3,958	475	118.75	59.38	475	7,125	475	0	0
Pachir Wa Agam	3,958	475	118.75	59.38	475	7,125	475	0	0
Behsud	3,958	475	118.75	59.38	475	7,125	475	0	0
Surkh Rod	3,958	475	118.75	59.38	475	7,125	475	0	0
Kama	3,958	475	118.75	59.38	475	7,125	475	0	0
Rodat	4,750	475	118.75	59.38	475	7,125	475	0	0
Kuz Kunar	4,750	475	118.75	59.38	475	7,125	475	0	0
Shinwar	4,750	475	118.75	59.38	475	7,125	475	0	0
Bati Lot	6,250	775	193.75	96.88	475	7,125	475	0	750
Chaparhar	4,750	475	118.75	59.38	475	7,125	475	0	0
Nangarhar Sub-total	52,956	6,000	1,500	750	5,700	85,500	5,700	0	750
Qarghai	12,500	1,250	312.50	156.25	350	7,500	0	500	375
Mehtarlam	12,500	1,250	312.50	156.25	350	7,500	0	500	375
Laghman Sub-total	25,000	2,500	625.00	312.50	700	15,000	0	1,000	750
Asad Abad	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Khas Kunar	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Chawkay	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Narang	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Nurgal	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Sirkanay	2,500	250	62.50	31.25	100	1,249	66.66	0	0
Kunar Sub-total	15,000	1,500	375.00	187.5	600	7,494	399.96	0	0
Grand-Total	92,956	10,000	2,500	1,250	7,000	107,994	6,100	1,000	1,500

Annex –II: ALP/E Market Information System products

Product	Grade(Units/Kg)	Variety/Origin	Price Week 2 May, 2006		
			Rs/Char k	Rs/Kg	Afg/Kg
Fruits					
Apple	5 - 6	Marling(Afg)	130	74	61
	5 - 6	Yellow(Afg - Pak)	85	49	40
	7 - 9	Marling(Afg)	100	57	47
	7 - 9	Yellow(Afg - Pak)	70	40	33
	10 - 11	Marling(Afg)	70	40	33
	10 - 11	Yellow(Afg - Pak)	50	29	23
Banana	Large	Pak	100	57	47
	Medium	Pak	85	49	40
	Small	Pak	80	46	37
Sweet Orange	5 - 6	Pak	40	23	19
	7 - 8	Pak	50	29	23
	9 - 11	Pak	40	23	19
Sugarcane	Large	Afg	40	23	19
	Medium	Afg	30	17	14
	Small	Afg	30	17	14
Vegetables					
Tomato	Large	Pak	30	17	14
	Medium	Gala(Pak)	30	17	14
Potato	Medium	Pak	30	17	14
	Small	Pak	25	14	12
Onion	Large	Pak	25	14	12
	Medium	Pak	20	11	9
Bean	Medium	Afg	40	23	19
Yam	Medium	Afg	25	14	12
	Small	Afg	20	11	9
Product					
Grade(Units/Kg)			Price Week 2 May, 2006		
Eggplant	Medium	Pak	35	20	16
	Small	Afg	15	9	7
Spinach	Medium	Local(Afg)	25	14	12
Garlic	Medium	China	60	34	28
Pepper	Medium	Pak	120	69	56
Leek	Medium	Afg	20	11	9
Okra	Medium	Pak	40	23	19
	Small	Pak	45	26	21
Marrow	Large	Afg	12	7	6
Parsnip	Medium	Afg	25	14	12
Lettuce	Medium	Afg	35	20	16
Meat					
Live Chicken	Medium	Broiler	250	143	117
Frozen Chicken	Kg	Frozen(Iran)	190	109	89
Mutton	Kg	Pak	420	240	197
Fish	Charik	Silver(Pak)	350	200	164
	Charik	Lawa(Pak)	350	200	164
	Charik	Domestic(Afg)	350	200	164
Beef	Kg	Pak	245	140	115

Annex –III: Person Employed, Employment Days, and Wages Paid on ALP/E CFW Projects

Province	District	Project Name	Project No	Person Employed			Employment Days			Waged Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Kunar	Chawkay	Dewagal Road Repair	CFW101303	38	12	150	926	55	981	3,704	220	3,924
Kunar	Khas Kunar	Shankar Canal Repair	CFW101501	181	14	195	7,412	566	7,978	27,992	2,264	30,256
Kunar	Khas Kunar	Tanar Road Rehabilitation	CFW101502	84	6	90	3,735	276	4,011	14,098	1,104	15,202
Kunar	Narang	Bar Narang Road Improvement	CFW101203	182	16	198	4,151	362	4,513	16,604	1,448	18,052
Kunar	Narang	Sharalo Badil Road Rehabilitation	CFW101204	141	12	153	3,331	276	3,607	13,324	1,104	14,428
Kunar	Nurgal	Seenda Wala Canal Rehabilitation	CFW101402	105	8	113	7,011	539	7,550	26,648	2,156	28,804
Sub-total Kunar Province				831	68	899	26,566	2,074	28,640	102,370	8,296	110,666
Laghman	Alingar	Ghundai Nazar Khil Protection Wall	CFW090302	211	8	219	17,462	2,572	20,034	64,657	9,446	74,103
Laghman	Alingar	Khoja Khil Sofla Canal Rehabilitation	CFW090301	1,329	38	1,367	11,100	408	11,508	52,597	1,596	54,193
Laghman	Alingar	Qasaba Protection Wall	CFW090303	201	7	208	15,437	2,405	17,842	59,090	10,061	69,151
Laghman	Alishing	Akhund Sahib Protection Wall	CFW090704	360	9	369	24,352	482	24,834	95,600	1,928	97,528
Laghman	Alishing	Jamshdabad Additional Work	CFW090702B	186	5	191	12,636	324	12,960	49,228	1,296	50,524
Laghman	Alishing	Jamshidabad Protection Wall	CFW090702A	450	4	454	21,566	164	21,730	75,883	656	76,539
Laghman	Alishing	Mustafa Kalay Protection Wall	CFW090703	500	18	518	17,082	565	17,647	60,917	2,260	63,177
Laghman	Alishing	Nolo Protection Wall	CFW090701	399	7	406	24,345	381	24,726	90,552	1,524	92,076
Laghman	Mehtarlam	Deh Zairat Protection Wall	CFW090101	525	10	535	37,920	693	38,613	143,053	2,773	145,826
Laghman	Mehtarlam	Hayadarkhani Canal Rehabilitation	CFW090106	117	4	121	4,753	151	4,904	19,425	604	20,029
Laghman	Mehtarlam	Karaho Protection Wall	CFW090102	209	4	213	13,744	155	13,899	115,181	1,557	116,738
Laghman	Mehtarlam	Mulayano Kalay Protection Wall	CFW090104	369	12	381	27,222	918	28,140	99,279	3,540	102,819
Laghman	Mehtarlam	Shamangal Canal Rehabilitation	CFW090105	168	7	175	9,251	367	9,618	35,703	1,444	37,147
Laghman	Mehtarlam	Terkaray Protection Wall	CFW090103	331	8	339	28,043	665	28,708	109,403	2,644	112,047
Laghman	Qarghayi	Char Bagh Canal Rehabilitation	CFW090202	133	5	138	6,503	266	6,769	24,172	1,048	25,220
Laghman	Qarghayi	Daronata Road Repair (Darunta Bypass)	CFW090204	226	2	228	11,346	86	11,432	42,404	344	42,748
Laghman	Qarghayi	Darunta Bypass Cobble Stone Road Second Reach	CFW090209	20	2	22	59	6	65	236	24	260
Laghman	Qarghayi	Dopi and Longalam Protection Wall	CFW090201	301	13	314	21,544	823	22,367	78,287	3,124	81,411
Laghman	Qarghayi	Kalakot Canal Rehabilitation	CFW090203	159	6	165	7,957	280	8,237	27,116	1,076	28,192
Laghman	Qarghayi	Kanda Canal Rehabilitation	CFW090208	52	2	54	809	22	831	2,837	88	2,925

Province	District	Project Name	Project No	Person Employed			Employment Days			Waged Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Laghman	Qarghayi	Shamshirabad Flood Protection Wall	CFW090205	412	14	426	18,160	777	18,937	66,636	2,644	69,280
Sub-total Laghman Province				6,658	185	6,843	331,291	12,510	343,801	1,312,256	49,677	1,361,933
Nangarhar	Achin	Pekha Protection Wall & Groynes	CFW081002	461	-	461	24,539	-	24,539	89,680	-	89,680
Nangarhar	Behsud	Abdian Road Rehabilitation	CFW082101	185	-	185	4,898	-	4,898	18,617	-	18,617
Nangarhar	Behsud	Binigah Flood Protection Wall	CFW082102	78	6	84	2,216	76	2,292	8,705	304	9,009
Nangarhar	Behsud	Sammarkhil Flood Protection Wall	CFW082103	207	17	224	6,312	561	6,873	24,863	2,244	27,107
Nangarhar	Behsud	Spin Jumat Embankment	CFW082104	51	4	55	474	40	514	1,896	160	2,056
Nangarhar	Chaparhar	Daulat Zai Intake	CFW080601	72	6	78	504	47	551	2,016	188	2,204
Nangarhar	Chaparhar	Garatic and Chardahi Canal Intakes	CFW080602	79	6	85	676	48	724	2,704	192	2,896
Nangarhar	Dur Baba	Mahsil and Qasaba Kalay Irrigation Reservoir and Erosion Protection	CFW081201	141	2	143	2,095	8	2,103	8,380	32	8,412
Nangarhar	Dur Baba	Sasobi Irrigation Reservoir and Flood Protection Wall	CFW081202	163	8	171	2,886	24	2,910	11,544	96	11,640
Nangarhar	Goshta	Bar & Kuz Bela Protection wall	CFW081601	244	18	262	11,331	1,022	12,353	42,705	4,088	46,793
Nangarhar	Goshta	Bar Bila Flood Protection wall	CFW081602	90	8	98	2,549	197	2,746	15,736	788	16,524
Nangarhar	Goshta	Bila Flood Protection wall(Dikes)	CFW081603	89	6	95	4,948	335	5,283	18,399	1,340	19,739
Nangarhar	Hisarak	Hesarak Road Repair	CFW080301	286	26	312	13,451	1,208	14,659	52,632	4,832	57,464
Nangarhar	Hisarak	Shana Zawara Road Repair	CFW080302	93	7	100	4,410	298	4,708	17,232	1,192	18,424
Nangarhar	Jalalabad	Jalalabad city Side ditches Cleaning	CFW080101	63	-	63	2,622	-	2,622	9,363	-	9,363
Nangarhar	Jalalabad	Jalalabad city Side ditches Rehabilitation	CFW080102	540	-	540	20,530	-	20,530	75,624	-	75,624
Nangarhar	Khogyani	Kalagho Road Rehabilitation	CFW080502	106	9	115	4,688	408	5,096	18,331	1,632	19,963
Nangarhar	Khogyani	Khawaran Road Rehabilitation	CFW080501	139	11	150	5,353	407	5,760	20,880	1,628	22,508
Nangarhar	Kuz Kunar	Bodiali and soraj Irrigation Rehabilitation	CFW081902	98	9	107	1,502	120	1,622	6,008	480	6,488
Nangarhar	Lal Pur	Guldag Flood Protection Wall	CFW081502	163	13	176	2,806	195	3,001	11,224	780	12,004
Nangarhar	Muhmand Dara	Girdi Ghos Protection Wall	CFW081403	82	3	85	1,455	61	1,516	5,820	244	6,064
Nangarhar	Muhmand Dara	Zara Sultankhil Protection Wall	CFW081402	67	-	67	2,216	-	2,216	8,728	-	8,728
Nangarhar	Sherzad	Ashpan Protection Wall	CFW080403	203	18	221	8,335	761	9,096	32,913	3,044	35,957
Nangarhar	Sherzad	Gandomak Road Repair	CFW080401	152	14	166	5,678	484	6,162	22,484	1,936	24,420
Nangarhar	Sherzad	Toto Road Rehabilitation	CFW080402	122	8	130	5,115	361	5,476	19,988	1,444	21,432
Nangarhar	Spin Ghar	Maidanak Road Rehabilitation	CFW082301	465	-	465	16,857	-	16,857	61,271	-	61,271

Province	District	Project Name	Project No	Person Employed			Employment Days			Waged Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Nangarhar	Surkh Rod	Shamshapur Cobble Stone Road (Part2)	CFW080206	90	-	90	187	-	187	748	-	748
Nangarhar	Surkh Rod	Shamshapur Darunta Road Improvement	CFW080205	160	-	160	652	-	652	2,608	-	2,608
Nangarhar	Surkh Rod	Shamshapur Road Construction	CFW080201	393	16	409	18,773	851	19,624	71,332	3,404	74,736
Sub-total Nangarhar Province				5,082	215	5,297	178,058	7,512	185,570	682,430	30,048	712,478
Grand Total				12,571	468	13,039	535,915	22,096	558,011	2,097,056	88,021	2,185,077
