



Biweekly Report

October 1-15, 2006

ALTERNATIVE LIVELIHOODS
PROGRAM - EASTERN REGION



Disadvantaged women nominated by the Department of Women's Affairs to work at the Jalalabad Wholesale Market cash-for-work construction site

ALP/E General Information

Project	Alternative Livelihoods Program – Eastern Region
Start Date	15 February, 2005 (contract signing)
End Date	14 February, 2009
Contract Number	Contract Number GS-10F-0359M
Order Number	Order Number 306-M-00-05-00515-00
Cognizant Technical Officer	Brian Bacon
Contracting Officer	Margaret Kline
Geographic Coverage	Nangarhar, Laghman, Kunar and Nuristan Provinces

ALP/E'S MISSION STATEMENT

The overall objective of ALP/E is to accelerate broad-based, sustainable economic development in the Eastern Region, providing the population with licit livelihood options, and contributing to the elimination of poppy production as an economic element. This will be accomplished by working with the public and private sectors to increase the competitiveness and diversity of regional agricultural and non-agricultural sub-sectors; improving access to markets, inputs and business services; consolidating the presence of supportive public and productive infrastructure; building public and private sector capacity to function in a competitive and transparent economy; and addressing the needs of populations that are heavily reliant on the poppy economy.



EXECUTIVE SUMMARY

Highlights of ALP/E activities and achievements during this reporting period:

- ALP/E's Wheat Seed and Fertilizer Distribution Program completed the voucher redemption process in Nuristan. About 75% of the beneficiaries in Kunar province have also received the vouchers, with the participation of government officials, community leaders and farmers.
- The Vegetable Marketing Program was recently launched integrating several activities along the vegetable supply chains, from seedling production to end markets for high-value vegetables in Afghanistan and abroad.
- The Fruit Marketing Program is beginning a new phase of implementation; promoting the establishment of a Regional Fruit Producers Association and facilitating the adoption of a basic Regional Quality Standard. The latter is expected to substantially improve the competitiveness of the fruit produced in the eastern region.
- Evaluation of the 23 bids received for the Kama Road Improvement Project continued during the reporting period. Two clarification meetings were held with a potential contractor and final negotiations were discussed.
- The construction work on Mashina Road in Qarghai district by the contractor HADF is progressing satisfactorily. Site testing of concrete and road compaction began, and increased quality has been observed.
- The technical feasibility report for Qasimabad Road was submitted to USAID on September 20, and once final approval is granted implementation through competitive bidding will proceed.
- The Construction Trades Training Center (CTTC) group of 41 ALP/E supported tradesmen continued their 30-day course in trade skills at the CTTC, while courses in cobblestone road construction also continued. A total of 260 skilled workers and 43 Engineers and Technicians have been trained in cobblestone road technology to date.
- Cash-For-Work (CFW) activities:
 - **Nangarhar Province:** Twenty one CFW projects are underway with a cumulative total of 492,236 employment days.
 - **Laghman Province:** Sixteen CFW projects underway with a cumulative total of 491,358 employment days.
 - **Kunar Province:** Seven CFW projects underway with a cumulative total of 141,227 employment days.
 - **Nuristan Province:** One CFW Cobblestone road project underway with a cumulative total of 1,819 employment days.
- The Business Development Center (BDC) Strategic Planning Workshop convened to plan future events and examine opportunities for the BDC. The workshop was held on Saturday October 7, in the ALP/2 conference room. The 18 participants of the workshop included BDC staff, board members, and directors of partner organizations (AISA, AFC, AWBA, ACCI and NIA).
- The data from the ALP/E informal tax survey was analyzed and discussed with the Provincial Finance Department and Nangarhar Customs House to compare data and to make an effective comparison between the actual tax and the current tax being charged at the road check points. The findings should help decrease informal taxes being levied on businesses transporting their products through the eastern region.
- The Gender and Micro-Enterprise (GME) staff presented an overview of the Eastern Region Directorate of Women's Affairs Capacity Building plan to H.E. Bono Zagarfan, Minister of Women's Affairs. The Minister was pleased with the plan and is looking forward to visiting the ALP/E programs in the eastern region soon.
- The GME program aired its first radio program on Saturday, October 1, 2006. Self Help Groups (SHGs) will be informed about the weekly radio schedule and members will be encouraged to listen and discuss topics of interest during their weekly meetings. The main objectives of the radio program are to introduce the GME program, motivate women to achieve economic access and inform women about existing business support programs in the eastern region.
- GME in collaboration with the Infrastructure Unit trained 10 female daily laborers to make metal strips for the Jalalabad Wholesale Market.

SECTOR ACTIVITIES

A description of the activities and achievements of the ALP/E programs during the reporting period:


I. AGRIBUSINESS

I.1 2006 Wheat Seed and Fertilizer Distribution Program (WSP)

During the reporting period the WSP completed the distribution of wheat seed and fertilizer to beneficiaries in Nuristan and made substantial progress in Northern Kunar, distributing over 13,000 input packages. The distribution was led by ALP/E staff, district representatives of the Ministry of Agriculture, representatives of the District Governors and Shura members. Despite the obvious logistic challenges of delivering large quantities of seed and fertilizer to Nuristan and Northern Kunar, including security and transportation, the entire process has been implemented according to schedule.



Wheat seed and fertilizer distribution in Northern Kunar

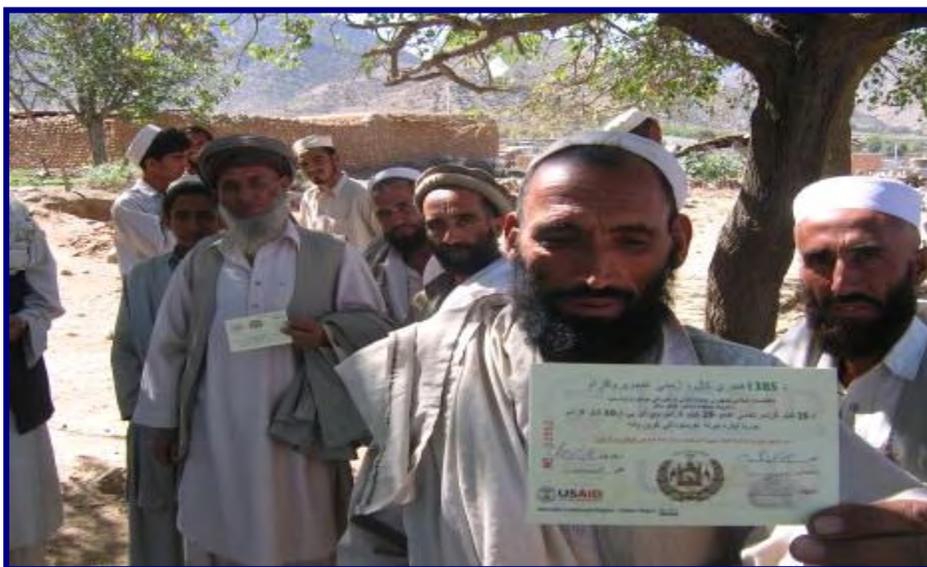


Farmers displaying ALP/E voucher for seed and fertilizer for one jerib

The WSP is covering vulnerable villages that typically are neglected, where the population may be encouraged to grow poppy by dealers; these areas are high risk due to a lack of security and a history of poppy production, which are increasingly correlated. ALP/E prioritized target districts based on planting data from UNODC as a way to maximize impact of this alternative. Following the selection of districts, district-level representatives of the Ministry of Agriculture, District Governors and District Shuras selected the target villages to be served, based on a series of—poppy production related—criteria provided by ALP/E.

Once at the villages, Community Development Committees, local authorities and representatives of farmers selected the program beneficiaries. ALP/E monitors have been involved throughout the entire process, from selection of districts to identification of individual beneficiaries; thereby ensuring accountability at all levels. One of the tasks of ALP/E's monitors has been to raise awareness of the fact that rural communities face increased responsibility in their commitment not to grow poppy, emphasizing that individual farmer's inability to comply will impact on the entire community when the village is excluded from future programs and ALP/E cooperation.

The map below shows the coverage and the dimension of the program, which is serving up to 70,000 farmers. The main objective of this pro-active program is to provide farmers with a licit alternative to poppy, supporting them in achieving food self-reliance, and reducing their likelihood of accepting loans for poppy at planting time.

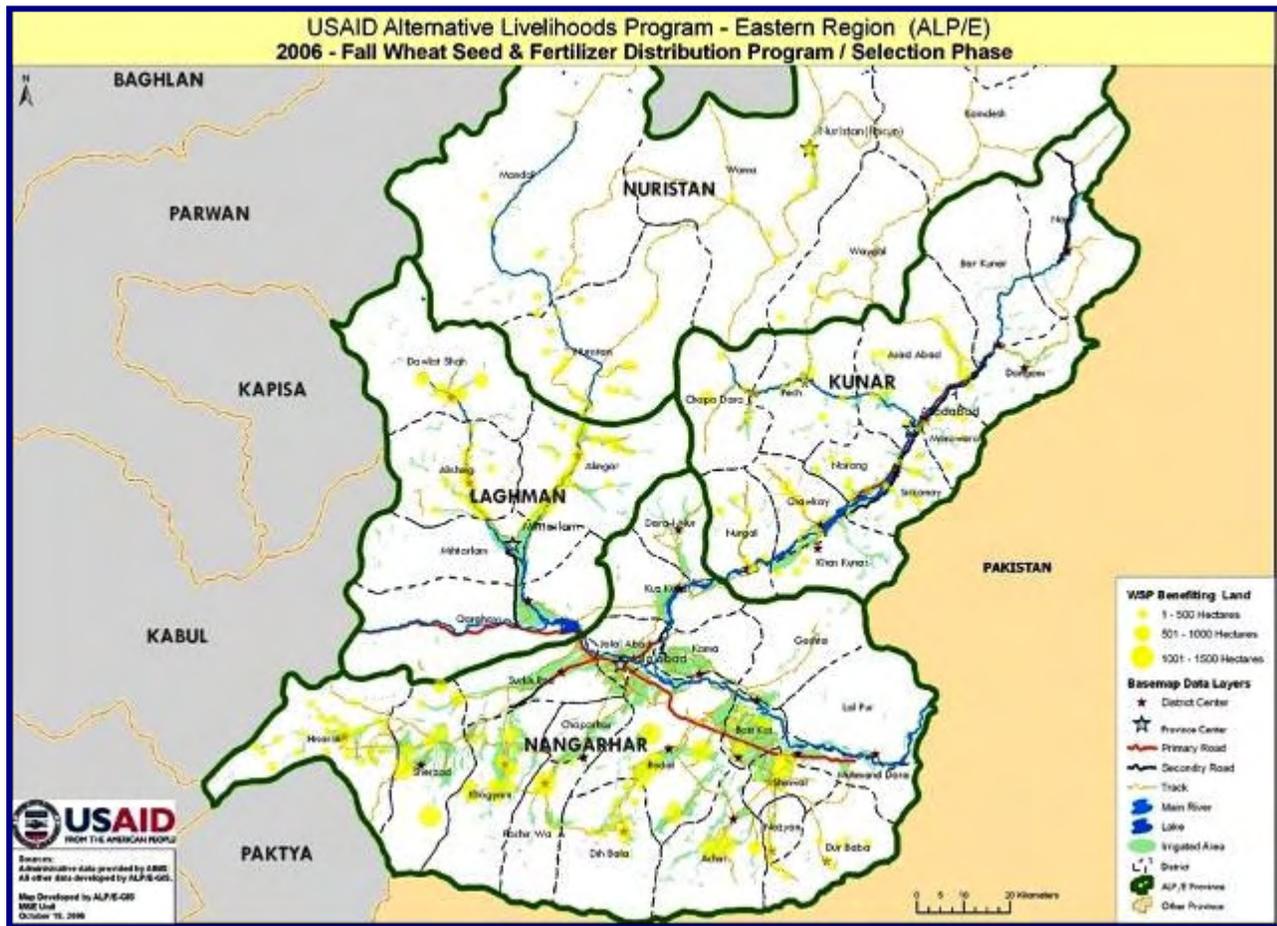


WSP Distribution Map

The villages have been chosen in locations that are possibly considering poppy cultivation this season. The distribution does a number of things, it provides a viable alternative at planting time, it allows the GOA to point out the concrete benefits of not growing poppy, it expands the project activities into the more inaccessible areas, and serves as an entry point to the community for expanded programs subsequently. The program was originally planned for 80,000 farmers, though due to a procurement shortage from the supplier IFDC, the number of program beneficiaries will likely need to be reduced.

1.2 Vegetable Marketing Program (VMP)

ALP/E recently brought it a short term expert to lead the launch of the VMP activities for the current season. The size of the program was constrained due to a delay in the approval for procurement of seeds. Nonetheless, the VMP focused on structuring the value chain for fresh vegetables linking male and female farmers with wholesalers and high-end markets in Kabul and Dubai. Thirty women entrepreneurs are currently producing plug seedlings for high-value vegetables, which will be used by ALP/E commercial demonstration farms and male and female farmers devoted to winter production. The VMP team has also facilitated linkages between farmer groups and vegetable wholesalers, who are being supported through the provision of access to cold storage and packing facilities recently renovated by the project.

ALP/E is also facilitating sales of high-value vegetables to hotels and restaurants in Kabul, and will soon support leading traders to export high-value crops to Dubai. The process—depicted below—is consistent with ALP/E’s Value Chain Approach, providing support to the different actors participating in vegetable production and marketing; ensuring that each of them has the technical and managerial capacity to meet market requirements.

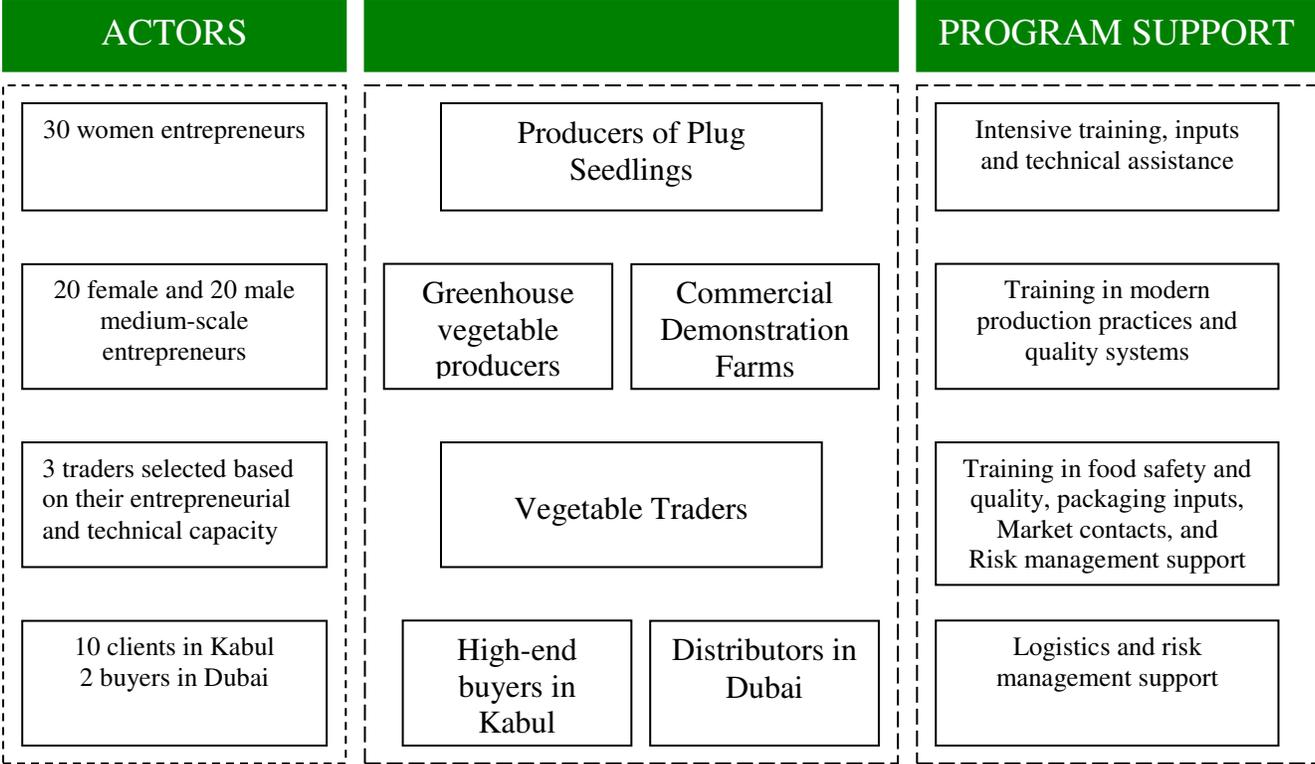

ALP/E’s VMP, in partnership with Peace Dividend Trust is currently organizing an exhibition of high-value fruit and vegetables from the eastern region. The event, which will take place in Kabul, in February 2007, will promote the finest produce from the region and will bring together the hospitality industry and institutional buyers from Afghanistan’s capital.

As a complement to this program, ALP/E has recently issued a request for proposals (RFP) for its Innovations for Market-Led Economic Rehabilitation (TIMER) Program. This program will serve the needs for 15,000 smallholder farmers, providing them with access to modern crop production technologies, including access to seeds of short-cycle hybrid vegetables, modern production practices and market linkages. The launch of ALP/E’s Regional Vegetable Marketing Program (REVAMP) has been postponed until spring 2007, due to a failure to procure the right kinds of seeds on time to meet program needs.

1.3. Fruit Marketing Program

ALP/E’s FMP has entered a new stage of implementation; facilitating the establishment of a Regional Fruit Producers Association, a joint effort of the program’s Agribusiness and Institutional Capacity Development Teams. Four thousand farmers are currently being organized in district-level committees, whose representatives will form

the Regional Assembly. At the same time, the Fruit Marketing Team is preparing for the citrus harvest, which is expected to result in about 800MT of sales in a period of over a month. (See label below)



Recognizing the need for the adoption of strict grades and standards as a mechanism to improve the competitiveness of the regional fruit industry, ALP/E is currently assisting a group of leading traders and farmers to design a basic system of standards for fruit. The standard, which will soon be expanded to cover vegetable crops will be managed by the Standard Administration Commission; composed of producer and wholesaler associations, a representative of AISA and the Ministry of Agriculture, and housed at the Eastern Region Business Development Center. The proposed “industry-wide standard” will constitute the basis for the establishment of a certification program, seeking to build the region’s reputation as high-end fruit and vegetable producers.

Economic Development Projects

Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
			Design	Execution				
Eastern Region Orchards Development Program (ERODP)	10 districts	Nangarhar/Laghman	100%	50%	IF Hope	5-Jul-05	July-08	Ongoing
Ag. Extension Radio Program	All districts	Nangarhar/Laghman /Kunar	100%	50%	ALP/E	12-Feb-06	June-07	Ongoing
Smallholder Livestock Development Program	Village based Self Help Groups	Nangarhar/Laghman /Kunar	100%	50%	ALP/E	1-Aug-06	May-07	Ongoing
Training for Commercial Nursery Owners	Behsud, Asadabad, Mehtarlam	Nangarhar/Laghman	100%	90%	ALP/E	1-May-06	Dec-06	Ongoing
Training for Female Nursery Owners	Behsud, Surkh Rod, Qarghayi	Nangarhar/Laghman	100%	80%	ALP/E with RI	1-Apr-06	Dec-06	Ongoing
Adaptive Research Technology Dissemination and Development of Seed Supply Systems	17 districts of Eastern Region	Nangarhar/Laghman /Kunar	100%	2%	ICARDA	Oct 06	Dec 08	Subcontract Signed
Input Supply Support Program	20 districts of Eastern Region	Nangarhar/Laghman /Kunar	100%	97%	ALP/E	Sep 05	Oct 06	On going
Market Information System	Throughout Eastern Region	Nangarhar/Laghman /Kunar	100%	30%	ALP/E&DoA	Mar 06	Dec 08	Ongoing
Fruit Marketing Program	15 districts of Eastern Region	Nangarhar/Laghman /Kunar	100%	20%	ALP/E	May 06	Dec 08	Ongoing
Eastern Region Annual Crops Initiative	Eastern Region	Nangarhar/Laghman /Kunar	100%	3%	ALP/E	Jul 06	Dec 08	Ongoing
Eastern Region Commercial Livestock Development Program	Eastern Region	Nangarhar/Laghman /Kunar	90%	4%	ALP/E	Jun 06	Dec 08	Ongoing
Fall Wheat Program (2006)	Selected villages in all four Provinces	Nangarhar/Laghman /Kunar/Nuristan	100%	20%	ALP/E&DoA	1-Jul	Nov-06	Ongoing

2. INFRASTRUCTURE DEVELOPMENT

The Infrastructure Unit completed the following activities during the reporting period:

2.1. PRODUCTIVE INFRASTRUCTURE PROJECTS (PIP)


2.1.1 Capacity Building

Construction Trades Training Center (CTTC) Training: The Class of 41 ALP/E supported tradesmen continued their 30-day course in trade skills at the CTTC, which started on September 28, 2006. It will be completed at the end of October.

Cobblestone Road Training Center: During the reporting period, two courses were held, the first for 56 skilled workers and the second for 14 Site Engineers and Assistant Engineers. The courses were held at the CTTC Cobblestone Road Training Center, with site visits to ongoing ALP/E cobblestone project sites roads in Surkhrud and Qarghai. The skilled workers came from Kot district of Nangarhar province (31 trainees) and Qarghai District of Laghman province (25 trainees). The engineers included 13 from Surkhrud, Chaparhar, Pachir, Nazian, Bati Kot, Kot and Sherzad Districts of Nangarhar Province and 1 from Qarghai district of Laghman Province.



Site / Assistant Engineers classroom training at the CTTC

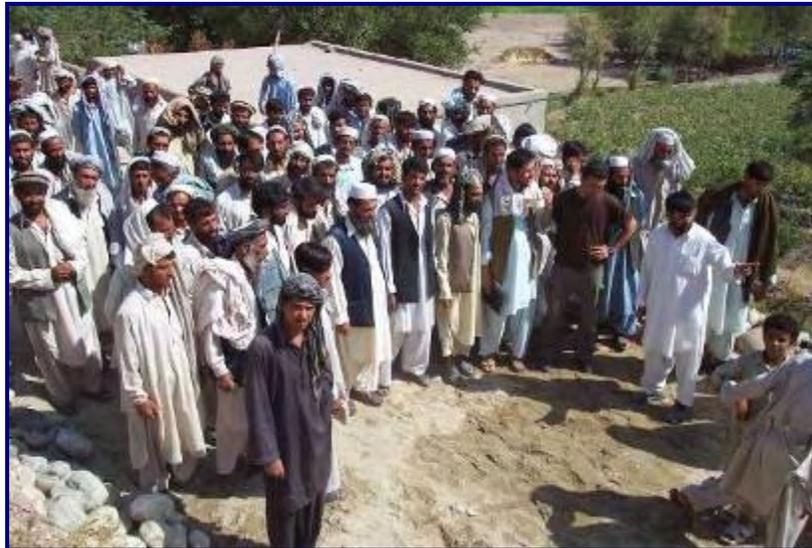

Skilled laborers training in cobblestone laying on Shamshapoor Road Project in Surkhrud district

Total number of trainees who have been trained on cobblestone roads since the courses started on August 8:


Trainees	Number trained
Skilled Cobblestone Workers	260
Engineers	32
Technicians	11
TOTAL	303

2.1.2 Improving Access to Markets

Improvements to existing roads and bridges connecting priority production areas to district centers continue under ALP/E Annual Work Plan Year Two (AWP2). Progress during this period is below:

Mashina Road (7.5 km): The improvement work on the Mashina road in Qarghai District implemented by HADF is progressing satisfactorily. Remedial work has been completed to the required standard, and quality has improved. Concrete strength tests and site CBR compaction tests were made to verify the quality of work. The overall progress on the project is 33% completed, with the following achievements to date:

- Completed construction of five pipe culverts and 3 box culverts
- Completed 30m length of retaining wall
- Scarified road surface and laying compacted fill for length of 2,200m

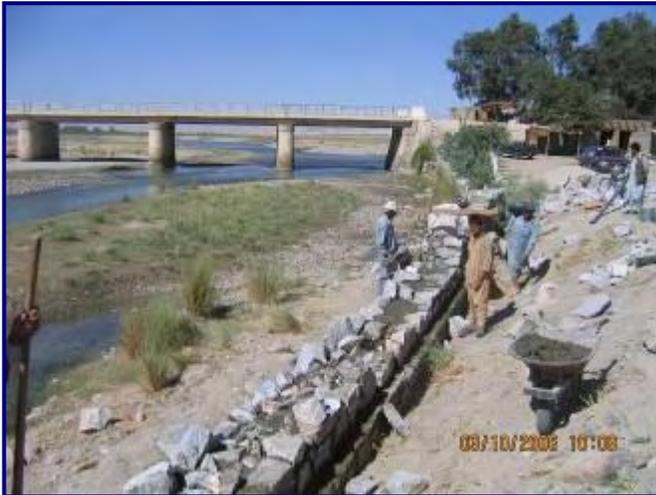

Work inspection at Mashina Road

Kama Road (14.6 km): Evaluation of the 23 bids received for the Kama Road Improvement Project continued during the reporting period. Two clarification meetings were held with a potential contractor and final negotiations were discussed.

Qasimabad Road (5.7 km): The technical feasibility report for Qasimabad Road has been submitted to USAID on September 20, and once final approval is granted implementation through competitive bidding will proceed.

Abuzai Bridge: The technical feasibility report for Abuzai Bridge has been finalized and will be submitted to USAID during the next reporting period.

Lalpur Road (12 km): The design of the road profile, cross-sections and structures is completed, and a visit is planned during the next week to check the design on site.

Sherzad to Hisarak Road Section I (15.4 km): The design has been completed and first draft of Feasibility Report has been prepared.

Barabad to Mangwal Road Section I (11.5 km). Surveys were completed this period and the total length of Section I is 11.5 km. Typical cross sections of the road, design of structures, drawings of structures and cost estimates have been completed and are included in the draft technical feasibility report.

Barabad to Mangwal Road Section II (9.6 km)

Alignment and cross sections surveys were completed during the period from km 11+500 to 21+080. The total length of Section 2 is 9.6 km.

Nangarhar Road Inventory Team:

During the reporting period, the NRIT completed GPS surveys in the following districts:

#	District surveyed	# of Roads	Length (km)
1	Pachir wa Agam	3	12
2	Chaparhar	4	7.5
3	Khogjani	26	183
Total length		33	202.5

To date the NRIT has completed inventories for 1,764 km of roads in 20 Districts of Nangarhar Province. It is expected to complete the remaining work in Sherzad and Hesarak districts during the next reporting period.

Jalalabad Wholesale Market: Work continued on the Jalalabad Wholesale Market under CFW, with the target of completing the first half of the market soon after Eid. The detailed design for the septic tank to serve the new toilet block was prepared.

PRODUCTIVE INFRASTRUCTURE PROJECTS (PIP)								
Project Name	District	Province	% Design Completed	% Implementation Completed	Implementer	Activity Start Date	Activity Completion Date	Comments
Darunta by-pass Road	Qarghai	Laghman	100%	99%	DAI	Feb-06	Dec-06	Work being carried out under CFW
Mashina Road Improvement – 7.5 km	Qarghai	Laghman	100%	33%	HADF under Contract	2-Sep-06	15-Nov-06	Ongoing
Abuzai Bridge	Mehtarlam	Laghman	100 %	0%	Contract	Nov-06	June-07	Awaiting finalization of Technical Feasibility Report
Shamshapoor Road – 11.5 km	Surkhrud	Nangarhar	100%	99%	DAI	Feb-06	Feb-07	Work being carried out under CFW
Wazir Tatang Causeway	Surkhrud	Nangarhar	100%	0%	Contract	TBD	TBD	Pending
Jalalabad Wholesale Market	Jalalabad City	Danaher	100%	63%	DAI	June-06	Oct-2006	Work being carried out under CFW
Kama DBST Road - 14.6 km	Kama	Nangarhar	100%	0%	Contract	Nov-06	May-07	Tender evaluation has started, selection of contractor is in final stage.
Qasim Abad Road – 5.7 km	Behsud	Nangarhar	100%	0%	Contract	Dec-06	May-07	Technical Feasibility Report completed and submitted to USAID.
Rodat Road - 12.3 km	Rodat	Nangarhar	100%	0%	Contract	TBD	TBD	Design and BOQ completed.
Sherzad to Hesarak Road –Section-1 15.4 km	Sherzard & Hesarak	Nangarhar	80%	0%	Contract	Dec-06	Mar- 07	Survey and design completed and Feasibility Report 1st draft completed and submitted for finalization
Lal Pur to Goshta Road- 15km	Lal Pur	Nangarhar	50%	0%	Contract	Dec-06	May-07	Engineering survey completed. Design has been completed
Chardy-Ghaziabad road 12.6 km	Kot	Nangarhar	10%	0%	Contract	TBD	TBD	Engineering survey has been completed.
Dudarak Road,6.2km	Dari-Nur	Nangarhar	10%	0%	Contract	Jan-07	Apr-07	Engineering survey has been completed.
Barabad to Mangwa Road Section-1 11.5 km	Khas Kunar	Kunar	15%	0%	Contract	Jan- 07	June -07	Engineering survey completed, 1 st draft of Feasibility has been prepared
Barabad to Mangwal Road Section-2 9.58 km	Khas Kunar	Kunar	10 %	0%	Contract	Jan 07	June-07	Engineering survey completed

The numbers of projects currently being designed and implemented under PIP, along with their status, are below:

Province	Technical Feasibility Completed	Engineering Survey and Design Completed	Projects Under Tender Process	Contracts Awarded
Nangarhar	3	7	1	0
Laghman	2	2	0	1
Kunar	1	2	0	0
Total	6	11	1	1

2.2. CASH-FOR-WORK PROJECTS (CFW)

Four CFW projects were completed while work on four more cobblestone road projects started during the reporting period, creating a total of 45 ongoing projects in Laghman, Nangarhar, Kunar and Nuristan Provinces.

The daily employment rate was 5,668 workers per day, while 21,094 individual workers have been employed from June 2005 through October 15, 2006. Total employment days during the period were recorded as 56,778 and the cumulative total reached 1,126,640 employment days from June 2005 through October 15, 2006.

The status of work in each Province is below:

- **Nangarhar Province:** Twenty one CFW projects underway with a cumulative total of 492,236 employment days generated.
- **Laghman Province:** Sixteen CFW projects underway with a cumulative total of 491,358 employment days generated.
- **Kunar Province:** Seven CFW projects underway with a cumulative total of 141,227 employment days generated.
- **Nuristan Province:** One CFW Cobblestone road project underway with a cumulative total of 1,819 employment days generated.

SUMMARY OF CFW PROJECTS BY PROVINCE

SN	Province	Completed	Active
1	Nangarhar	32	21
2	Laghman	20	16
3	Kunar	6	7
4	Nuristan	0	1
Total		58	45

i. Nuristan Province: Work continued on the Dakor to Mashfa Road in Nangarhar during the reporting period- the first cobblestone road in Nuristan Province. To date, 309 people have been employed with a cumulative total of 1,819 employment days through October 15, 2006.

ii. Laghman Province: Under the supervision of ALP/E, Relief International (RI) continued to work on 14 CFW projects during the reporting period in Laghman, while one project was completed. Work has still not started on the Kakas Canal project in Qarghai District, due to a community dispute, and this project may have to be cancelled. One new project, the Deh Ziarat to Omarzai Cobblestone road, was started by ALP/E during this reporting period. Work also continued on the Darunta By-pass Cobblestone road project in Qarghai District under the direct supervision of ALP/E. The daily worker rate in Laghman reached an increased 2,460 workers per day, with a cumulative total of 9,533 individual workers employed from June 2005 through October 15, 2006. Employment days during the reporting period were 26,105 and the cumulative total reached 491,358 through October 15, 2006.

CFW PROJECTS: LAGHMAN

Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Pacha Joie Canal	CFW-090107	Mihtarlam	Laghman	100%	67%	RI	26-Aug-06	30-Nov-06	Ongoing
Abizai Flood Protection	CFW-090108	Mihtarlam	Laghman	100%	37%	RI	12-Sep-06	20-Dec-06	Ongoing

CFW PROJECTS: LAGHMAN

Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Gundy Baba Sah b Flood Protection	CFW-090112	Mihtarlam	Laghman	100%	38%	RI	10-Sep-06	20-Dec-06	Ongoing
Qala Shagee Flood Protection	CFW-090118	Mihtarlam	Laghman	100%	44%	RI	10-Sep-06	20-Dec-06	Ongoing
Baba Sahib Canal	CFW-090120	Mihtarlam	Laghman	100%	56%	RI	30-Aug-06	25-Nov-06	Ongoing
Dehziarat to Omarzai Cobblestone Road	CFW-090121	Mihtarlam	Laghman	100%	1%	DAI	3-Oct-06	3-May-07	Ongoing
Dopai and Langalam Protection wall	CFW-090201	Qarghai	Laghman	100%	100%	RI	24-Nov-05 01-Aug-06	30-Mar-06 5-Oct-06	Completed, including backfilling
Kakas Canal Rehabilitation	CFW-090207	Qarghai	Laghman	100%	0%	RI	TBD	TBD	PROJECT TO BE CANCELLED
Daronta Bypass Cobblestone Road, Second Reach	CFW-090209	Qarghai	Laghman	100%	93%	DAI	13-May-06	31-Oct-06	Ongoing
Kac Aziz Khan Canal	CFW-090210	Qarghai	Laghman	100%	51%	RI	5-Sep-06	10-Jan-07	Ongoing
Daronta Bypass Cobblestone Road, Third Reach	CFW-090213	Qarghai	Laghman	100%	0%	DAI	TBD	TBD	Approved by USAID
Qardy Kac Canal	CFW-090214	Qarghai	Laghman	100%	25%	RI	25-Sep-06	25-Dec-06	Ongoing
Ghunday Nazar Khil Protection	CFW-090302	Alingar	Laghman	100%	100%	RI	19-Dec-05 4-Oct-06	7-Jun-06	Backfilling 3% started this period
Qasaba Protection wall	CFW-090303	Alingar	Laghman	100%	100%	RI	10-Dec-05	15-Apr-06	Completed, further backfilling work planned after Eid
Bara Kandy and Kuza Kandy Canal Rehabilitation	CFW-090304	Alingar	Laghman	100%	93%	RI	27-May-06	31-Oct-06	Ongoing
Purwaie Flood Protection works	CFW-090305	Alingar	Laghman	100%	27%	RI	10-Sep-06	20-Nov-06	Ongoing
Mundal Flood Protection works	CFW-090306	Alingar	Laghman	100%	30%	RI	2-Sep-06	10-Nov-06	Ongoing
Kandi Sahib Canal	CFW-090705	Alishang	Laghman	100%	91%	RI	14-Aug-06	15-Nov-06	Ongoing
Qardi Salab Canal	CFW-090708	Alishang	Laghman	100%	75%	RI	17-Aug-06	20-Nov-06	Ongoing
Kalay Baya Canal	CFW-090709	Alishang	Laghman	100%	43%	RI	30-Aug-06	30-Nov-06	Ongoing

iii. Kunar Province: Work is ongoing in Kunar Province with all seven active projects in the province. A security incident occurred at the Dewagal Road improvement project in Chawkay District on October 9, and work has been suspended. To date, 1,990 people have been employed with a cumulative total of 141,227 employment days through October 15, 2006.

CFW PROJECTS: KUNAR

Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Dandono Kotgi Canal Intake	CFW-101201	Narang	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
Badil Khovar Flood Protection	CFW-101205	Narang	Kunar	100%	88%	DAI	11-Jul-06	31-Oct-06	Ongoing

Seend Wala Chawkey Intake	CFW-101301	Chawkey	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
Dewagal Road Improvement	CFW-101303	Chawkey	Kunar	100%	90%	DAI	16-Apr-06	31-Oct-06	Work stopped since 7 October due to security incident
Zarmandai Flood Protection	CFW-101304	Chawkey	Kunar	100%	92%	DAI	27-Jun-06	31-Oct-06	Ongoing
Chawkey Khower Flood Protection	CFW-101306	Chawkey	Kunar	100%	88%	DAI	10-Jul-06	31-Oct-06	Ongoing
Noorgal Seend Wala Intake	CFW-101401	Noorgal	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
Seend Wala Canal Rehabilitation	CFW-101402	Noorgal	Kunar	100%	100%	DAI	20-Feb-06	15-Aug-06	Completed, including additional work
Nurgal-Aret Road	CFW-101403	Noorgal	Kunar	100%	68%	DAI	18-Jun-06	25-Oct-06	Ongoing
Tora Tega Road	CFW-101404	Noorgal	Kunar	100%	60%	DAI	11-Jul-06	11-Nov-06	Ongoing
Daag Canal Repair	CFW-101501	Khas Kunar	Kunar	100%	100%	DAI	21-Feb-06	18-Sep-06	Additional works completed. Flood damage to retaining wall, needs additional funds.
Khas Kunar Clinic to Hakimabag Road	CFW-101503	Khas Kunar	Kunar	100%	50%	DAI	28-Aug-06	28-Nov-06	Ongoing

iv. Nangarhar Province: During the reporting period, work was completed on three projects and continued on 21 active projects, while four new cobblestone road projects started during this reporting period. The two approved projects in Torghar continued to be suspended, due to the security situation. Two other projects in Khogiani have also been suspended due to a community dispute and security problems. The daily workers employed in Nangarhar Province during the period were 2,120 workers per day with a cumulative total of 9,262 workers. Total employment days were 19,714 while total employment days reached 492,236 through October 15, 2006.

Work continued on the Jalalabad Wholesale Market, with the target of completing the first half of the market by the end of October. Overtime work on Fridays and during the evenings is ongoing. Eight disadvantaged women nominated by the Department of Women's Affairs for work are employed to prepare 8mm diameter steel stirrups in a secluded area of the market. Concreting of the columns and the roof for the first half of the market was completed; surface finishing work, tiling of the new toilet block, and casting of concrete floors in the shops are in progress. The old brick wall at the front of the market has been demolished and rebuilt in line with the new structure requested by the city administration. A motor grader and compactor were rented to prepare concreting of the main market concourse. Work is also in progress on the compacted base for the cobblestone road behind the market. The USAID team of auditors visited the market and Shamshapoor road on October 8 to see the work in progress and to meet with the beneficiaries.



Program Auditors from USAID's Regional Inspector General Office visit the Jalalabad Wholesale Market


CFW PROJECTS: NANGARHAR

Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Jalalabad Wholesale Market Rehabilitation	CFW-080103	Jalalabad	Nangarhar	100%	58%	DAI	5-Jun-06	5-Dec-06	Ongoing
Kakrak Road Improvement	CFW-080202	Sorkhrud	Nangarhar	100%	96%	DAI	29-May-06	31-Oct-06	Ongoing
Tatang Nawab Jabar Canal Rehabilitation	CFW-080203	Sorkhrud	Nangarhar	100%	100%	DAI	6-Jun-06	20-Sep-06	Completed, including additional works.
Shamshapoor-Daronta Road Improvement	CFW-080205	Sorkhrud	Nangarhar	100%	95%	DAI	8-May-06	31-Oct-06	Ongoing
Shamshapoor Cobble Stone Road second reach	CFW-080206	Sorkhrud	Nangarhar	100%	97%	DAI	14-May-06	31-Oct-06	Ongoing
Ghauchak Cobblestone Road	CFW-080207	Sorkhrud	Nangarhar	100%	5%	DAI	5-Oct-06	20-Feb-07	Ongoing
Sanzai Road	CFW-080305	Hisarak	Nangarhar	100%	100%	DAI	2-Jul-06	5-Oct-06	Completed this period.
Kodi Khil Cobblestone Road	CFW-080407	Shirzad	Nangarhar	100%	0%	DAI	TBD	TBD	Approved by USAID
Nemla Irrigation	CFW-080504	Khogaini	Nangarhar	100%	6%	DAI	17-Sep-06	17-Dec-06	Work still stopped due to security and community dispute.
Nemla Flood Protection	CFW-080507	Khogaini	Nangarhar	100%	86%	DAI	28-Jun-06	30-Oct-06	Work still stopped due to security and community dispute.
Dawlat Zai Canal Intake	CFW-080601	Chaparhar	Nangarhar	100%	119%	DAI	6-May-06	5-Oct-06	Completed this period including additional work.
Garatak Flood Protection Wall	CFW-080603	Chaparhar	Nangarhar	100%	100%	DAI	30-May-06	12-Oct-06	Completed this period
Chardahi Flood Protection Wall	CFW-080604	Chaparhar	Nangarhar	100%	113%	DAI	30-May-06	31-Oct-06	Ongoing
Sholana Flood Protection Wall	CFW-080605	Chaparhar	Nangarhar	100%	116%	DAI	30-May-06	15-Oct-06	Ongoing
Lawangapor Cobblestone Road	CFW-080606	Chaparhar	Nangarhar	100%	6%	DAI	1-Oct-06	31-Jan-07	Work started this week
Pacher Cobblestone Road	CFW-080702	Pachir wa Agam	Nangarhar	100%	0%	DAI	TBD	TBD	Approved by USAID
Deh Sarak Canal Intake	CFW-081001	Achin	Nangarhar	100%	14%	DAI	9-Sep-06	17-Nov-06	Ongoing
Terkhy Intake and Flood Protection	CFW-081101	Nazyan	Nangarhar	100%	70%	DAI	5-Jul-06	30-Oct-06	Ongoing.
Zysar Cobblestone Road	CFW-081102	Nazyan	Nangarhar	100%	5%	DAI	2-Oct-06	31-Mar-07	Ongoing.
Torlala Kaly Irrigation Reservoir & Flood Protection	CFW-081203	Dur Baba	Nangarhar	100%	88%	DAI	27-Jun-06	31-Oct-06	Ongoing.
Zakhil Irrigation Canal	CFW-081301	Shinwar	Nangarhar	100%	99%	DAI	25-Jun-06	31-Oct-06	Ongoing
Zara Sultankhil Protection Wall	CFW-081402	Momandara	Nangarhar	100%	100%	DAI	21-Mar-06 15-July-06	28-May-06 22-Sep-06	Completed, including additional work.
Basawal Banbaba Flood Protection	CFW-081404	Momandara	Nangarhar	100%	8%	DAI	4-Aug-06	30-Nov-06	Work stopped since flood on 19 September.
Spin Jumat Embankment	CFW-082204	Behsud	Nangarhar	100%	105%	DAI	25-Apr-06	31-Oct-06	Ongoing
Binigah II Flood Protection	CFW-082206	Behsud	Nangarhar	100%	5%	DAI	3-Oct-06	3-Feb-07	Ongoing
Inzari Khola Intakes	CFW-082302	Spinghar	Nangarhar	100%	0%	DAI	TBD	TBD	Project approved 30 August.
Hojoom, Kal Chelgazi Intakes	CFW-082303	Spinghar	Nangarhar	100%	8%	DAI	24-Sep-06	24-Dec-06	Ongoing
Lokhi Canal Intake	CFW-082304	Spinghar	Nangarhar	100%	0%	DAI	TBD	TBD	Project approved 30 August.
Girdi Nawagai Road	CFW-082305	Spinghar	Nangarhar	100%	67%	DAI	13-Jun-06	31-Oct-06	Ongoing


CFW PROJECTS: NANGARHAR

Project Name	Project Code	District	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Remarks
				Design	Execution				
Shangina Yousaf Kas Canal Rehabilitation	CFW-082401	Tor Ghar	Nangarhar	100%	0%	DAI	TBD	TBD	Cleared for starting but stopped again due to security problem.
Gachawy Mirano Road Improvement	CFW-082402	Tor Ghar	Nangarhar	100%	2%	DAI	19-Jul-06	TBD	Cleared for restarting but stopped again due to security problem.

Monthly Employment Days (in 1,000s) in CFW Projects since June 2005

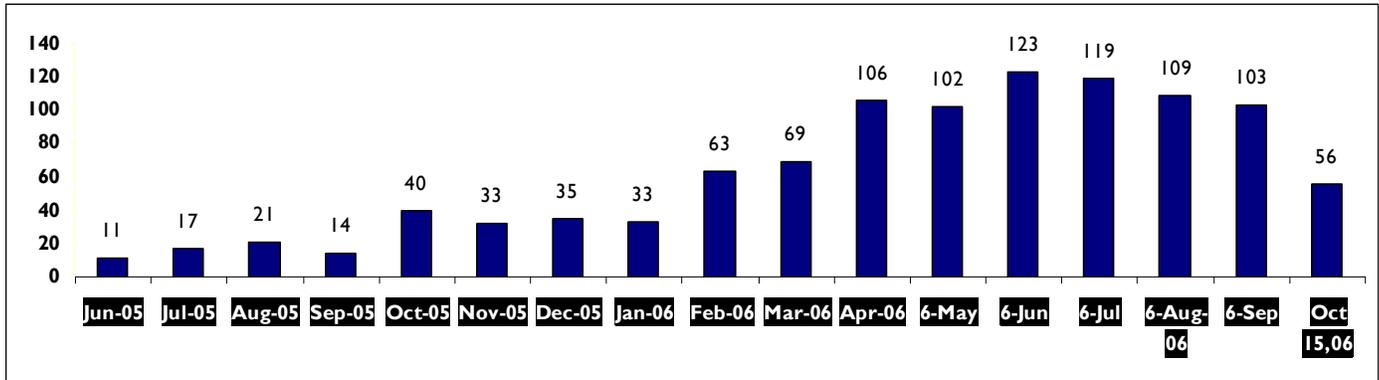

Persons Hired on CFW projects since June 2005

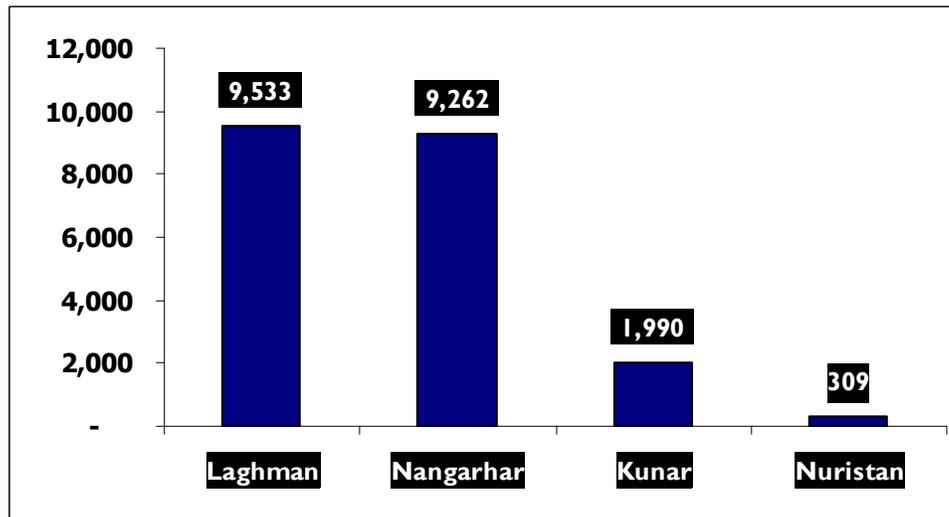

3. PRIVATE SECTOR DEVELOPMENT

The Private Sector Development Unit completed the following activities during the reporting period:

- Analyzed the data of the informal tax survey, and discussed the findings with the Provincial Finance Department and Nangarhar Customs House to compare data and to make an effective comparison between the actual tax and the current tax being charged at the road check points. The findings will help decrease informal taxes being levied on businesses transporting their products through the eastern region.
- Discussed implementation plans with the ALP/E Infrastructure Unit for alternative energy: 1) Private Sector and 2) Shura base hydropower.
- Developed a concept paper for the Dubai Construction Fair. Four marble processors from Jalalabad are going to Dubai to participate in the annual construction fair starting on October 28. This event will be an excellent opportunity for the eastern region marble processors to present the marble industry and market their products in the Middle East Market.

- Consulted with the following organizations during a visit to Kabul: the Director of Afghanistan Export Promotion Center; Acap Partners to discuss funding for three large projects in Nangarhar; an Afghan American Publication Company for BDC promotional materials (Magazine, newspaper, calendar, brochures and other promotional materials); participated in a USAID meeting for the new ARIES program, focusing on the potential for collaboration between ALP/E and ARIES. Follow up contacts were made with FINCA, Shore Bank and others.

PRIVATE SECTOR DEVELOPMENT PROJECTS					
Project Name	Location	Province	Activity Start Date	Activity Completion Date	Comments
Business Development Center	Jalalabad	Nangarhar	Apr-06	Feb-09	Ongoing
MIS (Market Information System)	Nangarhar	Nangarhar	May-06	In planning	Managed in time by the BDC.
Establishing Women Handicraft Center	Nangarhar	Nangarhar	TBD	TBD	Fielding an STTA to do a study of designs for the handicraft industry in ER.
Policy Reform	Nangarhar	Nangarhar	Nov-06	In planning	Further research and implementation of policy reform activities.
Training and Internship Program with Nangarhar University	Jalalabad	Nangarhar	ongoing	Ongoing	Formal agreement expected by end of September 2006
Regional Representative for CNFA (operating under an MOU)	Nangarhar	Nangarhar	Aug-05	On going	CNFA is implementing the AADP program and ALP/E represents CNFA..
Support the capacity building of Nangarhar Industrial Assn (NIA).	Nangarhar	Nangarhar	Apr-05	On going	Working on supporting their sub-groups and investment promotion activities
Support to Afghanistan Investment Support Agency (AISA).	Nangarhar	Nangarhar	Jan-06	On going	Supporting the establishment of a office at the BDC, and on ER focused investment promotion
Support to Afghanistan Women's Business Association (AWBA).	Nangarhar	Nangarhar	Jan-06	On going	Approval for supporting a Jalalabad office
Support to Afghanistan Finance Company (AFC).	Nangarhar	Nangarhar	Jan-06	On going	Support with establishment of office at the BDC, and with referrals for leasing/funding
Support and Collaboration with Afghan International Chamber of Commerce (AICC).	Nangarhar	Nangarhar	Jul-05	In planning	Seeking ways for greater collaboration between AICC and BDC (ALP/E)
Internet Cafes with Afghan Telecoms/PRT	Nangarhar	Nangarhar	Feb-06	In planning	Still determining the role for the private sector in the District Comm. Network.
Hygiene Program for food processors	Nangarhar	Nangarhar	Apr-06	In planning	1) assessment, 2) awareness, 3) training to targeted sub sectors. STTA here

Business Development Center Activities

- Drafted an initial marketing plan for the Business Development Center (BDC) through Nangarhar TV for airing an hour program each month. This effort will enable the eastern region business community to recognize and understand the BDC services and the opportunities for expanding local economic development.
- Convened the BDC Strategic Planning Workshop to plan future events and examine opportunities for the BDC. The workshop was held on Saturday October 7, in the ALP/2 conference room. The 18 participants of the workshop included BDC staff, board members, and directors of partner organizations (AISA, AFC, AWBA, ACCI and NIA).
- Visited Peshawar, Pakistan along with the BDC Director and Mr. Anwar owner of Sharif Redwan Ltd. to discuss the olive oil issue with a Pakistani trader Mr. Imran Mateen. The BDC director provided detailed terms and conditions for an agreement with the BDC and NVDA. It was decided that Mr. Mateen the potential buyer of the olive oil will come to Afghanistan around the middle of October to see and test the oil, and, if appropriate, sign a contract
- Finalized "How to Start a Small Business" training, and translated the materials into Pashtu.




Agribusiness consultant is observing the discussion of a group in the workshop

- Contacted the Provincial Finance Department to assess the impact of the BDC “Accounting and Balance Sheet Training” offered to construction and industrial companies. Mr. A. Aziz Manager of the program explained that five companies completed their balance sheets and provided the final documents to the Finance Department. All of the submitted balance sheets were well organized and met the standard of the Finance Department- thereby saving penalties and fines for the participants.
- Presented to the RIG auditors the achievements of the BDC during the six months of operations.



BDC activities presentation for USAID RIG auditors

Number of visitors to the BDC during the reporting period



- AISA reported that they have newly registered three Afghan companies with their investment details in this reporting period. The three registered Afghan Companies with their investment details are as following:

Company name	Amount invested USD
Chabek Afghan Construction and Engineering company	50,000
Dr. Baidara female diseases' hospital and birthplace	20,000
Nasir Zaman construction company	30,000

Moreover AISA renewed the following company's permits:

S.No	Company name	Amount invested USD
1	New Hilal Construction Company	65,217
2	Arica Afghan construction company	100,000
3	Qiamuddin Rahimi Construction company	100,000
4	Alingar Alokozai construction and road building company	446,200
5	Dewa construction company	100,000

ALP/E assisted businesses looking for support from CNFA

#	Company Name	New or Existing	Product	New Labor		Owner Contribution	CNFA Contribution	Total	Status
				Male	Female				
1	A haj Said Rahmanullah Cotton seed Factory	Existing	Refining Cotton and Cotton Seed	14		\$16,666	\$15,000	\$31,666	Submitted to CNFA and under study
2	Yousafi Qazi Zada Tomato Paste Factory	New	Tomato Paste	20		\$149,746	\$35,000	\$184,746	The grantee has been interviewed by CNFA and the application is still under study
3	Nawab Mal k Cotton Seeds Oil Production Company	New	Cotton Seed Oil	25		\$50,400	\$30,000	\$80,400	Submitted to CNFA and under study
4	Afghan Juice Production Company	Existing	Lemon and Orange Juice	4		\$12,000	\$5,000	\$17,000	Submitted to CNFA and currently exploring ways of linking to a big juice factory.
5	Ezat Gul Cotton Seed and Cotton Production Company	Existing	Refining Cotton and Cotton Seed	10		\$26,000	\$5,000	\$31,000	Submitted to CNFA and currently under revision
6	Nangarhar Women Tomato Paste and Pickle Producing Factory	New	Tomato Paste and Pickle	1	9	\$17,500	\$5,000	\$22,500	Rejected by CNFA because of the pickle and tomato not compatible.
7	Riyaz Carton Making Factory	New	Vegetable and Fruit Cartons	19	2	\$40,000	\$36,450	\$76,450	Submitted to CNFA
8	Shakir Sihami Shirkat	Existing	Soap and Pulp	10	5	\$157,200	\$72,000	\$229,200	Submitted to CNFA and currently under revision.
9	Wahid Oil Production Company	Existing	Pulp, and Cotton Seed	3	0	\$36,000	\$5,000	\$41,000	Submitted to CNFA and currently under revision
0	Mirwais Lalpuri Soap and Oil Factory	Existing	Soap, Pulp, unrefined oil and refine cotton	13	4	\$73,000	\$61,100	\$134,100	Submitted to CNFA
11	Mansoor Helmand Ed ble Oil Factory	Existing	Pulp, Soap and Edible oil	16	4	\$166,200	\$50,000	\$116,200	The grantee has been interviewed and CNFA requested for analysis of the oil.
12	Zar Mohammad Popcorn and poprice factory	Existing	Popcorn and pop rice	6	2	\$11,400	\$5,000	\$16,400	Approved and the contract has been signed between CNFA and the grantee.
13	Hamisha Bahar Vegetable and Fruit Dehydration Factory	New	Dried vegetables and fruit	5	3	\$21,600	\$9,500	\$31,100	The application has been submitted to CNFA. CNFA has approved the project and the contract will be signed between the grantee and CNFA in the near future.
14	Azizi Food Factory	Existing	Fried pulse, roasted peanuts,	15	8	\$34,100	\$13,000	\$47,100	The application has been submitted to CNFA. CNFA has approved the project and the contract will be signed between the grantee and CNFA in the near future.

Note: The figures above indicate only capital expenditures and do not include operating expenses, which will be paid by the owner.

4. GENDER AND MICRO-ENTERPRISE DEVELOPMENT

The Gender and Micro-Enterprise (GME) Unit completed the following activities during the reporting period:

- Micro-Enterprise Program:** The weekly gender radio program was scheduled and the first program will air Saturday, October 1, 2006. Self Help Groups (SHGs) will be informed about the weekly radio schedule and members will be encouraged to listen and discuss topics of interest during their weekly meetings. The main objectives of the radio program are to introduce the GME program, motivate women to achieve economic access, and inform women about existing business support programs. The radio programs will introduce women and business topics to radio in the eastern region. The topics for this month include: business for women according to Islam (Bibi Khadija – the Prophet's wife); overview of SHGs and success stories; interviews with business women; women in business role models; and credit opportunities.

- AITM has been selected to provide a ToT capacity building training for SHGs November 4-9.
- **Smallholder Livestock Management Program:** 717 women from Laghman and Nangarhar have been trained by three female paravets in the areas of livestock nutrition and management, identification and treatment of common diseases, and practices to improve productivity.
- **Women's Forestry Nursery Program:** Three day trainings are scheduled for the end of October, and the saplings will be ready for replanting in early January 2007. GME will be working with CFW regarding site selection and landscaping.
- **Handicraft:** A Rural Handicraft Exhibit is scheduled for November 14-27, 2006 in New Delhi, India sponsored by Global Network & India Trade Promotion Organization. ALP/E will assist four local firms participating in the exhibition, and will provide technical assistance in handicraft design to improve the competitiveness of Afghan handicrafts by enhancing the quality and selection of products, and provide financial assistance for travel, accommodation and exhibition costs, as well as assistance in the design and set-up of the exhibition. This will constitute the first step towards the promotion of handicrafts from Eastern Afghanistan in the international marketplace.
- **Capacity Building:** A six month Capacity Building Plan was developed in collaboration with the Director of Women's Affairs of Nangarhar, Laghman and Kunar. The plan will be implemented beginning in late October in collaboration with ALP/E's Institutional Development Team. Introductory meetings were scheduled with the Director of Women's Affairs. An overview of the program was also presented to H.E. Bano Zagarfan, Minister of Women's Affairs.
- **Vegetable Production:** The GME is working closely with the Natural Resource Management (NRM) Specialist to develop a vegetable seedling production work plan. Three sites have already been identified in Kama and Dar-i-Noor Districts. Three groups, each consisting of 15 women have been formed, and a STTA will provide additional assistance in November.
- **Women's Private Sector Initiative:** The Kaweyan Business Development Services team is in the process of completing data entry and compiling a final report expected in mid October 2006. In addition, AWBA conducted a four-day market access training for 20 women at the BDC.
- **Mainstreaming Gender:** CFW and GME staff attended the opening ceremony of the Benagha, Behsud project. GME staff also selected female cooks for the new sites and recruited 10 female laborers for construction of the Jalalabad Wholesale Market through the Labor Association and DoWA. Female laborers are being trained in making reinforcing wire stirrups for the market. GME is also recruiting ten more females for cobblestone road training.



GENDER AND MICRO-ENTERPRISES

Project Name	Location	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Comments
			Design	Execution				
Establishment of 4 women-owned nurseries	ER	Nangarhar, Laghman	100%	15%	ALP/E	1-Apr-06	15-Jan-07	Ongoing
Monitoring of Infrastructure Projects	ER	ER	100%		ALP/E	1-May-06	31-Jan-09	Ongoing
Selection of women for Food Service	ER	ER	100%		ALP/E	1-May-06	31-Jan-09	Ongoing
Smallholder Livestock Management Program	Village based Self Help Groups	Nangarhar/Laghman/Kunar	100%	10%	ALP/E	1-May-05	1-May-07	Ongoing
AWBA at the BDC	Nangarhar	Jalalabad	100%	10%	AWBA	13-Jun-06	30-Jun-08	Ongoing
Data Base collection on Businesses	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100%	20%	RI	06-Jul-06	05-Sep-06	Ongoing
Establishment of 5 Women Owned Vegetable Nurseries	Nangarhar	Nangarhar	100%	30%	ALP/E	Sep 15, 06	Jan 07	Ongoing

GENDER AND MICRO-ENTERPRISES

Project Name	Location	Province	% Complete		Firm	Activity Start Date	Activity Completion Date	Comments
			Design	Execution				
Handicraft Center	Nangarhar	Nangarhar/Laghman/Kunar/Nuristan	100%	0%	ALP/E	October 06	Sept 07	Planning
Weekly Women Economic Development Radio Program	Nangarhar	Nangarhar/Laghman/Kunar/Nuristan	100%	5%	RI/ALP-E	October 06	Sept 07	Ongoing
Poultry Farm	Nangarhar/Laghman/Kunar	Nangarhar/Laghman/Kunar	100%	0%	ALP/E	October 06	Sept 07	Planning
DoWA Capacity Building	Nangarhar/Laghman/Kunar/Nuristan	Nangarhar/Laghman/Kunar/Nuristan	100%	10%	ALP/E	October 06	March 07	Ongoing

5. INSTITUTIONAL CAPACITY DEVELOPMENT


The following activities were undertaken during the reporting period:

I. Support to Associations:

- Met with wholesalers to discuss the needs of their management group and to discuss strategies to address their marketing needs. They expressed interest in market expansion to China, India and Pakistan. The next step will be meeting with the respective embassies to identify trade fairs, or wholesalers from the above countries.
- Coordinated with village shura members of Shamshapoor village, Surkhrud district and discussed establishing a road maintenance association. The Shura members agreed to appoint two or three people in each village to be responsible for road maintenance. ALP/E will provide some equipment and the community will pay the maintenance staff a monthly salary.
- Coordinated with the village shura of Tatang village Surkhrud district and discuss road maintenance association; the Shura members were very interested in appointing some local people to maintain the road.
- Participated in a study tour of beef farms.

II. Support to Ministry of Agriculture:

- Traveled to Laghman for the following:
 - Monitored English and computer course being delivered to agriculture directorate staff
 - Met Laghman Women's Affairs Directorate; discussed ways to increase staff capacity in new technology, through English language and computer training
 - Discussed with the head of Women Affairs Directorate employment of females in technical officer positions
 - Researched English language and computer training
- Traveled to Kunar for the following:
 - Agreed with Kunar Women's Affairs Directorate on participants from her staff for language and computer training
 - Searched for female trainer and technical officer for Kunar Women's Affairs Directorate
 - Monitored Kunar Agriculture directorate staff training in English and computers.
- Participated in Technical Working Group (TWG) ACBAR meeting in Nangarhar Agriculture Directorate.
- Discussed with the education faculty staff at RANA institute, identifying female English and computer trainers, to train Nangarhar Women's Affairs Directorate staff.
- Met Nangarhar Women's Affairs Directorate, to finalize English language and computer training.
- Participated in Laghman PDC meeting

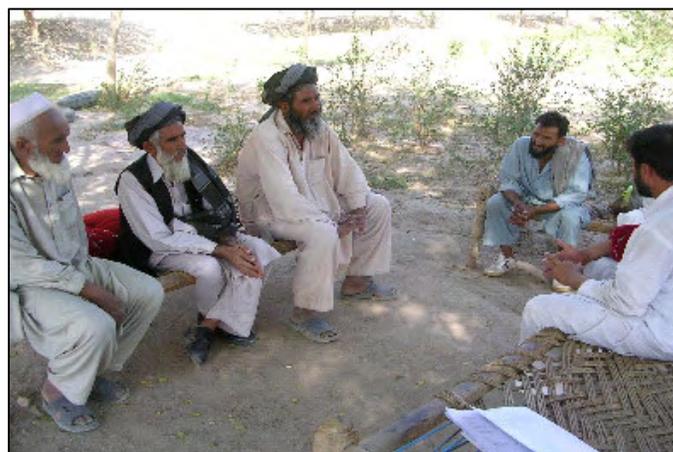

Shura meeting at Shamshapoor to discuss road maintenance association



Women's Affairs Directorate in Laghman

INSTITUTIONAL CAPACITY DEVELOPMENT									
Support to Ministries									
#	Project Name	Location	Province	% Complete		Implementer	Activity Start Date	Activity Completion Date	Comments
				Design	Implementation				
2	Computer and English language training for staff of Nangarhar Agricultural Directorate	Jalalabad	Nangarhar	100%	30%	RANA Institute	5-Jul-05	16-Feb-07	Ongoing
3	Computer and English language training for staff of Laghman Agricultural Directorate	Mihtarlam	Laghman	100%	20%	Laghman Educational Training Center	12-Sept-06	12-Apr-07	Ongoing
4	Computer and English language training for staff of Kunar Agricultural Directorate	Asadabad	Kunar	100%	10%	Kunar Community Educational Center	19-Sept-07	19-March-07	Ongoing
5	Province wide survey and sampling - Nangarhar Agricultural Directorate	Jalalabad	Nangarhar	20%	0%				Ongoing
6	Project Planning training for selected staff of Laghman Agricultural Directorate	Mihtarlam	Laghman	80%	0%	AITM	31-Oct-06	02-Nov-16	Ongoing
7	Management Training for selected staff of Laghman Agricultural Directorate	Mihtarlam	Laghman	80%	0%	AITM	09-Nov-06	23-Nov-16	Ongoing
8	Project Planning Training for selected staff of Kunar Agricultural Directorate	Asadabad	Kunar	20%	0%		28-Nov-06	30-Nov-06	Ongoing
9	Management Training for selected staff of Kunar Agricultural Directorate	Asadabad	Kunar	01%	0%		05-Dec-06	07-Dec-06	Ongoing
10	Computer and English language training for staff of Nangarhar Women Affairs Directorate	Jalalabad	Nangarhar	90%	0%		09-Oct-06	09-Dec-06	Ongoing

INSTITUTIONAL CAPACITY DEVELOPMENT Support to Associations

#	Project Name	Location	Province	% Complete		Implementer	Activity		Comments
				Design	Implementation		Start Date	Completion Date	
11	Computer and English language training for support staff of selected local associations	Jalalabad	Nangarhar	100%	20%	RANA	28-Aug-06	28-April-07	Ongoing
12	Establishment of Eastern Region Livestock Development Association	Jalalabad	Nangarhar	100%	100%	ALP/E	24-Aug-06	01-Oct-06	Being registered
13	Establishment of Carpet Producers Association	Jalalabad	Nangarhar	100%	100%	ALP/E	27-Aug-06	15-Oct-06	Being registered
14	Support to Fresh Fruits and Vegetable Wholesalers Association	Jalalabad	Nangarhar	70%	10%	ALP/E	20-Aug-06		Ongoing
15	Establishment of Road User Association	Shanshapor	Nangarhar	80%	0%	ALP/E	16-Sept-06	25-Dec-06	On going
16	Establishment of Handicraft Association	Jalalabad	Nangarhar	05%	0%	ALP/E	02-Oct-06	10-Dec-06	On going

6. COORDINATION WITH THE GOVERNMENT

ALP/E continued to work towards improving efforts with government bodies and other organizations during this reporting period:

- Attended the fifth Poppy Elimination Program (PEP) meeting in Nangarhar Province, attended by government officials, community representatives, members of the Provincial Council, PRT, IFHOPE, PAL GTZ, RTV, WFP, ACBAR, and other NGO representatives. The deputy governor welcomed all participants of the meeting and declared that sustainable poppy elimination in the eastern region will be strong and effective with alternative livelihood projects.
- Attended the provincial coordination body (PCB) meeting held in the Governor's house of Laghman. The participants of the meeting were the directors of government departments, UNICEF, UNHCR, UNAMA, WHO, DACAAR, RI, PRT, PAL GTZ, FAO, IFHOP, MI, and UNMACA. After welcoming the participants, Governor Al-Haj Gulab Mengal thanked the international community for its continued efforts and new projects.



Participants in Laghman PCB meeting

ADDITIONAL INFORMATION

I. SECURITY

- The security situation in the eastern region continued to be tense during the reporting period. A total of 31 security related incidents took place. The AGEs/Insurgents are increasing activities throughout the region, specifically in Kunar- Nari, Marawara and Pech districts and in Laghman- Alingar, Alishang and Dawlat Shah District. The risk of VBIED/BBIED attacks is increasing particularly in Nangarhar and Kunar Provinces, with reports of attackers targeting government and security positions. Additionally, a special warning was received for Jalalabad City, the Jalalabad –Torkham highway and the Jalalabad-Asadabad highway.
- The security situation in the Province of Nangarhar was relatively tense with thirteen incidents noted during the reporting period in Jalalabad. The infiltration of a new group of 25 AGEs/ Insurgents reportedly crossed the Pakistani border through the eastern districts to conduct attacks against governmental installations of the Province. The infiltration of a group of 100 AGEs through Rodat district was also reported. This group has been tasked to conduct attacks against governmental structures in the area, the nationality of the group members is not clear yet. In addition, the small arms fire on an NGO vehicle on the Kabul/Jalalabad Road was a disturbing issue that has led to all road missions from Jalalabad to Kabul being canceled.
- The security situation in Laghman was calm with three incidents reported during the period. These incidents were reported from Qarghai, Alingar and Alishang districts with RPG rounds and BM-12 rockets. ALP/E continues to prohibit international staff from traveling to Dawlat Shah, Alingar and Alishang Districts of Laghman Province as the situation is uncertain with continued reports of insurgents' movements and infiltration. However, elsewhere operations are going smoothly without interruption by the subcontractor Relief International (RI).
- The security situation in Kunar remained tense with fifteen incidents reported during the period. The province is assessed as being a high risk area for the aid community due to the presence of AGEs, and regular IED, RCIED and rocket attacks against government and Coalition Forces (CF). It is widely believed that Insurgents have almost complete freedom of movement in the border areas and reports indicate a group of suicide attackers entered Kunar Province to target CF, ANSF and International aid workers. ALP/E operations continue in the four districts of Narang, Nurgal, Khas Kunar and Chawkay.
- The CF operation in Eastern and Central Nuristan continued, reportedly to destroy AGE hideouts in the remote areas of Nuristan and clear the area from AGEs.

2. MONITORING AND EVALUATION

Monitoring and Evaluation (M&E) completed the following activities during the reporting period:

- The ALP/E M&E Team conducted monitoring missions to seven ongoing and three completed CFW projects in the region. The findings and recommendations were shared with technical units for follow-up action. The monitoring missions focused on; 1) physical progress, assessing whether planned physical progress was achieved in terms of length, width, and quantities provided, 2) financial disbursements, laborers working on CFW projects were directly interviewed to determine whether they have been paid for hours worked. Project financial data submitted to the ALP/E finance section was cross checked with laborers attendance sheets and pay roll, and 3) persons employed and employment days; individual laborers from each group were counted in spot checks to cross check their physical attendance with the reports. In addition, a monitoring visit was conducted to the Business Development Center (BDC) to monitor activities.
- The USAID GeoBase database was updated for 43 active and completed CFW, Agribusiness, and GME projects' activities.
- The M&E GIS component continued supporting the Nangarhar Road Inventory Team (NRIT) to track standard data collection, downloading, and cleaning field GPS data and sharing the information. In addition, numerous maps on program, security, administration, and other topics were produced during the reporting period.
- The M&E Team has been tracking the process of selecting the farmers under the ALP/E Fall 2006 Wheat Seed and Fertilizer Distribution Program. The team completed the process of selecting beneficiaries in Nangarhar, and is currently distributing vouchers among the selected beneficiaries in Nangarhar.

Short Term Technical Assistance

#	Name	Title	Activity	Status
1	Conrado Camacho	Cobblestone Training Advisor	Training for cobblestone roads	Ongoing
2	Anne Williams	Business Training Advisor	Business skills training and Private Sector Development assistance	Ongoing
3	Alia Afshar	ALP/E Associate	Operational and technical support	Ongoing
4	Alvaro Pacheco	Agribusiness Advisor	Agr business assessment and technical assistance	Ongoing
5	Danilo Benavides	Agribusiness Advisor	Agr business assessment and technical assistance	Ongoing
6	David Love	Livestock Advisor	Slaughterhouse assessment	Ongoing
7	Gleyn Bedsoe	Food Safety Consultant	Food safety assessment	Ongoing

ALP/E CONTACT INFORMATION

Organization: Development Alternatives, Inc. (Nangarhar Office)
 Address: Jalalabad, Nangarhar, Afghanistan
 Name: Jonathan Greenham, COP
 Afghanistan cell: 0798-039432
jonathan_greenham@dai.com

Organization: Development Alternatives, Inc. (Home Office)
 Address: 7250 Woodmont Avenue, Suite 200
 Telephone: (301) 718-8699
 Fax : (301) 718-7968
 Web site : www.dai.com

REQUIRED PERFORMANCE DATA

Annex-I ALP/E Activity Level Indicators¹ Reporting Period October 15th, 2006

Indicator	Unit of Measure	Added (Bi-weekly)	Target (LOP)	Total LOP (To date)	Target (FY 07)	Target (FY 08)	By Province (To date)				By Gender (To date)	
							N	L	K	Nur	Male	Female
Total Kms irrigation and drainage canals and karezes ALP	# km	0.35	2,581	2,432	2,581	2,581	2,385	32	14	0	0	0
ALP Kms. of rural roads repaired in poppy regions	# km	26.3	548	377	548	548	293	15	52	7	0	0
ALP/E Hectares of improved irrigation as a result of ALP infrastructure works	# hec	740	233,060	177,072	233,060	233,060	138,406	34,306	4,360		0	0
ALP/E Amount paid in CFW in AL programs	USD (\$)	\$225,416	\$18,092,363	\$14,277,449	\$18,092,363	\$18,092,363	\$11,781,833	\$1,927,320	\$561,020	\$7,276	\$12,629,486	\$1,647,962
ALP/E Afghans paid through CFW salaries	#	1,396	179,000	155,094	179,000	179,000	143,262	9,533	1,990	309	134,341	20,753
ALP/E Total labor days for CFW	#	56,778	4,767,708	4,094,348	4,767,708	4,767,708	3,459,944	491,358	141,227	1819	3,606,742	487,606
Afghans trained in business skills	#	857	4,000	2,969	3,000	4,000	2,119	470	300	0	806	2,163
Farmers trained in agricultural practices in targeted poppy provinces under ALP	#	0	175,000	95,106	155,000	175,000	54,794	25,312	15,000	0	95,106	0
Farmers receiving seed and fertilizer	#	0	177,961	92,956	177,961	177,961	52,956	25,000	15,000	0	92,956	0
Afghans receiving credit through ALP	#	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA

¹ The table shows aggregated figures of both ALP and AINP project

Annex –II: Person Employed, Employment Days, and Wages Paid on ALP/E CFW Projects through October 15th, 2006

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Kunar	Chawkey	CFW101303	Dewagal Road Improvement	177	14	191	17752	1304	19056	\$71,010	\$5,216	\$76,226
Kunar	Chawkey	CFW101304	Zarmandai and Kulmani Flood Protection Wall	160	14	174	13171	916	14087	\$52,684	\$3,664	\$56,348
Kunar	Chawkey	CFW101306	Chawkey Khower Flood Protection Wall	160	14	174	10221	667	10888	\$40,888	\$2,668	\$43,556
Kunar	Khas Kunar	CFW101501	Daag Canal Repair	235	17	252	13359	801	14160	\$51,780	\$3,204	\$54,984
Kunar	Khas Kunar	CFW101502	Tanar Road Rehabilitation	84	6	90	4682	328	5010	\$17,886	\$1,312	\$19,198
Kunar	Khas Kunar	CFW101503	Clinic To Hakim Abad Road	76	4	80	2474	85	2559	\$9,896	\$340	\$10,236
Kunar	Khas Kunar	CFW101504	Khas Kunar Middle Road	77	5	82	4711	300	5011	\$18,844	\$1,200	\$20,044
Kunar	Narang	CFW101203	Bar Narang Road Improvement	216	16	232	17845	1422	19267	\$71,380	\$5,688	\$77,068
Kunar	Narang	CFW101204	Sharalo Badil Road Improvement	200	14	214	15924	1216	17140	\$63,696	\$4,864	\$68,560
Kunar	Narang	CFW101205	Badil Khawar Flood Protection Walls and Irrigation Intake	103	8	111	6167	312	6479	\$24,668	\$1,248	\$25,916
Kunar	Nurgal	CFW101402	Seenda Wala Canal Rehabilitation	105	8	113	8843	539	9382	\$33,976	\$2,156	\$36,132
Kunar	Nurgal	CFW101403	Nurgal Aret Road	178	14	192	13024	855	13879	\$52,096	\$3,420	\$55,516
Kunar	Nurgal	CFW101404	Kuz Nurgal Tora Tega Road Improvement	79	6	85	4085	224	4309	\$16,340	\$896	\$17,236
Kunar Province Sub-total				1,850	140	1,990	132,258	8,969	141,227	\$525,144	\$35,876	\$561,020
Laghman	Alingar	CFW090301	Khoja Khil Sofla Canal Rehabilitation	1329	38	1367	11100	408	11508	\$52,597	\$1,596	\$54,193
Laghman	Alingar	CFW090302	Ghundai Nazar Khil Protection	211	8	219	20549	2651	23200	\$75,756	\$9,762	\$85,518
Laghman	Alingar	CFW090303	Qasaba Protection Wall	201	7	208	15437	2405	17842	\$59,090	\$10,061	\$69,151
Laghman	Alingar	CFW090304	Bar Kanday and Kuz Kanday Canal Rehabilitation	108	4	112	7595	262	7857	\$28,558	\$1,048	\$29,606
Laghman	Alingar	CFW090305	Purai Protection Wall	122	4	126	2863	34	2897	\$9,809	\$136	\$9,945
Laghman	Alingar	CFW090306	Mandol Protection Wall	114	4	118	3091	51	3142	\$10,813	\$204	\$11,017
Laghman	Alishing	CFW090701	Nolo Protection Wall	399	7	406	24345	381	24726	\$90,552	\$1,524	\$92,076
Laghman	Alishing	CFW090702A	Jamshidabad Protection Wall	450	4	454	21566	164	21730	\$75,883	\$656	\$76,539
Laghman	Alishing	CFW090702B	Jamshidabad Flood Protection Wall Additional Work	186	5	191	12636	324	12960	\$49,228	\$1,296	\$50,524
Laghman	Alishing	CFW090703	Mustafa Kalay Protection Wall	500	18	518	17082	565	17647	\$60,917	\$2,260	\$63,177
Laghman	Alishing	CFW090704	Akhund Sahib Protection Wall	360	9	369	24352	482	24834	\$95,600	\$1,928	\$97,528
Laghman	Alishing	CFW090705	Kandi Sah b Canal Rehabilitation	126	5	131	5558	133	5691	\$21,538	\$532	\$22,070
Laghman	Alishing	CFW090708	Qardi Salab Canal Rehabilitation	168	6	174	7082	158	7240	\$26,970	\$632	\$27,602
Laghman	Alishing	CFW090709	Kalay Baya Canal Rehabilitation	180	4	184	3884	55	3939	\$14,032	\$200	\$14,232
Laghman	Mihtarlam	CFW090101	Deh Zairat Protection Wall	525	10	535	43484	923	44407	\$160,625	\$3,693	\$164,318
Laghman	Mihtarlam	CFW090102	Karaho Protection Wall	209	4	213	13744	155	13899	\$115,181	\$1,557	\$116,738
Laghman	Mihtarlam	CFW090103	Tergari Protection Wall	331	8	339	33494	927	34421	\$126,773	\$3,692	\$130,465
Laghman	Mihtarlam	CFW090104	Mulayan Protection Wall	369	12	381	27892	933	28825	\$102,319	\$3,600	\$105,919

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Laghman	Mihtarlam	CFW090105	Shamangal Canal Reconstruction	168	7	175	14319	563	14882	\$56,453	\$2,222	\$58,675
Laghman	Mihtarlam	CFW090106	Hayadarkhani Canal Reconstruction	219	4	223	5390	173	5563	\$22,922	\$692	\$23,614
Laghman	Mihtarlam	CFW090107	Pacha Joie Canal Rehabilitation	159	7	166	5739	109	5848	\$21,434	\$436	\$21,870
Laghman	Mihtarlam	CFW090108	Abi Zai Flood Protection Wall	165	7	172	3950	50	4000	\$18,375	\$200	\$18,575
Laghman	Mihtarlam	CFW090112	Ghundy Baba Flood Protection Wall	165	6	171	3454	46	3500	\$12,241	\$184	\$12,425
Laghman	Mihtarlam	CFW090118	Qala Shagee Protection Wall	177	8	185	5104	90	5194	\$17,895	\$360	\$18,255
Laghman	Mihtarlam	CFW090120	Baba Sahib Canal Rehabilitation	128	5	133	3531	62	3593	\$13,694	\$248	\$13,942
Laghman	Mihtarlam	CFW090121	Dehziarat/Omarzai village Cobble Stone Road Improvement	138	0	138	905	0	905	\$3,620	\$0	\$3,620
Laghman	Qarghayi	CFW090201	Dopi and Longalam Protection Wall	301	13	314	22741	860	23601	\$82,389	\$3,272	\$85,661
Laghman	Qarghayi	CFW090202	Char Bagh Canal Reconstruction	157	5	162	11607	446	12053	\$44,063	\$1,768	\$45,831
Laghman	Qarghayi	CFW090203	Kalakot and Longalam Canal Reconstruction	186	6	192	15903	532	16435	\$59,107	\$2,084	\$61,191
Laghman	Qarghayi	CFW090204	Daronata Road Repair (Daronta Bypass)	226	2	228	11346	86	11432	\$42,404	\$344	\$42,748
Laghman	Qarghayi	CFW090205	Shamsherabad Flood Protection	412	14	426	27294	1151	28445	\$102,280	\$4,140	\$106,420
Laghman	Qarghayi	CFW090208	Kanda Canal Rehabilitation	149	6	155	9856	387	10243	\$38,449	\$1,548	\$39,997
Laghman	Qarghayi	CFW090209	Daronta Bypass Cobble Stone Road Second Reach	303	2	305	30602	242	30844	\$122,408	\$968	\$123,376
Laghman	Qarghayi	CFW090210	Kac Aziz khan Canal	127	4	131	3538	47	3585	\$13,519	\$188	\$13,707
Laghman	Qarghayi	CFW090212	Farman Khil and Jue Daman Canal	96	0	96	2599	0	2599	\$10,396	\$0	\$10,396
Laghman	Qarghayi	CFW090214	Gardi Kac Canal Rehabilitation	116	0	116	1871	0	1871	\$6,399	\$0	\$6,399
Laghman Province Sub-total				9,280	253	9,533	475,503	15,855	491,358	\$1,864,289	\$63,031	\$1,927,320
Nangarhar	Achin	CFW081001	Deh Sarak Canal Intake Improvement	74	6	80	1698	52	1750	\$6,792	\$208	\$7,000
Nangarhar	Achin	CFW081002	Pekha Protection Flood Protection Wall	461	0	461	29769	0	29769	\$110,600	\$0	\$110,600
Nangarhar	Behsud	CFW082201	Abdian Road Rehabilitation	185	0	185	7952	0	7952	\$30,833	\$0	\$30,833
Nangarhar	Behsud	CFW082202	Biniga Flood Protection Wall	78	6	84	5093	285	5378	\$20,213	\$1,140	\$21,353
Nangarhar	Behsud	CFW082203	Sammarkhil Erosion Protection	207	17	224	6312	561	6873	\$24,863	\$2,244	\$27,107
Nangarhar	Behsud	CFW082204	Spin Jumat Embankment	75	5	80	6244	355	6599	\$24,976	\$1,420	\$26,396
Nangarhar	Behsud	CFW082206	Benigah Flood Protection Embankment Stage II	82	0	82	712	0	712	\$2,848	\$0	\$2,848
Nangarhar	Chaparhar	CFW080601	Daulat Zai Canal Intake	133	10	143	12320	872	13192	\$49,280	\$3,488	\$52,768
Nangarhar	Chaparhar	CFW080602	Garatic and Chardahi Canal Intakes	159	13	172	7498	563	8061	\$29,992	\$2,252	\$32,244
Nangarhar	Chaparhar	CFW080603	Garatic Flood Protection Wall	142	11	153	10667	706	11373	\$42,668	\$2,824	\$45,492
Nangarhar	Chaparhar	CFW080604	Chardahi Flood Protection Wall	126	9	135	10147	600	10747	\$40,588	\$2,400	\$42,988
Nangarhar	Chaparhar	CFW080605	Sholana Flood Protection Wall	127	9	136	11060	701	11761	\$44,240	\$2,804	\$47,044
Nangarhar	Chaparhar	CFW080606	Lawangapur Village Cobble Stone Road Improvement	77	0	77	938	0	938	\$3,752	\$0	\$3,752

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Nangarhar	Dur Baba	CFW081201	Mahsil and Qasaba Kalay Irrigation Reservoir and Erosion Protection	188	2	190	7010	8	7018	\$28,040	\$32	\$28,072
Nangarhar	Dur Baba	CFW081202	Sasobi Irrigation Reservoir and Flood Protection Wall	186	8	194	10692	24	10716	\$42,768	\$96	\$42,864
Nangarhar	Dur Baba	CFW081203	Torlala Kalay Irrigation Reservoir and Flood Protection	153	4	157	8792	172	8964	\$35,168	\$688	\$35,856
Nangarhar	Goshta	CFW081601	Kuz and Bar Billa Flood Protection Wall 1	244	18	262	13384	1147	14531	\$50,917	\$4,588	\$55,505
Nangarhar	Goshta	CFW081602	Kuz and Bar Billa Flood Protection Wall 2	90	8	98	2549	197	2746	\$15,736	\$788	\$16,524
Nangarhar	Goshta	CFW081603	Kuz and Bar Billa Flood Protection Wall 3	89	6	95	5301	382	5683	\$19,811	\$1,528	\$21,339
Nangarhar	Hisarak	CFW080301	Mana Road Rehabilitation	288	26	314	20876	1894	22770	\$82,332	\$7,576	\$89,908
Nangarhar	Hisarak	CFW080302	Shana Zawara Road Rehabilitation	116	10	126	8454	652	9106	\$33,408	\$2,608	\$36,016
Nangarhar	Hisarak	CFW080305	Sanzai Road Improvement	65	4	69	4418	300	4718	\$17,672	\$1,200	\$18,872
Nangarhar	Jalalabad	CFW080101	Jalalabad city Main Drain	63	0	63	2622	0	2622	\$9,363	\$0	\$9,363
Nangarhar	Jalalabad	CFW080102	Jalalabad city Road Side Drains	540	0	540	22174	0	22174	\$82,200	\$0	\$82,200
Nangarhar	Jalalabad	CFW080103	Whole Sale Market Rehabilitation	199	11	210	14272	99	14371	\$57,088	\$396	\$57,484
Nangarhar	Khogyani	CFW080501	Khawaran Road Rehabilitation	146	14	160	9153	741	9894	\$36,080	\$2,964	\$39,044
Nangarhar	Khogyani	CFW080502	Kalagho Road Rehabilitation	181	16	197	9103	781	9884	\$35,991	\$3,124	\$39,115
Nangarhar	Khogyani	CFW080504	Nemla Irrigation Intakes and Canal Repair	50	4	54	302	16	318	\$1,208	\$64	\$1,272
Nangarhar	Khogyani	CFW080506	Khawaza khil and Malam Khil Road	48	3	51	2718	179	2897	\$10,872	\$716	\$11,588
Nangarhar	Khogyani	CFW080507	Nemla Flood Protection Works	110	7	117	7280	424	7704	\$29,120	\$1,696	\$30,816
Nangarhar	Kuz Kunar	CFW081902	Bodiali and soraj Irrigation Rehabilitation	128	9	137	6346	484	6830	\$25,384	\$1,936	\$27,320
Nangarhar	Lal Pur	CFW081502	Guldag Flood Protection Wall	163	13	176	3094	199	3293	\$12,376	\$796	\$13,172
Nangarhar	Muhmand Dara	CFW081402	Zara Sultankhil Protection Wall	67	1	68	3477	33	3510	\$13,772	\$132	\$13,904
Nangarhar	Muhmand Dara	CFW081403	Girdi Ghos Protection Wall	82	3	85	2637	112	2749	\$10,948	\$448	\$11,396
Nangarhar	Muhmand Dara	CFW081404	Basawal Banbaba Flood Protection Wall	73	6	79	1496	118	1614	\$5,984	\$472	\$6,456
Nangarhar	Nazyan	CFW081101	Tarkhy Flood Protection Works and Irrigation Intake	99	8	107	7080	494	7574	\$28,320	\$1,976	\$30,296
Nangarhar	Nazyan	CFW081102	Zysar Village Cobble Stone Road Improvement	143	0	143	945	0	945	\$3,780	\$0	\$3,780
Nangarhar	Sherzad	CFW080401	Gandomak Road Rehabilitation	180	16	196	10924	936	11860	\$43,468	\$3,744	\$47,212
Nangarhar	Sherzad	CFW080402	Toto Road Rehabilitation	129	8	137	8970	631	9601	\$35,408	\$2,524	\$37,932
Nangarhar	Sherzad	CFW080403	Ashpan Flood Protection	203	18	221	10764	971	11735	\$42,629	\$3,884	\$46,513
Nangarhar	Sherzad	CFW080405	Patlaw Road Rehabilitation	109	7	116	7053	507	7560	\$28,140	\$2,028	\$30,168
Nangarhar	Shinwar	CFW081301	Zakhil Wash Irrigation Canal	224	0	224	3834	0	3834	\$15,336	\$0	\$15,336
Nangarhar	Spin Ghar	CFW082301	Maidanak Road Rehabilitation	465	0	465	16857	0	16857	\$61,271	\$0	\$61,271
Nangarhar	Spin Ghar	CFW082303	Hajoom Kal Chelgazi Canal Intakes	96	0	96	1516	0	1516	\$6,064	\$0	\$6,064
Nangarhar	Spin Ghar	CFW082305	Girdi Nawagai Road Repair	156	13	169	13819	976	14795	\$55,276	\$3,904	\$59,180

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Nangarhar	Surkh Rod	CFW080201	Shamshapoor Cobble Stone Road Pilot	393	16	409	18773	851	19624	\$71,332	\$3,404	\$74,736
Nangarhar	Surkh Rod	CFW080202	Kakrak Road Improvement	258	20	278	16723	567	17290	\$66,892	\$2,268	\$69,160
Nangarhar	Surkh Rod	CFW080203	Tatang Nawab Jabar Canal Rehabilitation	158	11	169	8084	217	8301	\$32,336	\$868	\$33,204
Nangarhar	Surkh Rod	CFW080204	Sarband and Jalawanano Canal Intake	87	7	94	5218	308	5526	\$20,872	\$1,232	\$22,104
Nangarhar	Surkh Rod	CFW080205	Shamshapoor Daronta Road Improvement	283	6	289	24319	336	24655	\$97,276	\$1,344	\$98,620
Nangarhar	Surkh Rod	CFW080206	Shamshapoor Cobble Stone Road Second Reach	390	16	406	38331	1391	39722	\$153,324	\$5,564	\$158,888
Nangarhar	Surkh Rod	CFW080207	Ghauchak Cobble Stone Road Improvement	94	0	94	720	0	720	\$2,880	\$0	\$2,880
Nangarhar	Tor Ghar	CFW082401	Shangina Yousaf Kas Canal Rehabilitation	153	0	153	840	0	840	\$3,360	\$0	\$3,360
Nangarhar	Tor Ghar	CFW082402	Gachway Mirano Road Improvement	42	0	42	64	0	64	\$256	\$0	\$256
Nangarhar Province Sub-total				8,857	405	9,262	471,394	20,842	492,236	\$1,856,102	\$83,368	\$1,939,470
Nuristan	Nur Gram	CFW300801	Dakor Mashafa Cobblestone Road	309	0	309	1819	0	1819	\$7,276	\$0	\$7,276
Grand Total				20,296	798	21,094	1,080,974	45,666	1,126,640	\$4,252,811	\$182,275	\$4,435,086

Note: USAID/AINP Performance Data: i. Work Days Generated (#.): 2,967,708 ii. Salaries Paid to Workers: \$9,842,363 iii. People Employed (#.): 134,000 iv. Irrigation Canals, drainage, ditches, and Karezes repaired or cleaned (Km): 2,281 v. Land Benefiting from Improved Irrigation (Ha): 113,060 vi. Roads Repaired (Km): 148
