USAID | WEST BANK/GAZA

MONTHLY PROGRESS REPORT

TASK ORDER NO. 13-00014

Multiple Roads in the North Area (MRNII)

APCO/ArCon

June, 2014

MONTHLY TASK ORDER PROGRESS REPORT

INFRASTRUCTURE NEEDS PROGRAM

Contract No. 294-I-00-12-00005
Task Order No. AID-294-TO-13-00014

From June 01, 2014 to June 30, 2014

DISCLAIMER

"This report is made possible by the support of the American People through the United States Agency for International Development (USAID.) The contents of this report are the sole responsibility of APCO/ArCon and do not necessarily reflect the views of USAID or the United States Government."

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

USAID Contract No.: 294-I-00-12-00005
TO No.: AID-294-TO-13-00014
Contractor: APCO/ArCon Construction and Services

T.O Key Personnel (shared among 2 Projects):
Ahmad Sawafta T.O.M
Murad Shaghnoubi- Q.C.M
Naji Shamasneh- S.E.O
Jameel Abu Baker- Surveyor

Monthly Progress Report number 07

TABLE OF CONTENTS

Task Order Overview		2-4
Safety		4
Environmental Compliance		4-5
Traffic Control Measures		5
Community Outreach and Gender Consideration		5
Coordination		6
Site Visitors		6
Material or Equipment Delivered to Site		6
Progress and Scheduling		6
Activities during this Reporting Period		7
Planned Activities for Next Month		7-8
Indicator No. 01- Number of kilometers of transportation infrastructure constructed or repaired through USG assistance		8
Working / Non-working Days		8
Indicator No. 02- Generated Person-Days of Employment		9
Site Memos		9
Procurement		9
Inspection Requests		10
Quality Control and Test Results		10-11
Submittals		11
RFIs		11
Transmittals		11-13
Payments		13
Variation Order		13-14
Variation Order Requests		14
Obstacles and Challenges		15
Progress Photos		18
Annexes		
A	Materials- Equipment Receiving Log	19-25
B	Detailed Time Schedule for the Project	26-54
	One Month Look ahead	55-62
	Completed and In progress Activities	63-73
C	Progress S-Curve versus Actual	74-77
D	Site Memos Log	78-81
E	Inspection Requests Log	82-102
F	Submittals Log for the Reporting Period	103-128
G	RFI's Log for the Reporting Period	129-131
H	Geo-MIS Data Collection Sheet	132-139
	Generated Person-Days of Employment	

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

TASK ORDER OVERVIEW:

Task Order Project Name	Multiple Roads Project in the North area (MRNII)
Contract No.	294-I-00-12-00005
Task Order No.	AID-294-TO-13-00014
Employer	USAID
Contractor	APCO/ArCon
Engineer / CMC	Black and Veatch
Notice of Award (NOA)	Sep. 19, 2013
Notice To Proceed (NTP)	Dec. 03, 2013
Task Order Completion Date	Dec. 02, 2014
Task Order Contract Value	$16,495,593
Projects Total Value	$16,195,593
Day Work	$300,000
Modified Projects Total Value	$15,571,028 (VO#02)
Modified Day Work	$924,565.00 (VO#02)

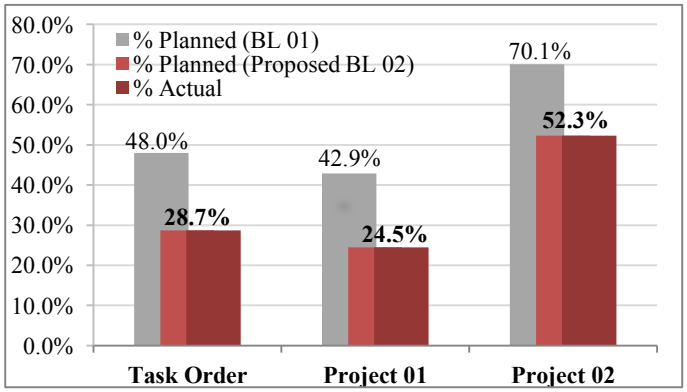

Project 01- Nablus – Beit Iba- Deir Sharaf Road

Project Description	A heavily travelled road with high visibility consisting of 5.5 km of 4 lane roadway stretching through areas A, B and C. Major construction activities include road reconstruction, concrete works, drainage systems, and water networks. The SOW demands this project be carried out within 365 calendar days.
Statement of Work (SOW)	The SOW consists of excavation works, embankment filling, pavement layer construction, milling and overlay, construction of retaining structures, installation and/or rehabilitation of storm water drainage systems, installation of new water lines, sewer lines, installation of safety features (signage, road marking, cat eyes, and guardrails) and any other work items needed to complete this activity as specified.
Project Location	Nablus District
Project Value	$13,170,228
Modified Project Value	$12,545,663 (per VO#02)
Subcontractor Name	Brothers Company
Start of Construction	January 23, 2014
Contractual period of Performance	365 Calendar days
Contractual End Date	Dec. 02, 2014
Modified period of Performance	---
Modified End Date	---
Estimated Completion Date	Dec. 02, 2014
Planned Percentage of Completion	42.9% (Baseline 01)
Planned Percentage of Completion	24.5% (Proposed Baseline 02, subject to USAID Approval)
Actual Percentage of Completion	24.5%

USAID | WEST BANK/GAZA

Project 02- Deir Sharaf –Tulkarem Road

Project Description	A continuation of project 01, a heavily travelled 2.2 km two lane regional road passes mostly through agricultural valley and totally located in area C. the scope of work requires reconstruction and milling and overlay. The SOW demands this project be carried out within 240 calendar days.
Statement of Work (SOW)	The SOW consists of excavation works, embankment filling, pavement layer construction, construction of retaining structures, installation and/or rehabilitation of storm water drainage systems, installation of safety features (signage, road marking, cat eyes, and guardrails) and any other work items needed to complete this activity as specified.
Project Location	Nablus District
Project Value	$3,025,365
Modified Project Value	---
Subcontractor Name	Shaltaf Company
Start of Construction	Feb. 16, 2014
Contractual period of Performance	240 Calendar Days
Contractual End Date	July. 30, 2014
Modified period of Performance	---
Modified End Date	---
Estimated Completion Date	July. 30, 2014
Planned Percentage of Completion	70.1% (Baseline 01)
Planned Percentage of Completion	52.3% (Proposed Baseline 02, subject to USAID Approval)
Actual Percentage of Completion	52.3%

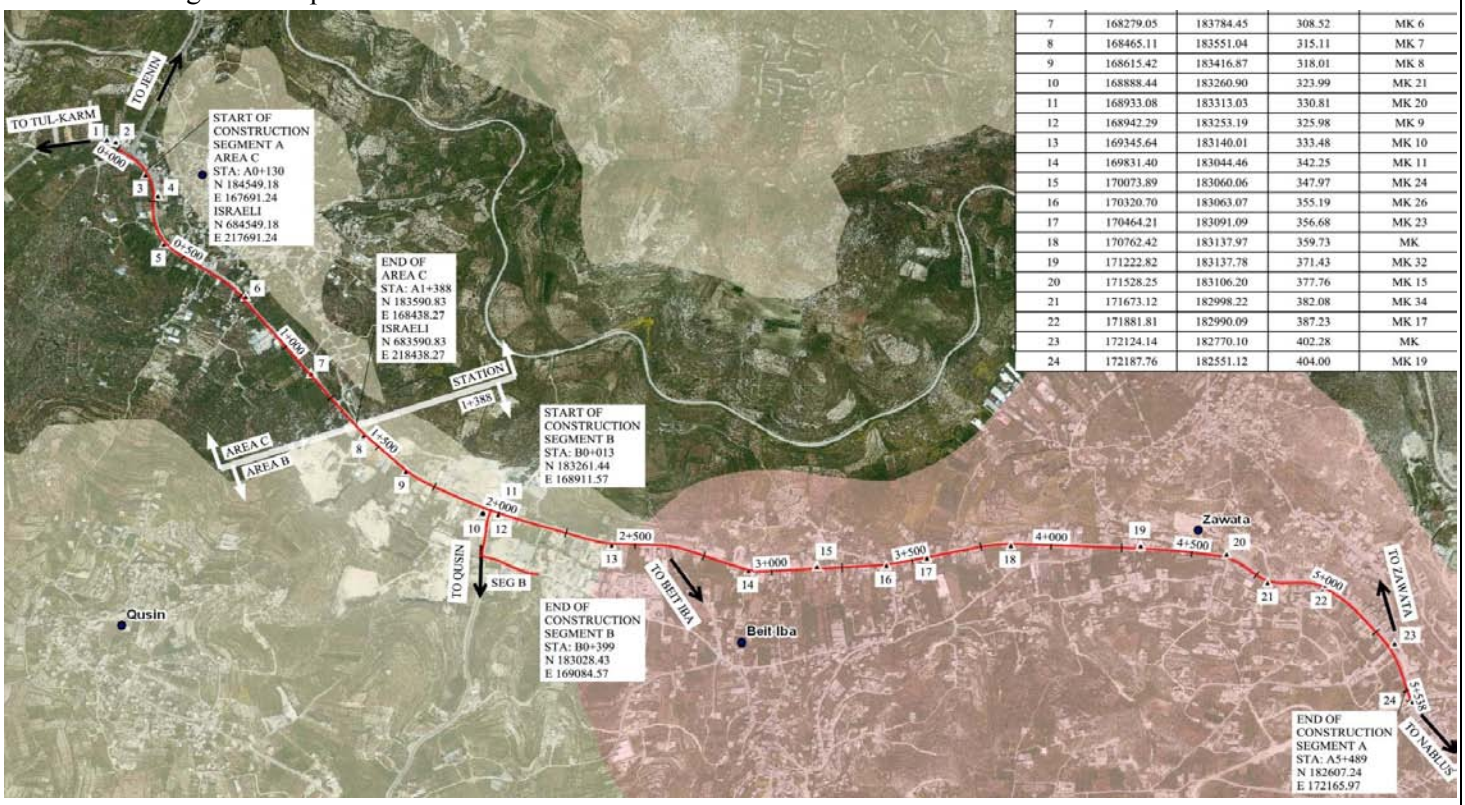

7	168279.05	183784.45	308.52	MK 6
8	168465.11	183551.04	315.11	MK 7
9	168615.42	183416.87	318.01	MK 8
10	168888.44	183260.90	323.99	MK 21
11	168933.08	183313.03	330.81	MK 20
12	168942.29	183253.19	325.98	MK 9
13	169345.64	183140.01	333.48	MK 10
14	169831.40	183044.46	342.25	MK 11
15	170073.89	183060.06	347.97	MK 24
16	170320.70	183063.07	355.19	MK 26
17	170464.21	183091.09	356.68	MK 23
18	170762.42	183137.97	359.73	MK
19	171222.82	183137.78	371.43	MK 32
20	171528.25	183106.20	377.76	MK 15
21	171673.12	182998.22	382.08	MK 34
22	171881.81	182990.09	387.23	MK 17
23	172124.14	182770.10	402.28	MK
24	172187.76	182551.12	404.00	MK 19

Figure 01- Project 01- Nablus – Beit Iba- Deir Sharaf Road Location.

Figure 02- Project 02- Deir Sharaf – Tulkarem Road Location

SAFETY:

During this reporting period, zero accidents were reported, one Notice of Unsafe Condition (NUC) was issued as detailed below, and **1** safety toolbox talk was conducted at project 01 for subcontractor labors and staff as detailed in below safety toolbox log:

Date:	Tool Box No.	Location	Description
June 09	19	Project 01 (NAB)	Manhole cover and trench safety requirements and measures.

NUCs Log

NUC	Date	Location	Level	Hazardous condition	Taken corrective measures
02	06/11/2014	Project 01	A	Open excavation without Proper safety measures	Open shallow excavations was protected by safety measures.
			A	Unsafe and hazard concrete barriers due to lack of proper tapering	Concrete barriers were installed for tapering.
			A	Lack of Proper traffic management implementation along project alignment	Reflective chevrons were installed every 40 m along the project, in addition to other safety measures.
			B	Lack of regular maintenance of traffic management material	Alignment and maintenance of the traffic was applied to the site.
			B	Lack of Proper dust control measures	Dust control and water spraying was conducted every 3 hours.

ENVIRONMENTAL COMPLIANCE:

Environmental mitigation plan detailed methods that respond to special conditions and construction activities that may impact on projects surroundings was developed and submitted to CMC. Approval received on Jan. 26, 2014.

Environmental mitigation plan measures (such as public and labors health and safety, traffic control, dust control, underground utilities protection and monitoring, and other measures) were implemented during this reporting period. 2 Environmental checklists were received for the month of May on June 15, 2014. Recommendations of the lists were minor. At project 01 CMC recommended the contractor to perform regular inspection and monitor for site

housekeeping, provide protective hearing devises and breathing masks for probable emergency cases onsite, use efficient dust control system, perform regular cleaning and maintenance for all work vehicles, and repairs for any infrastructure damages.

In addition to previous mentioned recommendation CMC recommended the followings for Project 02: monitoring workers' adherence in PPEs and Flagman working hours.

APCO/ArCon responded to some of these recommendations and the CMC received our actions on the received lists on June 18, 2014, other recommendations were followed during June and the required corrections and mitigations were implemented.

TRAFFIC CONTROL MEASURES:

For project 01: approved traffic control plan is implemented, construction activities started on site in Area B and A from Sta. 2+020 to Sta. 5+538. Verbal approval on Traffic Plan for Area C from Sta. 0+000 to Sta. 2+020 was received and 13 copies were submitted to DCL for final approval and stamps. On May 4th, 2014 written approval received from ICA for road segment from sta. 0+000 to sta. 2+020.

For project 02: Written approval was received from DCL on Thursday Feb. 20th, 2014 on traffic plan of road segment from sta. 0+000 to sta. 2+180 (Phase #1). On April 29th revised temporary traffic plan for road segment from sta. 0+000 to sta. 2+100 was submitted to DCL for approval, taking into account the DCL's request "not to fully close any road segment". ICA verbal approval was received on May 25th, 2014 (13 copies) were requested to provide the written approval.

Regarding traffic plan for phase #2 (Milling and Overlay of the road segment between the entrance of Shave Shamron (St. 2+180) and the intersection with HWY 557) was prepared and submitted to DCL. They refused to receive the plan as this segment is maintained by Maatz and there is a plan to mill and overlay it by Maatz in the near future, the DCL requested to de-scope this road segment from the scope of work.

Maatz approval was received for Phase #1 on April 10, 2014.

COMMUNITY OUTREACH, PUBLIC INFORMATION AND GENDER CONSIDERATION:

Coordinations with local councils and utility owners were conducted as detailed in below coordination log. Our public relation officer and Safety Officer continued to conduct several meetings and safety toolbox talks with local residents, local councils, and shop owners as detailed below:

June 05, 2014	Project 01- Meeting at An Najah National University- Engineering college to discuss the possibility of training Architecture and Civil enginnering students within NAB project.
June 09, 2014	Project 01- Meeting at Beit Iba village council to coordinate works nearby existing schools or residents where Tawjehi Students live or perform their exams.
June 19, 2014	Project 01- Meeting with Al Shaghour Pool owner, a business owner at St. 4+100 coordinating for retaining walls works and R.O.W.
June 18, 2014	Project 01- Meeting with Nablus governoner and MoPWH to discuss the status of deteriorated residence at St. 3+300.

Figures 03 and 04: Project 01- Meeting with Nablus governoner and MoPWH to discuss the status of deteriorated residence at St. 3+300 LHS.

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

COORDINATION:

During this reporting period, the following coordination's and meetings occurred :

Date	Attendees	Subject	Description
June 05,2014	Black& Veatch : Karim Al Husari- Saleem Tafesh Adel Rabie- APCO/ ArCon: Ibrahim Hindi Murad Shaghnoubi Ahmad Sawafteh Subcontractor : Shaheer Hanani	Bi Weekly Meeting	Discuss general safety issues, quality issues, and work progress.
June 15, 2014	B&V- Adnan Joulani, Salah Tamimi APCO- Najim Saymuah, Narmeen Al Bakri Amar Dwiekat, Amani Krunz IRD- Public Relation Officer	Public Relation Meeting (All Task Orders)	B&V presented and introduction about USAID's communications and outreach interests and INP II communications vision and discussed the already conducted PR activities by the contractors.
June 16,2014	APCO/ArCon: Ahmad Sawafteh Qamar Dwiekat Business owner Kamal Sokhtyan	Coordination Meeting	Discuss general Requirement about work progress at St. 4+100 RHS.
June 18,2014	Nablus Governor – Akram Rojoub, Salam Fretaikh Black & Veatch : Saleem Tafesh APCO/ArCon Ahmad Sawafteh Qamar Dwiekat	Coordination Meeting	Discuss issues and conditions of the existing house at St.3+330 - LHS
June 25, 2014.	USAID Representatives B&V Representatives APCO Representatives. Subcontractors Representatives	Monthly CO Meeting	APCO Briefly presented Projects status and discussed projects progress and issues.

SITE VISITORS:

During this reporting period, the following visits have occurred:

Date	Company	Location	Description
June 18, 2014	USAID- Anan Al Masri	Project 01 -NAB	Site Visit – discus safety issues and progress of work
June 19 ,2014	USAID- Anan Al Masri	Project 01- NAB	Site Visit to follow up work progress, quality and safety.

MATERIAL OR EQUIPMENT DELIVERED TO SITE:

Please refer to **Annex A-** Equipment and Material receiving log.

PROGRESS and SCHEDULING:

% of Completion:

- Survey 90.0%
- Project 01- Shop Drawing 74.0%
- Project 01- Excavation works 43%
- Project 01- Topping 37%
- Project 01- Basecourse 26%
- Project 01- UPVC12 inch Pipes 60%
- Project 01- UPVC 8 inch Pipes 49 %
- Project 01- UPVC 16 inch Pipes 28%
- Project 01- Storm water pipes 45%
- Project 01- 3 inch steel pipeline 66%
- Project 01- 12 inch steel pipeline 50%
- Project 01- Concrete works 17%
- Project 01- Asphalt works 10.0%
- Project 02- Shop Drawing 96.0%
- Project 02- Excavation 95%
- Project 02- Filling Layers 93.0%
- Project 02- Topping 95%
- Project 02- Basecourse 92%
- Project 02- Asphalt works 23%

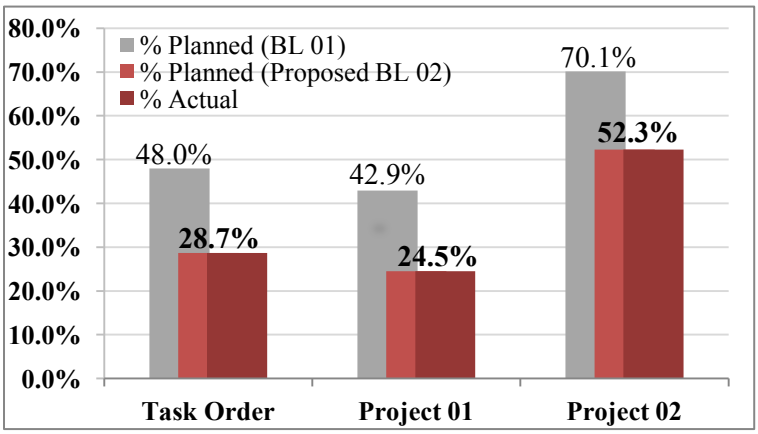

Overall percentages of completion are :

Completion%	T.O	P 01	P 02
Planned % (BL1)	48%	42.9%	70.1%
Planned % (proposed BL2)	28.7%	24.5%	52.3%
Actual %	28.7%	24.5%	52.3%

Refer to **Appendix C** Progress s-curve planned versus Actual.

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

ACTIVITIES DURING THIS REPORTING PERIOD:

Project 01:

- Continue survey works.
- Continue submittals preparation for material and shop drawings.
- Maintain implementation of traffic control plan.
- Finish topping layer from St. A3+440 to St.A4+080 RHS & LHS.
- Finish 16" UPVC pipes for drainage with catch basin from St. A3+610 to St.A3+800.
- Finish first base course layer from St. A3+440 to St. 4+080 RHS and LHS.
- Start second base course layer from St. A2+500 to St.A3+000 RHS and LHS (35 % complete).
- Finish road excavation to required sub grade main road from St. A4+100 to St. 4+260 RHS.
- Finish road excavation to required subgrade main road from St. A4+100 to St. 4+300 LHS.
- Start topping layer from St. A4+100 to St. 4+260 RHS. (90 % complete).
- Start first base course layer from St. A4+100 to St. 4+260 RHS. (90 % complete).
- Start construction of Box culverts at St 3+610 RHS
- Finish construction of retaining walls from A3+650 to A3+690 RHS (75% complete).
- Start road excavation to required sub grade main road from St. A1+500 to St. A2+000 RHS& LHS (90%)
- Start installation of 12" steel pipeline from St. 1+500 To St. 1+900 LHS
- Start topping layer from St. A1+500 to St.A2+000 RHS & LHS (60 % complete).

Project 02

- Continue survey works.
- Continue submittals preparation for materials and shop drawings.
- Maintain implementation of traffic control plan.
- Finish first layer asphalt from St. 0+260 to St.1+460.
- Finish first layer asphalt from 2+050 to 2+200.
- Finish construction of new pipe culvert at St. 1+995.
- Finish construction of new pipe culvert at St. 1+480.
- Finish open ditch construction from St. 0+440 to St. 0+860.
- Finish base course second layer from St.1+460 to St. 2+050
- Start construction of reinforced concrete beam and step barriers from St. 1+300 to St. 1+880 (95 % complete)

PLANNED ACTIVITIES FOR NEXT MONTH:

Project 01

- Continue survey works
- Continue submittals preparation for materials and shop drawings.
- Maintain implementation of traffic control plan.
- Finish installation of 2" steel pipeline from St. 3+800 To St. 4+100 LHS.
- Finish 16" UPVC pipes for drainage W. catch basin from St. A1+900 to St.A2+020.
- Finish topping layer from St. A1+500 to St.A2+000 LHS.
- Finish second base course layer from St. A3+400 to St.A4+100 LHS.
- Finish second base course layer from St. A3+400 to St.A4+100 RHS.
- Finish construction of retaining walls from A3+650 to A3+690 RHS.
- Finish road excavation to required sub grade main road from St. A4+300 to St. A4+800 RHS and LHS.
- Start installation of 60 cm concrete pipes for drainage water from A3+610 to A3+840.
- Finish installation of 12" steel pipeline from St. 4+630 To St. 5+500 RHS
- Finish topping layer from St. A4+100 to St.A4+500 RHS and LHS.
- Start Second base course layer from St. A3+500 to St.A4+000 RHS & LHS.
- Start topping layer from St. A4+000 to St. A4+500 RHS and LHS.
- Finish road excavation in phase two from Sta. A1+500 to Sta. A2+020.
- Start installation of 60 cm Concrete Pipes for drainage with manholes from A1+500 to A1+620 L= 120 m
- Start installation of 12" steel pipeline from St. 1+000 To St. 2+000 LHS
- Start topping layer in phase two from Sta. A1+500 to Sta. A2+020 RHS and LHS.
- Start road excavation in phase two from Sta. A1+000 to Sta. A1+500.

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

- Start installation of Precast Conc. Curbstone for LHS & RHS (Median and side curb)
- Finish 7 cm Asphalt Binder Course Including Prime Coat from St. 3+400 to St. 4+100 LHS width 6 m.
- Finish 7 cm Asphalt Binder Course Including Prime Coat from St. 3+400 to St. 4+100 RHS.

Project 02

- Continue survey works
- Continue submittals preparation for materials and shop drawings.
- Maintain implementation of traffic control plan.
- Finish open ditch constructions.
- Finish all step barriers construction.
- Finish second wearing course asphalt from St 0+260 to St 2+200.

INDICATOR NO. 01- Number of kilometers of transportation infrastructure constructed or repaired through USG assistance:

Project 01-

Total Road reconstruction (100% Completed)	0.00 Km
Target value	5.50 Km
Number of kilometers constructed or repaired through end of this reporting period=	**0.00** Km

Project 02-

Total Road reconstruction (100% Completed)	0.00 Km
Target value	2.20Km
Number of kilometers constructed or repaired through end of this reporting period=	**0.00** Km

WORKING / NON-WORKING DAYS

Project 01- NAB

1	Total Period of Performance (Original)	365
2	Total Excusable delays/approved extensions	0
3	Modified Period of Performance	---
4	Modified Completion Date	---
5	No. of Working Days during this reporting Period	26
6	Accumulated Working Days	171
7	Total No. of non-working days (Holidays and weekends) during this reporting Period	4
8	Accumulated non-working days (Holidays and weekends)	30
9	No. of other non-working days during this month**	0
10	Accumulated other non-working days	9

Project 02- DSR

1	Total Period of Performance (Original)	240
2	Total Excusable delays/approved extensions	0
3	Modified Period of Performance	---
4	Modified Completion Date	---
5	No. of Working Days during this reporting Period	26
6	Accumulated Working Days	167
7	Total No. of non-working days (Holidays and weekends) during this reporting Period	4
8	Accumulated non-working days (Holidays and weekends)	30
9	No. of other non-working days during this month**	0
10	Accumulated other non-working days	13

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

INDICATOR NO. 2: GENERATED PERSON-DAYS OF EMPLOYMENT:
All reported materials are up to date and meet the five quality data standards (Clause H.9).

This indicator count only local Palestinian staff whose time is charged to the USAID activity (the Contractor at the "prime" and "first tier" subcontractor level only). Neither expatriate person days of employment (i.e. those worked by American or other Third Country National staff) nor management nor administrative person days of employment (i.e. program level and other general and administrative staff shared among multiple task orders) are included. All reported person-days are calculated based on the approved Daily Joint Reports.
Note: numbers are rounded to the nearest integer number (man-day).

Task Order

- Target value= **33,912**
- Employment generated previously = 8,204 Man-Days (per CMC audit up to Feb. 2014)
- Employment generated this month = 2,883 Man-Days
- Total cumulative employment (male and female) generated to-date= **11,087** Man-Days
- Total cumulative female employment generated previously= **144** Man-Days
- Total cumulative female employment generated this month= **32** Man-Days
- Total cumulative female employment generated to-date= **176** Man-Days

Project 1:

- Target value= **27,733**
- Employment generated previously = 6,537 Man-Days (per CMC audit up to Feb. 2014)
- Employment generated this month =1,956 Man-Days
- Total cumulative employment (male and female) generated to-date= **8,493** Man-Days
- Total cumulative female employment generated previously= **123** Man-Days
- Total cumulative female employment generated this month= **22** Man-Days
- Total cumulative female employment generated to-date= **145** Man-Days

Project 2

- Target value= **6,180**
- Employment generated previously = 1,667 Man-Days (per CMC audit up to Feb. 2014)
- Employment generated this month =927 Man-Days
- Total cumulative employment (male and female) generated to-date=**2,594** Man-Days
- Total cumulative female employment generated previously= 21 Man-Days
- Total cumulative female employment generated this month= 10 Man-Days
- Total cumulative female employment generated to-date= **31** Man-Days

Total Job Days (Male and Female)	**No. of Full Time Equivalent (FTE) Jobs =** (Total Job Days / 23.8)
Generated previously = 8,204 Man-days	Generated previously = 344
During this reporting period = 2,883 Man-days	During this reporting period = 121
Total generated to-date = **11,087** Man-days	Total generated to-date = 466
Total Job Days (Female)	**No. of Full Time Equivalent (FTE) Jobs =** (Total Job Days / 23.8)
Generated previously = 144 Man-days	Generated previously = 6
During this reporting period = 32 Man-days	During this reporting period = 1
Total generated to-date = **176** Man-days	Total generated to-date = 7

SITE MEMO:

- **See Appendix D** Site Memos log

PROCUREMENT:

No special procurements, all materials are within the West Bank. For details of delivered material, please refer to the attached **"Materials Receiving Log/ June 2014"**

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

INSPECTION REQUEST:

During this reporting period **233** inspection requests were issued and/or closed as follow:

Project No.	No. of IRs	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review Not Required
P01 (NAB)	113	112	1	95	0	16	1	0
P02 (DSR)	120	116	4	106	0	10	0	0
Total	233	228	5	201	0	26	1	0
%		97.9%	2.1%	86.3%	0.0%	11.2%	0.4%	0.0%

Please refer to **Appendix E**- Inspection request log

Non Compliance Report Log - NCR -

No NCRs were issued during this reporting period.

QUALITY CONTROL AND TEST RESULTS:

During this reporting period **84** test reports were submitted and/or closed as follow:

MRSII	No. of Tests	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review Not Required
No.	84	71	13	68	0	3	0	0
%		84.5%	15.5%	81.0%	0.0%	3.6%	0.0%	0.0%

Tests Log summary table Up to this reporting period including material source testing:

Material Description	Test description	Number of tests	Pass	Fail	Notes (Action taken for failed tests)
Project 01- NAB					
Topping	Comprehensive Test	9	9	0	
	Field Density	32	29	3	Re-worked, re-compacted and retested.
Base course	Comprehensive Test	14	14	0	
	Field Density	78	74	4	Re-worked, re-compacted and retested.
Single Size	Sieve Analysis	4	4	0	
Bedding (Somsom)	Sieve and Sand Equivalent Test	4	4	0	
Strata of Soil	Slope Excavation – Geotechnical Report	1	1	0	
Reinforcement	Tensile , Yielding	7	7	0	
Concrete	Concrete Compressive Strength	63	63	0	
Concrete Pipe Φ 80	Crushing	1	1	0	
Subgrade	Soil Classification	4	0	4	Improvement of soil by supplying of crushed aggregate compacted base course layer of 200 mm - two layers.
	Field Density	38	38	0	
Bituminous Mixture	Marshall Analysis	13	13	0	
	Asphalt cores	21	21	1	

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

Material Description	Test description	Number of tests	Pass	Fail	Notes (Action taken for failed tests)
Project 02- DSR					
Base course	Comprehensive Test	13	13	0	
	Field Density	41	41	0	
Single Size	Sieve Analysis	3	3	0	
Bedding (Somsom)	Sieve and Sand Equivalent Test	3	3	0	
Pulverization	Comprehensive Test	9	9	0	
	Field Density	26	20	6	Re-worked, re-compacted and retested.
Subgrade	Field Density	25	25	0	
Bituminous Mixture	Marshall Analysis	3	3	0	
	Asphalt cores	0	0	0	
Reinforcement	Tensile , Yielding	6	6	0	
Concrete	Concrete Compressive Strength	15	15	0	

SUBMITTALS:

- **See Appendix F** Submittals log for this reporting period including tests log.

Total Submitted and/or closed submittals during this reporting period:

MRN II	No. of SUB	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review Not required
No.	25	19	6	0	15	2	0	2
%		76.0%	24.0%	0.0%	60.0%	8.0%	0.0%	8.0%

RFI

- **See Appendix G** RFI's log for this reporting period.

TRANSMITTALS:

Outgoing / Incoming USAID Transmittals (USAID/ APCO/ArCon)

Date	Contractor Trans. No.	Sender/Recipient	Subject
June 02, 2014	By Email	USAID/ APCO/ArCon	CO Meeting requests
June 02, 2014	By Email	APCO/ArCon/ USAID	TO 13-00014: Recovery plan for Nablus Beit Iba Project
June 02, 2014	By Email	APCO/ArCon/ USAID	TO 13-00014: Deir Sharaf Tulkarem Road Recovery plan
June 04, 2014	By Email	APCO/ArCon/ USAID	TO#11 and TO#14 Environmental/Safety Officer request for change
June 05, 2014	By Email	APCO/ArCon/ USAID	T.O 14- May 2014 - Monthly Report
June 05, 2014	By Email	APCO/ArCon/ USAID	TO 13-00014 MRNII: Contractor's Monthly Report- April, 2014- COR approval
June 06, 2014	By Email	USAID/ APCO/ArCon	Re: TO#11 and TO#14 Environmental/Safety Officer request for change
June 06, 2014	By Email	USAID/ APCO/ArCon	Re: TO 13-00014 MRNII: Contractor's Monthly Report- April, 2014- COR approval
June 13, 2014	By Email	USAID/ APCO/ArCon	Fwd: TO 13-00014 MRNII: NUC- Project 01
June 16, 2014	By Email	APCO/ArCon/ USAID	Reminder: T.O 14- May 2014 - Monthly Report- COR Comments

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

Date	Contractor Trans. No.	Sender/Recipient	Subject
June 16, 2014	By Email	APCO/ArCon/ USAID	RE: TO 13-00014 MRNII: NUC- Project 01
June 17, 2014	By Email	USAID/ APCO/ArCon	Security reports
June 18, 2014	By Email	APCO/ArCon/ USAID	Message from DCL Ramallah
June 21, 2014	By Email	APCO/ArCon/ USAID	RE: TO 13-00014 MRNII: Comments on Contractor's Monthly Report- May, 2014- Modified
June 21, 2014	By Email	APCO/ArCon/ USAID	RE: Important- accruals
June 23, 2014	By Email	USAID/ APCO/ArCon	Re: Monthly Contracting Officer's Meeting
June 26, 2014	By Email	USAID/ APCO/ArCon	Lack of proper site management/ lack of proper safety and traffic control- TO 14

Outgoing / Incoming Consultant Correspondences (B&V/ APCO/ArCon)

Date	Contractor Trans. No.	Sender/Recipient	Subject
June 01, 2014	By Email	B&V/APCO/ArCon	RE: Aggregate filled Bags as Barriers
June 01, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Asphalt work at project 1
June 02, 2014	By Email	APCO/ArCon /B&V	RE: TO 13-00014 MRNII: Asphalt work at project 1
June 02, 2014	By Email	B&V/APCO/ArCon	RE: All Task Orders: Traffic Plan Status Update
June 02, 2014	By Email	B&V/APCO/ArCon	RE: TO 13-00014 MRNII: Asphalt work at project 1
June 03, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Agenda for Progress Meeting 08
June 03, 2014	By Email	B&V/APCO/ArCon	RE: All Task Orders: Traffic Plan Status Update
June 03, 2014	By Email	B&V/APCO/ArCon	Introduction, INP II Communications Vision
June 04, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Agenda for Progress Meeting 08
June 05, 2014	By Email	APCO/ArCon /B&V	May 2014- Geo-MIS Data
June 07, 2014	By Email	B&V/APCO/ArCon	RE: TO 13-00014 MRNII : Works need closeout
June 09, 2014	By Email	APCO/ArCon /B&V	RE: Introduction, INP II Communications Vision
June 10, 2014	By Email	B&V/APCO/ArCon	RE: Introduction, INP II Communications Vision
June 10, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Draft Minutes of Progress Meeting 08
June 10, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: NUC- Project 01
June 11, 2014	By Email	APCO/ArCon /B&V	RE: TO 13-00014 MRNII: NUC- Project 01
June 11, 2014	By Email	APCO/ArCon /B&V	RE: TO 13-00014 MRNII: NUC- Project 01
June 11, 2014	By Email	APCO/ArCon /B&V	Stone Walls all TOs
June 12, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Minutes of Progress Meeting #08
June 12, 2014	By Email	APCO/ArCon /B&V	RE: TO 13-00014 MRNII: Minutes of Progress Meeting #08
June 12, 2014	By Email	APCO/ArCon /B&V	RE: TO 13-00014 MRNII: Minutes of Progress Meeting #08
June 12, 2014	By Email	B&V/APCO/ArCon	RE: TO 13-00014 MRNII: NUC- Project 01
June 16, 2014	By Email	APCO/ArCon /B&V	RE: T.O 14- Project 01- Deteriorated Residence at St. 3+300 LHS
June 16, 2014	By Email	APCO/ArCon /B&V	TO 13-00014: Obstacle- Vehicular Weighing Scale
June 17, 2014	By Email	B&V/APCO/ArCon	RE: Work in-and - Changes in Area C
June 17, 2014	By Email	B&V/APCO/ArCon	RE: Stone Walls all TOs
June 17, 2014	By Email	B&V/APCO/ArCon	RE: All Task Orders: Traffic Plan Status Update
June 18, 2014	By Email	APCO/ArCon /B&V	Message from DCL Ramallah
June 18, 2014	By Email	B&V/APCO/ArCon	USAID visit to the north
June 18, 2014	By Email	APCO/ArCon /B&V	TO 13-00014: HVET VOR

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

Date	Contractor Trans. No.	Sender/Recipient	Subject
June 22, 2014	By Email	B&V/APCO/ArCon	FW: TO 13-00014 MRNII: Primary Office Needs
June 22, 2014	By Email	B&V/APCO/ArCon	RE: USAID Visit to TO 11 and 14
June 23, 2014	By Email	APCO/ArCon /B&V	TO 13-00014: NAB - Signed MOU and VOR 11A
June 23, 2014	By Email	B&V/APCO/ArCon	CO Monthly Meeting: Percentages of Completion for APCO Task Orders
June 24, 2014	By Email	APCO/ArCon /B&V	RE: CO Monthly Meeting: Percentages of Completion for APCO Task Orders
June 25, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Variation Order #03 - Part 1 of 2
June 25, 2014	By Email	B&V/APCO/ArCon	RE: TO 13-00014 MRNII: Variation Order #03 - Part 2 of 2
June 26, 2014	By Email	B&V/APCO/ArCon	RESENDING: TO 13-00014 MRNII: Variation Order #03 - Part 1 of 2
June 26, 2014	By Email	APCO/ArCon /B&V	RE: RESENDING: TO 13-00014 MRNII: Variation Order #03 - Part 1 of 2
June 26, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Unsafe Condition Observed at Project - 1
June 29, 2014	By Email	B&V/APCO/ArCon	RE: Proposed VO#3 for TO 13-00014 MRNII
June 29, 2014	By Email	B&V/APCO/ArCon	RE: TO 13-00014 MRNII: safety violations at Project # 1
June 29, 2014	By Email	APCO/ArCon /B&V	RE: TO 13-00014 MRNII: safety violations at Project # 1
June 29, 2014	By Email	B&V/APCO/ArCon	RE: TO 13-00014 MRNII: safety violations at Project # 1
June 29, 2014	By Email	B&V/APCO/ArCon	TO 13-00014 MRNII: Variation Order #03
June 29, 2014	By Email	B&V/APCO/ArCon	RE: TO 13-00014 MRNII: Variation Order #03
June 30, 2014	By Email	APCO/ArCon /B&V	RE: TO 13-00014 MRNII: Variation Order #03- Signed

PAYMENTS:

Voucher Number	Submitted Date	Amount	Retention Amount	Amount Received	Date Received
01	January 19, 2014	$ 616,975.00	$0.00	$ 616,975.00	January 31, 2014
02	March 27, 2014	$ 261,917.24	$0.00	$ 261,917.24	April 11, 2014
03	May 06, 2014	$ 787,446.40	$0.00	$ 787,446.40	May 23, 2014
04	June 12, 2014	$1,172,298.85	$0.00	$1,172,298.85	June 27, 2014
Total		**$2,838,637.49**	**$0.00**	**$2,838,637.49**	

APCO/ArCon total accrued expenditures $1,468,309.51

VARIATION ORDERS

VO No.	DESCRIPTION	VO Status (AP/PE /RE/RJ)			Date Sent to B&V	USAD Approval Date	Variation order Amount	Time Ex. Days
		APCO	B&V	USAID				
01	Rename Road Project 2 Deir Sharaf- Inab Road to Road Project 2 Deir Sharaf- Tulkarem Road	AP	AP	AP	Jan. 10, 2014	Jan. 10, 2014	-	-
02	Installation of 12" Water Pipeline and deletion of the box culvert from Sta. 4+190 to Sta. 4+740 at Project #1	AP	AP	AP	April 28,2014	April 30,2014	($624,565)	-

03	Changes in Requirements, New Items, New Definitive Quantities and Time Extension at Project #1 & #2	AP	PE	PE	June 30, 2014	PE	$(563,688.9)	P01- 35 P02- 21

AP: Approved PE: Pending RE: Revise RJ: Rejected

VARIATION ORDER REQUESTS:

VOR No.	DESCRIPTION	Date Sent to B&V	Variation order Amount	Time Ex.
01-A	Project 01: Revised plan profile and cross sections, Deletion of box Culvert	March 25, 2014	$(1,116,819.00) Approved, included under VO#02	00
02-A	Project 01: Installation only of 12" Steel pipe	March 26, 2014	$ 492,254.00 resubmitted	P.01 = 23 days
02-B	Project 01: Installation only of 12" Steel pipe	April 16, 2014	$ 492,254.00 Approved, included under VO#02	P.01 =23 days
03-A	Project 02: Supply and installation of 3 "water pipeline and 6 "UPVC road crossing.	April 08, 2014	$83,984.75/ resubmitted	P.02= 33 days
03-B	Project 02: Supply and installation of 3 "water pipeline and 6 "UPVC road crossing.	May 21, 2014	$ 66,413.46/ Closed under VO#03	P.02= 12 days
04-A	MRNII- Change in the Requirements, New Item, Revised Scope of Work and Existing Site Condition	April 17, 2014	$148,652.5/ Partially included under VO#03	P.01=21 days P.02 = 03 days
04-B	MRNII- Change in the Requirements, New Item, Revised Scope of Work and Existing Site Condition	June 17, 2014	$0.00 In Process	P.01= 38 days P.02= 21 days
05-A	Project 01- Change in the Requirements, New Item, Revised Scope of Work and Time Extension	April 26, 2014	35,193,88/Rejected	P.01= 4 days
06-A	Project 01- Time extension for Project #1 due to additional works performed / requested by CMC (Construction of new (Retaining Walls, Installation 12 inch & 3 and 2" inch steel pipeline and roundabouts)	May 13, 2014	$0.00 Rejected	P.01= 38 days
06-B		May 25, 2014	$0.00 Closed under VO#03	P.01= 38 days
07-A	Project 02- Revised Scope of Work- Limit construction activities from 0+000 to 2+180 and revised BOQ	May 18, 2014	($73,265) Closed under VO#03	00
08-A	Project 02- New Scope of Work, Change in the Scope of Work- Step Barriers, Retaining wall, and increase paved shoulder.	May 25, 2014	$ 207,724.7 Closed under VO#03	P.02= 21 days
09-A	MRNII- New Items, Existing Site Conditions	June 11, 2014	$ 133,315.60 Closed under VO#03	P.01= 38 days P.02= 21 days
10-A	Project 02- 600mm Storm Water Drainage Pipes	June 22, 2014	$41,917.56 In Process	P.02= Refer to VOR 8A
11-A	Project 01- Relocation of High Voltage Electric Towers and low Voltage Poles versus Installation of High Voltage Underground Cable	June 23, 2014	$0.00 Closed under VO#03	P.01= 38 Days

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

OBSTACLES AND CHALLENGES

Issue	Action
Project 01- NAB	
1. Relocation of existing High Voltage Electrical Towers (HVET) North District Electricity Company (NEDCO) indicated that relocation is not possible due to safety concerns (adjacent buildings) and desire the electrical cables be installed underground.	1. Intensive coordination with CMC, Nablus municipality and NEDCO were conducted, an agreement was drawn out to replace the overhead HV wires with an underground system to be implemented by our subcontractor in lieu of relocating the towers. Municipality insisted that APCO/ArCon be a signatory to the agreement, however, the IQC contract and Mission Order 21 prevent the prime contractor from signing such agreements. Issue is not resolved yet. APCO informed COR via email of planned meeting with mayor on March 31st, COR replied and indicated agreements have to comply with USAID regulations. APCO informed COR the same day that the mayor reiterated his previous position during the meeting. Consequently, APCO emailed the COR on April 21st that the issue still persists and requested direction, COR replied indicating that contractor can sign MOU, APCO emailed MOU to USAID on April 29th which was acknowledged by COR. MOU was finalized and signed by NEDCO on June 21, 2014. Underground cable installation and relocation of HVET commenced, issue resolved.
2. Existing deteriorated residence at St. 3+330 LHS. The residence construction elements exhibit severs long time major structural cracks rendering the residence unstable and beyond repair. A middle-aged mother and her four young children live in the residence with their life safety in serious jeopardy.	2. Specialty testing lab (Hijjawi Construction Labs) investigated and evaluated existing building conditions, their report dated April 27, 2014 indicated that the residence is structurally unstable and may collapse any time. USAID and CMC were informed; several meetings with Beit Iba village council, residence owners, Nablus municipality and Nablus governorate were conducted as detailed earlier in this report under the coordination log, a formal letter dated May 27, 2014 was submitted to CMC and USAID raising the contractor concerns regarding this issue. Construction in the area of the residence has been seized since this issue came to light, and a safe area in front of and around the structure is barricaded and fenced, our subcontractor and all personnel are under strict orders to stay away from doing any work regardless of how critical the construction activity maybe until it is safe to resume construction. Still waiting USAID and CMC further instructions. Issue is not resolved yet. Work stopped from St. 3+200 to St. 3+300 since April 28, 2014.
Project 02- DSR	
No Issues during this reporting period.	

USAID | WEST BANK/GAZA

PROGRESS PHOTOS:

Project 01- Before construction- At St. 2+280 (R.H.S) forward

Project 01- First Asphalt layer, storm water drainage system and sewerlines works- At St. 2+280 (R.H.S) forward

Project 01- Installation of concrete pipe for storm water from St. 1+820 to 1+860- backward

Project 01- Bedding and Placed warning tape along power cable trench from St. 1+980 to 2+620-backward

Project 01- Installation of UPVC crossing sleeves at St. 3+560- backward

Project 01- Grading and compacting base course 1st layer from St. 3+560 to 3+620 RHS- backward

Project 01- Rebar Work for Box culvert foundation at St. 3+610 RHS- backward

Project 01- Rebar work for Retaining Wall from St. 1+860 to 1+935RHS

Project 02- St. 0+700 Backward- Before Construction.

Project 02- St. 0+700 Backward- Bituminous binder course, excavation for 3" water pipe line, concrete ditches.

Project 02- Grading and compacting 2nd base course layer from 1+200-1+420 RHS.

Project 02- Asphalt Binder course layer works.

Project 02- Asphalt Binder course layer works.	Project 02- Shaping works for ditch from sta. 1+440 to St. 1+620.
Project 02- Insulation works for barrier beams.	Project 02- Casting concrete for barrier beam.

A | Materials- Equipments Receiving Log

Project 01: Nablus- Beit Iba- Deir Sharaf Road
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Equipment receiving log/June 2014

Date	Grader Cat, G12, H140		Bob Cat		Road Marking Machine		Pneumatic Asphalt Roller		JCB		Guardrail Machine		Truck Actros, 2007		Steel Roller		Truck w/ Crane		WATER TANK 10M3		Car		Pick Up(4*4)		Asphalt Steel Roller		Asphalt Finisher		Wheel Loader		Big Wheel Excavator		Chain excavator		Mobile Crusher		Asphalt Cutting Machine		Conrete Mixer		Concrete pump		Mobile Crusher		Milling Machine	
	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	2	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle
1-Jun	1		1						1				4		1				1		1								1		1			1					2		1					
2-Jun	1		1						2				4		1				1		1								1		1			1					1		1					
3-Jun	1		1						2				4		1				1		1								1		1			1												
4-Jun	1		1						2				4		1				1		1								1		1			1												
5-Jun	1		1						2				4		1				1		1								1		1			1												
6-Jun																																														
7-Jun	1		1						2				4		1				1		1								1		1			1												
8-Jun	1		1						2				4		1				1		1								1		1			1					1							
9-Jun	1		1						2				4		1				1		1								1		1			1												
10-Jun	1		1						2				4		1				1		1								1		1			1												
11-Jun	1		1						2				4		1				1		1								1		1			1												
12-Jun	1		1						2				6		1				1		1								1		1			1												
13-Jun																																														
14-Jun	1		1						2				6		1				1		1								1		1			1												
15-Jun	1		1						2				6		1				1		1								1		1			1					2		1					
16-Jun	1		1						2				6		1				1		1								1		1		1						2		1					
17-Jun	1		1						2				6		1				2		1								1		1			1												
18-Jun	1		1						2				6		1				2		1								1		1			1					2		1					
19-Jun	1		1						2				6		1		1		2		1								1		1			1					2		1					
20-Jun	1		1						2				4		1		1		1										1																	
21-Jun	1		1						2				6		1		1		2		1								1		1			1					2		1					
22-Jun	1		1						2				4		1		1		2		1								1		1			1					2		1					
23-Jun	1		1						2				4		1		1		1		1								1		1			1					2		1					
24-Jun	1		1						2				6		1		1		2		1								1		1			1					2		1					
25-Jun	1		1						2				6		1		1		2		1								1		1			1					1							
26-Jun	1		1						2				6		1		1		2		1								1		1			1					1							
27-Jun																																														
28-Jun	1		1						2				6		1		1		2		1								1		1			1					1							
29-Jun	2		1						2				6		1		1		2		1								1		1			1					1							
30-Jun	1		1						2				6		1		1		2		1								1		1			1					4		1					

Project 02: Deir Sharaf -Tulkarem Road
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Equipment receiving log/June 2014

Date	Grader Cat, G12, H140		Bob Cat		Road Marking Machine		Pneumatic Asphalt Roller		JCB		Guardrail Machine		Truck Actros, 2007		Steel Roller		Truck w/ Crane		WATER TANK 10M3		Car		Pick Up(4*4)		Asphalt Wheel Roller		Asphalt Finisher		Asphalt Cutting Machine		Chain Excavator		Wheel loader		Mobile Crusher		Trencher		Concrete Mixer		Concrete Pump	
	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle
1-Jun	2								1				3		1				1												1		1									
2-Jun	2								1				3		1				1												1		1									
3-Jun	2								1				3		1				1												1			1					4			
4-Jun	2								1				3		1				1												1		1						4		1	
5-Jun	2								1				3		2				1						2		1				1		1									
6-Jun																																										
7-Jun	2								1				3		2				1						2		1				1		1									
8-Jun	2								1				3		2				1												1		1						2		1	
9-Jun	2								1				3		2				1												1		1						2		1	
10-Jun	2								1				3		2				1						2		1					1	1						2			
11-Jun	2								1				3		1				1													1	1						2			
12-Jun	1								1				3		1				1													1							2		1	
13-Jun																																										
14-Jun	1								1				3		1				1													1							2		1	
15-Jun	1								1				3		1				1													1							2		1	
16-Jun	1								1				3		1				1													1										
17-Jun	1								1				3		1				1													1							2			
18-Jun	1						2		1				3		3				1								1					1							2		1	
19-Jun	1								1				3		1				1													1							2		1	
20-Jun	1								1				2		1				1													1										
21-Jun	1								1				3		1				1													1										
22-Jun	1								1				3		1				1													1							1			
23-Jun	1								2				2		2				1						1		1					1							1			
24-Jun	1								2				2		1				1													1							1			
25-Jun	1								2				2		1				1													1							1			
26-Jun	1								2				2		1				1													1							1			
27-Jun																																							4		1	
28-Jun	1								2				2		1				1													1							1			
29-Jun	1								1				1		1				1																							
30-Jun	1								1				1		1				1																							

Project 01: Nablus- Beit Iba- Deir Sharaf Road
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Materials Receiving Log/June,2014

Date	Material Delivered to Site	Quantity
1-Jun	Somsom	120 Tons
	Single Size	120 Tons
	Concrete B 300	15 m3
	Concrete B 200	3 m3
2-Jun	Somsom	90 Tons
	Single Size	60Tons
	Concrete B 300	7 m3
3-Jun	Sand	120 Tons
4-Jun	Topping	1200 Tons
	Curb stone	200 units
	Steel Pipes 3”	60 Tons
5-Jun	Single size	30 Tons
	Somsom	30 Tons
	Concrete B 300	2 m3
6-Jun		
7-Jun	Topping layer	220 Tons
8-Jun	Base course	1000 Tons
	Concrete B 200	5 m3
9-Jun	Base course	350 Tons
10-Jun	Base course	350 Tons
11-Jun	Single size	100 Tons
	Sand	17 Tons
12-Jun	Concrete B 200	5 m3
	Concrete B 300	4 m3
13-Jun		
14-Jun	Base course	459 Tons
15-Jun	Concrete B 300	16 m3
16-Jun	Concrete B 300	16 m3
	Base Course	405 Tons
17-Jun	Topping materials	357 Tons
	Base course	393 Tons
	Somsom	60 Tons
18-Jun	Topping materials	54 Tons
	Somsom	62 Tons
	Concrete B 300	15 m3
19-Jun	Base course	432 Tons
	Concrete B 200	27 m3
20-Jun	Topping layer	351 Tons
21-Jun	Concrete B 200	32 m3
22-Jun	Concrete B 200	18 m3
	Concrete B 300	15 m3

Project 01: Nablus- Beit Iba- Deir Sharaf Road
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Materials Receiving Log/June,2014

Date	Material Delivered to Site	Quantity
23-Jun		
24-Jun	Concrete B 300	13 m3
	Concrete B 350	2 m3
25-Jun	Topping	432 Tons
26-Jun	Base Course	297 Tons
	somsom	120 Tons
	Curbstone	600 Pcs
	Concrete	4 m3
27-Jun		
28-Jun	Base course	297 Tons
	Somsom	120
	Concrete	3.5 m3
29-Jun	Topping layer	100 Tons
	Base Course	120 Tons
30-Jun	Topping layer	100 Tons
	Base Course	120 Tons
	Concrete B 350	2 m3
	Concrete B300	65 m3

Project 02: Deir Sharaf - Tulkarem Road
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Materials Receiving Log/June,2014

Date	Material Delivered to Site	Quantity
1-Jun	Pulverization materials	160 m3
	Base course	280
2-Jun	Base course	500 m3
3-Jun	Base course	460 m3
	Concrete B 250	35.5 m3
4-Jun	Base course	400 m3
	Concrete B 250	60 m3
5-Jun	Base course	300 m3
	Asphalt binder course	560 Tons
6-Jun		
7-Jun	Base course	400 m3
	Asphalt binder course	450 ton
8-Jun	Base course	400 m3
	Concrete B 250	44 m3
9-Jun	Base course	400 m3
	Concrete B 250	44 m3
	Concrete B 200	4 m3
10-Jun	Asphalt binder Course	600 Tons
	Concrete B 250	16 m3
	Base course	480 m3
11-Jun	Base course	320 m3
	Concrete B 250	22 m3
12-Jun	Base course	150 Tons
	Concrete B 250	24 m3
13-Jun		
14-Jun	Base course	120 Tons
	Concrete B 250	32 m3
15-Jun	Base course	120 Tons
	Concrete B 250	42 m3
16-Jun	Base course	120 Tons
17-Jun	Base course	200 Tons
	Concrete B 250	11.5 m3
18-Jun	Base course	200 m3
	Concrete B 250	12 m3
	Asphalt	750 Tons
19-Jun	Base course	280 m3
	Concrete B 250	19 m3
20-Jun	Base course	180 m3
21-Jun	Base course	120 m3
22-Jun	Base course	250 m3
	Concrete B 250	14 m3

Project 02: Deir Sharaf - Tulkarem Road
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Materials Receiving Log/June,2014

Date	Material Delivered to Site	Quantity
23-Jun	Asphalt	300 Tons
	Concrete B 250	7 m3
24-Jun	Concrete B 250	12.5 m3
25-Jun	Concrete B 250	6 m3
26-Jun	Concrete B 250	6 m3
27-Jun	Concrete B 250	165 m3
28-Jun	Concrete B 250	22 m3
29-Jun		
30-Jun		

B | Detailed Time Schedule for the Project

BL2 is proposed by the Contractor and subject to USAID approval.

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
Multiple Roads Project North (II)		411d		190d	03-Dec-13	17-Jan-15	03-Dec-13 A	06-Jan-15	0d	$4,306,947	$15,007,339
Milestones		400d		190d	03-Dec-13	06-Jan-15	03-Dec-13 A	06-Jan-15	0d	$0	$0
General Milestone		400d		0d	03-Dec-13	06-Jan-15	03-Dec-13 A	06-Jan-15	0d	$0	$0
MRNII0000	Start Date NTP	0d	100%	0d	03-Dec-13		03-Dec-13 A			$0	$0
MRNII0010	Completion Task order	0d	0%	0d		06-Jan-15		06-Jan-15	0d	$0	$0
Intermediate Milestones		400d		190d	03-Dec-13	06-Jan-15	03-Dec-13 A	06-Jan-15	0d	$0	$0
Completion Milestones		139d		139d	20-Aug-14	06-Jan-15	20-Aug-14	06-Jan-15	0d	$0	$0
MRNII0020	Completion Project 2 Deir Sharaf Tulkarem Road	0d	0%	0d		20-Aug-14		20-Aug-14*	0d	$0	$0
MRNII0030	Completion Project 1 Nablus - Beit Iba - Deir Sharaf Road	0d	0%	0d		06-Jan-15		06-Jan-15	0d	$0	$0
Preconstuction Milestones		110d		0d	04-Dec-13	07-May-14	08-Dec-13 A	13-May-14 A		$0	$0
MRNII0040	Start Preconstruction Submittal	0d	100%	0d	04-Dec-13		08-Dec-13 A			$0	$0
MRNII0050	Finish Preconstruction Submittal	0d	100%	0d		07-May-14		13-May-14 A		$0	$0
PROJECT 01 Nablus - Beit Iba - Deir Sharaf Road		392d		190d	03-Dec-13	29-Dec-14	03-Dec-13 A	06-Jan-15	0d	$0	$0
Mobilization		13d		0d	07-Dec-13	23-Dec-13	04-Dec-13 A	23-Jan-14 A		$0	$0
MRNII0060	Start Mobilization	0d	100%	0d	07-Dec-13		04-Dec-13 A			$0	$0
MRNII0070	Finish Mobilization	0d	100%	0d		23-Dec-13		23-Jan-14 A		$0	$0
Shop Drawing		235d		0d	28-Dec-13	29-Oct-14	09-Jan-14 A	29-Oct-14	56d	$0	$0
MRNII0080	Start Shop Drawing Submittal	0d	100%	0d	28-Dec-13		09-Jan-14 A			$0	$0
MRNII0090	Finish Shop Drawing Submittal	0d	0%	0d		29-Oct-14		29-Oct-14	56d	$0	$0
Material		208d		0d	04-Jan-14	27-Sep-14	25-Dec-13 A	27-Sep-14	80d	$0	$0
MRNII0100	Start Material Submittal	0d	100%	0d	04-Jan-14		25-Dec-13 A			$0	$0
MRNII0110	Finish Material submittal	0d	0%	0d		27-Sep-14		27-Sep-14	80d	$0	$0
Construction		280d		0d	06-Jan-14	29-Dec-14	23-Jan-14 A	29-Dec-14	0d	$0	$0
MRNII0120	Start Construction (Ground Breaking)	0d	100%	0d	06-Jan-14		23-Jan-14 A			$0	$0
MRNII0130	Finish Construction Phase	0d	0%	0d		29-Dec-14		29-Dec-14	0d	$0	$0
Project Duration		364d		190d	03-Dec-13	01-Dec-14	03-Dec-13 A	06-Jan-15	0d	$0	$0
MRNII0140	Project Duration (Calendar Days)	364d	47.8%	190d	03-Dec-13	01-Dec-14	03-Dec-13 A	06-Jan-15	0d	$0	$0
MRNII0150	Project Duration (Working Days)	279d	48.66%	143d	03-Dec-13	01-Dec-14	03-Dec-13 A	06-Jan-15	0d	$0	$0
MRNII0160	Construction Duration (Working Days)	240d	42.69%	137d	06-Jan-14	10-Nov-14	23-Jan-14 A	29-Dec-14	0d	$0	$0
PROJECT 02 Deir Sharaf Tulkarem Road		287d		51d	03-Dec-13	15-Sep-14	03-Dec-13 A	20-Aug-14	0d	$0	$0

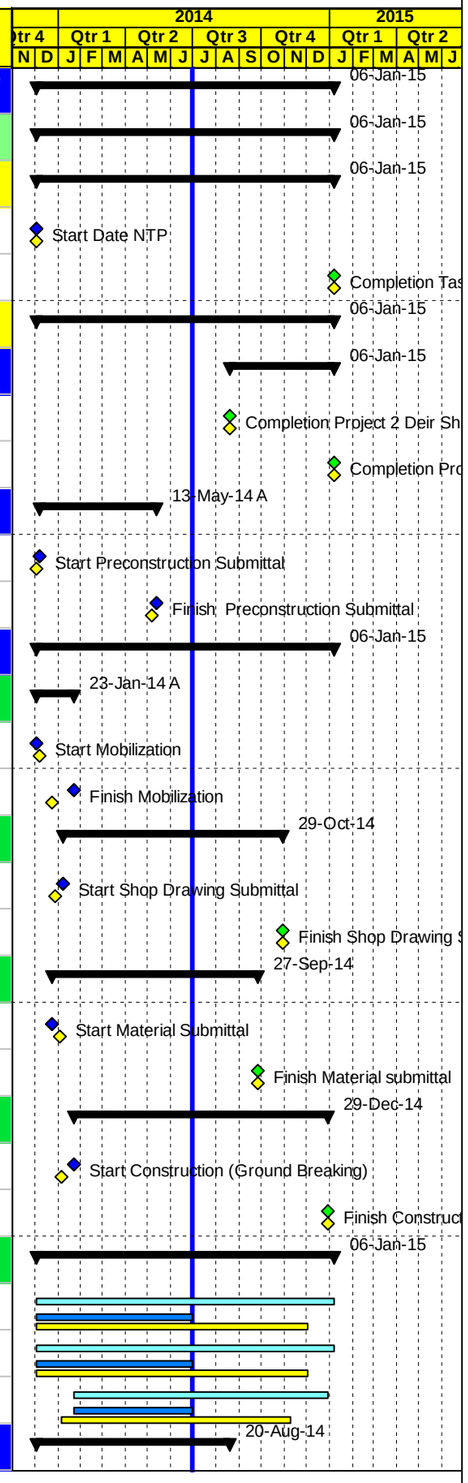

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Page 1 of 28

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
Mobilization		19d		0d	07-Dec-13	04-Jan-14	04-Dec-13 A	20-Jan-14 A		$0	$0
MRNII0170	Start Mobilization	0d	100%	0d	07-Dec-13		04-Dec-13 A			$0	$0
MRNII0180	Finish Mobilization	0d	100%	0d		04-Jan-14		20-Jan-14 A		$0	$0
Shop Drawing Milestones		108d		0d	01-Mar-14	12-Jul-14	15-Jan-14 A	12-Jul-14	25d	$0	$0
MRNII0190	Start Shop Drawing Submittal	0d	100%	0d	01-Mar-14		15-Jan-14 A			$0	$0
MRNII0200	Finish Shop Drawing Submittal	0d	0%	0d		12-Jul-14		12-Jul-14	25d	$0	$0
Material		102d		0d	01-Mar-14	01-Jul-14	25-Dec-13 A	25-Feb-14 A		$0	$0
MRNII0210	Start Material Submittal	0d	100%	0d	01-Mar-14		25-Dec-13 A			$0	$0
MRNII0220	Finish Material submittal	0d	100%	0d		01-Jul-14		25-Feb-14 A		$0	$0
Construction		117d		0d	12-Mar-14	13-Aug-14	23-Feb-14 A	13-Aug-14	0d	$0	$0
MRNII0230	Start Construction (Ground Breaking)	0d	100%	0d	12-Mar-14		23-Feb-14 A			$0	$0
MRNII0240	Finish Construction Phase	0d	0%	0d		13-Aug-14		13-Aug-14	0d	$0	$0
Project Duration		287d		51d	03-Dec-13	15-Sep-14	03-Dec-13 A	20-Aug-14	0d	$0	$0
MRNII0250	Project Duration (Calendar Days)	240d	78.81%	51d	03-Dec-13	30-Jul-14	03-Dec-13 A	20-Aug-14	0d	$0	$0
MRNII0260	Project Duration (Working Days)	179d	82.68%	31d	03-Dec-13	27-Jul-14	03-Dec-13 A	20-Aug-14	0d	$0	$0
MRNII0270	Construction Duration (Working Days)	145d	82.77%	25d	12-Mar-14	15-Sep-14	23-Feb-14 A	13-Aug-14	0d	$0	$0
Task order Duration		364d		190d	03-Dec-13	01-Dec-14	03-Dec-13 A	06-Jan-15	0d	$0	$0
MRNII0280	Project Duration (Calendar Days)	364d	47.8%	190d	03-Dec-13	01-Dec-14	03-Dec-13 A	06-Jan-15	0d	$0	$0
MRNII0290	Project Duration (Working Days)	279d	48.66%	143d	03-Dec-13	01-Dec-14	03-Dec-13 A	06-Jan-15	0d	$0	$0
Pre Construction Phase		162d		0d	04-Dec-13	14-May-14	08-Dec-13 A	13-May-14 A		$0	$0
Pre Construction Submittals		115d		0d	04-Dec-13	14-May-14	08-Dec-13 A	13-May-14 A		$0	$0
MRNII1100	Bank Guarantee Certificates	10d	100%	0d	05-Dec-13	18-Dec-13	08-Dec-13 A	31-Dec-13 A		$0	$0
MRNII1090	30- Day Schedule (Pre Construction Submittals & Mobilization phase)	10d	100%	0d	04-Dec-13	17-Dec-13	08-Dec-13 A	22-Dec-13 A		$0	$0
MRNII1110	Temporary and Permanent Project Sign Plan	10d	100%	0d	08-Dec-13	19-Dec-13	08-Dec-13 A	22-Dec-13 A		$0	$0
MRNII1190	Subcontractors' profile	10d	100%	0d	15-Dec-13	26-Dec-13	22-Dec-13 A	31-Dec-13 A		$0	$0
MRNII1130	Testing Lab	10d	100%	0d	10-Dec-13	23-Dec-13	23-Dec-13 A	05-Jan-14 A		$0	$0
MRNII1170	Key Personnel Plan	10d	100%	0d	12-Dec-13	25-Dec-13	25-Dec-13 A	31-Dec-13 A		$0	$0
MRNII1200	QCP-Quality Control Program	10d	100%	0d	15-Dec-13	26-Dec-13	25-Dec-13 A	09-Jan-14 A		$0	$0
MRNII1180	Safety Plan	10d	100%	0d	12-Dec-13	25-Dec-13	25-Dec-13 A	13-Jan-14 A		$0	$0
MRNII1140	Field Offices Furniture & Equipment Plan	10d	100%	0d	10-Dec-13	23-Dec-13	25-Dec-13 A	09-Feb-14 A		$0	$0

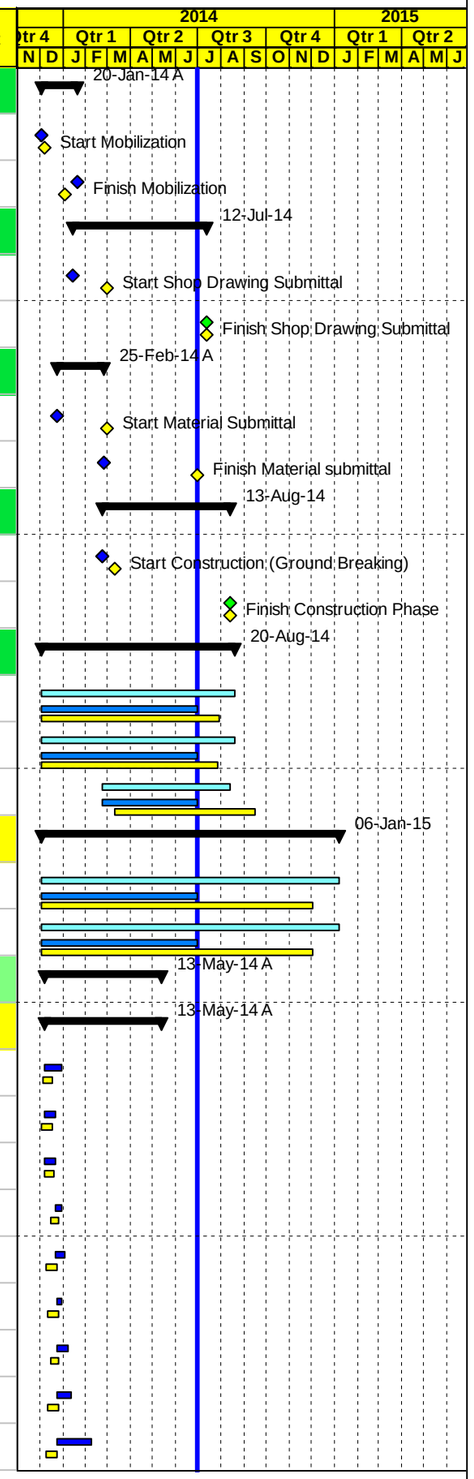

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
MRNII1260	USAID Branding Plan	10d	100%	0d	23-Dec-13	06-Jan-14	25-Dec-13 A	07-Jan-14 A		$0	$0
MRNII1120	Insurances	10d	100%	0d	08-Dec-13	19-Dec-13	25-Dec-13 A	06-Jan-14 A		$0	$0
MRNII1150	Existing Survey Plan for Project 01	10d	100%	0d	11-Dec-13	24-Dec-13	29-Dec-13 A	22-Jan-14 A		$0	$0
MRNII1230	Schedule Submittals	10d	100%	0d	17-Dec-13	30-Dec-13	29-Dec-13 A	13-Jan-14 A		$0	$0
MRNII1310	Method Statement Plan	10d	100%	0d	31-Dec-13	14-Jan-14	29-Dec-13 A	22-Jan-14 A		$0	$0
MRNII1330	CPM-Construction Schedule and S-Curve	10d	100%	0d	31-Dec-13	14-Jan-14	29-Dec-13 A	04-Mar-14 A		$0	$0
MRNII1240	60-Day Plan of Operation	10d	100%	0d	18-Dec-13	31-Dec-13	29-Dec-13 A	08-Jan-14 A		$0	$0
MRNII1245	Project Overview Bar Chart	10d	100%	0d	18-Dec-13	31-Dec-13	29-Dec-13 A	08-Jan-14 A		$0	$0
MRNII1210	Coordination with local Authorities Plan	10d	100%	0d	15-Dec-13	26-Dec-13	30-Dec-13 A	13-Jan-14 A		$0	$0
MRNII1160	Existing Survey Plan for Project 02	10d	100%	0d	12-Dec-13	25-Dec-13	31-Dec-13 A	14-Jan-14 A		$0	$0
MRNII1220	Field Offices Location & Layout	10d	100%	0d	15-Dec-13	26-Dec-13	06-Jan-14 A	09-Jan-14 A		$0	$0
MRNII1270	Dilapidation Survey (Project 01)	10d	100%	0d	26-Dec-13	09-Jan-14	07-Jan-14 A	05-Mar-14 A		$0	$0
MRNII1280	Dilapidation Survey (Project 02)	10d	100%	0d	26-Dec-13	09-Jan-14	15-Jan-14 A	21-Jan-14 A		$0	$0
MRNII1320	Environmental Mitigation Plan	10d	100%	0d	31-Dec-13	14-Jan-14	16-Jan-14 A	26-Jan-14 A		$0	$0
MRNII1290	Risk Management Plan (Project 01)	10d	100%	0d	26-Dec-13	09-Jan-14	19-Jan-14 A	03-Mar-14 A		$0	$0
MRNII1250-new	Proposed staging and storage yard -Nablus Beit Iba Der Sharaf Road -Project 01	10d	100%	0d	22-Dec-13	05-Jan-14	19-Jan-14 A	21-Jan-14 A		$0	$0
MRNII1340	Traffic Control Plan Phase I- from Sta.0+000 to Sta.2+180 (Project 02)	10d	100%	0d	30-Dec-13	13-Jan-14	26-Jan-14 A	05-Feb-14 A		$0	$0
MRNII1300	Risk Management Plan (Project 02)	10d	100%	0d	26-Dec-13	09-Jan-14	29-Jan-14 A	05-Feb-14 A		$0	$0
MRNII1350	Traffic Control Plan (Area A and B) from Sta.2+020 to Sta.2+540-Nablus Beit Iba Der Sharaf Road -Project 01	10d	100%	0d	30-Dec-13	13-Jan-14	05-Feb-14 A	06-Feb-14 A		$0	$0
MRNII1250	Proposed Dumping Area -Project 01	10d	100%	0d	22-Dec-13	05-Jan-14	11-Feb-14 A	12-Feb-14 A		$0	$0
MRNII1310-new	Traffic Control Plan from Sta.A2+540 to Sta.A3+500 -Phase II-Project 01	10d	100%	0d	10-Apr-14	23-Apr-14	17-Feb-14 A	02-Mar-14 A		$0	$0
MRNII1315-new	12" inch Procedure Qualification Record (PQR)	10d	100%	0d	20-Mar-14	02-Apr-14	05-Mar-14 A	20-Mar-14 A		$0	$0
MRNII1316-new	Welding Procedure 3-12 inch pipes- Project 01	10d	100%	0d	20-Mar-14	02-Apr-14	24-Mar-14 A	31-Mar-14 A		$0	$0
MRNII1317-new	Specific Method Statement for Sewer lines Leakage Testing Project 01	10d	100%	0d	01-Apr-14	14-Apr-14	25-Mar-14 A	30-Mar-14 A		$0	$0
MRNII1318-new	Traffic Control Plan from Sta.3+520 to Sta.4+620-Project 01	10d	100%	0d	10-Apr-14	23-Apr-14	08-Apr-14 A	28-Apr-14 A		$0	$0
MRNII1319-new	Special Method Statements for Hydrostatic Test for concrete pipes - project 01	10d	100%	0d	10-Apr-14	23-Apr-14	21-Apr-14 A	24-Apr-14 A		$0	$0
MRNII1320-new	Traffic Control Plan Phase II from Sta.0+000 to Sta.2+000 -Nablus Beit Iba Der Sharaf Road -Project 01	10d	100%	0d	24-Apr-14	07-May-14	28-Apr-14 A	13-May-14 A		$0	$0
MRNII1325-new	Confined space safety plan -Project 01	10d	100%	0d	01-May-14	14-May-14	06-May-14 A	08-May-14 A		$0	$0
Mobilization Offices		4d		0d	28-Dec-13	31-Dec-13	25-Dec-13 A	06-Jan-14 A		$0	$0
MRNII1370	Supply and install Office Furniture's and Supplies	3d	100%	0d	28-Dec-13	30-Dec-13	25-Dec-13 A	06-Jan-14 A		$0	$0

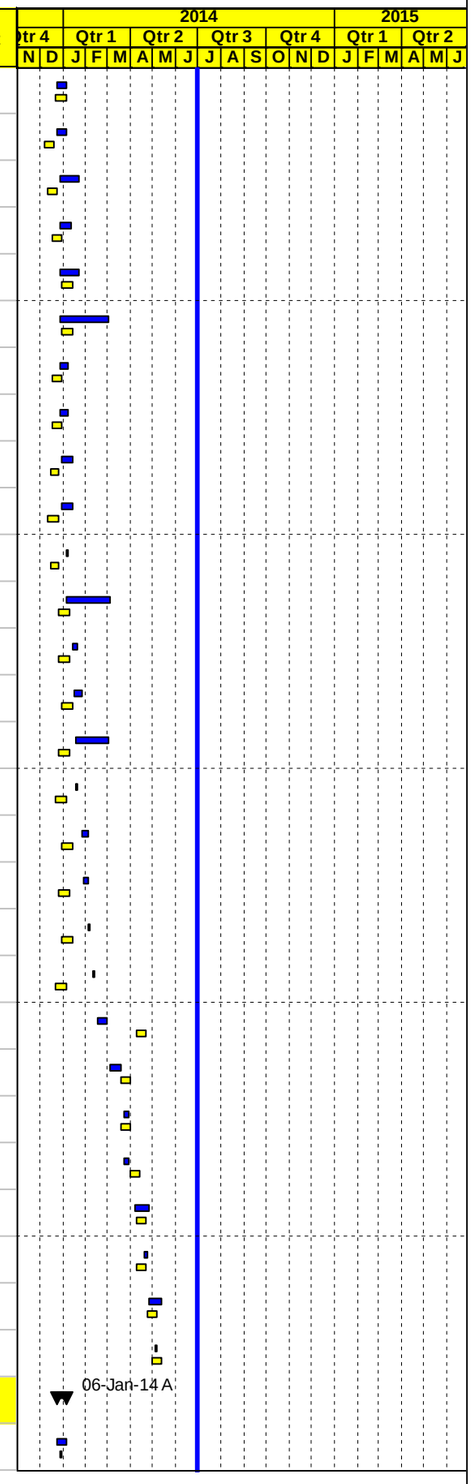

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
MRNII1380	Supply and install Office IT Equipments & Applience	3d	100%	0d	29-Dec-13	31-Dec-13	25-Dec-13 A	06-Jan-14 A		$0	$0
PROJECT 01 Nablus - Beit Iba - Deir Sharaf Road		411d		190d	03-Dec-13	17-Jan-15	03-Dec-13 A	06-Jan-15	0d	$3,123,891	$12,743,361
PROJECT 01 Preconstruction Phase		50d		12d	03-Dec-13	21-Jan-14	03-Dec-13 A	12-Jul-14	178d	$501,723	$501,723
PROJECT 01 Conformed Drawings and Coordination		40d		12d	03-Dec-13	11-Jan-14	03-Dec-13 A	12-Jul-14	178d	$0	$0
NAB0110	Coordination with Israeli authorities for approval and permit area C Project 01	40d	70%	12d	03-Dec-13	11-Jan-14	03-Dec-13 A	12-Jul-14	178d	$0	$0
NAB0100	Final for Construction Drawing (Conformed)	0d	100%	0d	03-Dec-13		03-Dec-13 A			$0	$0
PROJECT 01 Mobilization		31d		0d	07-Dec-13	21-Jan-14	04-Dec-13 A	23-Jan-14 A		$501,723	$501,723
NAB0140	Mobilization Total Cost (4.0%)	13d	100%	0d	07-Dec-13	23-Dec-13	04-Dec-13 A	23-Jan-14 A		$501,723	$501,723
NAB0170	Site Hand Over	1d	100%	0d	08-Dec-13	08-Dec-13	08-Dec-13 A	08-Dec-13 A		$0	$0
NAB0190	Start Preparation Construction Submittals (Survey plan , Shop Drawings & Materials)	13d	100%	0d	07-Dec-13	23-Dec-13	15-Dec-13 A	04-Jan-14 A		$0	$0
NAB0200	Install Temporary Project Sign	2d	100%	0d	20-Jan-14	21-Jan-14	20-Jan-14 A	20-Jan-14 A		$0	$0
NAB0205	Storage yard preparation and mobilizing equipment	3d	100%	0d	30-Dec-13	04-Jan-14	20-Jan-14 A	23-Jan-14 A		$0	$0
NAB0180	Checking With CMC Existing-Bench Marks, Survey Control Points	0d	100%	0d	11-Dec-13	11-Dec-13	22-Jan-14 A	22-Jan-14 A		$0	$0
PROJECT 01 Construction Phase		411d		182d	03-Dec-13	17-Jan-15	25-Dec-13 A	29-Dec-14	8d	$2,622,168	$12,116,208
PROJECT 01 Construction Submittals		331d		121d	03-Dec-13	29-Oct-14	25-Dec-13 A	29-Oct-14	69d	$0	$0
PROJECT 01 Shop Drawing Submittals		252d		87d	03-Dec-13	29-Oct-14	09-Jan-14 A	29-Oct-14	56d	$0	$0
Plan Profile and Cross Sections Phase One		177d		12d	03-Dec-13	23-Jul-14	09-Jan-14 A	23-Jul-14	19d	$0	$0
NAB0240	Main Road From St. A2+020 To St. A2+600	12d	100%	0d	03-Dec-13	18-Dec-13	09-Jan-14 A	09-Feb-14 A		$0	$0
NAB0250	Main Road From St. A2+600 To St. A3+000	12d	100%	0d	14-Dec-13	30-Dec-13	16-Feb-14 A	25-Feb-14 A		$0	$0
NAB0260	Main Road From St. A3+000 To St. A3+600	12d	100%	0d	01-Mar-14	15-Mar-14	02-Mar-14 A	26-Mar-14 A		$0	$0
NAB0270	Main Road From St. A3+600 To St. A4+100	12d	100%	0d	05-Mar-14	19-Mar-14	06-Mar-14 A	17-Mar-14 A		$0	$0
NAB0280	Main Road From St. A4+100 To St. A4+850	12d	100%	0d	01-Apr-14	14-Apr-14	27-Mar-14 A	07-May-14 A		$0	$0
NAB0301-new	Junction at Sta.3+420	12d	100%	0d	24-Apr-14	08-May-14	24-Apr-14 A	13-May-14 A		$0	$0
NAB0302-new	Junction at Sta.2+600 LHS and at Sta.2+640 RHS	12d	100%	0d	03-May-14	15-May-14	04-May-14 A	06-May-14 A		$0	$0
NAB0285-new	Junction from Sta.1+910 to Sta.2+040	12d	100%	0d	03-May-14	15-May-14	24-May-14 A	05-Jun-14 A		$0	$0
NAB0300	Main Road From St. A4+850 To St. A5+450	12d	0%	12d	01-Jul-14	23-Jul-14	01-Jul-14	23-Jul-14	19d	$0	$0
Plan Profile and Cross Sections Phase Two		83d		12d	07-Apr-14	23-Jul-14	10-Apr-14 A	23-Jul-14	61d	$0	$0
NAB0370	Main Road From St. A1+500 To St. A2+020	12d	100%	0d	07-Apr-14	21-Apr-14	10-Apr-14 A	05-May-14 A		$0	$0
NAB0360	Main Road From St. A1+000 To St. A1+500	12d	100%	0d	19-May-14	01-Jun-14	15-May-14 A	22-Jun-14 A		$0	$0
NAB0380	Seg B From St. B0+000 To St. B0+399	12d	50%	6d	25-Jun-14	14-Jul-14	18-Jun-14 A	12-Jul-14	67d	$0	$0

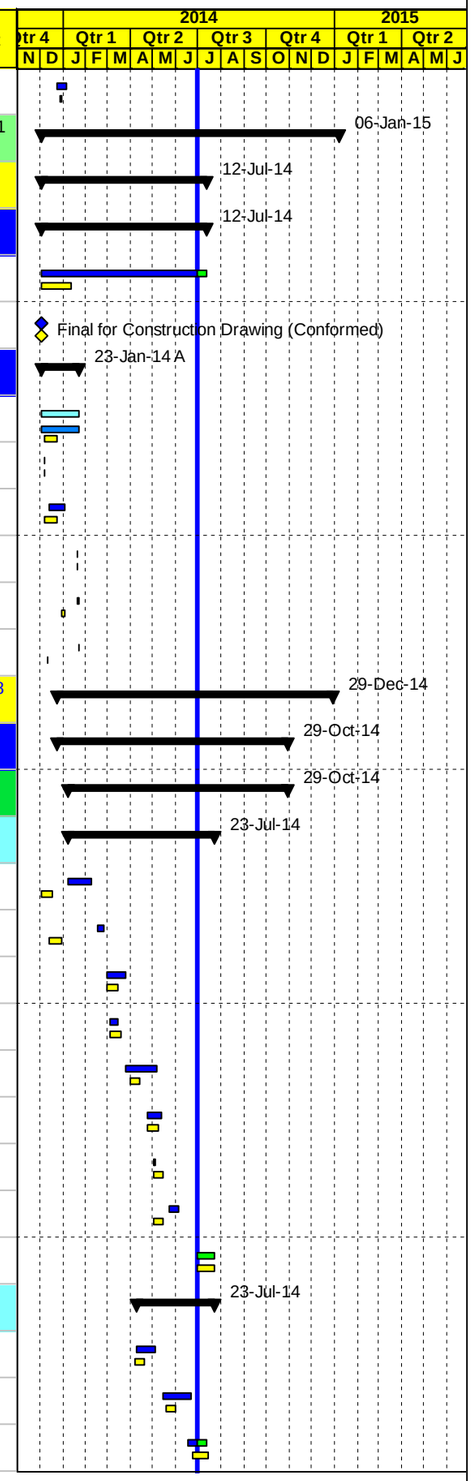

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB0340	Main Road From St. A0+000 To St. A1+000	12d	0%	12d	01-Jul-14	23-Jul-14	01-Jul-14	23-Jul-14	9d	$0	$0
Waterline		175d		12d	15-Jan-14	30-Aug-14	16-Jan-14 A	30-Aug-14	9d	$0	$0
NAB0400	Water pipeline from St. A 1+900 to A 2+500 (3") (LHS)	12d	100%	0d	15-Jan-14	01-Feb-14	16-Jan-14 A	20-Mar-14 A		$0	$0
NAB0400-NEW	12 " Deir Sharaf steel water pipeline from St. A 2+000 to A 3+000 (12") (RHS)	12d	100%	0d	20-Mar-14	02-Apr-14	17-Mar-14 A	23-Mar-14 A		$0	$0
NAB0401-NEW	12 " Deir Sharaf steel water pipeline from St. A 3+000 to A 4+100 (12") (RHS)	12d	100%	0d	20-Mar-14	02-Apr-14	03-Apr-14 A	08-Apr-14 A		$0	$0
NAB0402-NEW	3" Deir Sharaf steel water pipeline from St. A 2+900 to A 4+400 (3") (LHS)	12d	100%	0d	20-Mar-14	02-Apr-14	10-Apr-14 A	16-Apr-14 A		$0	$0
NAB0420	12" Deir Sharaf steel water pipeline from St. Sta.1+050 to Sta.2+000 (LHS)	12d	100%	0d	17-May-14	29-May-14	28-Apr-14 A	01-Jun-14 A		$0	$0
NAB0403-NEW	12 " Deir Sharaf steel water pipeline from St. A 4+100 to A 4+850 (12") (RHS)	12d	100%	0d	03-May-14	15-May-14	05-May-14 A	07-May-14 A		$0	$0
NAB0410	12 " Deir Sharaf steel water pipeline from St. A 0+060 to A 1+050 (12") (LHS)	12d	0%	12d	16-Aug-14	30-Aug-14	16-Aug-14	30-Aug-14	9d	$0	$0
Sewer line		160d		24d	15-Jan-14	12-Aug-14	20-Jan-14 A	12-Aug-14	103d	$0	$0
NAB0430	Sewer line (LHS) from St. 1+930 to 2+610 (12")	12d	100%	0d	15-Jan-14	01-Feb-14	20-Jan-14 A	09-Feb-14 A		$0	$0
NAB0435-new	Sewer line (LHS) from Sta.3+407 to Sta.3+560	12d	100%	0d	03-May-14	15-May-14	13-May-14 A	15-May-14 A		$0	$0
NAB0440	Sewer line (LHS) from St. 4+100 to 4+600 (12")	12d	50%	6d	01-Jul-14	23-Jul-14	26-Jun-14 A	12-Jul-14	121d	$0	$0
NAB0450	Sewer line (LHS) from St. 0+290 to 0+520 (10")	12d	0%	12d	23-Jul-14	12-Aug-14	23-Jul-14	12-Aug-14	52d	$0	$0
Concrete walls Phase One		183d		18d	03-Dec-13	05-Aug-14	06-Feb-14 A	05-Aug-14	61d	$0	$0
NAB0443-New	Retaining Wall from Sta.2+339 to Sta.2+369 (RHS)	12d	100%	0d	03-Dec-13	18-Dec-13	06-Feb-14 A	09-Feb-14 A		$0	$0
NAB0444-New	Concrete Wall from Sta.2+040 to Sta.2+065 (LHS)	12d	100%	0d	03-Dec-13	18-Dec-13	06-Feb-14 A	13-Mar-14 A		$0	$0
NAB0447-New	Retaining Wall from Sta.A2+475 to Sta.A2+515 (RHS)	12d	100%	0d	03-Dec-13	18-Dec-13	16-Feb-14 A	23-Feb-14 A		$0	$0
NAB0449-New	Retaining Wall from Sta.2+740 to Sta.2+850 (RHS)	12d	100%	0d	01-Mar-14	15-Mar-14	02-Mar-14 A	05-Mar-14 A		$0	$0
NAB0451-New	Retaining Wall from Sta.A2+980 to Sta.A3+010 (LHS)	12d	100%	0d	01-Mar-14	15-Mar-14	10-Mar-14 A	31-Mar-14 A		$0	$0
NAB0452-New	Retaining Wall from Sta.A2+719 to Sta.A2+730 (LHS) L= 11m	12d	100%	0d	24-Apr-14	08-May-14	10-Mar-14 A	05-May-14 A		$0	$0
NAB0461-New	Retaining Wall from Sta.3+230 to Sta.3+300 (RHS) L= 70 m	12d	100%	0d	13-Mar-14	26-Mar-14	16-Mar-14 A	06-Apr-14 A		$0	$0
NAB0467-New	Retaining Wall from Sta.3+230 to Sta.3+300 (RHS) L= 70 m	12d	100%	0d	13-Mar-14	26-Mar-14	16-Mar-14 A	06-Apr-14 A		$0	$0
NAB0460	Conc. Retaining walls from A3+160 to A3+190 (LHS) L= 40 m & A3+160 to A3+190 (RHS) L= 40 m	12d	100%	0d	19-Apr-14	04-May-14	19-Mar-14 A	31-Mar-14 A		$0	$0
NAB0462-New	Conc. Retaining walls from Sta.A3+560 to Sta.A3+590 (RHS)	12d	100%	0d	13-Mar-14	26-Mar-14	19-Mar-14 A	24-Mar-14 A		$0	$0
NAB0463-New	Conc. Retaining walls from Sta.A3+010 to Sta.A3+020 (RHS)	12d	100%	0d	13-Mar-14	26-Mar-14	24-Mar-14 A	27-Mar-14 A		$0	$0
NAB0466-New	Retaining Wall from Sta.A3+341 to Sta.A3+370 (RHS) L= 29 m	12d	100%	0d	10-Apr-14	24-Apr-14	25-Mar-14 A	22-Apr-14 A		$0	$0
NAB0464-New	Conc. Retaining walls from Sta.3+655 to Sta.3+695 (RHS)	12d	100%	0d	13-Mar-14	26-Mar-14	27-Mar-14 A	06-Apr-14 A		$0	$0
NAB0465-New	Conc. Retaining walls from Sta.3+373 to Sta.3+402 (LHS)	12d	100%	0d	13-Mar-14	26-Mar-14	31-Mar-14 A	06-Apr-14 A		$0	$0
NAB0470	Conc. Retaining walls from A3+828.5 to A3+855.5 (RHS) L= 27 m	12d	100%	0d	19-Apr-14	04-May-14	03-Apr-14 A	05-May-14 A		$0	$0

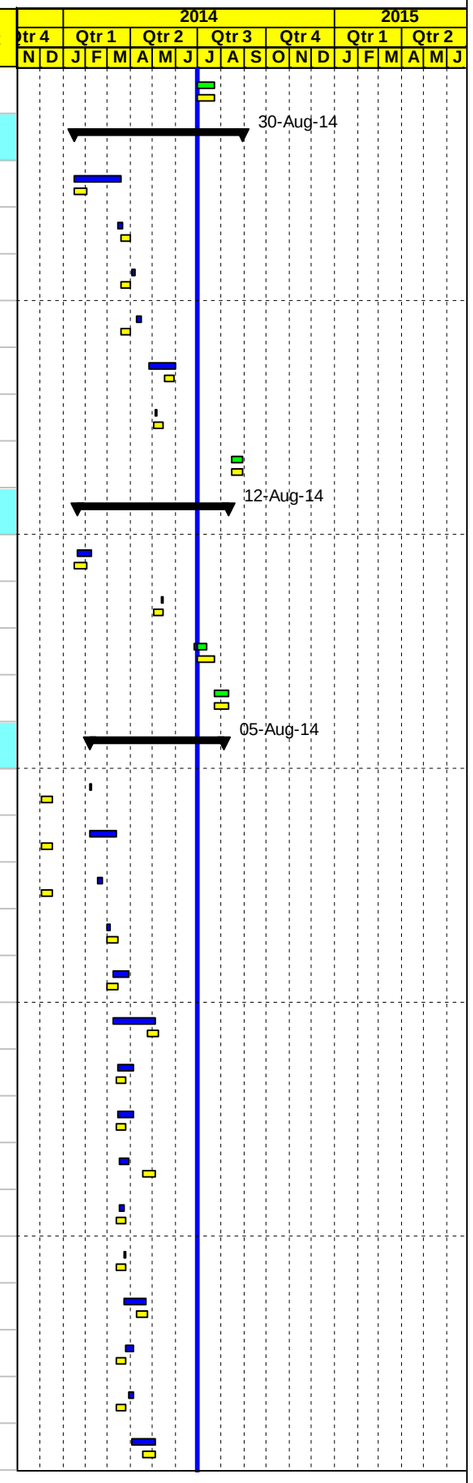

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB0480	Conc. Retaining walls from A3+950 to A3+982 (LHS) L= 32 m	12d	100%	0d	01-Jul-14	23-Jul-14	03-Apr-14 A	30-Apr-14 A		$0	$0
NAB0468-New	Boundary wall from Sta.3+950 to Sta.3+985 (LHS)	12d	100%	0d	13-Mar-14	26-Mar-14	03-Apr-14 A	30-Apr-14 A		$0	$0
NAB0469-New	Retaining Wall from Sta.4+090 to Sta.4+100	12d	50%	6d	24-Apr-14	08-May-14	24-Apr-14 A	12-Jul-14	61d	$0	$0
NAB0472-New	Retaining Wall from Sta.3+217 to Sta.3+226 LHS L= 9 m and Concrete Stair from Sta. 3+226 to Sta.3+229 LHS L= 3	12d	100%	0d	03-May-14	15-May-14	07-May-14 A	19-May-14 A		$0	$0
NAB0473-New	Retaining Wall from Sta.3+715 to Sta.3+740 LHS L= 25 m	12d	100%	0d	03-May-14	15-May-14	12-May-14 A	22-Jun-14 A		$0	$0
NAB0500	Conc. Retaining walls from A4+545 to Sta.A4+617 RHS L= 72 m	12d	100%	0d	02-Jun-14	15-Jun-14	13-May-14 A	21-May-14 A		$0	$0
NAB0510	Conc. Retaining walls from A4+830 to A4+865 (RHS) L= 35 m	12d	100%	0d	16-Jun-14	30-Jun-14	14-May-14 A	21-May-14 A		$0	$0
NAB0490	Conc.boundary walls from A4+578 to A4+600 (LHS) L= 22 m	12d	0%	12d	12-Jul-14	05-Aug-14	12-Jul-14	05-Aug-14	61d	$0	$0
Concrete walls Phase Two		77d		19d	03-May-14	14-Aug-14	04-May-14 A	14-Aug-14	117d	$0	$0
NAB0470-New	Retaining Wall from Sta.1+720 to Sta.1+750 RHS L= 30 m	12d	100%	0d	03-May-14	15-May-14	04-May-14 A	07-May-14 A		$0	$0
NAB0471-New	Retaining Wall from Sta.1+865 to Sta.1+930 RHS L= 65 m	12d	100%	0d	03-May-14	15-May-14	05-May-14 A	07-May-14 A		$0	$0
NAB0550	Retaining walls with step barrier & channel from A`1+000 to A1+110 (RHS) L= 110 m	12d	0%	12d	14-Jul-14	06-Aug-14	14-Jul-14	06-Aug-14	22d	$0	$0
NAB0520	Retaining walls with step barrier & channel from A0+500 to A0+620 (RHS) L= 120 m	12d	0%	12d	23-Jul-14	12-Aug-14	23-Jul-14	12-Aug-14	65d	$0	$0
NAB0530	Retaining walls with step barrier & channel from A0+750 to A0+910 (RHS) L= 160 m	12d	0%	12d	23-Jul-14	12-Aug-14	23-Jul-14	12-Aug-14	73d	$0	$0
NAB0540	Retaining walls with step barrier & channel from A0+916 to A1+000 (RHS) L= 84 m	12d	0%	12d	23-Jul-14	12-Aug-14	23-Jul-14	12-Aug-14	119d	$0	$0
NAB0560	Conc. Retaining walls from B0+230 to B0+340 LHS L= 110 m	12d	0%	12d	27-Jul-14	14-Aug-14	27-Jul-14	14-Aug-14	67d	$0	$0
60 cm Conc. Pipes for drainage LHS Phase One		157d		21d	15-Jan-14	09-Aug-14	16-Jan-14 A	09-Aug-14	122d	$0	$0
NAB0590	60 cm Conc. Pipes for drainage from A2+500 to A2+580 L= 80 m	12d	100%	0d	01-Mar-14	15-Mar-14	16-Jan-14 A	13-Feb-14 A		$0	$0
NAB0570	60 cm Conc. Pipes for drainage from A2+020 to A2+180 L= 160 m	12d	100%	0d	15-Jan-14	01-Feb-14	16-Jan-14 A	13-Feb-14 A		$0	$0
NAB0580	60 cm Conc. Pipes for drainage from A2+220 to A2+500 L= 280 m	12d	100%	0d	20-Jan-14	04-Feb-14	16-Jan-14 A	13-Feb-14 A		$0	$0
NAB0610	60 cm Conc. Pipes for drainage from A2+870 to A2+980 L= 110 m	12d	100%	0d	16-Mar-14	29-Mar-14	06-Mar-14 A	10-Mar-14 A		$0	$0
NAB0600	60 cm Conc. Pipes for drainage from A2+580 to A2+980 L= 160 m	12d	100%	0d	09-Mar-14	22-Mar-14	06-Mar-14 A	10-Mar-14 A		$0	$0
NAB0630	60 cm Conc. Pipes for drainage from Sta.3+600 to Sta.3+840 L= 240 m	12d	100%	0d	03-May-14	15-May-14	14-Apr-14 A	13-May-14 A		$0	$0
NAB0601	60 cm Conc. Pipes for drainage from Sta.3+000 to Sta.3+120	12d	100%	0d	17-Apr-14	03-May-14	17-Apr-14 A	21-Apr-14 A		$0	$0
NAB0602-	60 cm Conc. Pipes for drainage from Sta.4+100 to Sta.4+560	12d	50%	6d	01-Jul-14	23-Jul-14	26-Jun-14 A	12-Jul-14	137d	$0	$0
NAB0650	60 cm Conc. Pipes for drainage from A4+600 to A4+800 L= 200 m	12d	0%	12d	01-Jul-14	23-Jul-14	01-Jul-14	23-Jul-14	18d	$0	$0
NAB0660	60 cm Conc. Pipes for drainage from A4+840 to A5+000 L= 160 m	12d	0%	12d	12-Jul-14	05-Aug-14	12-Jul-14	05-Aug-14	18d	$0	$0
NAB0670	60 cm Conc. Pipes for drainage from A5+000 to A5+120 L= 120 m	12d	0%	12d	17-Jul-14	09-Aug-14	17-Jul-14	09-Aug-14	18d	$0	$0
60 cm Conc. Pipes for drainage RHS Phase Two		30d		25d	25-Jun-14	13-Aug-14	19-May-14 A	13-Aug-14	118d	$0	$0
NAB0740	60 cm Conc. Pipes for drainage from A1+690 to A2+020 L= 330 m	12d	100%	0d	13-Jul-14	05-Aug-14	19-May-14 A	27-May-14 A		$0	$0

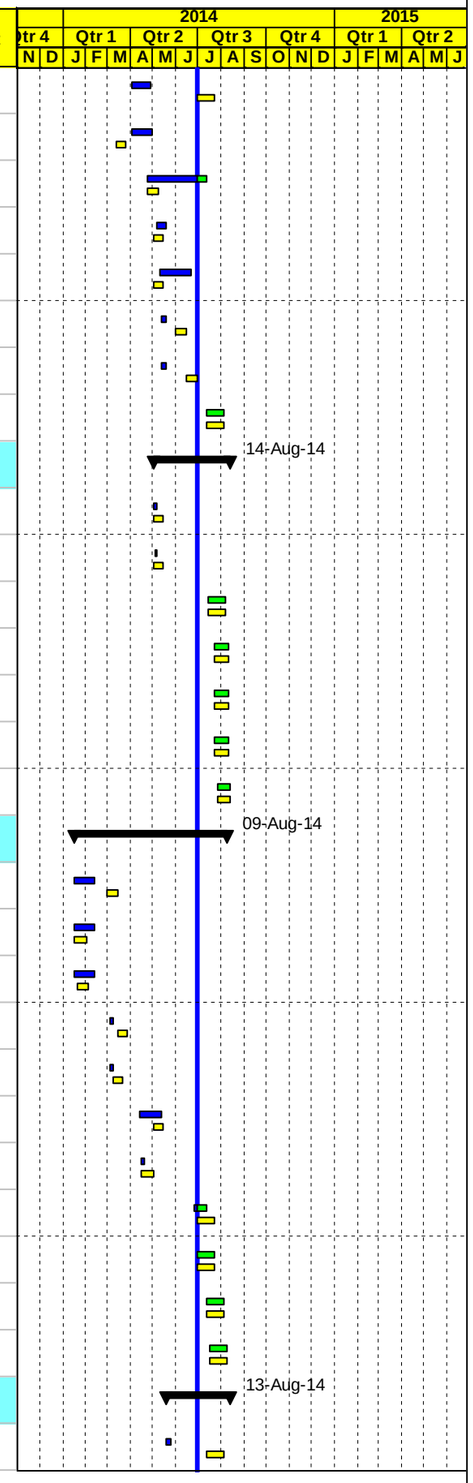

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB0745-new	60 cm Conc. Pipes for drainage from Sta.0+030 to Sta.0+180	12d	50%	6d	25-Jun-14	14-Jul-14	15-Jun-14 A	12-Jul-14	58d	$0	$0
NAB0720	60 cm Conc. Pipes for drainage from A1+300 to A1+500 L= 200 m	12d	50%	6d	06-Jul-14	02-Aug-14	26-Jun-14 A	12-Jul-14	34d	$0	$0
NAB0710	60 cm Conc. Pipes for drainage from A1+100 to A1+260 L= 160 m	12d	50%	6d	20-Jul-14	10-Aug-14	28-Jun-14 A	12-Jul-14	37d	$0	$0
NAB0730	60 cm Conc. Pipes for drainage from A1+500 to A1+620 L= 120 m	12d	0%	12d	01-Jul-14	23-Jul-14	01-Jul-14	23-Jul-14	131d	$0	$0
NAB0700	60 cm Conc. Pipes for drainage from A0+580 to A0+740 L= 160 m	12d	0%	12d	09-Jul-14	03-Aug-14	09-Jul-14	03-Aug-14	37d	$0	$0
NAB0690	60 cm Conc. Pipes for drainage from A0+360 to A0+460 L= 100 m	12d	0%	12d	22-Jul-14	11-Aug-14	22-Jul-14	11-Aug-14	39d	$0	$0
NAB0680	60 cm Conc. Pipes for drainage from A0+140 to A0+300 L= 160 m	12d	0%	12d	26-Jul-14	13-Aug-14	26-Jul-14	13-Aug-14	39d	$0	$0
New Conc.Pipe Culvert Dia. 80 cm and Box Culvert RHS Phase One		130d		30d	12-Mar-14	27-Aug-14	16-Jan-14 A	27-Aug-14	18d	$0	$0
NAB0750	New Conc.Pipe Culvert Dia. 80 cm @ St. A2+220 length L= 55 m	12d	100%	0d	12-Mar-14	25-Mar-14	16-Jan-14 A	13-Feb-14 A		$0	$0
NAB0790	New double box culvert 2 (2*2) @ St. A3+610 length L= 66 m	12d	100%	0d	12-Mar-14	25-Mar-14	15-May-14 A	04-Jun-14 A		$0	$0
NAB0800	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+240 length L= 12 m	12d	0%	12d	14-Jul-14	06-Aug-14	14-Jul-14	06-Aug-14	29d	$0	$0
NAB0810	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+600 length L= 9 m	12d	0%	12d	26-Jul-14	13-Aug-14	26-Jul-14	13-Aug-14	29d	$0	$0
NAB0820	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+840 length L= 9 m	12d	0%	12d	26-Jul-14	13-Aug-14	26-Jul-14	13-Aug-14	29d	$0	$0
NAB0830	New Conc.Pipe Culvert Dia. 80 cm @ St. A5+160 length L= 15 m	12d	0%	12d	13-Aug-14	27-Aug-14	13-Aug-14	27-Aug-14	18d	$0	$0
New Conc.Pipe Culvert Dia. 80 cm and Box Culvert RHS Phase Two		22d		22d	12-Jul-14	17-Aug-14	12-Jul-14	17-Aug-14	72d	$0	$0
NAB0940	New Conc.Pipe Culvert Dia.80 cm @ St. A1+300 length L= 84 m	12d	0%	12d	12-Jul-14	05-Aug-14	12-Jul-14	05-Aug-14	50d	$0	$0
NAB0910	New Conc.Pipe Culvert Dia.80 cm @ St. A1+100 length L= 14 m	12d	0%	12d	14-Jul-14	06-Aug-14	14-Jul-14	06-Aug-14	54d	$0	$0
NAB0930	New box culvert (2*2.5) @ St. A1+095 RHS length L= 15.5 m	12d	0%	12d	14-Jul-14	06-Aug-14	14-Jul-14	06-Aug-14	51d	$0	$0
NAB0890	New box culvert (2*2.5) @ St. A0+595 RHS length L= 7 m	12d	0%	12d	16-Jul-14	07-Aug-14	16-Jul-14	07-Aug-14	80d	$0	$0
NAB0900	New Conc.Pipe Culvert Dia.80 cm @ St. A0+700 length L= 14 m	12d	0%	12d	20-Jul-14	10-Aug-14	20-Jul-14	10-Aug-14	76d	$0	$0
NAB0860	New Conc.Pipe Culvert Dia.80 cm @ St. A0+360 length L= 29 m	12d	0%	12d	22-Jul-14	11-Aug-14	22-Jul-14	11-Aug-14	66d	$0	$0
NAB0840	New Conc.Pipe Culvert Dia. 60 cm @ St. A0+000 length L= 60 m	12d	0%	12d	23-Jul-14	12-Aug-14	23-Jul-14	12-Aug-14	42d	$0	$0
NAB0850	New Conc.Pipe Culvert Dia.80 cm @ St. A0+140 length L= 67 m	12d	0%	12d	26-Jul-14	13-Aug-14	26-Jul-14	13-Aug-14	39d	$0	$0
NAB0920	New box culvert (2*2.5) @ St. A0+915 RHS length L= 6 m	12d	0%	12d	26-Jul-14	13-Aug-14	26-Jul-14	13-Aug-14	37d	$0	$0
NAB0870	New box culvert (2*2.5) @ St. A0+510 RHS length L= 11 m	12d	0%	12d	02-Aug-14	14-Aug-14	02-Aug-14	14-Aug-14	71d	$0	$0
NAB0880	New Conc.Pipe Culvert Dia.80 cm @ St. A0+580 length L= 11.5 m	12d	0%	12d	04-Aug-14	17-Aug-14	04-Aug-14	17-Aug-14	72d	$0	$0
Connection and Valves Chambers		48d		48d	30-Aug-14	29-Oct-14	30-Aug-14	29-Oct-14	9d	$0	$0
NAB1000	250 Wash out chamber @ A0+070	12d	0%	12d	30-Aug-14	13-Sep-14	30-Aug-14	13-Sep-14	9d	$0	$0
NAB1010	80 ARV chamber @ A0+810 , B0+100 & B0+365	12d	0%	12d	03-Sep-14	17-Sep-14	03-Sep-14	17-Sep-14	9d	$0	$0
NAB1020	200 Wash out chamber @ A0+820	12d	0%	12d	17-Sep-14	01-Oct-14	17-Sep-14	01-Oct-14	9d	$0	$0

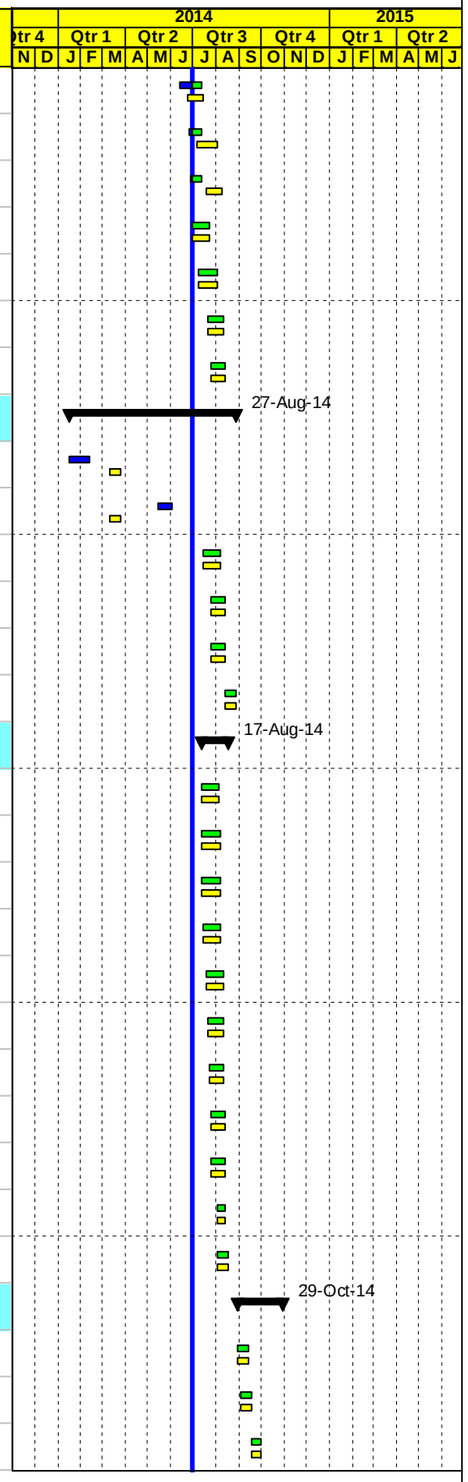

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB1030	Nablus connection chamber st B 0+035 (RHS)	12d	0%	12d	23-Sep-14	12-Oct-14	23-Sep-14	12-Oct-14	9d	$0	$0
NAB1040	Qusin flow monitoring chamber st B 0+190 (RHS	12d	0%	12d	29-Sep-14	18-Oct-14	29-Sep-14	18-Oct-14	9d	$0	$0
NAB1050	Beit Eba connection chamber st B 0+340 (LHS)	12d	0%	12d	09-Oct-14	23-Oct-14	09-Oct-14	23-Oct-14	9d	$0	$0
NAB1060	SHAVI SHAMRON monitoring chamber	12d	0%	12d	15-Oct-14	29-Oct-14	15-Oct-14	29-Oct-14	9d	$0	$0
Stone Walls		36d		0d	24-Apr-14	05-Jun-14	16-Apr-14 A	13-May-14 A		$0	$0
NAB1110	Stone wall from (Sta.A2+980 to Sta.A3+010 LHS) L=30 m (LHS)	12d	100%	0d	10-May-14	22-May-14	16-Apr-14 A	21-Apr-14 A		$0	$0
NAB1120	Stone wall from (A3+162 to Sta.A3+189) L=27 m (LHS)	12d	100%	0d	15-May-14	28-May-14	16-Apr-14 A	21-Apr-14 A		$0	$0
NAB1121-new	Stone Wall from Sta.3+376 to Sta.3+402 L= 26 m (LHS)	5d	100%	0d	24-Apr-14	29-Apr-14	24-Apr-14 A	28-Apr-14 A		$0	$0
NAB1160	Stone wall from A4+710 to A4+780 L=70 m (LHS)	12d	100%	0d	24-May-14	05-Jun-14	12-May-14 A	13-May-14 A		$0	$0
Otheres		128d		0d	20-Mar-14	02-Sep-14	19-Feb-14 A	02-Sep-14	75d	$0	$0
NAB5050-new	Street Lighting Poles from Sta.2+033 to Sta.2+983	12d	100%	0d	20-Mar-14	02-Apr-14	19-Feb-14 A	25-May-14 A		$0	$0
NAB5055-new	Street Lighting Poles from Sta.1+500 to Sta.2+000 &from sta.3+000 to Sta.4+850	12d	100%	0d	25-Jun-14	14-Jul-14	18-Jun-14 A	22-Jun-14 A		$0	$0
NAB5060-new	Side Walk from sta.2+000 to sta.2+600	12d	100%	0d	25-Jun-14	14-Jul-14	18-Jun-14 A	23-Jun-14 A		$0	$0
NAB1250	Road furnishing/Gurad Rail	0d	0%	0d	02-Sep-14	02-Sep-14	02-Sep-14	02-Sep-14	75d	$0	$0
PROJECT 01 Material Submittals		267d		89d	04-Jan-14	27-Sep-14	25-Dec-13 A	27-Sep-14	101d	$0	$0
NAB1340	UPVC	12d	100%	0d	22-Jan-14	05-Feb-14	25-Dec-13 A	13-Jan-14 A		$0	$0
NAB1290	Concrete Pipes	12d	100%	0d	01-Mar-14	15-Mar-14	25-Dec-13 A	15-Jan-14 A		$0	$0
NAB1410	Prime Coat	12d	100%	0d	01-Mar-14	15-Mar-14	25-Dec-13 A	05-Jan-14 A		$0	$0
NAB1420	Tack Coat	12d	100%	0d	01-Mar-14	15-Mar-14	25-Dec-13 A	05-Jan-14 A		$0	$0
NAB1520	Cat eyes	12d	100%	0d	01-Mar-14	15-Mar-14	25-Dec-13 A	05-Jan-14 A		$0	$0
NAB1530	Thermoplastic paint	12d	100%	0d	01-Mar-14	15-Mar-14	25-Dec-13 A	05-Jan-14 A		$0	$0
NAB1560	Curbstone paint material	12d	100%	0d	01-Mar-14	15-Mar-14	25-Dec-13 A	05-Jan-14 A		$0	$0
NAB1445	Concrete joint sealant material	12d	100%	0d	01-Mar-14	15-Mar-14	25-Dec-13 A	15-Jan-14 A		$0	$0
NAB1440	Bituminous Wearing Course-Mix Design	12d	100%	0d	08-Feb-14	20-Feb-14	30-Dec-13 A	09-Jan-14 A		$0	$0
NAB1400	Curbstone	12d	100%	0d	05-Feb-14	19-Feb-14	30-Dec-13 A	31-Dec-13 A		$0	$0
NAB1430	Bituminous Binder Course-Mix Design	12d	100%	0d	08-Feb-14	20-Feb-14	02-Jan-14 A	09-Jan-14 A		$0	$0
NAB1550	Traffic sign	12d	100%	0d	01-Mar-14	15-Mar-14	05-Jan-14 A	08-Jan-14 A		$0	$0
NAB1270	Steel pipeline	12d	100%	0d	04-Jan-14	21-Jan-14	19-Jan-14 A	27-Jan-14 A		$0	$0
NAB1310	Base Course Source	12d	100%	0d	01-Mar-14	15-Mar-14	22-Jan-14 A	26-Jan-14 A		$0	$0
NAB1360	Bedding material	12d	100%	0d	27-Jan-14	10-Feb-14	22-Jan-14 A	26-Jan-14 A		$0	$0

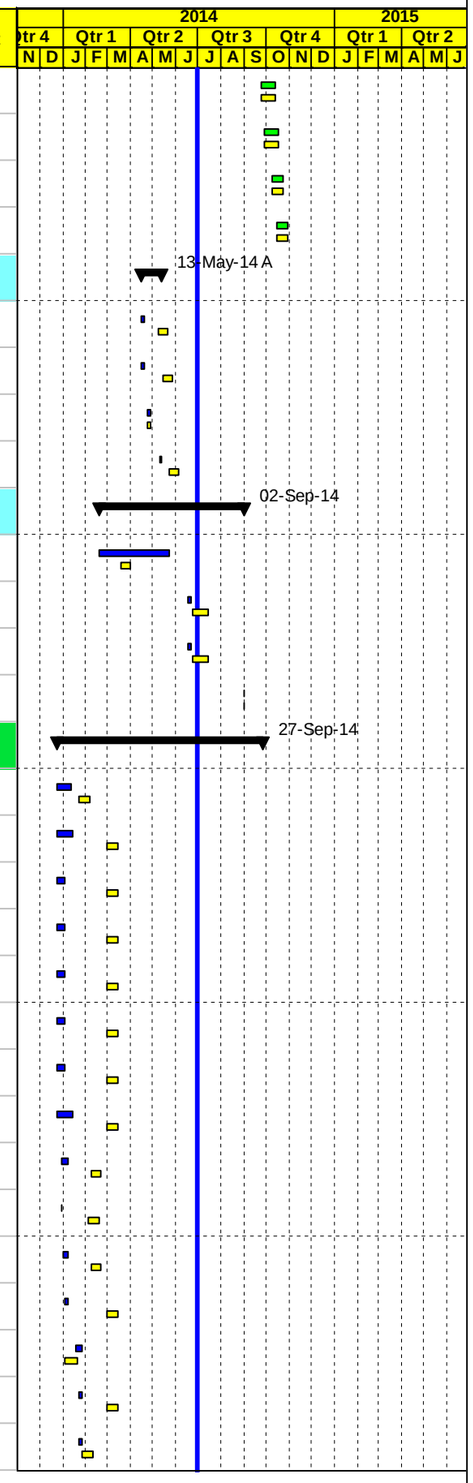

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB1350	Backfilling material	12d	100%	0d	01-Mar-14	15-Mar-14	22-Jan-14 A	26-Jan-14 A		$0	$0
NAB1280	Concrete Mix Design including Cement type	12d	100%	0d	08-Jan-14	25-Jan-14	28-Jan-14 A	03-Feb-14 A		$0	$0
NAB1370	Manholes and catch basin	12d	100%	0d	01-Feb-14	15-Feb-14	04-Feb-14 A	11-Feb-14 A		$0	$0
NAB1380	Cast iron manhole and catch basin cover	12d	100%	0d	02-Feb-14	16-Feb-14	04-Feb-14 A	11-Feb-14 A		$0	$0
NAB1573-new	Galvanized Malleable Iron Fittings up to 2 inch	12d	100%	0d	01-Mar-14	15-Mar-14	17-Feb-14 A	25-Feb-14 A		$0	$0
NAB1300	Steel Reinforcement	12d	100%	0d	01-Mar-14	15-Mar-14	19-Feb-14 A	23-Feb-14 A		$0	$0
NAB1564-new	Concrete Water Proofer for Manholes outside painting	12d	100%	0d	01-Mar-14	15-Mar-14	19-Feb-14 A	23-Feb-14 A		$0	$0
NAB1565	Street Lighting	12d	100%	0d	29-Mar-14	10-Apr-14	23-Feb-14 A	02-Mar-14 A		$0	$0
NAB1563-new	Epoxy Paint for Concrete protection	12d	100%	0d	01-Mar-14	15-Mar-14	02-Mar-14 A	05-Mar-14 A		$0	$0
NAB1565-new	Precast Concrete Curbstone & Edge beam	12d	100%	0d	03-May-14	15-May-14	21-May-14 A	26-May-14 A		$0	$0
NAB1567-new	Lamp,Cable and Cobra Pipe for street lighting	12d	100%	0d	28-May-14	10-Jun-14	28-May-14 A	05-Jun-14 A		$0	$0
NAB1566-new	Portland Cement Sulfate Resisting for concrete benching for manholes	12d	50%	6d	28-May-14	10-Jun-14	28-May-14 A	12-Jul-14	133d	$0	$0
NAB1555	Interlocking Blocks	12d	0%	12d	25-Aug-14	07-Sep-14	25-Aug-14	07-Sep-14	97d	$0	$0
NAB1553	Galvanized steel Handrail	12d	0%	12d	14-Sep-14	27-Sep-14	14-Sep-14	27-Sep-14	54d	$0	$0
PROJECT 01 Procurements		167d		0d	01-Mar-14	29-Sep-14	27-Jan-14 A	29-Sep-14	54d	$0	$0
NAB1580	Order steel pipes and fittings	0d	100%	0d	01-Mar-14		27-Jan-14 A			$0	$0
NAB1590	Start Delivery steel pipes and fittings	0d	100%	0d		03-May-14		22-Mar-14 A		$0	$0
NAB1600	Order Street Lighting Poles	0d	100%	0d	25-Jun-14		25-Jun-14 A			$0	$0
NAB1610	Delivery Street Lighting Poles	0d	0%	0d		29-Sep-14		29-Sep-14	54d	$0	$0
PROJECT 01 Construction		360d		182d	22-Jan-14	17-Jan-15	23-Jan-14 A	29-Dec-14	8d	$2,622,168	$12,116,208
Phase One from A2+020 TO 5+450 closed /area B & A		262d		131d	22-Jan-14	21-Dec-14	23-Jan-14 A	21-Dec-14	13d	$2,356,407	$5,203,285
Main Road From St. A2+020 To St. A2+500 LHS & RHS Area B		148d		17d	22-Jan-14	04-Aug-14	23-Jan-14 A	04-Aug-14	126d	$694,054	$883,599
NAB1680	Maintain traffic control and safety plan ,Relocating utilities	148d	88.52%	17d	22-Jan-14	04-Aug-14	23-Jan-14 A	04-Aug-14	126d	$0	$0
Excavation		107d		2d	22-Jan-14	01-Jun-14	23-Jan-14 A	05-Jul-14	141d	$96,069	$100,736
NAB1690	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	100%	0d	22-Jan-14	18-Feb-14	23-Jan-14 A	30-Mar-14 A		$54,068	$54,068
NAB2620	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	2d	08-May-14	01-Jun-14	28-Jan-14 A	05-Jul-14	141d	$42,002	$46,669
Storm System		74d		0d	02-Feb-14	03-May-14	15-Feb-14 A	21-Apr-14 A		$186,559	$186,559
NAB1710	60 cm Conc. Pipes for drainage W. manholes from A2+020 to A2+180 L= 160 m LHS	16d	100%	0d	02-Feb-14	22-Feb-14	15-Feb-14 A	18-Feb-14 A		$28,200	$28,200
NAB1740	60 cm Conc. Pipes for drainage W. manholes from A2+220 to A2+500 L= 280 m LHS	27d	100%	0d	01-Mar-14	01-Apr-14	18-Feb-14 A	25-Feb-14 A		$81,361	$81,361
NAB2630	New Conc.Pipe Culvert Dia. 80 cm with outlet @ St. A2+084 length L= 55 m RHS	18d	100%	0d	12-Mar-14	01-Apr-14	05-Mar-14 A	06-Mar-14 A		$25,509	$25,509

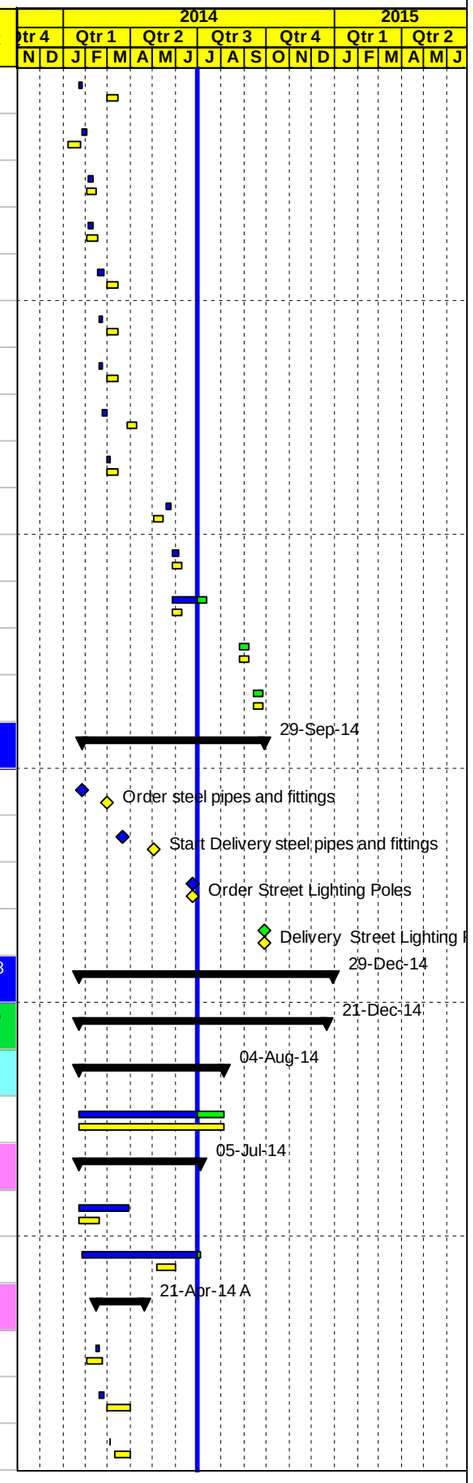

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB1730	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	18d	100%	0d	10-Apr-14	03-May-14	05-Apr-14 A	21-Apr-14 A		$29,526	$29,526
NAB2640	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	14d	100%	0d	10-Apr-14	27-Apr-14	05-Apr-14 A	20-Apr-14 A		$21,962	$21,962
Water lines		37d		0d	12-Mar-14	24-Apr-14	23-Mar-14 A	21-Apr-14 A		$97,265	$97,265
NAB2962-new	12" Steel pipeline beit iba from st 2+220 To st 2+450 RHS	21d	100%	0d	12-Mar-14	05-Apr-14	23-Mar-14 A	25-Mar-14 A		$68,900	$68,900
NAB1720	3" Steel Water pipeline from St. A 2+020 to A 2+500 (LHS) L=480 m LHS	12d	100%	0d	10-Apr-14	24-Apr-14	03-Apr-14 A	21-Apr-14 A		$28,365	$28,365
Sewer line		42d		0d	02-Feb-14	24-Mar-14	08-Feb-14 A	21-Apr-14 A		$59,981	$59,981
NAB1700	12" Sewer line from St. A2+020 to St. A2+500 L=480 m LHS	25d	100%	0d	02-Feb-14	04-Mar-14	08-Feb-14 A	25-Mar-14 A		$54,415	$54,415
NAB1990-new	8" Sewer line (house connection from St. A2+020 to St. A2+500 LHS	11d	100%	0d	12-Mar-14	24-Mar-14	08-Feb-14 A	21-Apr-14 A		$5,566	$5,566
Concrete works		21d		0d	12-Mar-14	05-Apr-14	08-Mar-14 A	30-Mar-14 A		$9,437	$9,437
NAB2960-new	Conc. Retaining walls from A2+339 to A2+369 L= 30 m RHS	21d	100%	0d	12-Mar-14	05-Apr-14	08-Mar-14 A	30-Mar-14 A		$9,437	$9,437
Tooping and Basecourse		70d		1d	20-Mar-14	11-Jun-14	11-Mar-14 A	03-Jul-14	142d	$119,268	$132,520
NAB1750	20 cm Thick Topping Layer LHS	13d	90%	1d	25-Mar-14	08-Apr-14	11-Mar-14 A	03-Jul-14	132d	$24,404	$27,115
NAB2650	20 cm Thick Topping Layer RHS	13d	90%	1d	20-Mar-14	03-Apr-14	25-Mar-14 A	03-Jul-14	139d	$12,398	$13,775
NAB2670	20 cm Thick Base Course- First Layer RHS	13d	90%	1d	24-Apr-14	10-May-14	13-Apr-14 A	03-Jul-14	142d	$18,963	$21,070
NAB1780	20 cm Thick Base Course- First Layer LHS	13d	90%	1d	24-Apr-14	10-May-14	15-Apr-14 A	03-Jul-14	142d	$22,491	$24,990
NAB2680	20 cm Thick Base Course- Second Layer RHS	13d	90%	1d	10-May-14	25-May-14	17-Apr-14 A	03-Jul-14	139d	$18,963	$21,070
NAB1790	20 cm Thick Base Course- Second Layer LHS	13d	90%	1d	28-May-14	11-Jun-14	20-Apr-14 A	03-Jul-14	56d	$22,050	$24,500
Asphalt binder		29d		3d	10-Jun-14	22-Jul-14	24-Apr-14 A	22-Jul-14	132d	$112,892	$178,092
NAB2810-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+140 to St. 2+550 RHS	2d	100%	0d	10-Jun-14	11-Jun-14	24-Apr-14 A	25-Apr-14 A		$69,806	$69,806
NAB1980-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+140 to St. 2+570 width 6 m LHS	2d	100%	0d	10-Jun-14	11-Jun-14	27-Apr-14 A	28-Apr-14 A		$43,086	$43,086
NAB2820	7 cm Asphalt Binder Course Including Prime Coat from St. 2+020 to St. 2+140 RHS	3d	0%	3d	16-Jul-14	22-Jul-14	16-Jul-14	22-Jul-14	132d	$0	$65,200
Street Lighting Poles and Curbstone		17d		17d	01-Jul-14	04-Aug-14	25-Jun-14 A	04-Aug-14	61d	$12,583	$119,010
NAB2690	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	5d	50%	3d	08-Jul-14	17-Jul-14	25-Jun-14 A	05-Jul-14	68d	$12,583	$22,197
NAB2660	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	01-Jul-14	19-Jul-14	01-Jul-14	19-Jul-14	61d	$0	$0
NAB1800	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	7d	03-Jul-14	16-Jul-14	03-Jul-14	16-Jul-14	56d	$0	$23,493
NAB1810	Conc. Sidewalk and ramps including base course LHS	9d	0%	9d	13-Jul-14	02-Aug-14	13-Jul-14	02-Aug-14	56d	$0	$25,496
NAB2700	Conc. Sidewalk and ramps including base course RHS	7d	0%	7d	20-Jul-14	04-Aug-14	20-Jul-14	04-Aug-14	61d	$0	$47,824
Main Road From St. A2+500 To St. A3+000 LHS & RHS Area A		133d		35d	05-Mar-14	25-Aug-14	13-Feb-14 A	25-Aug-14	108d	$610,445	$774,050
NAB1820	Maintain traffic control and safety plan ,Relocating utilities	133d	73.55%	35d	05-Mar-14	25-Aug-14	13-Feb-14 A	25-Aug-14	108d	$0	$0
Excavation		84d		2d	09-Mar-14	16-Jun-14	22-Feb-14 A	05-Jul-14	141d	$57,758	$64,175

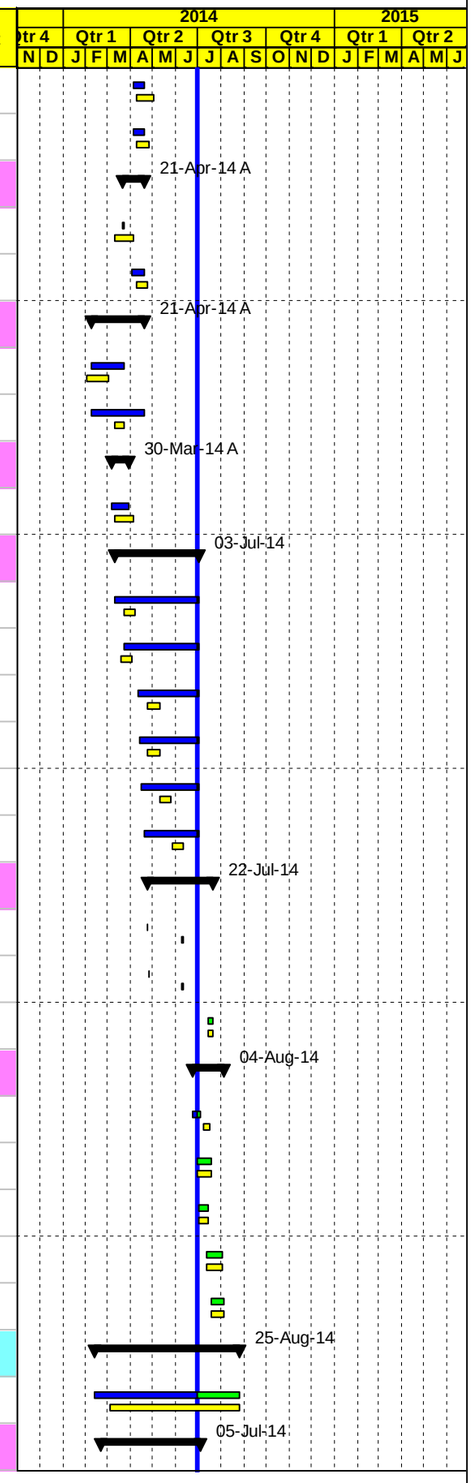

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB2720	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	2d	24-May-14	16-Jun-14	22-Feb-14 A	05-Jul-14	141d	$27,923	$31,025
NAB1830	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	90%	2d	09-Mar-14	01-Apr-14	25-Feb-14 A	05-Jul-14	141d	$29,835	$33,150
Storm System		49d		0d	16-Mar-14	13-May-14	23-Feb-14 A	15-May-14 A		$117,997	$117,997
NAB1840	60 cm Conc. Pipes for drainage W. manholes from A2+500 to A2+620 L= 120 m LHS	11d	100%	0d	16-Mar-14	27-Mar-14	23-Feb-14 A	11-Mar-14 A		$34,825	$34,825
NAB1880	60 cm Conc. Pipes for drainage W. manholes from A2+640 to A2+740 L= 100 m LHS	12d	100%	0d	20-Mar-14	02-Apr-14	15-Mar-14 A	15-Apr-14 A		$32,370	$32,370
NAB1890	60 cm Conc. Pipes for drainage W. manholes from A2+860 to A2+980 L= 120 m LHS	10d	100%	0d	29-Mar-14	08-Apr-14	17-Mar-14 A	26-Mar-14 A		$32,170	$32,170
NAB2730	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	14d	100%	0d	24-Apr-14	11-May-14	17-Apr-14 A	15-May-14 A		$8,962	$8,962
NAB1860	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	16d	100%	0d	24-Apr-14	13-May-14	24-Apr-14 A	30-Apr-14 A		$9,670	$9,670
Water lines		43d		0d	12-Mar-14	03-May-14	25-Mar-14 A	26-May-14 A		$80,270	$80,270
NAB2726-new	12" Steel pipeline beit iba from st 2+450 To st 2+950 RHS	21d	100%	0d	12-Mar-14	05-Apr-14	25-Mar-14 A	26-May-14 A		$61,970	$61,970
NAB1850	3" Steel Water pipeline from St. A 2+500 to A 2+700 (LHS) L =200 M LHS	7d	100%	0d	24-Apr-14	03-May-14	21-Apr-14 A	22-Apr-14 A		$12,200	$12,200
NAB1921-new	3" Steel Water pipeline from St. A 2+900 to A 3+000 (LHS) L=100 m LHS	2d	100%	0d	24-Apr-14	26-Apr-14	27-Apr-14 A	29-Apr-14 A		$6,100	$6,100
Sewer line		16d		1d	05-Mar-14	24-Mar-14	13-Feb-14 A	02-Jul-14	142d	$16,045	$16,992
NAB1870	12" Sewer line from St. A2+500 to St. A2+580 L=80 LHS	12d	90%	1d	05-Mar-14	19-Mar-14	13-Feb-14 A	02-Jul-14	142d	$12,718	$13,664
NAB1841-new	8" Sewer line (house connection from St. A2+500 to St. A3+000 LHS	11d	90%	1d	12-Mar-14	24-Mar-14	14-Apr-14 A	02-Jul-14	46d	$3,328	$3,328
Concrete works		21d		0d	12-Mar-14	05-Apr-14	22-Mar-14 A	03-May-14 A		$92,243	$92,243
NAB2722-new	Conc. Retaining walls from A2+475 to A2+515 L= 40 m RHS	21d	100%	0d	12-Mar-14	05-Apr-14	22-Mar-14 A	29-Mar-14 A		$15,165	$15,165
NAB2724-new	Conc. Retaining walls from A2+740 to A2+850 L= 110 m RHS	21d	100%	0d	12-Mar-14	05-Apr-14	31-Mar-14 A	03-May-14 A		$50,974	$50,974
NAB2725-new	Conc. Retaining walls from A2+880 to A2+916 L= 36 m RHS	21d	100%	0d	12-Mar-14	05-Apr-14	14-Apr-14 A	03-May-14 A		$14,021	$14,021
NAB2728-new	Conc. Retaining walls from A2+937 to A2+954 L= 17 m RHS	15d	100%	0d	12-Mar-14	29-Mar-14	15-Apr-14 A	02-May-14 A		$6,400	$6,400
NAB2730-new	Conc. Retaining walls from A2+965 to A2+980 L= 25 m RHS	15d	100%	0d	12-Mar-14	29-Mar-14	16-Apr-14 A	03-May-14 A		$5,682	$5,682
Tooping and Basecourse		58d		0d	09-Apr-14	17-Jun-14	06-Mar-14 A	27-May-14 A		$133,575	$133,575
NAB1900	20 cm Thick Topping Layer LHS	13d	100%	0d	09-Apr-14	24-Apr-14	06-Mar-14 A	14-May-14 A		$18,850	$18,850
NAB2760	20 cm Thick Topping Layer RHS	13d	100%	0d	26-Apr-14	12-May-14	06-Mar-14 A	14-May-14 A		$13,050	$13,050
NAB2780	20 cm Thick Base Course- First Layer RHS	13d	100%	0d	25-May-14	09-Jun-14	13-Apr-14 A	21-Apr-14 A		$27,930	$27,930
NAB2790	20 cm Thick Base Course- Second Layer RHS	13d	100%	0d	02-Jun-14	17-Jun-14	17-Apr-14 A	28-Apr-14 A		$27,930	$27,930
NAB1920	20 cm Thick Base Course- First Layer LHS	13d	100%	0d	07-May-14	21-May-14	22-Apr-14 A	03-May-14 A		$17,885	$17,885
NAB1950	20 cm Thick Base Course- Second Layer LHS	13d	100%	0d	10-May-14	24-May-14	27-Apr-14 A	27-May-14 A		$27,930	$27,930
Asphalt binder		45d		3d	01-Jun-14	06-Aug-14	27-May-14 A	06-Aug-14	46d	$112,558	$153,264
NAB2820-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+540 to St. 2+950 RHS	2d	100%	0d	01-Jun-14	02-Jun-14	27-May-14 A	28-May-14 A		$67,134	$67,134

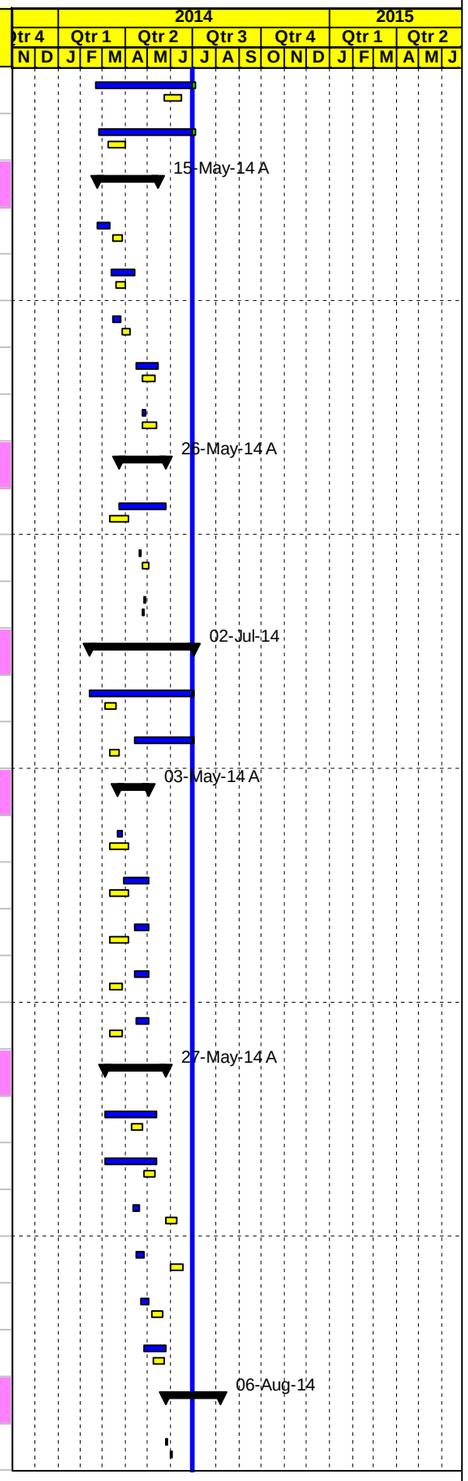

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB1985-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+550 to St. 3+000 LHS width 6 m. LHS	2d	100%	0d	01-Jun-14	02-Jun-14	28-May-14 A	29-May-14 A		$45,424	$45,424
NAB1980	7 cm Asphalt Binder Course Including Prime Coat remining 2+500 to St. 3+000 LHS	3d	0%	3d	03-Aug-14	06-Aug-14	03-Aug-14	06-Aug-14	46d	$0	$40,706
Street Lighting Poles and Curbstone		16d		16d	06-Aug-14	25-Aug-14	06-Aug-14	25-Aug-14	52d	$0	$115,534
NAB1960	Precast Conc. Curbstone forLHS (Mediane and side curb) LHS	7d	0%	7d	06-Aug-14	14-Aug-14	06-Aug-14	14-Aug-14	46d	$0	$24,036
NAB2800	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	7d	0%	7d	06-Aug-14	14-Aug-14	06-Aug-14	14-Aug-14	52d	$0	$23,224
NAB2770	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	07-Aug-14	19-Aug-14	07-Aug-14	19-Aug-14	57d	$0	$0
NAB1970	Conc. Sidewalk and ramps including base course LHS	9d	0%	9d	14-Aug-14	25-Aug-14	14-Aug-14	25-Aug-14	46d	$0	$26,392
NAB2810	Conc. Sidewalk and ramps including base course RHS	9d	0%	9d	14-Aug-14	25-Aug-14	14-Aug-14	25-Aug-14	52d	$0	$41,882
Main Road St. A3+000 To St. A3+500 LHS & RHS Area A		158d		45d	12-Mar-14	29-Sep-14	18-Mar-14 A	06-Sep-14	98d	$445,701	$848,541
NAB2000	Maintain traffic control and safety plan ,Relocating utilities	158d	71.46%	45d	12-Mar-14	29-Sep-14	18-Mar-14 A	06-Sep-14	98d	$0	$0
Excavation		115d		2d	27-Mar-14	25-Aug-14	18-Mar-14 A	05-Jul-14	141d	$51,255	$56,950
NAB2010	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	90%	2d	27-Mar-14	21-Apr-14	18-Mar-14 A	05-Jul-14	141d	$25,245	$28,050
NAB2840	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	2d	02-Aug-14	25-Aug-14	06-Apr-14 A	05-Jul-14	120d	$26,010	$28,900
Storm System		95d		23d	10-May-14	11-Sep-14	18-Apr-14 A	11-Aug-14	120d	$52,335	$85,311
NAB2011-new	60 cm Conc. Pipes for drainage W. manholes from A2+980 to A3+120 L= 140 m LHS	18d	90%	2d	10-May-14	29-May-14	18-Apr-14 A	03-Jul-14	70d	$35,775	$36,675
NAB2870	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	16d	100%	0d	25-Aug-14	11-Sep-14	10-May-14 A	20-May-14 A		$6,890	$6,890
NAB2030	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	16d	100%	0d	20-May-14	07-Jun-14	15-May-14 A	21-May-14 A		$9,670	$9,670
NAB2860	New Conc.Pipe Culvert Dia. 80 cm @ St. A3+280 length L= 132 m RHS	23d	0%	23d	01-Jul-14	11-Aug-14	01-Jul-14	11-Aug-14	120d	$0	$32,076
Water lines		46d		1d	12-Mar-14	06-May-14	01-Apr-14 A	02-Jul-14	71d	$93,835	$95,235
NAB2849-new	12" Steel pipeline beit iba from st 2+950 To st 3+450 RHS	10d	100%	0d	12-Mar-14	23-Mar-14	01-Apr-14 A	20-Apr-14 A		$67,300	$68,700
NAB2961-new	3" Steel Water pipeline from St. A 3+000 to A 3+500 (LHS) L=500m LHS	10d	90%	1d	24-Apr-14	06-May-14	27-Apr-14 A	02-Jul-14	71d	$26,535	$26,535
Concrete works		40d		1d	24-Apr-14	10-Jun-14	18-Apr-14 A	02-Jul-14	77d	$61,795	$61,795
NAB2842-new	Conc. Retaining walls from A3+006 to A3+018 L=12 m RHS	12d	90%	1d	24-Apr-14	08-May-14	18-Apr-14 A	02-Jul-14	77d	$4,545	$4,545
NAB2851-new	Conc. Retaining walls from A3+240 to A3+300 L=60m RHS	5d	100%	0d	24-Apr-14	29-Apr-14	25-Apr-14 A	06-May-14 A		$22,016	$22,016
NAB2850	Conc. Retaining walls from A3+180 to A3+240 L=60m RHS	12d	100%	0d	24-Apr-14	08-May-14	29-Apr-14 A	07-May-14 A		$19,783	$19,783
NAB2875-new	Conc. Retaining walls from A3+341 to A3+370 L=29m RHS	12d	100%	0d	28-May-14	10-Jun-14	07-May-14 A	20-May-14 A		$15,452	$15,452
Tooping and Basecourse		113d		6d	05-May-14	29-Sep-14	01-May-14 A	12-Jul-14	138d	$94,691	$137,995
NAB2040	20 cm Thick Topping Layer LHS	13d	70%	4d	05-May-14	20-May-14	01-May-14 A	08-Jul-14	139d	$12,180	$17,400
NAB2880	20 cm Thick Topping Layer RHS	13d	80%	3d	30-Aug-14	13-Sep-14	03-May-14 A	06-Jul-14	141d	$11,020	$13,775
NAB2910	20 cm Thick Base Course- First Layer RHS	13d	80%	3d	06-Sep-14	20-Sep-14	03-May-14 A	06-Jul-14	141d	$22,344	$27,930

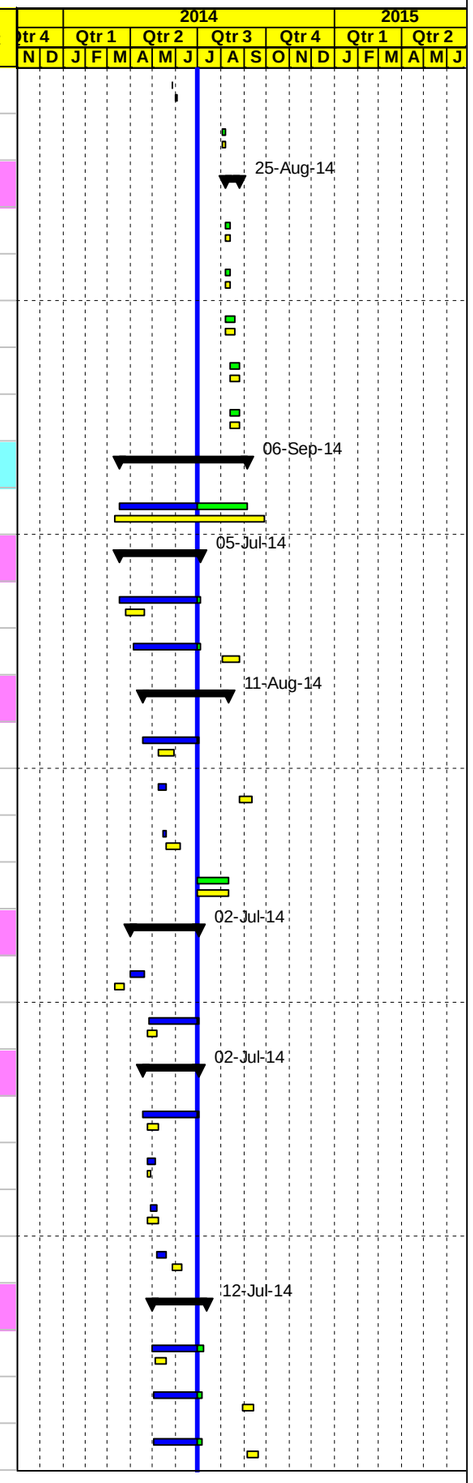

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB2070	20 cm Thick Base Course- First Layer LHS	13d	55%	6d	31-May-14	14-Jun-14	05-May-14 A	12-Jul-14	138d	$15,362	$27,930
NAB2920	20 cm Thick Base Course- Second Layer RHS	13d	80%	3d	15-Sep-14	29-Sep-14	10-May-14 A	06-Jul-14	75d	$18,424	$23,030
NAB2090	20 cm Thick Base Course- Second Layer LHS	13d	55%	6d	11-Jun-14	25-Jun-14	17-May-14 A	12-Jul-14	66d	$15,362	$27,930
Asphalt binder		33d		5d	01-Jun-14	15-Jul-14	27-May-14 A	15-Jul-14	72d	$86,910	$265,367
NAB2879-new	7 cm Asphalt Binder Course Including Prime Coat from St. 3+000 to St. 3+220 RHS.	2d	100%	0d	01-Jun-14	02-Jun-14	27-May-14 A	28-May-14 A		$38,410	$38,410
NAB2095-new	7 cm Asphalt Binder Course Including Prime Coat from St. 3+000 to St. 3+170 LHS width 6 m LHS	2d	100%	0d	01-Jun-14	02-Jun-14	28-May-14 A	29-May-14 A		$48,500	$48,500
NAB2930	7 cm Asphalt Binder Course Including Prime Coat from St. 3+220 to St. 3+450 RHS.	2d	0%	2d	06-Jul-14	09-Jul-14	06-Jul-14	09-Jul-14	75d	$0	$89,228
NAB2100	7 cm Asphalt Binder Course Including Prime Coat LHS remining	2d	0%	2d	12-Jul-14	15-Jul-14	12-Jul-14	15-Jul-14	66d	$0	$89,228
Street Lighting Poles and Curbstone		72d		45d	31-May-14	06-Sep-14	21-Apr-14 A	06-Sep-14	98d	$4,880	$145,888
NAB2060	Reconstruct stone wall from (A3+160 to A3+190) & (A3+240 to A3+282) L=72 m LHS	12d	95%	1d	31-May-14	12-Jun-14	21-Apr-14 A	01-Jul-14	117d	$4,880	$5,795
NAB2900	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	01-Jul-14	19-Jul-14	01-Jul-14	19-Jul-14	87d	$0	$0
NAB2050	Reconstruct stone wall from A3+000 to A3+100 L=100 m LHS	15d	0%	15d	07-Jul-14	06-Aug-14	07-Jul-14	06-Aug-14	117d	$0	$8,540
NAB2940	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	7d	0%	7d	09-Jul-14	22-Jul-14	09-Jul-14	22-Jul-14	75d	$0	$23,343
NAB2110	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	7d	15-Jul-14	02-Aug-14	15-Jul-14	02-Aug-14	66d	$0	$23,224
NAB2890	Reconstruct stone wall from A3+345 to A3+370 L= 25 m RHS	8d	0%	8d	06-Aug-14	16-Aug-14	06-Aug-14	16-Aug-14	117d	$0	$3,050
NAB2120	Conc. Sidewalk and ramps including base course LHS	10d	0%	10d	25-Aug-14	06-Sep-14	25-Aug-14	06-Sep-14	46d	$0	$29,032
NAB2950	Conc. Sidewalk and ramps including base course RHS	10d	0%	10d	25-Aug-14	06-Sep-14	25-Aug-14	06-Sep-14	52d	$0	$52,904
Main Road St. A3+500 To St. A4+000 LHS & RHS Area A		154d		55d	12-Mar-14	24-Sep-14	22-Apr-14 A	17-Sep-14	88d	$401,792	$825,072
NAB2130	Maintain traffic control and safety plan ,Relocating utilities	154d	64.22%	55d	12-Mar-14	24-Sep-14	22-Apr-14 A	17-Sep-14	88d	$0	$0
Excavation		91d		0d	27-Apr-14	26-Aug-14	29-Apr-14 A	21-Jun-14 A		$69,906	$69,906
NAB2140	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	100%	0d	27-Apr-14	22-May-14	29-Apr-14 A	17-Jun-14 A		$32,300	$32,300
NAB3010	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	20d	100%	0d	04-Aug-14	26-Aug-14	08-May-14 A	21-Jun-14 A		$37,606	$37,606
Storm System		87d		43d	10-May-14	03-Sep-14	07-May-14 A	03-Sep-14	101d	$111,917	$169,540
NAB2150	60 cm Conc. Pipes for drainage W. manholes from A3+610 to A3+840 L= 230 m LHS	23d	85%	3d	10-May-14	04-Jun-14	07-May-14 A	07-Jul-14	140d	$40,928	$48,150
NAB3030	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	18d	100%	0d	30-Jun-14	04-Aug-14	10-Jun-14 A	16-Jun-14 A		$7,740	$7,740
NAB2170	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	15d	100%	0d	01-Jun-14	17-Jun-14	12-Jun-14 A	18-Jun-14 A		$5,880	$5,880
NAB3020	New double box culvert 2 (2*2) @ St. A3+610 RHS length L= 28 m First part RHS	24d	5%	23d	25-Jun-14	06-Aug-14	17-Jun-14 A	11-Aug-14	101d	$32,591	$61,015
NAB3040	New double box culvert 2 (2*2) @ St. A3+610 RHS length L= 28 m second part RHS	24d	5%	23d	05-Aug-14	01-Sep-14	17-Jun-14 A	11-Aug-14	121d	$24,779	$29,220
NAB2160	New double box culvert 2 (2*2) @ St. A3+610 LHS length L=10 m LHS	16d	0%	16d	16-Aug-14	03-Sep-14	16-Aug-14	03-Sep-14	101d	$0	$17,535
Water lines		10d		1d	12-Mar-14	23-Mar-14	22-Apr-14 A	02-Jul-14	142d	$68,560	$68,700

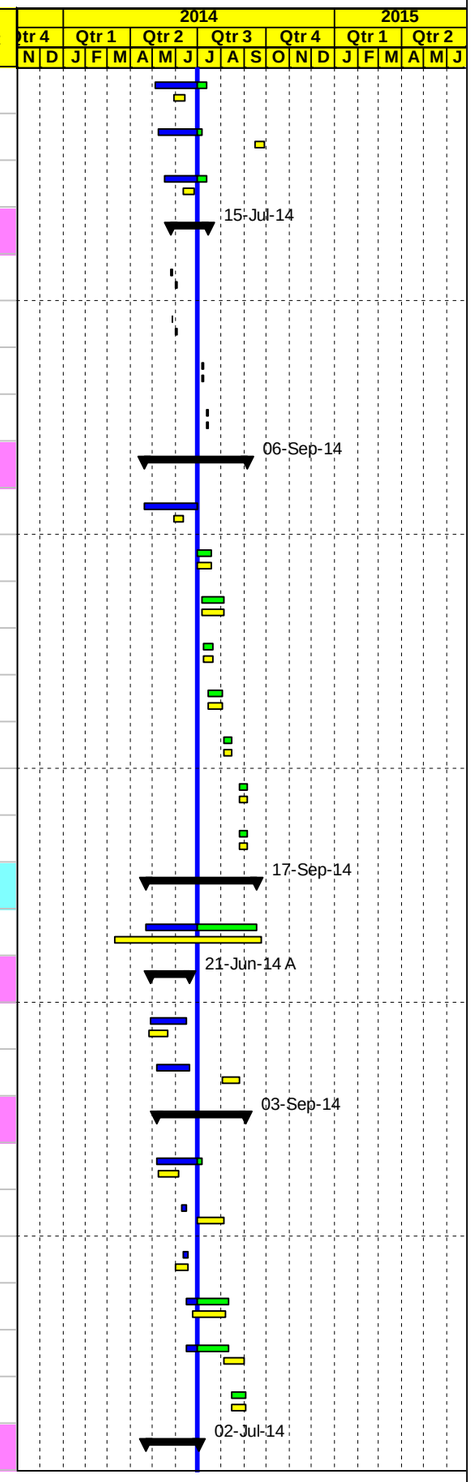

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB3005-new	12" Steel pipeline beit iba from st 3+450 To st 3+950 RHS	10d	90%	1d	12-Mar-14	23-Mar-14	22-Apr-14 A	02-Jul-14	142d	$68,560	$68,700
Sewer line		21d		0d	01-Jun-14	24-Jun-14	31-May-14 A	10-Jun-14 A		$26,375	$26,375
NAB2155-new	12" Sewer line from St. A4+007 to St. A4+260 L=260 m LHS	21d	100%	0d	01-Jun-14	24-Jun-14	31-May-14 A	10-Jun-14 A		$26,375	$26,375
Concrete works		73d		16d	28-May-14	04-Sep-14	01-May-14 A	03-Aug-14	66d	$31,214	$49,123
NAB3015-new	Conc. Retaining walls from A3+560 to A3+590 L=30m RHS	15d	100%	0d	28-May-14	14-Jun-14	01-May-14 A	24-May-14 A		$14,226	$14,226
NAB3050	Conc. Retaining walls from A3+828 to A3+858 L= 30 m RHS	15d	100%	0d	19-Aug-14	04-Sep-14	17-May-14 A	22-Jun-14 A		$2,037	$2,037
NAB3025-new	Conc. Retaining walls from A3+650 to A3+690 L=40m RHS	15d	100%	0d	28-May-14	14-Jun-14	21-May-14 A	17-Jun-14 A		$14,951	$14,951
NAB2180	Conc. retaining wall from A3+950 TO A3+982 L= 32M LHS	16d	0%	16d	01-Jul-14	03-Aug-14	01-Jul-14	03-Aug-14	66d	$0	$17,909
Tooping and Basecourse		82d		10d	07-Jun-14	24-Sep-14	24-May-14 A	20-Jul-14	71d	$93,820	$133,020
NAB3060	20 cm Thick Topping Layer RHS	13d	100%	0d	10-Sep-14	24-Sep-14	24-May-14 A	22-Jun-14 A		$16,530	$16,530
NAB2190	20 cm Thick Topping Layer LHS	13d	100%	0d	07-Jun-14	21-Jun-14	01-Jun-14 A	21-Jun-14 A		$16,530	$16,530
NAB2210	20 cm Thick Base Course- First Layer LHS	13d	100%	0d	19-Jun-14	07-Jul-14	05-Jun-14 A	25-Jun-14 A		$26,460	$26,460
NAB3080	20 cm Thick Base Course- First Layer RHS	13d	100%	0d	02-Sep-14	16-Sep-14	05-Jun-14 A	28-Jun-14 A		$24,500	$24,500
NAB2220	20 cm Thick Base Course- Second Layer LHS	13d	20%	10d	11-Aug-14	26-Aug-14	27-Jun-14 A	20-Jul-14	71d	$4,900	$24,500
NAB3090	20 cm Thick Base Course- Second Layer RHS	13d	20%	10d	26-Aug-14	10-Sep-14	27-Jun-14 A	20-Jul-14	71d	$4,900	$24,500
Asphalt binder		2d		2d	03-Aug-14	05-Aug-14	03-Aug-14	05-Aug-14	72d	$0	$184,817
NAB2230	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	03-Aug-14	05-Aug-14	03-Aug-14	05-Aug-14	66d	$0	$92,408
NAB3092	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	03-Aug-14	05-Aug-14	03-Aug-14	05-Aug-14	72d	$0	$92,408
Street Lighting Poles and Curbstone		40d		40d	03-Aug-14	17-Sep-14	03-Aug-14	17-Sep-14	82d	$0	$123,591
NAB2200	Reconstruct stone wall from A3+720 to A3+820 L=100 m LHS	15d	0%	15d	03-Aug-14	19-Aug-14	03-Aug-14	19-Aug-14	107d	$0	$4,697
NAB2240	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	7d	05-Aug-14	13-Aug-14	05-Aug-14	13-Aug-14	66d	$0	$23,224
NAB3094	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	7d	0%	7d	05-Aug-14	13-Aug-14	05-Aug-14	13-Aug-14	72d	$0	$23,224
NAB3070	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	06-Aug-14	18-Aug-14	06-Aug-14	18-Aug-14	78d	$0	$0
NAB2250	Conc. Sidewalk and ramps including base course LHS	10d	0%	10d	06-Sep-14	17-Sep-14	06-Sep-14	17-Sep-14	46d	$0	$26,392
NAB3096	Conc. Sidewalk and ramps including base course RHS	10d	0%	10d	06-Sep-14	17-Sep-14	06-Sep-14	17-Sep-14	52d	$0	$46,053
Main Road St. A4+000 To St. A4+500 LHS & RHS Area A		161d		65d	12-Mar-14	02-Oct-14	25-Apr-14 A	29-Sep-14	78d	$136,065	$674,560
NAB2260	Maintain traffic control and safety plan ,Relocating utilities	161d	59.57%	65d	12-Mar-14	02-Oct-14	25-Apr-14 A	29-Sep-14	78d	$0	$0
Excavation		28d		8d	25-Jun-14	11-Aug-14	14-May-14 A	14-Jul-14	136d	$40,154	$76,653
NAB3114	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	15d	55%	7d	16-Jul-14	11-Aug-14	14-May-14 A	13-Jul-14	0d	$20,103	$36,550
NAB2270	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	15d	50%	8d	25-Jun-14	20-Jul-14	10-Jun-14 A	14-Jul-14	136d	$20,052	$40,103

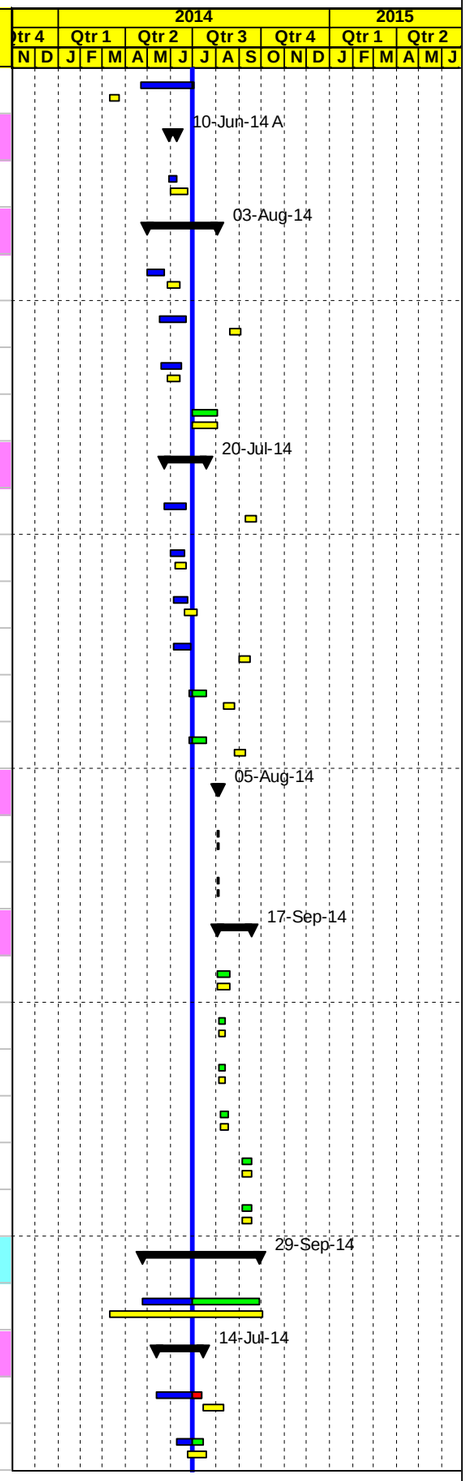

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
Storm System		59d		24d	01-Jul-14	22-Sep-14	15-Jun-14 A	12-Aug-14	119d	$0	$79,554
NAB3150	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+240 length L= 12 m RHS	12d	15%	10d	09-Sep-14	22-Sep-14	15-Jun-14 A	20-Jul-14	127d	$0	$0
NAB2290	60 cm Conc. Pipes for drainage W. manholes from A4+240 to A4+500 L= 260 m LHS	24d	0%	24d	01-Jul-14	12-Aug-14	01-Jul-14	12-Aug-14	119d	$0	$53,890
NAB2305	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	15d	0%	15d	17-Jul-14	12-Aug-14	17-Jul-14	12-Aug-14	119d	$0	$25,664
Water lines		10d		0d	12-Mar-14	23-Mar-14	25-Apr-14 A	25-May-14 A		$68,700	$68,700
NAB3099-new	12" Steel pipeline beit iba from st 3+950 To st 4+450 RHS	10d	100%	0d	12-Mar-14	23-Mar-14	25-Apr-14 A	25-May-14 A		$68,700	$68,700
Sewer line		20d		20d	01-Jul-14	07-Aug-14	01-Jul-14	07-Aug-14	117d	$0	$31,603
NAB2280	12" Sewer line From St. A4+100 to St. A4+300 L=200 M LHS	10d	0%	10d	01-Jul-14	19-Jul-14	01-Jul-14	19-Jul-14	117d	$0	$17,154
NAB2300	12" Sewer line From St. A4+300 to St. A4+500 L=200 M LHS	10d	0%	10d	20-Jul-14	07-Aug-14	20-Jul-14	07-Aug-14	117d	$0	$14,450
Tooping and Basecourse		56d		12d	23-Jul-14	02-Oct-14	05-Jun-14 A	23-Jul-14	131d	$27,211	$129,900
NAB3160	20 cm Thick Topping Layer RHS	13d	30%	9d	08-Sep-14	22-Sep-14	05-Jun-14 A	17-Jul-14	134d	$4,785	$15,950
NAB3180	20 cm Thick Base Course- First Layer RHS	13d	30%	9d	18-Sep-14	02-Oct-14	10-Jun-14 A	17-Jul-14	134d	$7,350	$24,500
NAB2310	20 cm Thick Topping Layer LHS	13d	30%	9d	09-Aug-14	23-Aug-14	11-Jun-14 A	17-Jul-14	134d	$4,785	$15,950
NAB2320	20 cm Thick Base Course- First Layer LHS	13d	7%	12d	17-Aug-14	31-Aug-14	15-Jun-14 A	23-Jul-14	131d	$1,716	$24,500
NAB3190	20 cm Thick Base Course- Second Layer RHS	13d	20%	10d	23-Jul-14	13-Aug-14	22-Jun-14 A	20-Jul-14	81d	$4,900	$24,500
NAB2330	20 cm Thick Base Course- Second Layer LHS	13d	15%	11d	26-Aug-14	10-Sep-14	28-Jun-14 A	21-Jul-14	81d	$3,675	$24,500
Asphalt binder		2d		2d	05-Aug-14	07-Aug-14	05-Aug-14	07-Aug-14	81d	$0	$177,556
NAB2360	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	05-Aug-14	07-Aug-14	05-Aug-14	07-Aug-14	74d	$0	$92,408
NAB3194	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	05-Aug-14	07-Aug-14	05-Aug-14	07-Aug-14	81d	$0	$85,147
Street Lighting Poles and Curbstone		45d		45d	07-Aug-14	29-Sep-14	07-Aug-14	29-Sep-14	46d	$0	$110,595
NAB2340	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	7d	07-Aug-14	16-Aug-14	07-Aug-14	16-Aug-14	74d	$0	$23,224
NAB3192	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	5d	0%	5d	07-Aug-14	13-Aug-14	07-Aug-14	13-Aug-14	82d	$0	$23,224
NAB3170	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	07-Aug-14	19-Aug-14	07-Aug-14	19-Aug-14	81d	$0	$0
NAB2350	Conc. Sidewalk and ramps including base course LHS	10d	0%	10d	17-Sep-14	29-Sep-14	17-Sep-14	29-Sep-14	46d	$0	$29,252
NAB3196	Conc. Sidewalk and ramps including base course RHS	4d	0%	4d	17-Sep-14	22-Sep-14	17-Sep-14	22-Sep-14	52d	$0	$34,894
Main Road St. A4+500 To St. A5+000 LHS & RHS Area A		101d		108d	13-Jul-14	24-Nov-14	22-May-14 A	24-Nov-14	26d	$68,350	$668,742
NAB2370	Maintain traffic control and safety plan ,Relocating utilities	101d	0%	108d	13-Jul-14	24-Nov-14	22-May-14 A	24-Nov-14	26d	$0	$0
Excavation		24d		24d	13-Jul-14	20-Aug-14	13-Jul-14	20-Aug-14	0d	$0	$68,448
NAB2380	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	12d	0%	12d	13-Jul-14	06-Aug-14	13-Jul-14	06-Aug-14	0d	$0	$43,085
NAB3340	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	12d	0%	12d	06-Aug-14	20-Aug-14	06-Aug-14	20-Aug-14	0d	$0	$25,363

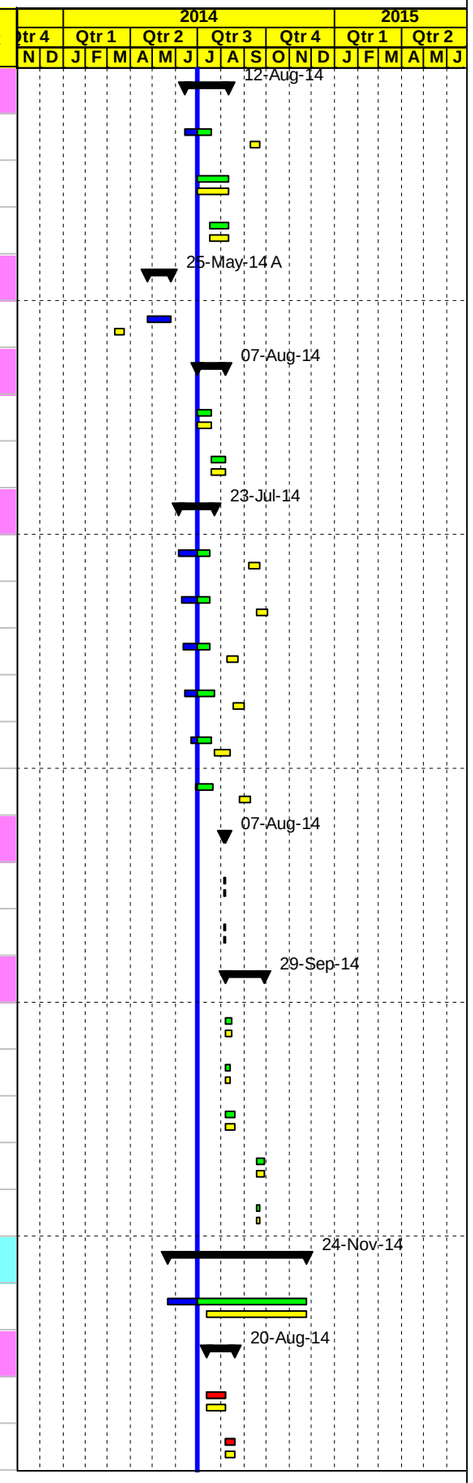

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
Storm System		21d		21d	06-Aug-14	30-Aug-14	06-Aug-14	30-Aug-14	59d	$0	$88,974
NAB2430	60 cm Conc. Pipes for drainage W. manholes from A4+840 to A5+000 L= 160 m LHS	20d	0%	20d	06-Aug-14	30-Aug-14	06-Aug-14	30-Aug-14	52d	$0	$37,490
NAB2420	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	15d	0%	15d	12-Aug-14	30-Aug-14	12-Aug-14	30-Aug-14	52d	$0	$27,028
NAB3360	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+600 length L= 9 m RHS	12d	0%	12d	14-Aug-14	27-Aug-14	14-Aug-14	27-Aug-14	61d	$0	$5,346
NAB3390	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+840 length L= 9 m RHS	12d	0%	12d	17-Aug-14	30-Aug-14	17-Aug-14	30-Aug-14	31d	$0	$5,346
NAB3370	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	10d	0%	10d	18-Aug-14	30-Aug-14	18-Aug-14	30-Aug-14	60d	$0	$13,764
Water lines		10d		3d	22-Sep-14	02-Oct-14	22-May-14 A	05-Jul-14	56d	$68,350	$68,700
NAB3350-new	12" Steel pipeline beit iba from st 4+450 To st 4+950 RHS	10d	75%	3d	22-Sep-14	02-Oct-14	22-May-14 A	05-Jul-14	56d	$68,350	$68,700
Sewer line		12d		12d	06-Aug-14	20-Aug-14	06-Aug-14	20-Aug-14	28d	$0	$8,619
NAB2410	12" Sewer line for from St. A4+500 to St. A4+600 L=100 M LHS	12d	0%	12d	06-Aug-14	20-Aug-14	06-Aug-14	20-Aug-14	28d	$0	$8,619
Concrete works		29d		29d	06-Aug-14	09-Sep-14	06-Aug-14	09-Sep-14	51d	$0	$70,190
NAB2400	Conc.boundary walls from A4+578 to A4+600 L= 22 m LHS	12d	0%	12d	06-Aug-14	20-Aug-14	06-Aug-14	20-Aug-14	60d	$0	$12,699
NAB3350	Conc. Retaining walls from A4+560 to A4+620 L= 60 m RHS	25d	0%	25d	11-Aug-14	09-Sep-14	11-Aug-14	09-Sep-14	51d	$0	$37,775
NAB3380	Conc. Retaining walls from A4+830 to A4+865 L= 35 m RHS	19d	0%	19d	16-Aug-14	07-Sep-14	16-Aug-14	07-Sep-14	13d	$0	$19,716
Tooping and Basecourse		48d		48d	07-Sep-14	06-Nov-14	07-Sep-14	06-Nov-14	13d	$0	$145,277
NAB2440	20 cm Thick Topping Layer LHS	8d	0%	8d	07-Sep-14	16-Sep-14	07-Sep-14	16-Sep-14	13d	$0	$18,937
NAB3400	20 cm Thick Topping Layer RHS	8d	0%	8d	16-Sep-14	25-Sep-14	16-Sep-14	25-Sep-14	13d	$0	$13,601
NAB2460	20 cm Thick Base Course- First Layer LHS	8d	0%	8d	25-Sep-14	09-Oct-14	25-Sep-14	09-Oct-14	13d	$0	$30,679
NAB3420	20 cm Thick Base Course- First Layer RHS	8d	0%	8d	09-Oct-14	19-Oct-14	09-Oct-14	19-Oct-14	13d	$0	$25,691
NAB2470	20 cm Thick Base Course- Second Layer LHS	8d	0%	8d	19-Oct-14	28-Oct-14	19-Oct-14	28-Oct-14	13d	$0	$30,679
NAB3430	20 cm Thick Base Course- Second Layer RHS	8d	0%	8d	28-Oct-14	06-Nov-14	28-Oct-14	06-Nov-14	13d	$0	$25,691
Asphalt binder		2d		2d	06-Nov-14	09-Nov-14	06-Nov-14	09-Nov-14	34d	$0	$143,076
NAB2480	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	06-Nov-14	09-Nov-14	06-Nov-14	09-Nov-14	13d	$0	$86,048
NAB3450	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	06-Nov-14	09-Nov-14	06-Nov-14	09-Nov-14	34d	$0	$57,027
Street Lighting Poles and Curbstone		22d		22d	28-Oct-14	24-Nov-14	28-Oct-14	24-Nov-14	26d	$0	$75,459
NAB2450	Stone wall from A4+710 to A4+780 L=70 m LHS	11d	0%	11d	28-Oct-14	10-Nov-14	28-Oct-14	10-Nov-14	24d	$0	$5,368
NAB3410	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	06-Nov-14	19-Nov-14	06-Nov-14	19-Nov-14	30d	$0	$0
NAB2490	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	7d	09-Nov-14	18-Nov-14	09-Nov-14	18-Nov-14	13d	$0	$23,224
NAB2500	Conc. Sidewalk and ramps including base course LHS	10d	0%	10d	11-Nov-14	24-Nov-14	11-Nov-14	24-Nov-14	13d	$0	$23,642
NAB3440	Precast Conc. Curbstone for RHS (Mediane) RHS	4d	0%	4d	13-Nov-14	19-Nov-14	13-Nov-14	19-Nov-14	30d	$0	$23,224

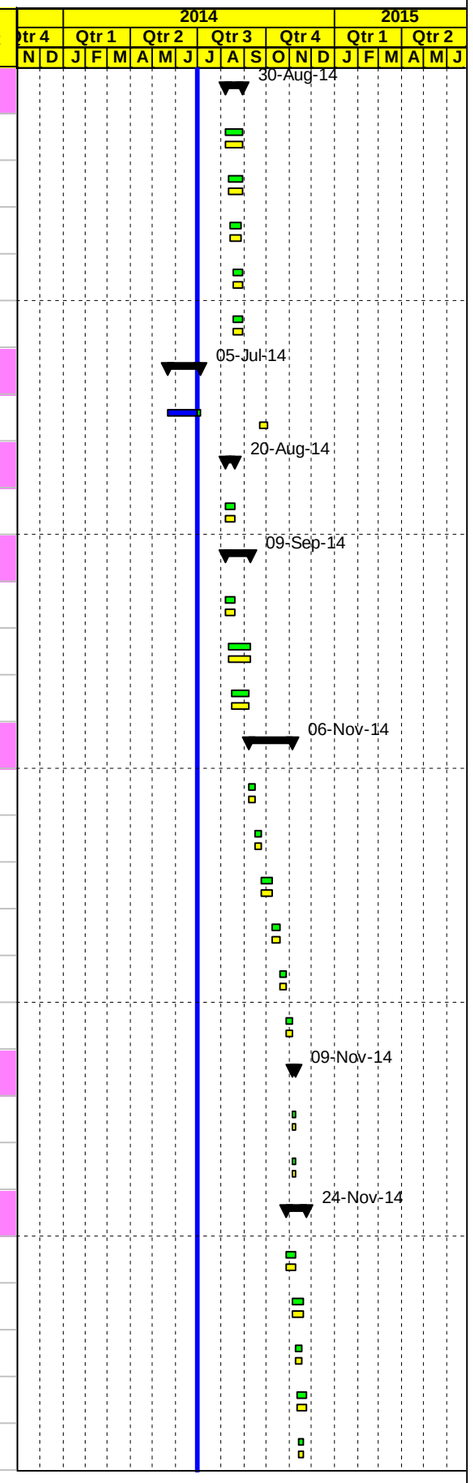

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
Main Road St. A5+000 To St. A5+450 LHS & RHS Area A		131d		131d	01-Jul-14	21-Dec-14	01-Jul-14	21-Dec-14	7d	$0	$528,722
NAB5000	Maintain traffic control and safety plan ,Relocating utilities	131d	0%	131d	01-Jul-14	21-Dec-14	01-Jul-14	21-Dec-14	7d	$0	$0
Excavation		24d		24d	20-Aug-14	17-Sep-14	20-Aug-14	17-Sep-14	0d	$0	$72,553
NAB2520	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	12d	0%	12d	20-Aug-14	03-Sep-14	20-Aug-14	03-Sep-14	0d	$0	$43,587
NAB3470	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	12d	0%	12d	03-Sep-14	17-Sep-14	03-Sep-14	17-Sep-14	0d	$0	$28,967
Storm System		14d		14d	17-Sep-14	08-Oct-14	17-Sep-14	08-Oct-14	32d	$0	$56,251
NAB2530	60 cm Conc. Pipes for drainage W. manholes from A5+000 to A5+120 L= 120 m LHS	13d	0%	13d	17-Sep-14	02-Oct-14	17-Sep-14	02-Oct-14	33d	$0	$26,430
NAB3480	New Conc.Pipe Culvert Dia. 80 cm @ St. A5+160 length L= 15 m RHS	14d	0%	14d	17-Sep-14	08-Oct-14	17-Sep-14	08-Oct-14	0d	$0	$6,831
NAB2540	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	10d	0%	10d	21-Sep-14	02-Oct-14	21-Sep-14	02-Oct-14	33d	$0	$22,990
Water lines		10d		10d	01-Jul-14	19-Jul-14	01-Jul-14	19-Jul-14	59d	$0	$74,084
NAB3460-new	12" Steel pipeline beit iba from st 4+950 To st 5+450 RHS	10d	0%	10d	01-Jul-14	19-Jul-14	01-Jul-14	19-Jul-14	59d	$0	$74,084
Tooping and Basecourse		48d		48d	08-Oct-14	04-Dec-14	08-Oct-14	04-Dec-14	0d	$0	$150,542
NAB2550	20 cm Thick Topping Layer LHS	8d	0%	8d	08-Oct-14	18-Oct-14	08-Oct-14	18-Oct-14	0d	$0	$17,415
NAB3490	20 cm Thick Topping Layer RHS	8d	0%	8d	18-Oct-14	27-Oct-14	18-Oct-14	27-Oct-14	0d	$0	$16,008
NAB2560	20 cm Thick Base Course- First Layer LHS	8d	0%	8d	27-Oct-14	05-Nov-14	27-Oct-14	05-Nov-14	0d	$0	$27,612
NAB3510	20 cm Thick Base Course- First Layer RHS	8d	0%	8d	05-Nov-14	16-Nov-14	05-Nov-14	16-Nov-14	0d	$0	$27,303
NAB2570	20 cm Thick Base Course- Second Layer LHS	8d	0%	8d	16-Nov-14	25-Nov-14	16-Nov-14	25-Nov-14	0d	$0	$32,512
NAB3520	20 cm Thick Base Course- Second Layer RHS	8d	0%	8d	25-Nov-14	04-Dec-14	25-Nov-14	04-Dec-14	0d	$0	$29,694
Asphalt binder		2d		2d	04-Dec-14	07-Dec-14	04-Dec-14	07-Dec-14	7d	$0	$99,409
NAB2580	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	04-Dec-14	07-Dec-14	04-Dec-14	07-Dec-14	0d	$0	$63,594
NAB3540	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	04-Dec-14	07-Dec-14	04-Dec-14	07-Dec-14	7d	$0	$35,815
Street Lighting Poles and Curbstone		14d		14d	04-Dec-14	21-Dec-14	04-Dec-14	21-Dec-14	7d	$0	$75,882
NAB3500	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	04-Dec-14	16-Dec-14	04-Dec-14	16-Dec-14	11d	$0	$0
NAB2590	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	7d	07-Dec-14	15-Dec-14	07-Dec-14	15-Dec-14	0d	$0	$21,908
NAB3530	Precast Conc. Curbstone for RHS (Mediane) RHS	4d	0%	4d	07-Dec-14	11-Dec-14	07-Dec-14	11-Dec-14	15d	$0	$23,224
NAB2600	Conc. Sidewalk and ramps including base course LHS	10d	0%	10d	09-Dec-14	21-Dec-14	09-Dec-14	21-Dec-14	0d	$0	$30,750
Phase Two closed (RHS & LHS) from St. A0+000 - A2+020		181d		175d	25-Jun-14	22-Dec-14	24-Apr-14 A	22-Dec-14	7d	$151,761	$3,190,370
Main Road St. A2+020 To St. A1+500 RHS & LHS Area B		146d		85d	25-Jun-14	17-Nov-14	24-Apr-14 A	24-Sep-14	67d	$151,761	$813,593
NAB4030	Maintain traffic control and safety plan ,Relocating utilities	107d	43.18%	61d	25-Jun-14	17-Nov-14	24-Apr-14 A	24-Sep-14	51d	$0	$0
Excavation		69d		4d	25-Jun-14	28-Sep-14	24-Apr-14 A	08-Jul-14	72d	$49,828	$66,751

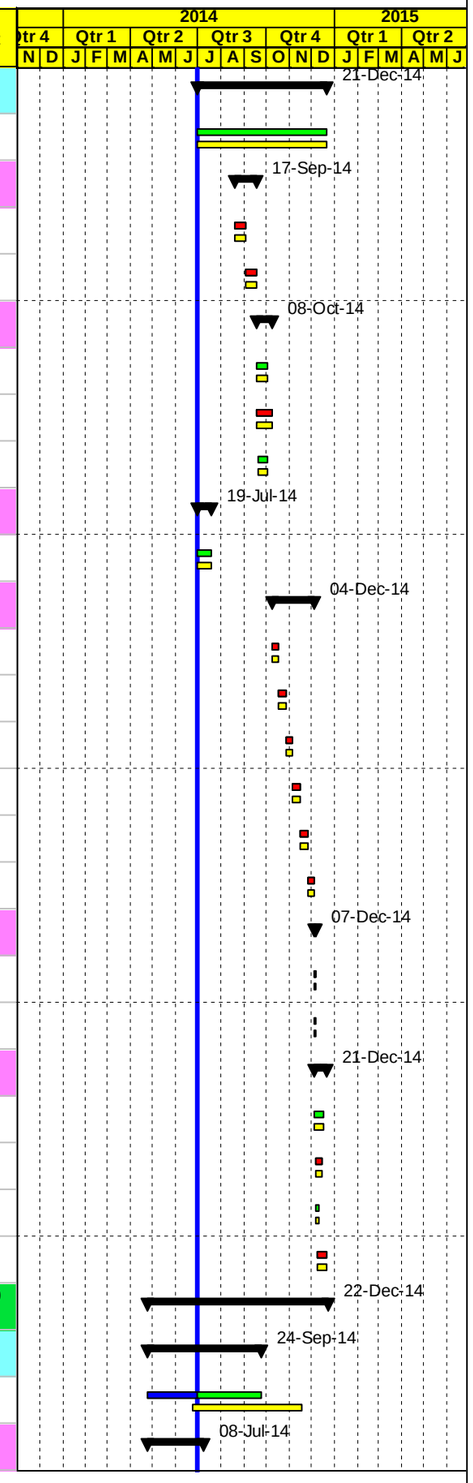

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB4790	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	14d	70%	4d	25-Jun-14	17-Jul-14	24-Apr-14 A	08-Jul-14	72d	$25,008	$35,726
NAB4040	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	20d	80%	4d	06-Sep-14	28-Sep-14	08-Jun-14 A	08-Jul-14	0d	$24,820	$31,025
Storm System		30d		17d	25-Jun-14	13-Aug-14	18-Jun-14 A	04-Aug-14	63d	$71,243	$156,564
NAB4060	New Conc.Pipe Culvert Dia.80 cm @ St. A1+690 length L= 46 m RHS	18d	100%	0d	14-Jul-14	13-Aug-14	18-Jun-14 A	21-Jun-14 A		$9,278	$9,278
NAB4070	60 cm Conc. Pipes for drainage W. manholes from A1+690 to A2+020 L= 330 m RHS	29d	90%	3d	25-Jun-14	12-Aug-14	18-Jun-14 A	06-Jul-14	55d	$61,965	$68,850
NAB4050	60 cm Conc. Pipes for drainage W. manholes from A1+500 to A1+620 L= 120 m RHS	14d	0%	14d	06-Jul-14	04-Aug-14	06-Jul-14	04-Aug-14	55d	$0	$33,180
NAB4830	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	10d	0%	10d	14-Jul-14	04-Aug-14	14-Jul-14	04-Aug-14	55d	$0	$42,156
NAB4080	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	10d	0%	10d	14-Jul-14	04-Aug-14	14-Jul-14	04-Aug-14	63d	$0	$3,100
Water lines		12d		12d	08-Jul-14	03-Aug-14	08-Jul-14	03-Aug-14	72d	$0	$140,880
NAB4090	12" Steel pipeline deir sharaf @ A1+960 TO Nablus connection RHS	5d	0%	5d	08-Jul-14	17-Jul-14	08-Jul-14	17-Jul-14	71d	$0	$8,820
NAB4820	3" Water pipeline from St. A 1+900 to A 2+020 (LHS) =120 M LHS	6d	0%	6d	08-Jul-14	20-Jul-14	08-Jul-14	20-Jul-14	78d	$0	$7,320
NAB4800	12" Steel pipeline deir sharaf project L = 570 m LHS	12d	0%	12d	08-Jul-14	03-Aug-14	08-Jul-14	03-Aug-14	72d	$0	$124,740
Sewer line		3d		3d	08-Jul-14	14-Jul-14	08-Jul-14	14-Jul-14	81d	$0	$7,774
NAB4810	12" Sewer line from St. A1+930 to St. A2+020 L=90 M LHS	3d	0%	3d	08-Jul-14	14-Jul-14	08-Jul-14	14-Jul-14	81d	$0	$7,774
Concrete works		21d		0d	25-Jun-14	15-Jul-14	15-Jun-14 A	24-Jun-14 A		$23,730	$23,730
NAB4680-new	Conc. Retaining walls from A1+860 to A1+935 L=75m RHS	21d	100%	0d	25-Jun-14	15-Jul-14	15-Jun-14 A	24-Jun-14 A		$18,393	$18,393
NAB4685-new	Conc. Retaining walls from A1+720 to A1+750 L=30m RHS	21d	100%	0d	25-Jun-14	15-Jul-14	17-Jun-14 A	24-Jun-14 A		$5,337	$5,337
Tooping and Basecourse		98d		45d	09-Jul-14	17-Nov-14	21-Jun-14 A	06-Sep-14	51d	$6,960	$170,741
NAB4100	20 cm Thick Topping Layer RHS	8d	40%	5d	08-Nov-14	17-Nov-14	21-Jun-14 A	09-Jul-14	51d	$6,960	$17,400
NAB4840	20 cm Thick Topping Layer LHS	8d	0%	8d	09-Jul-14	24-Jul-14	09-Jul-14	24-Jul-14	51d	$0	$21,982
NAB4120	20 cm Thick Base Course- First Layer RHS	8d	0%	8d	24-Jul-14	09-Aug-14	24-Jul-14	09-Aug-14	51d	$0	$30,679
NAB4850	20 cm Thick Base Course- First Layer LHS	8d	0%	8d	09-Aug-14	18-Aug-14	09-Aug-14	18-Aug-14	51d	$0	$35,001
NAB4130	20 cm Thick Base Course- Second Layer RHS	8d	0%	8d	18-Aug-14	27-Aug-14	18-Aug-14	27-Aug-14	51d	$0	$30,679
NAB4860	20 cm Thick Base Course- Second Layer LHS	8d	0%	8d	27-Aug-14	06-Sep-14	27-Aug-14	06-Sep-14	51d	$0	$35,001
Asphalt binder		2d		2d	06-Sep-14	08-Sep-14	06-Sep-14	08-Sep-14	57d	$0	$179,765
NAB4875	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	06-Sep-14	08-Sep-14	06-Sep-14	08-Sep-14	51d	$0	$103,943
NAB4160	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	06-Sep-14	08-Sep-14	06-Sep-14	08-Sep-14	57d	$0	$75,823
Street Lighting Poles and Curbstone		24d		24d	27-Aug-14	24-Sep-14	27-Aug-14	24-Sep-14	51d	$0	$67,389
NAB4110	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	27-Aug-14	08-Sep-14	27-Aug-14	08-Sep-14	65d	$0	$0
NAB4870	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	6d	0%	6d	08-Sep-14	15-Sep-14	08-Sep-14	15-Sep-14	51d	$0	$10,078

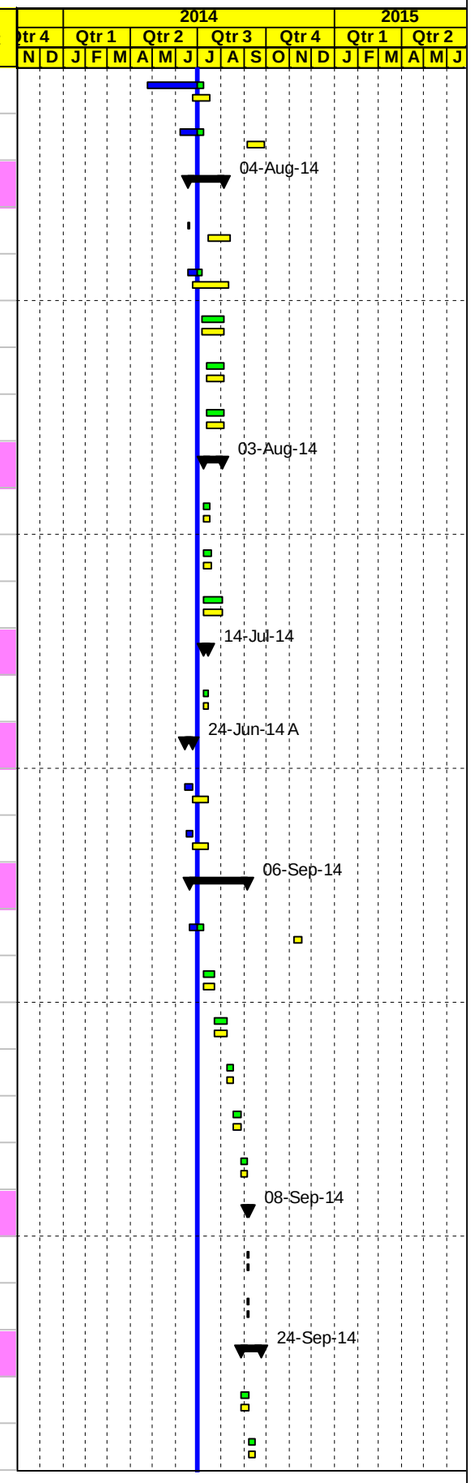

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB4140	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	6d	0%	6d	08-Sep-14	15-Sep-14	08-Sep-14	15-Sep-14	52d	$0	$23,224
NAB4873	Conc. Sidewalk and ramps including base course LHS	8d	0%	8d	15-Sep-14	24-Sep-14	15-Sep-14	24-Sep-14	51d	$0	$24,716
NAB4150	Conc. Sidewalk and ramps including base course RHS	7d	0%	7d	15-Sep-14	23-Sep-14	15-Sep-14	23-Sep-14	52d	$0	$9,370
Main Road St. A1+500 To St. A1+000 RHS & LHS Area C		93d		93d	08-Jul-14	10-Nov-14	08-Jul-14	10-Nov-14	22d	$0	$819,427
NAB3880	Maintain traffic control and safety plan ,Relocating utilities RHS	93d	0%	93d	08-Jul-14	10-Nov-14	08-Jul-14	10-Nov-14	22d	$0	$0
Excavation		24d		24d	08-Jul-14	17-Aug-14	08-Jul-14	17-Aug-14	0d	$0	$87,532
NAB3890	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	12d	0%	12d	08-Jul-14	03-Aug-14	08-Jul-14	03-Aug-14	0d	$0	$44,501
NAB4590	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	12d	0%	12d	03-Aug-14	17-Aug-14	03-Aug-14	17-Aug-14	0d	$0	$43,031
Storm System		27d		27d	03-Aug-14	03-Sep-14	03-Aug-14	03-Sep-14	47d	$0	$208,129
NAB3950	60 cm Conc. Pipes for drainage W. manholes from A1+300 to A1+500 L= 200 m RHS	22d	0%	22d	03-Aug-14	28-Aug-14	03-Aug-14	28-Aug-14	24d	$0	$58,200
NAB3920	New box culvert (2*2.5) @ St. A1+095 RHS length L= 15.5 m RHS	20d	0%	20d	06-Aug-14	30-Aug-14	06-Aug-14	30-Aug-14	51d	$0	$33,341
NAB3930	60 cm Conc. Pipes for drainage W. manholes from A1+100 to A1+260 L= 160 m RHS	17d	0%	17d	07-Aug-14	27-Aug-14	07-Aug-14	27-Aug-14	53d	$0	$57,610
NAB3940	New Conc.Pipe Culvert Dia.80 cm @ St. A1+300 length L= 84 m RHS	22d	0%	22d	09-Aug-14	03-Sep-14	09-Aug-14	03-Sep-14	47d	$0	$23,760
NAB3910	New Conc.Pipe Culvert Dia.80 cm @ St. A1+100 length L= 14 m RHS	17d	0%	17d	10-Aug-14	30-Aug-14	10-Aug-14	30-Aug-14	51d	$0	$5,940
NAB4610	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	10d	0%	10d	17-Aug-14	28-Aug-14	17-Aug-14	28-Aug-14	24d	$0	$29,278
Water lines		11d		11d	17-Aug-14	30-Aug-14	17-Aug-14	30-Aug-14	23d	$0	$109,200
NAB4600	12" Steel pipeline deir sharaf project L = 500 m LHS	11d	0%	11d	17-Aug-14	30-Aug-14	17-Aug-14	30-Aug-14	23d	$0	$109,200
Concrete works		21d		21d	07-Aug-14	31-Aug-14	07-Aug-14	31-Aug-14	22d	$0	$54,168
NAB3900	Retaining walls with step barrier & channel from A`1+000 to A1+110 L= 110 m RHS	21d	0%	21d	07-Aug-14	31-Aug-14	07-Aug-14	31-Aug-14	22d	$0	$54,168
Tooping and Basecourse		42d		42d	01-Sep-14	23-Oct-14	01-Sep-14	23-Oct-14	22d	$0	$157,550
NAB3960	20 cm Thick Topping Layer RHS	7d	0%	7d	01-Sep-14	08-Sep-14	01-Sep-14	08-Sep-14	22d	$0	$20,300
NAB4620	20 cm Thick Topping Layer LHS	7d	0%	7d	09-Sep-14	16-Sep-14	09-Sep-14	16-Sep-14	22d	$0	$15,225
NAB3970	20 cm Thick Base Course- First Layer RHS	7d	0%	7d	17-Sep-14	24-Sep-14	17-Sep-14	24-Sep-14	22d	$0	$32,296
NAB4630	20 cm Thick Base Course- First Layer LHS	7d	0%	7d	25-Sep-14	02-Oct-14	25-Sep-14	02-Oct-14	22d	$0	$29,121
NAB3990	20 cm Thick Base Course- Second Layer RHS	7d	0%	7d	08-Oct-14	15-Oct-14	08-Oct-14	15-Oct-14	22d	$0	$31,487
NAB4640	20 cm Thick Base Course- Second Layer LHS	7d	0%	7d	16-Oct-14	23-Oct-14	16-Oct-14	23-Oct-14	22d	$0	$29,121
Asphalt binder		2d		2d	25-Oct-14	26-Oct-14	25-Oct-14	26-Oct-14	22d	$0	$152,370
NAB4670	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	25-Oct-14	26-Oct-14	25-Oct-14	26-Oct-14	22d	$0	$67,757
NAB4020	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	25-Oct-14	26-Oct-14	25-Oct-14	26-Oct-14	22d	$0	$84,614
Street Lighting Poles and Curbstone		22d		22d	16-Oct-14	10-Nov-14	16-Oct-14	10-Nov-14	22d	$0	$50,478

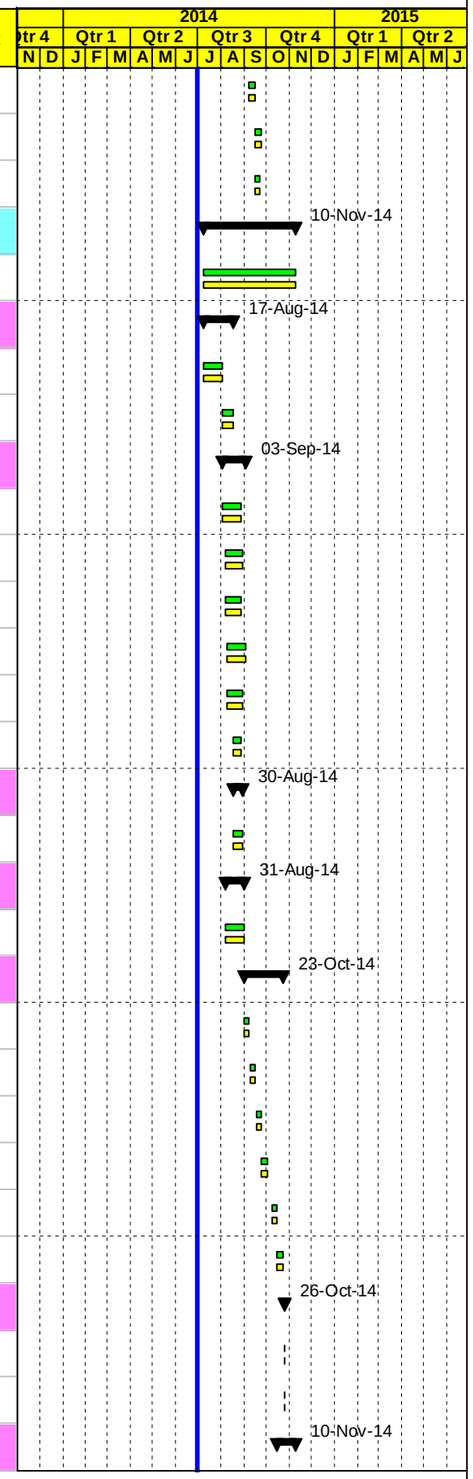

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB3980	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	16-Oct-14	27-Oct-14	16-Oct-14	27-Oct-14	34d	$0	$0
NAB4650	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	6d	0%	6d	27-Oct-14	02-Nov-14	27-Oct-14	02-Nov-14	22d	$0	$10,078
NAB4000	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	6d	0%	6d	27-Oct-14	02-Nov-14	27-Oct-14	02-Nov-14	22d	$0	$13,146
NAB4660	Conc. Sidewalk and ramps including base course LHS	7d	0%	7d	03-Nov-14	10-Nov-14	03-Nov-14	10-Nov-14	22d	$0	$23,642
NAB4010	Conc. Sidewalk and ramps including base course RHS	7d	0%	7d	03-Nov-14	10-Nov-14	03-Nov-14	10-Nov-14	22d	$0	$3,612
Main Road St. A1+000 To St. A0+500 RHS & LHS Area C		87d		87d	17-Aug-14	02-Dec-14	17-Aug-14	02-Dec-14	17d	$0	$897,855
NAB3700	Maintain traffic control and safety plan ,Relocating utilities RHS	87d	0%	87d	17-Aug-14	02-Dec-14	17-Aug-14	02-Dec-14	17d	$0	$0
Excavation		24d		24d	17-Aug-14	14-Sep-14	17-Aug-14	14-Sep-14	0d	$0	$84,034
NAB3710	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	12d	0%	12d	17-Aug-14	31-Aug-14	17-Aug-14	31-Aug-14	0d	$0	$43,575
NAB4460	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	12d	0%	12d	31-Aug-14	14-Sep-14	31-Aug-14	14-Sep-14	0d	$0	$40,460
Storm System		24d		24d	31-Aug-14	28-Sep-14	31-Aug-14	28-Sep-14	51d	$0	$165,780
NAB3800	New box culvert (2*2.5) @ St. A0+915 RHS length L= 6 m RHS	14d	0%	14d	31-Aug-14	16-Sep-14	31-Aug-14	16-Sep-14	22d	$0	$15,191
NAB3760	60 cm Conc. Pipes for drainage W. manholes from A0+580 to A0+740 L= 160 m RHS	16d	0%	16d	31-Aug-14	18-Sep-14	31-Aug-14	18-Sep-14	20d	$0	$57,990
NAB3780	New Conc.Pipe Culvert Dia.80 cm @ St. A0+700 length L= 14 m RHS	17d	0%	17d	02-Sep-14	22-Sep-14	02-Sep-14	22-Sep-14	56d	$0	$6,534
NAB3770	New box culvert (2*2.5) @ St. A0+595 RHS length L= 7 m RHS	15d	0%	15d	03-Sep-14	21-Sep-14	03-Sep-14	21-Sep-14	57d	$0	$18,876
NAB3740	New Conc.Pipe Culvert Dia.80 cm @ St. A0+580 length L= 11.5 m RHS	15d	0%	15d	04-Sep-14	22-Sep-14	04-Sep-14	22-Sep-14	56d	$0	$6,534
NAB4490	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	10d	0%	10d	07-Sep-14	18-Sep-14	07-Sep-14	18-Sep-14	20d	$0	$24,814
NAB3720	New box culvert (2*2.5) @ St. A0+510 RHS length L= 11 m RHS	18d	0%	18d	07-Sep-14	28-Sep-14	07-Sep-14	28-Sep-14	51d	$0	$23,441
NAB3730	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	10d	0%	10d	07-Sep-14	18-Sep-14	07-Sep-14	18-Sep-14	59d	$0	$12,400
Water lines		27d		27d	14-Sep-14	20-Oct-14	14-Sep-14	20-Oct-14	25d	$0	$109,200
NAB4480	12" Steel pipeline deir sharaf project L = 500 m LHS	11d	0%	11d	14-Sep-14	27-Sep-14	14-Sep-14	27-Sep-14	13d	$0	$109,200
NAB4500	Construct 80 ARV chamber @ A0+810 LHS	12d	0%	12d	27-Sep-14	15-Oct-14	27-Sep-14	15-Oct-14	29d	$0	$0
NAB4510	Construct 200 Wash out chamber @ A0+820 LHS	12d	0%	12d	01-Oct-14	20-Oct-14	01-Oct-14	20-Oct-14	25d	$0	$0
Sewer line		3d		3d	14-Sep-14	17-Sep-14	14-Sep-14	17-Sep-14	21d	$0	$5,792
NAB4470	10" Sewer line from St. 0+450 to 0+520 LHS L=70 M LHS	3d	0%	3d	14-Sep-14	17-Sep-14	14-Sep-14	17-Sep-14	21d	$0	$5,792
Concrete works		30d		30d	31-Aug-14	09-Oct-14	31-Aug-14	09-Oct-14	45d	$0	$203,428
NAB3810	Retaining walls with step barrier & channel from A0+916 to A1+000 L= 84 m RHS	19d	0%	19d	31-Aug-14	22-Sep-14	31-Aug-14	22-Sep-14	56d	$0	$48,393
NAB3805	Retaining walls with step barrier & channel from A0+830 to A0+910 L= 80 m RHS	18d	0%	18d	02-Sep-14	23-Sep-14	02-Sep-14	23-Sep-14	55d	$0	$48,674
NAB3790	Retaining walls with step barrier & channel from A0+750 to A0+830 L= 80 m RHS	18d	0%	18d	03-Sep-14	24-Sep-14	03-Sep-14	24-Sep-14	54d	$0	$48,674
NAB3750	Retaining walls with step barrier & channel from A0+500 to A0+620 L= 120 m RHS	26d	0%	26d	04-Sep-14	09-Oct-14	04-Sep-14	09-Oct-14	45d	$0	$57,688

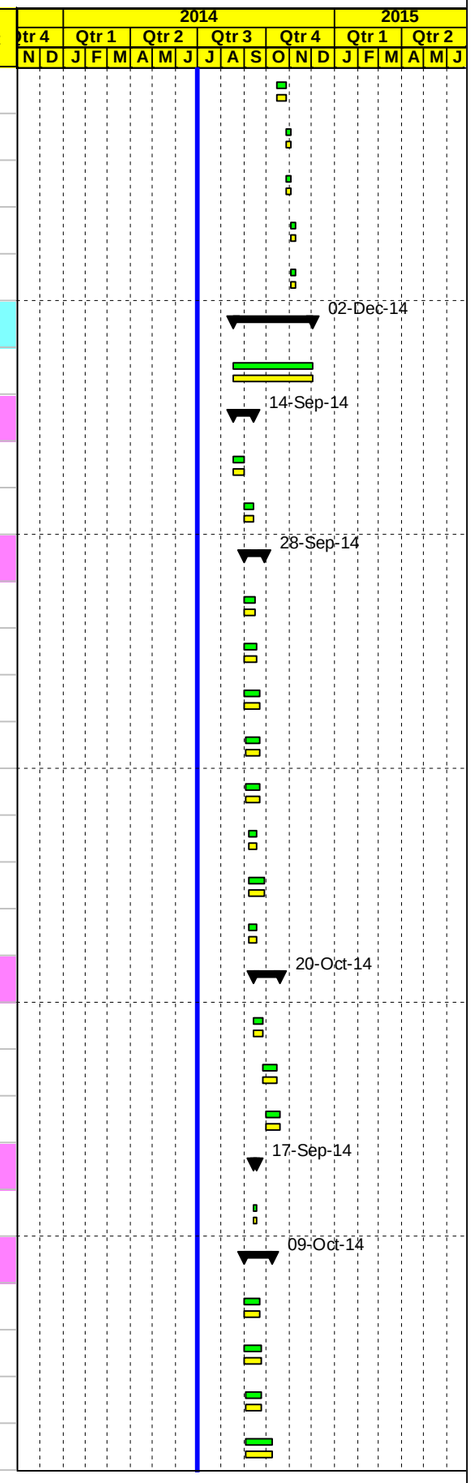

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
Tooping and Basecourse		42d		42d	27-Sep-14	20-Nov-14	27-Sep-14	20-Nov-14	17d	$0	$146,175
NAB3820	20 cm Thick Topping Layer RHS	7d	0%	7d	27-Sep-14	09-Oct-14	27-Sep-14	09-Oct-14	13d	$0	$16,907
NAB4520	20 cm Thick Topping Layer LHS	7d	0%	7d	09-Oct-14	18-Oct-14	09-Oct-14	18-Oct-14	13d	$0	$15,530
NAB3840	20 cm Thick Base Course- First Layer RHS	7d	0%	7d	18-Oct-14	26-Oct-14	18-Oct-14	26-Oct-14	13d	$0	$26,911
NAB4530	20 cm Thick Base Course- First Layer LHS	7d	0%	7d	26-Oct-14	03-Nov-14	26-Oct-14	03-Nov-14	13d	$0	$27,509
NAB4540	20 cm Thick Base Course- Second Layer LHS	7d	0%	7d	03-Nov-14	11-Nov-14	03-Nov-14	11-Nov-14	13d	$0	$27,509
NAB3850	20 cm Thick Base Course- Second Layer RHS	7d	0%	7d	11-Nov-14	20-Nov-14	11-Nov-14	20-Nov-14	17d	$0	$31,811
Asphalt binder		9d		9d	11-Nov-14	23-Nov-14	11-Nov-14	23-Nov-14	20d	$0	$139,219
NAB4570	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	11-Nov-14	13-Nov-14	11-Nov-14	13-Nov-14	13d	$0	$67,466
NAB3870	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	20-Nov-14	23-Nov-14	20-Nov-14	23-Nov-14	20d	$0	$71,753
Street Lighting Poles and Curbstone		15d		15d	13-Nov-14	02-Dec-14	13-Nov-14	02-Dec-14	17d	$0	$44,226
NAB4550	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	6d	0%	6d	13-Nov-14	22-Nov-14	13-Nov-14	22-Nov-14	13d	$0	$10,078
NAB3830	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	20-Nov-14	02-Dec-14	20-Nov-14	02-Dec-14	17d	$0	$0
NAB4560	Conc. Sidewalk and ramps including base course LHS	9d	0%	9d	22-Nov-14	02-Dec-14	22-Nov-14	02-Dec-14	13d	$0	$21,002
NAB3860	Precast Conc. Curbstone for RHS (Mediane) RHS	5d	0%	5d	26-Nov-14	02-Dec-14	26-Nov-14	02-Dec-14	17d	$0	$13,146
Main Road From St. A0+500 To St. A0+000 RHS & LHS Area C		80d		80d	14-Sep-14	22-Dec-14	14-Sep-14	22-Dec-14	5d	$0	$659,495
NAB3560	Maintain traffic control and safety plan ,Relocating utilities RHS	80d	0%	80d	14-Sep-14	22-Dec-14	14-Sep-14	22-Dec-14	5d	$0	$0
Excavation		24d		24d	14-Sep-14	16-Oct-14	14-Sep-14	16-Oct-14	0d	$0	$91,177
NAB3570	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	12d	0%	12d	14-Sep-14	28-Sep-14	14-Sep-14	28-Sep-14	0d	$0	$45,431
NAB4330	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	12d	0%	12d	28-Sep-14	16-Oct-14	28-Sep-14	16-Oct-14	0d	$0	$45,746
Storm System		20d		20d	28-Sep-14	26-Oct-14	28-Sep-14	26-Oct-14	28d	$0	$159,314
NAB3580	New Conc.Pipe Culvert Dia.80 cm @ St. A0+140 length L= 67 m RHS	20d	0%	20d	28-Sep-14	26-Oct-14	28-Sep-14	26-Oct-14	0d	$0	$26,730
NAB3610	60 cm Conc. Pipes for drainage W. manholes from A0+140 to A0+300 L= 160 m RHS	16d	0%	16d	28-Sep-14	21-Oct-14	28-Sep-14	21-Oct-14	4d	$0	$37,490
NAB3590	New Conc.Pipe Culvert Dia. 60 cm @ St. A0+000 length L= 60 m RHS	18d	0%	18d	28-Sep-14	23-Oct-14	28-Sep-14	23-Oct-14	2d	$0	$9,840
NAB3620	New Conc.Pipe Culvert Dia.80 cm @ St. A0+360 length L= 29 m RHS	16d	0%	16d	28-Sep-14	21-Oct-14	28-Sep-14	21-Oct-14	25d	$0	$10,098
NAB3630	60 cm Conc. Pipes for drainage W. manholes from A0+360 to A0+460 L= 100 m RHS	12d	0%	12d	28-Sep-14	16-Oct-14	28-Sep-14	16-Oct-14	29d	$0	$42,000
NAB4370	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	10d	0%	10d	09-Oct-14	21-Oct-14	09-Oct-14	21-Oct-14	32d	$0	$18,278
NAB3600	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	10d	0%	10d	09-Oct-14	21-Oct-14	09-Oct-14	21-Oct-14	25d	$0	$14,878
Water lines		27d		27d	16-Oct-14	18-Nov-14	16-Oct-14	18-Nov-14	9d	$0	$102,690
NAB4340	12" Steel pipeline deir sharaf project to A0+450 L = 470 m LHS	10d	0%	10d	16-Oct-14	28-Oct-14	16-Oct-14	28-Oct-14	2d	$0	$102,690

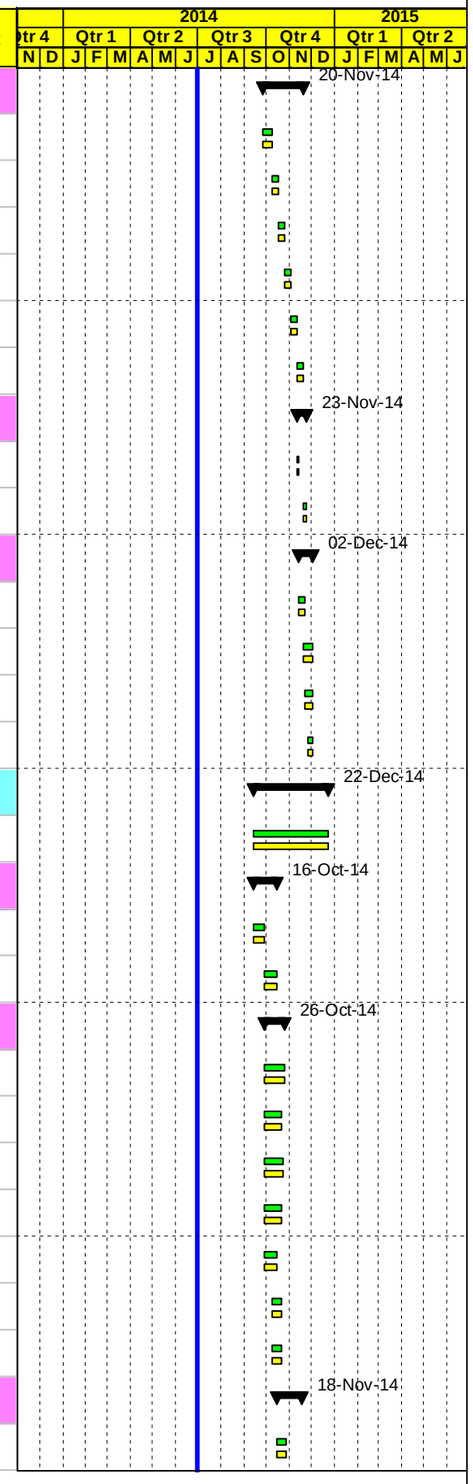

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB4360	Construct 250 Wash out chamber @ A0+070 LHS	12d	0%	12d	28-Oct-14	11-Nov-14	28-Oct-14	11-Nov-14	14d	$0	$0
NAB4350	Construct SHAVI SHAMRON monitoring chamber LHS	16d	0%	16d	29-Oct-14	18-Nov-14	29-Oct-14	18-Nov-14	9d	$0	$0
Sewer line		8d		8d	16-Oct-14	26-Oct-14	16-Oct-14	26-Oct-14	0d	$0	$13,156
NAB4380	10" Sewer line from St. 0+290 to 0+450 LHS L=160 M LHS	8d	0%	8d	16-Oct-14	26-Oct-14	16-Oct-14	26-Oct-14	0d	$0	$13,156
Tooping and Basecourse		35d		35d	26-Oct-14	07-Dec-14	26-Oct-14	07-Dec-14	0d	$0	$147,610
NAB4390	20 cm thick topping layer From A0+130 to A0+450 LHS	7d	0%	7d	26-Oct-14	03-Nov-14	26-Oct-14	03-Nov-14	0d	$0	$13,485
NAB3640	20 cm thick topping layer From A0+130 to A0+500 RHS	7d	0%	7d	26-Oct-14	03-Nov-14	26-Oct-14	03-Nov-14	0d	$0	$14,036
NAB3670	20 cm thick base course - first layer From A0+130 to A0+500 RHS	7d	0%	7d	03-Nov-14	11-Nov-14	03-Nov-14	11-Nov-14	0d	$0	$27,239
NAB4400	20 cm thick base course - first layer From A0+130 to A0+450 LHS	7d	0%	7d	11-Nov-14	20-Nov-14	11-Nov-14	20-Nov-14	0d	$0	$31,850
NAB3680	20 cm thick base course - second layer From A0+130 to A0+500 RHS	7d	0%	7d	20-Nov-14	29-Nov-14	20-Nov-14	29-Nov-14	0d	$0	$31,600
NAB4410	20 cm thick base course - second layer From A0+130 to A0+450 LHS	7d	0%	7d	29-Nov-14	07-Dec-14	29-Nov-14	07-Dec-14	0d	$0	$29,400
Asphalt binder		9d		9d	29-Nov-14	09-Dec-14	29-Nov-14	09-Dec-14	11d	$0	$103,627
NAB4990	7 cm Asphalt Binder Course Including Prime Coat RHS	2d	0%	2d	29-Nov-14	01-Dec-14	29-Nov-14	01-Dec-14	18d	$0	$59,033
NAB4440	7 cm Asphalt Binder Course Including Prime Coat LHS	2d	0%	2d	07-Dec-14	09-Dec-14	07-Dec-14	09-Dec-14	0d	$0	$44,594
Street Lighting Poles and Curbstone		20d		20d	29-Nov-14	22-Dec-14	29-Nov-14	22-Dec-14	5d	$0	$41,922
NAB3650	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	10d	29-Nov-14	10-Dec-14	29-Nov-14	10-Dec-14	15d	$0	$0
NAB3660	Reshape to Match with exist. Earth channel from A0+430 TO A0+500 RHS	7d	0%	7d	29-Nov-14	07-Dec-14	29-Nov-14	07-Dec-14	18d	$0	$0
NAB3690	Precast Conc. Curbstone for RHS (Mediane) RHS	5d	0%	5d	04-Dec-14	10-Dec-14	04-Dec-14	10-Dec-14	15d	$0	$10,116
NAB4420	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	5d	0%	5d	09-Dec-14	15-Dec-14	09-Dec-14	15-Dec-14	5d	$0	$10,078
NAB4430	Conc. Sidewalk and ramps including base course LHS	9d	0%	9d	11-Dec-14	22-Dec-14	11-Dec-14	22-Dec-14	5d	$0	$21,728
Phase Three Seg. B from sta.B0+000 to B0+399 Total Close (Area B)		76d		76d	16-Aug-14	17-Nov-14	16-Aug-14	17-Nov-14	35d	$0	$323,248
NAB4180	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade	15d	0%	15d	16-Aug-14	01-Sep-14	16-Aug-14	01-Sep-14	52d	$0	$43,736
NAB4170	Maintain traffic control and safety plan ,Relocating utilities	76d	0%	76d	16-Aug-14	17-Nov-14	16-Aug-14	17-Nov-14	35d	$0	$0
NAB4210	12" Steel pipeline deir sharaf @B0+000 TO Beit Eba connection L= 370 m	10d	0%	10d	02-Sep-14	13-Sep-14	02-Sep-14	13-Sep-14	58d	$0	$80,850
NAB4190	New box culvert 3 (2*1.5) @ St. B0+094 length L= 14 m	21d	0%	21d	02-Sep-14	25-Sep-14	02-Sep-14	25-Sep-14	57d	$0	$34,424
NAB4200	Conc. Retaining walls from B0+230 to B0+340 LHS L= 110 m	26d	0%	26d	02-Sep-14	01-Oct-14	02-Sep-14	01-Oct-14	52d	$0	$33,967
NAB4270	20 cm Thick Base Course- First Layer	10d	0%	10d	14-Sep-14	24-Sep-14	14-Sep-14	24-Sep-14	58d	$0	$30,498
NAB4220	Construct 80 ARV chamber @ B0+100	12d	0%	12d	14-Sep-14	27-Sep-14	14-Sep-14	27-Sep-14	66d	$0	$0
NAB4230	Construct 80 ARV chamber @ B0+365	12d	0%	12d	14-Sep-14	27-Sep-14	14-Sep-14	27-Sep-14	66d	$0	$0
NAB4280	20 cm Thick Base Course- Second Layer	10d	0%	10d	02-Oct-14	18-Oct-14	02-Oct-14	18-Oct-14	52d	$0	$28,347

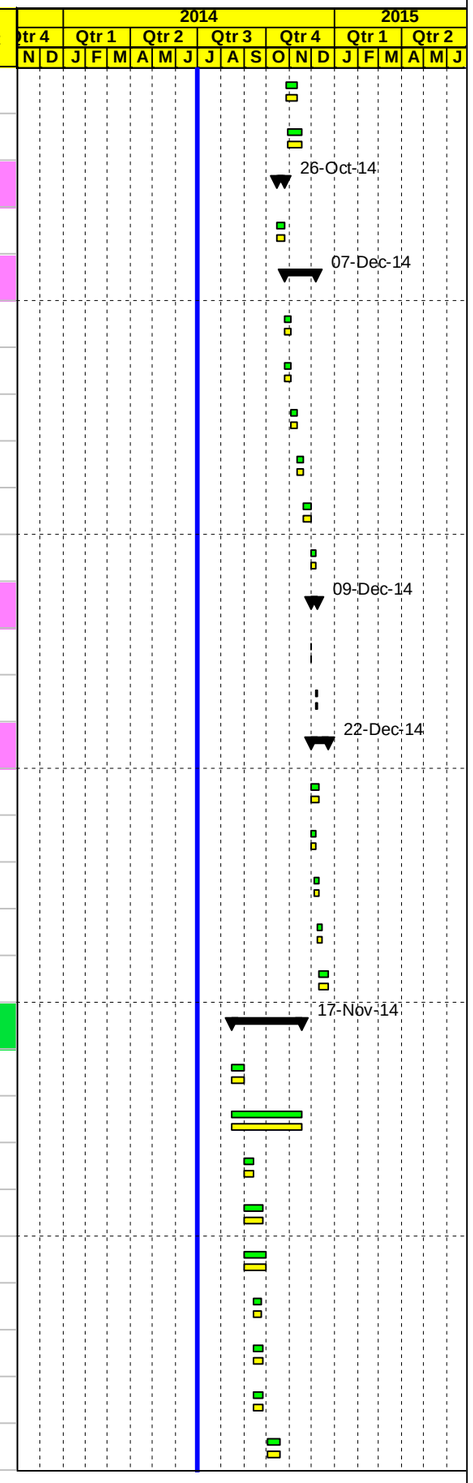

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
NAB4240	Nablus connection chamber st B 0+035 (RHS)	12d	0%	12d	12-Oct-14	26-Oct-14	12-Oct-14	26-Oct-14	45d	$0	$0
NAB4250	Qusin flow monitoring chamber st B 0+190 (RHS	12d	0%	12d	18-Oct-14	01-Nov-14	18-Oct-14	01-Nov-14	40d	$0	$0
NAB4260	Beit Eba connection chamber st B 0+340 (LHS)	12d	0%	12d	23-Oct-14	06-Nov-14	23-Oct-14	06-Nov-14	35d	$0	$0
NAB4310	5 cm Asphalt Binder Course Including Prime Coat	2d	0%	2d	06-Nov-14	09-Nov-14	06-Nov-14	09-Nov-14	35d	$0	$68,038
NAB4290	Precast Conc. Curbstone for RHS (Mediane)	3d	0%	3d	09-Nov-14	12-Nov-14	09-Nov-14	12-Nov-14	35d	$0	$0
NAB4300	Conc. Sidewalk and ramps including base course	3d	0%	3d	12-Nov-14	17-Nov-14	12-Nov-14	17-Nov-14	35d	$0	$3,388
Temporary Detours		152d		6d	01-Jul-14	17-Jan-15	12-Apr-14 A	12-Jul-14	131d	$114,000	$142,500
NAB4915	Milling for detours Sara	3d	100%	0d	13-Jan-15	17-Jan-15	12-Apr-14 A	12-Apr-14 A		$10,000	$10,000
NAB4879	5 cm thick Wearing Course Including Prime Coat for temporary detours (Sara & Beit Iba)	2d	100%	0d	01-Nov-14	02-Nov-14	12-Apr-14 A	15-Apr-14 A		$104,000	$104,000
NAB4877	Excavation & Base-course for Paved Temporary Detours	6d	0%	6d	01-Jul-14	12-Jul-14	01-Jul-14	12-Jul-14	131d	$0	$28,500
Miscellaneous activities - If any as location is not determined yet		21d		21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$321,349
NAB4888	Road Crossings 6" dia. Pipe	21d	0%	21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$110,000
NAB4890	UPVC pipes For 6" dia Pipe	21d	0%	21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$35,750
NAB4892	UPVC pipes For 8" dia Pipe	21d	0%	21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$52,619
NAB4896	Sewage Manholes 1000 mm dia.	21d	0%	21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$56,700
NAB4898	Edge beam	21d	0%	21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$19,000
NAB4899	Adjustment manhole heavy duty (25 Ton)	21d	0%	21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$18,000
NAB4894	3" Steel Water pipeline	21d	0%	21d	01-Jul-14	09-Aug-14	01-Jul-14	09-Aug-14	116d	$0	$29,280
Asphalt and Miscellaneous Works		182d		182d	01-Jul-14	29-Dec-14	01-Jul-14	29-Dec-14	0d	$0	$2,935,457
NAB1760	stone wall	23d	0%	23d	01-Jul-14	11-Aug-14	01-Jul-14	11-Aug-14	114d	$0	$21,350
NAB5000-new	Connecting with Existing lines at two points	10d	0%	10d	01-Jul-14	19-Jul-14	01-Jul-14	19-Jul-14	106d	$0	$12,500
NAB5000-new10	Installation 2 inch	5d	0%	5d	09-Oct-14	13-Oct-14	09-Oct-14	13-Oct-14	77d	$0	$30,120
NAB5000-new20	Sewer manholes	5d	0%	5d	09-Oct-14	13-Oct-14	09-Oct-14	13-Oct-14	77d	$0	$71,877
NAB4900	7 cm & 5 cm Asphalt Wearing Course Including Tack Coat	21d	0%	21d	03-Dec-14	29-Dec-14	03-Dec-14	29-Dec-14	0d	$0	$1,990,700
NAB4910	Install Street Lighting Poles	18d	0%	18d	03-Dec-14	24-Dec-14	03-Dec-14	24-Dec-14	3d	$0	$456,750
NAB4920	Guardrail and hand rail	15d	0%	15d	04-Dec-14	22-Dec-14	04-Dec-14	22-Dec-14	0d	$0	$67,500
NAB4930	Agricultural Soil and Landscaping Work	7d	0%	7d	04-Dec-14	13-Dec-14	04-Dec-14	13-Dec-14	0d	$0	$134,750
NAB4940	Traffic signs	14d	0%	14d	06-Dec-14	22-Dec-14	06-Dec-14	22-Dec-14	5d	$0	$52,760
NAB4950	Cat eyes and road marking	18d	0%	18d	07-Dec-14	29-Dec-14	07-Dec-14	29-Dec-14	0d	$0	$81,150
NAB4955	Grouted rip rap	15d	0%	15d	07-Dec-14	24-Dec-14	07-Dec-14	24-Dec-14	3d	$0	$16,000

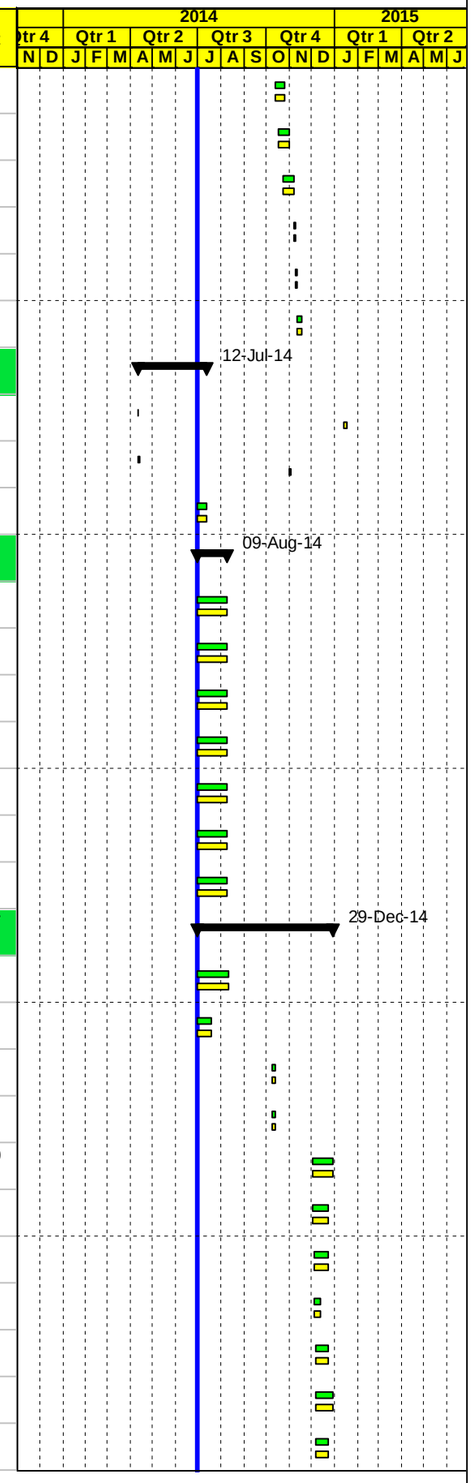

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
PROJECT 01 Post Construction Phase		6d		6d	29-Dec-14	06-Jan-15	29-Dec-14	06-Jan-15	0d	$0	$125,430
NAB4960	Walk Through & Punch List	6d	0%	6d	29-Dec-14	06-Jan-15	29-Dec-14	06-Jan-15	0d	$0	$0
NAB4970	Start Demoblization and Start Submitting Close Out document	1d	0%	1d	05-Jan-15	06-Jan-15	05-Jan-15	06-Jan-15	0d	$0	$125,430
NAB4980	Start preparation as built drawings	0d	0%	0d		06-Jan-15		06-Jan-15	0d	$0	$0
PROJECT 02 Deir Sharaf Tulkarem Road		261d		51d	03-Dec-13	20-Aug-14	03-Dec-13 A	20-Aug-14	139d	$1,183,056	$2,263,977
PROJECT 02 Pre Construction Phase		40d		0d	03-Dec-13	11-Jan-14	03-Dec-13 A	05-Feb-14 A		$115,252	$115,252
PROJECT 02 Conformed Drawings and Coordination		40d		0d	03-Dec-13	11-Jan-14	03-Dec-13 A	05-Feb-14 A		$0	$0
DSR1010	Final for Construction Drawing (Conformed)	0d	100%	0d	03-Dec-13		03-Dec-13 A			$0	$0
DSR1000	Coordination with Israeli authorities for approval and permit area C Project 02	40d	100%	0d	03-Dec-13	11-Jan-14	03-Dec-13 A	05-Feb-14 A		$0	$0
PROJECT 02 Mobilization		19d		0d	07-Dec-13	04-Jan-14	04-Dec-13 A	20-Jan-14 A		$115,252	$115,252
DSR1060	Site Hand Over	1d	100%	0d	08-Dec-13	08-Dec-13	04-Dec-13 A	04-Dec-13 A		$0	$0
DSR1070	Checking With CMC Existing-Bench Marks, Survey Control Points	2d	100%	0d	09-Dec-13	10-Dec-13	04-Dec-13 A	04-Dec-13 A		$0	$0
DSR1050	Mobilization Total Cost (4.0%)	19d	100%	0d	07-Dec-13	04-Jan-14	04-Dec-13 A	20-Jan-14 A		$115,252	$115,252
DSR1080	Start Preparation Construction Submittals (Survey plan , Shop Drawings & Materials)	12d	100%	0d	16-Dec-13	04-Jan-14	16-Dec-13 A	04-Jan-14 A		$0	$0
DSR1090	Install Temporary Project Sign	2d	100%	0d	07-Dec-13	08-Dec-13	20-Jan-14 A	20-Jan-14 A		$0	$0
PROJECT 02 Construction Phase		227d		45d	30-Dec-13	14-Aug-14	25-Dec-13 A	14-Aug-14	145d	$1,067,804	$2,119,912
PROJECT 02 Construction Submittals		158d		6d	30-Dec-13	23-Jul-14	25-Dec-13 A	12-Jul-14	137d	$0	$0
PROJECT 02 Shop Drawing Submittals		158d		6d	30-Dec-13	23-Jul-14	15-Jan-14 A	12-Jul-14	137d	$0	$0
Plan Profile and Cross Sections		158d		6d	30-Dec-13	23-Jul-14	15-Jan-14 A	12-Jul-14	137d	$0	$0
DSR1140	From St. 0+100 To St. 0+700	12d	100%	0d	30-Dec-13	19-Jan-14	15-Jan-14 A	09-Feb-14 A		$0	$0
DSR1150	From St. 0+700 To St. 1+200	12d	100%	0d	01-Mar-14	15-Mar-14	02-Mar-14 A	24-Apr-14 A		$0	$0
DSR1160	From St. 1+200 To St. 1+800	12d	100%	0d	10-Apr-14	24-Apr-14	08-Apr-14 A	09-Apr-14 A		$0	$0
DSR1180	From St. 1+800 To St. 2+100	12d	100%	0d	27-Apr-14	11-May-14	27-Apr-14 A	29-Apr-14 A		$0	$0
DSR1190	from Sta. 2+100 to Sta. 2+540	12d	100%	0d	06-May-14	19-May-14	08-May-14 A	15-May-14 A		$0	$0
DSR1200-new	Simple Access at Sta.0+170 LHS ,0+360 RHS , 0+430 RHS,0+930 RHS,0+990 RHS,1+100 LHS,1+439,1+460 LHS,1+950	12d	50%	6d	01-Jul-14	23-Jul-14	28-Jun-14 A	12-Jul-14	137d	$0	$0
Water Line		12d		0d	25-Jun-14	14-Jul-14	12-Jun-14 A	22-Jun-14 A		$0	$0
DSR1175-new	Water Pipeline from Sta.0+410 to Sta.1+100 (3")	12d	100%	0d	25-Jun-14	14-Jul-14	12-Jun-14 A	22-Jun-14 A		$0	$0
Culverts		26d		0d	24-Apr-14	25-May-14	30-Apr-14 A	08-Jun-14 A		$0	$0
DSR1210	Pipe Culvert 1000mm @ St.0+860 length 15 m	12d	100%	0d	24-Apr-14	08-May-14	30-Apr-14 A	07-May-14 A		$0	$0
DSR1220	Pipe Culvert 1000mm @ St. 1+480 length 16 m	12d	100%	0d	08-May-14	21-May-14	19-May-14 A	21-May-14 A		$0	$0

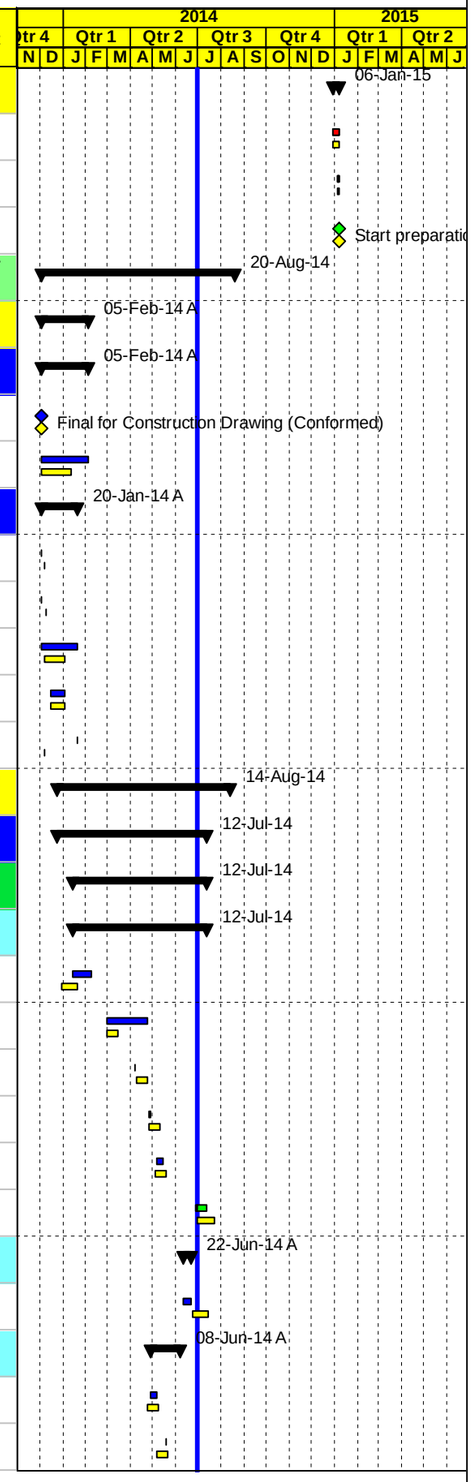

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
DSR1230	Double Pipe Culvert at Sta.1+995	12d	100%	0d	12-May-14	25-May-14	22-May-14 A	08-Jun-14 A		$0	$0
Concrete Walls		12d		0d	03-May-14	15-May-14	26-May-14 A	29-Jun-14 A		$0	$0
DSR1245-new	Retaining Wall from Sta.1+300 to Sta.1+310 LHS L= 10 m and from Sta.1+700 to Sta.1+760 LHS L= 60 m	12d	100%	0d	03-May-14	15-May-14	26-May-14 A	28-May-14 A		$0	$0
DSR1250-new	Retaining Wall from Sta.1+475 to Sta.1+500 LHS	12d	100%	0d	03-May-14	15-May-14	27-May-14 A	29-Jun-14 A		$0	$0
Otheres		38d		6d	01-Jun-14	23-Jul-14	12-Jun-14 A	12-Jul-14	25d	$0	$0
DSR1255	Ditch and Concrete Step Barrier from Sta.0+000 to Sta.2+180	12d	100%	0d	01-Jun-14	14-Jun-14	12-Jun-14 A	17-Jun-14 A		$0	$0
DSR1365-new	Directional Signs	12d	50%	6d	01-Jul-14	23-Jul-14	01-Jul-14 A	12-Jul-14	25d	$0	$0
PROJECT 02 Material Submittals		73d		0d	02-Mar-14	28-May-14	25-Dec-13 A	25-Feb-14 A		$0	$0
DSR1560	Cat eyes	12d	100%	0d	12-Apr-14	26-Apr-14	25-Dec-13 A	05-Jan-14 A		$0	$0
DSR1565	Thermoplastic paint	12d	100%	0d	12-Apr-14	26-Apr-14	25-Dec-13 A	05-Jan-14 A		$0	$0
DSR1575	Curbstone paint material	12d	100%	0d	15-May-14	28-May-14	25-Dec-13 A	05-Jan-14 A		$0	$0
DSR1550	Traffic sign	12d	100%	0d	12-Apr-14	26-Apr-14	25-Dec-13 A	05-Jan-14 A		$0	$0
DSR1460	Prime Coat	12d	100%	0d	31-Mar-14	13-Apr-14	25-Dec-13 A	05-Jan-14 A		$0	$0
DSR1470	Tack Coat	12d	100%	0d	31-Mar-14	13-Apr-14	25-Dec-13 A	05-Jan-14 A		$0	$0
DSR1540	Guard Rail	12d	100%	0d	12-Apr-14	26-Apr-14	29-Dec-13 A	25-Feb-14 A		$0	$0
DSR1450	Curbstone	12d	100%	0d	31-Mar-14	13-Apr-14	30-Dec-13 A	31-Dec-13 A		$0	$0
DSR1400	Pipe Culverts	12d	100%	0d	02-Mar-14	16-Mar-14	30-Dec-13 A	05-Feb-14 A		$0	$0
DSR1382-New	Single size aggregate material source	12d	100%	0d	17-Mar-14	30-Mar-14	22-Jan-14 A	26-Jan-14 A		$0	$0
DSR1384-New	Bedding (somsom)	12d	100%	0d	17-Mar-14	30-Mar-14	22-Jan-14 A	26-Jan-14 A		$0	$0
DSR1380	Base Course Source and Topping	12d	100%	0d	02-Mar-14	16-Mar-14	22-Jan-14 A	26-Jan-14 A		$0	$0
DSR1573	Concrete joint sealant material	12d	100%	0d	17-Mar-14	30-Mar-14	03-Feb-14 A	05-Feb-14 A		$0	$0
DSR1390	Concrete Mix Design including cement type	12d	100%	0d	02-Mar-14	16-Mar-14	03-Feb-14 A	05-Feb-14 A		$0	$0
DSR1420	Steel Reinforcement	12d	100%	0d	08-Mar-14	20-Mar-14	19-Feb-14 A	23-Feb-14 A		$0	$0
DSR1480	Bituminous Wearing Course-Mix Design	12d	100%	0d	31-Mar-14	13-Apr-14	19-Feb-14 A	23-Feb-14 A		$0	$0
PROJECT 02 Construction		167d		45d	01-Mar-14	14-Aug-14	05-Feb-14 A	14-Aug-14	145d	$1,067,804	$2,119,912
PROJECT 02 Implement traffic control		0d		0d	01-Mar-14	01-Mar-14	05-Feb-14 A	22-Feb-14 A		$0	$0
DSR1620	Implement traffic control & safety Plan phase1,2 & 3	0d	100%	0d	01-Mar-14	01-Mar-14	05-Feb-14 A	22-Feb-14 A		$0	$0
Phase #1 Totally closed from St. 0+100 To St. 2+180 Area C		154d		24d	12-Mar-14	13-Aug-14	15-Feb-14 A	24-Jul-14	166d	$909,716	$1,065,858
From St. 0+100 To St. 0+700 Area C		106d		0d	12-Mar-14	27-Jul-14	15-Feb-14 A	05-Jun-14 A		$136,096	$136,096
DSR1660	Relocation Exist. Utilities , Maintain traffic control & safety Plan (totally closed)	53d	100%	0d	12-Mar-14	15-May-14	15-Feb-14 A	21-May-14 A		$0	$0

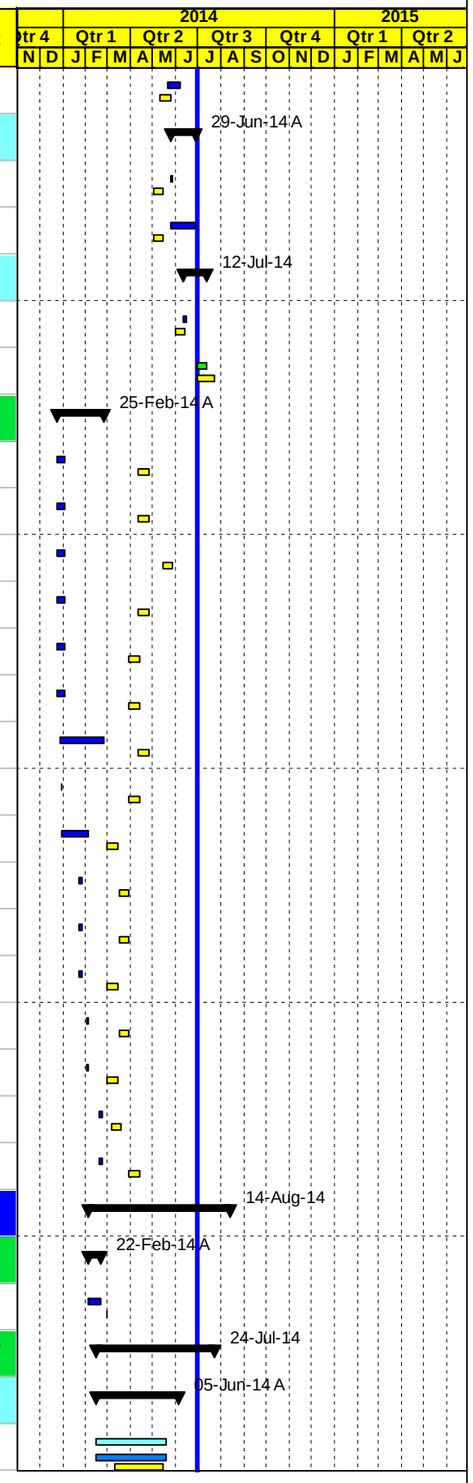

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
DSR1670	Divert Wadi and Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	22d	100%	0d	13-Mar-14	08-Apr-14	23-Feb-14 A	10-Apr-14 A		$39,200	$39,200
DSR1690	20 cm Thick Topping Layer/ Pulverization	14d	100%	0d	20-Mar-14	05-Apr-14	11-Mar-14 A	14-Apr-14 A		$23,400	$23,400
DSR1670-new	Filling horizontal Layers	9d	100%	0d	19-Mar-14	29-Mar-14	15-Mar-14 A	24-Mar-14 A		$6,204	$6,204
DSR1700	20 cm Thick Base Course- First Layer	14d	100%	0d	10-Apr-14	27-Apr-14	06-Apr-14 A	25-Apr-14 A		$30,500	$30,500
DSR1750-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 0+440	14d	100%	0d	01-Jul-14	27-Jul-14	20-Apr-14 A	20-Apr-14 A		$1,162	$1,162
DSR1755-new	8" UPVC for Sewer Pipe Line at station 0+440	14d	100%	0d	01-Jul-14	27-Jul-14	22-Apr-14 A	23-Apr-14 A		$1,755	$1,755
DSR1760-new	1000 mm Dia Sewer Manhole at station 0+440	14d	100%	0d	22-Apr-14	08-May-14	22-Apr-14 A	23-Apr-14 A		$2,100	$2,100
DSR1710	20 cm Thick Base Course- Second Layer	14d	100%	0d	28-May-14	12-Jun-14	17-May-14 A	05-Jun-14 A		$31,775	$31,775
From St.0+700 To St. 1+280 Area C		132d		7d	15-Mar-14	24-Jul-14	13-Mar-14 A	07-Jul-14	183d	$168,023	$171,291
DSR1720	Relocation Exist. Utilities , Maintain traffic control & safety Plan (totally closed)	60d	100%	0d	15-Mar-14	25-May-14	13-Mar-14 A	31-May-14 A		$0	$0
DSR1730	Divert Wadi and Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	21d	100%	0d	20-Mar-14	13-Apr-14	15-Mar-14 A	22-Apr-14 A		$31,500	$31,500
DSR1731-new	Filling horizontal Layers	9d	100%	0d	19-Mar-14	27-Mar-14	08-Apr-14 A	12-Apr-14 A		$4,248	$4,248
DSR1755	20 cm Thick Topping Layer/ Pulverization	14d	100%	0d	26-Apr-14	13-May-14	10-Apr-14 A	23-Apr-14 A		$22,503	$22,503
DSR1780	20 cm Thick Base Course- First Layer	14d	100%	0d	12-May-14	27-May-14	16-Apr-14 A	07-May-14 A		$42,500	$42,500
DSR1785-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 0+720	13d	100%	0d	01-Jul-14	13-Jul-14	20-Apr-14 A	20-Apr-14 A		$996	$996
DSR1790-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 1+000	12d	100%	0d	01-Jul-14	12-Jul-14	20-Apr-14 A	20-Apr-14 A		$1,162	$1,162
DSR1795-new	8" UPVC for Sewer Pipe Line at station 1+000	13d	100%	0d	01-Jul-14	24-Jul-14	22-Apr-14 A	23-Apr-14 A		$1,462	$1,462
DSR1796-new	8" UPVC for Sewer Pipe Line at station 1+100	13d	100%	0d	01-Jul-14	13-Jul-14	22-Apr-14 A	23-Apr-14 A		$731	$731
DSR1797-new	8" UPVC for Sewer Pipe Line at station 1+300	13d	100%	0d	01-Jul-14	24-Jul-14	22-Apr-14 A	23-Apr-14 A		$1,645	$1,645
DSR1798-new	1000 mm Dia Sewer Manhole at station 1+000 ,1+100,1+300	12d	100%	0d	01-Jul-14	23-Jul-14	22-Apr-14 A	23-Apr-14 A		$3,150	$3,150
DSR1750	New Pipe Culvert 800mm @ St. 0+780	12d	70%	4d	28-May-14	10-Jun-14	15-May-14 A	07-Jul-14	140d	$7,626	$10,894
DSR1790	20 cm Thick Base Course- Second Layer	14d	100%	0d	05-Jun-14	21-Jun-14	19-May-14 A	16-Jun-14 A		$50,500	$50,500
Asphalt Works From St. 0+100 To St. 1+280		6d		0d	03-Jul-14	14-Jul-14	06-Jun-14 A	19-Jun-14 A		$203,746	$203,746
DSR1800	7 cm Asphalt Binder Course Including Prime Coat	6d	100%	0d	03-Jul-14	14-Jul-14	06-Jun-14 A	19-Jun-14 A		$203,746	$203,746
From St. 1+280 To St. 1+730 Area C		146d		5d	19-Mar-14	11-Aug-14	13-Apr-14 A	05-Jul-14	185d	$205,934	$279,139
DSR1810	Relocation Exist. Utilities ,Maintain traffic control & safety Plan (totally closed)	60d	100%	0d	17-Apr-14	29-Jun-14	13-Apr-14 A	21-Jun-14 A		$0	$0
DSR1850	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	17d	100%	0d	26-Apr-14	15-May-14	15-Apr-14 A	05-May-14 A		$49,210	$49,210
DSR1900	20 cm Thick Topping Layer/ Pulverization	13d	100%	0d	12-May-14	26-May-14	29-Apr-14 A	18-May-14 A		$24,960	$24,960
DSR1950-new	Filling horizontal Layers	9d	100%	0d	19-Mar-14	27-Mar-14	01-May-14 A	09-May-14 A		$6,036	$6,036
DSR1910	20 cm Thick Base Course- First Layer	13d	100%	0d	01-Jun-14	15-Jun-14	24-May-14 A	19-Jun-14 A		$45,000	$45,000

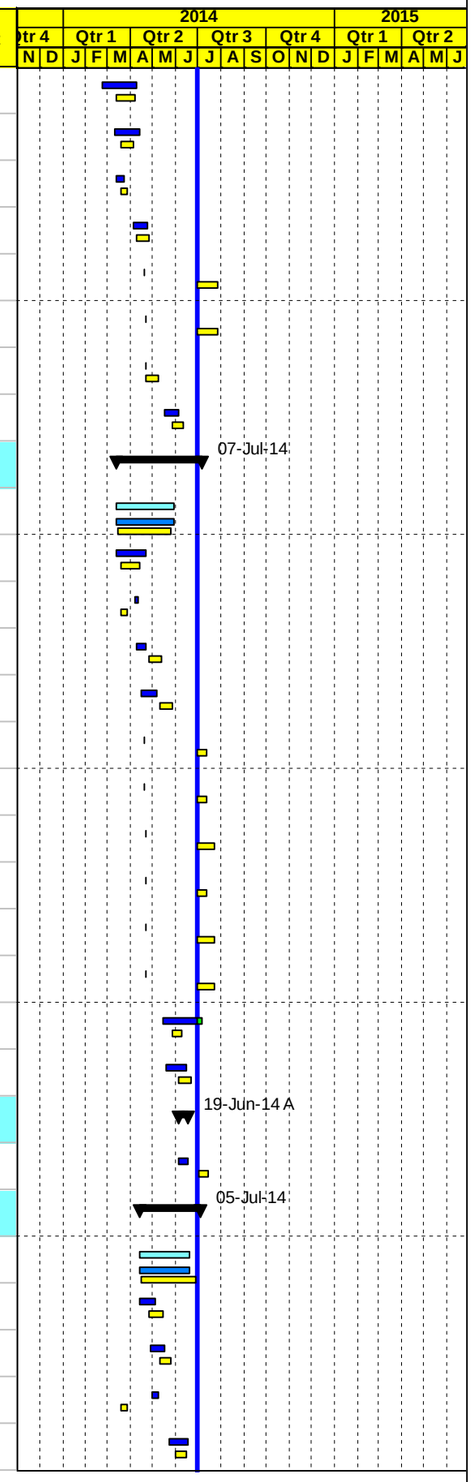

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
DSR1880	Pipe Culvert 1000mm @ St. 1+480 length 16 m	12d	100%	0d	28-May-14	10-Jun-14	27-May-14 A	27-May-14 A		$9,277	$9,277
DSR1870	Retaining wall from St. 1+470to 1+505 LHS	22d	100%	0d	03-Jul-14	11-Aug-14	04-Jun-14 A	21-Jun-14 A		$14,334	$14,334
DSR1920	20 cm Thick Base Course- Second Layer	13d	100%	0d	25-Jun-14	16-Jul-14	11-Jun-14 A	21-Jun-14 A		$30,500	$30,500
DSR1930	7 cm Asphalt Binder Course Including Prime Coat	2d	26.98%	1d	16-Jul-14	20-Jul-14	18-Jun-14 A	03-Jul-14	142d	$26,618	$98,661
DSR1955-new	6" UPVC for ROAD CROSSING (SLEEVES)	5d	0%	5d	01-Jul-14	05-Jul-14	01-Jul-14	05-Jul-14	29d	$0	$1,162
From St. 1+730 To St. 2+180 Area C		148d		24d	19-Mar-14	13-Aug-14	01-May-14 A	24-Jul-14	20d	$195,918	$275,587
DSR1940	Relocation Exist. Utilities , Maintain traffic control & safety Plan (totally closed)	50d	100%	0d	02-Jun-14	13-Aug-14	01-May-14 A	23-Jun-14 A		$0	$0
DSR1980	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	19d	100%	0d	28-May-14	18-Jun-14	03-May-14 A	22-May-14 A		$31,500	$31,500
DSR2030-new	Filling horizontal Layers	9d	100%	0d	19-Mar-14	27-Mar-14	10-May-14 A	25-May-14 A		$6,012	$6,012
DSR2020	20 cm Thick Topping Layer/ Pulverization	13d	100%	0d	19-Jun-14	07-Jul-14	15-May-14 A	03-Jun-14 A		$14,300	$14,300
DSR2030	20 cm Thick Base Course- First Layer	13d	100%	0d	25-Jun-14	16-Jul-14	01-Jun-14 A	23-Jun-14 A		$33,415	$33,415
DSR1990	Pipe Culvert 600mm @ St. 1+995	9d	70%	3d	03-Jul-14	20-Jul-14	04-Jun-14 A	06-Jul-14	22d	$18,005	$25,722
DSR2265-new	Retaining wall from St. 1+665to 1+760 LHS	12d	88.99%	1d	01-Jul-14	23-Jul-14	05-Jun-14 A	03-Jul-14	17d	$29,759	$33,440
DSR2040	20 cm Thick Base Course- Second Layer	13d	100%	0d	09-Jul-14	04-Aug-14	07-Jun-14 A	23-Jun-14 A		$31,375	$31,375
DSR2050	7 cm Asphalt Binder Course Including Prime Coat	2d	31.98%	1d	05-Aug-14	06-Aug-14	23-Jun-14 A	03-Jul-14	15d	$31,551	$98,661
DSR2266-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 1+760	13d	0%	13d	01-Jul-14	24-Jul-14	01-Jul-14	24-Jul-14	5d	$0	$1,162
Phase #2 From St. 0+000 to 0+100		36d		18d	19-Jun-14	14-Aug-14	22-May-14 A	05-Aug-14	0d	$0	$46,215
DSR2060	Relocation Exist. Utilities , Maintain traffic control & safety Plan (RHS&LHS)	36d	55.56%	16d	19-Jun-14	14-Aug-14	22-May-14 A	03-Aug-14	0d	$0	$0
DSR2070	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	4d	0%	4d	01-Jul-14	08-Jul-14	01-Jul-14	08-Jul-14	0d	$0	$16,244
DSR2080	20 cm Thick Topping Layer/ Pulverization	4d	0%	4d	08-Jul-14	15-Jul-14	08-Jul-14	15-Jul-14	0d	$0	$1,417
DSR2090	20 cm Thick Base Course- First Layer	4d	0%	4d	15-Jul-14	23-Jul-14	15-Jul-14	23-Jul-14	0d	$0	$2,435
DSR2100	20 cm Thick Base Course- Second Layer	4d	0%	4d	23-Jul-14	03-Aug-14	23-Jul-14	03-Aug-14	0d	$0	$2,000
DSR2110	7 cm Asphalt Binder Course Including Prime Coat	2d	0%	2d	03-Aug-14	05-Aug-14	03-Aug-14	05-Aug-14	0d	$0	$24,119
Miscellaneous Works		45d		45d	01-Jul-14	14-Aug-14	27-May-14 A	14-Aug-14	0d	$158,088	$1,007,840
DSR1885-new	Concrete step barrier	13d	90.99%	1d	01-Jul-14	24-Jul-14	27-May-14 A	02-Jul-14	17d	$119,758	$131,611
DSR1765-new	Concrete Ditch from St. 0+460 +860	14d	100%	0d	01-Jul-14	27-Jul-14	27-Jun-14 A	27-Jun-14 A		$38,330	$38,330
DSR2150	Curbstone if any	6d	0%	6d	01-Jul-14	12-Jul-14	01-Jul-14	12-Jul-14	17d	$0	$10,500
DSR1925	3" Water Pipeline	10d	0%	10d	08-Jul-14	18-Jul-14	08-Jul-14	18-Jul-14	18d	$0	$57,084
DSR2190	Geo-cell	8d	0%	8d	03-Aug-14	12-Aug-14	03-Aug-14	12-Aug-14	1d	$0	$11,500
DSR2160	7 cm Asphalt Wearing Course Including tack Coat	8d	0%	8d	05-Aug-14	14-Aug-14	05-Aug-14	14-Aug-14	0d	$0	$448,107

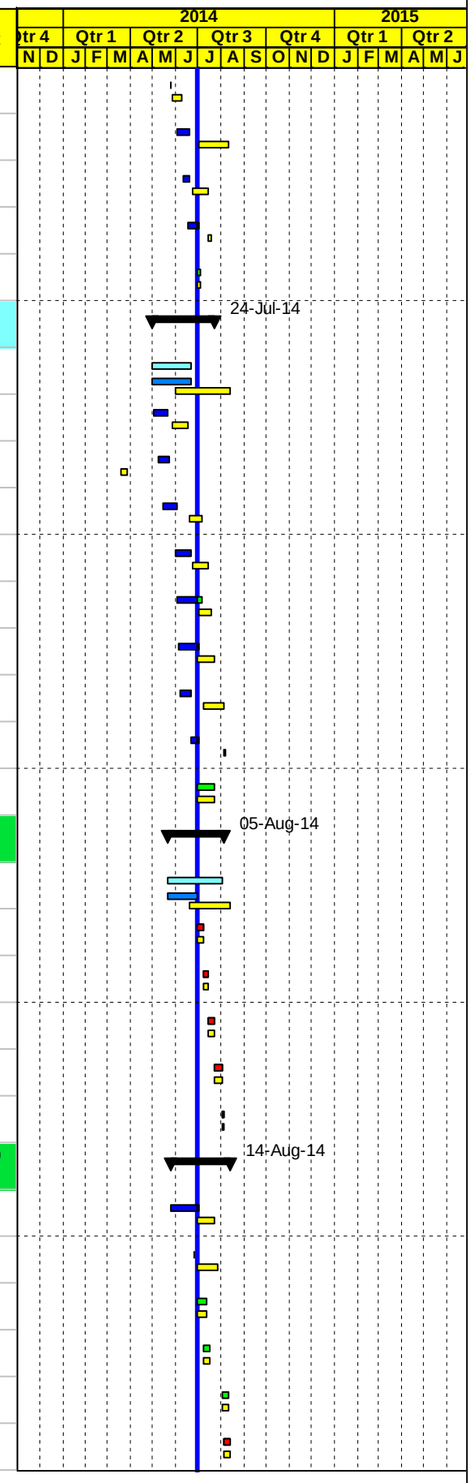

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

June 30, 2014

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	BL2 Start	BL2 Finish	Start	Finish	Total Float	Actual Total Cost	Budgeted Total Cost
DSR2180	Grouted rip rap protection	7d	0%	7d	05-Aug-14	13-Aug-14	05-Aug-14	13-Aug-14	0d	$0	$16,000
DSR1915	Miscellaneous activities - If any as location is not determined yet	5d	0%	5d	05-Aug-14	10-Aug-14	05-Aug-14	10-Aug-14	3d	$0	$6,965
DSR2170	Concrete Ditch ST. 0+000 to 0+460 +860-2+180	8d	0%	8d	05-Aug-14	13-Aug-14	05-Aug-14	13-Aug-14	0d	$0	$189,913
DSR2175	Road furnishing/Guard Rail	5d	0%	5d	07-Aug-14	13-Aug-14	07-Aug-14	13-Aug-14	0d	$0	$97,830
PROJECT 02 Post Construction Phase		7d		7d	13-Aug-14	20-Aug-14	13-Aug-14	20-Aug-14	0d	$0	$28,813
DSR2220	Walk Through & Punch List	7d	0%	7d	13-Aug-14	20-Aug-14	13-Aug-14	20-Aug-14	0d	$0	$0
DSR2230	Start Demoblization	1d	0%	1d	19-Aug-14	20-Aug-14	19-Aug-14	20-Aug-14	0d	$0	$28,813
DSR2240	Start preparation as built drawings	0d	0%	0d		20-Aug-14		20-Aug-14	0d	$0	$0
Post Construction Phase		0d		0d	06-Jan-15	06-Jan-15	06-Jan-15	06-Jan-15	0d	$0	$0
Post Submittals		0d		0d	06-Jan-15	06-Jan-15	06-Jan-15	06-Jan-15	0d	$0	$0
MRNII1620	Start preparation Warranties (to USAID)	0d	0%	0d	06-Jan-15		06-Jan-15		0d	$0	$0
MRNII1630	Start preparation Final Acceptance Certificate	0d	0%	0d	06-Jan-15		06-Jan-15		0d	$0	$0
MRNII1640	Start preparation Release of liens and waiver of debts and claims againts the government	0d	0%	0d	06-Jan-15		06-Jan-15		0d	$0	$0
MRNII1650	Start preparation Final payment	0d	0%	0d	06-Jan-15		06-Jan-15		0d	$0	$0
MRNII1660	Start preparation Final Report	0d	0%	0d	06-Jan-15		06-Jan-15		0d	$0	$0
MRNII1680	Start preparation Clearance certificate from local entities/ Authorities invloved	0d	0%	0d	06-Jan-15		06-Jan-15		0d	$0	$0

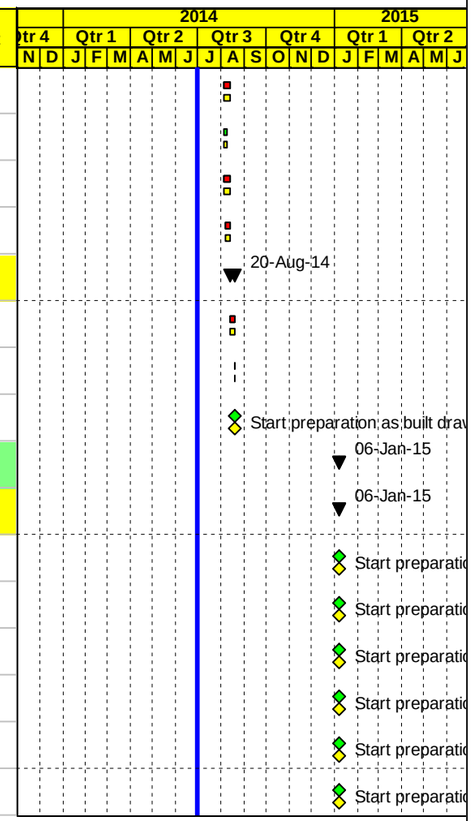

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

B | One Month Look ahead

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
One Month Lookahead

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Multiple Roads Project North (II)		383d		03-Dec-13 A	06-Jan-15	0d
Milestones		364d		03-Dec-13 A	06-Jan-15	0d
General Milestone		0d				0d
Intermediate Milestones		364d		03-Dec-13 A	06-Jan-15	0d
Completion Milestones		0d				0d
Preconstuction Milestones		0d				0d
PROJECT 01 Nablus - Beit Iba - Deir Sharaf Road		364d		03-Dec-13 A	06-Jan-15	0d
Mobilization		0d				0d
Shop Drawing		0d				0d
Material		0d				0d
Construction		0d				0d
Project Duration		364d		03-Dec-13 A	06-Jan-15	0d
MRNII0140	Project Duration (Calendar Days)	364d	47.8%	03-Dec-13 A	06-Jan-15	0d
MRNII0150	Project Duration (Working Days)	279d	48.66%	03-Dec-13 A	06-Jan-15	0d
MRNII0160	Construction Duration (Working Days)	240d	42.69%	23-Jan-14 A	29-Dec-14	0d
PROJECT 02 Deir Sharaf Tulkarem Road		287d		03-Dec-13 A	20-Aug-14	0d
Mobilization		0d				0d
Shop Drawing Milestones		0d		12-Jul-14	12-Jul-14	25d
MRNII0200	Finish Shop Drawing Submittal	0d	0%		12-Jul-14	25d
Material		0d				0d
Construction		0d				0d
Project Duration		287d		03-Dec-13 A	20-Aug-14	0d
MRNII0250	Project Duration (Calendar Days)	240d	78.81%	03-Dec-13 A	20-Aug-14	0d
MRNII0260	Project Duration (Working Days)	179d	82.68%	03-Dec-13 A	20-Aug-14	0d
MRNII0270	Construction Duration (Working Days)	145d	82.77%	23-Feb-14 A	13-Aug-14	0d
Task order Duration		364d		03-Dec-13 A	06-Jan-15	0d
MRNII0280	Project Duration (Calendar Days)	364d	47.8%	03-Dec-13 A	06-Jan-15	0d
MRNII0290	Project Duration (Working Days)	279d	48.66%	03-Dec-13 A	06-Jan-15	0d
Pre Construction Phase		0d				0d
Pre Construction Submittals		0d				0d
Mobilization Offices		0d				0d
PROJECT 01 Nablus - Beit Iba - Deir Sharaf Road		383d		03-Dec-13 A	21-Dec-14	17d
PROJECT 01 Preconstruction Phase		40d		03-Dec-13 A	12-Jul-14	178d
PROJECT 01 Conformed Drawings and Coordination		40d		03-Dec-13 A	12-Jul-14	178d
NAB0110	Coordination with Israeli authorities for approval and permit area C Project 01	40d	70%	03-Dec-13 A	12-Jul-14	178d
PROJECT 01 Mobilization		0d				0d
PROJECT 01 Construction Phase		333d		23-Jan-14 A	21-Dec-14	17d
PROJECT 01 Construction Submittals		113d		24-Apr-14 A	14-Aug-14	145d
PROJECT 01 Shop Drawing Submittals		113d		24-Apr-14 A	14-Aug-14	145d
Plan Profile and Cross Sections Phase One		12d		01-Jul-14	23-Jul-14	19d
NAB0300	Main Road From St. A4+850 To St. A5+450	12d	0%	01-Jul-14	23-Jul-14	19d
Plan Profile and Cross Sections Phase Two		17d		18-Jun-14 A	23-Jul-14	61d
NAB0380	Seg B From St. B0+000 To St. B0+399	12d	50%	18-Jun-14 A	12-Jul-14	67d
NAB0340	Main Road From St. A0+000 To St. A1+000	12d	0%	01-Jul-14	23-Jul-14	9d
Waterline		0d				0d
Sewer line		24d		26-Jun-14 A	12-Aug-14	103d
NAB0440	Sewer line (LHS) from St. 4+100 to 4+600 (12")	12d	50%	26-Jun-14 A	12-Jul-14	121d
NAB0450	Sewer line (LHS) from St. 0+290 to 0+520 (10")	12d	0%	23-Jul-14	12-Aug-14	52d
Concrete walls Phase One		75d		24-Apr-14 A	05-Aug-14	61d
NAB0469-New	Retaining Wall from Sta.4+090 to Sta.4+100	12d	50%	24-Apr-14 A	12-Jul-14	61d
NAB0490	Conc.boundary walls from A4+578 to A4+600 (LHS) L= 22 m	12d	0%	12-Jul-14	05-Aug-14	61d

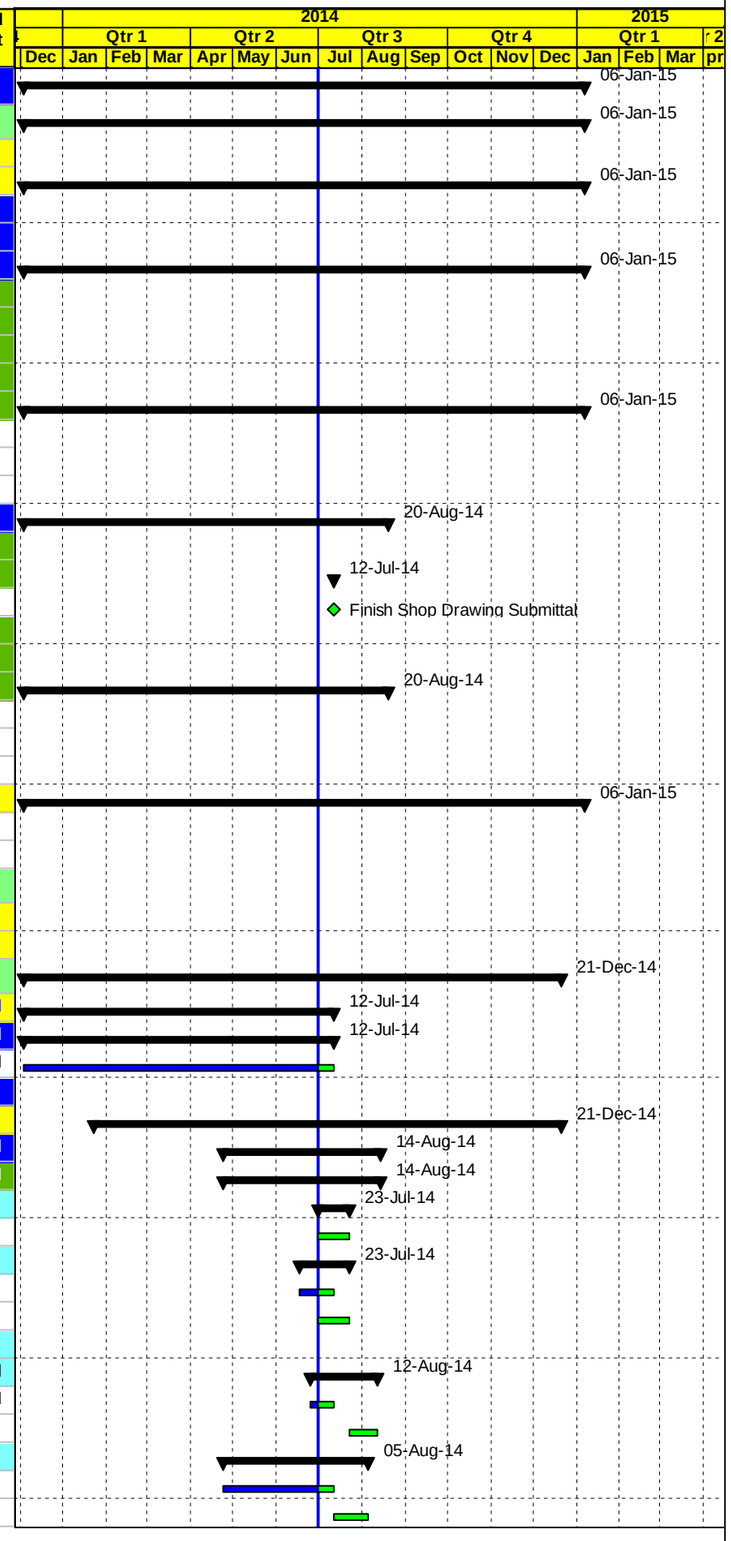

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program

One Month Lookahead

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Concrete walls Phase Two		19d		14-Jul-14	14-Aug-14	117d
NAB0550	Retaining walls with step barrier & channel from A`1+000 to A1+110 (RHS) L= 110 m	12d	0%	14-Jul-14	06-Aug-14	22d
NAB0520	Retaining walls with step barrier & channel from A0+500 to A0+620 (RHS) L= 120 m	12d	0%	23-Jul-14	12-Aug-14	65d
NAB0530	Retaining walls with step barrier & channel from A0+750 to A0+910 (RHS) L= 160 m	12d	0%	23-Jul-14	12-Aug-14	73d
NAB0540	Retaining walls with step barrier & channel from A0+916 to A1+000 (RHS) L= 84 m	12d	0%	23-Jul-14	12-Aug-14	119d
NAB0560	Conc. Retaining walls from B0+230 to B0+340 LHS L= 110 m	12d	0%	27-Jul-14	14-Aug-14	67d
60 cm Conc. Pipes for drainage LHS Phase One		21d		26-Jun-14 A	09-Aug-14	122d
NAB0602-	60 cm Conc. Pipes for drainage from Sta.4+100 to Sta.4+560	12d	50%	26-Jun-14 A	12-Jul-14	137d
NAB0650	60 cm Conc. Pipes for drainage from A4+600 to A4+800 L= 200 m	12d	0%	01-Jul-14	23-Jul-14	18d
NAB0660	60 cm Conc. Pipes for drainage from A4+840 to A5+000 L= 160 m	12d	0%	12-Jul-14	05-Aug-14	18d
NAB0670	60 cm Conc. Pipes for drainage from A5+000 to A5+120 L= 120 m	12d	0%	17-Jul-14	09-Aug-14	18d
60 cm Conc. Pipes for drainage RHS Phase Two		30d		15-Jun-14 A	13-Aug-14	118d
NAB0745-new	60 cm Conc. Pipes for drainage from Sta.0+030 to Sta.0+180	12d	50%	15-Jun-14 A	12-Jul-14	58d
NAB0720	60 cm Conc. Pipes for drainage from A1+300 to A1+500 L= 200 m	12d	50%	26-Jun-14 A	12-Jul-14	34d
NAB0710	60 cm Conc. Pipes for drainage from A1+100 to A1+260 L= 160 m	12d	50%	28-Jun-14 A	12-Jul-14	37d
NAB0730	60 cm Conc. Pipes for drainage from A1+500 to A1+620 L= 120 m	12d	0%	01-Jul-14	23-Jul-14	131d
NAB0700	60 cm Conc. Pipes for drainage from A0+580 to A0+740 L= 160 m	12d	0%	09-Jul-14	03-Aug-14	37d
NAB0690	60 cm Conc. Pipes for drainage from A0+360 to A0+460 L= 100 m	12d	0%	22-Jul-14	11-Aug-14	39d
NAB0680	60 cm Conc. Pipes for drainage from A0+140 to A0+300 L= 160 m	12d	0%	26-Jul-14	13-Aug-14	39d
New Conc.Pipe Culvert Dia. 80 cm and Box Culvert RHS Phase One		18d		14-Jul-14	13-Aug-14	29d
NAB0800	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+240 length L= 12 m	12d	0%	14-Jul-14	06-Aug-14	29d
NAB0810	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+600 length L= 9 m	12d	0%	26-Jul-14	13-Aug-14	29d
NAB0820	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+840 length L= 9 m	12d	0%	26-Jul-14	13-Aug-14	29d
New Conc.Pipe Culvert Dia. 80 cm and Box Culvert RHS Phase Two		19d		12-Jul-14	13-Aug-14	75d
NAB0940	New Conc.Pipe Culvert Dia.80 cm @ St. A1+300 length L= 84 m	12d	0%	12-Jul-14	05-Aug-14	50d
NAB0910	New Conc.Pipe Culvert Dia.80 cm @ St. A1+100 length L= 14 m	12d	0%	14-Jul-14	06-Aug-14	54d
NAB0930	New box culvert (2*2.5) @ St. A1+095 RHS length L= 15.5 m	12d	0%	14-Jul-14	06-Aug-14	51d
NAB0890	New box culvert (2*2.5) @ St. A0+595 RHS length L= 7 m	12d	0%	16-Jul-14	07-Aug-14	80d
NAB0900	New Conc.Pipe Culvert Dia.80 cm @ St. A0+700 length L= 14 m	12d	0%	20-Jul-14	10-Aug-14	76d
NAB0860	New Conc.Pipe Culvert Dia.80 cm @ St. A0+360 length L= 29 m	12d	0%	22-Jul-14	11-Aug-14	66d
NAB0840	New Conc.Pipe Culvert Dia. 60 cm @ St. A0+000 length L= 60 m	12d	0%	23-Jul-14	12-Aug-14	42d
NAB0850	New Conc.Pipe Culvert Dia.80 cm @ St. A0+140 length L= 67 m	12d	0%	26-Jul-14	13-Aug-14	39d
NAB0920	New box culvert (2*2.5) @ St. A0+915 RHS length L= 6 m	12d	0%	26-Jul-14	13-Aug-14	37d
Connection and Valves Chambers		0d				0d
Stone Walls		0d				0d
Otheres		0d				0d
PROJECT 01 Material Submittals		12d		28-May-14 A	12-Jul-14	133d
NAB1566-new	Portland Cement Sulfate Resisting for concrete benching for manholes	12d	50%	28-May-14 A	12-Jul-14	133d
PROJECT 01 Procurements		0d				0d
PROJECT 01 Construction		333d		23-Jan-14 A	21-Dec-14	17d
Phase One from A2+020 TO 5+450 closed /area B & A		333d		23-Jan-14 A	21-Dec-14	17d
Main Road From St. A2+020 To St. A2+500 LHS & RHS Area B		194d		23-Jan-14 A	04-Aug-14	155d
NAB1680	Maintain traffic control and safety plan ,Relocating utilities	148d	88.52%	23-Jan-14 A	04-Aug-14	126d
Excavation		21d		28-Jan-14 A	05-Jul-14	141d
NAB2620	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	28-Jan-14 A	05-Jul-14	141d
Storm System		0d				0d
Water lines		0d				0d
Sewer line		0d				0d
Concrete works		0d				0d
Tooping and Basecourse		70d		11-Mar-14 A	03-Jul-14	142d
NAB1750	20 cm Thick Topping Layer LHS	13d	90%	11-Mar-14 A	03-Jul-14	132d
NAB2650	20 cm Thick Topping Layer RHS	13d	90%	25-Mar-14 A	03-Jul-14	139d

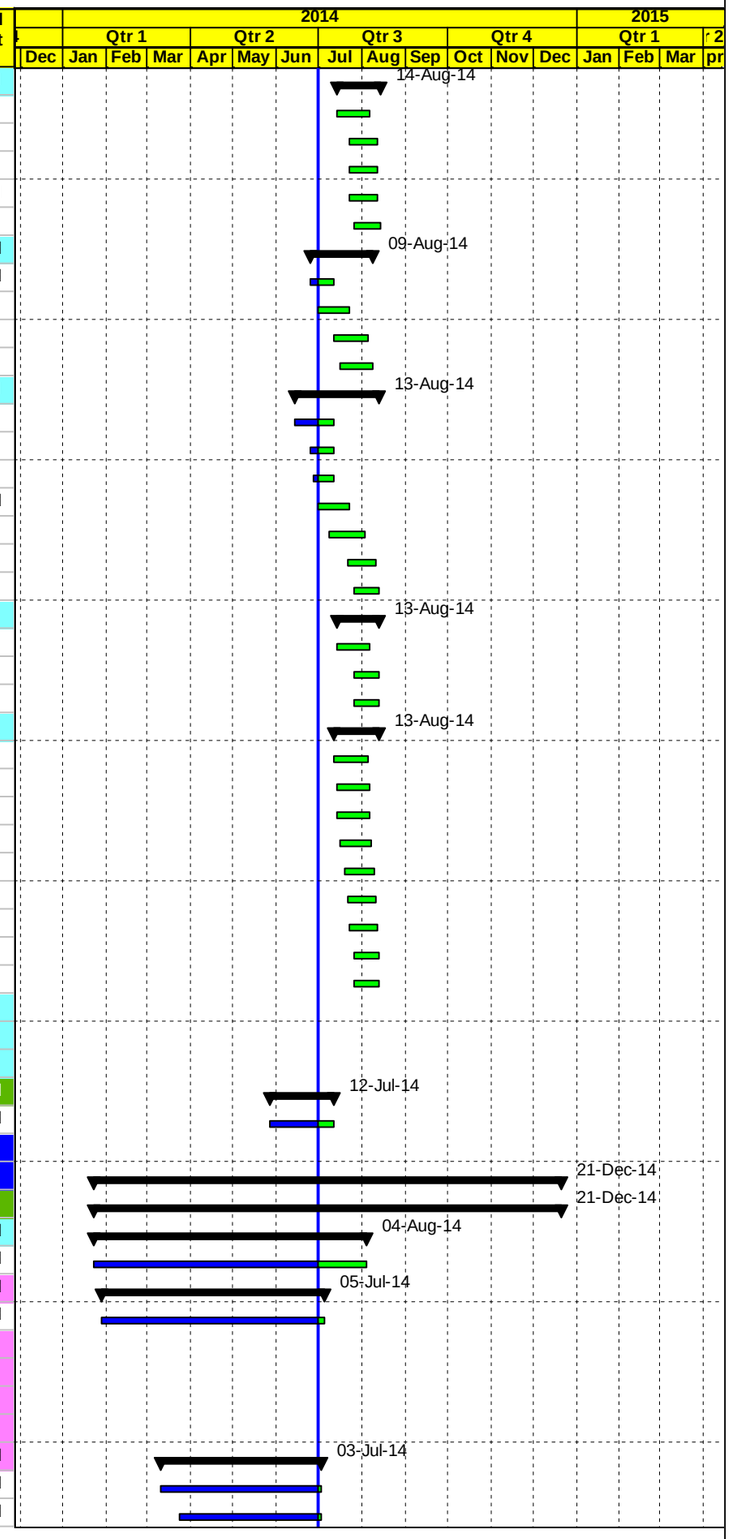

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
One Month Lookahead

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
NAB2670	20 cm Thick Base Course- First Layer RHS	13d	90%	13-Apr-14 A	03-Jul-14	142d
NAB1780	20 cm Thick Base Course- First Layer LHS	13d	90%	15-Apr-14 A	03-Jul-14	142d
NAB2680	20 cm Thick Base Course- Second Layer RHS	13d	90%	17-Apr-14 A	03-Jul-14	139d
NAB1790	20 cm Thick Base Course- Second Layer LHS	13d	90%	20-Apr-14 A	03-Jul-14	56d
Asphalt binder		3d		16-Jul-14	22-Jul-14	132d
NAB2820	7 cm Asphalt Binder Course Including Prime Coat from St. 2+020 to St. 2+140 RHS	3d	0%	16-Jul-14	22-Jul-14	132d
Street Lighting Poles and Curbstone		17d		25-Jun-14 A	04-Aug-14	61d
NAB2690	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	5d	50%	25-Jun-14 A	05-Jul-14	68d
NAB2660	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	01-Jul-14	19-Jul-14	61d
NAB1800	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	03-Jul-14	16-Jul-14	56d
NAB1810	Conc. Sidewalk and ramps including base course LHS	9d	0%	13-Jul-14	02-Aug-14	56d
NAB2700	Conc. Sidewalk and ramps including base course RHS	7d	0%	20-Jul-14	04-Aug-14	61d
Main Road From St. A2+500 To St. A3+000 LHS & RHS Area A		174d		13-Feb-14 A	25-Aug-14	134d
NAB1820	Maintain traffic control and safety plan ,Relocating utilities	133d	73.55%	13-Feb-14 A	25-Aug-14	108d
Excavation		84d		22-Feb-14 A	05-Jul-14	141d
NAB2720	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	22-Feb-14 A	05-Jul-14	141d
NAB1830	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	90%	25-Feb-14 A	05-Jul-14	141d
Storm System		0d				0d
Water lines		0d				0d
Sewer line		16d		13-Feb-14 A	02-Jul-14	142d
NAB1870	12" Sewer line from St. A2+500 to St. A2+580 L=80 LHS	12d	90%	13-Feb-14 A	02-Jul-14	142d
NAB1841-new	8" Sewer line (house connection from St. A2+500 to St. A3+000 LHS	11d	90%	14-Apr-14 A	02-Jul-14	46d
Concrete works		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A3+000 To St. A3+500 LHS & RHS Area A		158d		18-Mar-14 A	06-Sep-14	98d
NAB2000	Maintain traffic control and safety plan ,Relocating utilities	158d	71.46%	18-Mar-14 A	06-Sep-14	98d
Excavation		115d		18-Mar-14 A	05-Jul-14	141d
NAB2010	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	90%	18-Mar-14 A	05-Jul-14	141d
NAB2840	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	06-Apr-14 A	05-Jul-14	120d
Storm System		68d		18-Apr-14 A	11-Aug-14	120d
NAB2011-new	60 cm Conc. Pipes for drainage W. manholes from A2+980 to A3+120 L= 140 m LHS	18d	90%	18-Apr-14 A	03-Jul-14	70d
NAB2860	New Conc.Pipe Culvert Dia. 80 cm @ St. A3+280 length L= 132 m RHS	23d	0%	01-Jul-14	11-Aug-14	120d
Water lines		10d		27-Apr-14 A	02-Jul-14	71d
NAB2961-new	3" Steel Water pipeline from St. A 3+000 to A 3+500 (LHS) L=500m LHS	10d	90%	27-Apr-14 A	02-Jul-14	71d
Concrete works		12d		18-Apr-14 A	02-Jul-14	77d
NAB2842-new	Conc. Retaining walls from A3+006 to A3+018 L=12 m RHS	12d	90%	18-Apr-14 A	02-Jul-14	77d
Tooping and Basecourse		113d		01-May-14 A	12-Jul-14	138d
NAB2040	20 cm Thick Topping Layer LHS	13d	70%	01-May-14 A	08-Jul-14	139d
NAB2880	20 cm Thick Topping Layer RHS	13d	80%	03-May-14 A	06-Jul-14	141d
NAB2910	20 cm Thick Base Course- First Layer RHS	13d	80%	03-May-14 A	06-Jul-14	141d
NAB2070	20 cm Thick Base Course- First Layer LHS	13d	55%	05-May-14 A	12-Jul-14	138d
NAB2920	20 cm Thick Base Course- Second Layer RHS	13d	80%	10-May-14 A	06-Jul-14	75d
NAB2090	20 cm Thick Base Course- Second Layer LHS	13d	55%	17-May-14 A	12-Jul-14	66d
Asphalt binder		5d		06-Jul-14	15-Jul-14	72d
NAB2930	7 cm Asphalt Binder Course Including Prime Coat from St. 3+220 to St. 3+450 RHS.	2d	0%	06-Jul-14	09-Jul-14	75d
NAB2100	7 cm Asphalt Binder Course Including Prime Coat LHS remining	2d	0%	12-Jul-14	15-Jul-14	66d
Street Lighting Poles and Curbstone		45d		21-Apr-14 A	06-Aug-14	117d
NAB2060	Reconstruct stone wall from (A3+160 to A3+190) & (A3+240 to A3+282) L=72 m LHS	12d	95%	21-Apr-14 A	01-Jul-14	117d
NAB2900	Foundation & Civil Works of Street Lighting Poles RHS	10d	0%	01-Jul-14	19-Jul-14	87d
NAB2050	Reconstruct stone wall from A3+000 to A3+100 L=100 m LHS	15d	0%	07-Jul-14	06-Aug-14	117d

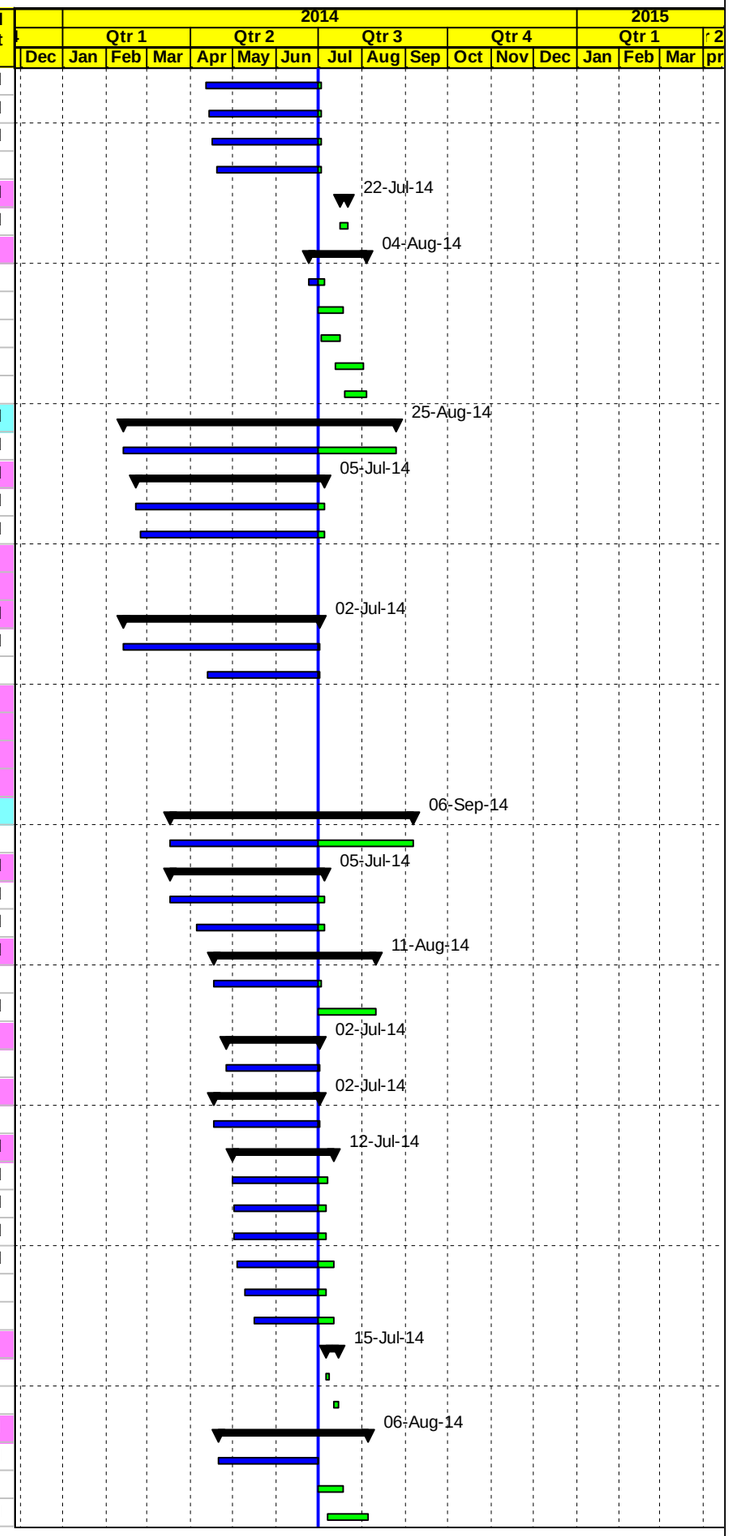

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
One Month Lookahead

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
NAB2940	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	7d	0%	09-Jul-14	22-Jul-14	75d
NAB2110	Precast Conc. Curbstone for LHS (Mediane and side curb) LHS	7d	0%	15-Jul-14	02-Aug-14	66d
Main Road St. A3+500 To St. A4+000 LHS & RHS Area A		197d		22-Apr-14 A	17-Sep-14	111d
NAB2130	Maintain traffic control and safety plan ,Relocating utilities	154d	64.22%	22-Apr-14 A	17-Sep-14	88d
Excavation		0d				0d
Storm System		86d		07-May-14 A	11-Aug-14	121d
NAB2150	60 cm Conc. Pipes for drainage W. manholes from A3+610 to A3+840 L= 230 m LHS	23d	85%	07-May-14 A	07-Jul-14	140d
NAB3020	New double box culvert 2 (2*2) @ St. A3+610 RHS length L= 28 m First part RHS	24d	5%	17-Jun-14 A	11-Aug-14	101d
NAB3040	New double box culvert 2 (2*2) @ St. A3+610 RHS length L= 28 m second part RHS	24d	5%	17-Jun-14 A	11-Aug-14	121d
Water lines		10d		22-Apr-14 A	02-Jul-14	142d
NAB3005-new	12" Steel pipeline beit iba from st 3+450 To st 3+950 RHS	10d	90%	22-Apr-14 A	02-Jul-14	142d
Sewer line		0d				0d
Concrete works		16d		01-Jul-14	03-Aug-14	66d
NAB2180	Conc. retaining wall from A3+950 TO A3+982 L= 32M LHS	16d	0%	01-Jul-14	03-Aug-14	66d
Tooping and Basecourse		26d		27-Jun-14 A	20-Jul-14	71d
NAB2220	20 cm Thick Base Course- Second Layer LHS	13d	20%	27-Jun-14 A	20-Jul-14	71d
NAB3090	20 cm Thick Base Course- Second Layer RHS	13d	20%	27-Jun-14 A	20-Jul-14	71d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A4+000 To St. A4+500 LHS & RHS Area A		205d		25-Apr-14 A	29-Sep-14	99d
NAB2260	Maintain traffic control and safety plan ,Relocating utilities	161d	59.57%	25-Apr-14 A	29-Sep-14	78d
Excavation		28d		14-May-14 A	14-Jul-14	136d
NAB3114	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	15d	55%	14-May-14 A	13-Jul-14	0d
NAB2270	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	15d	50%	10-Jun-14 A	14-Jul-14	136d
Storm System		59d		15-Jun-14 A	12-Aug-14	119d
NAB3150	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+240 length L= 12 m RHS	12d	15%	15-Jun-14 A	20-Jul-14	127d
NAB2290	60 cm Conc. Pipes for drainage W. manholes from A4+240 to A4+500 L= 260 m LHS	24d	0%	01-Jul-14	12-Aug-14	119d
NAB2305	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	15d	0%	17-Jul-14	12-Aug-14	119d
Water lines		0d				0d
Sewer line		20d		01-Jul-14	07-Aug-14	117d
NAB2280	12" Sewer line From St. A4+100 to St. A4+300 L=200 M LHS	10d	0%	01-Jul-14	19-Jul-14	117d
NAB2300	12" Sewer line From St. A4+300 to St. A4+500 L=200 M LHS	10d	0%	20-Jul-14	07-Aug-14	117d
Tooping and Basecourse		56d		05-Jun-14 A	23-Jul-14	131d
NAB3160	20 cm Thick Topping Layer RHS	13d	30%	05-Jun-14 A	17-Jul-14	134d
NAB3180	20 cm Thick Base Course- First Layer RHS	13d	30%	10-Jun-14 A	17-Jul-14	134d
NAB2310	20 cm Thick Topping Layer LHS	13d	30%	11-Jun-14 A	17-Jul-14	134d
NAB2320	20 cm Thick Base Course- First Layer LHS	13d	7%	15-Jun-14 A	23-Jul-14	131d
NAB3190	20 cm Thick Base Course- Second Layer RHS	13d	20%	22-Jun-14 A	20-Jul-14	81d
NAB2330	20 cm Thick Base Course- Second Layer LHS	13d	15%	28-Jun-14 A	21-Jul-14	81d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A4+500 To St. A5+000 LHS & RHS Area A		134d		22-May-14 A	24-Nov-14	30d
NAB2370	Maintain traffic control and safety plan ,Relocating utilities	101d	0%	22-May-14 A	24-Nov-14	26d
Excavation		12d		13-Jul-14	06-Aug-14	0d
NAB2380	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	12d	0%	13-Jul-14	06-Aug-14	0d
Storm System		0d				0d
Water lines		10d		22-May-14 A	05-Jul-14	56d
NAB3350-new	12" Steel pipeline beit iba from st 4+450 To st 4+950 RHS	10d	75%	22-May-14 A	05-Jul-14	56d
Sewer line		0d				0d
Concrete works		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d

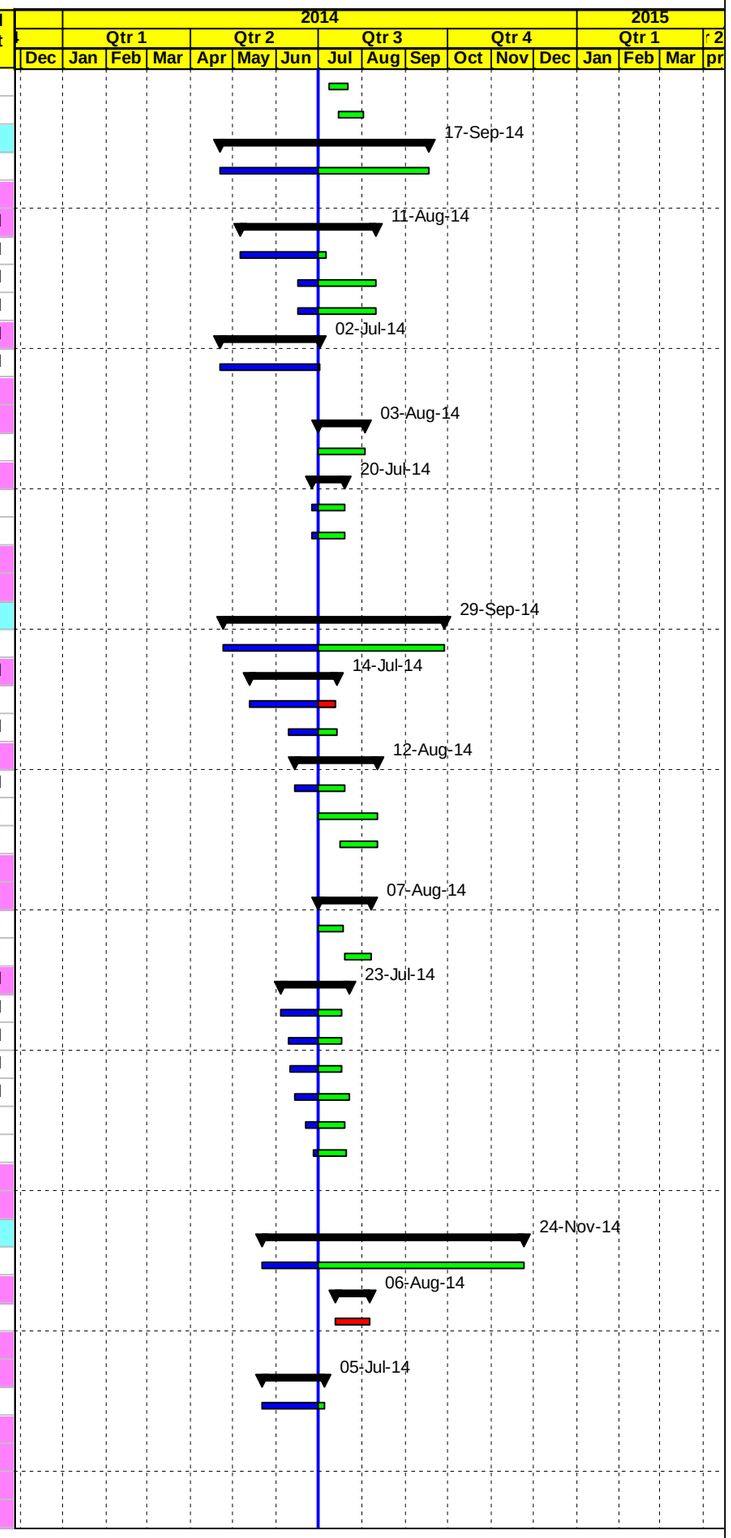

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
One Month Lookahead

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A5+000 To St. A5+450 LHS & RHS Area A		173d		01-Jul-14	21-Dec-14	9d
NAB5000	Maintain traffic control and safety plan ,Relocating utilities	131d	0%	01-Jul-14	21-Dec-14	7d
Excavation		0d				0d
Storm System		0d				0d
Water lines		10d		01-Jul-14	19-Jul-14	59d
NAB3460-new	12" Steel pipeline beit iba from st 4+950 To st 5+450 RHS	10d	0%	01-Jul-14	19-Jul-14	59d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Phase Two closed (RHS & LHS) from St. A0+000 - A2+020		146d		24-Apr-14 A	10-Nov-14	27d
Main Road St. A2+020 To St. A1+500 RHS & LHS Area B		146d		24-Apr-14 A	24-Sep-14	67d
NAB4030	Maintain traffic control and safety plan ,Relocating utilities	107d	43.18%	24-Apr-14 A	24-Sep-14	51d
Excavation		69d		24-Apr-14 A	08-Jul-14	72d
NAB4790	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	14d	70%	24-Apr-14 A	08-Jul-14	72d
NAB4040	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	20d	80%	08-Jun-14 A	08-Jul-14	0d
Storm System		29d		18-Jun-14 A	04-Aug-14	63d
NAB4070	60 cm Conc. Pipes for drainage W. manholes from A1+690 to A2+020 L= 330 m RHS	29d	90%	18-Jun-14 A	06-Jul-14	55d
NAB4050	60 cm Conc. Pipes for drainage W. manholes from A1+500 to A1+620 L= 120 m RHS	14d	0%	06-Jul-14	04-Aug-14	55d
NAB4830	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	10d	0%	14-Jul-14	04-Aug-14	55d
NAB4080	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	10d	0%	14-Jul-14	04-Aug-14	63d
Water lines		12d		08-Jul-14	03-Aug-14	72d
NAB4090	12" Steel pipeline deir sharaf @ A1+960 TO Nablus connection RHS	5d	0%	08-Jul-14	17-Jul-14	71d
NAB4820	3" Water pipeline from St. A 1+900 to A 2+020 (LHS) =120 M LHS	6d	0%	08-Jul-14	20-Jul-14	78d
NAB4800	12" Steel pipeline deir sharaf project L = 570 m LHS	12d	0%	08-Jul-14	03-Aug-14	72d
Sewer line		3d		08-Jul-14	14-Jul-14	81d
NAB4810	12" Sewer line from St. A1+930 to St. A2+020 L=90 M LHS	3d	0%	08-Jul-14	14-Jul-14	81d
Concrete works		0d				0d
Tooping and Basecourse		98d		21-Jun-14 A	09-Aug-14	51d
NAB4100	20 cm Thick Topping Layer RHS	8d	40%	21-Jun-14 A	09-Jul-14	51d
NAB4840	20 cm Thick Topping Layer LHS	8d	0%	09-Jul-14	24-Jul-14	51d
NAB4120	20 cm Thick Base Course- First Layer RHS	8d	0%	24-Jul-14	09-Aug-14	51d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A1+500 To St. A1+000 RHS & LHS Area C		126d		08-Jul-14	10-Nov-14	27d
NAB3880	Maintain traffic control and safety plan ,Relocating utilities RHS	93d	0%	08-Jul-14	10-Nov-14	22d
Excavation		12d		08-Jul-14	03-Aug-14	0d
NAB3890	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	12d	0%	08-Jul-14	03-Aug-14	0d
Storm System		0d				0d
Water lines		0d				0d
Concrete works		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A1+000 To St. A0+500 RHS & LHS Area C		0d				0d
Excavation		0d				0d
Storm System		0d				0d
Water lines		0d				0d
Sewer line		0d				0d
Concrete works		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d

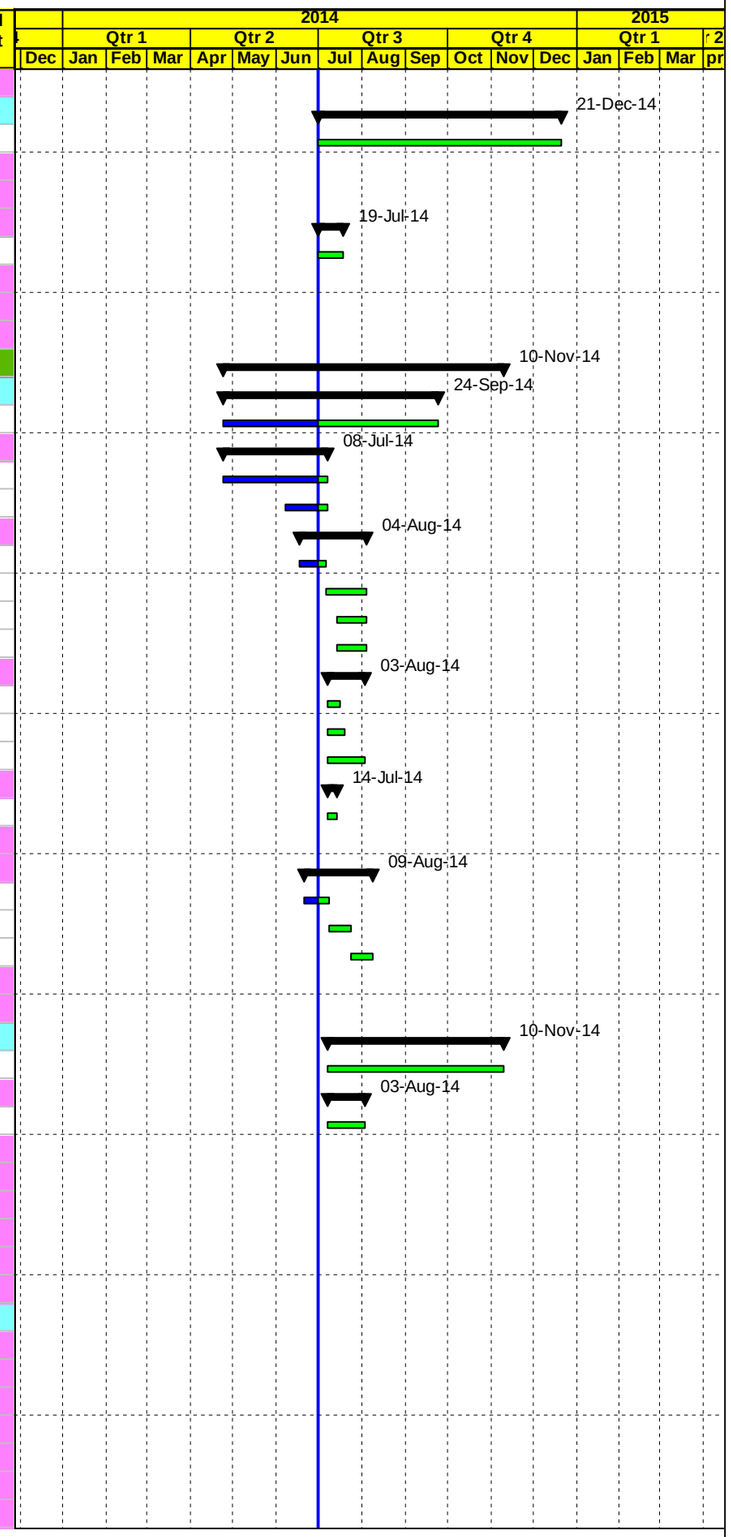

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
One Month Lookahead

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
	Street Lighting Poles and Curbstone	0d				0d
	Main Road From St. A0+500 To St. A0+000 RHS & LHS Area C	0d				0d
	Excavation	0d				0d
	Storm System	0d				0d
	Water lines	0d				0d
	Sewer line	0d				0d
	Tooping and Basecourse	0d				0d
	Asphalt binder	0d				0d
	Street Lighting Poles and Curbstone	0d				0d
	Phase Three Seg. B from sta.B0+000 to B0+399 Total Close (Area B)	0d				0d
	Temporary Detours	6d		01-Jul-14	12-Jul-14	131d
NAB4877	Excavation & Base-course for Paved Temporary Detours	6d	0%	01-Jul-14	12-Jul-14	131d
	Miscellaneous activities - If any as location is not determined yet	21d		01-Jul-14	09-Aug-14	116d
NAB4888	Road Crossings 6" dia. Pipe	21d	0%	01-Jul-14	09-Aug-14	116d
NAB4890	UPVC pipes For 6" dia Pipe	21d	0%	01-Jul-14	09-Aug-14	116d
NAB4892	UPVC pipes For 8" dia Pipe	21d	0%	01-Jul-14	09-Aug-14	116d
NAB4896	Sewage Manholes 1000 mm dia.	21d	0%	01-Jul-14	09-Aug-14	116d
NAB4898	Edge beam	21d	0%	01-Jul-14	09-Aug-14	116d
NAB4899	Adjustment manhole heavy duty (25 Ton)	21d	0%	01-Jul-14	09-Aug-14	116d
NAB4894	3" Steel Water pipeline	21d	0%	01-Jul-14	09-Aug-14	116d
	Asphalt and Miscellaneous Works	23d		01-Jul-14	11-Aug-14	114d
NAB1760	stone wall	23d	0%	01-Jul-14	11-Aug-14	114d
NAB5000-new	Connecting with Existing lines at two points	10d	0%	01-Jul-14	19-Jul-14	106d
	PROJECT 01 Post Construction Phase	0d				0d
	PROJECT 02 Deir Sharaf Tulkarem Road	79d		15-May-14 A	03-Aug-14	156d
	PROJECT 02 Pre Construction Phase	0d				0d
	PROJECT 02 Conformed Drawings and Coordination	0d				0d
	PROJECT 02 Mobilization	0d				0d
	PROJECT 02 Construction Phase	79d		15-May-14 A	03-Aug-14	156d
	PROJECT 02 Construction Submittals	22d		28-Jun-14 A	12-Jul-14	179d
	PROJECT 02 Shop Drawing Submittals	22d		28-Jun-14 A	12-Jul-14	179d
	Plan Profile and Cross Sections	12d		28-Jun-14 A	12-Jul-14	137d
DSR1200-new	Simple Access at Sta.0+170 LHS ,0+360 RHS , 0+430 RHS,0+930 RHS,0+990 RHS,1+100 LHS,1+439,1+460 LHS	12d	50%	28-Jun-14 A	12-Jul-14	137d
	Water Line	0d				0d
	Culverts	0d				0d
	Concrete Walls	0d				0d
	Otheres	12d		01-Jul-14 A	12-Jul-14	25d
DSR1365-new	Directional Signs	12d	50%	01-Jul-14 A	12-Jul-14	25d
	PROJECT 02 Material Submittals	0d				0d
	PROJECT 02 Construction	79d		15-May-14 A	03-Aug-14	156d
	PROJECT 02 Implement traffic control	0d				0d
	Phase #1 Totally closed from St. 0+100 To St. 2+180 Area C	71d		15-May-14 A	24-Jul-14	166d
	From St. 0+100 To St. 0+700 Area C	0d				0d
	From St.0+700 To St. 1+280 Area C	12d		15-May-14 A	07-Jul-14	140d
DSR1750	New Pipe Culvert 800mm @ St. 0+780	12d	70%	15-May-14 A	07-Jul-14	140d
	Asphalt Works From St. 0+100 To St. 1+280	0d				0d
	From St. 1+280 To St. 1+730 Area C	20d		18-Jun-14 A	05-Jul-14	185d
DSR1930	7 cm Asphalt Binder Course Including Prime Coat	2d	26.98%	18-Jun-14 A	03-Jul-14	142d
DSR1955-new	6" UPVC for ROAD CROSSING (SLEEVES)	5d	0%	01-Jul-14	05-Jul-14	29d
	From St. 1+730 To St. 2+180 Area C	19d		04-Jun-14 A	24-Jul-14	12d
DSR1990	Pipe Culvert 600mm @ St. 1+995	9d	70%	04-Jun-14 A	06-Jul-14	22d
DSR2265-new	Retaining wall from St. 1+665to 1+760 LHS	12d	88.99%	05-Jun-14 A	03-Jul-14	17d

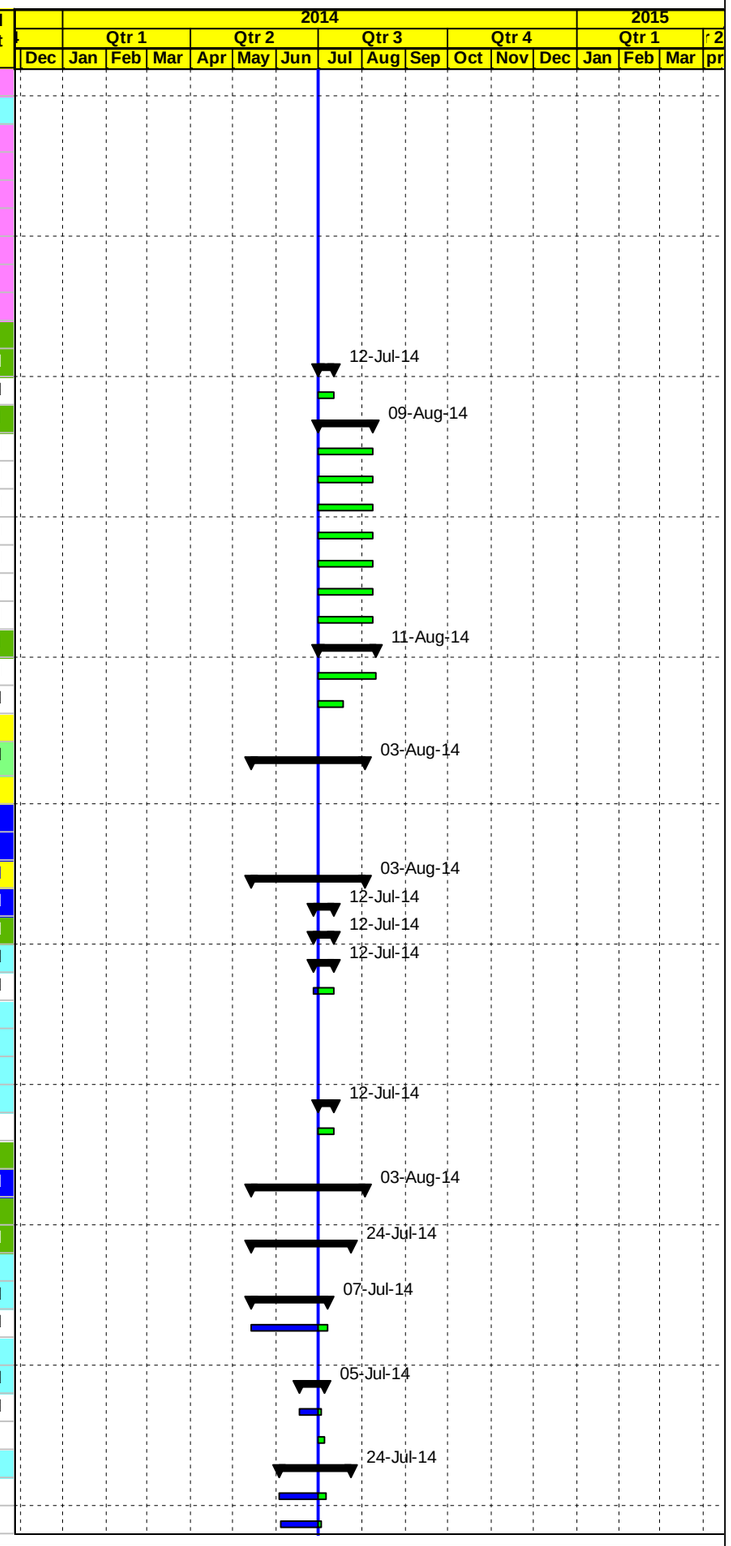

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program

One Month Lookahead

TO14

Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DSR2050	7 cm Asphalt Binder Course Including Prime Coat	2d	31.98%	23-Jun-14 A	03-Jul-14	15d
DSR2266-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 1+760	13d	0%	01-Jul-14	24-Jul-14	5d
Phase #2 From St. 0+000 to 0+100		36d		22-May-14 A	03-Aug-14	0d
DSR2060	Relocation Exist. Utilities , Maintain traffic control & safety Plan (RHS&LHS)	36d	55.56%	22-May-14 A	03-Aug-14	0d
DSR2070	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	4d	0%	01-Jul-14	08-Jul-14	0d
DSR2080	20 cm Thick Topping Layer/ Pulverization	4d	0%	08-Jul-14	15-Jul-14	0d
DSR2090	20 cm Thick Base Course- First Layer	4d	0%	15-Jul-14	23-Jul-14	0d
DSR2100	20 cm Thick Base Course- Second Layer	4d	0%	23-Jul-14	03-Aug-14	0d
Miscellaneous Works		24d		27-May-14 A	18-Jul-14	24d
DSR1885-new	Concrete step barrier	13d	90.99%	27-May-14 A	02-Jul-14	17d
DSR2150	Curbstone if any	6d	0%	01-Jul-14	12-Jul-14	17d
DSR1925	3" Water Pipeline	10d	0%	08-Jul-14	18-Jul-14	18d
PROJECT 02 Post Construction Phase		0d				0d
Post Construction Phase		0d				0d
Post Submittals		0d				0d

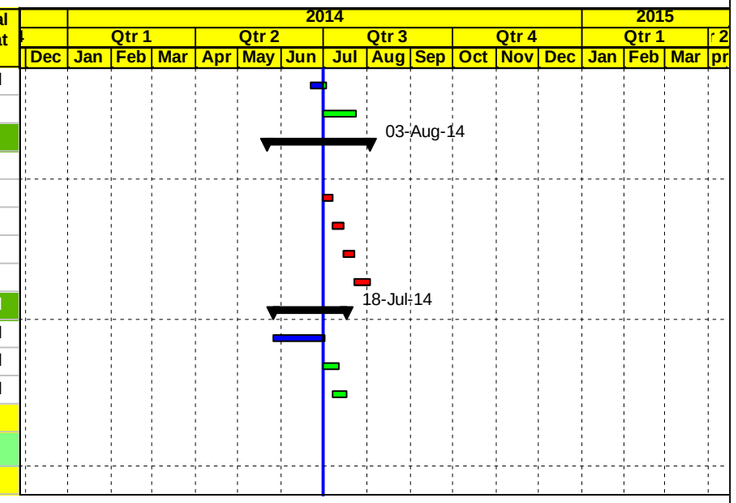

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Multiple Roads Project North (II)		411d		03-Dec-13 A	06-Jan-15	0d
Milestones		364d		03-Dec-13 A	06-Jan-15	0d
General Milestone		0d		03-Dec-13 A	03-Dec-13 A	
MRNII0000	Start Date NTP	0d	100%	03-Dec-13 A		
Intermediate Milestones		364d		03-Dec-13 A	06-Jan-15	0d
Completion Milestones		0d				0d
Preconstuction Milestones		110d		08-Dec-13 A	13-May-14 A	
MRNII0040	Start Preconstruction Submittal	0d	100%	08-Dec-13 A		
MRNII0050	Finish Preconstruction Submittal	0d	100%		13-May-14 A	
PROJECT 01 Nablus - Beit Iba - Deir Sharaf Road		364d		03-Dec-13 A	06-Jan-15	0d
Mobilization		13d		04-Dec-13 A	23-Jan-14 A	
MRNII0060	Start Mobilization	0d	100%	04-Dec-13 A		
MRNII0070	Finish Mobilization	0d	100%		23-Jan-14 A	
Shop Drawing		0d		09-Jan-14 A	09-Jan-14 A	
MRNII0080	Start Shop Drawing Submittal	0d	100%	09-Jan-14 A		
Material		0d		25-Dec-13 A	25-Dec-13 A	
MRNII0100	Start Material Submittal	0d	100%	25-Dec-13 A		
Construction		0d		23-Jan-14 A	23-Jan-14 A	
MRNII0120	Start Construction (Ground Breaking)	0d	100%	23-Jan-14 A		
Project Duration		364d		03-Dec-13 A	06-Jan-15	0d
MRNII0140	Project Duration (Calendar Days)	364d	47.8%	03-Dec-13 A	06-Jan-15	0d
MRNII0150	Project Duration (Working Days)	279d	48.66%	03-Dec-13 A	06-Jan-15	0d
MRNII0160	Construction Duration (Working Days)	240d	42.69%	23-Jan-14 A	29-Dec-14	0d
PROJECT 02 Deir Sharaf Tulkarem Road		287d		03-Dec-13 A	20-Aug-14	0d
Mobilization		19d		04-Dec-13 A	20-Jan-14 A	
MRNII0170	Start Mobilization	0d	100%	04-Dec-13 A		
MRNII0180	Finish Mobilization	0d	100%		20-Jan-14 A	
Shop Drawing Milestones		0d		15-Jan-14 A	15-Jan-14 A	
MRNII0190	Start Shop Drawing Submittal	0d	100%	15-Jan-14 A		
Material		102d		25-Dec-13 A	25-Feb-14 A	
MRNII0210	Start Material Submittal	0d	100%	25-Dec-13 A		
MRNII0220	Finish Material submittal	0d	100%		25-Feb-14 A	
Construction		0d		23-Feb-14 A	23-Feb-14 A	
MRNII0230	Start Construction (Ground Breaking)	0d	100%	23-Feb-14 A		
Project Duration		287d		03-Dec-13 A	20-Aug-14	0d
MRNII0250	Project Duration (Calendar Days)	240d	78.81%	03-Dec-13 A	20-Aug-14	0d
MRNII0260	Project Duration (Working Days)	179d	82.68%	03-Dec-13 A	20-Aug-14	0d
MRNII0270	Construction Duration (Working Days)	145d	82.77%	23-Feb-14 A	13-Aug-14	0d
Task order Duration		364d		03-Dec-13 A	06-Jan-15	0d
MRNII0280	Project Duration (Calendar Days)	364d	47.8%	03-Dec-13 A	06-Jan-15	0d
MRNII0290	Project Duration (Working Days)	279d	48.66%	03-Dec-13 A	06-Jan-15	0d
Pre Construction Phase		162d		08-Dec-13 A	13-May-14 A	
Pre Construction Submittals		115d		08-Dec-13 A	13-May-14 A	
MRNII1100	Bank Guarantee Certificates	10d	100%	08-Dec-13 A	31-Dec-13 A	
MRNII1090	30- Day Schedule (Pre Construction Submittals & Mobilization phase)	10d	100%	08-Dec-13 A	22-Dec-13 A	
MRNII1110	Temporary and Permanent Project Sign Plan	10d	100%	08-Dec-13 A	22-Dec-13 A	
MRNII1190	Subcontractors' profile	10d	100%	22-Dec-13 A	31-Dec-13 A	
MRNII1130	Testing Lab	10d	100%	23-Dec-13 A	05-Jan-14 A	
MRNII1170	Key Personnel Plan	10d	100%	25-Dec-13 A	31-Dec-13 A	

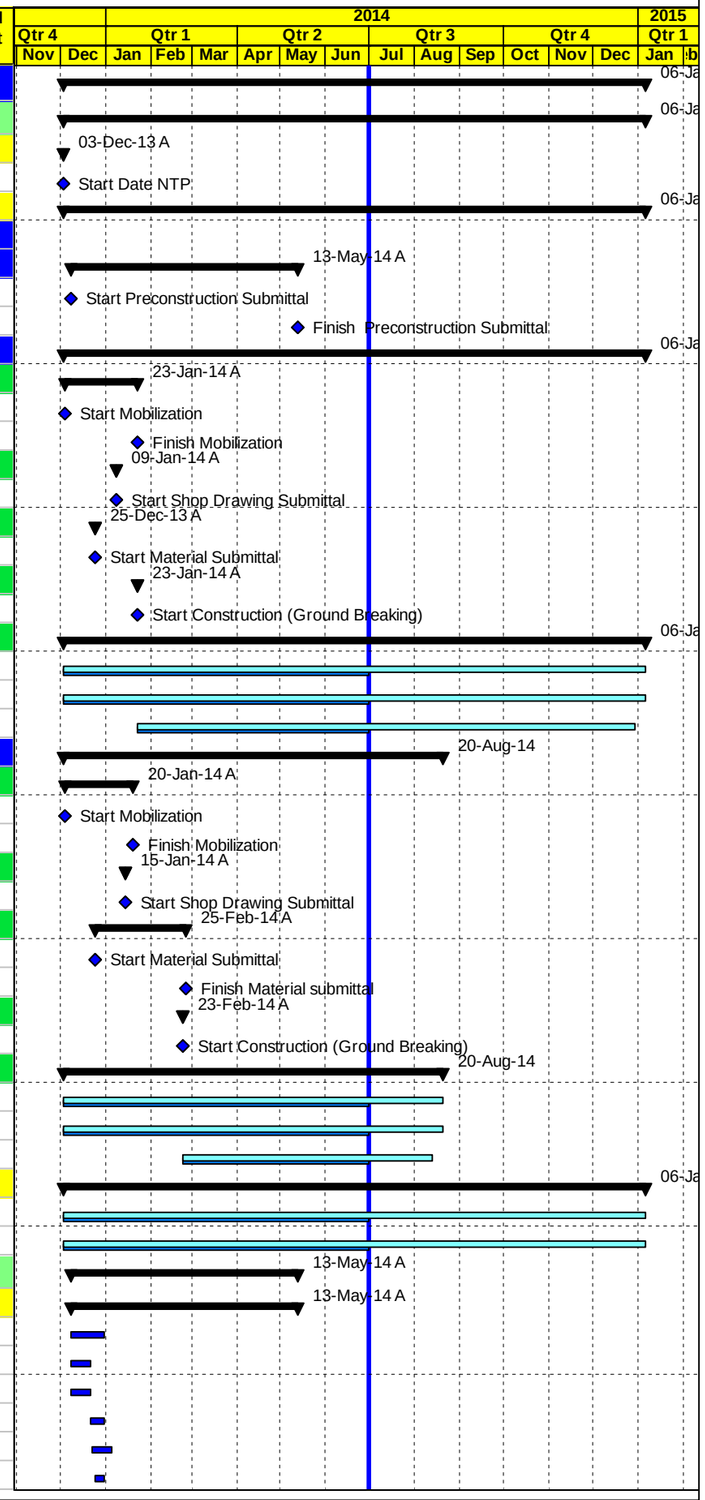

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
MRNII1200	QCP-Quality Control Program	10d	100%	25-Dec-13 A	09-Jan-14 A	
MRNII1180	Safety Plan	10d	100%	25-Dec-13 A	13-Jan-14 A	
MRNII1140	Field Offices Furniture & Equipment Plan	10d	100%	25-Dec-13 A	09-Feb-14 A	
MRNII1260	USAID Branding Plan	10d	100%	25-Dec-13 A	07-Jan-14 A	
MRNII1120	Insurances	10d	100%	25-Dec-13 A	06-Jan-14 A	
MRNII1150	Existing Survey Plan for Project 01	10d	100%	29-Dec-13 A	22-Jan-14 A	
MRNII1230	Schedule Submittals	10d	100%	29-Dec-13 A	13-Jan-14 A	
MRNII1310	Method Statement Plan	10d	100%	29-Dec-13 A	22-Jan-14 A	
MRNII1330	CPM-Construction Schedule and S-Curve	10d	100%	29-Dec-13 A	04-Mar-14 A	
MRNII1240	60-Day Plan of Operation	10d	100%	29-Dec-13 A	08-Jan-14 A	
MRNII1245	Project Overview Bar Chart	10d	100%	29-Dec-13 A	08-Jan-14 A	
MRNII1210	Coordination with local Authorities Plan	10d	100%	30-Dec-13 A	13-Jan-14 A	
MRNII1160	Existing Survey Plan for Project 02	10d	100%	31-Dec-13 A	14-Jan-14 A	
MRNII1220	Field Offices Location & Layout	10d	100%	06-Jan-14 A	09-Jan-14 A	
MRNII1270	Dilapidation Survey (Project 01)	10d	100%	07-Jan-14 A	05-Mar-14 A	
MRNII1280	Dilapidation Survey (Project 02)	10d	100%	15-Jan-14 A	21-Jan-14 A	
MRNII1320	Environmental Mitigation Plan	10d	100%	16-Jan-14 A	26-Jan-14 A	
MRNII1290	Risk Management Plan (Project 01)	10d	100%	19-Jan-14 A	03-Mar-14 A	
MRNII1250-new	Proposed staging and storage yard -Nablus Beit Iba Der Sharaf Road -Project 01	10d	100%	19-Jan-14 A	21-Jan-14 A	
MRNII1340	Traffic Control Plan Phase I- from Sta.0+000 to Sta.2+180 (Project 02)	10d	100%	26-Jan-14 A	05-Feb-14 A	
MRNII1300	Risk Management Plan (Project 02)	10d	100%	29-Jan-14 A	05-Feb-14 A	
MRNII1350	Traffic Control Plan (Area A and B) from Sta.2+020 to Sta.2+540-Nablus Beit Iba Der Sharaf Road -Project 01	10d	100%	05-Feb-14 A	06-Feb-14 A	
MRNII1250	Proposed Dumping Area -Project 01	10d	100%	11-Feb-14 A	12-Feb-14 A	
MRNII1310-new	Traffic Control Plan from Sta.A2+540 to Sta.A3+500 -Phase II-Project 01	10d	100%	17-Feb-14 A	02-Mar-14 A	
MRNII1315-new	12" inch Procedure Qualification Record (PQR)	10d	100%	05-Mar-14 A	20-Mar-14 A	
MRNII1316-new	Welding Procedure 3-12 inch pipes- Project 01	10d	100%	24-Mar-14 A	31-Mar-14 A	
MRNII1317-new	Specific Method Statement for Sewer lines Leakage Testing Project 01	10d	100%	25-Mar-14 A	30-Mar-14 A	
MRNII1318-new	Traffic Control Plan from Sta.3+520 to Sta.4+620-Project 01	10d	100%	08-Apr-14 A	28-Apr-14 A	
MRNII1319-new	Special Method Statements for Hydrostatic Test for concrete pipes - project 01	10d	100%	21-Apr-14 A	24-Apr-14 A	
MRNII1320-new	Traffic Control Plan Phase II from Sta.0+000 to Sta.2+000 -Nablus Beit Iba Der Sharaf Road -Project 01	10d	100%	28-Apr-14 A	13-May-14 A	
MRNII1325-new	Confined space safety plan -Project 01	10d	100%	06-May-14 A	08-May-14 A	
Mobilization Offices		4d		25-Dec-13 A	06-Jan-14 A	
MRNII1370	Supply and install Office Furniture's and Supplies	3d	100%	25-Dec-13 A	06-Jan-14 A	
MRNII1380	Supply and install Office IT Equipments & Applience	3d	100%	25-Dec-13 A	06-Jan-14 A	
PROJECT 01 Nablus - Beit Iba - Deir Sharaf Road		411d		03-Dec-13 A	24-Nov-14	44d
PROJECT 01 Preconstruction Phase		50d		03-Dec-13 A	12-Jul-14	178d
PROJECT 01 Conformed Drawings and Coordination		40d		03-Dec-13 A	12-Jul-14	178d
NAB0110	Coordination with Israeli authorities for approval and permit area C Project 01	40d	70%	03-Dec-13 A	12-Jul-14	178d
NAB0100	Final for Construction Drawing (Conformed)	0d	100%	03-Dec-13 A		
PROJECT 01 Mobilization		31d		04-Dec-13 A	23-Jan-14 A	
NAB0140	Mobilization Total Cost (4.0%)	13d	100%	04-Dec-13 A	23-Jan-14 A	
NAB0170	Site Hand Over	1d	100%	08-Dec-13 A	08-Dec-13 A	
NAB0190	Start Preparation Construction Submittals (Survey plan , Shop Drawings & Materials)	13d	100%	15-Dec-13 A	04-Jan-14 A	
NAB0200	Install Temporary Project Sign	2d	100%	20-Jan-14 A	20-Jan-14 A	
NAB0205	Storage yard preparation and mobilizing equipment	3d	100%	20-Jan-14 A	23-Jan-14 A	
NAB0180	Checking With CMC Existing-Bench Marks, Survey Control Points	0d	100%	22-Jan-14 A	22-Jan-14 A	
PROJECT 01 Construction Phase		411d		25-Dec-13 A	24-Nov-14	44d
PROJECT 01 Construction Submittals		251d		25-Dec-13 A	12-Jul-14	178d
PROJECT 01 Shop Drawing Submittals		251d		09-Jan-14 A	12-Jul-14	179d

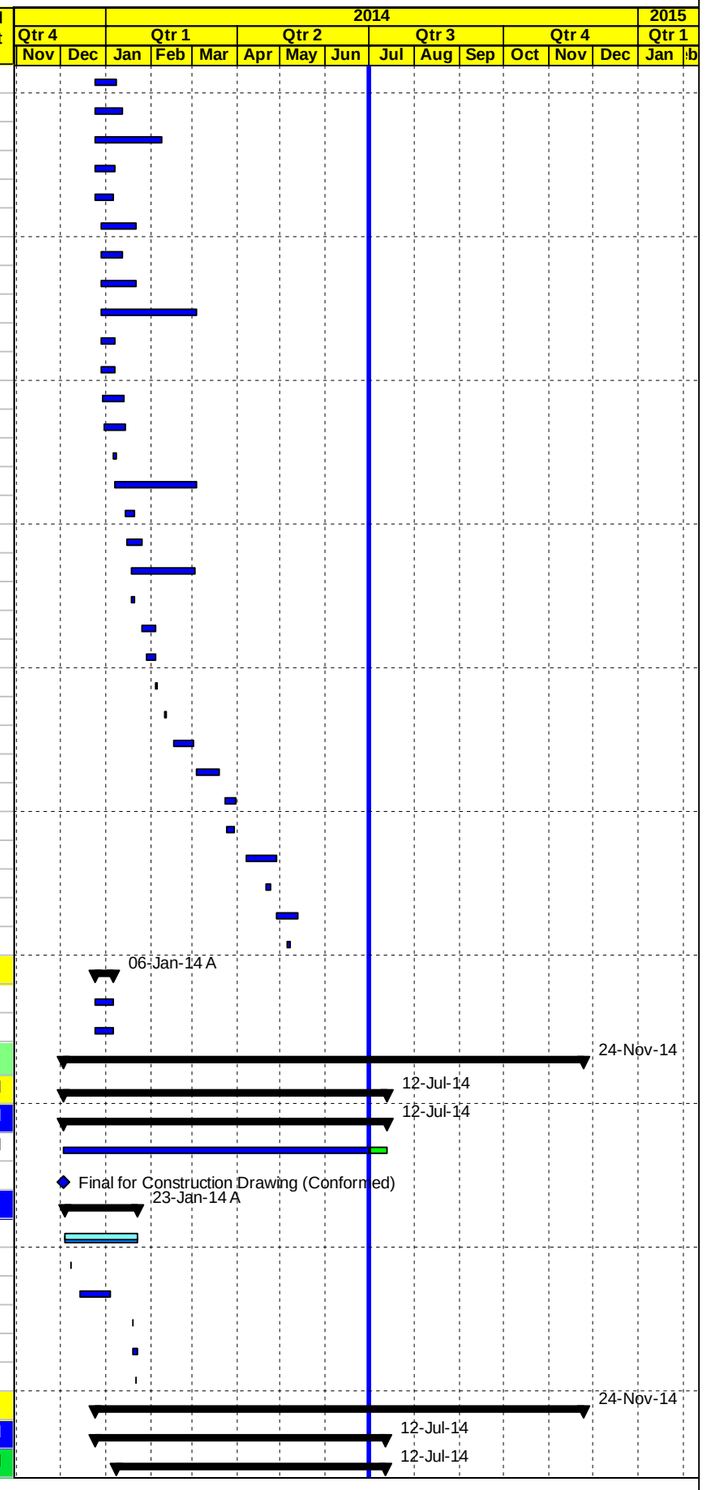

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Plan Profile and Cross Sections Phase One		126d		09-Jan-14 A	05-Jun-14 A	
NAB0240	Main Road From St. A2+020 To St. A2+600	12d	100%	09-Jan-14 A	09-Feb-14 A	
NAB0250	Main Road From St. A2+600 To St. A3+000	12d	100%	16-Feb-14 A	25-Feb-14 A	
NAB0260	Main Road From St. A3+000 To St. A3+600	12d	100%	02-Mar-14 A	26-Mar-14 A	
NAB0270	Main Road From St. A3+600 To St. A4+100	12d	100%	06-Mar-14 A	17-Mar-14 A	
NAB0280	Main Road From St. A4+100 To St. A4+850	12d	100%	27-Mar-14 A	07-May-14 A	
NAB0301-new	Junction at Sta.3+420	12d	100%	24-Apr-14 A	13-May-14 A	
NAB0302-new	Junction at Sta.2+600 LHS and at Sta.2+640 RHS	12d	100%	04-May-14 A	06-May-14 A	
NAB0285-new	Junction from Sta.1+910 to Sta.2+040	12d	100%	24-May-14 A	05-Jun-14 A	
Plan Profile and Cross Sections Phase Two		78d		10-Apr-14 A	12-Jul-14	67d
NAB0370	Main Road From St. A1+500 To St. A2+020	12d	100%	10-Apr-14 A	05-May-14 A	
NAB0360	Main Road From St. A1+000 To St. A1+500	12d	100%	15-May-14 A	22-Jun-14 A	
NAB0380	Seg B From St. B0+000 To St. B0+399	12d	50%	18-Jun-14 A	12-Jul-14	67d
Waterline		109d		16-Jan-14 A	01-Jun-14 A	
NAB0400	Water pipeline from St. A 1+900 to A 2+500 (3") (LHS)	12d	100%	16-Jan-14 A	20-Mar-14 A	
NAB0400-NEW	12 " Deir Sharaf steel water pipeline from St. A 2+000 to A 3+000 (12") (RHS)	12d	100%	17-Mar-14 A	23-Mar-14 A	
NAB0401-NEW	12 " Deir Sharaf steel water pipeline from St. A 3+000 to A 4+100 (12") (RHS)	12d	100%	03-Apr-14 A	08-Apr-14 A	
NAB0402-NEW	3" Deir Sharaf steel water pipeline from St. A 2+900 to A 4+400 (3") (LHS)	12d	100%	10-Apr-14 A	16-Apr-14 A	
NAB0420	12" Deir Sharaf steel water pipeline from St. Sta.1+050 to Sta.2+000 (LHS)	12d	100%	28-Apr-14 A	01-Jun-14 A	
NAB0403-NEW	12 " Deir Sharaf steel water pipeline from St. A 4+100 to A 4+850 (12") (RHS)	12d	100%	05-May-14 A	07-May-14 A	
Sewer line		148d		20-Jan-14 A	12-Jul-14	121d
NAB0430	Sewer line (LHS) from St. 1+930 to 2+610 (12")	12d	100%	20-Jan-14 A	09-Feb-14 A	
NAB0435-new	Sewer line (LHS) from Sta.3+407 to Sta.3+560	12d	100%	13-May-14 A	15-May-14 A	
NAB0440	Sewer line (LHS) from St. 4+100 to 4+600 (12")	12d	50%	26-Jun-14 A	12-Jul-14	121d
Concrete walls Phase One		177d		06-Feb-14 A	12-Jul-14	61d
NAB0443-New	Retaining Wall from Sta.2+339 to Sta.2+369 (RHS)	12d	100%	06-Feb-14 A	09-Feb-14 A	
NAB0444-New	Concrete Wall from Sta.2+040 to Sta.2+065 (LHS)	12d	100%	06-Feb-14 A	13-Mar-14 A	
NAB0447-New	Retaining Wall from Sta.A2+475 to Sta.A2+515 (RHS)	12d	100%	16-Feb-14 A	23-Feb-14 A	
NAB0449-New	Retaining Wall from Sta.2+740 to Sta.2+850 (RHS)	12d	100%	02-Mar-14 A	05-Mar-14 A	
NAB0451-New	Retaining Wall from Sta.A2+980 to Sta.A3+010 (LHS)	12d	100%	10-Mar-14 A	31-Mar-14 A	
NAB0452-New	Retaining Wall from Sta.A2+719 to Sta.A2+730 (LHS) L= 11m	12d	100%	10-Mar-14 A	05-May-14 A	
NAB0461-New	Retaining Wall from Sta.3+230 to Sta.3+300 (RHS) L= 70 m	12d	100%	16-Mar-14 A	06-Apr-14 A	
NAB0467-New	Retaining Wall from Sta.3+230 to Sta.3+300 (RHS) L= 70 m	12d	100%	16-Mar-14 A	06-Apr-14 A	
NAB0460	Conc. Retaining walls from A3+160 to A3+190 (LHS) L= 40 m & A3+160 to A3+190 (RHS) L= 40 m	12d	100%	19-Mar-14 A	31-Mar-14 A	
NAB0462-New	Conc. Retaining walls from Sta.A3+560 to Sta.A3+590 (RHS)	12d	100%	19-Mar-14 A	24-Mar-14 A	
NAB0463-New	Conc. Retaining walls from Sta.A3+010 to Sta.A3+020 (RHS)	12d	100%	24-Mar-14 A	27-Mar-14 A	
NAB0466-New	Retaining Wall from Sta.A3+341 to Sta.A3+370 (RHS) L= 29 m	12d	100%	25-Mar-14 A	22-Apr-14 A	
NAB0464-New	Conc. Retaining walls from Sta.3+655 to Sta.3+695 (RHS)	12d	100%	27-Mar-14 A	06-Apr-14 A	
NAB0465-New	Conc. Retaining walls from Sta.3+373 to Sta.3+402 (LHS)	12d	100%	31-Mar-14 A	06-Apr-14 A	
NAB0470	Conc. Retaining walls from A3+828.5 to A3+855.5 (RHS) L= 27 m	12d	100%	03-Apr-14 A	05-May-14 A	
NAB0480	Conc. Retaining walls from A3+950 to A3+982 (LHS) L= 32 m	12d	100%	03-Apr-14 A	30-Apr-14 A	
NAB0468-New	Boundary wall from Sta.3+950 to Sta.3+985 (LHS)	12d	100%	03-Apr-14 A	30-Apr-14 A	
NAB0469-New	Retaining Wall from Sta.4+090 to Sta.4+100	12d	50%	24-Apr-14 A	12-Jul-14	61d
NAB0472-New	Retaining Wall from Sta.3+217 to Sta.3+226 LHS L= 9 m and Concrete Stair from Sta. 3+226 to Sta.3+229 LHS L= 3	12d	100%	07-May-14 A	19-May-14 A	
NAB0473-New	Retaining Wall from Sta.3+715 to Sta.3+740 LHS L= 25 m	12d	100%	12-May-14 A	22-Jun-14 A	
NAB0500	Conc. Retaining walls from A4+545 to Sta.A4+617 RHS L= 72 m	12d	100%	13-May-14 A	21-May-14 A	
NAB0510	Conc. Retaining walls from A4+830 to A4+865 (RHS) L= 35 m	12d	100%	14-May-14 A	21-May-14 A	
Concrete walls Phase Two		12d		04-May-14 A	07-May-14 A	
NAB0470-New	Retaining Wall from Sta.1+720 to Sta.1+750 RHS L= 30 m	12d	100%	04-May-14 A	07-May-14 A	

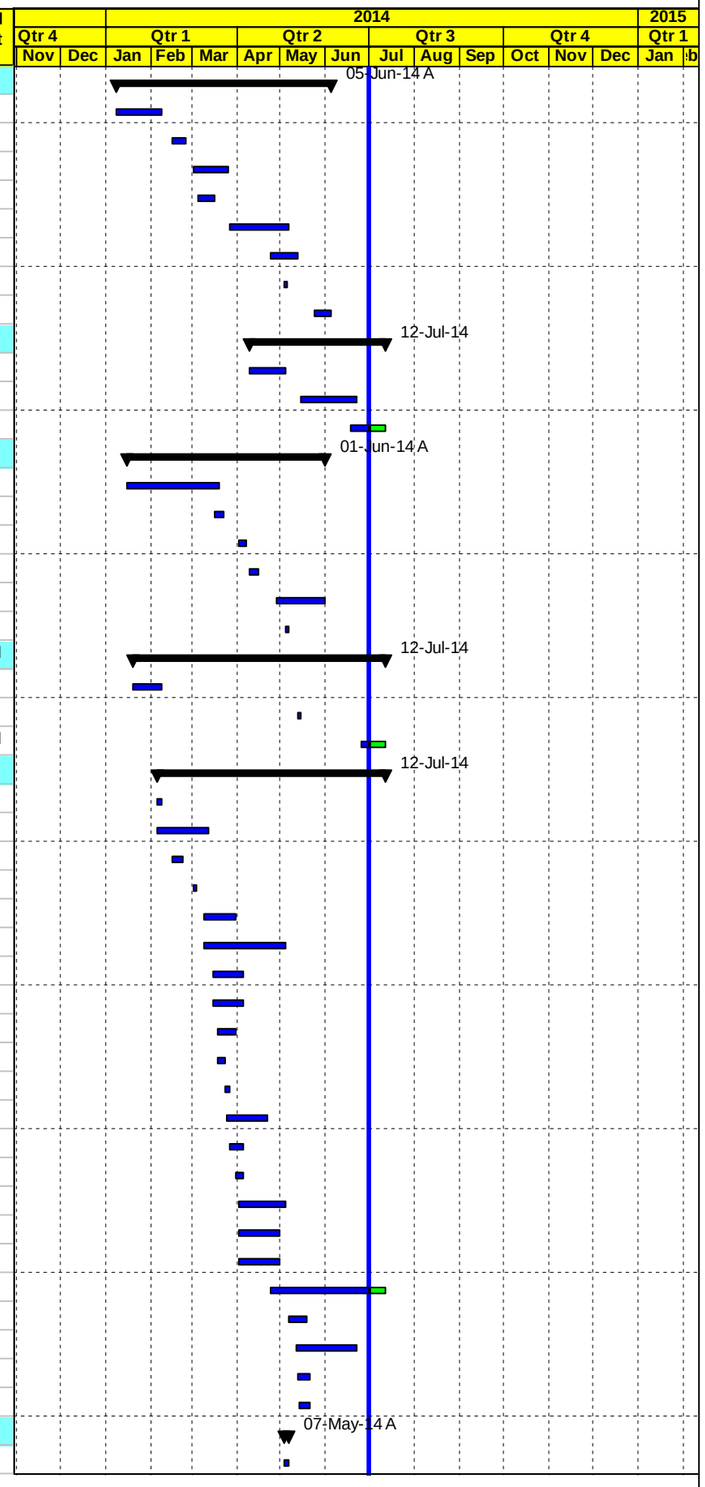

◆ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
NAB0471-New	Retaining Wall from Sta.1+865 to Sta.1+930 RHS L= 65 m	12d	100%	05-May-14 A	07-May-14 A	
60 cm Conc. Pipes for drainage LHS Phase One		148d		16-Jan-14 A	12-Jul-14	137d
NAB0590	60 cm Conc. Pipes for drainage from A2+500 to A2+580 L= 80 m	12d	100%	16-Jan-14 A	13-Feb-14 A	
NAB0570	60 cm Conc. Pipes for drainage from A2+020 to A2+180 L= 160 m	12d	100%	16-Jan-14 A	13-Feb-14 A	
NAB0580	60 cm Conc. Pipes for drainage from A2+220 to A2+500 L= 280 m	12d	100%	16-Jan-14 A	13-Feb-14 A	
NAB0610	60 cm Conc. Pipes for drainage from A2+870 to A2+980 L= 110 m	12d	100%	06-Mar-14 A	10-Mar-14 A	
NAB0600	60 cm Conc. Pipes for drainage from A2+580 to A2+980 L= 160 m	12d	100%	06-Mar-14 A	10-Mar-14 A	
NAB0630	60 cm Conc. Pipes for drainage from Sta.3+600 to Sta.3+840 L= 240 m	12d	100%	14-Apr-14 A	13-May-14 A	
NAB0601	60 cm Conc. Pipes for drainage from Sta.3+000 to Sta.3+120	12d	100%	17-Apr-14 A	21-Apr-14 A	
NAB0602-	60 cm Conc. Pipes for drainage from Sta.4+100 to Sta.4+560	12d	50%	26-Jun-14 A	12-Jul-14	137d
60 cm Conc. Pipes for drainage RHS Phase Two		27d		19-May-14 A	12-Jul-14	58d
NAB0740	60 cm Conc. Pipes for drainage from A1+690 to A2+020 L= 330 m	12d	100%	19-May-14 A	27-May-14 A	
NAB0745-new	60 cm Conc. Pipes for drainage from Sta.0+030 to Sta.0+180	12d	50%	15-Jun-14 A	12-Jul-14	58d
NAB0720	60 cm Conc. Pipes for drainage from A1+300 to A1+500 L= 200 m	12d	50%	26-Jun-14 A	12-Jul-14	34d
NAB0710	60 cm Conc. Pipes for drainage from A1+100 to A1+260 L= 160 m	12d	50%	28-Jun-14 A	12-Jul-14	37d
New Conc.Pipe Culvert Dia. 80 cm and Box Culvert RHS Phase One		12d		16-Jan-14 A	04-Jun-14 A	
NAB0750	New Conc.Pipe Culvert Dia. 80 cm @ St. A2+220 length L= 55 m	12d	100%	16-Jan-14 A	13-Feb-14 A	
NAB0790	New double box culvert 2 (2*2) @ St. A3+610 length L= 66 m	12d	100%	15-May-14 A	04-Jun-14 A	
New Conc.Pipe Culvert Dia. 80 cm and Box Culvert RHS Phase Two		0d				0d
Connection and Valves Chambers		0d				0d
Stone Walls		36d		16-Apr-14 A	13-May-14 A	
NAB1110	Stone wall from (Sta.A2+980 to Sta.A3+010 LHS) L=30 m (LHS)	12d	100%	16-Apr-14 A	21-Apr-14 A	
NAB1120	Stone wall from (A3+162 to Sta.A3+189) L=27 m (LHS)	12d	100%	16-Apr-14 A	21-Apr-14 A	
NAB1121-new	Stone Wall from Sta.3+376 to Sta.3+402 L= 26 m (LHS)	5d	100%	24-Apr-14 A	28-Apr-14 A	
NAB1160	Stone wall from A4+710 to A4+780 L=70 m (LHS)	12d	100%	12-May-14 A	13-May-14 A	
Otheres		93d		19-Feb-14 A	23-Jun-14 A	
NAB5050-new	Street Lighting Poles from Sta.2+033 to Sta.2+983	12d	100%	19-Feb-14 A	25-May-14 A	
NAB5055-new	Street Lighting Poles from Sta.1+500 to Sta.2+000 &from sta.3+000 to Sta.4+850	12d	100%	18-Jun-14 A	22-Jun-14 A	
NAB5060-new	Side Walk from sta.2+000 to sta.2+600	12d	100%	18-Jun-14 A	23-Jun-14 A	
PROJECT 01 Material Submittals		158d		25-Dec-13 A	12-Jul-14	178d
NAB1340	UPVC	12d	100%	25-Dec-13 A	13-Jan-14 A	
NAB1290	Concrete Pipes	12d	100%	25-Dec-13 A	15-Jan-14 A	
NAB1410	Prime Coat	12d	100%	25-Dec-13 A	05-Jan-14 A	
NAB1420	Tack Coat	12d	100%	25-Dec-13 A	05-Jan-14 A	
NAB1520	Cat eyes	12d	100%	25-Dec-13 A	05-Jan-14 A	
NAB1530	Thermoplastic paint	12d	100%	25-Dec-13 A	05-Jan-14 A	
NAB1560	Curbstone paint material	12d	100%	25-Dec-13 A	05-Jan-14 A	
NAB1445	Concrete joint sealant material	12d	100%	25-Dec-13 A	15-Jan-14 A	
NAB1440	Bituminous Wearing Course-Mix Design	12d	100%	30-Dec-13 A	09-Jan-14 A	
NAB1400	Curbstone	12d	100%	30-Dec-13 A	31-Dec-13 A	
NAB1430	Bituminous Binder Course-Mix Design	12d	100%	02-Jan-14 A	09-Jan-14 A	
NAB1550	Traffic sign	12d	100%	05-Jan-14 A	08-Jan-14 A	
NAB1270	Steel pipeline	12d	100%	19-Jan-14 A	27-Jan-14 A	
NAB1310	Base Course Source	12d	100%	22-Jan-14 A	26-Jan-14 A	
NAB1360	Bedding material	12d	100%	22-Jan-14 A	26-Jan-14 A	
NAB1350	Backfilling material	12d	100%	22-Jan-14 A	26-Jan-14 A	
NAB1280	Concrete Mix Design including Cement type	12d	100%	28-Jan-14 A	03-Feb-14 A	
NAB1370	Manholes and catch basin	12d	100%	04-Feb-14 A	11-Feb-14 A	
NAB1380	Cast iron manhole and catch basin cover	12d	100%	04-Feb-14 A	11-Feb-14 A	

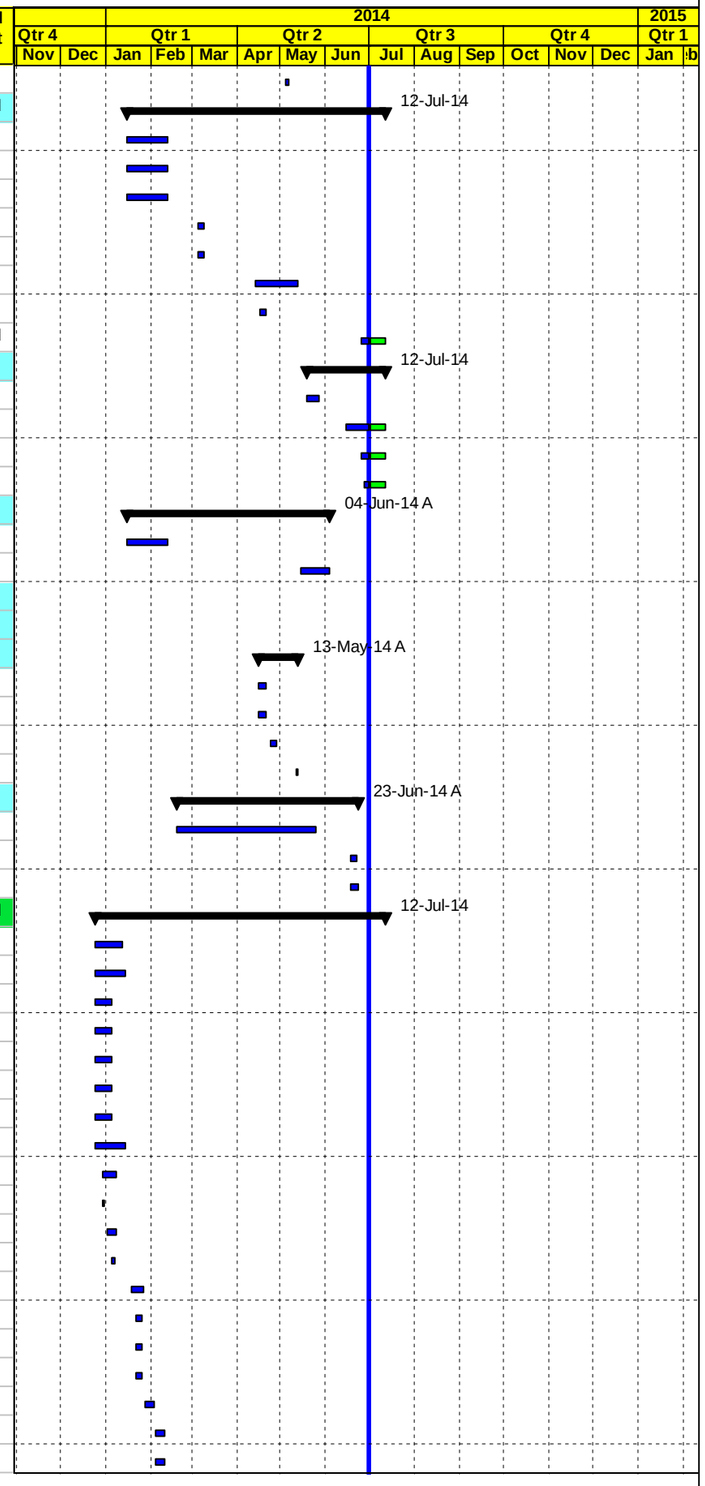

◇ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
NAB1573-new	Galvanized Malleable Iron Fittings up to 2 inch	12d	100%	17-Feb-14 A	25-Feb-14 A	
NAB1300	Steel Reinforcement	12d	100%	19-Feb-14 A	23-Feb-14 A	
NAB1564-new	Concrete Water Proofer for Manholes outside painting	12d	100%	19-Feb-14 A	23-Feb-14 A	
NAB1565	Street Lighting	12d	100%	23-Feb-14 A	02-Mar-14 A	
NAB1563-new	Epoxy Paint for Concrete protection	12d	100%	02-Mar-14 A	05-Mar-14 A	
NAB1565-new	Precast Concrete Curbstone & Edge beam	12d	100%	21-May-14 A	26-May-14 A	
NAB1567-new	Lamp,Cable and Cobra Pipe for street lighting	12d	100%	28-May-14 A	05-Jun-14 A	
NAB1566-new	Portland Cement Sulfate Resisting for concrete benching for manholes	12d	50%	28-May-14 A	12-Jul-14	133d
PROJECT 01 Procurements		97d		27-Jan-14 A	25-Jun-14 A	
NAB1580	Order steel pipes and fittings	0d	100%	27-Jan-14 A		
NAB1590	Start Delivery steel pipes and fittings	0d	100%		22-Mar-14 A	
NAB1600	Order Street Lighting Poles	0d	100%	25-Jun-14 A		
PROJECT 01 Construction		360d		23-Jan-14 A	24-Nov-14	44d
Phase One from A2+020 TO 5+450 closed /area B & A		306d		23-Jan-14 A	24-Nov-14	44d
Main Road From St. A2+020 To St. A2+500 LHS & RHS Area B		148d		23-Jan-14 A	04-Aug-14	126d
NAB1680	Maintain traffic control and safety plan ,Relocating utilities	148d	88.52%	23-Jan-14 A	04-Aug-14	126d
Excavation		107d		23-Jan-14 A	05-Jul-14	141d
NAB1690	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	100%	23-Jan-14 A	30-Mar-14 A	
NAB2620	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	28-Jan-14 A	05-Jul-14	141d
Storm System		74d		15-Feb-14 A	21-Apr-14 A	
NAB1710	60 cm Conc. Pipes for drainage W. manholes from A2+020 to A2+180 L= 160 m LHS	16d	100%	15-Feb-14 A	18-Feb-14 A	
NAB1740	60 cm Conc. Pipes for drainage W. manholes from A2+220 to A2+500 L= 280 m LHS	27d	100%	18-Feb-14 A	25-Feb-14 A	
NAB2630	New Conc.Pipe Culvert Dia. 80 cm with outlet @ St. A2+084 length L= 55 m RHS	18d	100%	05-Mar-14 A	06-Mar-14 A	
NAB1730	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	18d	100%	05-Apr-14 A	21-Apr-14 A	
NAB2640	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	14d	100%	05-Apr-14 A	20-Apr-14 A	
Water lines		37d		23-Mar-14 A	21-Apr-14 A	
NAB2962-new	12" Steel pipeline beit iba from st 2+220 To st 2+450 RHS	21d	100%	23-Mar-14 A	25-Mar-14 A	
NAB1720	3" Steel Water pipeline from St. A 2+020 to A 2+500 (LHS) L=480 m LHS	12d	100%	03-Apr-14 A	21-Apr-14 A	
Sewer line		42d		08-Feb-14 A	21-Apr-14 A	
NAB1700	12" Sewer line from St. A2+020 to St. A2+500 L=480 m LHS	25d	100%	08-Feb-14 A	25-Mar-14 A	
NAB1990-new	8" Sewer line (house connection from St. A2+020 to St. A2+500 LHS	11d	100%	08-Feb-14 A	21-Apr-14 A	
Concrete works		21d		08-Mar-14 A	30-Mar-14 A	
NAB2960-new	Conc. Retaining walls from A2+339 to A2+369 L= 30 m RHS	21d	100%	08-Mar-14 A	30-Mar-14 A	
Tooping and Basecourse		70d		11-Mar-14 A	03-Jul-14	142d
NAB1750	20 cm Thick Topping Layer LHS	13d	90%	11-Mar-14 A	03-Jul-14	132d
NAB2650	20 cm Thick Topping Layer RHS	13d	90%	25-Mar-14 A	03-Jul-14	139d
NAB2670	20 cm Thick Base Course- First Layer RHS	13d	90%	13-Apr-14 A	03-Jul-14	142d
NAB1780	20 cm Thick Base Course- First Layer LHS	13d	90%	15-Apr-14 A	03-Jul-14	142d
NAB2680	20 cm Thick Base Course- Second Layer RHS	13d	90%	17-Apr-14 A	03-Jul-14	139d
NAB1790	20 cm Thick Base Course- Second Layer LHS	13d	90%	20-Apr-14 A	03-Jul-14	56d
Asphalt binder		2d		24-Apr-14 A	28-Apr-14 A	
NAB2810-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+140 to St. 2+550 RHS	2d	100%	24-Apr-14 A	25-Apr-14 A	
NAB1980-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+140 to St. 2+570 width 6 m LHS	2d	100%	27-Apr-14 A	28-Apr-14 A	
Street Lighting Poles and Curbstone		5d		25-Jun-14 A	05-Jul-14	68d
NAB2690	Precast Conc. Curbstone for RHS (Mediane and side curb) RHS	5d	50%	25-Jun-14 A	05-Jul-14	68d
Main Road From St. A2+500 To St. A3+000 LHS & RHS Area A		174d		13-Feb-14 A	25-Aug-14	134d
NAB1820	Maintain traffic control and safety plan ,Relocating utilities	133d	73.55%	13-Feb-14 A	25-Aug-14	108d
Excavation		84d		22-Feb-14 A	05-Jul-14	141d
NAB2720	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	22-Feb-14 A	05-Jul-14	141d

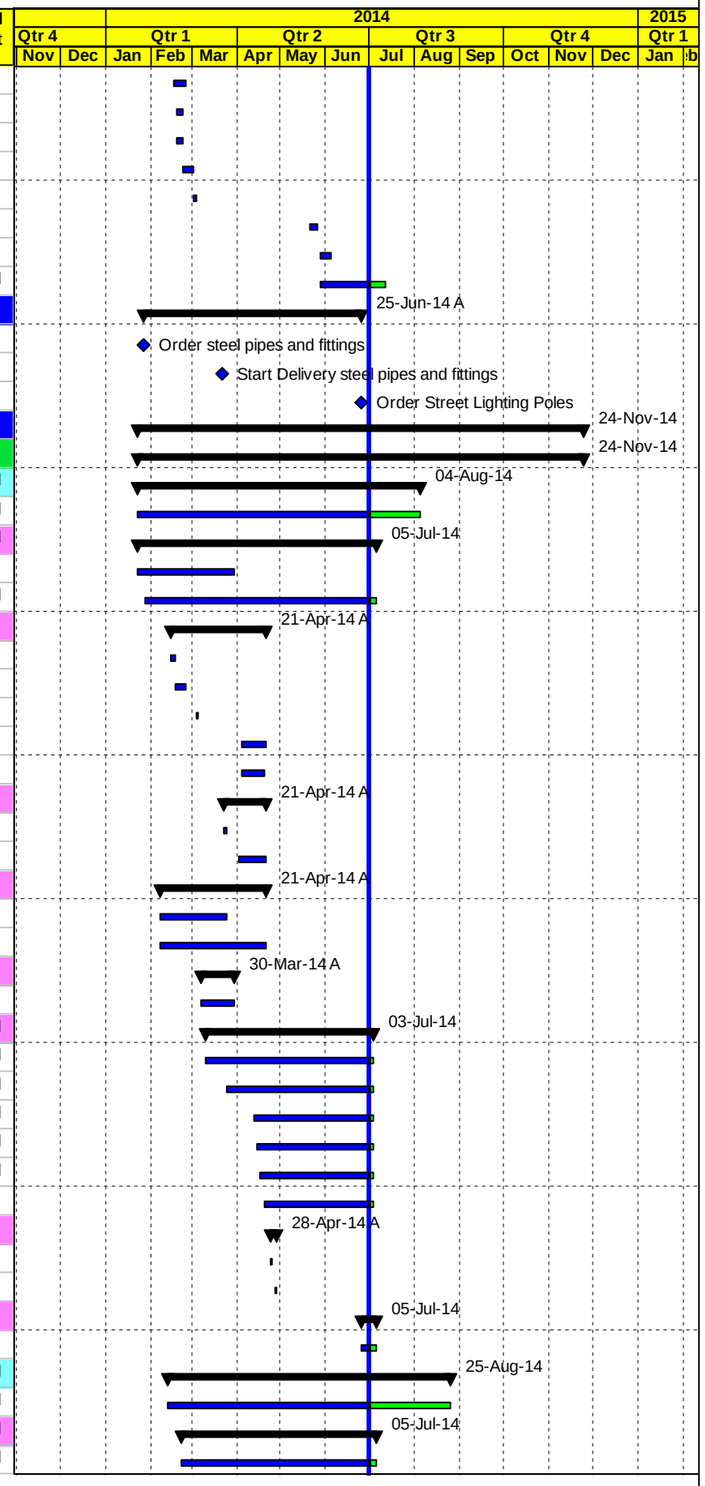

◇ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
NAB1830	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	90%	25-Feb-14 A	05-Jul-14	141d
Storm System		49d		23-Feb-14 A	15-May-14 A	
NAB1840	60 cm Conc. Pipes for drainage W. manholes from A2+500 to A2+620 L= 120 m LHS	11d	100%	23-Feb-14 A	11-Mar-14 A	
NAB1880	60 cm Conc. Pipes for drainage W. manholes from A2+640 to A2+740 L= 100 m LHS	12d	100%	15-Mar-14 A	15-Apr-14 A	
NAB1890	60 cm Conc. Pipes for drainage W. manholes from A2+860 to A2+980 L= 120 m LHS	10d	100%	17-Mar-14 A	26-Mar-14 A	
NAB2730	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	14d	100%	17-Apr-14 A	15-May-14 A	
NAB1860	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	16d	100%	24-Apr-14 A	30-Apr-14 A	
Water lines		43d		25-Mar-14 A	26-May-14 A	
NAB2726-new	12" Steel pipeline beit iba from st 2+450 To st 2+950 RHS	21d	100%	25-Mar-14 A	26-May-14 A	
NAB1850	3" Steel Water pipeline from St. A 2+500 to A 2+700 (LHS) L =200 M LHS	7d	100%	21-Apr-14 A	22-Apr-14 A	
NAB1921-new	3" Steel Water pipeline from St. A 2+900 to A 3+000 (LHS) L=100 m LHS	2d	100%	27-Apr-14 A	29-Apr-14 A	
Sewer line		16d		13-Feb-14 A	02-Jul-14	142d
NAB1870	12" Sewer line from St. A2+500 to St. A2+580 L=80 LHS	12d	90%	13-Feb-14 A	02-Jul-14	142d
NAB1841-new	8" Sewer line (house connection from St. A2+500 to St. A3+000 LHS	11d	90%	14-Apr-14 A	02-Jul-14	46d
Concrete works		21d		22-Mar-14 A	03-May-14 A	
NAB2722-new	Conc. Retaining walls from A2+475 to A2+515 L= 40 m RHS	21d	100%	22-Mar-14 A	29-Mar-14 A	
NAB2724-new	Conc. Retaining walls from A2+740 to A2+850 L= 110 m RHS	21d	100%	31-Mar-14 A	03-May-14 A	
NAB2725-new	Conc. Retaining walls from A2+880 to A2+916 L= 36 m RHS	21d	100%	14-Apr-14 A	03-May-14 A	
NAB2728-new	Conc. Retaining walls from A2+937 to A2+954 L= 17 m RHS	15d	100%	15-Apr-14 A	02-May-14 A	
NAB2730-new	Conc. Retaining walls from A2+965 to A2+980 L= 25 m RHS	15d	100%	16-Apr-14 A	03-May-14 A	
Tooping and Basecourse		58d		06-Mar-14 A	27-May-14 A	
NAB1900	20 cm Thick Topping Layer LHS	13d	100%	06-Mar-14 A	14-May-14 A	
NAB2760	20 cm Thick Topping Layer RHS	13d	100%	06-Mar-14 A	14-May-14 A	
NAB2780	20 cm Thick Base Course- First Layer RHS	13d	100%	13-Apr-14 A	21-Apr-14 A	
NAB2790	20 cm Thick Base Course- Second Layer RHS	13d	100%	17-Apr-14 A	28-Apr-14 A	
NAB1920	20 cm Thick Base Course- First Layer LHS	13d	100%	22-Apr-14 A	03-May-14 A	
NAB1950	20 cm Thick Base Course- Second Layer LHS	13d	100%	27-Apr-14 A	27-May-14 A	
Asphalt binder		2d		27-May-14 A	29-May-14 A	
NAB2820-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+540 to St. 2+950 RHS	2d	100%	27-May-14 A	28-May-14 A	
NAB1985-new	7 cm Asphalt Binder Course Including Prime Coat from St. 2+550 to St. 3+000 LHS width 6 m. LHS	2d	100%	28-May-14 A	29-May-14 A	
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A3+000 To St. A3+500 LHS & RHS Area A		158d		18-Mar-14 A	06-Sep-14	98d
NAB2000	Maintain traffic control and safety plan ,Relocating utilities	158d	71.46%	18-Mar-14 A	06-Sep-14	98d
Excavation		115d		18-Mar-14 A	05-Jul-14	141d
NAB2010	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	90%	18-Mar-14 A	05-Jul-14	141d
NAB2840	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	21d	90%	06-Apr-14 A	05-Jul-14	120d
Storm System		95d		18-Apr-14 A	03-Jul-14	70d
NAB2011-new	60 cm Conc. Pipes for drainage W. manholes from A2+980 to A3+120 L= 140 m LHS	18d	90%	18-Apr-14 A	03-Jul-14	70d
NAB2870	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	16d	100%	10-May-14 A	20-May-14 A	
NAB2030	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	16d	100%	15-May-14 A	21-May-14 A	
Water lines		46d		01-Apr-14 A	02-Jul-14	71d
NAB2849-new	12" Steel pipeline beit iba from st 2+950 To st 3+450 RHS	10d	100%	01-Apr-14 A	20-Apr-14 A	
NAB2961-new	3" Steel Water pipeline from St. A 3+000 to A 3+500 (LHS) L=500m LHS	10d	90%	27-Apr-14 A	02-Jul-14	71d
Concrete works		40d		18-Apr-14 A	02-Jul-14	77d
NAB2842-new	Conc. Retaining walls from A3+006 to A3+018 L=12 m RHS	12d	90%	18-Apr-14 A	02-Jul-14	77d
NAB2851-new	Conc. Retaining walls from A3+240 to A3+300 L=60m RHS	5d	100%	25-Apr-14 A	06-May-14 A	
NAB2850	Conc. Retaining walls from A3+180 to A3+240 L=60m RHS	12d	100%	29-Apr-14 A	07-May-14 A	
NAB2875-new	Conc. Retaining walls from A3+341 to A3+370 L=29m RHS	12d	100%	07-May-14 A	20-May-14 A	
Tooping and Basecourse		113d		01-May-14 A	12-Jul-14	138d

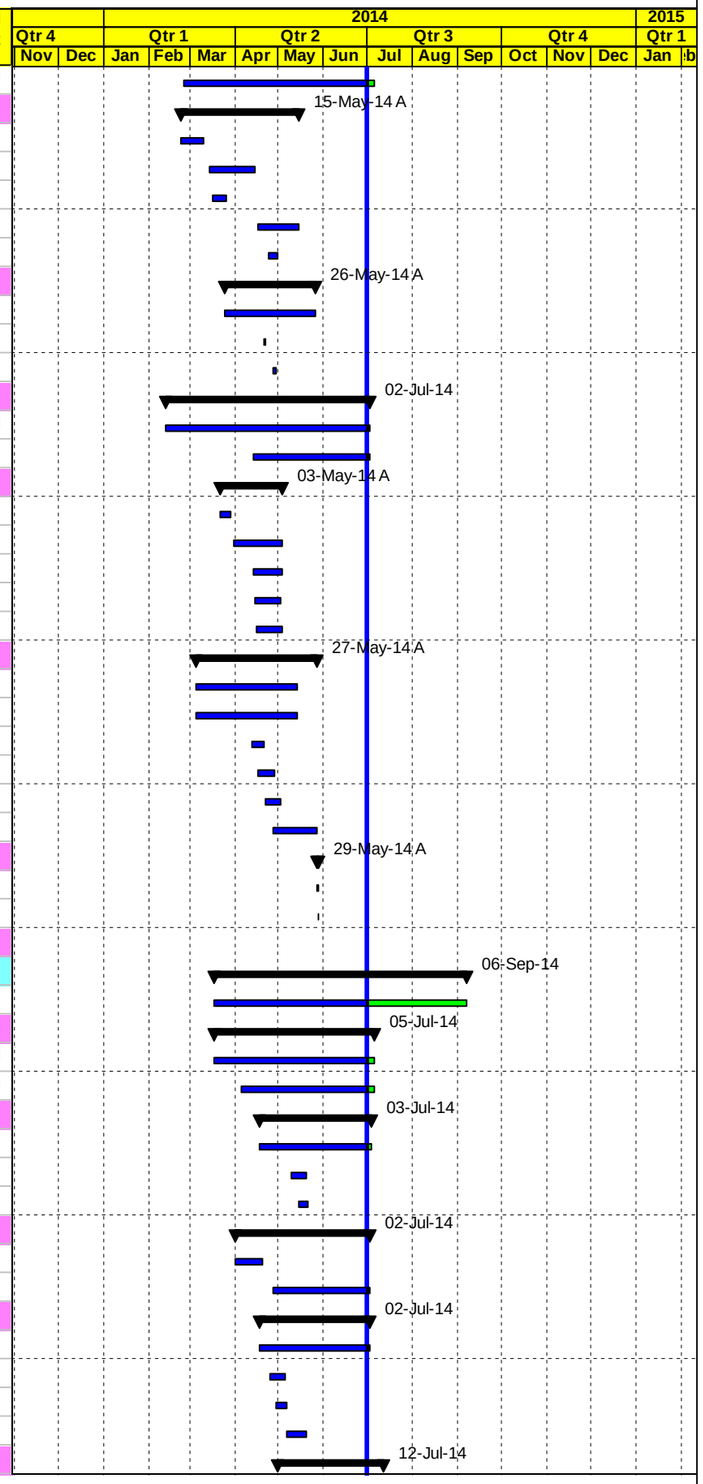

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
NAB2040	20 cm Thick Topping Layer LHS	13d	70%	01-May-14 A	08-Jul-14	139d
NAB2880	20 cm Thick Topping Layer RHS	13d	80%	03-May-14 A	06-Jul-14	141d
NAB2910	20 cm Thick Base Course- First Layer RHS	13d	80%	03-May-14 A	06-Jul-14	141d
NAB2070	20 cm Thick Base Course- First Layer LHS	13d	55%	05-May-14 A	12-Jul-14	138d
NAB2920	20 cm Thick Base Course- Second Layer RHS	13d	80%	10-May-14 A	06-Jul-14	75d
NAB2090	20 cm Thick Base Course- Second Layer LHS	13d	55%	17-May-14 A	12-Jul-14	66d
Asphalt binder		2d		27-May-14 A	29-May-14 A	
NAB2879-new	7 cm Asphalt Binder Course Including Prime Coat from St. 3+000 to St. 3+220 RHS.	2d	100%	27-May-14 A	28-May-14 A	
NAB2095-new	7 cm Asphalt Binder Course Including Prime Coat from St. 3+000 to St. 3+170 LHS width 6 m LHS	2d	100%	28-May-14 A	29-May-14 A	
Street Lighting Poles and Curbstone		12d		21-Apr-14 A	01-Jul-14	117d
NAB2060	Reconstruct stone wall from (A3+160 to A3+190) & (A3+240 to A3+282) L=72 m LHS	12d	95%	21-Apr-14 A	01-Jul-14	117d
Main Road St. A3+500 To St. A4+000 LHS & RHS Area A		197d		22-Apr-14 A	17-Sep-14	111d
NAB2130	Maintain traffic control and safety plan ,Relocating utilities	154d	64.22%	22-Apr-14 A	17-Sep-14	88d
Excavation		91d		29-Apr-14 A	21-Jun-14 A	
NAB2140	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	21d	100%	29-Apr-14 A	17-Jun-14 A	
NAB3010	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	20d	100%	08-May-14 A	21-Jun-14 A	
Storm System		86d		07-May-14 A	11-Aug-14	121d
NAB2150	60 cm Conc. Pipes for drainage W. manholes from A3+610 to A3+840 L= 230 m LHS	23d	85%	07-May-14 A	07-Jul-14	140d
NAB3030	16" UPVC pipes for drainage W. catch basin if needed along this segment RHS	18d	100%	10-Jun-14 A	16-Jun-14 A	
NAB2170	16" UPVC pipes for drainage W. catch basin if needed along this segment LHS	15d	100%	12-Jun-14 A	18-Jun-14 A	
NAB3020	New double box culvert 2 (2*2) @ St. A3+610 RHS length L= 28 m First part RHS	24d	5%	17-Jun-14 A	11-Aug-14	101d
NAB3040	New double box culvert 2 (2*2) @ St. A3+610 RHS length L= 28 m second part RHS	24d	5%	17-Jun-14 A	11-Aug-14	121d
Water lines		10d		22-Apr-14 A	02-Jul-14	142d
NAB3005-new	12" Steel pipeline beit iba from st 3+450 To st 3+950 RHS	10d	90%	22-Apr-14 A	02-Jul-14	142d
Sewer line		21d		31-May-14 A	10-Jun-14 A	
NAB2155-new	12" Sewer line from St. A4+007 to St. A4+260 L=260 m LHS	21d	100%	31-May-14 A	10-Jun-14 A	
Concrete works		73d		01-May-14 A	22-Jun-14 A	
NAB3015-new	Conc. Retaining walls from A3+560 to A3+590 L=30m RHS	15d	100%	01-May-14 A	24-May-14 A	
NAB3050	Conc. Retaining walls from A3+828 to A3+858 L= 30 m RHS	15d	100%	17-May-14 A	22-Jun-14 A	
NAB3025-new	Conc. Retaining walls from A3+650 to A3+690 L=40m RHS	15d	100%	21-May-14 A	17-Jun-14 A	
Tooping and Basecourse		82d		24-May-14 A	20-Jul-14	71d
NAB3060	20 cm Thick Topping Layer RHS	13d	100%	24-May-14 A	22-Jun-14 A	
NAB2190	20 cm Thick Topping Layer LHS	13d	100%	01-Jun-14 A	21-Jun-14 A	
NAB2210	20 cm Thick Base Course- First Layer LHS	13d	100%	05-Jun-14 A	25-Jun-14 A	
NAB3080	20 cm Thick Base Course- First Layer RHS	13d	100%	05-Jun-14 A	28-Jun-14 A	
NAB2220	20 cm Thick Base Course- Second Layer LHS	13d	20%	27-Jun-14 A	20-Jul-14	71d
NAB3090	20 cm Thick Base Course- Second Layer RHS	13d	20%	27-Jun-14 A	20-Jul-14	71d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A4+000 To St. A4+500 LHS & RHS Area A		205d		25-Apr-14 A	29-Sep-14	99d
NAB2260	Maintain traffic control and safety plan ,Relocating utilities	161d	59.57%	25-Apr-14 A	29-Sep-14	78d
Excavation		28d		14-May-14 A	14-Jul-14	136d
NAB3114	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	15d	55%	14-May-14 A	13-Jul-14	0d
NAB2270	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	15d	50%	10-Jun-14 A	14-Jul-14	136d
Storm System		12d		15-Jun-14 A	20-Jul-14	127d
NAB3150	New Conc.Pipe Culvert Dia. 80 cm @ St. A4+240 length L= 12 m RHS	12d	15%	15-Jun-14 A	20-Jul-14	127d
Water lines		10d		25-Apr-14 A	25-May-14 A	
NAB3099-new	12" Steel pipeline beit iba from st 3+950 To st 4+450 RHS	10d	100%	25-Apr-14 A	25-May-14 A	
Sewer line		0d				0d

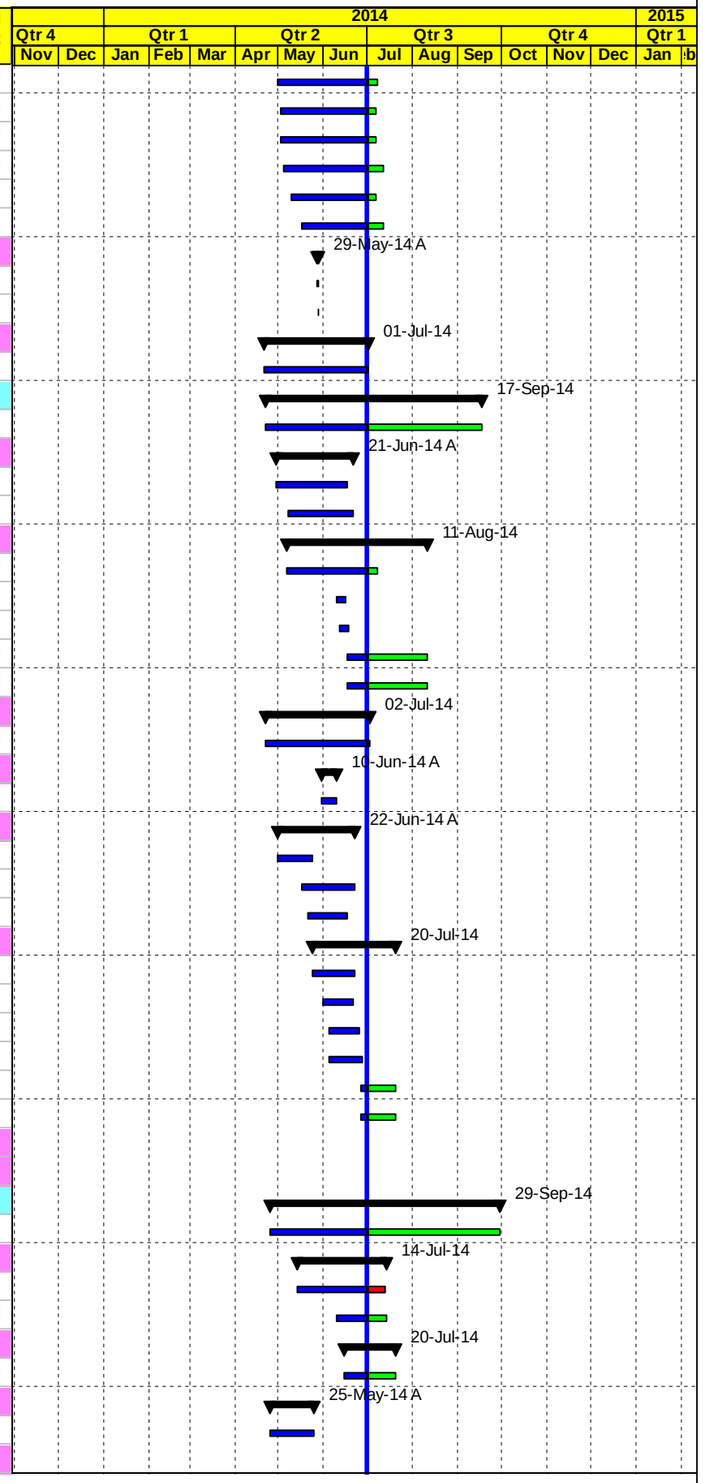

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Tooping and Basecourse		56d		05-Jun-14 A	23-Jul-14	131d
NAB3160	20 cm Thick Topping Layer RHS	13d	30%	05-Jun-14 A	17-Jul-14	134d
NAB3180	20 cm Thick Base Course- First Layer RHS	13d	30%	10-Jun-14 A	17-Jul-14	134d
NAB2310	20 cm Thick Topping Layer LHS	13d	30%	11-Jun-14 A	17-Jul-14	134d
NAB2320	20 cm Thick Base Course- First Layer LHS	13d	7%	15-Jun-14 A	23-Jul-14	131d
NAB3190	20 cm Thick Base Course- Second Layer RHS	13d	20%	22-Jun-14 A	20-Jul-14	81d
NAB2330	20 cm Thick Base Course- Second Layer LHS	13d	15%	28-Jun-14 A	21-Jul-14	81d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A4+500 To St. A5+000 LHS & RHS Area A		134d		22-May-14 A	24-Nov-14	30d
NAB2370	Maintain traffic control and safety plan ,Relocating utilities	101d	0%	22-May-14 A	24-Nov-14	26d
Excavation		0d				0d
Storm System		0d				0d
Water lines		10d		22-May-14 A	05-Jul-14	56d
NAB3350-new	12" Steel pipeline beit iba from st 4+450 To st 4+950 RHS	10d	75%	22-May-14 A	05-Jul-14	56d
Sewer line		0d				0d
Concrete works		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A5+000 To St. A5+450 LHS & RHS Area A		0d				0d
Excavation		0d				0d
Storm System		0d				0d
Water lines		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Phase Two closed (RHS & LHS) from St. A0+000 - A2+020		146d		24-Apr-14 A	24-Sep-14	67d
Main Road St. A2+020 To St. A1+500 RHS & LHS Area B		146d		24-Apr-14 A	24-Sep-14	67d
NAB4030	Maintain traffic control and safety plan ,Relocating utilities	107d	43.18%	24-Apr-14 A	24-Sep-14	51d
Excavation		69d		24-Apr-14 A	08-Jul-14	72d
NAB4790	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade LHS	14d	70%	24-Apr-14 A	08-Jul-14	72d
NAB4040	Demo. Exist. Struc. ,Road excavation including (cut/fill) to required subgrade RHS	20d	80%	08-Jun-14 A	08-Jul-14	0d
Storm System		30d		18-Jun-14 A	06-Jul-14	55d
NAB4060	New Conc.Pipe Culvert Dia.80 cm @ St. A1+690 length L= 46 m RHS	18d	100%	18-Jun-14 A	21-Jun-14 A	
NAB4070	60 cm Conc. Pipes for drainage W. manholes from A1+690 to A2+020 L= 330 m RHS	29d	90%	18-Jun-14 A	06-Jul-14	55d
Water lines		0d				0d
Sewer line		0d				0d
Concrete works		21d		15-Jun-14 A	24-Jun-14 A	
NAB4680-new	Conc. Retaining walls from A1+860 to A1+935 L=75m RHS	21d	100%	15-Jun-14 A	24-Jun-14 A	
NAB4685-new	Conc. Retaining walls from A1+720 to A1+750 L=30m RHS	21d	100%	17-Jun-14 A	24-Jun-14 A	
Tooping and Basecourse		8d		21-Jun-14 A	09-Jul-14	51d
NAB4100	20 cm Thick Topping Layer RHS	8d	40%	21-Jun-14 A	09-Jul-14	51d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A1+500 To St. A1+000 RHS & LHS Area C		0d				0d
Excavation		0d				0d
Storm System		0d				0d
Water lines		0d				0d

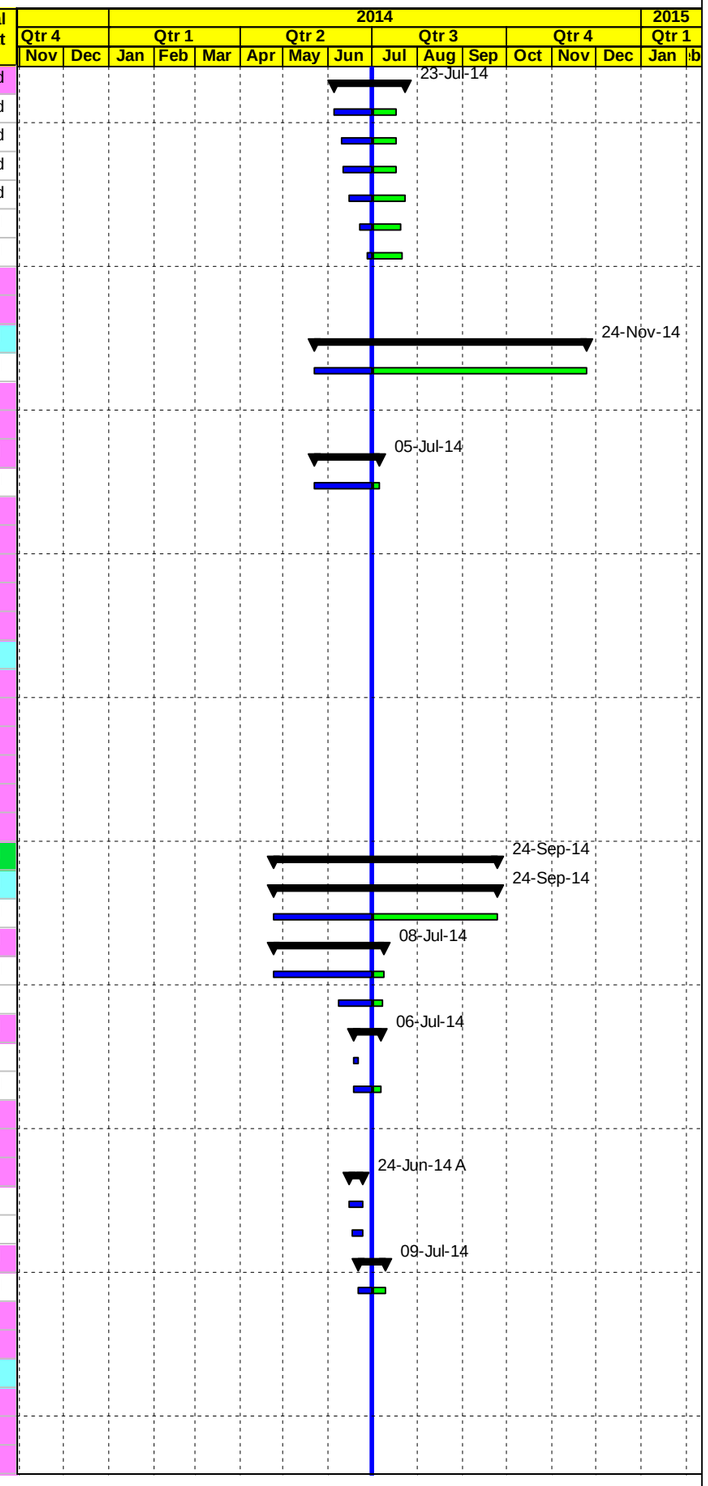

◆ Milestone Early Bar
Actual Work
◆ Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Concrete works		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road St. A1+000 To St. A0+500 RHS & LHS Area C		0d				0d
Excavation		0d				0d
Storm System		0d				0d
Water lines		0d				0d
Sewer line		0d				0d
Concrete works		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Main Road From St. A0+500 To St. A0+000 RHS & LHS Area C		0d				0d
Excavation		0d				0d
Storm System		0d				0d
Water lines		0d				0d
Sewer line		0d				0d
Tooping and Basecourse		0d				0d
Asphalt binder		0d				0d
Street Lighting Poles and Curbstone		0d				0d
Phase Three Seg. B from sta.B0+000 to B0+399 Total Close (Area B)		0d				0d
Temporary Detours		64d		12-Apr-14 A	15-Apr-14 A	
NAB4915	Milling for detours Sara	3d	100%	12-Apr-14 A	12-Apr-14 A	
NAB4879	5 cm thick Wearing Course Including Prime Coat for temporary detours (Sara & Beit Iba)	2d	100%	12-Apr-14 A	15-Apr-14 A	
Miscellaneous activities - If any as location is not determined yet		0d				0d
Asphalt and Miscellaneous Works		0d				0d
PROJECT 01 Post Construction Phase		0d				0d
PROJECT 02 Deir Sharaf Tulkarem Road		255d		03-Dec-13 A	03-Aug-14	156d
PROJECT 02 Pre Construction Phase		40d		03-Dec-13 A	05-Feb-14 A	
PROJECT 02 Conformed Drawings and Coordination		40d		03-Dec-13 A	05-Feb-14 A	
DSR1010	Final for Construction Drawing (Conformed)	0d	100%	03-Dec-13 A		
DSR1000	Coordination with Israeli authorities for approval and permit area C Project 02	40d	100%	03-Dec-13 A	05-Feb-14 A	
PROJECT 02 Mobilization		19d		04-Dec-13 A	20-Jan-14 A	
DSR1060	Site Hand Over	1d	100%	04-Dec-13 A	04-Dec-13 A	
DSR1070	Checking With CMC Existing-Bench Marks, Survey Control Points	2d	100%	04-Dec-13 A	04-Dec-13 A	
DSR1050	Mobilization Total Cost (4.0%)	19d	100%	04-Dec-13 A	20-Jan-14 A	
DSR1080	Start Preparation Construction Submittals (Survey plan , Shop Drawings & Materials)	12d	100%	16-Dec-13 A	04-Jan-14 A	
DSR1090	Install Temporary Project Sign	2d	100%	20-Jan-14 A	20-Jan-14 A	
PROJECT 02 Construction Phase		227d		25-Dec-13 A	03-Aug-14	156d
PROJECT 02 Construction Submittals		158d		25-Dec-13 A	12-Jul-14	137d
PROJECT 02 Shop Drawing Submittals		158d		15-Jan-14 A	12-Jul-14	137d
Plan Profile and Cross Sections		158d		15-Jan-14 A	12-Jul-14	137d
DSR1140	From St. 0+100 To St. 0+700	12d	100%	15-Jan-14 A	09-Feb-14 A	
DSR1150	From St. 0+700 To St. 1+200	12d	100%	02-Mar-14 A	24-Apr-14 A	
DSR1160	From St. 1+200 To St. 1+800	12d	100%	08-Apr-14 A	09-Apr-14 A	
DSR1180	From St. 1+800 To St. 2+100	12d	100%	27-Apr-14 A	29-Apr-14 A	
DSR1190	from Sta. 2+100 to Sta. 2+540	12d	100%	08-May-14 A	15-May-14 A	
DSR1200-new	Simple Access at Sta.0+170 LHS ,0+360 RHS , 0+430 RHS,0+930 RHS,0+990 RHS,1+100 LHS,1+439,1+460 LHS,1	12d	50%	28-Jun-14 A	12-Jul-14	137d

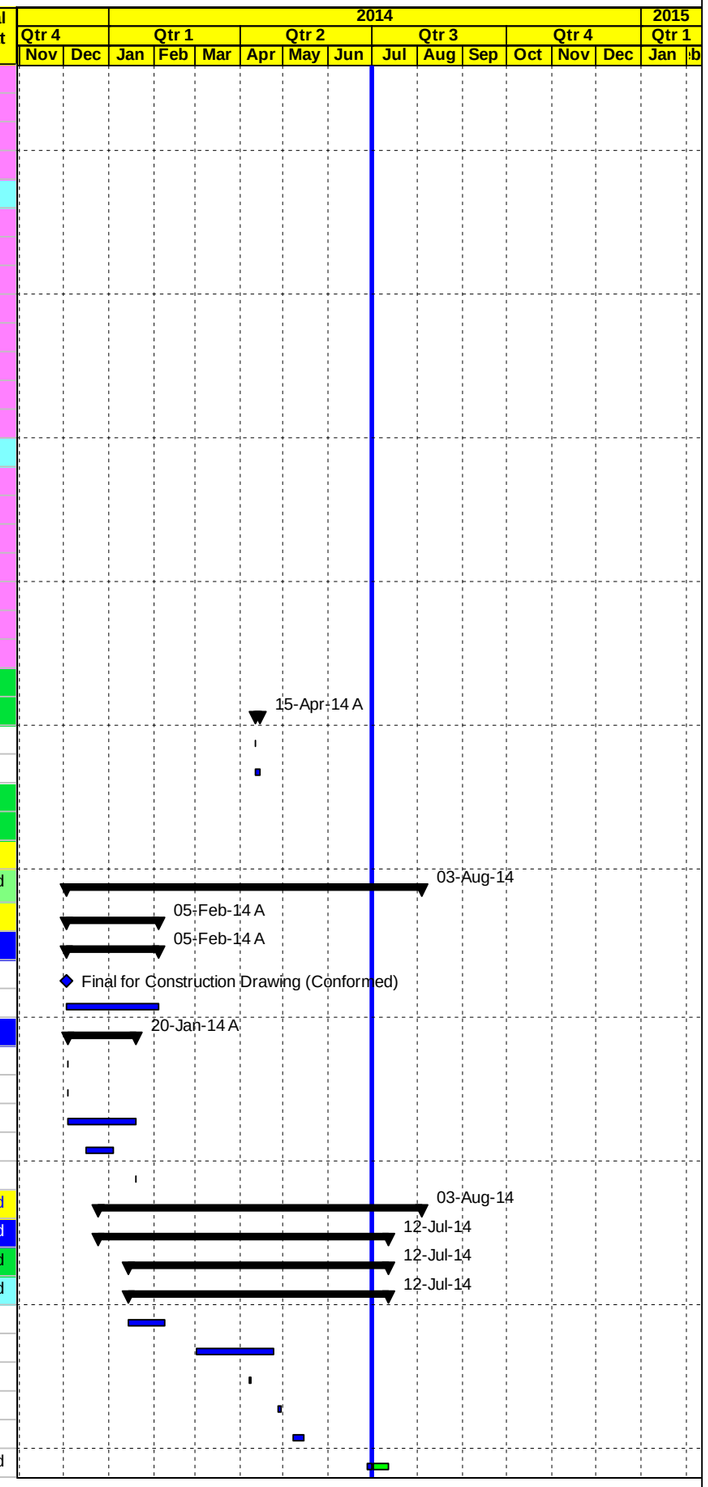

◇ Milestone Early Bar
Actual Work
◆ Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Water Line		12d		12-Jun-14 A	22-Jun-14 A	
DSR1175-new	Water Pipeline from Sta.0+410 to Sta.1+100 (3")	12d	100%	12-Jun-14 A	22-Jun-14 A	
Culverts		26d		30-Apr-14 A	08-Jun-14 A	
DSR1210	Pipe Culvert 1000mm @ St.0+860 length 15 m	12d	100%	30-Apr-14 A	07-May-14 A	
DSR1220	Pipe Culvert 1000mm @ St. 1+480 length 16 m	12d	100%	19-May-14 A	21-May-14 A	
DSR1230	Double Pipe Culvert at Sta.1+995	12d	100%	22-May-14 A	08-Jun-14 A	
Concrete Walls		12d		26-May-14 A	29-Jun-14 A	
DSR1245-new	Retaining Wall from Sta.1+300 to Sta.1+310 LHS L= 10 m and from Sta.1+700 to Sta.1+760 LHS L= 60 m	12d	100%	26-May-14 A	28-May-14 A	
DSR1250-new	Retaining Wall from Sta.1+475 to Sta.1+500 LHS	12d	100%	27-May-14 A	29-Jun-14 A	
Otheres		38d		12-Jun-14 A	12-Jul-14	25d
DSR1255	Ditch and Concrete Step Barrier from Sta.0+000 to Sta.2+180	12d	100%	12-Jun-14 A	17-Jun-14 A	
DSR1365-new	Directional Signs	12d	50%	01-Jul-14 A	12-Jul-14	25d
PROJECT 02 Material Submittals		73d		25-Dec-13 A	25-Feb-14 A	
DSR1560	Cat eyes	12d	100%	25-Dec-13 A	05-Jan-14 A	
DSR1565	Thermoplastic paint	12d	100%	25-Dec-13 A	05-Jan-14 A	
DSR1575	Curbstone paint material	12d	100%	25-Dec-13 A	05-Jan-14 A	
DSR1550	Traffic sign	12d	100%	25-Dec-13 A	05-Jan-14 A	
DSR1460	Prime Coat	12d	100%	25-Dec-13 A	05-Jan-14 A	
DSR1470	Tack Coat	12d	100%	25-Dec-13 A	05-Jan-14 A	
DSR1540	Guard Rail	12d	100%	29-Dec-13 A	25-Feb-14 A	
DSR1450	Curbstone	12d	100%	30-Dec-13 A	31-Dec-13 A	
DSR1400	Pipe Culverts	12d	100%	30-Dec-13 A	05-Feb-14 A	
DSR1382-New	Single size aggregate material source	12d	100%	22-Jan-14 A	26-Jan-14 A	
DSR1384-New	Bedding (somsom)	12d	100%	22-Jan-14 A	26-Jan-14 A	
DSR1380	Base Course Source and Topping	12d	100%	22-Jan-14 A	26-Jan-14 A	
DSR1573	Concrete joint sealant material	12d	100%	03-Feb-14 A	05-Feb-14 A	
DSR1390	Concrete Mix Design including cement type	12d	100%	03-Feb-14 A	05-Feb-14 A	
DSR1420	Steel Reinforcement	12d	100%	19-Feb-14 A	23-Feb-14 A	
DSR1480	Bituminous Wearing Course-Mix Design	12d	100%	19-Feb-14 A	23-Feb-14 A	
PROJECT 02 Construction		167d		05-Feb-14 A	03-Aug-14	156d
PROJECT 02 Implement traffic control		0d		05-Feb-14 A	22-Feb-14 A	
DSR1620	Implement traffic control & safety Plan phase1,2 & 3	0d	100%	05-Feb-14 A	22-Feb-14 A	
Phase #1 Totally closed from St. 0+100 To St. 2+180 Area C		154d		15-Feb-14 A	07-Jul-14	183d
From St. 0+100 To St. 0+700 Area C		106d		15-Feb-14 A	05-Jun-14 A	
DSR1660	Relocation Exist. Utilities , Maintain traffic control & safety Plan (totally closed)	53d	100%	15-Feb-14 A	21-May-14 A	
DSR1670	Divert Wadi and Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	22d	100%	23-Feb-14 A	10-Apr-14 A	
DSR1690	20 cm Thick Topping Layer/ Pulverization	14d	100%	11-Mar-14 A	14-Apr-14 A	
DSR1670-new	Filling horizontal Layers	9d	100%	15-Mar-14 A	24-Mar-14 A	
DSR1700	20 cm Thick Base Course- First Layer	14d	100%	06-Apr-14 A	25-Apr-14 A	
DSR1750-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 0+440	14d	100%	20-Apr-14 A	20-Apr-14 A	
DSR1755-new	8" UPVC for Sewer Pipe Line at station 0+440	14d	100%	22-Apr-14 A	23-Apr-14 A	
DSR1760-new	1000 mm Dia Sewer Manhole at station 0+440	14d	100%	22-Apr-14 A	23-Apr-14 A	
DSR1710	20 cm Thick Base Course- Second Layer	14d	100%	17-May-14 A	05-Jun-14 A	
From St.0+700 To St. 1+280 Area C		132d		13-Mar-14 A	07-Jul-14	183d
DSR1720	Relocation Exist. Utilities , Maintain traffic control & safety Plan (totally closed)	60d	100%	13-Mar-14 A	31-May-14 A	
DSR1730	Divert Wadi and Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	21d	100%	15-Mar-14 A	22-Apr-14 A	
DSR1731-new	Filling horizontal Layers	9d	100%	08-Apr-14 A	12-Apr-14 A	
DSR1755	20 cm Thick Topping Layer/ Pulverization	14d	100%	10-Apr-14 A	23-Apr-14 A	
DSR1780	20 cm Thick Base Course- First Layer	14d	100%	16-Apr-14 A	07-May-14 A	

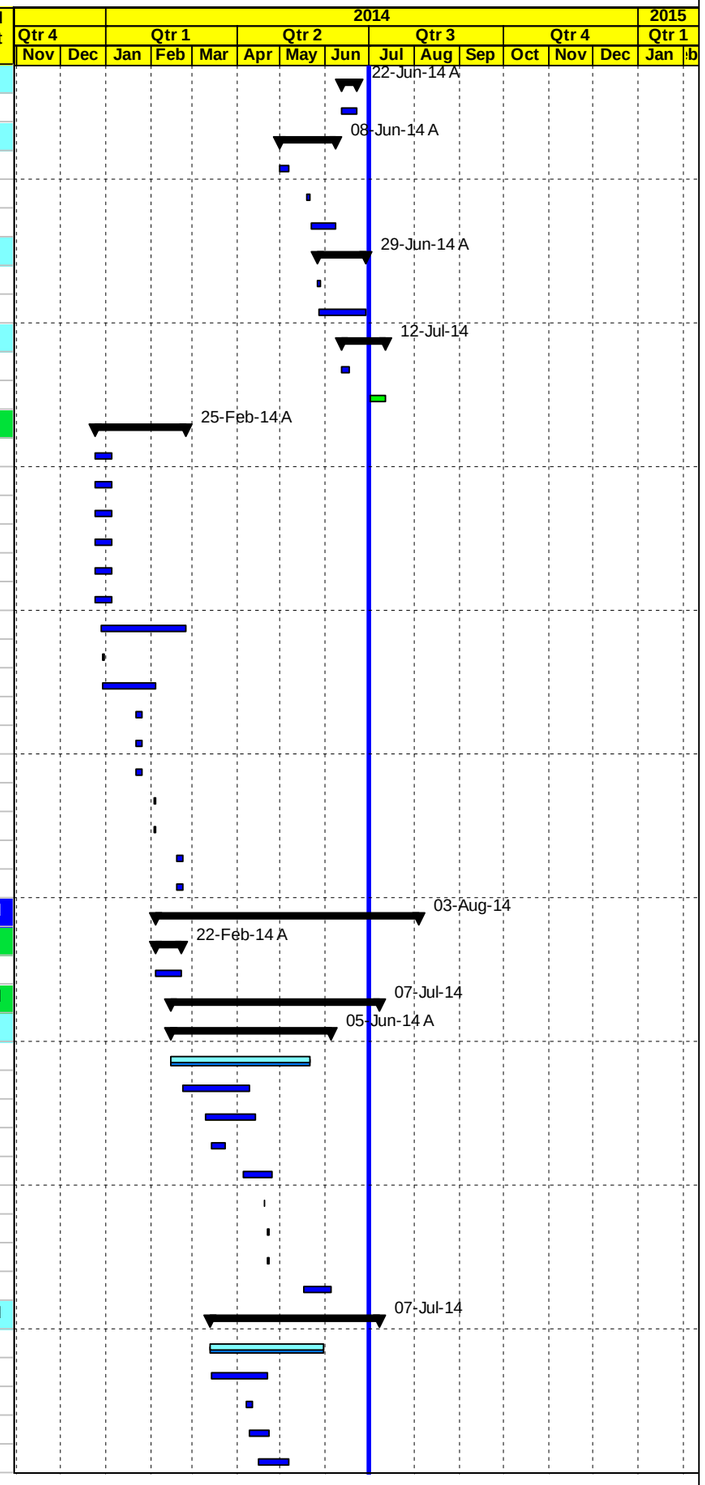

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
03-Jul-14			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO14
Multiple Roads Project North (II)

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DSR1785-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 0+720	13d	100%	20-Apr-14 A	20-Apr-14 A	
DSR1790-new	6" UPVC for ROAD CROSSING (SLEEVES) at station 1+000	12d	100%	20-Apr-14 A	20-Apr-14 A	
DSR1795-new	8" UPVC for Sewer Pipe Line at station 1+000	13d	100%	22-Apr-14 A	23-Apr-14 A	
DSR1796-new	8" UPVC for Sewer Pipe Line at station 1+100	13d	100%	22-Apr-14 A	23-Apr-14 A	
DSR1797-new	8" UPVC for Sewer Pipe Line at station 1+300	13d	100%	22-Apr-14 A	23-Apr-14 A	
DSR1798-new	1000 mm Dia Sewer Manhole at station 1+000 ,1+100,1+300	12d	100%	22-Apr-14 A	23-Apr-14 A	
DSR1750	New Pipe Culvert 800mm @ St. 0+780	12d	70%	15-May-14 A	07-Jul-14	140d
DSR1790	20 cm Thick Base Course- Second Layer	14d	100%	19-May-14 A	16-Jun-14 A	
Asphalt Works From St. 0+100 To St. 1+280		6d		06-Jun-14 A	19-Jun-14 A	
DSR1800	7 cm Asphalt Binder Course Including Prime Coat	6d	100%	06-Jun-14 A	19-Jun-14 A	
From St. 1+280 To St. 1+730 Area C		146d		13-Apr-14 A	03-Jul-14	188d
DSR1810	Relocation Exist. Utilities ,Maintain traffic control & safety Plan (totally closed)	60d	100%	13-Apr-14 A	21-Jun-14 A	
DSR1850	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	17d	100%	15-Apr-14 A	05-May-14 A	
DSR1900	20 cm Thick Topping Layer/ Pulverization	13d	100%	29-Apr-14 A	18-May-14 A	
DSR1950-new	Filling horizontal Layers	9d	100%	01-May-14 A	09-May-14 A	
DSR1910	20 cm Thick Base Course- First Layer	13d	100%	24-May-14 A	19-Jun-14 A	
DSR1880	Pipe Culvert 1000mm @ St. 1+480 length 16 m	12d	100%	27-May-14 A	27-May-14 A	
DSR1870	Retaining wall from St. 1+470to 1+505 LHS	22d	100%	04-Jun-14 A	21-Jun-14 A	
DSR1920	20 cm Thick Base Course- Second Layer	13d	100%	11-Jun-14 A	21-Jun-14 A	
DSR1930	7 cm Asphalt Binder Course Including Prime Coat	2d	26.98%	18-Jun-14 A	03-Jul-14	142d
From St. 1+730 To St. 2+180 Area C		148d		01-May-14 A	06-Jul-14	38d
DSR1940	Relocation Exist. Utilities , Maintain traffic control & safety Plan (totally closed)	50d	100%	01-May-14 A	23-Jun-14 A	
DSR1980	Road Excavation Including (Cut/Fill) Up to Finish Sub Grade Level	19d	100%	03-May-14 A	22-May-14 A	
DSR2030-new	Filling horizontal Layers	9d	100%	10-May-14 A	25-May-14 A	
DSR2020	20 cm Thick Topping Layer/ Pulverization	13d	100%	15-May-14 A	03-Jun-14 A	
DSR2030	20 cm Thick Base Course- First Layer	13d	100%	01-Jun-14 A	23-Jun-14 A	
DSR1990	Pipe Culvert 600mm @ St. 1+995	9d	70%	04-Jun-14 A	06-Jul-14	22d
DSR2265-new	Retaining wall from St. 1+665to 1+760 LHS	12d	88.99%	05-Jun-14 A	03-Jul-14	17d
DSR2040	20 cm Thick Base Course- Second Layer	13d	100%	07-Jun-14 A	23-Jun-14 A	
DSR2050	7 cm Asphalt Binder Course Including Prime Coat	2d	31.98%	23-Jun-14 A	03-Jul-14	15d
Phase #2 From St. 0+000 to 0+100		36d		22-May-14 A	03-Aug-14	0d
DSR2060	Relocation Exist. Utilities , Maintain traffic control & safety Plan (RHS&LHS)	36d	55.56%	22-May-14 A	03-Aug-14	0d
Miscellaneous Works		14d		27-May-14 A	02-Jul-14	17d
DSR1885-new	Concrete step barrier	13d	90.99%	27-May-14 A	02-Jul-14	17d
DSR1765-new	Concrete Ditch from St. 0+460 +860	14d	100%	27-Jun-14 A	27-Jun-14 A	
PROJECT 02 Post Construction Phase		0d				0d
Post Construction Phase		0d				0d
Post Submittals		0d				0d

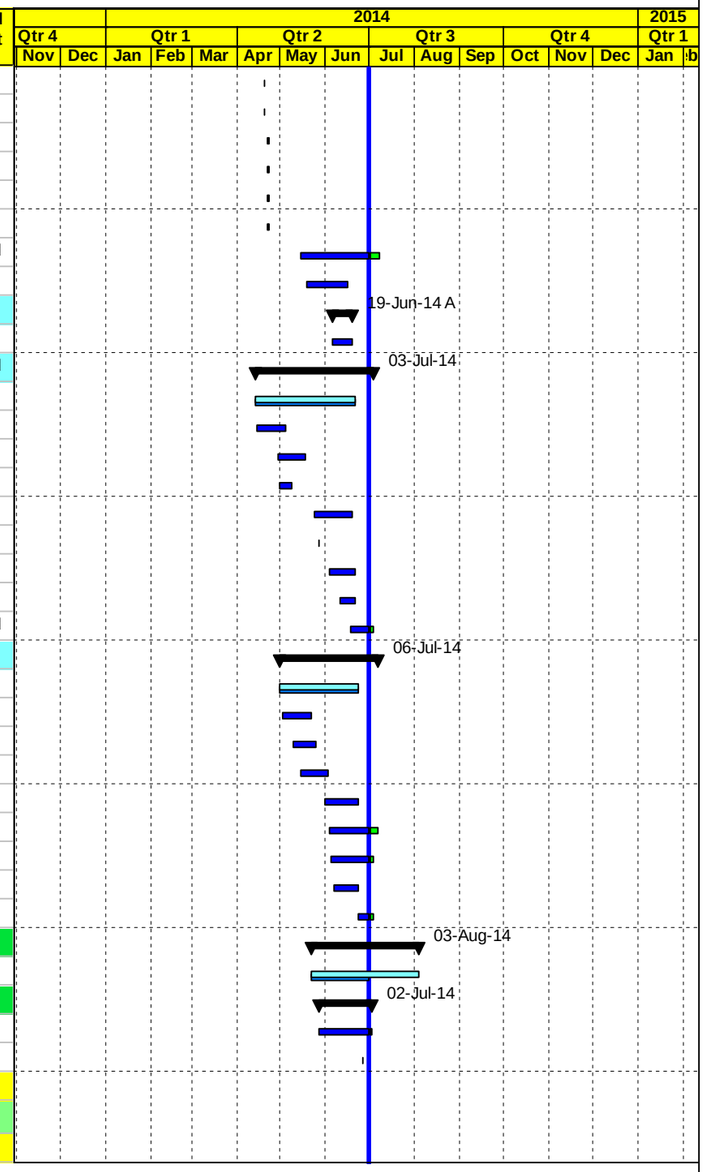

◇ Milestone Early Bar
Actual Work
◆ Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
03-Jul-14			

C | Progress S-Curve Versus Actual

BL2 is proposed by the Contractor considering the potential VO#03 and subject to USAID approval.

Construction Progress S-Curve

Total Contract Value	**$**	**16,495,593**
Total Contract Value (Day Work Not Included):	**$**	**16,195,593**
Total Contract Value (VO3-BL2):	**$**	**15,007,339**
Project Duration :	**365 Calender Days**	
Time Extension	**35 Calender Days**	
Revised Project Duration :	**400 Calender Days**	
NTP Date:	**3-Dec-13**	

*** Day Work Not Included**

	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	June. 2014	July. 2014	August. 2014	September. 2014	October. 2014	November. 2014	December. 2014	January. 2015	TOTAL
Planned Value	$ 517,406	$ 124,250	$ 361,014	$ 886,265	$ 1,739,223	$ 1,847,417	$ 2,293,757	$ 1,891,477	$ 1,816,718	$ 926,901	$ 795,463	$ 2,870,274	$ 125,430		$ 16,195,593
Planned Value (CUM)	$ 517,406	$ 641,656	$ 1,002,670	$ 1,888,935	$ 3,628,158	$ 5,475,574	$ 7,769,331	$ 9,660,808	$ 11,477,525	$ 12,404,427	$ 13,199,889	$ 16,070,163	$ 16,195,593	$ 16,195,593	
% Planned	3.2%	0.8%	2.23%	5.5%	10.7%	11.4%	14.2%	11.7%	11.2%	5.7%	4.9%	17.7%	0.8%	0.0%	**100%**
% Planned (CUM)	3.19%	3.96%	6.2%	11.7%	22.4%	33.8%	48.0%	59.7%	70.9%	76.6%	81.5%	99.2%	100.0%	100.0%	
Planned Value (Baseline2)	$ 483,829	$ 222,060	$ 206,794	$ 394,566	$ 1,070,404	$ 811,033	$ 1,118,261	$ 1,726,814	$ 2,348,704	$ 1,466,122	$ 886,139	$ 1,023,101	$ 3,124,081	$ 125,431	**$ 15,007,339**
Planned Value (CUM)	$ 483,829	$ 705,889	$ 912,683	$ 1,307,249	$ 2,377,653	$ 3,188,686	$ 4,306,947	$ 6,033,761	$ 8,382,465	$ 9,848,587	$ 10,734,726	$ 11,757,827	$ 14,881,908	$ 15,007,339	
% Planned	3.2%	1.5%	1.4%	2.6%	7.1%	5.4%	7.5%	11.5%	15.7%	9.8%	5.9%	6.8%	20.8%	0.8%	**100.00%**
% Planned (CUM) BL2	3.2%	4.7%	6.1%	8.7%	15.8%	21.2%	28.7%	40.2%	55.9%	65.6%	71.5%	78.3%	99.2%	100.0%	
Actual Value	**$ 483,829**	**$ 222,060**	**$ 206,794**	**$ 394,566**	**$ 1,070,404**	**$ 811,033**	**$ 1,118,261**								$ 4,306,947
Actual Value (CUM)	**$ 483,829**	**$ 705,889**	**$ 912,683**	**$ 1,307,249**	**$ 2,377,653**	**$ 3,188,686**	**$ 4,306,947**								
% Actual	**3.2%**	**1.5%**	**1.4%**	**2.6%**	**7.1%**	**5.4%**	**7.5%**								28.7%
% Actual (CUM)	**3.2%**	**4.7%**	**6.1%**	**8.7%**	**15.8%**	**21.2%**	**28.7%**								

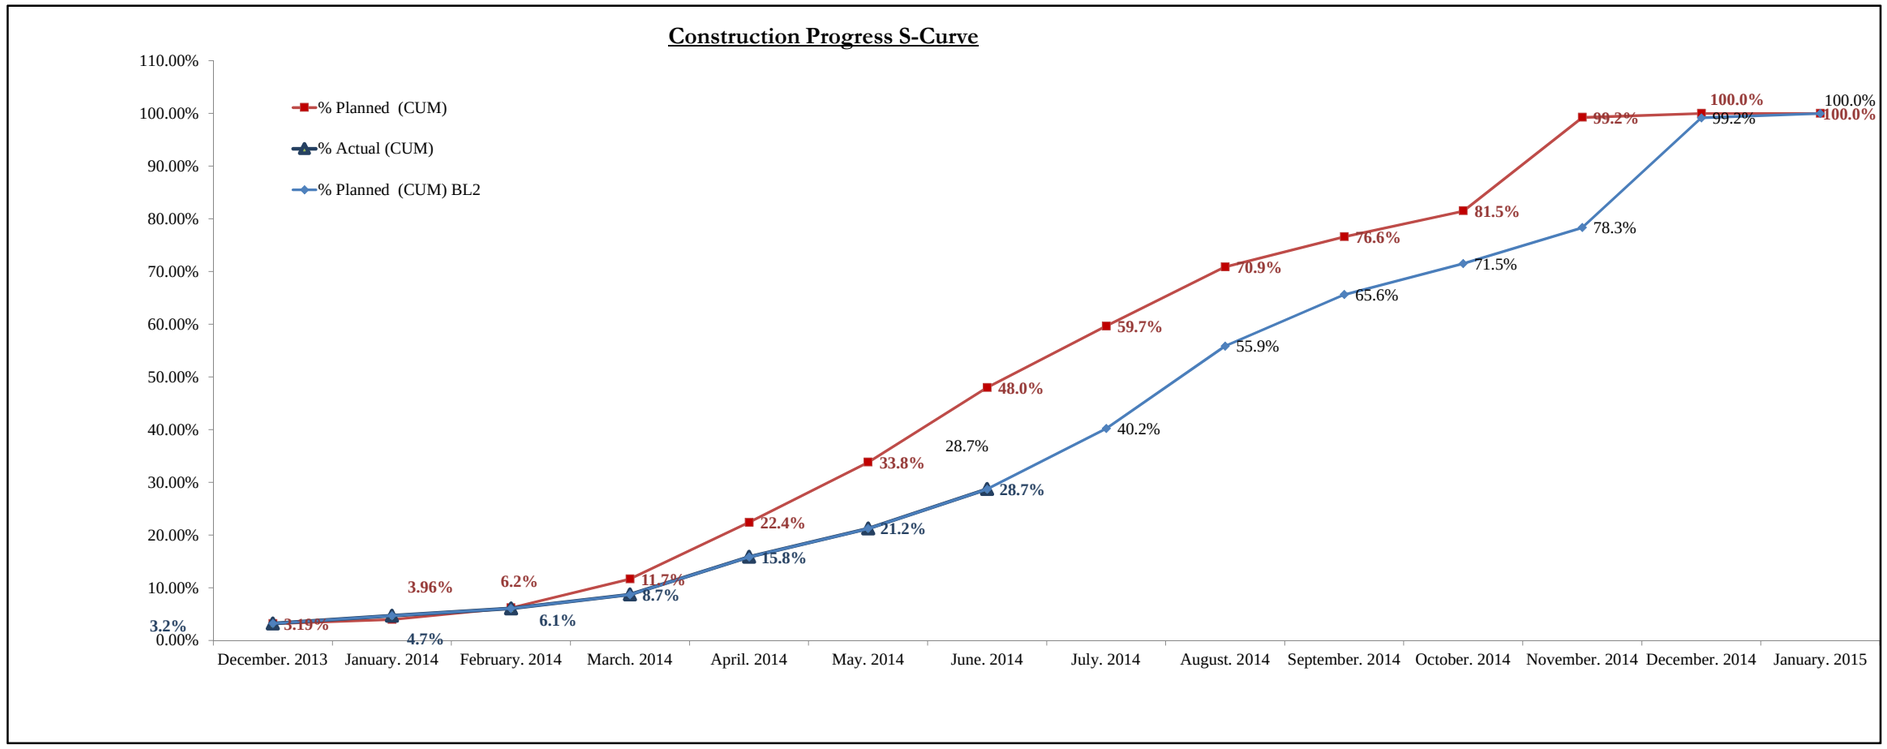

Construction Progress S-Curve

Total Contract Value (Day Work Not Included):	**$ 13,170,228**
Total Contract Value (VO3-BL-2):	**$ 12,743,361**
Project Duration :	**365 Calender Days**
Time Extension	**35 Calender Days**
Revised Project Duration :	**400 Calender Days**
NTP Date:	**3-Dec-13**

*** Day Work Not Included**

	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	June. 2014	July. 2014	August. 2014	September. 2014	October. 2014	November. 2014	December. 2014	January. 2015	TOTAL
Planned Value	$ 408,220	$ 106,363	$ 241,188	$ 588,675	$ 1,041,307	$ 1,452,029	$ 1,809,384	$ 988,276	$ 1,816,718	$ 926,901	$ 795,463	$ 2,870,274	$ 125,430		$ 13,170,228
Planned Value (CUM)	$ 408,220	$ 514,583	$ 755,771	$ 1,344,446	$ 2,385,753	$ 3,837,782	$ 5,647,166	$ 6,635,442	$ 8,452,160	$ 9,379,061	$ 10,174,524	$ 13,044,798	$ 13,170,228	$ 13,044,798	
% Planned	3.1%	0.8%	1.83%	4.5%	7.9%	11.0%	13.7%	7.5%	13.8%	7.0%	6.0%	21.8%	1.0%	0.0%	**100%**
% Planned (CUM)	3.1%	3.9%	5.7%	10.2%	18.1%	29.1%	42.9%	50.4%	64.2%	71.2%	77.3%	99.0%	100.0%	100.0%	
Planned Value (Baseline2)	$ 391,915	$ 198,722	$ 191,066	$ 316,990	$ 904,833	$ 624,160	$ 496,205	$ 1,223,334	$ 1,771,263	$ 1,466,122	$ 886,139	$ 1,023,101	$ 3,124,081	$ 125,430	**$ 12,743,361**
Planned Value (CUM)	$ 391,915	$ 590,637	$ 781,703	$ 1,098,693	$ 2,003,526	$ 2,627,686	$ 3,123,891	$ 4,347,225	$ 6,118,488	$ 7,584,610	$ 8,470,749	$ 9,493,850	$ 12,617,931	$ 12,743,361	
% Planned	3.1%	1.6%	1.5%	2.5%	7.1%	4.9%	3.9%	9.6%	13.9%	11.5%	7.0%	8.0%	24.5%	1.0%	**100.00%**
% Planned (CUM) BL2	3.1%	4.6%	6.1%	8.6%	15.7%	20.6%	24.5%	34.1%	48.0%	59.5%	66.5%	74.5%	99.0%	100.0%	
Actual Value	**$ 391,915**	**$ 198,722**	**$ 191,066**	**$ 316,990**	**$ 904,833**	**$ 624,160**	**$ 496,205**								**$ 3,123,891**
Actual Value (CUM)	**$ 391,915**	**$ 590,637**	**$ 781,703**	**$ 1,098,693**	**$ 2,003,526**	**$ 2,627,686**	**$ 3,123,891**								
% Actual	**3.1%**	**1.6%**	**1.5%**	**2.5%**	**7.1%**	**4.9%**	**3.9%**								**24.51%**
% Actual (CUM)	**3.1%**	**4.6%**	**6.1%**	**8.6%**	**15.7%**	**20.6%**	**24.5%**								

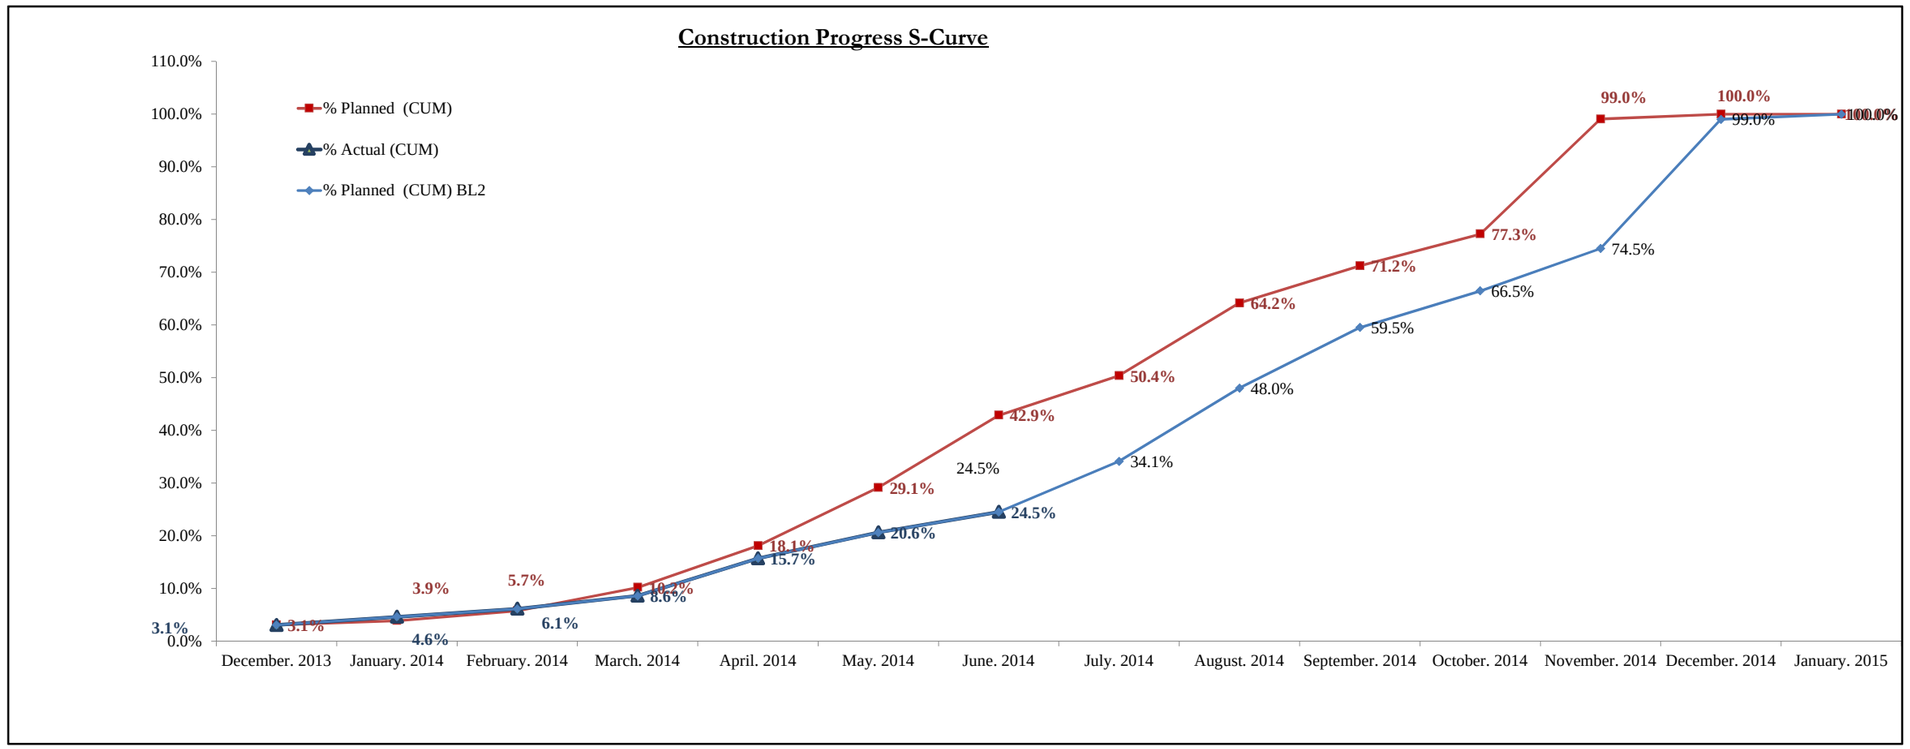

Construction Progress S-Curve

Total Contract Value $ 3,025,365
Total Contract Value (VO3-BL2) $ 2,263,977
Project Duration : 240 Calender Days
Time Extension 21 Calender Days
Revised Project Duration : 261 Calender Days
NTP Date: 3-Dec-13
*** Day Work Not Included**

	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	June. 2014	July. 2014	August. 2014	TOTAL
Planned Value	$ 109,186	$ 17,887	$ 119,825	$ 297,589	$ 697,916	$ 395,388	$ 484,373	$ 903,200		$ 3,025,364
Planned Value (CUM)	$ 109,186	$ 127,073	$ 246,898	$ 544,487	$ 1,242,403	$ 1,637,791	$ 2,122,164	$ 3,025,364	$ 3,025,364	
% Planned	3.6%	0.6%	3.96%	9.8%	23.1%	13.1%	16.0%	29.9%	0.0%	**100%**
% Planned (CUM)	3.6%	4.2%	8.2%	18.0%	41.1%	54.1%	70.1%	100.0%	100.0%	
Planned Value (Baseline2)	$ 91,915	$ 23,337	$ 15,728	$ 77,576	$ 165,571	$ 186,873	$ 622,056	$ 503,480	$ 577,441	**$ 2,263,977**
Planned Value (CUM)	$ 91,915	$ 115,252	$ 130,980	$ 208,556	$ 374,127	$ 561,000	$ 1,183,056	$ 1,686,536	$ 2,263,977	
% Planned	4.1%	1.0%	0.7%	3.4%	7.3%	8.3%	27.5%	22.2%	25.5%	**100.00%**
% Planned (CUM) BL2	4.1%	5.1%	5.8%	9.2%	16.5%	24.8%	52.3%	74.5%	100.0%	
Actual Value	$ 91,915	$ 23,337	$ 15,728	$ 77,576	$ 165,571	$ 186,873	$ 622,056			**$ 1,183,056**
Actual Value (CUM)	$ 91,915	$ 115,252	$ 130,980	$ 208,556	$ 374,127	$ 561,000	$ 1,183,056			
% Actual	4.1%	1.0%	0.7%	3.4%	7.3%	8.3%	27.5%			**52.26%**
% Actual (CUM)	4.1%	5.1%	5.8%	9.2%	16.5%	24.8%	52.3%			

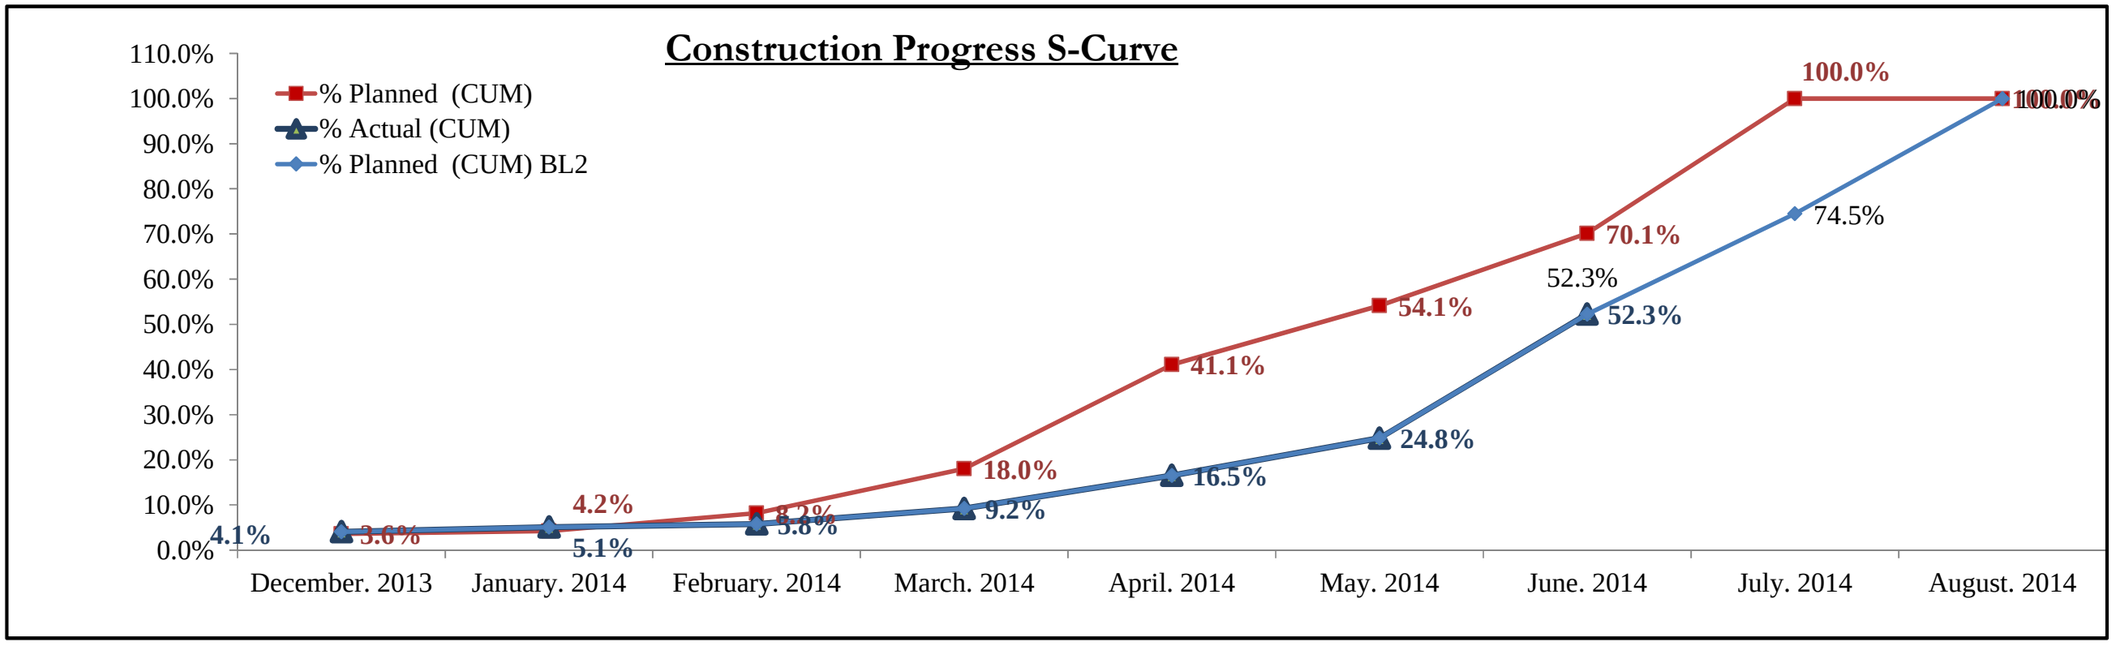

D | Site Memos Log

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT(North II)
Site Memo Log (C-E)

SUBMITTAL				TRACKING DATES	
Spec. No.	Site Memo No	Subject	Project	Submitted on (M/D/Y)	Remarks
	SM-13-00014-NAB-C-E-001	Revised Plans and Cross Sections from Sta.4+160 to Sta.5+450 -Project 01	NAB	12/23/13	Other
	SM-13-00014-NAB-C-E-002	Contradiction between SD review comment and Design Drawing -Project 01	NAB	04/12/14	Other
	SM-13-00014-NAB-C-E-003	Construction of concrete retaining walls from sta. 1+720 to sta. 1+750 RHS and from sta. 1+865 to sta. 1+935 RHS, Project #1	NAB	05/27/14	Other
	SM-13-00014-NAB-C-E-004	Box Culvert at Sta.3+610- Nablus Der Sharaf -Beit Iba Road -Project 01	NAB	06/04/14	Other
	SM-13-00014-NAB-C-E-005	Design center line from Sta.0+000 to Sta.2+000	NAB	06/11/14	Other
	SM-13-00014-NAB-C-E-006	Concrete work for side walk from St.2+000 to Sta.3+000	NAB	06/12/14	Record of Joint Walkthrough
	SM-13-00014-NAB-C-E-007	Existing Steel Container at sta.1+850 LHS	NAB	06/17/14	Other

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (North II)
Site Memo Log (E-C)

SUBMITTAL				TRACKING DATES	
Spec. No.	Submittal No	Subject	Project	Submitted on (M/D/Y)	Remarks
	SM-13-00014-NAB-E-C-001	Revised Plans and Cross Sections from Sta.4+160 to Sta.5+450	NAB	12/09/13	Site Instruction
	SM-13-00014-DSR-E-C-002	Modified Plan and Profile of Project 02 (Deir Sharaf Tulkarem)Road	DSR	01/23/14	Site Instruction
	SM-13-00014-NAB-E-C-003	Unauthorized Dumping of Excavated Materials -Project 01	NAB	01/26/14	Site Instruction
	SM-13-00014-DSR-E-C-004	Safety Enhancement at Project 02 Detour	DSR	02/10/14	Site Instruction
	SM-13-00014-MRNII-E-C-005	Required Approvals for Traffic Control Plan	MRNII	02/17/14	Site Instruction
	SM-13-00014-MRNII-E-C-006	Relocation of the Existing Electrical Utilities -Project 01 & Project 02	MRNII	02/18/14	Site Instruction
	SM-13-00014-NAB-E-C-007	Soil Improvement under the Retaining Wall at Project 01-NAB	NAB	03/04/14	Site Instruction
	SM-13-00014-NAB-E-C-008	Providing House Connection for Sewer Line at Project 01-NAB	NAB	03/10/14	Site Instruction
	SM-13-00014-NAB-E-C-009	Construction of Sewer Pipeline Project 01	NAB	03/10/14	Site Instruction
	SM-13-00014-NAB-E-C-010	Installation of 12" Water Steel Pipeline at Project 01	NAB	03/11/14	Site Instruction
	SM-13-00014-NAB-E-C-011	Replacement of the Concrete Parapet with CHB Parapet at Project 01	NAB	03/11/14	Site Instruction
	SM-13-00014-NAB-E-C-012	Sarra Detour Enhancement at Project 01-NAB	NAB	03/12/14	Site Instruction
	SM-13-00014-DSR-E-C-013	Revised Plan of Project No. 02 from Sta. 0+790 to Sta. 0+890	DSR	03/20/14	Site Instruction
	SM-13-00014-NAB-E-C-014	Revised Alignment from Sta.0+000 to Sta.2+060 at Project 01	NAB	03/25/14	Site Instruction
	SM-13-00014-NAB-E-C-015	Soil Replacement and Improvement at Project 01	NAB	03/26/14	Record of Verbal Site Instruction
	SM-13-00014-DSR-E-C-016	Soil Replacement and Improvement at Project 02	DSR	03/26/14	Record of Verbal Site Instruction
	SM-13-00014-DSR-E-C-017	Perform Infrastructure Works at Project 02	DSR	03/27/14	Site Instruction
	SM-13-00014-NAB-E-C-018	Perform and Connect 8" diameter UPVC Pipeline to the Existing Sewage Manholes at Project 01-NAB	NAB	03/30/14	Site Instruction
	SM-13-00014-NAB-E-C-019	Rehabilitation of the Temporary Detour (Sarra Detour) at Project 01-NAB	NAB	03/30/14	Site Instruction
	SM-13-00014-NAB-E-C-020	Proposed 3" Water Pipeline at Project 01	NAB	04/02/14	Site Instruction
	SM-13-00014-NAB-E-C-021	Closing for SM-13-00014-MRNII-C-E-002-(Contradiction between SD review comments and Design Drawing, Project 01)	NAB	04/14/14	Other
	SM-13-00014-NAB-E-C-022	Quality of Stones Used in Stonewall Construction at Project 01	NAB	04/17/14	Site Instruction
	SM-13-00014-NAB-E-C-023	Road Crossing (Sleeves) at Project # 1	NAB	04/17/14	Site Instruction
	SM-13-00014-NAB-E-C-024	Construction of Retaining Wall and RC Stair at Project #01	NAB	04/21/14	Site Instruction
	SM-13-00014-NAB-E-C-025	Construction of Stone Wall and RC Stair at Project 01	NAB	04/22/14	Site Instruction
	SM-13-00014-NAB-E-C-026	Temporary Access for Existing Building at Project 01	NAB	04/28/14	Record of Unsafe Condition
	SM-13-00014-DSR-E-C-027	Unsafe Condition Observed at Project 02	DSR	04/30/14	Record of Unsafe Condition
	SM-13-00014-NAB-E-C-028	Replace 3" Steel Water Pipe by 2" Galvanized Steel Pipe at Project 01	NAB	05/08/14	Site Instruction
	SM-13-00014-NAB-E-C-029	Slow Rate of Progress and Delays at Project 01	NAB	05/13/14	Site Instruction
	SM-13-00014-DSR-E-C-030	Limits of Construction at Project 02	DSR	05/15/14	Site Instruction
	SM-13-00014-NAB-E-C-031	Submitting Shop Drawing for the Intersection at Sta.2+000 -Project 01	NAB	05/19/14	Site Instruction
	SM-13-00014-NAB-E-C-032	Installing Precast Concrete Manholes -Project 01	NAB	05/19/14	Site Instruction

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (North II)
Site Memo Log (E-C)

SUBMITTAL				TRACKING DATES	
Spec. No.	Submittal No	Subject	Project	Submitted on (M/D/Y)	Remarks
	SM-13-00014-DSR-E-C-033	Step Barrier Construction at Project 02	DSR	05/21/14	Site Instruction
	SM-13-00014-DSR-E-C-034	Increasing Width for the paved Shoulder at Project 02	DSR	05/21/14	Site Instruction
	SM-13-00014-DSR-E-C-035	Shop Drawing of the Retaining Wall at Project 02	DSR	05/22/14	Site Instruction
	SM-13-00014-NAB-E-C-036	Roundabout at Deir Sharaf Intersection at Project 01	NAB	05/29/14	Site Instruction
	SM-13-00014-NAB-E-C-037	Box Culvert at Sta.3+610 at Project 01	NAB	06/05/14	Site Instruction
	SM-13-00014-NAB-E-C-038	Retaining Wall from Sta.3+217 to Sta.3+229 LHS at Project 01	NAB	06/08/14	Site Instruction
	SM-13-00014-NAB-E-C-039	Closing for SM-13-00014-MRNII-C-E-003 at Project 01	NAB	06/09/14	Site Instruction
	SM-13-00014-NAB-E-C-040	Judicial Response (Weighbridges at Sta.4+130 RHS)	NAB	06/09/14	Site Instruction
	SM-13-00014-NAB-E-C-041	Response to Contractor's Site Memo SM-13-00014-NAB-C-E-005	NAB	06/12/14	Site Instruction
	SM-13-00014-NAB-E-C-042	Lighting System at Project # 01	NAB	06/15/14	Site Instruction
	SM-13-00014-NAB-E-C-043	ICA Approval for the Roundabout at Sta.0+000 at Project 01	NAB	06/23/14	Site Instruction
	SM-13-00014-NAB-E-C-044	Quality of Concrete Retaining Wall Finish at Project 01	NAB	06/23/14	Record of Non Quality Compliance
	SM-13-00014-DSR-E-C-045	Poor Quality of Concrete Step Barrier at Project 02	DSR	06/30/14	Record of Non Quality Compliance

E | Inspection Requests Log

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-001-A	Implementation of traffic control plan , from st.0+020 to Sta. 3+000	01/19/14	01/19/14	01/20/14	1	C
	IR-13-00014-NAB-001-B	Implementation of traffic control plan , from st.0+020 to Sta. 3+000	01/22/14	01/22/14	01/23/14	1	A
	IR-13-00014-NAB-002-A	Setting out center line , designed control point	01/20/14	01/20/14	01/21/14	1	A
	IR-13-00014-NAB-003-A	Check bench mark , from Sta. 2+000 to Sta. 2+600	01/22/14	01/22/14	01/23/14	1	A
	IR-13-00014-NAB-004-A	Check natural ground level , from Sta. 2+000 to Sta. 2+600	01/23/14	01/23/14	01/23/14	0	C
	IR-13-00014-NAB-005-A	Start excavation , removal of asphalt layer at LHS from Sta. 2+020 to Sta.2+240	01/23/14	01/23/14	01/23/14	0	A
	IR-13-00014-NAB-006-A	Start excavation , removal of asphalt layer at RHS from Sta. 2+020 to Sta.2+280	02/02/14	02/02/14	02/02/14	0	A
	IR-13-00014-NAB-007-A	Widening at RHS from Sta. 2+280 to 2+540	02/02/14	02/02/14	02/02/14	0	C
	IR-13-00014-NAB-007-B	Widening at RHS from Sta. 2+280 to 2+540	02/09/14	02/09/14	02/09/14	0	C
	IR-13-00014-NAB-007-C	Widening at RHS from Sta. 2+280 to 2+540	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-NAB-008-A	Start excavation , removal of asphalt layer at LHS from Sta. 2+280 to Sta.2+540	02/02/14	02/02/14	02/02/14	0	C
	IR-13-00014-NAB-008-B	Start excavation , removal of asphalt layer at LHS from Sta. 2+280 to Sta.2+540	02/09/14	02/09/14	02/09/14	0	C
	IR-13-00014-NAB-008-C	Start excavation , removal of asphalt layer at LHS from Sta. 2+280 to Sta.2+540	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-NAB-009-A	Check the sewer alignment from Sta . 2+080 to 2+280	02/09/14	02/09/14	02/09/14	0	C
	IR-13-00014-NAB-009-B	Check the sewer alignment from Sta . 2+080 to 2+281	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-NAB-010-A	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 13- Manhole 12.	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-NAB-011-A	Check bedding materials, installation of pipes 12”according to level , from Manhole 12- Manhole 13	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-NAB-012-A	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 12- Manhole 09.	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-NAB-013-A	Check bedding materials, installation of pipes 12”according to level , from Manhole 12- Manhole 09	02/11/14	02/11/14	02/11/14	0	A
	IR-13-00014-NAB-014-A	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 08- Manhole 07.	02/11/14	02/11/14	02/11/14	0	C
	IR-13-00014-NAB-014-B	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 08- Manhole 07.	02/12/14	02/12/14	02/12/14	0	A
	IR-13-00014-NAB-015-A	Check bedding materials, installation of pipes 12”according to level , from Manhole 09- Manhole 07	02/11/14	02/11/14	02/11/14	0	A
	IR-13-00014-NAB-016-A	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 06- Manhole 05.	02/11/14	02/11/14	02/11/14	0	C
	IR-13-00014-NAB-016-B	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 06- Manhole 05.	02/13/14	02/13/14	02/13/14	0	A
	IR-13-00014-NAB-017-A	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 05- Manhole 04.	02/12/14	02/12/14	02/12/14	0	A
	IR-13-00014-NAB-018-A	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 04- Manhole 03.	02/12/14	02/12/14	02/12/14	0	A
	IR-13-00014-NAB-019-A	Check bedding materials, installation of pipes 12”according to level , from Manhole 05- Manhole 04	02/12/14	02/12/14	02/13/14	1	A
	IR-13-00014-NAB-020-A	Check bedding materials, installation of pipes 12”according to level , from Manhole 04- Manhole 03	02/13/14	02/13/14	02/13/14	0	A
	IR-13-00014-NAB-021-A	Check the excavation, elevation and dimensions for sewer line trench, from Manhole 03- Manhole 02.	02/13/14	02/13/14	02/13/14	0	A
	IR-13-00014-NAB-022-A	Check and approve alignment of storm water from Sta. 2+080 to Sta. 2+580	02/13/14	02/13/14	02/13/14	0	A
	IR-13-00014-NAB-023-A	Check bedding materials, installation of pipes 12”according to level , from Manhole 07- Manhole 06, and M 03- M02	02/13/14	02/13/14	02/13/14	0	A
	IR-13-00014-NAB-024-A	Check excavation, elevation and dimensions for Storm water, from M #114-M#40 , and from M# 40 – M#41	02/16/14	02/16/14	02/16/14	0	A
	IR-13-00014-NAB-025-A	Prior start excavation , removal of asphalt layers at RHS ,from Sta. 2+280 to 2+590	02/16/14	02/16/14	02/16/14	0	A
	IR-13-00014-NAB-026-A	Check the excavation, elevation and dimensions for Storm water , from Manhole 41- Manhole 42, Manhole 42- Manhole 43.	02/17/14	02/17/14	02/17/14	0	A
	IR-13-00014-NAB-027-A	Installation of concrete pipes for storm water , from M # 41- M# 42, M#42- M# 43	02/17/14	02/17/14	02/18/14	1	A
	IR-13-00014-NAB-028-A	Installation of concrete pipes for storm water , from M # 40- M# 41	02/18/14	02/18/14	02/18/14	0	C
	IR-13-00014-NAB-028-B	Installation of concrete pipes for storm water , from M # 40- M# 41	02/19/14	02/19/14	02/19/14	0	A
	IR-13-00014-NAB-029-A	Check the excavation, elevation and dimensions for Storm water , from Manhole 43- Manhole 44	02/18/14	02/18/14	02/18/14	0	A
	IR-13-00014-NAB-030-A	Check ecxacation , dimentions, elevations, and coordinate for storm water manhole form M # 13- M#08	02/18/14	02/18/14	02/19/14	1	C
	IR-13-00014-NAB-030-B	Check ecxacation , dimentions, elevations, and coordinate for storm water manhole form M # 13- M#08	02/23/14	02/23/14	02/23/14	0	A
	IR-13-00014-NAB-031-A	Check excavtion , elevation , and dimensions for storm water from manhloes , M#44- M#45	02/18/14	02/18/14	02/19/14	1	A
	IR-13-00014-NAB-032-A	Check excavtion , elevation , and dimensions for storm water from manhloes , M#45- M#46	02/19/14	02/19/14	02/19/14	0	A
	IR-13-00014-NAB-033-A	Check bedding materials, installation of concrete pipes from manholes, M #39 - M# 40	02/19/14	02/19/14	02/19/14	0	A
	IR-13-00014-NAB-034-A	Check bedding materials, installation of concrete pipes from manholes, M #43- M# 44	02/19/14	02/19/14	02/19/14	0	A
	IR-13-00014-NAB-035-A	Check bedding materials, installation of concrete pipes from manholes, M #44- M# 45	02/19/14	02/19/14	02/19/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-036-A	Check ecxacation , dimentions, elevations, and coordinate for storm water manhole, M # 46- M#47	02/19/14	02/19/14	02/19/14	0	A
	IR-13-00014-NAB-037-A	Check ecxacation , dimentions, elevations, and coordinate for storm water manhole, M # 47- M#48	02/19/14	02/19/14	02/19/14	0	A
	IR-13-00014-NAB-038-A	Check bedding materials, installation of concrete pipes from manholes, M #45- M# 46	02/19/14	02/19/14	02/19/14	0	A
	IR-13-00014-NAB-039A	Check bedding materials, installation of concrete pipes from manholes, M #46- M# 47	02/20/14	02/22/14	02/22/14	0	A
	IR-13-00014-NAB-040-A	Check bedding materials, installation of concrete pipes from manholes, M #47- M# 48	02/20/14	02/22/14	02/22/14	0	A
	IR-13-00014-NAB-041-A	Check excavtion , elevation , and dimensions for storm water from manhloes , M#48- M#49	02/20/14	02/22/14	02/22/14	0	A
	IR-13-00014-NAB-042-A	Check excavtion , elevation , and dimensions for storm water from manhloes , M#49- M#50	02/20/14	02/22/14	02/22/14	0	A
	IR-13-00014-NAB-043-A	Check bedding materials, installation of concrete pipes from manholes, M #48- M# 49	02/22/14	02/22/14	02/23/14	1	A
	IR-13-00014-NAB-044-A	Check bedding materials, installation of concrete pipes from manholes, M #49- M# 50	02/22/14	02/22/14	02/23/14	1	A
	IR-13-00014-NAB-045-A	Check excavtion , elevation , and dimensions for storm water from manhloes , M#50- M#51	02/22/14	02/22/14	02/23/14	1	C
	IR-13-00014-NAB-045-B	Check excavtion , elevation , and dimensions for storm water from manhloes , M#50- M#51	02/24/14	02/24/14	02/24/14	0	A
	IR-13-00014-NAB-046-A	Installation of pre cast sewer manholes , pipes installation . From M # 13 to M # 08	02/23/14	02/23/14	02/24/14	1	A
	IR-13-00014-NAB-047-A	Check ecxacation , dimentions, elevations, and coordinate for storm water manhole from M # 07- M#02	02/23/14	02/23/14	02/24/14	1	A
	IR-13-00014-NAB-048-A	Check natural ground level , from Sta. 2+600 to Sta.3+000	02/24/14	02/24/14	02/24/14	0	A
	IR-13-00014-NAB-049-A	Check excavation , breaking out , removal asphalt layer and deposit it from site , at RHS m from Sa 2+600 to Sta. 2+920	02/24/14	02/24/14	02/24/14	0	A
	IR-13-00014-NAB-050-A	Inspection for BM , from Sta. (2+600 to 3+000)	02/25/14	02/25/14	02/25/14	0	A
	IR-13-00014-NAB-051-A	Check blinding concrete, form work and reinforcement for storm water manhole (M #40- M#43), also inspect manhole coordinate and level prior to proceed with concrete	02/25/14	02/25/14	02/26/14	1	A
	IR-13-00014-NAB-052-A	Excavation, removal asphalt layer, deposit it from site at LHS, FROM Sta. 2+600 to 3+000	02/26/14	02/26/14	02/26/14	0	A
	IR-13-00014-NAB-053-A	Check excavation , elevation , dimensions for storm water manhole (M #38- M#39)	02/27/14	03/01/14	03/02/14	1	A
	IR-13-00014-NAB-054-A	Check bedding and backfilling materials around sewer line manhole , from M # 13 to M # 08	02/27/14	03/01/14	03/02/14	1	A
	IR-13-00014-NAB-055-A	Check Rebar for storm water Manhole (M # 40 to M # 41)prior to start formwork	02/27/14	03/01/14	03/02/14	1	A
	IR-13-00014-NAB-056-A	Check Installation concrete Pipes Φ 80 cm from (M # 39 to M # 38	03/02/14	03/02/14	03/03/14	1	C
	IR-13-00014-NAB-056-B	Check Installation concrete Pipes Φ 80 cm from (M # 39 to M # 38	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-057-A	Check excavation , elevation , dimensions for storm water manhole (M # 38 to M wadi)	03/02/14	03/02/14	03/03/14	1	C
	IR-13-00014-NAB-057-B	Check excavation , elevation , dimensions for storm water manhole (M # 38 to M wadi)	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-058-A	Rebar for Strom Water Manholes (M #42 -M# 43) prior to start formwork	03/03/14	03/03/14	03/03/14	0	A
	IR-13-00014-NAB-059-A	Excavation, elevation, dimensions fro sewer line (M # 13- M # 14)	03/03/14	03/03/14	03/03/14	0	A
	IR-13-00014-NAB-060-A	Bedding materials, installation of concrete Pipes 60 cm , for strom water line (M # 50- M # 51)	03/03/14	03/03/14	03/03/14	0	A
	IR-13-00014-NAB-061-A	Casting B 350 concrete for Storm water Manhole (M # 42- M #43)	03/03/14	03/03/14	03/03/14	0	A
	IR-13-00014-NAB-062-A	Installation UPVC Pipes 12" for sewer line - (M #14 -M # 13)	03/04/14	03/04/14	03/04/14	0	A
	IR-13-00014-NAB-063-A	Casting blinding concrete for Storm water Manhole (M # 38- M #39)- (M# 50- M#51)	03/04/14	03/04/14	03/05/14	1	A
	IR-13-00014-NAB-064-A	Casting B 350 concrete for Storm water Manhole base (M # 44- M #48	03/04/14	03/04/14	03/05/14	1	A
	IR-13-00014-NAB-065-A	Check excavation , elevation , dimensions , for sewer line from (M # 02- M# 01)	03/05/14	03/05/14	03/05/14	0	A
	IR-13-00014-NAB-066-A	Check excavation , elevation , dimensions , for sewer line from (M # 01- M# 01-A)	03/05/14	03/05/14	03/05/14	0	A
	IR-13-00014-NAB-067-A	Check subgrade level at LHS, from Sta. (2+730 -2+800)	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-068-A	Casting blinding B 150 Concrete for RW , from sta. 2+339- 2+369 at RHS	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-069-A	Check backfilling single size around storm water Manhole (M # 40 -M# 41)	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-070-A	Chwck rebar work for storm water Manhole (M # 48- M# 49) prior to start formwork	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-071-A	Check Bedding materials , installation of UPVC pipes for sewer line, form Sta (M # 01- M # 02)	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-072-A	Check Bedding materials , installation of UPVC pipes for sewer line, form Sta (M # 01- M # 01-A)	03/06/14	03/06/14	03/06/14	0	A
	IR-13-00014-NAB-073-A	Check backfilling single size around storm water Manhole (M # 42 -M# 43)	03/06/14	03/08/14	03/09/14	1	A
	IR-13-00014-NAB-074-A	Check Bedding materials , installation of concrete pipes , Φ 80 cm , of storm water line , from (M #38- M # wadi)	03/06/14	03/08/14	03/09/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-075-A	Check Casting B 350 concrete for storm water manhole walls , from (M # 48- M 49)	03/06/14	03/08/14	03/09/14	1	A
	IR-13-00014-NAB-076-A	Check Casting B 350 concrete forbase of RW , from Sta. (2+339- 2+369) at RHS	03/06/14	03/08/14	03/09/14	1	C
	IR-13-00014-NAB-076-B	Check Casting B 350 concrete forbase of RW , from Sta. (2+339- 2+369) at RHS	03/09/14	03/09/14	03/09/14	0	A
	IR-13-00014-NAB-077-A	Casting concrete for storm water manhole base, from manhole (M # 44-45-39)	03/10/14	03/10/14	03/10/14	0	A
	IR-13-00014-NAB-078-A	Check sewer line (HC) (200 mm) , installation , prior to backfill from (M# 13-M # 08), from (M# 06-M#04)	03/11/14	03/11/14	03/11/14	0	A
	IR-13-00014-NAB-079-A	Check Rebars prior to proceed with formwork for RW , from sta. 2+360-2+347 at RHS	03/11/14	03/11/14	03/11/14	0	A
	IR-13-00014-NAB-080-A	Casting concrete , for Retaining Wall , from Sta 2+360-2+347 at RHS	03/11/14	03/11/14	03/12/14	1	A
	IR-13-00014-NAB-081-A	Rebar for Storm water Manholes(# 47 - # 46) , prior to start formwork	03/11/14	03/11/14	03/12/14	1	A
	IR-13-00014-NAB-082-A	Check excavation , elevation dimensions, for storm water Manhole , from (M#51-M#55)	03/11/14	03/11/14	03/12/14	1	A
	IR-13-00014-NAB-083-A	Check subgrade layer , level and compaction prior to start Topping layer from Sta. 2+100-2+280 at LHS	03/11/14	03/11/14	03/12/14	1	A
	IR-13-00014-NAB-084-A	Check subgrade layer , level and compaction prior to start Topping layer from Sta. 2+320-2+480 at LHS	03/11/14	03/11/14	03/12/14	1	C
	IR-13-00014-NAB-084-B	Check subgrade layer , level and compaction prior to start Topping layer from Sta. 2+320-2+480 at LHS	03/24/14	03/24/14	03/24/14	0	C
	IR-13-00014-NAB-084-C	Check subgrade layer , level and compaction prior to start Topping layer from Sta. 2+320-2+480 at LHS	03/31/14	03/31/14	03/31/14	0	A
	IR-13-00014-NAB-085-A	Check installation concrete Pipes Φ 60 cm from (M # 51 - M # 55	03/11/14	03/11/14	03/12/14	1	A
	IR-13-00014-NAB-086-A	Check NGL. C.L , from St. 3+000-03+500	03/13/14	03/15/14	03/16/14	1	A
	IR-13-00014-NAB-087-A	Check excavation , elevation dimensions, for storm water Manhole , from (M#55-M#54)	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00014-NAB-088-A	Bedding materials, installation of concrete Pipes 60 cm , for strom water line (M # 55- M # 54)	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00014-NAB-089-A	Check excavation , elevation dimensions, for storm water Manhole , from (M#54-M#53)	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00014-NAB-090-A	Casting concrete for storm water manhole base, from manhole walls (M # 47-M#46	03/16/14	03/16/14	03/17/14	1	A
	IR-13-00014-NAB-091-A	Bedding materials, installation of concrete Pipes 60 cm , for strom water line (M # 54 M # 53)	03/16/14	03/16/14	03/17/14	1	A
	IR-13-00014-NAB-092-A	Check excavation , elevation dimensions, for storm water Manhole , from (M#53-M#52)	03/16/14	03/16/14	03/17/14	1	A
	IR-13-00014-NAB-093-A	Bedding materials, installation of concrete Pipes 60 cm , for strom water line (M # 53 M # 52)	03/17/14	03/17/14	03/18/14	1	A
	IR-13-00014-NAB-094-A	Check excavation , elevation dimensions, for storm water Manhole , from (M#59-M#60)	03/17/14	03/17/14	03/17/14	0	D
	IR-13-00014-NAB-094-B	Check excavation , elevation dimensions, for storm water Manhole , from (M#59-M#60)	03/18/14	03/18/14	03/18/14	0	A
	IR-13-00014-NAB-095-A	Casting concrete for RW . From Sta, 2+360-2+366 at RHS	03/18/14	03/18/14	03/18/14	0	A
	IR-13-00014-NAB-096-A	Bedding materials, installation of concrete Pipes 60 cm , for strom water line (M # 59 M # 60)	03/18/14	03/18/14	03/18/14	0	A
	IR-13-00014-NAB-097-A	Check excavation , elevation dimensions, for storm water Manhole , from (M#59-M#58)	03/18/14	03/18/14	03/18/14	0	A
	IR-13-00014-NAB-098-A	Check subgrade layer, level, and compaction , from Sta. 2+830-2+880 at LHS	03/18/14	03/18/14	03/19/14	1	A
	IR-13-00014-NAB-099-A	Bedding materials, installation of concrete Pipes 60 cm , for strom water line (M # 58 M # 59)	03/18/14	03/18/14	03/19/14	1	A
	IR-13-00014-NAB-100-A	Check Rebar for storm water Manhole (M # 45) prior to start formwork	03/19/14	03/19/14	03/20/14	1	A
	IR-13-00014-NAB-101-A	Check Backfilling single size around storm water manhole (M# 46--47-48-49)	03/19/14	03/19/14	03/20/14	1	A
	IR-13-00014-NAB-102-A	Casting blinding concrete for Retaining Wall from Sta. 2+475-2+515 at RHS	03/20/14	03/20/14	03/20/14	0	A
	IR-13-00014-NAB-103-A	Check rebar work for storm water manhole (M# 44) prior to start formwork	03/20/14	03/20/14	03/20/14	0	A
	IR-13-00014-NAB-104-A	casting concrete for storm water manhole base (M# 51)	03/20/14	03/20/14	03/20/14	0	A
	IR-13-00014-NAB-105-A	Check natural Ground Level , Center Line , from Sta. 3+500-4+100	03/22/14	03/22/14	03/23/14	1	A
	IR-13-00014-NAB-106-A	Casting concrete for Storm Water Manhole Wall M# 44	03/22/14	03/22/14	03/23/14	1	A
	IR-13-00014-NAB-107-A	Check Start Excavation Of 12" water pipeline , from Sta, 2+00-2+200	03/23/14	03/23/14	03/23/14	0	A
	IR-13-00014-NAB-108-A	Check Subgrade level, Compaction , shaping prior to start Topping layer from Sta. 2+480-2+580	03/23/14	03/23/14	03/24/14	1	A
	IR-13-00014-NAB-109-A	Check Rebar , Casting concrete for Base of Retaining Wall from Sta. 2+475-2+515 at RHS	03/23/14	03/23/14	03/23/14	0	A
	IR-13-00014-NAB-110-A	Check excavation up to required level, , trench dimensions , bedding layer , installation of 12" pipes prior to start back filling from , Sta. 2+140-2+240	03/23/14	03/23/14	03/24/14	1	A
	IR-13-00014-NAB-111-A	Check Rebar work to proceed casting concrete for storm water manhole Wall , (M# 39-M#50)	03/24/14	03/24/14	03/24/14	0	C
	IR-13-00014-NAB-111-B	Check Rebar work to proceed casting concrete for storm water manhole Wall , (M# 39)	03/24/14	03/24/14	03/25/14	1	A
	IR-13-00014-NAB-112-A	Check Rebar work to proceed casting concrete for storm water manhole base , (M# 51-M#55)	03/24/14	03/24/14	03/24/14	0	A
	IR-13-00014-NAB-113-A	Check subgrade layer , level , compaction & shaping prior to start Topping layer from Sta. 2+680-2+730 at LHS	03/24/14	03/24/14	03/25/14	1	A
	IR-13-00014-NAB-114-A	Check subgrade layer , level , compaction & shaping prior to start Topping layer from Sta. 2+880-2+300 at LHS	03/24/14	03/24/14	03/25/14	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-114-B	Check subgrade layer , level , compaction & shaping prior to start Topping layer from Sta. 2+880-2+980 at LHS	03/31/14	03/31/14	03/31/14	0	A
	IR-13-00014-NAB-115-A	Check casting concrete for storm water manhole base (M# 54-53-52-60)	03/25/14	03/25/14	03/25/14	0	A
	IR-13-00014-NAB-116-A	Check Rebar work for Retaining Wall, from Sta. 2+475-2+480, 2+490-2+500 and from 2+510-2+515 , to proceed casting concrete	03/25/14	03/25/14	03/25/14	0	A
	IR-13-00014-NAB-117-A	Check subgrade layer and coordinate prior to start Topping layer from sta. 2+100-2+240 at RHS	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-118-A	Check casting concrete for storm water manhole base (M# 58-59)	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-119-A	Check Rebar work to proceed casting concrete for storm water manhole Wall (M# 51)	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-120-A	check Casting concrete for Retaining Wall, from sta. 2+475-2+480- 2+490-2+500 and from 2+510-2+515 at RHS	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-121-A	Check Casting concrete for base of Retaining Wall, from sta. 2+344-2+339 at RHS	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-122-A	Check Excavation, replacement with filling materials, at St. 2+220 at RHS , 2+190 at RHS , and at St . 2+160 at RHS	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-123-A	Check Isolation for Storm Water manhole (M# 44), prior to start backfilling	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-124-A	Check excavation for 12" water pipeline trench , dimensions , level, coordinate from sta. 2+040-2+500 at RHS	03/26/14	03/26/14	03/26/14	0	A
	IR-13-00014-NAB-125-A	check Bedding layer , installation of 12" pipes , welding of pipes , prior to backfill from Sta. 2+040-2+500 at RHS	3/26/2014	3/26/2014	03/26/14	0	A
	IR-13-00014-NAB-126-A	Check subgrade layer , level, coordinate , from Sta. 2+80-2+440 at RHS	03/27/14	03/27/14	03/27/14	0	A
	IR-13-00014-NAB-127-A	Check Rebar work for Retaining Wall , from Sta. 2+339-2+344 at RH	03/27/14	03/27/14	03/27/14	0	C
	IR-13-00014-NAB-127-B	Check Rebar work for Retaining Wall , from Sta. 2+339-2+344 at RHS	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-128-A	Check Casting concrete for storm water manhole base , for manhole (M# 45-M# 38)	03/27/14	03/27/14	03/27/14	0	C
	IR-13-00014-NAB-128-B	Check Casting concrete for storm water manhole base , for manhole (M# 45-M# 38)	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-129-A	Check bedding layer , installation of 12 " pipes , welding pipes , prior backfilling , from sta. 2+500-2+662.82 at RHS	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-130-A	Check Bench Mark (BM). and design control point , from Sta. 3+000-3+600	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-131-A	Check Rebars work for Retaining Wall for Sta. 2+490, 2+500 and 2+510 at RHS	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-132-A	Check Installation of House connection (200 mm)for sewer line for (M# 3-M#2-M#1-M# 1-a)	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-133-A	Check subgrade layer , level , coordinate from Sta. 2+420-2+580 at RHS	03/27/14	03/29/14	03/30/14	1	C
	IR-13-00014-NAB-133-B	Check subgrade layer , level , coordinate from Sta. 2+420-2+580 at RHS	03/30/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-134-A	Check Single size around storm water manhole (M# 39-M# 51)	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-135-A	Check Topping layer from St. 2+120-2+580, at RHS	03/27/14	03/29/14	03/30/14	1	C
	IR-13-00014-NAB-135-B	Check Topping layer from St. 2+120-2+580, at RHS	03/31/14	03/31/14	03/31/14	0	A
	IR-13-00014-NAB-136-A	Check Rebars ,to proceed casting concrete for storm water manhole walls, for (M# 54-M# 53)	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-137-A	Check casting concrete for Retaining Wall , at St. 2+490- 2+500-2+510-2+339-and 2+344 at RHS	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00014-NAB-138-A	Check base course 1st layer under Retaining Wall . From St .2+740 to Sta.2+850 at RHS	03/30/14	03/30/14	03/30/14	0	A
	IR-13-00014-NAB-139-A	Check base course 2nd layer under Retaining Wall . From St .2+740 to Sta.2+850 at RHS	03/31/14	03/31/14	03/31/14	0	A
	IR-13-00014-NAB-140-A	Check rebar for storm water manhole wall to proceed casting concrete for M#45	03/31/14	03/31/14	03/31/14	0	A
	IR-13-00014-NAB-141-A	Check rebar for storm water manhole wall to proceed casting concrete for M#55	03/31/14	03/31/14	03/31/14	0	C
	IR-13-00014-NAB-141-B	Check rebar for storm water manhole wall to proceed casting concrete for M#55	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00014-NAB-142-A	Check casting blinding concrete for Retaining Wall from St. 2+740-2+850 at RHS	03/31/14	03/31/14	03/31/14	0	A
	IR-13-00014-NAB-143-A	to check start excavation , removal existing asphalt layer and deposit it from site , form Sta. 3+000-3+300 at LHS	04/01/14	04/01/14	04/01/14	0	A
	IR-13-00014-NAB-144-A	Check Rebar work to proceed casting concrete for storm water manhole wall for (M# 38) at Sta. 2+084 , at LHS	04/01/14	04/01/14	04/01/14	0	A
	IR-13-00014-NAB-145-A	Check backfilling (single size)around storm water manhole for (M# 54) at Sta. 2+680 , and for (M# 53) at Sta. 2+720	04/01/14	04/01/14	04/01/14	0	A
	IR-13-00014-NAB-146-A	Check leakage test for sewer line, from (M# 03-M#01-a)	04/01/14	04/01/14	04/02/14	1	A
	IR-13-00014-NAB-147-A	Check design control point , from Sta. 3+000-4+320	04/01/14	04/01/14	04/02/14	1	C
	IR-13-00014-NAB-147-B	Check design control point , from Sta. 3+000-4+300	04/03/14	04/03/14	04/03/14	0	A
	IR-13-00014-NAB-148-A	Check Rebar work to proceed casting concrete for storm water manhole wall for (M# 52 at Sta. 2+740	04/02/14	04/02/14	04/02/14	0	A
	IR-13-00014-NAB-149-A	Check Excavation for 3" water pipeline trench , dimensions , level, coordinate , from Sta. 2+020-2+500 at LHS	04/03/14	04/03/14	04/03/14	0	A
	IR-13-00014-NAB-150-A	Excavation for base of Retaining Wall , dimensions , level, coordinate , from Sta. 2+880-2+916 at RHS to Proceed Base course layers	04/03/14	04/03/14	04/03/14	0	A
	IR-13-00014-NAB-151-A	Check Rebar work for storm water manhole (M# 58) at St 2+960 to proceed casting concrete	04/03/14	04/03/14	04/03/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-152-A	Check backfilling single size for storm water manhole (M# 45) at St. 2+320	04/03/14	04/03/14	04/03/14	0	A
	IR-13-00014-NAB-153-A	Check Excavation for base of Retaining Wall , dimensions, from Sta. 2+937-2+954, 2+965-2+980 at RHS to Proceed Base course layers	04/03/14	04/03/14	04/03/14	0	A
	IR-13-00014-NAB-154-A	Check casting concrete for storm water manhole base M# 61 at St. 2+870	04/03/14	04/03/14	04/06/14	3	C
	IR-13-00014-NAB-154-B	Check casting concrete for storm water manhole base M# 61 at St. 2+870	04/08/14	04/08/14	04/09/14	1	A
	IR-13-00014-NAB-155-A	Check casting concrete for storm water manhole walls (M# 60 at St. 2+880-M# 59 at St 2+920).	04/03/14	04/05/14	04/06/14	1	C
	IR-13-00014-NAB-155-B	Check casting concrete for storm water manhole walls (M# 60 at St. 2+880-M# 59 at St 2+920).	04/06/14	04/06/14	04/06/14	0	C
	IR-13-00014-NAB-155-C	Check casting concrete for storm water manhole walls (M# 59 at St 2+920).	04/07/14	04/07/14	04/07/14	0	A
	IR-13-00014-NAB-156-A	Check Excavation , bedding , installation and backfilling of 16" storm water catch basin from St. 2+084-0+580 at RHS	04/03/14	04/05/14	04/06/14	1	C
	IR-13-00014-NAB-156-B	Check Excavation , bedding , installation and backfilling of 16" storm water catch basin from M#48-M#51 at RHS	04/06/14	04/06/14	04/07/14	1	A
	IR-13-00014-NAB-157-A	Check Base Course 1st layer under foundation of Retaining Wall from St. 2+880-2+916, from St. 2+937-2+954, and from St. 2+965-2+980 at RHS	04/03/14	04/05/14	04/06/14	1	A
	IR-13-00014-NAB-158-A	Check Rebars work for foundation of Retaining from St. 2+740-2+850 at RHS	04/03/14	04/05/14	04/06/14	1	A
	IR-13-00014-NAB-159-A	Check casting concrete for foundation of Retaining from St. 2+740-2+850 at RHS	04/06/14	04/06/14	04/06/14	0	A
	IR-13-00014-NAB-160-A	check start excavation , removal existing asphalt layer and deposit it from site , form Sta. 3+000-3+400 at RHS	04/06/14	04/06/14	04/06/14	0	A
	IR-13-00014-NAB-161-A	Check rebar work for storm water manhole walls (M# 60 at St. 2+880-M# 59 at St 2+920).	04/06/14	04/06/14	04/06/14	0	A
	IR-13-00014-NAB-162-A	Check Base Course 2 nd layer under foundation of Retaining Wall from St. 2+880-2+916	04/06/14	04/06/14	04/06/14	0	A
	IR-13-00014-NAB-163-A	Check casting blinding concrete for foundation of Retaining from St. 2+880-2+916 at RHS	04/06/14	04/06/14	04/06/14	0	A
	IR-13-00014-NAB-164-A	Check backfilling single size for storm water manhole (M#58-52-38)	04/07/14	04/07/14	04/07/14	0	A
	IR-13-00014-NAB-165-A	Check Excavation , bedding , installation and backfilling of 16" storm water catch basin from M#41-M#43 at RHS	04/07/14	04/07/14	04/08/14	1	A
	IR-13-00014-NAB-166-A	Check rebar work for Retaining Wall, from Sta. 2+740-2+745, 2+750-2+760 RHS a to proceed casting Backfilling	04/08/14	04/08/14	04/08/14	0	A
	IR-13-00014-NAB-167-A	Check rebar work for Retaining Wall, from Sta. 2+770-2+780, RHS a to proceed casting Backfilling	04/09/14	04/09/14	04/09/14	0	D
	IR-13-00014-NAB-167-B	Check rebar work for Retaining Wall, from Sta. 2+770-2+780, RHS a to proceed casting Backfilling	04/09/14	04/09/14	04/09/14	0	A
	IR-13-00014-NAB-168-A	Check Excavation , bedding , installation and backfilling of 16" storm water catch basin from M#48-M#46-M# 45-M#44 at LHS	04/09/14	04/09/14	04/09/14	0	C
	IR-13-00014-NAB-168-B	Check Excavation , bedding , installation and backfilling of 16" storm water catch basin from M#48-M#46-M# 45-M#44 at LHS	04/28/14	04/28/14	04/28/14	0	C
	IR-13-00014-NAB-169-A	Check casting concrete for Retaining Wall, from Sta. 2+740-2+745, 2+750-2+760 RHS	04/09/14	04/09/14	04/09/14	0	A
	IR-13-00014-NAB-170-A	Check casting concrete for Retaining Wall, from St. 2+770-2+780 - RHS	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00014-NAB-171-A	Check casting concrete for foundation of Retaining Wall, from St. 2+880-2+916 - RHS	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00014-NAB-172-A	Check rebar work for storm water manhole M# 55 at St. 2+640, M# 61 at St.2+872	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00014-NAB-173-A	Check Base Course 1st layer under foundation of Retaining Wall from St. 2+937-2+954, and from St. 2+965-2+980 at RHS	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00014-NAB-174-A	Rebar work for Retaining Wall , from St. 2+790-2+800- RHS	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00014-NAB-175-A	Requested Check rebar work for Retaining Wall ,to proceed formwork from St. 2+810-2+820- RHS	04/10/14	04/12/14	04/13/14	1	A
	IR-13-00014-NAB-176-A	Check casting concrete for Retaining Wall , from St. 2+790-2+800-and from St. 2+810-2+820- RHS	04/10/14	04/12/14	04/13/14	1	A
	IR-13-00014-NAB-177-A	Excavation , bedding , installation and backfilling of 16" storm water catch basin from St. 2+140-2+480 RHS	04/10/14	04/12/14	04/13/14	1	A
	IR-13-00014-NAB-178-A	Check bedding layer , installation of 12 " pipes , welding pipes , prior backfilling , from sta. 3+000-3+400 at RHS	04/10/14	04/12/14	04/12/14	0	A
	IR-13-00014-NAB-179-A	Requested Check casting blinding concrete for base of retaining wall from St. 2+937-2+954, and from St. 2+965-2+980 RHS	04/10/14	04/12/14	04/13/14	1	A
	IR-13-00014-NAB-180-A	Check casting concrete for storm water mnahole wall for M# 55 at St. 2+640, M# 61at St. 2+872	04/12/14	04/12/14	04/13/14	1	A
	IR-13-00014-NAB-181-A	Check Topping layer from St. 2+300-2+580, at RHS	04/12/14	04/12/14	04/13/14	1	A
	IR-13-00014-NAB-182-A	Check rebar work for Retaining Wall from St. 2+830-2+840	04/13/14	04/13/14	04/13/14	0	A
	IR-13-00014-NAB-183-A	Check Excavation , bedding , installation of 16" storm water catch basin from M# 52 at St. 2+740- LHS	04/13/14	04/13/14	04/14/14	1	A
	IR-13-00014-NAB-184-A	Check rebar work for Retaining Wall to proceed formwork , from St. 2+745-2+750 -RHS	04/13/14	04/13/14	04/13/14	0	A
	IR-13-00014-NAB-185-A	Check excavation work for Retaining Wall, from St. 3+006-3+016 -RHS And from St. 3+240-3+300- RHS	04/14/14	04/14/14	04/14/14	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-185-B	Check excavation work for Retaining Wall, from St. 3+006-3+016 -RHS And from St. 3+240-3+300- RHS	04/17/14	04/17/14	04/17/14	0	A
	IR-13-00014-NAB-186-A	Check rebar work for Retaining Wall to proceed formwork , from St. 2+760-2+770 -RHS	04/14/14	04/14/14	04/14/14	0	A
	IR-13-00014-NAB-187-A	Chec Topping layer , from st. 2+100-2+580 LHS	04/14/14	04/14/14	04/14/14	0	A
	IR-13-00014-NAB-188-A	Check casting concrete for retaining wall from St. 2+745-2+750, 2+760-2+770, 2+830-2+840	04/14/14	04/14/14	04/14/14	0	A
	IR-13-00014-NAB-189-A	Check casting concrete for base of retaining wall from St. 2+937-2+954, and from St. 2+965-2+980 RHS	04/14/14	04/14/14	04/14/14	0	A
	IR-13-00014-NAB-190-A	Check rebar work for retaining wall from St. 2+780 to 2+790 – RHS	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00014-NAB-191-A	Check rebar work for retaining wall from St. 2+800 to 2+810 – RHS	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00014-NAB-192-A	Check Excavation , bedding , installation of 16" storm water catch basin from M# 60 at St. 2+900-M# 59 at St.2+940-M#58 at St.2+980	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00014-NAB-193-A	Check backfilling (single size) around storm water manhole fro M# 61 at St. 2+872, M# 55 at St. 2+620	04/15/14	04/15/14	04/15/14	0	C
	IR-13-00014-NAB-193-B	Check backfilling (single size) around storm water manhole fro M# 61 at St. 2+872, M# 55 at St. 2+620	04/22/14	04/22/14	04/22/14	0	A
	IR-13-00014-NAB-194-A	Check casting concrete for retaining wall from St. 2+780 to 2+790, and from St. 2+800-to 2+810 – RHS	04/15/14	04/15/14	04/16/14	1	A
	IR-13-00014-NAB-195-A	Check Excavation , bedding , installation of 8" sewer line at St. 2+965	04/15/14	04/15/14	04/15/14	0	C
	IR-13-00014-NAB-195-B	Check Excavation , bedding , installation of 8" sewer line at St. 2+965	04/22/14	04/22/14	04/22/14	0	A
	IR-13-00014-NAB-196-A	Check over lay asphalt layer for Beit Iba detour	04/15/14	04/15/14	04/16/14	1	A
	IR-13-00014-NAB-197-A	Check rebar work for retaining wall to proceed form work , from St. 2+820 to 2+830, 2+840 to 2+850- RHS	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00014-NAB-198-A	Check base course 1st layer under foundation of retaining wall from St. 3+240 to 3+300- RHS	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00014-NAB-199-A	Check casting concrete for retaining wall, from St. 2+820 to 2+830, 2+840 to 2+850- RHS	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00014-NAB-200-A	Check excavation, elevation and dimensions for sewer line trench, from Manhole 08 – Manhole 07	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00014-NAB-201-A	Check Excavation , bedding , installation of 8" house connection for sewer line at St. 2+890, and St. 2+930	04/16/14	04/16/14	04/16/14	0	A
	IR-13-00014-NAB-202-A	Check installation of catch basin manhole M# 40 at St. 2+140, M# 41at St. 2+180, M# 42 at St. 2+200, M#43 at St. 2+260, M# 44 at St. 2+300, M# 45 at St. 2+340 to proceed backfilling	04/17/14	04/17/14	04/17/14	0	A
	IR-13-00014-NAB-203-A	Check leakage testing for sewer line manhole M# 08 at St. 2+280, M# 07 at St. 2+320	04/17/14	04/17/14	04/17/14	0	A
	IR-13-00014-NAB-204-A	Check base course 1st layer , level from St. 2+120-2+400 RHS	04/17/14	04/17/14	04/17/14	0	A
	IR-13-00014-NAB-205-A	Check base course 1st layer under foundation of Retaining Wall from St. 3+006 to 3+018 RHS	04/17/14	04/17/14	04/17/14	0	A
	IR-13-00014-NAB-206-A	Check 2nd layer base course under foundation of Retaining Wall , from St. 3+006-3+018- RHS	04/17/14	04/17/14	04/19/14	2	A
	IR-13-00014-NAB-207-A	Check 2nd layer base course under foundation of Retaining Wall , from St. 3+240 to 3+300 - RHS	04/17/14	04/17/14	04/19/14	2	A
	IR-13-00014-NAB-208-A	Check excavation works for Retaining Wall from St. 3+180 to 3+220 RHS	04/17/14	04/17/14	04/19/14	2	C
	IR-13-00014-NAB-208-B	Check excavation works for Retaining Wall from St. 3+180 to 3+220 RHS	04/24/14	04/26/14	04/26/14	0	A
	IR-13-00014-NAB-209-A	Check rebar work for Retaining Wall to proceed formwork , from St. 2+880 to 2+916, and from St. 2+937 to 2+954 RHS	04/17/14	04/19/14	04/19/14	0	A
	IR-13-00014-NAB-210-A	Check casting concrete for Retaining Wall , from St. 2+880 to 2+916, and from St. 2+937 to 2+954 RHS	04/17/14	04/19/14	04/19/14	0	C
	IR-13-00014-NAB-210-B	Check casting concrete for Retaining Wall , from St. 2+880 to 2+916, and from St. 2+937 to 2+954 RHS	04/20/14	04/20/14	04/20/14	0	A
	IR-13-00014-NAB-211-A	Check Excavation , bedding , installation of 3" water pipeline from St. 2+400 to 2+700	04/17/14	04/19/14	04/19/14	0	A
	IR-13-00014-NAB-212-A	Check Excavation , bedding , installation of electricity sleeve from St. 2+100 to 2+600	04/17/14	04/19/14	04/19/14	0	C
	IR-13-00014-NAB-212-B	Check Excavation , bedding , installation of electricity sleeve from St. 2+100 to 2+601	04/20/14	04/20/14	04/20/14	0	A
	IR-13-00014-NAB-213-A	Check Excavation , bedding , installation of catch basin manhole for M# 46 to M# 51	04/17/14	04/19/14	04/19/14	0	A
	IR-13-00014-NAB-214-A	Check base course 1st layer , level, from St. 2+100 to 2+300 LHS	04/17/14	04/19/14	04/19/14	0	A
	IR-13-00014-NAB-215-A	Check base course 1st layer , level, from St. 2+300 to 2+580 LHS	04/17/14	04/20/14	04/20/14	0	C
	IR-13-00014-NAB-215-B	Check base course 1st layer , level, from St. 2+300 to 2+580 LHS	04/22/14	04/22/14	04/22/14	0	A
	IR-13-00014-NAB-216-A	Check base course 2nd layer , level, from St. 2+120to 2+400 RHS	04/17/14	04/20/14	04/20/14	0	C
	IR-13-00014-NAB-216-B	Check base course 2nd layer , level, from St. 2+120to 2+400 RHS	04/23/14	04/23/14	04/24/14	1	C
	IR-13-00014-NAB-216-C	Check base course 2nd layer , level, from St. 2+120to 2+400 RHS	04/24/14	04/24/14	04/24/14	0	A
	IR-13-00014-NAB-217-A	Check isloation work for Retaining Wall to proceed backfilling from St. 2+740 to 2+850	04/20/14	04/20/14	04/20/14	0	A
	IR-13-00014-NAB-218-A	Inspect a sample of stone wall , from St. 3+160 to 3+190- LHS	04/20/14	04/20/14	04/20/14	0	E
	IR-13-00014-NAB-219-A	Inspect rebar works for foundation of Retaining Wall from St. 3+006 to 3+018 – RHS	04/21/14	04/21/14	04/21/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-220-A	Casting concrete for foundation of Retaining Wall from St. 3+006 to 3+018 – RHS	04/21/14	04/21/14	04/21/14	0	A
	IR-13-00014-NAB-221-A	Inspect excavation work for Retaining Wall , from St. 3+560 to 3+590 –RHS	04/21/14	04/21/14	04/21/14	0	A
	IR-13-00014-NAB-222-A	to inspect check excavation , dimensions, elevations, for Storm water line (600 mm) , from Manholes (M # 58 at St. 2+980 and M# 70 at St. 3+030)	04/21/14	04/21/14	04/21/14	0	A
	IR-13-00014-NAB-223-A	to inspect check excavation , dimensions, elevations, for Storm water line (600 mm) , from Manholes (M # 70 at St. 3+030 and M# 69 at St. 3+080)	04/21/14	04/21/14	04/21/14	0	A
	IR-13-00014-NAB-224-A	inspect bedding materials , installation of concrete pipes 600 mm for storm water line from (M # 58 at St. 2+980 and M# 70 at St. 3+030)	04/21/14	04/21/14	04/22/14	1	A
	IR-13-00014-NAB-225-A	inspect bedding materials , installation of concrete pipes 600mm, for Storm water line from Manholes (M # 70 at St. 3+030 and M# 69 at St. 3+080)	04/21/14	04/21/14	04/22/14	1	A
	IR-13-00014-NAB-226-A	inspect topping layer , level, from St. 2+700 to 2+900 LHS	04/21/14	04/21/14	04/21/14	0	A
	IR-13-00014-NAB-227-A	Check installation of catch basin manhole M# 40 at St. 2+140, M# 41at St. 2+180, M# 42 at St. 2+200, M#43 at St. 2+260, M# 44 at St. 2+300, M# 45 at St. 2+340, M# 46 at St. 2+380, M#47 at St. 2+420, M#48 at St. 2+460, M#49 at St. 2+500, M# 50 at St. 2+540, M# 51 at St. 2+580 –LHS to proceed backfilling	04/21/14	04/21/14	04/22/14	1	C
	IR-13-00014-NAB-227-B	Check installation of catch basin manhole M# 40 at St. 2+140, M# 41at St. 2+180, M# 42 at St. 2+200, M#43 at St. 2+260, M# 44 at St. 2+300, M# 45 at St. 2+340, M# 46 at St. 2+380, M#47 at St. 2+420, M#48 at St. 2+460, M#49 at St. 2+500, M# 50 at St. 2+540, M# 51 at St. 2+580 –LHS to proceed backfilling	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-NAB-228-A	to inspect excavation , bedding , installation of 8" pipes for duct crossing (Road Crossing sleeve) at St. 2+485 both sides , as per SM# 023	04/21/14	04/21/14	04/22/14	1	A
	IR-13-00014-NAB-229-A	Inspect base course 1st layer for Retaining Wall , from st .3+560 to 3+590	04/22/14	04/22/14	04/22/14	0	A
	IR-13-00014-NAB-230-A	to inspectk excavation , dimensions, elevations, for Storm water line (600 mm) , from Manholes (M # 69 at St.3+080 and M# 68 at St. 3+120)	04/22/14	04/22/14	04/22/14	0	A
	IR-13-00014-NAB-231-A	Check bedding layer , installation of 12 " pipes , welding pipes , prior backfilling , from sta. 3+720 to 3+860 at RHS	04/22/14	04/22/14	04/23/14	1	A
	IR-13-00014-NAB-232-A	Check installation of catch basin manhole M# 54 at St. 2+660, M# 53 at St. 2+700, M# 52 at St. 2+740 at RHS to proceed backfilling	04/22/14	04/22/14	04/23/14	1	C
	IR-13-00014-NAB-232-B	Check installation of catch basin manhole M# 54 at St. 2+660, M# 53 at St. 2+700, M# 52 at St. 2+740 at RHS to proceed backfilling	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-NAB-233-A	Excavation , bedding , installation of 8" pipes sewer line (house Connection) at St. 2+740 with total length 11.00 m , and at St. 2+690 with total length 9.00 m at RHS	04/22/14	04/22/14	04/23/14	1	A
	IR-13-00014-NAB-234-A	inspect rebar work for Retaining Wall to proceed formwork from St. 2+965 to 2+980- RHS	04/23/14	04/23/14	04/23/14	0	A
	IR-13-00014-NAB-235-A	to inspect rebar work for Retaining Wall to proceed formwork from St. 3+006 to 3+018 - RHS	04/23/14	04/23/14	04/23/14	0	A
	IR-13-00014-NAB-236-A	inspect base course 2nd layer , for Retaining wall foundation , from St. 3+560 to 3+590- RHS	04/23/14	04/23/14	04/23/14	0	A
	IR-13-00014-NAB-237-A	to inspect Casting concrete for Retaining Wall from St. 2+965 to 2+980-RHS , and from St. 3+006 to 3+018 –RHS	04/23/14	04/23/14	04/23/14	0	C
	IR-13-00014-NAB-237-B	to inspect Casting concrete for Retaining Wall from St. 2+965 to 2+980-RHS , and from St. 3+006 to 3+018 –RHS	04/24/14	04/24/14	04/24/14	0	A
	IR-13-00014-NAB-238-A	inspect rebar work for foundation of Retaining Wall from St. 3+240 to 3+300- RHS	04/23/14	04/23/14	04/23/14	0	A
	IR-13-00014-NAB-239-A	inspect casting concrete for foundation of Retaining Wall from St. 3+240 to 3+300- RHS	04/23/14	04/23/14	04/23/14	0	A
	IR-13-00014-NAB-240-A	12 ¾ OD, ERW welded steel pipes- Toscelik/Tzinorot-steel Grade B sch. 20 ASTM A 53, QTY=2500 m	04/23/14	04/24/14	04/27/14	3	A
	IR-13-00014-NAB-241-A	Check base course 2nd layer , level, from St. 2+400 to 2+580 RHS	04/23/14	04/23/14	04/24/14	1	C
	IR-13-00014-NAB-241-B	Check base course 2nd layer , level, from St. 2+400 to 2+580 RHS	04/24/14	04/24/14	04/24/14	0	A
	IR-13-00014-NAB-242-A	Check base course 2nd layer , level, from St. 2+120 to 2+580 LHS	04/24/14	04/26/14	04/27/14	1	C
	IR-13-00014-NAB-242-B	Check base course 2nd layer , level, from St. 2+120 to 2+580 LHS	04/27/14	04/27/14	04/27/14	0	C
	IR-13-00014-NAB-242-C	Check base course 2nd layer , level, from St. 2+120 to 2+580 LHS	04/27/14	04/27/14	04/28/14	1	A
	IR-13-00014-NAB-243-A	Check base course 1st layer for Retaining Wall foundation from St. 3+180 to 3+220 RHS	04/24/14	04/26/14	04/26/14	0	C
	IR-13-00014-NAB-243-B	Check base course 1st layer for Retaining Wall foundation from St. 3+180 to 3+220 RHS	04/27/14	04/27/14	04/27/14	0	A
	IR-13-00014-NAB-244-A	Inspect rebar work for Retaining Wall from St. 3+240 to 3+300- RHS	04/24/14	04/26/14	04/26/14	0	C
	IR-13-00014-NAB-244-B	Inspect rebar work for Retaining Wall from St. 3+240 to 3+300- RHS	04/27/14	4/27/2014	04/27/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-245-A	Inspect casting concrete for foundation of Retaining Wall from St. 3+240 to 3+300- RHS	04/24/14	04/26/14	04/26/14	0	C
	IR-13-00014-NAB-245-B	Inspect casting concrete for foundation of Retaining Wall from St. 3+240 to 3+300- RHS	04/27/14	04/27/14	04/28/14	1	A
	IR-13-00014-NAB-246-A	Inspect subgrade layer , from st.3+000 to 3+100 -LHS	04/24/14	04/26/14	04/26/14	0	C
	IR-13-00014-NAB-246-B	Inspect subgrade layer , from st.3+000 to 3+100 -LHS	04/27/14	04/27/14	04/27/14	0	C
	IR-13-00014-NAB-246-C	Inspect subgrade layer , from st.3+000 to 3+100 -LHS	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-247-A	Inspect subgrade layer , from st. 2+740 to 2+840 - RHS	04/24/14	04/26/14	04/26/14	0	A
	IR-13-00014-NAB-248-A	Requested for spraying MC to proceed asphalt works (binder layer) 1" from St. 2+120 to 2+580- RHS	04/24/14	04/26/14	04/26/14	0	A
	IR-13-00014-NAB-249-A	Check excavation, bedding and installation of pipes for 12" water pipeline from St. 4+070 to 4+200 – RHS	04/26/14	04/26/14	04/27/14	1	A
	IR-13-00014-NAB-250-A	Check excavation, bedding layer , installation of 3 " pipes, prior backfilling , from sta. 2+900 to 3+300 at LHS	04/27/14	04/27/14	04/28/14	1	A
	IR-13-00014-NAB-251-A	Check isolation 2nd coat prior to start backfilling for Retaining Wall as specification , from St. 2+880 to 2+916 & from St. 2+937 to 2+954 & from St. 2+965 to 2+980 and from St. 3+006 to 3+018- RHS	04/27/14	04/27/14	04/27/14	0	A
	IR-13-00014-NAB-252-A	Check rebar work for Reatining Wall foundation , from st. 3+560 to 3+590- RHS	04/27/14	04/27/14	04/27/14	0	A
	IR-13-00014-NAB-253-A	Check natural ground level , from St. 1+500 to 2+000	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-NAB-254-A	Check subgrade layer , level, from st. 2+680 to 2+740 - RHS	04/28/14	04/28/14	04/28/14	0	C
	IR-13-00014-NAB-254-B	Check subgrade layer , level, from st. 2+680 to 2+740 - RHS	05/06/14	05/06/14	05/06/14	0	A
	IR-13-00014-NAB-255-A	Check base course layer , level, from St. 2+680 to 2+880- LHS	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-NAB-256-A	Check rebar , casting concrete for storm water manhole base , m# 70at St. 3+030 , M# 69 at St. 3+080	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-NAB-257-A	Check topping layer, level from St. 2+740 to 2+840- RHS	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00014-NAB-258-A	Check topping layer, level from St. 2+900 to 3+060- LHS	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00014-NAB-259-A	Check base course 2nd layer under Retaining Wall . From St .3+180 to Sta.3+240 at RHS	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00014-NAB-260-A	Check casting blinding concrete for Retaining Wall foundation from st. 3+180 to 3+240 – RHS	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00014-NAB-261-A	Check rebar works , and casting concrete for storm water manhole base M# 68 at St. 3+120	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00014-NAB-262-A	Check rebar work for storm water manhole wall M# 70 to proceed fromwork	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00014-NAB-263-A	Check rebar work for Retaining Wall from St. 3+566.5 to 3+576.5, and from St. 3+582 to 3+589.5	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00014-NAB-264-A	Check subgrade layer , level from St. 2+940 to 3+040 RHS	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00014-NAB-265-A	Check rebar work for storm water manhole wall M# 69 to proceed fromwork	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00014-NAB-266-A	Inspect casting concrete for Retaining Wall from St. 3+566.50 to 3+576.5, and from St. 3+582.00 to 3+589.5	04/30/14	05/01/14	05/01/14	0	A
	IR-13-00014-NAB-267-A	Inspect rebar , and casting concrete for Retaining Wall foundation , from St. 3+180 to 3+240 –RHS	04/30/14	05/01/14	05/01/14	0	A
	IR-13-00014-NAB-268-A	Inspect excavation works for Retaining Wall from St. 3+341 to 3+370 –RHS	04/30/14	05/01/14	05/01/14	0	C
	IR-13-00014-NAB-268-B	Inspect excavation works for Retaining Wall from St. 3+341 to 3+370 –RHS	05/06/14	05/06/14	05/06/14	0	A
	IR-13-00014-NAB-269-A	Inspect subgrade layer , level, from St. 2+840 to 2+940 –RHS & FROM St. 3+040 to 3+180 RHS , and from St. 3+160 to 3+280 LHS	04/30/14	05/01/14	05/01/14	0	A
	IR-13-00014-NAB-270-A	Check casting concrete for storm water manhole wall , M# 69 at St,. 3+080, M# 70 at St. 3+030	04/30/14	05/01/14	05/01/14	0	A
	IR-13-00014-NAB-271-A	Inspect rebar work for Retaining Wall from St. 3+576.5 to 3+582.00	04/30/14	05/03/14	05/04/14	1	C
	IR-13-00014-NAB-271-B	Inspect rebar work for Retaining Wall from St. 3+576.5 to 3+582.00	05/04/14	05/04/14	05/04/14	0	A
	IR-13-00014-NAB-272-A	Inspect casting concrete for Retaining Wall from St. 3+576.5 to 3+582.00	04/30/14	05/03/14	05/04/14	1	C
	IR-13-00014-NAB-272-B	Inspect casting concrete for Retaining Wall from St. 3+576.5 to 3+582.00	05/05/14	05/05/14	05/05/14	0	A
	IR-13-00014-NAB-273-A	Inspect topping layer , level , from St. 2+840 to 3+000 RHS	05/03/14	05/03/14	05/04/14	1	A
	IR-13-00014-NAB-274-A	Inspect rebar works for storm water manhole wall for M# 68 at St. 3+120	05/04/14	05/04/14	05/04/14	0	A
	IR-13-00014-NAB-275-A	Inspect casting concrete for storm water manhole wall for M# 68 at St. 3+120	05/04/14	05/04/14	05/04/14	0	A
	IR-13-00014-NAB-276-A	Inspect rebar work for retaining wall from St. 3+180 to 3+190 RHS	05/04/14	05/04/14	05/04/14	0	A
	IR-13-00014-NAB-277-A	Inspect rebar work for retaining wall from St. 3+194 to 3+204 RHS	05/04/14	05/04/14	05/04/14	0	A
	IR-13-00014-NAB-278-A	Inspect topping layer, level , from St. 3+000 to 3+160 – RHS	05/04/14	05/04/14	05/04/14	0	A
	IR-13-00014-NAB-279-A	Inspect backfilling single size for storm water manhole M# 70 at St. 3+030 , M# 69 at St. 3+080	05/05/14	05/05/14	05/05/14	0	A
	IR-13-00014-NAB-280-A	Inspect excavation , bedding, and installation of 3" steel pipes from St. 3+160 to 3+385- LHS	05/05/14	05/05/14	05/05/14	0	A
	IR-13-00014-NAB-281-A	Inspect topping layer , level , from St. 3+160 to 3+280- LHS	05/05/14	05/05/14	05/05/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

APCO ArCon CONSTRUCTION AND SERVICES

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-282-A	Inspect casting concrete for Retaining Wall from St. 3+180 to 3+190 , and from St. 3+194 to 3+204	05/05/14	05/05/14	05/05/14	0	A
	IR-13-00014-NAB-283-A	Check isolation work for Retaining wall to proceed backfilling from St. 3+240 to 3+280 RHS	05/05/14	05/05/14	05/05/14	0	C
	IR-13-00014-NAB-283-B	Check isolation work for Retaining wall to proceed backfilling from St. 3+240 to 3+280 RHS	05/06/14	05/06/14	05/06/14	0	C
	IR-13-00014-NAB-283-C	Check isolation work for Retaining wall to proceed backfilling from St. 3+240 to 3+280 RHS	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-284-A	Check excavation work for Retaining Wall foundation from St. 3+284 to 3+294 RHS	05/06/14	05/06/14	05/06/14	0	A
	IR-13-00014-NAB-285-A	check bench mark (BM) from St. 3+500 to 4+100	05/06/14	05/06/14	05/06/14	0	A
	IR-13-00014-NAB-286-A	Check excavation, bedding , installation of 6" electrical sleeves at St. 2+620 with total length 6*27 =162 lm	05/06/14	05/06/14	05/06/14	0	C
	IR-13-00014-NAB-286-B	Check excavation, bedding , installation of 6" electrical sleeves at St. 2+620 with total length 6*27 =162 lm	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-287-A	Check rebar work for Retaining Wall from St. 3+190 to 3+194 , and from St. 3+204 to 3+214 – RHS	05/06/14	05/06/14	05/06/14	0	A
	IR-13-00014-NAB-288-A	Check backfilling single soze around storm water manhole M# 68 at St. 3+120	05/06/14	05/06/14	05/06/14	0	A
	IR-13-00014-NAB-289-A	Check vasting concrete for Retaining Wall from St. 3+190 to 3+194 , and from St. 3+204 to 3+214 – RHS	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-290-A	Check base course 1st layer, under Retaining Wall foundation , from St. 3+284 to 3+294 -RHS	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-291-A	Check backfilling selected materilas behind Retaining Wall from st. 3+240 to 3+280-RHS	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-292-A	Check base course 1st layer, under Retaining Wall foundation , from St. 3+341 to 3+370 -RHS	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-293-A	Check base course 2nd layer, under Retaining Wall foundation , from St. 3+284 to 3+294 -RHS	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-294-A	Check excavation, bedding , installation of 6" electrical sleeves at St. 2+950 with total length 4*27 =108 lm	05/07/14	05/07/14	05/07/14	0	C
	IR-13-00014-NAB-294-B	Check excavation, bedding , installation of 6" electrical sleeves at St. 2+950 with total length 4*27 =108 lm	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-295-A	check excavation , bedding , installation of 6"electrical sleeves , at St. 2+950, with total length 4*27=108 lm	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-296-A	to check alignment for stone wall , from St. 3+375 to 3+402 –LHS and for boundary wall from St. 3+950 to 3+986 LHS, and for boundary wall from St. 3+828 to 3+855 RHS	05/07/14	05/07/14	05/07/14	0	A
	IR-13-00014-NAB-297-A	Check casting blinding concrete for Retaining Wall foundation from ST.3+284 to 2+394- RHS	05/07/14	05/04/14	05/07/14	3	A
	IR-13-00014-NAB-298-A	Inspect excavation , dimensions, elevations, for Storm water line (600 mm) , from Manholes (M # 65 at St. 3+720 and M# 64 at St. 3+760)	05/11/14	05/11/14	05/11/14	0	A
	IR-13-00014-NAB-299-A	Inspect excavation , dimensions, elevations, for Storm water line (600 mm) , from Manholes (M # 64 at St. 3+760 and M# 63 at St. 3+800)	05/11/14	05/11/14	05/11/14	0	A
	IR-13-00014-NAB-300-A	Inspect isolattion work 1st coat for Reatining Wall , from st. 3+180 to 3+220 to proceed 2nd coat	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-301-A	Inspect isolattion work 2ND coat for Reatining Wall , from st. 3+180 to 3+220 to proceed backfilling	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-302-A	Inspect rebar work , and casting concrete for Retaining Wall foundation , from St. 3+560 to 3+566.5- RHS	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-303-A	Inspect base course 2nd layer under Retaining Wall foundation from St. 3+341 to 3+370- RHS	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-304-A	Inspect casting blinding concrete for Retaining Wall foundation from St. 3+341 to 3+370- RHS	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-305-A	Inspect base course 1st layer , level, from St. 2+740 to 2+880 –RHS	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-306-A	Inspect base course 1st layer , level, from St. 2+880 to 3+000 –RHS	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-307-A	Inspect installation , of concrete pipes 600 mm , and bedding for storm water line , from M# 66 at St. 3+680 to M# 65 at St. 3+720	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-308-A	Inspect rebar work , and casting concrete for Retaining Wall foundation , from St. 3+284 to 3+294- RHS	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-309-A	Inspect installation , of concrete pipes 600 mm , and bedding for storm water line , from M# 65 at St. 3+720 to M# 64 at St. 3+760 , and from M# 64 at St. 3+760 to M# 63 at St. 3+800	05/12/14	05/12/14	05/12/14	0	A
	IR-13-00014-NAB-310-A	Check excavation, bedding and installation of catch basin line from M# 70 at St. 3+030 with total length 12.25 m and M# 69 at St. 3+080 with total length 12.25 m – LHS	05/12/14	05/12/14	05/13/14	1	A
	IR-13-00014-NAB-311-A	Inspect rebar work for Retaining Wall from St. 3+284 to 3+294 –RHS to proceed from work	05/13/14	05/13/14	05/13/14	0	A
	IR-13-00014-NAB-312-A	Inspect subgrade layer , level , from St. 3+000 to 3+160- RHS	05/13/14	05/13/14	05/13/14	0	A
	IR-13-00014-NAB-313-A	Check Bench Mark from St. 1+000 to 2+000	05/13/14	05/13/14	05/13/14	0	A
	IR-13-00014-NAB-314-A	Check base course 1st layer , from St. 3+000 to 3+160-RHS	05/13/14	05/13/14	05/13/14	0	A
	IR-13-00014-NAB-315-A	Inspect isolation 1st coat for Retaining Wall from St. 3+560 to 3+590 to proceed 2nd coat	05/13/14	05/13/14	05/13/14	0	A
	IR-13-00014-NAB-316-A	Check excavation, bedding and installation of catch basin line from M# 70 at St. 3+030 & M# 69 at St. 3+080, and M# 68 at St. 3+120 – RHS	05/13/14	05/13/14	05/13/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-317-A	Inspect isolation 2nd coat for Retaining Wall from St. 3+560 to 3+590 to proceed backfilling	05/13/14	05/13/14	05/13/14	0	A
	IR-13-00014-NAB-318-A	Check rebar , casting concrete for base of storm water manhole M# 63 at St. 3+800, M# 64 at St. 3+760, M# 65 at St. 3+720	05/13/14	05/13/14	05/13/14	0	A
	IR-13-00014-NAB-319-A	Check casting concrete for Retaining Wall, from St. 3+284 to 3+294-RHS	05/14/14	05/14/14	05/14/14	0	A
	IR-13-00014-NAB-320-A	Check rebar and casting concrete for Retaining Wall foundation , from St. 3+341 to 3+370-RHS	05/14/14	05/14/14	05/14/14	0	A
	IR-13-00014-NAB-321-A	Check rebar work for storm water manhole wall for M# 65 at St. 3+720	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00014-NAB-322-A	Check topping layer , level, from St. 2+680 to 2+740 –RHS	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00014-NAB-323-A	Check subgrade layer , level, from St. 3+160 to 3+280 –RHS	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00014-NAB-324-A	Check casting concrete for storm water manhole M# 65 at St. 3+720	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00014-NAB-325-A	Check NGL , from St. 4+100 to 4+850	05/15/14	05/15/14	05/15/14	0	C
	IR-13-00014-NAB-325-B	Check NGL , from St. 4+100 to 4+850	05/18/14	05/18/14	05/18/14	0	C
	IR-13-00014-NAB-326-A	Check subgrade layer, from St. 3+480 to 3+600- RHS	05/15/14	05/17/14	05/18/14	1	C
	IR-13-00014-NAB-326-B	Check subgrade layer, from St. 3+440 to 3+540- RHS	05/20/14	05/20/14	05/20/14	0	A
	IR-13-00014-NAB-327-A	Check subgrade layer, from St. 3+700 to 3+860- RHS	05/15/14	05/17/14	05/18/14	1	C
	IR-13-00014-NAB-327-B	Check subgrade layer, from St. 3+700 to 3+860- RHS	05/28/14	05/28/14	05/28/14	0	C
	IR-13-00014-NAB-327-C	Check subgrade layer, from St. 3+700 to 3+860- RHS	05/29/14	05/29/14	05/29/14	0	A
	IR-13-00014-NAB-328-A	Check rebar work for storm water manhole wall , for M# 64 at St. 3+760 , M# 63 at St. 3+800	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00014-NAB-329-A	Check rebar work Retaining Wall, from St. 3+340 to 3+350, and from St. 3+360 to 3+370- RHS to proceed form work	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00014-NAB-330-A	Check excavation , bedding , installation of 12 " water pipeline , from St. 4+100 to 4+400	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00014-NAB-331-A	Check excavation for Junction at St. 2+620	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00014-NAB-332-A	check base course 1st layer , from St. 2+880 to 3+060 - LHS	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00014-NAB-333-A	Inspect solation 1st coat for Retaining Wall , from St. 3+284 to 3+294- RHS to proceed 2nd coat	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-334-A	Check casting concrete for storm water manhole M# 64 at St. 3+760, M3 63 at St. 3+800	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-335-A	Inspect isolation 2nd coat for Retaining Wall , from St. 3+284 to 3+294- RHS to proceed backfilling	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-336-A	Check casting concrete Retaining Wall, from St. 3+340 to 3+350, and from St. 3+360 to 3+370- RHS	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-337-A	Check topping layer , level, from St. 3+160 to 3+260- RHS	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-338-A	Check casting blinding concrete under Retaining all foundation from St. 3+828 to 3+854- RHS	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-339-A	Check backfilling around storm water manhole M# 65 at St. 3+720	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-340-A	Check implementation of traffic control plan from St. 1+380 to 2+000	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-NAB-341-A	Check rebar work for Retaining Wall, from St. 3+350 to 3+360- RHS to proceed shuttering	05/19/14	05/19/14	05/19/14	0	A
	IR-13-00014-NAB-342-A	Check topping layer , for Junction at St. 2+620 to 2+580	05/19/14	05/19/14	05/20/14	1	A
	IR-13-00014-NAB-343-A	Check casting concrete Retaining Wall, from St. 3+350 to 3+360- RHS	05/20/14	05/20/14	05/20/14	0	A
	IR-13-00014-NAB-344-A	Check Back filling around storm water manhole M# 64 at St. 3+760 , M# 63 at St. 3+800	05/20/14	05/20/14	05/20/14	0	A
	IR-13-00014-NAB-345-A	Check casting concrete for Boundary Wall foundation from St. 3+828 to 3+854- RHS	05/20/14	05/20/14	05/20/14	0	A
	IR-13-00014-NAB-346-A	Topping layer , level, from St. 3+060 to 3+160- LHS	05/21/14	05/21/14	05/21/14	0	A
	IR-13-00014-NAB-347-A	Check base course 1st layer , level, from St. 3+160 to 3+280- RHS	05/21/14	05/21/14	05/21/14	0	C
	IR-13-00014-NAB-347-B	Check base course 1st layer , level, from St. 3+160 to 3+280- RHS	05/22/14	05/22/14	05/22/14	0	C
	IR-13-00014-NAB-347-C	Check base course 1st layer , level, from St. 3+160 to 3+280- RHS	05/25/14	05/25/14	05/25/14	0	A
	IR-13-00014-NAB-348-A	Check base course 1st layer , level , for Junction at St. 2+580 to 2+620	05/21/14	05/21/14	05/22/14	1	A
	IR-13-00014-NAB-349-A	Check base course 1st layer , level , for Junction at St. 2+620 to 2+680	05/21/14	05/21/14	05/22/14	1	A
	IR-13-00014-NAB-350-A	Check backfilling single size for 12 " water pipeline , from St. 4+100 to 4+400	05/21/14	05/21/14	05/22/14	1	A
	IR-13-00014-NAB-351-A	Check base course 1st layer , from St. 2+680 to 2+740- RHS	05/22/14	05/22/14	05/22/14	0	A
	IR-13-00014-NAB-352-A	Check excavation for Retaining Wall , from St. 3+650 to 3+690- RHS	05/22/14	05/22/14	05/22/14	0	A
	IR-13-00014-NAB-353-A	Check removal unsuitable materials and replacement with rock fill. Layer , from St. 3+720 to 3+825- RHS	05/22/14	05/22/14	05/22/14	0	A
	IR-13-00014-NAB-354-A	Check base course 1st layer under Retaining Wall foundation , from St. 3+650 to 3+690- RHS	05/22/14	05/22/14	05/22/14	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-354-B	Check base course 1st layer under Retaining Wall foundation , from St. 3+650 to 3+690- RHS	05/24/14	05/24/14	05/24/14	0	A
	IR-13-00014-NAB-355-A	Check rebar work for concrete stairs at St. 3+370- LHS , to proceed form work	05/22/14	05/22/14	05/22/14	0	A
	IR-13-00014-NAB-356-A	Check casting concrete for concrete stairs at St. 3+370- LHS	05/22/14	05/22/14	05/22/14	0	A
	IR-13-00014-NAB-357-A	Check base course 2nd layer under Retaining Wall foundation , from St. 3+650 to 3+690- RHS	05/22/14	05/24/14	05/24/14	0	A
	IR-13-00014-NAB-358-A	Check casting blinding concrete under Retaining Wall foundation , from St. 3+650 to 3+690- RHS	05/22/14	05/24/14	05/24/14	0	A
	IR-13-00014-NAB-359-A	Check excavation , bedding , installation of 12 " water pipeline , from St. 4+400 to 4+600	05/22/14	05/24/14	05/24/14	0	A
	IR-13-00014-NAB-360-A	Check subgrade layer , level, from St. 3+980 to 4+080- RHS	05/22/14	05/24/14	05/24/14	0	A
	IR-13-00014-NAB-361-A	Check base course 1st layer , level, from St. 3+060 to 3+280- LHS	05/22/14	05/24/14	05/24/14	0	A
	IR-13-00014-NAB-362-A	Check base course 2nd layer , level, from St. 2+740 to 3+160- RHS	05/22/14	05/24/14	05/24/14	0	C
	IR-13-00014-NAB-362-B	Check base course 2nd layer , level, from St. 2+740 to 3+160- RHS	05/27/14	05/27/14	05/27/14	0	C
	IR-13-00014-NAB-363-A	Check base course 2nd layer , level, from St. 2+700 to 3+060- LHS	05/22/14	05/24/14	05/24/14	0	C
	IR-13-00014-NAB-363-B	Check base course 2nd layer , level, from St. 2+700 to 3+060- LHS	05/28/14	05/28/14	05/28/14	0	A
	IR-13-00014-NAB-364-A	Check isolation work 1st coat for Retaining Wall , from St. 3+341 to 3+370- RHS to proceed 2nd coat	05/25/14	05/25/14	05/25/14	0	A
	IR-13-00014-NAB-365-A	Check isolation work 2nd coat for Retaining Wall , from St. 3+341 to 3+370- RHS to proceed backfilling	05/25/14	05/25/14	05/25/14	0	A
	IR-13-00014-NAB-366-A	Check rebar work for Retaining Wall foundation , from St. 3+650 to 3+690-RHS to proceed casting concrete	05/26/14	05/26/14	05/26/14	0	A
	IR-13-00014-NAB-367-A	Check rebar work for parapet of stairs at St. 3+370 – RHS	05/26/14	05/26/14	05/26/14	0	A
	IR-13-00014-NAB-368-A	Check casting concrete for parapet of stairs at St. 3+370 – RHS	05/26/14	05/26/14	05/26/14	0	A
	IR-13-00014-NAB-369-A	Check topping layer , level, from St. 3+440 to 3+540- RHS	05/26/14	05/26/14	05/26/14	0	C
	IR-13-00014-NAB-369-B	Check topping layer , level, from St. 3+440 to 3+540- RHS	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-370-A	Check base course 2nd layer surface , for Junction , from St. 2+580 to 2+680 to proceed spray prime coat	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-371-A	Check toping layer , level ,from St. 3+980 to 4+080- RHS	05/27/14	05/27/14	05/27/14	0	C
	IR-13-00014-NAB-371-B	Check toping layer , level ,from St. 3+980 to 4+080- RHS	05/28/14	05/28/14	05/28/14	0	A
	IR-13-00014-NAB-372-A	Excavation , bedding , installation of 12 " water pipeline , from St. 4+600 to 4+700	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-373-A	Check base course 2nd layer , level, from St. 2+680 to 2+740- RHS	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-374-A	Check casting blinding concrete for boundary wall , from St. 3+3+828 to 3+854 - RHS	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-375-A	Check rebar work and casting concrete for boundary wall foundation , from St. 3+3+828 to 3+854 - RHS	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-376-A	Check removal unsuitable materials and replacement with suitable fill material , from St. 3+860 to 3+980- RHS full width	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-377-A	Check base course 2nd layer surface from St. 2+580 to 3+000 RHS, to proceed spray prime coat	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-NAB-378-A	Check rebar work for Retaining Wall from St. 3+670 to 3+680, and from St. 3+680 to 3+690- RHS	05/28/14	05/28/14	05/28/14	0	A
	IR-13-00014-NAB-379-A	Check base course 2nd layer , from St. 3+160 to 3+220- RHS	05/28/14	05/28/14	05/28/14	0	A
	IR-13-00014-NAB-380-A	Check base course 2nd layer surface from St. 2+680 to 3+060 LHS, to proceed spray prime coat	05/29/14	05/29/14	05/29/14	0	A
	IR-13-00014-NAB-381-A	Check casting concrete for Retaining Wall from St. 3+670 to 3+680, and from St. 3+680 to 3+690- RHS	05/29/14	05/29/14	05/29/14	0	A
	IR-13-00014-NAB-382-A	Check base course 1st layer , from St. 3+440 to 3+540- RHS	05/29/14	05/29/14	05/29/14	0	C
	IR-13-00014-NAB-382-B	Check base course 1st layer , from St. 3+440 to 3+540- RHS	06/10/14	06/10/14	06/10/14	0	A
	IR-13-00014-NAB-383-A	Check subgrade layer , from St. 3+540 to 3+600- RHS	05/29/14	05/29/14	05/29/14	0	A
	IR-13-00014-NAB-384-A	Check base course 2nd layer , level , from St. 3+060 to 3+260- LHS	05/29/14	05/29/14	05/29/14	0	C
	IR-13-00014-NAB-384-B	Check base course 2nd layer , level , from St. 3+060 to 3+260- LHS	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-NAB-385-A	Check subgrade layer , level , from St. 3+860 to 3+980- RHS	05/29/14	05/29/14	05/29/14	0	A
	IR-13-00014-NAB-386-A	Check excavation , dimension of sewer line from M# 20 to M#23	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-387-A	Check installation of sewer line , and bedding from M# 20 to M#23	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-388-A	Check rebar work for boundary wall , from St. 3+828 to 3+854- RHS	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-389-A	check rebar work for Retaining wall , from St. 3+650 to 3+660, and from St. 3+670 to 3+680- RHS	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-390-A	Check leakage test for sewer line pipes for M# 21 at St. 3+430 and M# 22 at St. 3+470	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-391-A	Check excavation , dimension of sewer line from M# 23 at St. 3+510 to M#24 at St. 3+560	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-392-A	Check bedding and installation of sewer line from M# 23 at St. 3+510 to M#24 at St. 3+560	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-393-A	Check casting concrete for boundary wall , from St. 3+828 to 3+854- RHS	06/01/14	06/01/14	06/01/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-394-A	Check casting concrete for Retaining wall , from St. 3+650 to 3+660 - RHS	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-395-A	Check casting blinding concrete for Retaining wall foundation , from St. 3+218 to 3+226 -LHS	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-NAB-396-A	Check casting concrete for Retaining wall , from St. 3+670 to 3+680 - RHS	06/02/14	06/02/14	06/02/14	0	A
	IR-13-00014-NAB-397-A	Check leakage test for sewer line pipes for M# 20 at St. 3+407 and M# 21 at St. 3+430	06/02/14	06/02/14	06/02/14	0	A
	IR-13-00014-NAB-398-A	Check subgrade layer, level from St. 3+820 to 4+080 LHS	06/02/14	06/02/14	06/02/14	0	A
	IR-13-00014-NAB-399-A	Check excavation , dimension for storm water manhole , from M# 67 at St. 3+640 to M# 66 at St. 3+680	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00014-NAB-400-A	Check bedding , installation of storm water manhole , from M# 67 at St. 3+640 to M# 66 at St. 3+680	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00014-NAB-401-A	Check isolation 1st coat for boundary wall from St. 3+828 to 3+854- RHS to proceed 2nd coat	06/03/14	06/03/14	06/03/14	0	C
	IR-13-00014-NAB-401-B	Check isolation 1st coat for boundary wall from St. 3+828 to 3+854- RHS to proceed 2nd coat	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-NAB-402-A	Check isolation work 1st coat for Retaining Wall from St. 3+650 to 3+690- RHs to proceed 2nd coat	06/03/14	06/03/14	06/03/14	0	C
	IR-13-00014-NAB-402-B	Check isolation work 1st coat for Retaining Wall from St. 3+650 to 3+690- RHs to proceed 2nd coat	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-NAB-403-A	Check bench mark (BM) from St. 4+100 to 4+700	06/05/14	06/05/14	06/05/14	0	A
	IR-13-00014-NAB-404-A	Check subgrade layer , level from St. 3+480 to 3+600 LHS	06/05/14	06/05/14	06/05/14	0	A
	IR-13-00014-NAB-405-A	Check topping layer , level from St. 3+840 to 4+060 LHS	06/05/14	06/07/14	06/08/14	1	A
	IR-13-00014-NAB-406-A	Check topping layer , level from St. 3+700 to 3+820 RHS	06/05/14	06/07/14	06/08/14	1	A
	IR-13-00014-NAB-407-A	Check topping layer , level from St. 3+500 to 3+600 LHS	06/08/14	06/08/14	06/08/14	0	C
	IR-13-00014-NAB-407-B	Check topping layer , level from St. 3+500 to 3+600 LHS	06/09/14	06/09/14	06/09/14	0	A
	IR-13-00014-NAB-408-A	Check topping layer , level from St. 3+860 to 3+980 RHS	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-NAB-409-A	Check subgrade layer , level from St. 3+720 to 3+820 LHS	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-NAB-410-A	Check the alignment of Retaining Wall from St. 1+865 to 1+935 , and from St. 1+720 to 1+750- RHS	06/09/14	06/09/14	06/09/14	0	A
	IR-13-00014-NAB-411-A	Check isolation 2nd coat for boundary wall from St. 3+828 to 3+854- RHS to proceed backfilling	06/10/14	06/10/14	06/10/14	0	A
	IR-13-00014-NAB-412-A	Check isolation work 2nd coat for Retaining Wall from St. 3+650 to 3+690- RHs to proceed backfilling	06/10/14	06/10/14	06/10/14	0	A
	IR-13-00014-NAB-413-A	Check base course 1st layer and level from St. 3+980 to 4+080 -RHS	06/10/14	06/10/14	06/10/14	0	A
	IR-13-00014-NAB-414-A	Check subgrade layer and level from St. 3+620 to 3+720- LHS	06/10/14	06/10/14	06/10/14	0	A
	IR-13-00014-NAB-415-A	Check topping layer and level from St. 3+720 to 3+820- LHS	06/10/14	06/10/14	06/10/14	0	C
	IR-13-00014-NAB-415-B	Check topping layer and level from St. 3+720 to 3+820- LHS	06/11/14	06/11/14	06/11/14	0	A
	IR-13-00014-NAB-416-A	Check excavation , level and coordinate to proceed casting blinding concrete for box culvert out let wall at St. 3+610	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00014-NAB-417-A	Check shuttering and rebar work for RC stair at St. 3+170 LHS to proceed casting concrete	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00014-NAB-418-A	Check casting blinding concrete for Retaining Wall from St. 1+860 to 1+935 –RHS	06/12/14	06/12/14	06/12/14	0	C
	IR-13-00014-NAB-418-B	Check casting blinding concrete for Retaining Wall from St. 1+860 to 1+935 –RHS	06/15/14	06/15/14	06/15/14	0	A
	IR-13-00014-NAB-419-A	Check excavation , bedding and installation of 16" catch basin , from M# 63 to M# 65	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00014-NAB-420-A	Check base course 1st layer , level from St. 3+500 to 3+600 LHS	06/12/14	06/14/14	06/14/14	0	A
	IR-13-00014-NAB-421-A	Check base course 1st layer , level from St. 3+820 to 4+060 LHS	0612/2014	06/14/14	06/14/14	0	A
	IR-13-00014-NAB-422-A	Check subgrade layer, level from St. 3+620 to 3+720 RHS	06/12/44	06/14/14	06/15/14	1	C
	IR-13-00014-NAB-422-B	Check subgrade layer, level from St. 3+620 to 3+720 RHS	06/16/14	06/16/14	06/16/14	0	A
	IR-13-00014-NAB-423-A	Check subgrade layer, level from St. 1+580 to 1+840 LHS	0612/2014	06/14/14	06/15/14	1	C
	IR-13-00014-NAB-424-A	Check excavation , bedding and installation of 16" catch basin , from M# 63at St. 3+800 , M# 64 at St. 3+760 and M# 65 at St. 3+720 LHS , for M# 66 at St. 3+680 RHS and M# 67 at St. 3+640 RHS	06/15/14	06/15/14	06/15/14	0	A
	IR-13-00014-NAB-425-A	Check `topping layer , level from St. 3+620 to 3+720 –LHS	06/15/14	06/15/14	06/15/14	0	A
	IR-13-00014-NAB-426-A	Check rebar work for box culvert foundation and bream to proceed casting concrete at St. 3+610	06/15/14	06/15/14	06/15/14	0	A
	IR-13-00014-NAB-427-A	Check excavation , bedding and installation of 16" catch basin at M# 67 at St. 3+640 LHS	06/16/14	06/16/14	06/16/14	0	A
	IR-13-00014-NAB-428-A	Check rebar and casting concrete for Retaining Wall foundation from St. 1+860 to 1+935 –RHS	06/16/14	06/16/14	06/16/14	0	A
	IR-13-00014-NAB-429-A	check excavation , dimension and elevation for storm water line from M wadi to M # 1	06/17/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-430-A	Check excavation work dimension for Retaining Wall from St. 1+735 to 1+750 RHS to proceed casting blinding concrete	06/17/14	06/17/14	06/17/14	0	A
	IR-13-00014-NAB-431-A	Check rebar work for Retaining Wall from St. 1+890 to 1+902.5 RHS to proceed formwork	06/17/14	06/17/14	06/17/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-432-A	Check installation , bedding for storm water line from M wadi to M # 01 to proceed backfilling	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-433-A	Check topping layer, level from St. 3+620 to 3+700 RHS , and from St. 3+560 to 3+600 RHS	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-434-A	Check center line , from St. 1+000 to 1+500	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-435-A	Check rebar work for Retaining Wall from St. 1+870 to 1+882 RHS to proceed formwork	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-436-A	Check casting concrete for Retaining Wall from St. 1+870 to 1+882 RHS and from St. 1+890 to 1+902.5	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-437-A	Check Natural Ground Level (NGL) from St. 1+050 to 1+500	06/18/14	06/18/14	06/19/14	1	A
	IR-13-00014-NAB-438-A	Check rebar work for RC stair at St. 3+245 RHS to proceed formwork	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-439-A	Check formwork for RC stair at St. 3+245 RHS to proceed casting concrete	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-NAB-440-A	Check rebar work for box culvert wall to proceed casting concrete at St. 3+610	06/19/14	06/19/14	06/19/14	0	D
	IR-13-00014-NAB-440-B	Check rebar work for box culvert wall to proceed casting concrete at St. 3+610	06/19/14	06/21/14	06/22/14	1	A
	IR-13-00014-NAB-441-A	Check casting blinding concrete for box culvert at St. 3+610	06/19/14	06/19/14	06/19/14	0	A
	IR-13-00014-NAB-442-A	Check excavation , dimension and elevation for storm water line from M#01 at St. 1+690 to M#02 at St. 1+740	06/19/14	06/19/14	06/19/14	0	A
	IR-13-00014-NAB-443-A	Check bedding and installation for storm water line from M#01 at St. 1+690 to M#02 at St. 1740	06/19/14	06/20/14	06/22/14	2	C
	IR-13-00014-NAB-444-A	Check subgrade layer , level and center line from St. 1+660 to 1+600- RHS	06/19/14	06/21/14	06/22/14	1	A
	IR-13-00014-NAB-445-A	Check base course 1st layer , level from St. 3+620 to 3+820 LHS	06/19/14	06/21/14	06/22/14	1	A
	IR-13-00014-NAB-446-A	Check rebar work for Retaining Wall from St. 1+902.5 to 1+913 RHS to proceed formwork	06/19/14	06/21/14	06/22/14	1	A
	IR-13-00014-NAB-447-A	Check rebar work for Retaining Wall from St. 1+863 to 1+870 RHS to proceed formwork	06/19/14	06/21/14	06/22/14	1	A
	IR-13-00014-NAB-448-A	Check rebar work and casting concrete for Retaining Wall foundation from St. 1+913 to 1+935 RHS	06/19/14	06/21/14	06/22/14	1	A
	IR-13-00014-NAB-449-A	Check casting concrete for box culvert wall at St. 3+610	06/19/14	06/21/14	06/22/14	1	A
	IR-13-00014-NAB-450-A	Check excavation , dimensions and elevation for storm water line from M# 06 at St. 1+900 to M# 07 at St. 1+940	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-NAB-451-A	Check excavation , dimensions and elevation for storm water line from M# 02 at St. 1+740 to M# 03 at St. 1+780, from M# 04 at St. 1+820 to M# 05 at St. 1+860	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-NAB-452-A	Check bedding and installation for storm water line from M# 02 at St. 1+740 to M# 03 at St. 1+780, from M# 04 at St. 1+820 to M# 05 at St. 1+860	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-NAB-453-A	Check rebar and casting concrete for Retaining Wall foundation from St. 1+735 to 1+750 RHS	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-NAB-454-A	Check subgrade layer , level and center line from St. 1+680 to 1+780 RHS	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-NAB-455-A	Check casting blinding concrete for box culvert at St. 3+610 RHS	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-NAB-456-A	Check subgrade layer , level and center line from St. 1+780 to 1+880 RHS	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-NAB-457-A	Check rebar work for Retaining Wall from St. 1+913 to 1+935 RHS to proceed formwork	06/23/14	06/23/14	06/23/14	0	A
	IR-13-00014-NAB-458-A	Check rebar work for Retaining Wall from St. 1+735 to 1+750 RHS to proceed formwork	06/23/14	06/23/14	06/23/14	0	A
	IR-13-00014-NAB-459-A	check excavation , elevation and bedding for storm water manhole from M# 02 at St. 1+740 to M# 03 at St. 1+780 to proceed backfilling single size	06/23/14	06/23/14	06/23/14	0	C
	IR-13-00014-NAB-459-B	check excavation , elevation and bedding for storm water manhole from M# 02 at St. 1+740 to M# 03 at St. 1+780 to proceed backfilling single size	06/30/14	06/30/14	06/30/14	0	C
	IR-13-00014-NAB-460-A	Check subgrade layer , level and center line from St. 4+120 to 4+200 LHS	06/23/14	06/23/14	06/23/14	0	C
	IR-13-00014-NAB-460-B	Check subgrade layer , level and center line from St. 4+120 to 4+200 LHS	06/23/14	06/23/14	06/24/14	1	A
	IR-13-00014-NAB-461-A	Check subgrade layer , level and center line from St. 2+020 to 2+080 RHS	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00014-NAB-462-A	Check casting concrete for Retaining Wall from St. 1+735 to 1+750 RHS &1+913 to 1+935 RHS	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00014-NAB-463-A	Check rebars & casting concrete for storm water base manholes # M5 at St. 1+860 & M6 at St 1+900	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00014-NAB-464-A	Check base course 1st layer , level from St. 3+720 to 3+860 RHS	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00014-NAB-465-A	Check base course 1st layer , level from St. 3+620 to 3+720 RHS	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00014-NAB-466-A	Check rebars & casting concrete for storm water manholes base for # M4at St. 1+820	06/25/14	06/25/14	06/26/14	1	A
	IR-13-00014-NAB-467-A	Check rebar for storm water manholes wall for # M5 at St. 1+860	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-NAB-468-A	Check casting concrete for storm water manholes wall for # M5 at St. 1+860	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-NAB-469-A	Check rebar work for storm water manholes wall for # M6 at St. 1+900	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-NAB-470-A	Check excavation, bedding and installation of 12" water pipeline from St. 1+920 to 1+820	06/26/14	06/26/14	06/26/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Nablus- Beit Iba-Deir Sharaf Road
Inspection Request Log - Project 01

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-NAB-471-A	Check isolation work 1st coat for Retaining Wall from St. 1+860 to 1+935 to proceed 2nd coat	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-NAB-472-A	Check casting concrete for storm water manholes wall for # M6 at St. 1+900	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00014-NAB-473-A	Check isolation work 2nd coat for Retaining Wall from St. 1+860 to 1+935 to proceed backfilling	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00014-NAB-474-A	Check excavation, bedding and installation of 12" water pipeline from St. 1+820 to 1+700	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00014-NAB-475-A	Check subgrade layer , level and center line from St. 4+200 to 4+300 LHS	06/26/14	06/28/14	06/29/14	1	C
	IR-13-00014-NAB-475-B	Check subgrade layer , level and center line from St. 4+200 to 4+300 LHS	06/29/14	06/29/14	06/29/14	0	A
	IR-13-00014-NAB-476-A	Check subgrade layer , level and center line from St. 4+120 to 4+250 RHS	06/26/14	06/28/14	06/29/14	1	C
	IR-13-00014-NAB-476-B	Check subgrade layer , level and center line from St. 4+120 to 4+250 RHS	06/29/14	06/29/14	06/29/14	0	A
	IR-13-00014-NAB-477-A	Check subgrade layer , level and center line from St. 3+540 to 3+600 RHS	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00014-NAB-478-A	Check rebar work and casting concrete for box culvert foundation at St. 3+610 RHS	06/26/14	06/28/14	06/29/14	1	C
	IR-13-00014-NAB-479-A	Check excavation , elevation and installation of concrete pipes for storm water line , from manhole M# 08 at St. 1+98 0 to M# 37	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00014-NAB-480-A	Check rebar work for storm water manhole wall M# 04 at St. 1+820 to proceed formwork	06/30/14	06/30/14	06/30/14	0	A
	IR-13-00014-NAB-481-A	Check formwork for storm water manhole wall M# 04 at St. 1+820 to proceed casting concrete	06/30/14	06/30/14	06/30/14	0	A
	IR-13-00014-NAB-482-A	Check topping layer , level from St. 3+440 to 3+500 LHS	06/30/14	06/30/14	06/30/14	0	A
	IR-13-00014-NAB-483-A	Check rebar and formwork for box culvert foundation at St. 3+610 RHS to proceed casting concrete at 11:00 pm	06/30/14	06/30/14	06/30/14	0	C
	IR-13-00014-NAB-483-B	Check rebar and formwork for box culvert foundation at St. 3+610 RHS to proceed casting concrete at 11:00 pm	06/30/14	06/30/14		PE	
	IR-13-00014-NAB-484-A	Check isolation work for storm water manhole wall M# 37 at St. 2+000 to proceed backfilling	06/30/14	06/30/14	06/30/14	0	C

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Deir Sharaf - Tulkarem Road
Inspection Request Log - Project 02

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-DSR-001-A	Implementation of traffic control plan	02/06/14	02/09/14	02/09/14	0	C
	IR-13-00014-DSR-001-B	Implementation of traffic control plan	02/13/14	02/15/14	02/16/14	1	C
	IR-13-00014-DSR-002-A	Inspect Natural Ground Level , from Sta. 0+100-0+700	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-DSR-003-A	Setting out Center Line , from Sta. 0+100-0+700	02/10/14	02/10/14	02/10/14	0	A
	IR-13-00014-DSR-004-A	Setting out Designed Control Point	02/16/14	02/16/14	02/16/14	0	A
	IR-13-00014-DSR-005-A	Start Excavation , from sta. 0+000-0+700	02/22/14	02/22/14	02/22/14	0	D
	IR-13-00014-DSR-005-B	Start Excavation , from sta. 0+000-0+700	02/23/14	02/23/14	02/24/14	1	A
	IR-13-00014-DSR-006-A	Check BM , from sta. 0+000-0+700	02/26/14	02/26/14	02/26/14	0	C
	IR-13-00014-DSR-006-B	Check BM , from sta. 0+000-0+700	03/03/14	03/03/14	03/03/14	0	A
	IR-13-00014-DSR-007-A	Check Subgrade level , from Sta .0+220-0+560	03/10/14	03/10/14	03/10/14	0	C
	IR-13-00014-DSR-007-B	Check Subgrade level , from Sta .0+260-0+440	03/24/14	03/24/14	03/24/14	0	A
	IR-13-00014-DSR-008-A	Check Natural Ground Level , from sta. 0+700-1+200	03/10/14	03/10/14	03/10/14	0	A
	IR-13-00014-DSR-009-A	Start Excavation , from sta. 0+700-1+200	03/10/14	03/10/14	03/10/14	0	D
	IR-13-00014-DSR-010-A	Check Subgrade level , from Sta .0+440-0+560	03/11/14	03/11/14	03/12/14	1	C
	IR-13-00014-DSR-009-B	Excavation and removal existing asphalt layer from Sta. 0+700-0+1+200	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00014-DSR-010-B	Check Subgrade level , from Sta .0+440-0+560	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00014-DSR-011-A	Check excavation, replacement with filling materials , from sta. 0+233-0+255, at RHS and from 0+530-0+579 at C.L	03/16/14	03/16/14	03/16/14	0	A
	IR-13-00014-DSR-012-A	Check Excavation, from Sta 0+150-0+200, and from Sta. 0+200-0+445 at LHS, and from 0+560-0+680 at LHS	03/22/14	03/22/14	03/23/14	1	A
	IR-13-00014-DSR-013-A	Check Subgrade level , coordianate , from Sta .0+560-0+660	03/24/14	03/24/14	03/24/14	0	A
	IR-13-00014-DSR-014-A	Check Subgrade level , coordianate , from Sta .0+150-0+260	03/27/14	03/27/14	03/27/14	0	C
	IR-13-00014-DSR-014-B	Check Subgrade level , coordianate , from Sta .0+150-0+260	03/30/14	03/30/14	03/30/14	0	A
	IR-13-00014-DSR-015-A	Check Bench Mark , from St. 0+700-1+200	03/30/14	03/30/14	03/30/14	0	A
	IR-13-00014-DSR-016-A	Check Pulverization layer , coocrdinate , from St. 0+480-0+650	03/31/14	03/31/14	04/01/14	1	A
	IR-13-00014-DSR-017-A	Check Natural Ground Level , and center line from sta. 1+200-1+800	04/01/14	04/01/14	04/01/14	0	A
	IR-13-00014-DSR-018-A	Check start Removal existing asphalt layer , from St. 1+200-1+800	04/01/14	04/01/14	04/01/14	0	D
	IR-13-00014-DSR-018-B	Check start Removal existing asphalt layer , from St. 1+200-1+800	04/03/14	04/03/14	04/03/14	0	A
	IR-13-00014-DSR-019-A	Check Pulverization layer , coocrdinate , from St. 0+150-0+480	04/03/14	04/05/14	04/06/14	1	A
	IR-13-00014-DSR-020-A	Base course layer , level , Coordinate, from Sta. 0+660 - 0+900	04/10/14	04/10/14	04/10/14	0	A
	IR-13-00014-DSR-021-A	Check subgrade layer , level , Coordinate from Sta. 0+800 - 1+100	04/10/14	04/12/14	04/13/14	1	A
	IR-13-00014-DSR-022-A	Check Excavation and Replacement with filling materials , from (0+870 to 0+880) R.H.S , (0+670 to 0+720) L.H.S) , (0+720 to 0+731)L.H.S, (0+760 to 0+780) L.H.S, (0+810 to 0+830) L.H.S and (0+940 to 0+1090) L.H.S	04/13/14	04/13/14	04/13/14	0	A
	IR-13-00014-DSR-023-A	Check base course layer , level and coordinate from St. 0+440-0+640	04/14/14	04/14/14	04/14/14	0	A
	IR-13-00014-DSR-024-A	Check pulverization layer , level and coordinate from St. 0+650-0+880	04/14/14	04/14/14	04/14/14	0	C
	IR-13-00014-DSR-024-B	Check pulverization layer , level and coordinate from St. 0+650-0+880	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00014-DSR-025-A	Check topping , level , Coordinate, and compaction test from Sta. 0+800 - 1+100	04/15/14	04/15/14	04/15/14	0	A
	IR-13-00014-DSR-026-A	Check base course layer , level , Coordinate, and compaction test from Sta. 0+260 to 0+440	04/17/14	04/17/14	04/17/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Deir Sharaf - Tulkarem Road
Inspection Request Log - Project 02

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-DSR-027-A	Check subgrade layer , level , Coordinate, from Sta.1+040 to 1+200	04/23/14	04/23/14	04/23/14	0	A
	IR-13-00014-DSR-028-A	Check base course 1st layer , level , Coordinate, from Sta. 0+640 - 1+000	04/26/14	04/26/14	04/27/14	1	A
	IR-13-00014-DSR-029-A	Check bedding materials and installation for road crossing duct diameter (6 in) at sta. 0+440 , sta.0+720 and	04/26/14	04/26/14	04/27/14	1	A
	IR-13-00014-DSR-030-A	Check excavation ,elevation for road crossing duct diameter (6 in) at sta. 0+440 , sta.0+720 and sta. 1+000	04/26/14	04/26/14	04/27/14	1	A
	IR-13-00014-DSR-031-A	Check pulverization layer , level , Coordinate, from Sta.1+040 to 1+200	04/27/14	04/27/14	04/27/14	0	A
	IR-13-00014-DSR-032-A	Check Bench Mark , from St. 1+200 to 1+800	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-DSR-033-A	Check Subgrade layer , level , and Coordinate from Sta. 1+200 to Sta. 1+400	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-DSR-034-A	Check excavation, bedding, installation of 8" UPVS pipes for sewer line at St. 1+000	04/28/14	04/28/14	04/28/14	0	A
	IR-13-00014-DSR-035-A	Check excavation, bedding, installation of 8" UPVS pipes for sewer line at St. 0+440	04/29/14	04/29/14	04/29/14	0	A
	IR-13-00014-DSR-036-A	Check NGL , from st. 1+800 to 2+100	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00014-DSR-037-A	Check Subgrade layer , level , and Coordinate from Sta. 1+400 to Sta. 1+600	04/30/14	05/03/14	05/04/14	1	A
	IR-13-00014-DSR-038-A	Check Pulverization layer , level and, Coordinate, from Sta. 1+200 - 1+400	05/05/14	05/05/14	05/05/14	0	A
	IR-13-00014-DSR-039-A	Check Subgrade layer , level , and Coordinate from Sta. 1+600 to Sta. 1+800	05/05/14	05/05/14	05/05/14	0	A
	IR-13-00014-DSR-040-A	check excavation and replacement with filling materials , from (1+280 to 1+325) L.H.S , (1+460 to 1+520)	05/14/14	05/14/14	05/14/14	0	A
	IR-13-00014-DSR-041-A	Check Pulverization layer , level and, Coordinate, from Sta. 1+400 - 1+520	05/14/14	05/14/14	05/14/14	0	A
	IR-13-00014-DSR-042-A	Check Excavation and Replacement with filling materials , from (1+880 to 2+020) R.H.S	05/14/14	05/14/14	05/14/14	0	A
	IR-13-00014-DSR-043-A	Check start delivering , spreading base course 2nd layer , from St. 0+260 to 0+550	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00014-DSR-044-A	Check Subgrade layer , level , and Coordinate from Sta. 1+800 to Sta. 2+100	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00014-DSR-045-A	Check excavation , bedding , installation of pipe culvert at St. 0+860	05/15/14	05/15/14	05/18/14	3	A
	IR-13-00014-DSR-046-A	Check backfilling single size around pipe culvert at St. 0+860	05/15/14	05/15/14	05/18/14	3	A
	IR-13-00014-DSR-047-A	Check excavation , bedding , installation of 6" future sleeves at St. 1+870 to proceed backfilling	05/15/14	05/15/14	05/18/14	3	A
	IR-13-00014-DSR-048-A	Check base course 1st layer , level , from Sta. 1+000 to Sta. 1+200	05/15/14	05/17/14	05/18/14	1	A
	IR-13-00014-DSR-049-A	Check pulverization layer, level , from St. 1+520 to 1+800	05/15/14	05/17/14	05/18/14	1	C
	IR-13-00014-DSR-049-B	Check pulverization layer, level , from St. 1+520 to 1+800	05/18/14	05/18/14	05/19/14	1	A
	IR-13-00014-DSR-050-A	Check start delivering , spreading base course 2nd layer , from St. 0+550 to 1+000	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-DSR-051-A	Check excavation , bedding and installation of sewer line pipes at St. 1+100	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-DSR-052-A	Check backfilling single size around sewer pips at St. 1+100	05/18/14	05/18/14	05/18/14	0	A
	IR-13-00014-DSR-053-A	C heck pulverization layer , level , from St. 1+800 to 2+020	05/19/14	05/19/14	05/19/14	0	D
	IR-13-00014-DSR-053-B	C heck pulverization layer , level , from St. 1+800 to 2+020	05/21/14	05/21/14	05/21/14	0	A
	IR-13-00014-DSR-054-A	Check subgrade layer , level , from St. 2+020 to 2+100	05/19/14	05/19/14	05/19/14	0	D
	IR-13-00014-DSR-055-A	Check excavation , bedding , and installation of future sleeves at St. 1+460 to proceed backfilling	05/21/14	05/21/14	05/21/14	0	A
	IR-13-00014-DSR-056-A	Check subgrade layer , level from St. 2+020 to 2+080	05/22/14	05/24/14	05/24/14	0	A
	IR-13-00014-DSR-057-A	Check alignment for step barrier , from St. 1+300 to 1+900 as Per SM-033	05/25/14	05/25/14	05/25/14	0	C
	IR-13-00014-DSR-058-A	Check alignment for step barrier , from St. 1+300 to 1+440 as Per SM-033	05/26/14	05/26/14	05/26/14	0	A
	IR-13-00014-DSR-059-A	Check rebar work for step barrier from St. 1+300 to 1+345 to proceed casting concrete	05/26/14	05/26/14	05/27/14	1	A
	IR-13-00014-DSR-060-A	Check excavation , bedding& installation of pipe culvert at St. 1+480	05/27/14	05/27/14	05/27/14	0	A
	IR-13-00014-DSR-061-A	Check backfilling single size for pipe culvert at St. 1+480	027/2014	05/27/14	05/27/14	0	A
	IR-13-00014-DSR-062-A	Check casting concrete for step barrier from St. 1+300 to 1+345	027/2014	05/27/14	05/27/14	0	A
	IR-13-00014-DSR-063-A	Check rebar work for step barrier beam from St. 1+345 to 1+390 to proceed casting concrete	05/27/14	05/27/14	05/27/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Deir Sharaf - Tulkarem Road
Inspection Request Log - Project 02

APCO/ArCon CONSTRUCTION AND SERVICES

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-DSR-064-A	Check subgrade layer , level , and Coordinate from Sta. 2+080 to Sta. 2+180	05/28/14	05/28/14	05/28/14	0	A
	IR-13-00014-DSR-065-A	Check rebar work for step barrier beam from St. 1+390 to 1+435 to proceed casting concrete	05/29/14	05/29/14	05/29/14	0	A
	IR-13-00014-DSR-066-A	Check Base Course second Layer, level , and Coordinate from Sta. 0+260 to Sta. 0+500	05/29/14	05/31/14	06/01/14	1	C
	IR-13-00014-DSR-066-B	Check Base Course second Layer, level , and Coordinate from Sta. 0+260 to Sta. 0+500	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-067-A	Check excavation work for the wall of inlet of pipe culvert at St. 0+860	05/29/14	05/31/14	06/01/14	1	A
	IR-13-00014-DSR-068-A	Check casting blinding concrete for inlet of pipe culvert at St. 0+860	05/29/14	05/31/14	06/01/14	1	A
	IR-13-00014-DSR-069-A	Check rebar work for step barrier beam from St. 1+435 to 1+457 to proceed casting concrete	05/29/14	05/31/14	06/01/14	1	A
	IR-13-00014-DSR-070-A	Check alignment for step barrier , from St. 1+515 to 1+585	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-DSR-071-A	Check rebar work for step barrier beam , from St. 1+515 to 1+585	06/01/14	06/01/14	06/01/14	0	A
	IR-13-00014-DSR-072-A	Check casting concrete for step barrier beam, from St. 1+515 to 1+585	06/01/201	06/01/14	06/01/14	0	A
	IR-13-00014-DSR-073-A	Check base course 2nd layer , level , from St.0+500 to 0+840	06/02/14	06/02/14	06/03/14	1	C
	IR-13-00014-DSR-073-B	Check base course 2nd layer , level , from St.0+500 to 0+830	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-074-A	Check alignment for step barrier , from St. 1+585 to 1+605	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00014-DSR-075-A	Check rebar work for step barrier beam , from St. 1+585 to 1+605	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00014-DSR-076-A	Check casting concrete for step barrier beam, from St. 1+585 to 1+605	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00014-DSR-077-A	Check alignment for step barrier beam , from St. 1+605 to 1+650	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-078-A	Check rebar and shuttering work for step barrier beam , from St. 1+605 to 1+650	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-079-A	Check casting concrete for step barrier beam , from St. 1+605 to 1+650	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-080-A	Check rebar and shuttering work for base of the inlet for pipe culvert at St. 0+860	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-081-A	Check casting concrete for base of the inlet for pipe culvert at St. 0+860	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-082-A	Check rebar and shuttering work for base of the inlet for pipe culvert at St. 1+995	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-083-A	Check casting concrete for base of the inlet for pipe culvert at St. 1+995	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-084-A	Check Pulverization layer , level and, Coordinate, from Sta. 2+020 - 2+180	06/03/14	06/03/14	06/04/14	1	A
	IR-13-00014-DSR-085-A	Check the surface of second base course layer to proceed prime coat , from St. 0+260 to 0+830	06/04/14	06/04/14	06/04/14	0	A
	IR-13-00014-DSR-086-A	Check the alignment and elevation of inlet of wall for pipe culvert at St. 0+860	06/04/14	06/04/14	06/05/14	1	A
	IR-13-00014-DSR-087-A	Check the rebar and shuttering of inlet of wall for pipe culvert at St. 0+860	06/04/14	06/04/14	06/05/14	1	A
	IR-13-00014-DSR-088-A	Check casting concrete of inlet of wall for pipe culvert at St. 0+860	06/04/14	06/04/14	06/05/14	1	A
	IR-13-00014-DSR-089-A	Check excavation for Retaining Wall , from St. 1+665 to 1+760	06/04/14	06/04/14	06/05/14	1	A
	IR-13-00014-DSR-090-A	Check rebar and shuttering for Retaining Wall , from St. 1+665 to 1+760 to proceed casting concrete	06/04/14	06/04/14	06/05/14	1	A
	IR-13-00014-DSR-091-A	Check excavation for Retaining Wall , from St. 1+470 to 1+500	06/04/14	06/04/14	06/05/14	1	A
	IR-13-00014-DSR-092-A	Check casting blinding concrete for Retaining Wall , from St. 1+470 to 1+500	06/04/14	06/04/14	06/05/14	1	A
	IR-13-00014-DSR-093-A	Check case course 2nd Layer, level , and coordinate from St. 0+890 to St. 1+120	06/05/14	06/05/14	06/05/14	0	C
	IR-13-00014-DSR-093-B	Check case course 2nd Layer, level , and coordinate from St. 0+890 to St. 1+120	06/07/14	06/07/14	06/08/14	1	A
	IR-13-00014-DSR-094-A	Check alignment of step barrier beam from St. 1+765 to 1+810	06/05/14	06/05/14	06/05/14	0	A
	IR-13-00014-DSR-095-A	Check rebar work of step barrier beam from St. 1+765 to 1+810	06/05/14	06/05/14	06/05/14	0	A
	IR-13-00014-DSR-096-A	Check casting concrete work of step barrier beam from St. 1+765 to 1+810	06/05/14	06/05/14	06/05/14	0	A
	IR-13-00014-DSR-097-A	Check base course 1st Layer, level , and coordinate from St. 1+200 to St. 1+420	06/05/14	06/07/14	06/07/14	0	A
	IR-13-00014-DSR-098-A	Check alignment of step barrier beam from St. 1+810 to 1+855	06/07/14	06/07/14	06/08/14	1	A
	IR-13-00014-DSR-099-A	Check rebar work for step barrier beam from St. 1+810 to 1+855	06/07/14	06/07/14	06/08/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Deir Sharaf - Tulkarem Road
Inspection Request Log - Project 02

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-DSR-100-A	Check formwork for the step barrier beam to proceed casting concrete from St. 1+810 to 1+855	06/07/14	06/07/14	06/08/14	1	A
	IR-13-00014-DSR-101-A	Check rebar work for the inlet of pipe culvert at St. 0+860 to proceed formwork	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-DSR-102-A	Check rebar work Retaining Wall foundation from St. 1+470 to 1+500 to proceed casting concrete	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-DSR-103-A	Check alignment for step barrier beam from St. 1+855 to 1+880	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-DSR-104-A	Check rebar work for step barrier beam from St. 1+855 to 1+880	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-DSR-105-A	Check formwork for step barrier beam from St. 1+855 to 1+880 to proceed casting concrete	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-DSR-106-A	Check alignment and elevation of pipe culvert at St. 1+995 LHS	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-DSR-107-A	Check base course 2nd layer , level from St. 0+830 to 0+890	06/08/14	06/08/14	06/08/14	0	A
	IR-13-00014-DSR-108-A	Check formwork of 2nd head wall of pipe culvert at St. 0+860 to proceed casting concrete	06/08/14	06/08/14	06/09/14	1	A
	IR-13-00014-DSR-109-A	Check base course 2nd layer , level from St. 1+120 to 1+160	06/09/14	06/09/14	06/09/14	0	A
	IR-13-00014-DSR-110-A	Check base course 1st layer , level from St. 2+040 to 2+198	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00014-DSR-111-A	Check formwork for encasement of pipe culvert at St. 1+995 LHS to proceed casting concrete	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00014-DSR-112-A	Check rebar and casting concrete for Retaining Wall foundation from St. 1+470 to 1+500- Part 2	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00014-DSR-113-A	Check casting blinding concrete for the inlet of pipe culvert at St. 1+480	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00014-DSR-114-A	Check the surface of second base course layer to proceed prime coat , from St. 0+820 to 1+140	06/09/14	06/09/14	06/10/14	1	A
	IR-13-00014-DSR-115-A	Check the base course 1st layer and level from St. 1+540 to 1+620	06/10/14	06/10/14	06/11/14	1	A
	IR-13-00014-DSR-116-A	Check the base course 1st layer and level from St. 1+780 to 1+880	06/10/14	06/10/14	06/11/14	1	A
	IR-13-00014-DSR-117-A	Check rebar work for Concrete Wall from St. 1+665 to 1+670	06/10/14	06/10/14	06/11/14	1	A
	IR-13-00014-DSR-118-A	Check formwork for Concrete Wall from St. 1+665 to 1+670 to proceed casting concrete	06/10/14	06/10/14	06/11/14	1	A
	IR-13-00014-DSR-119-A	Check rebar work for concrete wall from St. 1+480 to 1+500 to proceed formwork	06/11/14	06/11/14	06/11/14	0	A
	IR-13-00014-DSR-120-A	Check alignment of step barrier beam from St. 1+665 to 1+710	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00014-DSR-121-A	Check rebar work of step barrier beam from St. 1+665 to 1+710 to proceed formwork	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00014-DSR-122-A	Check formwork of step barrier beam from St. 1+665 to 1+710 to proceed casting concrete	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00014-DSR-123-A	Check rebar work for foundation for the inlet of pipe culvert at St. 1+480 to proceed formwork	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00014-DSR-124-A	Check formwork for the foundation for the inlet of pipe culvert at St. 1+480 to proceed casting concrete	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00014-DSR-125-A	Check base course 2nd layer , from st. 1+150 to 1+420	06/12/14	06/12/14	06/12/14	0	C
	IR-13-00014-DSR-126-A	Check casting concrete for Retaining Wall from St. 1+495 to 1+515	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00014-DSR-127-A	Check rebar work for Retaining Wall from St. 1+744 o 1+754 to proceed formwork	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00014-DSR-128-A	check formwork for Retaining Wall from St. 1+744 o 1+754 to proceed casting concrete	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00014-DSR-129-A	Check rebar wok for inlet wall of pipe culvert at St. 1+480 to proceed formwork	06/14/14	06/14/14	06/15/14	1	A
	IR-13-00014-DSR-130-A	check formwork for inlet wall of pipe culvert at St. 1+480 to proceed casting concrete	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00014-DSR-131-A	check alignment of step barrier beam from St. 1+710 to 1+765	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00014-DSR-132-A	Check rebar work for step barrier beam from St. 1+710 to 1+765 to proceed formwork	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00014-DSR-133-A	Check formwork for step barrier beam from St. 1+710 to 1+765 to proceed casting concrete	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00014-DSR-134-A	Check base course 1st layer , level from St. 1+880 to 1+960	06/15/14	06/15/14	06/16/14	1	A
	IR-13-00014-DSR-135-A	Check base course 2nd layer , level from St. 2+050 to 2+190	06/15/14	06/15/14	06/16/14	1	C
	IR-13-00014-DSR-135-B	Check base course 2nd layer , level from St. 2+050 to 2+190	06/16/14	06/17/14	06/17/14	0	C
	IR-13-00014-DSR-135-C	Check base course 2nd layer , level from St. 2+050 to 2+190	06/22/14	06/22/14	06/22/14		A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Deir Sharaf - Tulkarem Road
Inspection Request Log - Project 02

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-DSR-136-A	Check rebar work for concrete wall from St. 1+470 to 1+480 to proceed formwork	06/15/14	06/15/14	06/16/14	1	A
	IR-13-00014-DSR-137-A	Check formwork for concrete wall from St. 1+470 to 1+480 to proceed casting concrete	06/15/14	06/15/14	06/16/14	1	A
	IR-13-00014-DSR-138-A	Check rebar for retaining wall from St. 1+670 to 1+680 to proceed formwork	06/16/14	06/15/14	06/16/14	1	A
	IR-13-00014-DSR-139-A	Check formwork for retaining wall from St. 1+670 to 1+680 to proceed casting concrete	06/15/14	06/15/14	06/16/14	1	A
	IR-13-00014-DSR-140-A	Check base course 1stlayer , level from St. 1+620 to 1+780	06/17/14	06/17/14	06/17/14	0	A
	IR-13-00014-DSR-141-A	Check the surface of second base course layer to proceed spraying prime coat , from St. 1+140 to 1+420	06/17/14	06/17/14	06/17/14	0	A
	IR-13-00014-DSR-142-A	Check rebar work for concrete wall from St. 1+695 to 1+705 and from St. 1+730 to 1+740 to proceed formwork	06/17/14	06/17/14	06/17/14	0	A
	IR-13-00014-DSR-143-A	Check formwork for concrete wall from St. 1+695 to 1+705 and from St. 1+730 to 1+740 to proceed casting concrete	06/17/14	06/17/14	06/17/14	0	A
	IR-13-00014-DSR-144-A	Check rebar work for encasement of pipe culvert at St. 1+995 to proceed formwork	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-DSR-145-A	Check formwork for encasement of pipe culvert at St. 1+995 to proceed casting concrete	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00014-DSR-146-A	Check formwork for concrete wall from St. 1+695 to 1+705 and from St. 1+730 to 1+740 to proceed casting concrete – Part 2	06/18/14	06/18/14	06/19/14	1	A
	IR-13-00014-DSR-147-A	Check rebar for concrete wall from St. 1+470 to 1+485 to proceed formwork	06/18/14	06/18/14	06/19/14	1	A
	IR-13-00014-DSR-148-A	Check installation of concrete pipe culvert at St. 1+995 RHS	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00014-DSR-149-A	Check rebar work for Retaining Wall from St. 1+470 to 1+485 LHS to proceed formwork	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00014-DSR-150-A	Check formwork for Retaining Wall from St. 1+470 to 1+485 LHS to proceed casting concrete	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00014-DSR-151-A	Check rebar for encasement of pipe culvert at St. 1+995 LHS to proceed formwork	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00014-DSR-152-A	Check formwork for encasement of pipe culvert at St. 1+995 LHS to proceed casting concrete	06/19/14	06/19/14	06/22/14	3	A
	IR-13-00014-DSR-153-A	Check base course 2nd layer , level from St. 1+520 to 1+880	06/19/14	06/21/14	06/23/14	2	C
	IR-13-00014-DSR-154-A	Check the surface of second base course layer to proceed spraying prime coat , from St. 2+050 to 2+200	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00014-DSR-155-A	Check rebar work for Retaining Wall from St. 1+750 to 1+760 LHS to proceed formwork	06/22/14	06/22/14	06/23/14	1	A
	IR-13-00014-DSR-156-A	Check formwork for Retaining Wall from St. 1+750 to 1+760 LHS to proceed casting concrete	06/22/14	06/22/14	06/23/14	1	A
	IR-13-00014-DSR-157-A	Check formwork for Retaining Wall from St. 1+750 to 1+760 LHS and from St. 1+675 to 1+685 LHS –Part 2 to proceed casting concrete	06/23/14	06/23/14	06/24/14	1	A
	IR-13-00014-DSR-158-A	Check formwork and rebar for step barrier from St.(1+475) to St.(1+515)	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00014-DSR-159-A	Check casting concrete B 250 for step barrier from St.(1+475) to St.(1+515)	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00014-DSR-160-A	Check base course 1st layer , level and center line from St. 1+420 to 1+540	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00014-DSR-161-A	Check base course 1st layer , level and center line from St. 1+960 to 2+040	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00014-DSR-162-A	Check rebar work for concrete wall from St. 1+720 to 1+730 to proceed formwork	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00014-DSR-163-A	Check formwork for concrete wall from St. 1+720 to 1+730 to proceed casting concrete	06/25/14	06/25/14	06/25/14	0	A
	IR-13-00014-DSR-164-A	Check rebar work for step barrier from St. 1+300 to1+307.5 to proceed formwork	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-DSR-165-A	Check formwork for step barrier from St. 1+300 to1+307.5 to proceed casting concrete	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-DSR-166-A	Check rebar work for concrete wall from St. 1+720 to 1+730 to proceed formwork –Part 2	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-DSR-167-A	Check formwork for concrete wall from St. 1+720 to 1+730 to proceed casting concrete –Part 2	06/26/14	06/26/14	06/26/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #14, Deir Sharaf - Tulkarem Road
Inspection Request Log - Project 02

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00014-DSR-168-A	Check preparation , laying and shaping base course layer for concrete open ditches from St. 0+460 to 0+580 prior to start concrete open ditch construction	06/26/14	06/26/14	06/26/14	0	A
	IR-13-00014-DSR-169-A	Check preparation , laying and shaping base course layer for concrete open ditches from St. 0+580 to 0+860 prior to start concrete open ditch construction	06/26/14	06/27/14	06/29/14	2	A
	IR-13-00014-DSR-170-A	check rebar work for concrete open ditch to proceed casting concrete from St. 0+460 to 0+860	06/26/14	06/27/14	06/29/14	2	A
	IR-13-00014-DSR-171-A	Check pulverization layer , level from St. 0+250 to 0+120	06/26/14	06/28/14	06/29/14	1	C
	IR-13-00014-DSR-172-A	Chech rebar work for step barrier from St. 1+314.4 to 1+321.6, St. 1+328.8 to 1+336, St. 1+343.2 to 1+350.4 , St. 1+357.6 to 1+364.8, St. 1+372 to 1+379.2 , and from St. 1+386.4 to 1+393.6 to proceed formwork	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00014-DSR-173-A	Check formwork for step barrier from St. 1+314.4 to 1+321.6, St. 1+328.8 to 1+336, St. 1+343.2 to 1+350.4 , St. 1+357.6 to 1+364.8, St. 1+372 to 1+379.2 , and from St. 1+386.4 to 1+393.6 to proceed casting concrete	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00014-DSR-174-A	Check base course 2nd layer , level from St. 1+880 to 2+050	06/29/14	06/29/14	06/29/14	0	C
	IR-13-00014-DSR-175-A	Check excavation and elevation of 3" water pipeline from St. 0+440 to 0+720	06/30/14	06/30/14	06/30/14	0	C
	IR-13-00014-DSR-175-B	Check excavation and elevation of 3" water pipeline from St. 0+440 to 0+720	06/30/14	06/30/14		PE	
	IR-13-00014-DSR-176-A	Check base course 2nd layer , level from St. 1+420 to 1+540	06/30/14	06/30/14	06/30/14	0	A
	IR-13-00014-DSR-177-A	Check rebar work for step barriers from St. 1+307.2 to 1+314.4, St. 1+321.6 to 1+328.8, St. 1+336 to1+343.2 , St. 1+350.4 to 1+357.6 , St. 1+364.8 to 1+372 , St. 1+379.2 to 1+386.4 and from St. 1+393.6 to 1+400.8 to proceed formwork	06/30/14	07/01/14		PE	
	IR-13-00014-DSR-178-A	check formwork for step barriers from St. 1+307.2 to 1+314.4, St. 1+321.6 to 1+328.8, St. 1+336 to1+343.2 , St. 1+350.4 to 1+357.6 , St. 1+364.8 to 1+372 , St. 1+379.2 to 1+386.4 and from St. 1+393.6 to 1+400.8 to proceed casting concrete	06/30/14	07/01/14		PE	
	IR-13-00014-DSR-179-A	Check bedding , installation and welding of 3"water pipeline from St. 0+440 to 0+720 LHS	06/30/14	07/01/14		PE	

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

F | Submittals Log for the Reporting Period

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-MRNII-001-A	30- Days Schedule (Pre Construction Submittals & Mobilization Schedule)	MRNII	P	12/08/13	12/29/13	12/22/13	14	B
	SUB-13-00014-MRNII-002-A	Temporary and Permanent Signs Plan	MRNII	P	12/08/13	12/29/13	12/22/13	14	B
	SUB-13-00014-MRNII-003-A	Bank Guarantee	MRNII	P	12/08/13	12/29/13	12/31/13	23	E
	SUB-13-00014-MRNII-004-A	Subcontracting Plan	MRNII	P	12/22/13	01/12/14	12/31/13	9	E
	SUB-13-00014-MRNII-005-A	Testing Labs	MRNII	P	12/23/13	01/13/14	01/05/14	13	B
	SUB-13-00014-MRNII-006-A	Insurance Policy: Projects 01 and 02 Contractors all Risk Insurance, Amendment No. 1, Commercial General Liability, Vehicle Insurance, and Workmen's Compensation Policy, 2013.	MRNII	P	12/25/13	01/15/14	01/06/14	12	E
	SUB-13-00014-MRNII-007-A	Field Offices Furniture and Equipment List	MRNII	P	12/25/13	01/15/14	12/31/13	6	B
	SUB-13-00014-MRNII-008-A	Branding Plan	MRNII	P	12/25/13	01/15/14	01/07/14	13	E
	SUB-13-00014-MRNII-009-A	Quality Control Program (QCP)	MRNII	P	12/25/13	01/15/14	01/09/14	15	B
	SUB-13-00014-MRNII-010-A	Key Personnel Plan	MRNII	P	12/25/13	01/15/14	12/31/13	6	E
	SUB-13-00014-NAB-011-A	Water drainage RC Pipes - PCP Co. - Project 01- BOQ Item No. 4.02	NAB	M	12/25/13	01/15/14	01/05/14	11	C
	SUB-13-00014-NAB-011-B	Storm water drainage RC Pipes - PCP Co. - Project 01- BOQ Item No. 4.02	NAB	M	01/13/14	02/03/14	01/15/14	2	B
	SUB-13-00014-MRNII-012-A	Prime Coat - Pazkar - BOQ Item No. 3.01	MRNII	M	12/25/13	01/15/14	01/05/14	11	B
	SUB-13-00014-MRNII-013-A	Tack Coat - Pazkar - BOQ Item No. 3.02	MRNII	M	12/25/13	01/15/14	01/05/14	11	B
	SUB-13-00014-MRNII-014-A	Cat Eyes - Iriflex - BOQ Items No. 5.03.b and 5.03.c	MRNII	M	12/25/13	01/15/14	01/05/14	11	B
	SUB-13-00014-MRNII-015-A	Thermoplastic Paint- Prismo- BOQ Item No. 5.03.a	MRNII	M	12/25/13	01/15/14	01/05/14	11	B
	SUB-13-00014-NAB-016-A	UPVC Pipes - Royal Co. - Project 01- BOQ Item No. 4.04	NAB	M	12/25/13	01/15/14	01/13/14	19	A
	SUB-13-00014-MRNII-017-A	Curbstone Marking Paint- Tambour- BOQ Item No. 4.12	MRNII	M	12/25/13	01/15/14	01/05/14	11	B
	SUB-13-00014-MRNII-018-A	Safety Plan	MRNII	P	12/25/13	01/15/14	01/13/14	19	B
	SUB-13-00014-MRNII-019-A	Security System	MRNII	P	12/29/13	01/19/14	01/05/14	7	C
	SUB-13-00014-MRNII-019-B	Security System	MRNII	P	01/16/14	02/06/14	01/16/14	0	B
	SUB-13-00014-MRNII-020-A	Method Statement	MRNII	P	12/29/13	01/19/14	01/13/14	15	C
	SUB-13-00014-MRNII-020-B	Method Statement	MRNII	P	01/21/14	02/11/14	01/22/14	1	B
	SUB-13-00014-NAB-021-A	Survey Plan from Sta.0+000 to Sta. 5+537-Nablus Beit Iba Deir Sharaf Road - Project 01	NAB	P	12/29/13	01/19/14	01/15/14	17	C
	SUB-13-00014-NAB-021-B	Survey Plan from Sta.0+000 to Sta. 5+537-Nablus Beit Iba Deir Sharaf Road - Project 01	NAB	P	01/20/14	02/10/14	01/22/14	2	B
	SUB-13-00014-MRNII-022-A	60-Day Plan of Operation	MRNII	P	12/29/13	01/19/14	01/08/14	10	B
	SUB-13-00014-MRNII-023-A	Submittals Schedule	MRNII	P	12/29/13	01/19/14	01/13/14	15	B
	SUB-13-00014-MRNII-024-A	Project Overview Bar Chart & Master Plan	MRNII	P	12/29/13	01/19/14	01/08/14	10	E
	SUB-13-00014-DSR-025-A	Guardrail ESP4-N2-PRINS DOKKUM-Project 02-item 5.05.a	DSR	M	12/29/13	01/19/14	01/05/14	7	A
	SUB-13-00014-MRNII-026-A	Construction Time Schedule	MRNII	P	12/29/13	01/19/14	01/16/14	18	C
	SUB-13-00014-MRNII-026-B	Construction Time Schedule and S-Curve	MRNII	P	01/26/14	02/16/14	02/09/14	14	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-MRNII-026-C	Construction Time Schedule and S-Curve	MRNII	P	02/20/14	03/13/14	03/04/14	12	A
	SUB-13-00014-NAB-027-A	Traffic Control Plan (Area A and B) Phase I from Sta.2+020 to Sta.5+450-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	12/29/13	01/19/14	01/05/14	7	C
	SUB-13-00014-NAB-027-B	Traffic Control Plan (Area A and B) Phase I from Sta.2+020 to Sta.3+400-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	01/16/14	02/06/14	01/20/14	4	B
	SUB-13-00014-DSR-028-A	Storm Drainage RC pipes -PCP Co-item 4.02-Project 02	DSR	M	12/30/13	01/20/14	01/09/14	10	C
	SUB-13-00014-DSR-028-B	Storm water drainage RC Pipes - PCP Co. - Project 02- BOQ Item No. 4.02	DSR	M	02/03/14	02/24/14	02/05/14	2	B
	SUB-13-00014-MRNII-029-A	Proposed Project Signs Location	MRNII	P	12/30/13	01/20/14	01/05/14	6	B
	SUB-13-00014-NAB-030-A	Pre Cast Concrete Curbstone-Wolfman Co-item 4.12-Project 01	NAB	M	12/30/13	01/20/14	12/31/13	1	A
	SUB-13-00014-DSR-031-A	Pre Cast Concrete Curbstone-Wolfman Co-item 4.12.a-Project 02	DSR	M	12/30/13	01/20/14	12/31/13	1	A
	SUB-13-00014-MRNII-032-A	Coordination with Local Authorities Plan and List of Permits and Licenses	MRNII	P	12/30/13	01/20/14	01/13/14	14	B
	SUB-13-00014-NAB-033-A	JMF for Bituminous Wearing 3/4" -Developed Co-item No. 3.03 -Project 01	NAB	M	12/30/13	01/20/14	01/09/14	10	B
	SUB-13-00014-DSR-034-A	Survey Plan from Sta.0+000 to Sta. 2+592.7 -Project 02	DSR	P	12/31/13	01/21/14	01/14/14	14	B
	SUB-13-00014-NAB-035-A	JMF for Bituminous Binder 1inch_Developed Co_ Project 1_item 3.05	NAB	M	01/02/14	01/23/14	01/09/14	7	B
	SUB-13-00014-MRNII-036-A	Traffic signs material_ Netivey Hamifratz/Top Safety _item 5.01	MRNII	M	01/05/14	01/26/14	01/08/14	3	B
	SUB-13-00014-MRNII-037-A	Primary field office location and layout	MRNII	P	01/06/14	01/27/14	01/09/14	3	B
	SUB-13-00014-MRNII-038-A	Proposed Dumping Area		P	01/06/14	01/27/14	01/13/14	7	B
	SUB-13-00014-NAB-039-A	Dilapidation Survey -Phase 01- Project 01- Segment A	NAB	P	01/07/14	01/28/14	01/16/14	9	B
	SUB-13-00014-NAB-040-A	Shop Drawing: Plan, Profile and Cross Sections from St. 2+000 to St. 2+600-Project 01	NAB	S	01/09/14	01/30/14	01/16/14	7	C
	SUB-13-00014-NAB-040-B	Shop Drawing: Plan, Profile and Cross Sections from St. 2+000 to St. 2+600-Project 01	NAB	S	01/22/14	02/12/14	01/26/14	4	C
	SUB-13-00014-NAB-040-C	Shop Drawing: Plan, Profile and Cross Sections from St. 2+020 to St. 2+590-Project 01	NAB	S	02/04/14	02/25/14	02/09/14	5	B
	SUB-13-00014-DSR-041-A	Shop Drawing: Plan, Profile and Cross Sections from St. 0+100 to St. 0+700-Project 02	DSR	S	01/15/14	02/05/14	01/26/14	11	E
	SUB-13-00014-DSR-041-B	Shop Drawing: Plan, Profile and Cross Sections from St. 0+100 to St. 0+700-Project 02	DSR	S	02/03/14	02/24/14	02/09/14	6	B
	SUB-13-00014-DSR-042-A	Dilapidation Survey- Deer Sharaf Inab Road -Project 02	DSR	P	01/15/14	02/05/14	01/21/14	6	B
	SUB-13-00014-NAB-043-A	Shop Drawing: Storm Water Manholes: Plan ,Profile and Cross Section from Sta.2+020 to Sta.2+540-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	01/16/14	02/06/14	01/26/14	10	C
	SUB-13-00014-NAB-043-B	Shop Drawing: Storm Water : Plan ,Profile and Cross Section from Sta.2+020 to Sta.2+540-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	02/05/14	02/26/14	02/13/14	8	B
	SUB-13-00014-NAB-044-A	Shop Drawing: Water Pipeline: Plan from Sta.2+020 to Sta.2+500-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	01/16/14	02/06/14	01/26/14	10	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-044-B	Shop Drawing: Water Pipeline: Plan from Sta.2+020 to Sta.2+500-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	03/16/14	04/06/14	03/20/14	4	B
	SUB-13-00014-MRNII-045-A	Environmental Mitigation Plan	MRNII	P	01/16/14	02/06/14	01/26/14	10	B
	SUB-13-00014-NAB-046-A	Steel Pipes and fittings-Middle East EN Catalog-Project 01	NAB	M	01/19/14	02/09/14	01/27/14	8	B
	SUB-13-00014-NAB-047-A	Proposed staging and storage yard -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	01/19/14	02/09/14	01/21/14	2	B
	SUB-13-00014-NAB-048-A	Risk Management Program-Phase I from Sta.2+000 to Sta.3+000 -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	01/19/14	02/09/14	01/23/14	4	B
	SUB-13-00014-NAB-049-A	Proposed Welders for welders qualification test - CVs-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	01/20/14	02/10/14	01/26/14	6	B
	SUB-13-00014-NAB-050-A	Shop Drawings: Sewer System: Plan, Profile and Cross Section from Sta.1+900 to Sta.2+540-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	01/20/14	02/10/14	01/30/14	10	C
	SUB-13-00014-NAB-050-B	Shop Drawings: Sewer System: Plan, Profile and Cross Section from Sta.1+900 to Sta.2+540-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	02/02/14	02/23/14	02/09/14	7	B
	SUB-13-00014-DSR-051-A	Base-course Material Source- Abu Khanfa Crusher-Project 02	DSR	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-DSR-052-A	Base-course Material main Source- Abu Shusha Crusher-Project 02	DSR	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-DSR-053-A	Base-course Material Source- Al Ashaqar Crusher-Project 02	DSR	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-DSR-054-A	Single size aggregate material source -Project 02	DSR	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-DSR-055-A	Bedding (somsom) Material source -Project 02	DSR	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-MRNII-056-A	Water Quality Testing Lab-Scientific Center Co. for Food & Drug Analysis	MRNII	P	01/22/14	02/12/14	01/26/14	4	C
	SUB-13-00014-NAB-057-A	Base-course Material main Source- Abu Shusha Crusher-Project 01	NAB	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-NAB-058-A	Base-course Material Source- Al Ashaqar Crusher-Project 01	NAB	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-NAB-059-A	Base-course Material Source- Abu Khanfa Crusher-Project 01	NAB	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-NAB-060-A	Bedding (somsom) Material source -Project 01	NAB	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-NAB-061-A	Single size aggregate material source -Project 01	NAB	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-NAB-062-A	Topping Material Source- Abu Shusha Crusher-Project 01	NAB	M	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-DSR-063-A	Proposed storage yard and dumping area -Project 02	DSR	P	01/22/14	02/12/14	01/26/14	4	B
	SUB-13-00014-MRNII-064-A	Public Relation Plan	MRNII	P	01/26/14	02/16/14	02/03/14	8	E
	SUB-13-00014-DSR-065-A	Traffic Control Plan -Phase I- from Sta.0+000 to Sta.2+180 -Project 02	DSR	P	01/26/14	02/16/14	02/05/14	10	B
	SUB-13-00014-NAB-066-A	Concrete Mix Ready -Bonyan Ready mix plant -Project 01	NAB	M	01/28/14	02/18/14	02/03/14	6	B
	SUB-13-00014-NAB-067-A	Concrete Mix Ready -Muwasi Ready mix plant -Project 01	NAB	M	01/28/14	02/18/14	02/03/14	6	B
	SUB-13-00014-MRNII-068-A	Shop Drawings: Formwork System for Retaining Wall	MRNII	S	01/29/14	02/19/14	02/09/14	11	B
	SUB-13-00014-DSR-069-A	Risk Management Program - Der Sharaf Tulkarem Road -Project 02	DSR	P	01/29/14	02/19/14	02/05/14	7	B
	SUB-13-00014-NAB-070-A	Square and Circular Manholes- item No. 5.05 and 5.03 -Project 01	NAB	M	01/30/14	02/20/14	02/09/14	10	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-070-B	Square and Circular Manholes- item No. 4.03 and 4.05 -Project 01	NAB	M	02/16/14	03/09/14	02/17/14	1	B
	SUB-13-00014-NAB-071-A	Proposed Dumping Area -Project 01	NAB	P	01/30/14	02/20/14	02/02/14	3	C
	SUB-13-00014-MRNII-072-A	Elecometer 266 Holiday detector	MRNII	M	02/02/14	02/23/14	02/11/14	9	E
	SUB-13-00014-DSR-073-A	Concrete Mix Ready -Bonyan Ready mix plant -Project 02	DSR	M	02/03/14	02/24/14	02/05/14	2	B
	SUB-13-00014-DSR-074-A	Concrete Mix Ready -Muwasi Ready mix plant -Project 02	DSR	M	02/03/14	02/24/14	02/05/14	2	B
	SUB-13-00014-NAB-075-A	Catch basin- PCP- item 4.06.a-Project 01	NAB	M	02/04/14	02/25/14	02/11/14	7	B
	SUB-13-00014-NAB-076-A	Cast Iron Cover & curb for catch basin- item 4.06.a- Project 01	NAB	M	02/04/14	02/25/14	02/13/14	9	C
	SUB-13-00014-MRNII-077-A	Field Offices Furniture and Equipment List Amendment (For Submittal No.: SUB-13-00014-MRNII-007-A)	MRNII	P	02/05/14	02/26/14	02/09/14	4	B
	SUB-13-00014-NAB-078-A	Traffic Control Plan (Area A and B) from Sta.2+020 to Sta.2+540-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	02/05/14	02/26/14	02/06/14	1	B
	SUB-13-00014-NAB-079-A	Base-Course Source -Salous Crusher -B.O.Q item No. 2.02-Project 01	NAB	M	02/06/14	02/27/14	02/11/14	5	C
	SUB-13-00014-NAB-079-B	Base-Course Source -Salous Crusher -B.O.Q item No. 2.02-Project 01	NAB	M	03/31/14	04/21/14	04/01/14	1	A
	SUB-13-00014-NAB-080-A	Topping Material Source -Salous Crusher -B.O.Q item No. 1.02.b-Project 01	NAB	M	02/06/14	02/27/14	02/11/14	5	B
	SUB-13-00014-NAB-081-A	Shop Drawings: Retaining Wall from Sta.2+339 to Sta.2+369 RHS -Segment A-Project 01	NAB	S	02/06/14	02/27/14	02/09/14	3	B
	SUB-13-00014-NAB-082-A	Shop Drawings: Concrete Wall from Sta.2+040 to Sta.2+065 LHS -Segment A-Project 01	NAB	S	02/06/14	02/27/14	02/09/14	3	C
	SUB-13-00014-NAB-082-B	Shop Drawings: Retaining Wall from Sta.2+040 to Sta.2+059 LHS -Segment A-Project 01	NAB	S	03/11/14	04/01/14	03/13/14	2	B
	SUB-13-00014-NAB-083-A	Proposed Welders for welders qualification test - CVs	NAB	P	02/09/14	03/02/14	02/18/14	9	C
	SUB-13-00014-NAB-083-B	Proposed Welders for welders qualification test - CVs	NAB	P	05/12/14	06/02/14	05/13/14	1	A
	SUB-13-00014-NAB-084-A	Proposed Dumping Area -Project 01	NAB	P	02/11/14	03/04/14	02/12/14	1	B
	SUB-13-00014-NAB-085-A	Shop Drawings: Retaining Wall from Sta.A2+475 to Sta.A2+515 RHS -Project 01	NAB	S	02/16/14	03/09/14	02/23/14	7	B
	SUB-13-00014-NAB-086-A	Shop Drawings: Plan, Profile and Cross Sections from Sta. 2+600 to Sta. 3+000- Project 01	NAB	S	02/16/14	03/09/14	02/23/14	7	C
	SUB-13-00014-NAB-086-B	Shop Drawings: Plan, Profile and Cross Sections from Sta. 2+600 to Sta. 3+000- Project 01	NAB	S	02/24/14	03/17/14	02/25/14	1	B
	SUB-13-00014-NAB-087-A	Traffic Control Plan from Sta.A2+540 to Sta.A3+500 -Phase II-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	02/17/14	03/10/14	02/23/14	6	C
	SUB-13-00014-NAB-087-B	Traffic Control Plan from Sta.A2+540 to Sta.A3+500 -Phase II-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	02/26/14	03/19/14	03/02/14	4	A
	SUB-13-00014-NAB-088-A	Galvanized Malleable Iron Fittings up to 2”- Modgal	NAB	M	02/17/14	03/10/14	02/25/14	8	B
	SUB-13-00014-NAB-089-A	Branding Plan -Approved Flyers (Arabic & English) & Radio Advertisement	NAB	P	02/19/14	03/12/14	02/24/14	5	E

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-090-A	Shop Drawings: Lighting Details from Sta.2+033.73 to Sta.2+983.73-Project 01	NAB	S	02/19/14	03/12/14	03/02/14	11	C
	SUB-13-00014-NAB-090-B	Shop Drawings: Lighting Details from Sta.2+033.73 to Sta.2+983.73-Project 01	NAB	S	04/21/14	05/12/14	04/30/14	9	C
	SUB-13-00014-NAB-090-C	Shop Drawings: Lighting Details from Sta.2+000 to Sta.3+000-Project 01	NAB	S	05/08/14	05/29/14	05/25/14	17	B
	SUB-13-00014-NAB-091-A	Cast insitu concrete manhole for storm water -Project 01	NAB	M	02/19/14	03/12/14	03/02/14	11	C
	SUB-13-00014-NAB-091-B	Manholes for Storm System detail	NAB	M	03/20/14	04/10/14	03/23/14	3	B
	SUB-13-00014-MRNII-092-A	Reinforcement Steel (Israel+Turkey) -BOQ Item No.4.07-C	MRNII	M	02/19/14	03/12/14	02/23/14	4	B
	SUB-13-00014-MRNII-093-A	Concrete Water Proofer for Manholes outside painting -Nitroproof 30 ,Nitroproof 230	MRNII	M	02/19/14	03/12/14	02/23/14	4	B
	SUB-13-00014-NAB-094-A	3 inch Procedure Qualification Record (PQR)	NAB	P	02/19/14	03/12/14	02/26/14	7	B
	SUB-13-00014-DSR-095-A	JMF for Bituminous Wearing 3/4" -Developed Co-item No. 3.03 -Project 02	DSR	M	02/19/14	03/12/14	02/23/14	4	B
	SUB-13-00014-DSR-096-A	JMF for Bituminous Binder 1inch_Developed Co-item 3.05- Project 2	DSR	M	02/19/14	03/12/14	02/23/14	4	B
	SUB-13-00014-NAB-097-A	Street Lighting -BOQ No. 5.08 -Project 01	NAB	M	02/23/14	03/16/14	03/02/14	7	B
	SUB-13-00014-NAB-098-A	Safety Guardrail-Lime Berlin -Project 01	NAB	P	02/24/14	03/17/14	02/25/14	1	E
	SUB-13-00014-NAB-099-A	Risk Management Program-Phase II from Sta.0+000 to Sta.2+000 and from Sta.3+000 to the end of the Project -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	02/27/14	03/20/14	03/03/14	4	B
	SUB-13-00014-NAB-100-A	Dilapidation Survey and Risk Management Program -Segment B-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	02/27/14	03/20/14	03/05/14	6	B
	SUB-13-00014-NAB-101-A	Epoxy Paint for Concrete protection-Nitocote ET550	NAB	M	03/02/14	03/23/14	03/05/14	3	B
	SUB-13-00014-DSR-102-A	Shop Drawing: Plan ,Profile and Cross Section from Sta.0+700 to Sta.1+200 -Project 02	DSR	S	03/02/14	03/23/14	03/05/14	3	B
	SUB-13-00014-DSR-102-B	Shop Drawing: Plan ,Profile and Cross Section from Sta.0+700 to Sta.1+200 -Project 02-As per Site Memo # 13-Project 02	DSR	S	03/25/14	04/15/14	03/27/14	2	B
	SUB-13-00014-DSR-102-C	Shop Drawing: Plan ,Profile and Cross Section from Sta.0+700 to Sta.1+200 -Project 02-**For engineering Record**	DSR	S	04/21/14	05/12/14	04/24/14	3	B
	SUB-13-00014-NAB-103-A	Shop Drawings: Retaining Wall from Sta.2+740 to Sta.2+850 RHS -Project 01	NAB	S	03/02/14	03/23/14	03/05/14	3	B
	SUB-13-00014-NAB-104-A	Shop Drawing: Storm Water : Plan and Profile from Sta.2+900 to Sta.2+980 -Project 01	NAB	S	03/02/14	03/23/14	03/05/14	3	E
	SUB-13-00014-NAB-105-A	Shop Drawings: Plan ,Profile and Cross Section from Sta.3+000 to Sta.3+600 -Project 01	NAB	S	03/02/14	03/23/14	03/09/14	7	C
	SUB-13-00014-NAB-105-B	Shop Drawings: Plan ,Profile and Cross Section from Sta.3+000 to Sta.3+600 -Project 01	NAB	S	03/18/14	04/08/14	03/26/14	8	B
	SUB-13-00014-NAB-106-A	Shop Drawing: Retaining Wall from Sta.2+880 to Sta.2+916 RHS and from Sta.2+937 to Sta.2+980 RHS-Project 01	NAB	S	03/05/14	03/26/14	03/10/14	5	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-106-B	Shop Drawing: Retaining Wall from Sta.2+880 to Sta.2+916 RHS , from Sta.2+937 to Sta.2+954 RHS and from Sta.2+965 to Sta.2+980 RHS-Project 01	NAB	S	03/18/14	04/08/14	03/23/14	5	B
	SUB-13-00014-NAB-107-A	12" inch Procedure Qualification Record (PQR) -Project 01	NAB	P	03/05/14	03/26/14	03/13/14	8	C
	SUB-13-00014-NAB-107-B	12" inch Procedure Qualification Record (PQR) -Project 01	NAB	P	03/16/14	04/06/14	03/20/14	4	B
	SUB-13-00014-NAB-108-A	Shop Drawing: Plan ,Profile and Cross Section from Sta.3+500 to Sta.4+100 -Project 01	NAB	S	03/06/14	03/27/14	03/17/14	11	B
	SUB-13-00014-NAB-109-A	Supply of water pipes and fittings -FIP Co.- Project 01	NAB	M	03/06/14	03/27/14	03/13/14	7	C
	SUB-13-00014-NAB-109-B	Supply of water pipes and fittings -FIP Co.- Project 01	NAB	M	03/16/14	04/06/14	03/30/14	14	B
	SUB-13-00014-NAB-110-A	Shop Drawing: Storm Water : Plan , Profile and Cross Section from Sta.2+580 to Sta.2+740 and from Sta.2+870 to Sta.2+980-Project 01	NAB	S	03/06/14	03/27/14	03/10/14	4	B
	SUB-13-00014-MRNII-111-A	Updated Construction Schedule -February 2014	MRNII	SCH	03/09/14	03/30/14	03/16/14	7	B
	SUB-13-00014-NAB-112-A	Shop Drawings: Retaining Wall from Sta.A2+980 to Sta.A3+010 LHS -Project 01	NAB	S	03/10/14	03/31/14	03/17/14	7	C
	SUB-13-00014-NAB-112-B	Shop Drawings: Retaining Wall from Sta.A2+980 to Sta.A3+010 LHS -Project 01	NAB	S	03/25/14	04/15/14	03/31/14	6	B
	SUB-13-00014-NAB-113-A	Shop Drawings: Edge Wall from Sta.A2+718 to Sta.A2+730 LHS -Project 01	NAB	S	03/10/14	03/31/14	03/13/14	3	C
	SUB-13-00014-NAB-113-B	Shop Drawings: Retaining Wall from Sta.A2+719 to Sta.A2+730 LHS -Project 01	NAB	S	04/24/14	05/15/14	05/05/14	11	E
	SUB-13-00014-NAB-114-A	Shop Drawings: Plan , Profile and Cross Section from Sta.1+500 to Sta.2+000-Project 01	NAB	S	04/10/14	05/01/14	04/21/14	11	C
	SUB-13-00014-NAB-114-B	Shop Drawings: Plan , Profile and Cross Section from Sta.1+500 to Sta.2+000-Project 01	NAB	S	04/30/14	05/21/14	05/05/14	5	B
	SUB-13-00014-NAB-114-C	Shop Drawings: Plan , Profile and Cross Section from Sta.1+500 to Sta.2+000-Project 01-**For Engineering Record**	NAB	S	05/12/14	06/02/14	05/15/14	3	B
	SUB-13-00014-NAB-115-A	Shop Drawings: Retaining Wall from Sta.3+230 to Sta.3+300 RHS -Project 01	NAB	S	03/16/14	04/06/14	03/19/14	3	C
	SUB-13-00014-NAB-115-B	Shop Drawings: Retaining Wall from Sta.3+240 to Sta.3+300 RHS -Project 01	NAB	S	04/03/14	04/24/14	04/06/14	3	B
	SUB-13-00014-NAB-116-A	Shop Drawings: Retaining Wall from Sta.3+160 to Sta.3+190 LHS and from Sta.3+180 to Sta.3+220 RHS -Project 01	NAB	S	03/19/14	04/09/14	03/31/14	12	B
	SUB-13-00014-NAB-117-A	Shop Drawing: Water Pipeline 12": Plan ,Profile and Typical section from Sta.2+000 to Sta.3+000-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	03/17/14	04/07/14	03/23/14	6	B
	SUB-13-00014-NAB-118-A	Shop Drawings: Retaining Wall from Sta.A3+560 to Sta.A3+590 RHS -Project 01	NAB	S	03/19/14	04/09/14	03/24/14	5	B
	SUB-13-00014-NAB-119-A	Shop Drawings: Retaining Wall from Sta.A3+010 to Sta.A3+020 RHS -Project 01	NAB	S	03/24/14	04/14/14	03/27/14	3	B
	SUB-13-00014-NAB-120-A	Welding Procedure 3-12 inch pipes	NAB	P	03/24/14	04/14/14	03/31/14	7	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-121-A	Shop Drawings: Retaining Wall from Sta.A3+340 to Sta.A3+370 RHS -Project 01	NAB	S	03/25/14	04/15/14	04/01/14	7	C
	SUB-13-00014-NAB-121-B	Shop Drawings: Retaining Wall from Sta.A3+341 to Sta.A3+370 RHS -Project 01	NAB	S	04/06/14	04/27/14	04/22/14	16	B
	SUB-13-00014-NAB-122-A	Specific Method Statement for Sewer lines Leakage Testing-Project 01	NAB	P	03/25/14	04/15/14	03/30/14	5	B
	SUB-13-00014-NAB-123-A	Shop Drawing: Retaining Wall from Sta.3+655 to Sta.3+695 RHS-Project 01	NAB	S	03/27/14	04/17/14	04/06/14	10	B
	SUB-13-00014-NAB-124-A	Shop Drawing: Plan , Profile and Cross Section from Sta.4+100 to Sta.4+850 - Project 01	NAB	S	03/27/14	04/17/14	04/08/14	12	C
	SUB-13-00014-NAB-124-B	Shop Drawing: Plan , Profile and Cross Section from Sta.4+100 to Sta.4+850 - Project 01	NAB	S	05/04/14	05/25/14	05/07/14	3	B
	SUB-13-00014-NAB-125-A	Shop Drawing: Retaining Wall from Sta.3+373 to Sta.3+402 LHS-Project 01	NAB	S	03/31/14	04/21/14	04/06/14	6	B
	SUB-13-00014-NAB-126-A	Shop Drawing: Retaining Wall from Sta.3+828.5 to Sta.3+855.5 RHS-Project 01	NAB	S	04/03/14	04/24/14	04/06/14	3	C
	SUB-13-00014-NAB-126-B	Shop Drawings: Boundary wall from Sta.3+828 to Sta.3+854.5 RHS-Project 01	NAB	S	04/30/14	05/21/14	05/05/14	5	B
	SUB-13-00014-DSR-127-A	Shop Drawing: Pipe Culvert at Sta.0+946 -Project 01	DSR	S	04/03/14	04/24/14	04/14/14	11	E
	SUB-13-00014-NAB-128-A	Shop Drawings: Boundary wall from Sta.3+950 to Sta.3+985 LHS-Project 01	NAB	S	04/03/14	04/24/14	04/06/14	3	C
	SUB-13-00014-NAB-128-B	Shop Drawings: Boundary wall from Sta.3+950 to Sta.3+985 LHS-Project 01	NAB	S	04/24/14	05/15/14	04/30/14	6	B
	SUB-13-00014-NAB-129-A	Shop Drawings: Water 12" : Plan ,Profile and Typical Section from Sta.3+000 to Sta.4+100 -Project 01	NAB	S	04/03/14	04/24/14	04/08/14	5	B
	SUB-13-00014-MRNII-130-A	Updated Construction Schedule and S-curve -March 2014	MRNII	SCH	04/06/14	04/27/14	04/22/14	16	C
	SUB-13-00014-MRNII-130-B	Updated Construction Schedule and S-curve -March 2014	MRNII	SCH	04/30/14	05/21/14	05/13/14	13	B
	SUB-13-00014-DSR-131-A	Shop Drawings: Plan , Profile and Cross Section from Sta.1+200 to Sta.1+800- Project 02	DSR	S	04/08/14	04/29/14	04/09/14	1	B
	SUB-13-00014-NAB-132-A	Traffic Control Plan from Sta.3+520 to Sta.4+620 -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	04/08/14	04/29/14	04/14/14	6	C
	SUB-13-00014-NAB-132-B	Traffic Control Plan from Sta.3+520 to Sta.4+620 -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	04/28/14	05/19/14	04/28/14	0	B
	SUB-13-00014-NAB-133-A	Shop Drawings: Water 3" -Plan , Profile and Typical Section from Sta.2+900 to Sta.4+400 -Project 01	NAB	S	04/10/14	05/01/14	04/16/14	6	B
	SUB-13-00014-NAB-134-A	Shop Drawing: Storm Water : Plan and Profile from Sta.3+600 to Sta.3+840 - Project 01	NAB	S	04/14/14	05/05/14	04/23/14	9	C
	SUB-13-00014-NAB-134-B	Shop Drawing: Storm Water : Plan and Profile from Sta.3+600 to Sta.3+840 - Project 01	NAB	S	05/05/14	05/26/14	05/06/14	1	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-134-C	Shop Drawing: Storm Water : Plan and Profile from Sta.3+600 to Sta.3+840 - Project 01-For Engineering Record	NAB	S	05/08/14	05/29/14	05/13/14	5	B
	SUB-13-00014-NAB-135-A	Shop Drawings: Stone Wall from Sta.A2+980 to Sta.A3+010 LHS-Project 01	NAB	S	04/16/14	05/07/14	04/21/14	5	E
	SUB-13-00014-NAB-136-A	Shop Drawings: Stone Wall from Sta.A3+162 to Sta.A3+189 LHS-Project 01	NAB	S	04/16/14	05/07/14	04/21/14	5	E
	SUB-13-00014-NAB-137-A	Cover for catch basin_ related item 4.06.a-Project 01	NAB	M	04/17/14	05/08/14	04/22/14	5	C
	SUB-13-00014-NAB-138-A	Shop Drawing: Storm Water : Plan and Profile from Sta.3+000 to Sta.3+120 - Project 01	NAB	S	04/17/14	05/08/14	04/21/14	4	B
	SUB-13-00014-NAB-139-A	Special Method Statements for Hydrostatic Test for concrete pipes - project 01	NAB	P	04/22/14	05/13/14	04/24/14	2	B
	SUB-13-00014-NAB-140-A	Shop Drawing: Retaining Wall from Sta.4+090 to Sta.4+100 -Project 01	NAB	S	04/24/14	05/15/14	05/05/14	11	C
	SUB-13-00014-NAB-141-A	Shop Drawings: Plan , Profile and Cross Section for Junction at Sta.3+420 - Project 01	NAB	S	04/24/14	05/15/14	05/05/14	11	C
	SUB-13-00014-NAB-141-B	Shop Drawings: Plan , Profile and Cross Section for Junction at Sta.3+420 - Project 01	NAB	S	05/12/14	06/02/14	05/13/14	1	B
	SUB-13-00014-NAB-142-A	Shop Drawing: Stone Wall from Sta.3+376 to Sta.3+402 LHS-Project 01	NAB	S	04/24/14	05/15/14	04/28/14	4	B
	SUB-13-00014-DSR-143-A	Shop Drawings: Plan, Profile and Cross Section from Sta.1+800 to Sta.2+100 - Project 02	DSR	S	04/27/14	05/18/14	04/29/14	2	B
	SUB-13-00014-NAB-144-A	Traffic Control Plan Phase II from Sta.0+000 to Sta.2+000 -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	04/28/14	05/19/14	04/29/14	1	C
	SUB-13-00014-NAB-144-B	Traffic Control Plan Phase II from Sta.0+000 to Sta.2+000 -DCL Final Written Approval -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	05/07/14	05/28/14	05/13/14	6	B
	SUB-13-00014-NAB-145-A	Shop Drawings: Water 12" : Plan ,Profile and Typical Section from Sta.1+050 to Sta.2+000 -Project 01	NAB	S	04/28/14	05/19/14	05/08/14	10	C
	SUB-13-00014-NAB-145-B	Shop Drawings: Water 12" : Plan ,Profile and Typical Section from Sta.1+050 to Sta.2+000 -Project 01	NAB	S	05/22/14	06/12/14	06/01/14	10	B
	SUB-13-00014-NAB-146-A	Traffic Control Plan Phase II from Sta.1+381 to Sta.2+000 (Area B) -Nablus Beit Iba Der Sharaf Road -Project 01	NAB	P	04/29/14	05/20/14	05/04/14	5	B
	SUB-13-00014-DSR-147-A	Shop Drawings: Pipe Culvert at Sta.0+860-Project 02	DSR	S	04/30/14	05/21/14	05/07/14	7	B
	SUB-13-00014-NAB-148-A	Shop Drawings: Junction at Sta.2+600 LHS and at Sta.2+640 RHS -Project 01	NAB	S	05/04/14	05/25/14	05/06/14	2	B
	SUB-13-00014-NAB-148-B	Shop Drawings: Junction at Sta.2+600 LHS and at Sta.2+640 RHS -Project 01-For Engineering Record	NAB	S	05/13/14	06/03/14	05/15/14	2	B
	SUB-13-00014-NAB-149-A	Shop Drawings: Retaining Wall from Sta.1+720 to Sta.1+750 RHS-Project 01	NAB	S	05/04/14	05/25/14	05/07/14	3	B
	SUB-13-00014-NAB-150-A	Shop Drawings: Water 12" : Plan ,Profile and Typical Section from Sta.4+100 to Sta.4+850 -Project 01	NAB	S	05/05/14	05/26/14	05/07/14	2	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-151-A	Shop Drawings: Retaining Wall from Sta.1+865 to Sta.1+930 RHS-Project 01	NAB	S	05/05/14	05/26/14	05/07/14	2	B
	SUB-13-00014-NAB-152-A	Shop Drawings: Retaining Wall from Sta.3+217 to Sta.3+226 LHS and Concrete Stair from Sta. 3+226 to Sta.3+229 LHS -Project 01	NAB	S	05/07/14	05/28/14	05/19/14	12	B
	SUB-13-00014-MRNII-153-A	Updated Construction Schedule and S-curve -April 2014	MRNII	SCH	05/07/14	05/28/14	05/21/14	14	C
	SUB-13-00014-MRNII-153-B	Updated Construction Schedule and S-curve -April 2014	MRNII	SCH	05/26/14	06/16/14	05/29/14	3	B
	SUB-13-00014-NAB-154-A	Confined space safety plan -Project 01	NAB	P	05/06/14	05/27/14	05/08/14	2	B
	SUB-13-00014-NAB-155-A	Updated Risk Management Program from Sta.3+250 to Sta.3+350 -Project 01	NAB	P	05/12/14	06/02/14	05/14/14	2	C
	SUB-13-00014-DSR-156-A	Shop Drawings: Plan, Profile and Cross Sections from Sta. 2+100 to Sta. 2+540- Project 02	DSR	S	05/08/14	05/29/14	05/15/14	7	B
	SUB-13-00014-NAB-157-A	Shop Drawing: Stone Wall from Sta.4+710 to Sta.4+776 LHS-Project 01	NAB	S	05/12/14	06/02/14	05/13/14	1	E
	SUB-13-00014-NAB-158-A	Shop Drawings: Retaining Wall from Sta.3+715 to Sta.3+740 LHS-Project 01	NAB	S	05/12/14	06/02/14	05/28/14	16	B
	SUB-13-00014-NAB-158-B	Shop Drawings: Retaining Wall with stair from Sta.3+715 to Sta.3+740 LHS-Project 01-For Engineering Record	NAB	S	06/19/14	07/10/14	06/22/14	3	B
	SUB-13-00014-NAB-159-A	Shop Drawings: Sewer System: Plan, Profile and Cross Section from Sta.3+407 to Sta.3+560-Nablus Beit Iba Der Sharaf Road -Project 01	NAB	S	05/13/14	06/03/14	05/15/14	2	B
	SUB-13-00014-NAB-160-A	Shop Drawings: Retaining Wall from Sta.A4+545 to Sta.A4+617 RHS -Project 01	NAB	S	05/13/14	06/03/14	05/21/14	8	B
	SUB-13-00014-NAB-161-A	Shop Drawings: Retaining Wall from Sta.A4+826 to Sta.A4+865 RHS -Project 01	NAB	S	05/14/14	06/04/14	05/21/14	7	C
	SUB-13-00014-NAB-162-A	Shop Drawings: Box Culvert at Sta.3+610 -Project 01	NAB	S	05/15/14	06/05/14	05/21/14	6	B
	SUB-13-00014-NAB-162-B	Shop Drawings: Box Culvert at Sta.3+610 -Project 01-**For Engineering Record**	NAB	S	05/28/14	06/18/14	06/04/14	7	B
	SUB-13-00014-NAB-163-A	Shop Drawings: Plan , Profile and Cross Section from Sta.1+050 to Sta.1+500 -Project 01	NAB	S	05/15/14	06/05/14	05/27/14	12	C
	SUB-13-00014-NAB-163-B	Shop Drawings: Plan , Profile and Cross Section from Sta.1+050 to Sta.1+500 -Project 01	NAB	S	06/19/14	07/10/14	06/22/14	3	B
	SUB-13-00014-NAB-164-A	Shop Drawing: Storm Water : Plan and Profile from Sta.1+690 to Sta.2+020 -Project 01	NAB	S	05/19/14	06/09/14	05/27/14	8	B
	SUB-13-00014-DSR-165-A	Shop Drawings: Pipe Culvert at Sta.1+480-Project 02	DSR	S	05/19/14	06/09/14	05/21/14	2	B
	SUB-13-00014-NAB-166-A	Precast Concrete Curbstone & Edge beam -2000 Block and Investment Co.-item 4.12 -Project 01	NAB	M	05/21/14	06/11/14	05/26/14	5	B
	SUB-13-00014-MRNII-167-A	Testing Labs-Renewed Accreditation Certificate and Schedule (For Hijjawi Construction Labs)- Amendment to Submittal No. : SUB-13-00014-MRNII-005-A	MRNII	P	05/21/14	06/11/14	05/27/14	6	A
	SUB-13-00014-DSR-168-A	Shop Drawings: Pipe Culvert at Sta.1+995 -Project 02	DSR	S	05/22/14	06/12/14	05/28/14	6	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-DSR-168-B	Shop Drawings: Double Pipe Culvert at Sta.1+995 -Project 02-For Engineering Record	DSR	S	06/05/14	06/26/14	06/08/14	3	B
	SUB-13-00014-NAB-169-A	Shop Drawings: Plan , Profile and Cross Section for Junction from Sta.1+910 to Sta.2+040 -Project 01	NAB	S	05/25/14	06/15/14	06/05/14	11	B
	SUB-13-00014-NAB-169-B	Shop Drawings: Plan , Profile and Cross Section for Junction from Sta.1+910 to Sta.2+040 -Project 01-**For Engineering Record**	NAB	S	06/18/14	07/09/14	06/26/14	8	B
	SUB-13-00014-DSR-170-A	Shop Drawings: Retaining Wall from Sta.1+300 to Sta.1+310 LHS and from Sta.1+700 to Sta.1+760 LHS -Project 02	DSR	S	05/26/14	06/16/14	05/28/14	2	B
	SUB-13-00014-DSR-171-A	Shop Drawings: Retaining Wall from Sta.1+475 to Sta.1+500 LHS -Project 02	DSR	S	05/27/14	06/17/14	05/29/14	2	B
	SUB-13-00014-NAB-172-A	Portland Cement Sulfate Resisting – CEM III 42.5 N/B) for concrete benching for manholes-PCP Co. -Project 01	NAB	M	05/28/14	06/18/14	06/04/14	7	B
	SUB-13-00014-NAB-173-A	Lamp, Cable and Cobra Pipe for street lighting -Project 01	NAB	M	05/28/14	06/18/14	06/05/14	8	B
	SUB-13-00014-MRNII-174-A	Updated Construction Schedule and S-curve -May 2014	MRNII	SCH	06/05/14	06/26/14	06/22/14	17	B
	SUB-13-00014-NAB-175-A	Shop Drawings: Revised Plan , Profile and Cross Section for Intersection at Sta.0+000 , from Sta.0+000 to Sta.0+240 as per SM No. SM -13-00014-NAB-036	NAB	S	06/11/14	07/02/14	06/23/14	12	B
	SUB-13-00014-DSR-176-A	Shop Drawings: Plan for Ditch and Concrete Step Barrier from Sta.0+000 to Sta.2+180 -Project 02	DSR	S	06/12/14	07/03/14	06/17/14	5	B
	SUB-13-00014-DSR-177-A	Shop Drawings: Water 3" -Plan , Profile and Typical Section from Sta.0+410 to Sta.1+100 -Project 01	DSR	S	06/12/14	07/03/14	06/22/14	10	B
	SUB-13-00014-NAB-178-A	Shop Drawing: Storm Water : Plan and Profile from Sta.0+030 to Sta.0+180 -Project 01	NAB	S	06/15/14	07/06/14	06/26/14	11	C
	SUB-13-00014-DSR-179-A	Shop Drawing: Storm Water : Plan and Profile from Sta.0+100 to Sta.0+180 -Project 02	DSR	S	06/16/14	07/07/14	06/26/14	10	E
	SUB-13-00014-NAB-180-A	Shop Drawings: Plan , Profile and Cross Section from Sta.0+000 to Sta. 0+399-Segment B	NAB	S	06/18/14	07/09/14	06/26/14	8	C
	SUB-13-00014-NAB-181-A	Shop Drawings: Street Lighting Poles from Sta.1+500 to Sta.2+000 &from sta.3+000 to Sta.4+850 -Project 01	NAB	S	06/18/14	07/09/14	06/22/14	4	B
	SUB-13-00014-NAB-182-A	Shop Drawings: Side Walk from sta.2+000 to sta.2+600 -Project 01	NAB	S	06/18/14	07/09/14	06/23/14	5	B
	SUB-13-00014-DSR-183-A	Shop Drawings: Crossing Pipe Culvert from Sta.1+938 to Sta.1+962 RHS -Project 02	DSR	S	06/22/14	07/13/14	06/25/14	3	E
	SUB-13-00014-DSR-184-A	Shop Drawings: Plan , Details for Road Marking , Guardrail and Traffic Sign from Sta.0+000 to Sta.2+180 -Project 02	DSR	S	06/25/14	07/16/14		PE	
	SUB-13-00014-NAB-185-A	Shop Drawings: Storm Water : Plan and Profile from Sta.1+300 to Sta.1+620 -Project 01	NAB	S	06/26/14	07/17/14		PE	
	SUB-13-00014-NAB-186-A	Shop Drawings: Sewer System : Plan and Profile from Sta.4+100 to Sta.4+560 -Project 01	NAB	S	06/26/14	07/17/14		PE	

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00014-NAB-187-A	Shop Drawings: Storm System : Plan and Profile from Sta.4+100 to Sta.4+560 - Project 01	NAB	S	06/26/14	07/17/14		PE	
	SUB-13-00014-NAB-188-A	Shop Drawings: Storm System : Plan and Profile from Sta.1+100 to Sta.1+260 - Project 01	NAB	S	06/28/14	07/19/14		PE	
	SUB-13-00014-DSR-189-A	Shop Drawings: Simple Access Road at Sta.0+170 LHS ,0+360 RHS , 0+430 RHS ,0+930 RHS , 0+990 RHS ,1+100 LHS , 1+439 ,1+460 LHS ,1+950 RHS and 1+940 LHS -Project 02	DSR	S	06/28/14	07/19/14		PE	

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

P= Preconstruction - S= Shop drawings - M= Materials - O= Others

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT IN THE NORTH (MRNII)

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-001-A	Bedding Materials (Somsom) -M/1402/89	NAB	02/13/14	03/06/14	02/18/14	5	B
	Test -13-00014-NAB-002-A	Single size- M/1402/111	NAB	02/13/14	03/06/14	02/18/14	5	B
	Test -13-00014-NAB-003-A	Slope excavation -M/1401/299b	NAB	02/13/14	03/06/14	02/18/14	5	E
	Test -13-00014-NAB-004-A	Reinforcing Steel Bars- M/1402/239	NAB	03/02/14	03/23/14	03/03/14	1	B
	Test -13-00014-NAB-005-A	Reiforced Concrete Cylindrical Pipes for Storm Warer Φ 80 cm / M/1402/249	NAB	03/02/14	03/23/14	03/03/14	1	B
	Test -13-00014-NAB-006-A	Test for Subgarde of Retaining Wall, from St. (2+339- 2+369) P01-M/1402/289	NAB	03/03/14	03/24/14	03/04/14	1	C
	Test -13-00014-NAB-006-B	Test for Subgarde of Retaining Wall, from St. (2+339- 2+369) P01-M/1402/289	NAB	03/05/14	03/26/14	03/05/14	0	A
	Test -13-00014-NAB-007-A	Test for Subgarde of Retaining Wall, from St. (2+475- 2+515) P01-M/1402/269	NAB	03/03/14	03/24/14	03/04/14	1	B
	Test -13-00014-NAB-008-A	Field density test , from sta. (2+730- 2+800) P 01-(014-0297)	NAB	03/06/14	03/27/14	03/06/14	0	A
	Test -13-00014-NAB-009-A	Test Report on concrete compressive strength- Strom water manhole Walls , M# 40-M#41 (M/1403/22)	NAB	03/09/14	03/30/14	03/10/14	1	B
	Test -13-00014-NAB-010-A	Topping Material Tes t(014-0311)	NAB	03/09/14	03/30/14	03/10/14	1	C
	Test -13-00014-NAB-010-B	Topping Material Test (014-0311)	NAB	03/12/14	04/02/14	03/13/14	1	B
	Test -13-00014-NAB-011-A	Test Report on concrete Compressive Strength, for manhole Base (M # 40-41-42-43)- Project 01 (M/1402/282)	NAB	03/09/14	03/30/14	03/10/14	1	A
	Test -13-00014-DSR-012-A	Test on Granular Pulverized Materials -P 02(M/1403/81)	DSR	03/10/14	03/31/14	03/10/14	0	B
	Test -13-00014-NAB-013-A	Reinforcing Steel Bars- M/1403/79	NAB	03/11/14	04/01/14	03/12/14	1	B
	Test -13-00014-NAB-014-A	Compacted subgrade layer - Field density - Project 01	NAB	03/13/14	04/03/14	03/16/14	3	B
	Test -13-00014-NAB-015-A	Topping Material Test (014-0338)	NAB	03/16/14	04/06/14	03/16/14	0	B
	Test -13-00014-NAB-016-A	Concrete Cube for Manhole Wall (M# 48-M# 49) (014-0307)	NAB	03/16/14	04/06/14	03/17/14	1	B
	Test -13-00014-NAB-017-A	Report of compacted Subgrade layer (Field Deisity) , from Sta. 0+400-0+600 - Project 02	NAB	03/19/14	04/09/14	03/20/14	1	B
	Test -13-00014-NAB-018-A	Report of compacted Base Course under Retaining Wall (Field Deisity , from Sta. 0+475-0+515 - RHS -Project 01	NAB	03/20/14	04/10/14	03/24/14	4	C
	Test -13-00014-NAB-018-B	Report of Field Density Test (Under Retaining Wall)from St. 2+475-2+515 at RHS (MTC:014-0367)	NAB	03/30/14	04/20/14	03/31/14	1	A
	Test -13-00014-NAB-019-A	Report of compacted Subgrade layer (Field Deisity) , from Sta. 2+800-2+880 - Project 01	NAB	03/20/14	04/10/14	03/24/14	4	C
	Test -13-00014-NAB-019-B	Report of Field Density Test ,from St. 2+800-2+880 (MTC:014-0366)	NAB	03/30/14	04/20/14	03/31/14	1	B
	Test -13-00014-NAB-020-A	Report on concrete Compressive Strength – Base for Storm water Manhole # 48-49, Blinding for Storm Water Manhole # 50-51-38-39- Project 01	NAB	03/23/14	04/13/14	03/24/14	1	B
	Test -13-00014-NAB-021-A	Report on concrete Compressive Strength – Wall for Storm water Manhole # 42-43	NAB	03/23/14	04/13/14	03/24/14	1	B
	Test -13-00014-NAB-022-A	Concrete Cube for Manhole Wall (M# 46-M# 47) (014-0354)	NAB	03/25/14	04/15/14	03/26/14	1	B
	Test -13-00014-NAB-023-A	Test on Granular Topping Material-Comprehensive (Mobile Crusher) NAB- Project 01 (M-1403-225)	NAB	03/30/14	04/20/14	03/31/14	1	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT IN THE NORTH (MRNII)

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-024-A	Test on Concrete Compressive Strength (Base for Storm water Manhole # 40-41-42-43)-Project 01 (M-1402-282-a)	NAB	03/30/14	04/20/14	03/31/14	1	A
	Test -13-00014-NAB-025-A	Test on Concrete Compressive Strength (Retaining Wall from St. 2+339-2+369 at RHS)-Project 01(M-1403-190)	NAB	03/30/14	04/20/14	03/31/14	1	B
	Test -13-00014-NAB-026-A	Test on Granular Subgrade Material under Retaining Wall -Project 01 (M-1403-254)	NAB	03/30/14	04/20/14	03/31/14	1	B
	Test -13-00014-NAB-027-A	Concrete Cube for storm water manhole M#45(MTC: 014-0385)	NAB	03/30/14	04/20/14	04/01/14	2	E
	Test -13-00014-NAB-028-A	Concrete Cube for storm water manhole M#48-M# 49(MTC:014-0307)	NAB	03/30/14	04/20/14	04/01/14	2	B
	Test -13-00014-NAB-029-A	Field density test , from sta. (2+280- 2+350) -(0+350-0+420) P 01 (MTC:014-0443)	NAB	03/30/14	04/20/14	04/01/14	2	A
	Test -13-00014-NAB-030-A	Concrete Cube (storm water manhole)M# 46-47-(MTC:014-0354)	NAB	03/31/14	04/21/14	04/01/14	1	B
	Test -13-00014-NAB-031-A	Field Density (Compaction Test) - (MTC:014-0427)	NAB	03/31/14	04/21/14	04/01/14	1	C
	Test -13-00014-NAB-031-B	Field Density (Compaction Test) - (MTC:014-0427)	NAB	04/02/14	04/23/14	04/03/14	1	A
	Test -13-00014-NAB-032-A	Field Density (Compaction Test) - subgrade layer (MTC:014-0405)	NAB	03/31/14	04/21/14	04/01/14	1	C
	Test -13-00014-NAB-032-B	Field Density (Compaction Test) - subgrade layer (MTC:014-0405)	NAB	04/02/14	04/23/14	04/03/14	1	A
	Test -13-00014-NAB-033-A	Field Density (Compaction Test) for Subgrade layer from St. 2+320-2+480- at LHS , from St. 2+880-2+980 at LHS (M-0469-R)	NAB	04/02/14	04/23/14	04/03/14	1	A
	Test -13-00014-NAB-034-A	Compressive Strength for Storm water manhole Base (M# 51& M#55), and for Storm Water wall for (M# 50) (MTC:014-0421)	NAB	04/02/14	04/23/14	04/03/14	1	B
	Test -13-00014-NAB-035-A	Field Density of Base Course under Retaining Wall from (2+740-2+850) at RHS (MTC: 014-0466)	NAB	04/02/14	04/23/14	04/03/14	1	A
	Test -13-00014-NAB-036-A	Concrete Compressive Strength for Storm water manhole Wall – M#44, at 7 Days (M-1403-235)	NAB	04/02/14	04/23/14	04/03/14	1	B
	Test -13-00014-DSR-037-A	Field Density of Subgrade layer , from St. 0+260-0+660(M-1403-253)	DSR	04/02/14	04/23/14	04/03/14	1	A
	Test -13-00014-NAB-038-A	Concrete Compressive Strength for Base of Retaining wall from St. 2+339-2+369 RHS , at 7 days (M-1403-134)	NAB	04/03/14	04/24/14	04/03/14	0	B
	Test -13-00014-DSR-039-A	Field Density – subgrade layer from St. 0+150-0+260 (M-1403-313)	DSR	04/03/14	04/24/14	04/03/14	0	A
	Test -13-00014-NAB-040-A	Concrete Compressive Strength for Storm water manhole (M# 41-40) at 28 days (M-1403-22a)	NAB	04/03/14	04/24/14	04/03/14	0	A
	Test -13-00014-NAB-041-A	Concrete Compressive Strength for Bas of Retaining Wall from St. 2+475-2+515-RHS at 7 days (M-1403-247)	NAB	04/03/14	04/24/14	04/03/14	0	B
	Test -13-00014-NAB-042-A	Field Density of subgrade from St. 2+420-2+580- at RHS (M-0467)	NAB	04/03/14	04/24/14	04/03/14	0	A
	Test -13-00014-NAB-043-A	Concrete Compressive strength for storm water manhole Wall # 51-AT 7 Days - Project 01 (MTC:0429)	NAB	04/06/14	04/27/14	04/08/14	2	B
	Test -13-00014-NAB-044-A	Concrete Compressive strength for storm water manhole base M# 52, 53,54,60), and for manhole Wall (M# 39), blinding for Manhole M# 45 at 7 days - Project 01(MTC:014-0426)	NAB	04/06/14	04/27/14	04/08/14	2	B
	Test -13-00014-NAB-045-A	Compressive for Topping Materials from St .2+100-2+580 RHS- Project 01 (M-1403-330-a)	NAB	04/06/14	04/27/14	04/08/14	2	A

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-046-A	Compressive strength for base of storm water manhole # 48-49 at 28 Days - Project 01 (M-1403-58a)	NAB	04/07/14	04/28/14	04/08/14	1	A
	Test -13-00014-NAB-047-A	Soil Classification for subgrade under Retaining wall St.(2+880-2+916)-St.(2+937-2+954)-St. (2+965-2+980)- RHS Project 01 (M-1404-3)	NAB	04/07/14	04/28/14	04/08/14	1	B
	Test -13-00014-NAB-048-A	Concrete Compressive Strength of storm water manhole Wall M# 42-M#43 at 28 Days –Project 01 (M-1403-57a)	NAB	04/07/14	04/28/14	04/08/14	1	A
	Test -13-00014-NAB-049-A	Compressive for Topping Materials from St .2+100-2+580 LHS- Project 01 (MTC:014-0383)	NAB	04/07/14	04/28/14	04/08/14	1	B
	Test -13-00014-NAB-050-A	Concrete compressive strength for storm water manhole wall M# 48-M# 49 at 28 Days (MTC:0307)	NAB	04/08/14	04/29/14	04/14/14	6	A
	Test -13-00014-NAB-051-A	Comprehensive for Topping materials , from St. 2+680-2+980- LHS- Project 01(M-1404-54)	NAB	04/08/14	04/29/14	04/14/14	6	B
	Test -13-00014-NAB-052-A	Field density of base course under Retaining Wall, from St. 2+880-2+916- RHS- project 01(M-1404-55)	NAB	04/08/14	04/29/14	04/14/14	6	A
	Test -13-00014-NAB-053-A	Concrete Compressive strength for storm water manhole wall M# 53-54-, and fro Base M# 38-45 at 7 Days –Project 01(MTC:0451)	NAB	04/08/14	04/29/14	04/14/14	6	B
	Test -13-00014-NAB-054-A	Comprehensive of base course (mobile crusher)-Project 01 (MTC:014-0425)	NAB	04/13/14	05/04/14	04/15/14	2	B
	Test -13-00014-DSR-055-A	Field density of pulverization layer, from St. 0+480-0+650 –Project 02 (M-1404-53-a)	DSR	04/14/14	05/05/14	04/15/14	1	A
	Test -13-00014-DSR-056-A	Field density for pulverization layer , from St. 0+150-0+480- and Retest-Project 02 (M-1404-81)	DSR	04/14/14	05/05/14	04/15/14	1	C
	Test -13-00014-DSR-056-B	Field density for pulverization layer , at St. 0+180 and Retest-Project 02 (M-1405-188)	DSR	05/24/14	06/14/14	05/26/14	2	A
	Test -13-00014-DSR-057-A	Comprehensive test for base course from St.0+150-0+660-Project 02 (M-1404-71)	DSR	04/14/14	05/05/14	04/15/14	1	A
	Test -13-00014-NAB-058-A	Concrete Compressive strength for retaining wall from St.2+339-2+369- RHS at 28 days – Project 01(M-1403-134-a)	NAB	04/14/14	05/05/14	04/15/14	1	A
	Test -13-00014-NAB-059-A	Concrete Compressive strength for base of retaining wall from St.2+339-2+369- RHS at 28 days – Project 01 (M-1403-116-a)	NAB	04/14/14	05/05/14	04/15/14	1	A
	Test -13-00014-DSR-060-A	Comprehensive test for pulverization layer, from St. 0+150-0+660- Project 02 (M-1403-307)	DSR	04/14/14	05/05/14	04/15/14	1	A
	Test -13-00014-NAB-061-A	Concrete Compressive strength for retaining wall from St.2+475-2+515- RHS at 7 days – Project 01(N-1403-317)	NAB	04/14/14	05/05/14	04/15/14	1	B
	Test -13-00014-NAB-062-A	Concrete compressive strength for base of retaining wall from St. 2+740to 2+850- RHS- Project 01- (M-1404-70)	NAB	04/15/14	05/06/14	04/21/14	6	B
	Test -13-00014-NAB-063-A	Field density for base course 2nd layer under retaining wall , from St. 2+937-2+954, and from St. 2+965-2+980- RHS –Project 01(M-0511)	NAB	04/15/14	05/06/14	04/21/14	6	A
	Test -13-00014-NAB-064-A	Field density of topping layer , from St. 2+120 to St. 2+580- Project 01 (M-0512)	NAB	04/15/14	05/06/14	04/21/14	6	B

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-065-A	Field density of topping layer , from St. 2+120 to St. 2+580-LHS- Project 01(MTC:014-0567)	NAB	04/15/14	05/06/14	04/21/14	6	A
	Test -13-00014-NAB-066-A	Concrete Compressive strength for Retaining Wall from St. 2+339 to 2+369- part 2 at 28 Days – Project 01 (M-1403-190a)	NAB	04/20/14	05/11/14	04/22/14	2	A
	Test -13-00014-NAB-067-A	Concrete Compressive strength for Retaining Wall from St. 2+740 to 2+745,and from St. 2+750 to 2+760 at 7 Days – Project 01 (M-1404-124)	NAB	04/20/14	05/11/14	04/22/14	2	A
	Test -13-00014-DSR-068-A	Field density of subgrade layer , from St. 0+660 to 0+880 –Project 02 (M-1404-129)	DSR	04/20/14	05/11/14	04/22/14	2	A
	Test -13-00014-NAB-069-A	Comprehensive test for base course 1st layer , from St. 2+120 to 2+580 LHS- Project 01 (MTC:14-0566)	NAB	04/20/14	05/11/14	04/22/14	2	B
	Test -13-00014-NAB-070-A	Field density of base course 1st layer from St. 2+120 to 2+580- RHS –Project 01(MTC:014-0604)	NAB	04/20/14	05/11/14	04/22/14	2	A
	Test -13-00014-NAB-071-A	Field density of base course 1st layer from St. 2+100 to 2+300- LHS –Project 01(MTC:014-0608)	NAB	04/20/14	05/11/14	04/22/14	2	A
	Test -13-00014-DSR-072-A	Field density of subgrade layer , from St. 0+880 to 1+040- Project 02 (M-1404-142)	DSR	04/20/14	05/11/14	04/22/14	2	A
	Test -13-00014-DSR-073-A	Field density of Pulverization layer , from St. 0+650 to 0+720-P 02- (M-1404-156)	DSR	04/20/14	05/11/14	04/22/14	2	B
	Test -13-00014-DSR-074-A	Field density of Pulverization layer , from St. 0+720 to 0+880 and retest - Project 02 (M-1404-183)	DSR	04/20/14	05/11/14	04//22/2014	2	A
	Test -13-00014-DSR-075-A	Field density of Pulverization layer , from St. 0+880 to1+040 and retest - Project 02 (M-1404-189)	DSR	04/20/14	05/11/14	04/22/14	2	A
	Test -13-00014-NAB-076-A	Comprehensive test for base course 2nd layer from St. 2+120 to 2+258- LHS & RHS –Project 01(MTC:14-0605)	NAB	04/24/14	05/15/14	04/27/14	3	B
	Test -13-00014-DSR-077-A	Field Density of base course 1st layer from St. 0+260 to 0+440- Project 02(M-1404-212)	DSR	04/24/14	05/15/14	04/27/14	3	A
	Test -13-00014-NAB-078-A	Concrete compressive strength for wall of storm water manhole M# 46 at 28 Days –Project 01(MTC:14-0354)	NAB	04/24/14	05/15/14	04/27/14	3	A
	Test -13-00014-NAB-079-A	Concrete compressive strength for wall of storm water manhole M# 45 at 7 Days –Project 01(MTC:0471)	NAB	04/24/14	05/15/14	04/27/14	3	B
	Test -13-00014-NAB-080-A	Concrete compressive strength for wall of storm water manhole M# 52- M# 38 at 7 Days –Project 01(MTC:14-0490)	NAB	04/24/14	05/15/14	04/27/14	3	B
	Test -13-00014-NAB-081-A	Concrete compressive strength for wall of storm water manhole M# 58- at 7 Days –Project 01(MTC:14-097)	NAB	04/24/14	05/15/14	04/27/14	3	B
	Test -13-00014-NAB-082-A	Test report on Bituminous Mixture (3/4")- for Sarra detour – Project 01(M-1404-134)	NAB	04/24/14	05/15/14	04/28/14	4	B
	Test -13-00014-DSR-083-A	Comprehensive test for pulverization layer , from St. 0+660 to 1+000-Project 02 (M-1403-149)	DSR	04/24/14	05/15/14	04/27/14	3	A
	Test -13-00014-DSR-084-A	Field density of base course 1st layer from St. 0+440 to 0+640- Project 02 (M-1404-157)	DSR	04/24/14	05/15/14	04/27/14	3	A

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-085-A	Test report on Bituminous Mixture (3/4")- for Bei Iba detour Project 01 (M-1404-185)	NAB	04/24/14	05/15/14	04/28/14	4	B
	Test -13-00014-NAB-086-A	Concrete compressive strength for wall of storm water manhole M# 60 at 7 days –Project 01 (MTC:14-0521)	NAB	04/24/14	05/15/14	04/27/14	3	A
	Test -13-00014-NAB-087-A	Concrete compressive strength for wall of storm water manhole M# 59 at 7 days –Project 01 (MTC:14-0527)	NAB	04/24/14	05/15/14	04/27/14	3	B
	Test -13-00014-NAB-088-A	Concrete compressive strength for foundation of Retaining Wall , from St. 2+880 to 2+916 RHS- Project 01 (M-1404-119)	NAB	04/24/14	05/15/14	04/27/14	3	B
	Test -13-00014-NAB-089-A	Concrete compressive strength for Retaining Wall , from St. 2+790 to 2+800, and from St. 2+810 to 2+820- RHS- Project 01 (M-1404-143)	NAB	04/24/14	05/15/14	04/27/14	3	B
	Test -13-00014-NAB-090-A	Concrete compressive strength for wall of storm water manhole M# 44 at 28 Days –Project 01 (M-1403-235-a)	NAB	04/24/14	05/15/14	04/27/14	3	A
	Test -13-00014-NAB-091-A	Concrete compressive strength for Retaining Wall , from St. 2+770 to 2+780 –RHS-Project 01(m-1404-120)	NAB	04/24/14	05/15/14	04/28/14	4	B
	Test -13-00014-DSR-092-A	Field density for subgrade layer , from St. 1+040 to 1+200-Project 02(M-1404-296)	DSR	04/27/14	05/18/14	04/28/14	1	A
	Test -13-00014-DSR-093-A	Comprehensive test for base course 1st layer from St. 0+660 to 1+040- Project 02(M-1404-222)	DSR	04/27/14	05/18/14	04/28/14	1	B
	Test -13-00014-NAB-094-A	Test report for core test for Beit Iba Detour – Project 01(M-1404-370)	NAB	05/04/14	05/25/14	05/06/14	2	A
	Test -13-00014-DSR-095-A	Comprehensive test for Pulverization layer , from St. 1+040 to 1+500- Project 02 (M-1404-316)	DSR	05/04/14	05/25/14	05/06/14	2	A
	Test -13-00014-NAB-096-A	Test report on bituminous mixture (Marshal analysis) –for binder course from St. 2+140 to 2+340- Project 01(M-1404-321)	NAB	05/04/14	05/25/14	05/06/14	2	B
	Test -13-00014-NAB-097-A	Test report on bituminous mixture (Marshal analysis) –for binder course from St. 2+340 to 2+550- RHS-Project 01(M-1404-335)	NAB	05/04/14	05/25/14	05/06/14	2	B
	Test -13-00014-NAB-098-A	Field density of based course 2nd layer under retaining wall at St. 3+240- 3+600 –RHS-Project 01(MTC: 014-0611)	NAB	05/04/14	05/25/14	05/06/14	2	A
	Test -13-00014-NAB-099-A	Field density of based course 2nd layer under retaining wall at St. 3+560-3+590–RHS-Project 01 (MTC: 014-0640)	NAB	05/04/14	05/25/14	05/06/14	2	A
	Test -13-00014-NAB-100-A	Granular rock fill materials, from St. 2+740 to 2+850 behind Retaining Wall –RHS-Project 01(M-1404-251)	NAB	05/04/14	05/25/14	05/06/14	2	B
	Test -13-00014-NAB-101-A	Concrete compressive Strength for Retaining Wall , from St. 2+937 to 2+954, and from St. 2+965 to 2+980- RHS –Project 01(M-1404-172)	NAB	05/04/14	05/25/14	05/06/14	2	B
	Test -13-00014-NAB-102-A	Concrete compressive Strength for Retaining Wall , from St. 2+745 to 2+750, and from St. 2+830 to 2+840- RHS at 7 Days –Project 01(M-1404-173)	NAB	05/04/14	05/25/14	05/06/14	2	B
	Test -13-00014-NAB-103-A	Concrete compressive Strength for Retaining Wall , from St. 2+475 to 2+515- RHS at 28 Days –Project 01(M-1403-317a)	NAB	05/04/14	05/25/14	05/06/14	2	A
	Test -13-00014-NAB-104-A	Concrete compressive Strength for Retaining Wall , from St. 2+780 to 2+790 & from St. 2+800 to 2+810, & from St. 2+820 to 2+830 and from St. 2+840 to 2+850 - RHS at 7 Days –Project 01(M-1404-209)	NAB	05/04/14	05/25/14	05/06/14	2	B
	Test -13-00014-NAB-105-A	Concrete compressive Strength for Retaining Wall , from St. 2+880 to 2+916-RHS at 7 days- Project 01 (M-1404-263)	NAB	05/04/14	05/25/14	05/06/14	2	B

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-106-A	Test report for Asphalt core for Sarra detour – Project 01 (M-1404-370)	NAB	05/04/14	05/25/14	05/06/14	2	A
	Test -13-00014-NAB-107-A	Field density for back filling materials , behind Retaining Wall from St. 2+740 to 2+850 – RHS- Project 01(MTC: 014-0639)		05/04/14	05/25/14	05/06/14	2	A
	Test -13-00014-NAB-108-A	Field density of subgrade layer , from St. 2+740 to 2+840-RHS- Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-109-A	Field density of topping layer , from St. 2+840 to 3+000-RHS- Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-110-A	Field density of subgrade layer , from St. 2+840 to 2+940-RHS- Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-111-A	Field density of subgrade layer , from St. 3+040 to 3+180-RHS , and from St. 3+160 to 3+280 LHS-Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-112-A	Field density of subgrade layer , from St. 2+940 to 3+040- RHS-Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-113-A	Field density of topping layer , from St. 2+900 to 3+060 LHS & retest –Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-114-A	Field density of topping layer , from St. 2+740 to 2+840 RHS Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-115-A	Field density of base course 1st layer , from St. 2+680 to 2+880 – LHS –Project 01	NAB	05/05/14	05/26/14	05/06/14	1	A
	Test -13-00014-NAB-116-A	Concrete compressive strength for Retaining Wall from St. 3+240 to 3+280, and for Retaining Wall foundation from St. 3+560 to 3+590-RHS-Project 01(M-1404-361)	NAB	05/08/14	05/29/14	05/08/14	0	B
	Test -13-00014-NAB-117-A	Concrete compressive strength for base course of Retaining Wall from St.2+740 to 2+850-RHS at 28 Days -Project 01 (M-1404-70a)	NAB	05/08/14	05/29/14	05/08/14	0	A
	Test -13-00014-DSR-118-A	Field density of subgrade layer , from St. 1+500 to 1+600-Project 02(M-1405-5)	DSR	05/08/14	05/29/14	05/08/14	0	A
	Test -13-00014-NAB-119-A	Field density of topping layer , from St. 3+000 to 3+160-RHS-Project 01(MTC:014-0740)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-120-A	Field density of base course 2nd layer , from St. 2+120 to 2+580-LHS – Project 01(MTC:014-0674)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-121-A	Test report for bituminous mixture (binder) from St. 2+120 to 2+580-LGS-Project 01(MTC:14-0687)	NAB	05/11/14	06/01/14	05/14/14	3	B
	Test -13-00014-DSR-122-A	Field density for base course 1st layer , from St. 0+640 to 1+000 & retest –Project 02(M-1404-379)	DSR	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-DSR-123-A	Field density of pulverization layer m from St. 1+040 to 1+200 & retest -Project 02(M-1404-378)	DSR	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-DSR-124-A	Field density for pulverization layer, from St. 1+200 to 1+400 & retest-Project 02(,-1405-44)	DSR	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-DSR-125-A	Field density of subgrade layer , from St. 1+200 to 1+400 & retest –Project 02(M-1404-360)	DSR	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-DSR-126-A	Field density of subgrade layer , from St. 1+400 to 1+500–Project 02 (M-1405-4)	DSR	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-DSR-127-A	Field density of subgrade layer , from St. 1+600 to 1+800–Project 02(M-1405-43)	DSR	05/11/14	06/01/14	05/14/14	3	A

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-128-A	Concrete compressive strength for Retaining Wall , from St. 2+880 to 2+885, from St. 2+895 to 2+903, from St. 2+949 to 2+954, and for Retaining Wall foundation , from St. 3+240 to 3+300- RHS- at 7 days –Project 01(M-1404-309)	NAB	5/11/2014	06/01/14	05/14/14	3	B
	Test -13-00014-NAB-129-A	Field density for topping layer , from St. 3+160 to 3+280- LHS- Project 01(MTC:014-0754)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-130-A	Field density for topping layer , from St. 3+240 to 3+280- RHS- Project 01(MTC:014-0777)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-131-A	Field density for base course 1st layer , from St. 2+300 to 2+580- LHS- Project 01(MTC:014-0641)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-132-A	Field density for base course 1st layer ,under Retaining wall from St. 3+340 to 3+370- RHS- Project 01(MTC:014-0778)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-133-A	Field density for subgrade layer , from St. 3+000 to 3+100- LHS-Project 01(MTC:014-0661)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-134-A	Field density for topping layer , from St. 2+700 to 2+900- LHS-Project 01(MTC:014-0621)	NAB	05/11/14	06/01/14	05/14/14	3	A
	Test -13-00014-NAB-135-A	Field density for base course 1st layer , from St. 2+740 to 3+000 –RHS & retest Project 01 (MTC: 014-0815)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-136-A	Comprehensive test for topping layer from St. 2+680 to 3+300- LHS & RHS –Project 01(MTC:14-0733)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-137-A	Comprehensive test for base course 1st layer , from St. 2+680 to 3+180 RHS- Project 01 (MTC:14-0734)	NAB	05/14/14	06/04/14	05/19/14	5	B
	Test -13-00014-NAB-138-A	Comprehensive test for base course 1st layer from St. 2+640 to 3+160- LHS –Project 01(MTC: 14-0773)	NAB	05/14/14	06/04/14	05/19/14	5	B
	Test -13-00014-NAB-139-A	Concrete compressive strength for storm water manhole base for M# 51 & 55, storm water wall M# 50, and blinding for M# 54& 53& 52 & 60& 59& 58- at 28 Days –Project 01(MTC:14-0421)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-140-A	Concrete compressive strength for storm water manhole base for M# 52 & 53& 54& 60, storm water wall M# 39, and blinding for M# 45 at 28 Days –Project 01(MTC:14-0426)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-141-A	Concrete compressive strength for storm water manhole wall for M# 45 at 28 Days –Project 01 (MTC: 0471)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-142-A	Concrete compressive strength for storm water manhole wall for M# 51, for base M#45, M# 59, M#58, and blinding for M#38 at 28 Days (MTC:0429) –Project 01	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-143-A	Concrete compressive strength for storm water manhole wall for M# 55& M# 38, at 28 Days –Project 01 (MTC:14-0490)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-144-A	Concrete compressive strength for storm water manhole wall for M# 58, at 28 Days –Project 01 (MTC:14-0497)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-145-A	Concrete compressive strength for storm water manhole wall for M# 60 at 28 Days –Project 01(MTC: 14-0512)	NAB	05/14/14	06/04/14	05/19/14	5	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT IN THE NORTH (MRNII)

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-146-A	Concrete compressive strength for storm water manhole wall for M# 59 at 28 Days –Project 01 (MTC:14-0527)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-147-A	Concrete compressive strength for Retaining Wall, from St. 2+740 to 2+745, and from St. 2+750 to 2+760 at 28 Days- Project 01(M-1404-124a)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-148-A	Concrete compressive strength for Retaining Wall foundation, from St. 2+880 to 2+916- RHS at 28 Days- Project 01(M-1404-143a)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-149-A	Concrete compressive strength for Retaining Wall foundation, from St. 2+880 to 2+916- RHS at 28 Days- Project 01(M-1404-119a)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-150-A	Concrete compressive strength for Retaining Wall ,from St. 2+770 to 2+780- RHS at 28 Days- Project 01(M-1404-120-a)	NAB	05/14/14	06/04/14	05/19/14	5	A
	Test -13-00014-NAB-151-A	Concrete compressive strength for Retaining Wall ,from St. 3+247 to 3+255 , and from St. 3+262 to 3+273- RHS at 7 Days- Project 01 (M-1404-6)	NAB	05/14/14	06/04/14	05/19/14	5	B
	Test -13-00014-NAB-152-A	Concrete compressive strength for Retaining Wall ,from St. 3+566 to 3+576 , and from St. 3+582 to 3+589- and for Retaining wall foundation from St. 3+180 to 3+220-RHS at 7 Days- Project 01(M-1405-6)	NAB	05/14/14	06/04/14	05/19/14	5	B
	Test -13-00014-DSR-153-A	Comprehensive test for base course (Mobile Crusher)- Project 02(M-1405-29 a)	DSR	05/15/14	06/05/14	05/19/14	4	B
	Test -13-00014-NAB-154-A	Concrete compressive strength for Retaining Wall from St. 3+180 to 3+190, and from St. 3+194 to 3+204, and from St. 3+576 to 3+582 at 7 Days -Project 01 -(M-1405-54)	NAB	05/18/14	06/08/14	05/19/14	1	B
	Test -13-00014-NAB-155-A	Concrete compressive strength for Retaining Wall ,from St. 3+190 to 3+194 , and from St. 3+204 to 3+214- RHS at 7 Days- Project 01(M-1405-88)	NAB	05/18/14	06/08/14	05/19/14	1	B
	Test -13-00014-NAB-156-A	Concrete compressive strength for Retaining Wall ,from St. 2+780 to 2+790 , from St. 2+800 to 2+810, from St. 2+820 to 2+830, and from St. 2+840 to 2+850 RHS at 28 Days- Project 01(M-1404-209a)	NAB	05/18/14	06/08/14	05/19/14	1	A
	Test -13-00014-NAB-157-A	Concrete compressive strength for Retaining Wall ,from St. 2+937 to 2+954 , from St. 2+965 to 2+980 RHS at 28 Days- Project 01(M-1404-172a)	NAB	05/18/14	06/08/14	05/19/14	1	A
	Test -13-00014-NAB-158-A	Concrete compressive strength for Retaining Wall ,from St. 2+745 to 2+750 , from St. 2+830 to 2+840 RHS at 28 Days- Project 01 (M-1404-173 a)	NAB	05/18/14	06/08/14	05/19/14	1	A
	Test -13-00014-DSR-159-A	Comprehensive test for pulverization layer , from St. 1+500 to 2+000- Project 02 (MTC:14-0775)	DSR	05/21/14	06/11/14	05/26/14	5	A
	Test -13-00014-DSR-160-A	Field density for base course 1st layer , from St. 1+000 to 1+160- LHS –Project 02 (MTC:014-0865)	DSR	05/21/14	06/11/14	05/26/14	5	A
	Test -13-00014-DSR-161-A	Field density for subgrade layer, from St. 1+800 to 2+020- Project 02 (M-1405-172)	DSR	05/21/14	06/11/14	05/26/14	5	A
	Test -13-00014-DSR-162-A	Comprehensive test for base course 1st layer , from St. 1+000 to 1+200- Project 02 (M-1405-77)	DSR	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-163-A	Field density for base course 2nd layer , from St. 2+100 to 2+580- RHS-Project 01 (MTC: 014-0652)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-DSR-164-A	Comprehensive test for base course Mobile crusher- Project 02)MTC: 14-0837)	DSR	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-165-A	Comprehensive test for base course 2nd layer , from St. 2+740 to 3+180- RHS-Project 011 (M-1405-190)	NAB	05/25/14	06/15/14	05/26/14	1	A

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-166-A	Comprehensive test for base course Jamaeen Crusher –Project 01 (MTC: 14-0834)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-167-A	Field density for topping layer , from St. 2+580 to 2+680- RHS- Project 01(MTC:014-0874)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-168-A	Field density for base course 1st layer , from St. 2+880 to 3+060- LHS- Project 01 (MTC: 014-0867)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-169-A	Field density for subgrade layer , from St. 3+440 to 3+540- LHS-Project 01 (MTC:014-0882)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-170-A	Field density for subgrade layer , from St. 3+180 to 3+280- RHS-Project 01 (MTC:014-0845)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-171-A	Field density for subgrade layer , from St. 2+580 to 2+680 -Project 01 (MTC: 014-0859)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-172-A	Field density for topping layer , from St. 2+680 to 2+740- RHS-Project 01 (MTC:014-0846)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-173-A	Concrete compressive strength for Retaining Wall from St. (3+566 to 3+576) , & from St. 3+582 to 3+589), and for foundation from St. (3+180 to 3+220) –RHS –Project 01 (M-1405-7)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-174-A	Comprehensive test base course 1st layer from St. 3+160 to 3+300 RHS & LHS , and for junction , from St. 2+580 to 2+680 -Project 01 (M1405-233)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-175-A	Sieve & proctor for base course 2nd layer , from St. 2+680 to 2+860-LHS-Project 01 (MTC:14-0819)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-176-A	Field density for base course 1st layer, from St. 2+680 to 2+740 & from St. 3+180 to 3+280 -RHS-Project 01 (M-1405-282)	NAB	05/25/14	06/15/14	05/26/14	1	A
	Test -13-00014-NAB-177-A	Field density for subgrade layer , from St. 2+680 to 2+740- RHS- Project 01 (MTC: 014-0830B)	NAB	05/26/14	06/16/14	05/29/14	3	A
	Test -13-00014-NAB-178-A	Concrete compressive strength for Retaining Wall , from St. 2+880 to 2+916- RHS at 28 Days –Project 01 (M-1404-263a)	NAB	05/26/14	06/16/14	05/29/14	3	A
	Test -13-00014-NAB-179-A	Concrete compressive strength for Retaining Wall foundation , from St. 3+341 to 3+370, and for Retaining Wall from St. 3+284 to 3+294 - RHS at 7 Days –Project 01 (M-1405-179)	NAB	05/26/14	06/16/14	05/29/14	3	A
	Test -13-00014-NAB-180-A	Comprehensive test for base course 2nd layer , from St. 2+680 to 3+160- LHS –Project 01 (M-1405-249)	NAB	05/26/14	06/16/14	05/29/14	3	A
	Test -13-00014-NAB-181-A	Field density test for base course 1st layer , from St. 3+000 to 3+160-RHS- & retest Project 01 (MTC: 014-0830)	NAB	05/26/14	06/16/14	05/29/14	3	A
	Test -13-00014-DSR-182-A	Field density test for pulverization layer, from St. 1+400 to 1+800& retest –Project 02 (M-1405-188)	DSR	05/27/14	06/17/14	05/29/14	2	A
	Test -13-00014-NAB-183-A	Comprehensive test for topping layer , from St. 3+440 to 3+540- RHS-Project 01(MTC:14-0902)	NAB	05/27/14	06/17/14	05/29/14	2	A
	Test -13-00014-NAB-184-A	Concrete compressive strength for Retaining Wall , from St. 3+240 to 3+280- RHS , and for Retaining Wall foundation from St. 3+560 to 3+590- RHS-at 28 Days-Project 01 (M-1404-361)	NAB	05/27/14	06/17/14	05/29/14	2	A

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-185-A	Concrete compressive strength for Retaining Wall , from St. 3+340 to 3+350- RHS , and from St. 3+360 to 3+370- RHS-at 7 Days-Project 01(M-1405-220)	NAB	05/27/14	06/17/14	05/29/14	2	A
	Test -13-00014-DSR-186-A	Field density for subgrade layer , from St. 2+020 to 2+080- Project 02 (M-1405-325)	DSR	05/27/14	06/17/14	05/29/14	2	A
	Test -13-00014-DSR-187-A	Sieve & proctor test for base course 2nd layer , from St. 0+800 to 1+200 LHS –Project 02 (MTC: 14-0945)	DSR	06/03/14	06/24/14	06/08/14	5	A
	Test -13-00014-NAB-188-A	Field Density for subgrade layer , from St. 3+980 to 4+080- RHS Project 01 (MTC: 014-0913)	NAB	06/03/14	06/24/14	06/08/14	5	A
	Test -13-00014-NAB-189-A	Field Density for topping layer from St. 3+980 to 4+080-RHS Project 01 (MTC: 014-0948) (MTC: 014-0962)	NAB	06/03/14	06/24/14	06/08/14	5	A
	Test -13-00014-NAB-190A	Field Density for 2nd base course layer from St. 3+160 to 3+260-RHS Project 01 (MTC: 014-0961)	NAB	06/03/14	06/24/14	06/08/14	5	A
	Test -13-00014-NAB-191-A	Field Density for base course 1st layer from St. 3+060 to 3+280-LHS-Project 01 (MTC: 014-0912)	NAB	06/03/14	06/24/14	06/08/14	5	A
	Test -13-00014-NAB-192-A	Field Density for base course 1st layer from St. 2+580 to 2+680 Project 01(MTC: 014-0896)	NAB	06/03/14	06/24/14	06/08/14	5	A
	Test -13-00014-NAB-193-A	Test report for bituminous mixture (binder 1") from St. 3+060 to 3+220- LHS & RHS (MTC: 014-0973)	NAB	06/03/14	06/24/14	06/08/14	5	A
	Test -13-00014-NAB-194-A	Test report for bituminous mixture (binder 1") from St. 2+550 to 3+060 -RHS Project 01 (MTC: 14-0952)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-195-A	Test report for bituminous mixture (binder 1") from St. 2+580 to 3+060 -LHS Project 01 (MTC: 14-0954)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-196-A	Field density for subgrade layer from St. 3+860 to 3+980 THS- Project 01(MTC: 014-0965)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-197-A	Field density for subgrade layer from St. 3+540 to 3+600 and from St. 3+700 to 3+860 RHS-Project 01 (MTC: 014-0966)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-198-A	Field density for base course 2nd layer from St. 2+580 to 3+160 – RHS- Project 01 (MYC: 014-0940)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-199-A	Field density for base course 2nd layer from St. 3+060 to 3+220 – LHS- Project 01 (MTC: 014--0964)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-200-A	Comprehensive test for topping layer from St. 3+440 to 4+000- RHS- Project 01 (MTC: 14-0902)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-201-A	Comprehensive test base course 2nd layer from St. 2+580 to 2+680 RHS & LHS , and St. 2+680 to 2+740- RHS and St. 3+160 to 3+260 RHS & LHS – Project 01 (MTC: 14-0908)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-202-A	Field density for base course 2nd layer from St. 2+580 to 3+060- LHS (MTC:014-0947)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-DSR-203-A	Field density for pulverization layer from St. 1+800 to 2+020- LHS (M-1405-340)	NAB	06/04/14	06/25/14	06/08/14	4	C
	Test -13-00014-DSR-203-B	Field density for pulverization layer from St. 1+800 to 2+020- LHS & Retest(M-1405-323)(M-1405-368) (M-1405-340)	NAB	06/16/14	07/07/14	06/15/14	-1	A

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-NAB-204-A	Field density for topping layer from St. 3+440 to 3+540- RHS –Project 01 & retest (MTC: 014-0936) (MTC:014-0938)	NAB	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-DSR-205-A	Comprehensive test for base course 2nd layer from St. 0+250 to 1+000 RHS _Project 02 (MTC: 014-0878)	DSR	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-DSR-206-A	Comprehensive test for base course 2nd layer , from St. 0+260 to 1+000 – LHS –Project 02 (MTC:014-0860)	DSR	06/04/14	06/25/14	06/08/14	4	A
	Test -13-00014-NAB-207-A	Test report for bituminous mixture binder 1" from St. 2+550 to 3+060- RHS –Project 01 (MTC:14-0944)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-208-A	Test report for steel reinforcement Φ12- at Project 02 (M-1406-26)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-209-A	Field density for subgrade layer from St. 2+080 to 2+180- Project 02 (M-1405-357)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-210-A	Concrete compressive strength for Retaining Wall from St. 3+180 to 3+190- St. 3+194 to 3+204 and from St. 3+576 to 3+582 at 28 Days- Project 01 (M-1405-54 a)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-211-A	Field density of subgrade layer , from St. 3+820 to 4+060- Project 01 (M-1406-26)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-212-A	Concrete compressive strength for Retaining Wall from St. 3+247 to 3+255 and from St. 3+262 to 3+273 – RHS- at 28 Days –Project 01 (M-1406-6a)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-213-A	Concrete compressive strength for Retaining Wall from St. 3+190 to 3+194 and from St. 3+204 to 3+214 – RHS- at 28 Days –Project 01 (M-1405-88a)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-214-A	Concrete compressive strength for Retaining Wall from St. 3+565 to 3+576 and from St. 3+582 to 3+389, and foundation from St. 3+180 to 3+220 RHS at 28 Days –Project 01 (M-1405-7a)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-215-A	Concrete compressive strength for Retaining Wall from St. 3+550 to 3+360 RHS , and foundation for boundary wall from St. 3+828 to 3+854 RHS at 7 Days –Project 01 (M-1405-265)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-216-A	Concrete test report for foundation of step barrier from St. 1+390 to 1+425) Project 02 (M-1405-403)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-217-A	Concrete test report for step barrier beam from St. 1+300 to 1+390 at 7 Days –Project 02 (M-1405-359)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-218-A	Concrete compressive strength for boundary wall from St. 3+842 to 3+854 RHS and for foundation from St. 3+824 to 3+832) RHS- Project 01 (M-1405-358)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-219-A	Concrete test report for Retaining Wall from St. 3+660 to 3+670 and from St. 3+680 to 3+690 at 7 Days – Project 01 (M 1405-404)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-220-A	Concrete compressive strength for Retaining Wall foundation from St. 3+650 to 3+690 RHS , and Parapet for stair at St. 2+370 RHS – at 7 Days- Project 01 (M-1405-345)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-221-A	Comprehensive test for base course 1stlayer from St. 3+450 to 4+000- RHS- Project 01 (MTC: 14-0951)	NAB	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-222-A	Field density for base course 1st layer from St. 1+200 to 1+420- Project 02 (M-1406-85a)	DSR	06/10/14	07/01/14	06/11/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT IN THE NORTH (MRNII)

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-DSR-223-A	Comprehensive test for pulverization layer , from St. 2+000 to 2+180- Project 02 (MTC: 14-0981)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-224-A	Field density for pulverization layer from St. 2+000 to 2+180& Retest – Project 02 (MTC: 014-1006) (MTC:014-1012A)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-225-A	Comprehensive test for base course 1st layer from St. 1+200 to 1+700 RHS-Project 02 (M-1406-9)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-DSR-226-A	Comprehensive test for base course 1st layer from St. 1+200 to 1+700 LHS-Project 02 (M-1405-318)	DSR	06/10/14	07/01/14	06/11/14	1	A
	Test -13-00014-NAB-227-A	Field density for topping layer from St. 3+720 to 3+820 RHS and from St. 3+840 to 3+960 LHS & Retest – Project 01 (MTC:014-1047)(MTC: 014-1048)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-228-A	Comprehensive Test for topping layer from St. 3+440 to 4+000 LHS –Project 01 (MTC:014-1028)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-229-A	Comprehensive test for base course 1st layer from St. 3+500 to 4+000 LHS- Project 01 (M-1406-125)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-230-A	Field density for base course 1st layer from St. 3+440 to 3+980 RHS & Retest –Project 01 (MTC:014-1066)((MTC:014-1091)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-231-A	Field density for topping layer from St. 3+500 to 3+600 LHS-Project 01 (MTC: 014-1056)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-232-A	Field density for subgrade layer from St. 3+720 to 3+820 LHS- Project 01 (MTC: 014-1049)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-233-A	Field density for subgrade layer from St. 3+620 to 3+720 LHS- Project 01 (MTC: 014-1067)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-234-A	Field density for subgrade layer from St. 3+500 to 3+600 LHS- Project 01 (MTC: 014-1031)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-235-A	Field density for topping layer from St. 3+720 to 3+820 LHS- Project 01 (MTC: 014-1082)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-236-A	Concrete test report on Retaining Wall at St. 3+630 – RHS at 7 Days –Project 01 (M-1405-33)	NAB	06/16/14	07/07/14	06/19/14	3	A
	Test -13-00014-NAB-237-A	Field density for subgrade layer from St. 3+680 to 3+720 RHS- Project 01 (MYTC: 014-1120)	NAB	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-NAB-238-A	Field density for topping layer from St. 3+680 to 3+720 LHS- Project 01 (mtc:014-1109)	NAB	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-NAB-239-A	Test report on Asphalt core test from St. 2+170 to 3+200 – RHS- Project 01 (MTC: 14-1016)	NAB	06/21/14	07/12/14	06/24/14	3	C
	Test -13-00014-NAB-240-A	Concrete test report for Retaining Wall foundation at St. 3+280 at 28 Days- Project 01 (M-1405-132 a)	NAB	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-241-A	Field density for base course 1st layer from St. 1+880 to 1+980 – Project 02(MTC: 014-1119)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-242-A	Concrete test report for retaining Wall from St. 3+560 to 3+570 RHS and boundary Wall from St. 3+828 to 3+857- Project 02(M-1405-15)	DSR	06/21/14	07/12/14	06/24/14	3	C
	Test -13-00014-DSR-243-A	Concrete compressive strength for step barrier from St. 1+515 to 1+585- RHS –Project 02 (M-1405-16)	DSR	06/21/14	07/12/14	06/24/14	3	A

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-DSR-244-A	Concrete compressive strength for step barrier from St. 1+585 to 1+605- at 7 Days –Project 02(M-1405-32)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-245-A	Concrete compressive strength for step barrier from St. 1+418 to 1+440- at 7 Days –Project 02(M-1405-418)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-246-A	Test report on Reinforcement steel bars Φ14- Project 02(M-1406-126)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-247-A	Field density for base course 1st layer from St. 1+520 to 1+640 - & Retest –Project 02 (MTC:014-1070) (MTC:014-1094)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-248-A	Field density for base course 1st layer from St. 1+780 to 1+880-Project 02 (MTC:014-1071)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-249-A	Field density for base course 2nd layer from St. 0+260 to 0+830-Project 02 (MTC:014-1005)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-250-A	Field density for base course 1st layer from St. 2+020 to 2+200 & Retest -Project 02 (MTC:014-1058) (MTC:014-1059)	DSR	06/21/14	07/12/14	06/24/14	3	A
	Test -13-00014-DSR-251-A	Comprehensive test for base course 2nd layer from St. 1+500 to 2+000- Project 02 (MTC:14-1122)	DSR	06/23/14	07/14/14	06/24/14	1	A
	Test -13-00014-DSR-252-A	Comprehensive test for base course 2nd layer from St. 1+000 to 1+500- Project 02(MTC:14-1053)	DSR	06/23/14	07/14/14	06/24/14	1	A
	Test -13-00014-DSR-253-A	Comprehensive test for base course 1st layer from St. 1+700 to 2+180- Project 02 (MTC: 14-1013)	DSR	06/23/14	07/14/14	06/24/14	1	A
	Test -13-00014-DSR-254-A	Field density for base course 2nd layer , from St. 0+830 to 1+120 & Retest –Project 02 (MTC: 014-1055)(MTC:014-1055 A)	DSR	06/23/14	07/14/14	06/24/14	1	A
	Test -13-00014-DSR-255-A	Test report for Asphalt marshal test from St. 0+500 to 0+830 –Project 02 (MTC:014-1023)	DSR	06/23/14	07/14/14	06/24/14	1	A
	Test -13-00014-DSR-256-A	Test report for Asphalt marshal test from St. 0+260 to 0+500 –Project 02 (MTC:14-1032)	DSR	06/23/14	07/14/14	06/24/14	1	A
	Test -13-00014-NAB-257-A	Test Report for Steel Reinforcement Φ18 –Project 01-(M-1406-325)	NAB	06/28/14	07/19/14		PE	
	Test -13-00014-NAB-258-A	Field Density for Topping layer from St. 3+620 to 3+720 LHS- Project 01 (MTC:014-1109)	NAB	06/28/14	07/19/14		PE	
	Test -13-00014-NAB-259-A	Field Density subgrade layer from St. 1+600 to 1+660 –RHS- Project 01- (M-1406-278)	NAB	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-260-A	Test Report on Concrete Compressive strength for Wall of Pipe culvert at St. 0+860 –Project 02 (M-1406-133)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-261-A	Test Report on concrete Compressive Strength for Retaining Wall base from St. 1+470 to 1+500 at out let pipe culvert at St. 1+480- Project 02 (M-1406-134)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-262-A	Test Report on concrete Compressive Strength for Retaining Wall from St. 1+60 to 1+680 & at St. 1+470 to 1+480-at 7 Days Project 02 (M-1406-218)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-263-A	Test Report on concrete Compressive Strength for Retaining Wall from St. 1+690 to 1+700 & at St. 1+710 to 1+720-at 7 Days Project 02 (M-1406-149)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-264-A	Test Report on concrete Compressive Strength the base of inlet of pipe culvert at St. 1+480 at 7 Days Project 02(M-1406-170)	DSR	06/28/14	07/19/14		PE	

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT IN THE NORTH (MRNII)

SUBMITTAL				TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	Test -13-00014-DSR-265-A	Test Report on concrete Compressive Strength for step barrier at St. 1+665 to 1+710- Project 02 (M-1406-171)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-266-A	Test Report on concrete Compressive Strength for walls at St. 1+744 to 1+754- LHS- at 7 Days Project 02 (M-1406-182)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-267-A	Test Report on concrete Compressive Strength for Retaining walls at St. 1+465 to 1+515- LHS-at 7 Days Project 02 (M-1406-183)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-268-A	Test Report on concrete Compressive Strength step barrier beam from St. 1+710 to 1+765 at 7 Days Project 02 (M-1406-201)	DSR	06/28/14	07/19/14		PE	
	Test -13-00014-DSR-269-A	Test Report on Asphalt marshal (1" binder) from St. 1+100 to 1+400 – Project 02 (MTC: 14-1249)	DSR	06/28/14	07/19/14		PE	

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

G | RFI's Log for the Reporting Period

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
RFIs log - MRNII

Request For Information				TRACKING DATES				Response By
Spec. No.	RFI No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	RFI-13-00014-MRNII-001	Scope of work out of ROW Deir Sharaf – Inab road Project, TO # 14	NAB	01/15/14	02/05/14	01/28/14	13	Saleem Tafesh
	RFI-13-00014-MRNII-002	Storm water manholes in Nablus Beit Iba Der Sharaf Road-TO # 14	NAB	01/15/14	02/05/14	01/28/14	13	Saleem Tafesh
	RFI-13-00014-MRNII-003	New scope for underground utilities /Nablus -Beit iba Road project, TO # 14	NAB	01/30/14	02/20/14	02/13/14	14	Saleem Tafesh
	RFI-13-00014-MRNII-004	Outfall for storm water at Sta. 2+220 / Nablus - Beit Iba - Deir Sharaf Road Project TO # 14	NAB	02/05/14	02/26/14	02/13/14	8	Saleem Tafesh
	RFI-13-00014-MRNII-005	Part of Scope of work out of ROW- Nablus Beit Iba Der Sharaf Road-Segment A	NAB	02/11/14	03/04/14	02/24/14	13	Saleem Tafesh
	RFI-13-00014-MRNII-006	Unsuitable sub grade material in Nablus - Beit Iba - Deir Sharaf Road Project#1, TO # 14	NAB	02/11/14	03/04/14	02/24/14	13	Saleem Tafesh
	RFI-13-00014-MRNII-007	Stone Wall at cut slope at Nablus Beit Eba – Deir Sharaf Road, TO #14	NAB	02/13/14	03/06/14	02/24/14	11	Saleem Tafesh
	RFI-13-00014-MRNII-008	Site conditions and challenges to design requirements to be considered during the preparation of shop drawings from Sta.2+600 to Sta.3+000 - Project #1	NAB	02/16/14	03/09/14	02/24/14	8	Saleem Tafesh
	RFI-13-00014-MRNII-009	Storm water system -Outfall at Sta. 2+640 / Nablus - Beit Iba - Deir Sharaf Road Project TO # 14	NAB	03/01/14	03/22/14	03/05/14	4	Saleem Tafesh
	RFI-13-00014-MRNII-010	Site conditions and challenges to design requirements to be considered during the preparation of shop drawings from Sta.0+700 to Sta.1+200 AT Deir Sharaf –Tulkarem road Project Task Order #14	DSR	03/01/14	03/22/14	03/05/14	4	Saleem Tafesh
	RFI-13-00014-MRNII-011	Lighting Poles -SUB-13-00014-NAB-090-A-Nablus-Beit Iba -Project 01-T.O.14	NAB	03/06/14	03/27/14	03/10/14	4	Saleem Tafesh
	RFI-13-00014-MRNII-012	Existing sewer manholes at sta. 0+150, 0+193 and 0+420 Extend inlet of existing pipe culvert @sta. 0+180 AT Deir Sharaf –Tulkarem road Project # 2 Task Order #14	DSR	03/09/14	03/30/14	03/11/14	2	Saleem Tafesh
	RFI-13-00014-MRNII-013	Site conditions and challenges to design requirements to be considered during the preparation of shop drawings from Sta.3+500 to Sta.4+100 At Nablus – Beit Iba – Deir Sharaf Road Project #1, (TO #14)	NAB	03/09/14	03/30/14	03/18/14	9	Saleem Tafesh
	RFI-13-00014-MRNII-014	Site conditions and challenges to design requirements to be considered during the preparation of shop drawings from Sta.2+300 to Sta.3+500 -At Nablus – Beit Iba – Deir Sharaf Road Project #1, (TO #14)	NAB	03/09/14	03/30/14	03/13/14	4	Saleem Tafesh
	RFI-13-00014-MRNII-015	Replacement of Sub grade-Deir Sharaf –Tulkarem Road Project02 Task Order #14	DSR	03/10/14	03/31/14	03/11/14	1	Saleem Tafesh
	RFI-13-00014-MRNII-016	Revised Intersection at Sta. 2+600 -at Nablus – Beit Iba – Deir Sharaf Road Project #1, (TO #14)	NAB	04/02/14	04/23/14	04/15/14	13	Saleem Tafesh
	RFI-13-00014-MRNII-017	Existing pipe culvert at sta. 0+730 AT Deir Sharaf –Tulkarem road Project # 2 Task Order #14	DSR	04/06/14	04/27/14	04/15/14	9	Saleem Tafesh
	RFI-13-00014-MRNII-018	Double box culvert and Storm water system -Outfall at Sta. 3+609 / Nablus - Beit Iba - Deir Sharaf Road Project TO # 14	NAB	04/06/14	04/27/14	04/24/14	18	Saleem Tafesh

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #14, MULTIPLE ROADS PROJECT (NORTH II)
RFIs log - MRNII

Request For Information				TRACKING DATES				Response By
Spec. No.	RFI No	Description	DV	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	
	RFI-13-00014-MRNII-019	Outfall for storm water at Sta. 3+280 / Nablus - Beit Iba - Deir Sharaf Road Project TO # 14	NAB	04/17/14	05/08/14	04/24/14	7	Saleem Tafesh
	RFI-13-00014-MRNII-020	Working out of Road ROW from sta. 1+500 to sta. 2+020 (Project #1, TO # 14	NAB	04/28/14	05/19/14	05/12/14	14	Saleem Tafesh
	RFI-13-00014-MRNII-021	Working out of Road ROW from sta. 4+100 to sta. 4+105 RHS ,from Sta.4+410 to Sta.4+520 LHS and from Sta.4+820 to Sta.4+830 LHS (Project #1, TO # 14)	NAB	04/28/14	05/19/14	05/12/14	14	Saleem Tafesh
	RFI-13-00014-MRNII-022	Site conditions to be considered during the preparation of shop drawings from Sta.4+100 to Sta.4+800-at Nablus – Beit Iba – Deir Sharaf Road Project #1, (TO #14)	NAB	05/08/14	05/29/14	05/21/14	13	Saleem Tafesh
	RFI-13-00014-MRNII-023	Proposed pipe culvert at sta. 1+480 AT Deir Sharaf –Tulkarem road Project # 2 Task Order #14	DSR	05/12/14	06/02/14	05/14/14	2	Saleem Tafesh
	RFI-13-00014-MRNII-024	Unsuitable subgrade material and required concrete ditch/ protection from sta. 1+800 to sta. 2+180, Project #2, TO 13-00014.	DSR	05/19/14	06/09/14	05/26/14	7	Saleem Tafesh
	RFI-13-00014-MRNII-025	PALTEL regarding their proposed underground services / Deir Sharaf –Tulkarem road Project # 2 Task Order #14	DSR	05/25/14	06/15/14	05/26/14	1	Saleem Tafesh
	RFI-13-00014-MRNII-026	Additional precast manholes for underground high tension cables and for connection of future sewer pipelines at Nablus -Beit Iba Road project, TO # 14	NAB	05/25/14	06/15/14	06/04/14	10	Saleem Tafesh
	RFI-13-00014-MRNII-027	Existing storm pipes and manhole at sta. 3+920 RHS At Nablus – Beit Iba – Deir Sharaf Road Project #1, (TO #14)	NAB	06/30/14	07/21/14			

H | Geo-MIS DATA COLLECTION SHEET
Generated Person Days of Employment

USAID WEST BANK/ GAZA

INFRASTRUCTURE NEEDS PROGRAM INPII

CONTRACT NO. AID-294-I-00-12-00005

TASK ORDER NO. AID-294-TO-13-00014

Multiple Roads North-MRNII

Temproray Job Days Summary Report

Task Order Name: Multiple Roads North - MRNII

PERIOD FROM: December 03, 2013

Sub-project or Activity Name: Project 01- Nablus- Beit Iba- Deir Sharaf Road

PERIOD TO: June 30, 2014

CONTRACTOR: APCO/ArCon

Date		Site Staff Job Days**					Total Job Days	No of Full Time Equivalent (FTE) Jobs in the Month*	Notes of Comments
Month	Year	Management	Engineers	Skilled Labor	Unskilled Labor	Other			
October	2012						0	0	
November	2012						0	0	
December	2012						0	0	
January	2013						0	0	
February	2013						0	0	
March	2013						0	0	
April	2013						0	0	
May	2013						0	0	
June	2013						0	0	
July	2013						0	0	
August	2013						0	0	
September	2013						0	0	
Total of FY 2013							0	0	
October	2013						0	0	
November	2013						0	0	
December	2013	28	8	9	0	0	45	2	
January	2014	86	66	163	143	0	458	19	
February	2014	80	96	480	290	0	946	40	
March	2014	89	135	736	444	0	1404	59	
April	2014	83	153	1119	701	0	2056	86	
May	2014	74	110	823	622	0	1629	68	
June	2014	98	103	973	782	0	1956	82	
July	2014						0	0	
August	2014						0	0	
September	2014						0	0	
Total of FY 2014							8493	357	
October	2014						0	0	
November	2014						0	0	
December	2014						0	0	
January	2015						0	0	
February	2015						0	0	
March	2015						0	0	
April	2015						0	0	
May	2015						0	0	
June	2015						0	0	
July	2015						0	0	
August	2015						0	0	
September	2015						0	0	
Total of FY 2015							0	0	

Note :

* No of Full Time Equivalent (FTE) Jobs in the Month = Total Job Days / Avg. Days in the Month(23.8)

** This data collection sheet is for Palestinian staff only , experts and foreign employee shall not be included.

Note: Numbers are rounded to the nearest integer number.

USAID WEST BANK/ GAZA

INFRASTRUCTURE NEEDS PROGRAM INPII

CONTRACT NO. AID-294-I-00-12-00005

TASK ORDER NO. AID-294-TO-13-00014

Multiple Roads North-MRNII

Temproray Job Days Summary Report

Task Order Name: Multiple Roads North - MRNII

PERIOD FROM: December 03, 2013

Sub-project or Activity Name: Project 02- Deir Sharaf- Tulkarem Road

PERIOD TO: June 30, 2014

CONTRACTOR: APCO/ArCon

Date		Site Staff Job Days**					Total Job Days	No of Full Time Equivalent (FTE) Jobs in the Month*	Notes of Comments
Month	Year	Management	Engineers	Skilled Labor	Unskilled Labor	Other			
October	2012						0	0	
November	2012						0	0	
December	2012						0	0	
January	2013						0	0	
February	2013						0	0	
March	2013						0	0	
April	2013						0	0	
May	2013						0	0	
June	2013						0	0	
July	2013						0	0	
August	2013						0	0	
September	2013						0	0	
Total of FY 2013							0	0	
October	2013						0	0	
November	2013						0	0	
December	2013	18	5	6	0	0	28	1	
January	2014	27	14	1	4	0	46	2	
February	2014	30	37	27	25	0	118	5	
March	2014	39	41	197	114	0	391	16	
April	2014	40	65	345	111	0	559	24	
May	2014	34	67	313	110	0	524	22	
June	2014	31	77	486	333	0	927	39	
July	2014						0	0	
August	2014						0	0	
September	2014						0	0	
Total of FY 2014							2594	109	
October	2014						0	0	
November	2014						0	0	
December	2014						0	0	
January	2015						0	0	
February	2015						0	0	
March	2015						0	0	
April	2015						0	0	
May	2015						0	0	
June	2015						0	0	
July	2015						0	0	
August	2015						0	0	
September	2015						0	0	
Total of FY 2015							0	0	

Note :

* No of Full Time Equivalent (FTE) Jobs in the Month = Total Job Days / Avg. Days in the Month(23.8)

** This data collection sheet is for Palestinian staff only , experts and foreign employee shall not be included.

Note: Numbers are rounded to the nearest integer number.

Total Generated Man-days per fiscal year

Project Name	DV	FY14											
		QRT 1 Oct. 1, 2013 to Dec. 31, 2013			QRT 2 Jan. 1, 2014 to Mar. 31, 2014			QRT 3 Apr. 1, 2014 to June. 30, 2014			QRT 4 Jul. 1, 2014 to Sep. 30, 2014		
		October	**November**	**December**	**January**	**February**	**March**	**April**	**May**	**June**	**July**	**August**	**September**
Total	MRNII	**0**	**0**	**73**	**504**	**1064**	**1795**	**2615**	**2153**	**2883**	**0**	**0**	**0**
PROJECT 01	NAB	0	0	45	458	946	1404	2056	1629	1956			
PROJECT 02	DSR	0	0	28	46	118	391	559	524	927			

Project Name	DV	FY14	(FTE) Jobs
Total	MRNII	**11087**	**466**
PROJECT 01	NAB	**8493**	**357**
PROJECT 02	DSR	**2594**	**109**

Total Femal Employment days per fiscal year

Project Name	DV	FY14											
		QRT 1 Oct. 1, 2013 to Dec. 31, 2013			QRT 2 Jan. 1, 2014 to Mar. 31, 2014			QRT 3 Apr. 1, 2014 to June. 30, 2014			QRT 4 Jul. 1, 2014 to Sep. 30, 2014		
		October	**November**	**December**	**January**	**February**	**March**	**April**	**May**	**June**	**July**	**August**	**September**
Total (Days)	MRN(II)	**0**	**0**	**0**	**22**	**28**	**34**	**30**	**31**	**32**	**0**	**0**	**0**
PROJECT 01 (Hrs)	NAB	0	0	0	162	221	256	175	173	172			
PROJECT 02 (Hrs)	DSR	0	0	0	11	0	17	68	71	83			

Total Man-days

Project Name	DV	FY14	Total FTE
Total (Days)	MRN(II)	**176**	**7**
PROJECT 01	NAB	**145**	**6**
PROJECT 02	DSR	**31**	**1**

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM
TASK ORDER NO: AID-294-TO-12-00014

Multiple Roads Project (North II)
Geo-MIS DATA COLLECTION SHEET

CONTRACTOR: APCO/ArCon

PERIOD FROM: June 01, 2014
PERIOD TO: June 30, 2014

DATE	Nablus- Beit Iba- Deir Sharaf Road					SubTotal	Deir Sharaf- Tulkarem Road					SubTotal
	Management	Engineers	Skilled labor	Unskilled labor	Other		Management	Engineers	Skilled labor	Unskilled labor	Other	
June 1, 2014	4	4	35	25		68	1	3	17	9		30
June 2, 2014	4	4	35	25		68	2	3	18	9		31
June 3, 2014	4	4	34	19		61	1	3	18	9		31
June 4, 2014	5	4	37	44		90	1	3	21	15		40
June 5, 2014	5	4	36	41		87	1	3	22	13		40
June 6, 2014	0	0	0	0		0	0	0	0	0		0
June 7, 2014	4	4	36	41		86	2	3	22	12		39
June 8, 2014	4	4	37	41		86	1	3	20	12		37
June 9, 2014	4	4	36	33		77	1	3	20	12		37
June 10, 2014	5	5	36	33		78	2	3	22	18		45
June 11, 2014	0	4	36	33		74	1	3	25	13		43
June 12, 2014	4	4	37	25		70	1	3	25	13		42
June 13, 2014	0	0	0	0		0	0	0	0	0		0
June 14, 2014	4	4	37	25		70	1	3	25	13		41
June 15, 2014	4	4	39	25		71	1	3	18	8		30
June 16, 2014	4	4	40	30		79	1	3	17	8		29
June 17, 2014	4	4	39	30		78	1	3	18	8		30
June 18, 2014	4	4	40	30		79	1	3	21	14		39
June 19, 2014	3	4	42	30		79	1	3	17	14		34
June 20, 2014	1	0	19	11		31	0	1	6	3		10
June 21, 2014	4	4	42	30		80	1	3	16	14		34
June 22, 2014	3	5	39	30		77	2	3	13	7		24
June 23, 2014	4	4	41	30		79	2	3	20	25		50
June 24, 2014	4	4	41	30		80	2	3	17	19		41
June 25, 2014	4	4	41	30		80	1	3	17	19		41
June 26, 2014	4	4	41	30		80	2	3	18	18		41
June 27, 2014	0	0	0	1		1	0	0	0	0		0
June 28, 2014	4	4	41	30		79	1	3	18	18		40
June 29, 2014	4	3	37	26		70	1	3	14	7		25
June 30, 2014	0	0	0	0		0	0	0	0	0		0
	0	0	0	0		0	0	0	0	0		0
Sub Total of June	98	103	973	782	0	**1956**	31	77	486	333	0	**927**

June, 2014	Total Job Days	No of Full Time Equivalent (FTE) Jobs
	2883	121

Daily Work Force /June 2014
Project 01: Nablus - Beit Iba- Deir Sharaf Road
Contract No. AID-294-I-00-12-00005

APCO/ArCon CONSTRUCTION AND SERVICES

Daily Work Force /June 2014

Date	Name of Contractor /Subcontractor	Worker/Classification (Hours)																									Man-days			
		Management								Engineer			Skilled								Unskilled									
		IQC Manager	Task Order Manager	Quality Control Manager	Assistant QCM	Public Relation Officer (F)	Technical Engineer	Surveyor	Safety & Environmental Compliance Officer	Assistant Safety Officer	Project Manager / Engineer	Office Engineer (F)	Site Engineer	Foreman	Surveyor	Surveyor Assistance	Equipment Operator	Skilled Labor	CWI	Carpenter	Drivers	Unskilled Labor	Flagmen	Security officer	Office Boy	Total Management	Total Engineers	Total Skilled	Total Unskilled
June 1, 2014	APCO/ArCon		7	7				9	6		12	7												9	9	4	4	35	25
	Subcontractor												15	40	20		139	80				150	33						
June 2, 2014	APCO/ArCon		6	6				9	7		12	8												9	9	4	4	35	25
	Subcontractor												15	40	20		140	80				150	33						
June 3, 2014	APCO/ArCon		7	6				9	7		11	7												9	9	4	4	34	19
	Subcontractor												15	40	20		134	80				100	33						
June 4, 2014	APCO/ArCon		7	6				9	7	10	11	7												9	9	5	4	37	44
	Subcontractor												16	46	22		139	85				298	36						
June 5, 2014	APCO/ArCon		7	6				9	7	10	11	7												9	9	5	4	36	41
	Subcontractor												16	43	22		139	85				279	33						
June 6, 2014	APCO/ArCon																									0	0	0	0
	Subcontractor																												
June 7, 2014	APCO/ArCon		6	6				9	7	6	10	7												9	9	4	4	36	41
	Subcontractor												16	43	22		139	85				279	33						
June 8, 2014	APCO/ArCon		7	7				9	6	6	11	7												9	9	4	4	37	41
	Subcontractor												16	43	22		142	85				279	33						
June 9, 2014	APCO/ArCon		6	6				9	6	6	9	6												9	9	4	4	36	33
	Subcontractor												16	43	22		139	85				213	33						
June 10, 2014	APCO/ArCon		8	7				9	7	6	12	8												9	9	5	5	36	33
	Subcontractor												16	43	22		139	85				213	33						
June 11, 2014	APCO/ArCon		6	6				9	7	7	12	7												9	9		4	36	33
	Subcontractor												16	43	22		139	85				213	33						
June 12, 2014	APCO/ArCon		7	7				9		6	11	7				9								9	9	4	4	37	25
	Subcontractor												15	40	20		150	80				160	22						
June 13, 2014	APCO/ArCon																									0	0	0	0
	Subcontractor																												
June 14, 2014	APCO/ArCon		7	6				9		6	9	5				9								9	9	4	4	37	25
	Subcontractor												15	40	20		150	80				160	22						
June 15, 2014	APCO/ArCon		7	6				9	6	6	9	5				9								9	9	4	4	39	25
	Subcontractor												15	40	20		159	80				160	22						
June 16, 2014	APCO/ArCon		6	7				9	6	6	9	7				9								9	9	4	4	40	30
	Subcontractor												16	43	22		169	80				202	22						

Date	Name of Contractor /Subcontractor	Worker/Classification (Hour)																									Man-days			
		Management								Engineers			Skilled								Unskilled									
		IQC Manager	Task Order Manager	Quality Control Manager	Assistant QCM	Public Relation Officer (F)	Technical Engineer	Surveyor	Safety & Environmental Compliance Officer	Assistant Safety Officer	Project Manager / Engineer	Office Engineer (F)	Site Engineer	Foreman	Surveyor	Surveyor Assistance	Equipment Operator	Skilled Labor	CWI	Carpenter	Drivers	Unskilled Labor	Flagmen	Security officer	Office Boy	Total Management	Total Engineers	Total Skilled	Total Unskilled
June 17, 2014	APCO/ArCon		7					9	7	7	11	7				9								9	9	4	4	39	30
	Subcontractor												16	43	22		160	80				202	22						
June 18, 2014	APCO/ArCon		6	7				8	7	7	11	6				8								9	9	4	4	40	30
	Subcontractor												16	43	22		169	80				202	22						
June 19, 2014	APCO/ArCon		7	6				8		6	11	7				8								9	9	3	4	42	30
	Subcontractor												16	43	22		179	80				202	22						
June 20, 2014	APCO/ArCon		4																							1	0	19	11
	Subcontractor													8	8		108	27				90							
June 21, 2014	APCO/ArCon		6	6				8	7	7	11	7				8								9	9	4	4	42	30
	Subcontractor												16	43	22		179	80				202	22						
June 22, 2014	APCO/ArCon		6	6					7	7	12	8												9	9	3	5	39	30
	Subcontractor												16	43	22		159	85				202	22						
June 23, 2014	APCO/ArCon		6	6				8	7	7	12	7												9	9	4	4	41	30
	Subcontractor												16	43	22		174	85				202	22						
June 24, 2014	APCO/ArCon		6	6				8	7	7	11	7												9	9	4	4	41	30
	Subcontractor												16	43	22		179	85				202	22						
June 25, 2014	APCO/ArCon		7	6				8	7	7	11	7				8								9	9	4	4	41	30
	Subcontractor												16	43	22		170	85				202	22						
June 26, 2014	APCO/ArCon		6	7				8	7	7	11	7				8								9	9	4	4	41	30
	Subcontractor												15	43	22		173	85				202	22						
June 27, 2014	APCO/ArCon																								9	0	0	0	1
	Subcontractor																												
June 28, 2014	APCO/ArCon		8	7				8		7	11	4				8								9	9	4	4	41	30
	Subcontractor												16	43	22		172	85				202	22						
June 29, 2014	APCO/ArCon		6	5				8	6	6	8	5				8								9	9	4	3	37	26
	Subcontractor												14	36	18		158	72				171	18						
June 30, 2014	APCO/ArCon		6	5				8	6	6	8	5				8								9	9				
	Subcontractor												14	36	18		173	72				171	18						
Total																										**98**	**103**	**973**	**782**

Daily Work Force /June 2014

Project 02: **Deir Sharaf - Tulkarem Road**

Contract No. AID-294-I-00-12-00005

APCO/ArCon CONSTRUCTION AND SERVICES

Daily Work Force /June 2014

Date	Name of Contractor /Subcontractor	Worker/Classification (Hours)																								Man-days			
		Management									Engineer			Skilled							Unskilled							
		IQC Manager	Task Order Manager	Quality Control Manager	Assistant QCM	Public Relation Officer (F)	Technical Engineer	Surveyor	Safety & Environmental Compliance Officer	Assistant Safety Officer	Project Manager / Engineer	Office Engineer (F)	Site Engineer	Foreman	Surveyor	Surveyor Assistance	Equipment Operator	Skilled Labor	Carpenter	Drivers	Unskilled Labor	Flagmen	security officer	Office boy	Total Management	Total Engineers	Total Skilled	Total Unskilled
June 1, 2014	APCO/ArCon		4	3					3		11	3													1	3	17	9
	Subcontractor										8		5	19	8	8	80	16			64	9						
June 2, 2014	APCO/ArCon		4	4					5		11	3													2	3	18	9
	Subcontractor										8		5	24	8	8	80	16			64	9						
June 3, 2014	APCO/ArCon		3	4					3		11	3													1	3	18	9
	Subcontractor										8		5	24	8	8	84	16			64	9						
June 4, 2014	APCO/ArCon		3	4					4		11	3													1	3	21	15
	Subcontractor										8		5	24	13	8	100	16			112	9						
June 5, 2014	APCO/ArCon		3	4					4		11	3													1	3	22	13
	Subcontractor										8		5	24	13	8	112	16			96	9						
June 6, 2014	APCO/ArCon																											
	Subcontractor																											
June 7, 2014	APCO/ArCon		4	4					4	4	11	3													2	3	22	12
	Subcontractor										8		5	24	13	8	112	16			88	9						
June 8, 2014	APCO/ArCon		4	3					4	4	11	3													1	3	20	12
	Subcontractor										8		5	24	13	8	97	16			88	9						
June 9, 2014	APCO/ArCon		3	3					4	4	11	3													1	3	20	12
	Subcontractor										8		5	24	13	8	97	16			88	9						
June 10, 2014	APCO/ArCon		4	4					4	4	11	3													2	3	22	18
	Subcontractor										8		5	24	13	8	110	16			136	9						
June 11, 2014	APCO/ArCon		4	4					3	3	11	3													1	3	25	13
	Subcontractor										8		5	24	13	8	73	80			96	9						
June 12, 2014	APCO/ArCon		2	3						3	11	3													1	3	25	13
	Subcontractor										8		5	24	13	8	68	80			96	9						
June 13, 2014	APCO/ArCon																											
	Subcontractor																											
June 14, 2014	APCO/ArCon		2	3						3	9	3													1	3	25	13
	Subcontractor										8		5	24	13	8	68	80			96	9						
June 15, 2014	APCO/ArCon		2	3					3	3	9	3													1	3	18	8
	Subcontractor										8		5	16	13	8	65	40			56	9						
June 16, 2014	APCO/ArCon		3	2					3	3	9	3													1	3	17	8
	Subcontractor										8		5	16	13	8	56	40			56	9						

Date	Name of Contractor /Subcontractor	Worker/Classification (Hour)																								Man-days			
		Management									Engineer			Skilled							Unskilled							
		IQC Manager	Task Order Manager	Quality Control Manager	Assistant QCM	Public Relation Officer (F)	Technical Engineer	Surveyor	Safety & Environmental Compliance Officer	Assistant Safety Officer	Project Manager / Engineer	Office Engineer (F)	Site Engineer	Foreman	Surveyor	Surveyor assistant	Equipment Operator	Skilled Labor	Carpenter	Super Intendent	Unskilled Labor	Flagmen	Security officer	Office boy	Total Management	Total Engineers	Total Skilled	Total Unskilled
June 17, 2014	APCO/ArCon		4						4	4	9	3													1	3	18	8
	Subcontractor										8		5	16	13	8	60	40			56	9						
June 18, 2014	APCO/ArCon		4	3					3	3	9	3													1	3	21	14
	Subcontractor										8		5	16	13	8	94	32			104	9						
June 19, 2014	APCO/ArCon		4	3						3	9	3													1	3	17	14
	Subcontractor										8		5	16	13	8	58	32			104	9						
June 20, 2014	APCO/ArCon		2																						0	1	6	3
	Subcontractor										8						48				16	8						
June 21, 2014	APCO/ArCon		4	3					3	4	9	3													1	3	16	14
	Subcontractor										8		5	16	13	8	52	32			104	9						
June 22, 2014	APCO/ArCon		4	4					4	4	9	3													2	3	13	7
	Subcontractor										8		5	16	13	8	58				48	9						
June 23, 2014	APCO/ArCon		4	4					4	4	11	4													2	3	20	25
	Subcontractor										8		5	16	13	8	78	40			192	9						
June 24, 2014	APCO/ArCon		4	4					4	4	11	4													2	3	17	19
	Subcontractor										8		5	16	13	8	56	40			144	9						
June 25, 2014	APCO/ArCon		3	4					4	4	11	4													1	3	17	19
	Subcontractor										8		5	16	13	8	56	40			144	9						
June 26, 2014	APCO/ArCon		4	3					5	4	11	4													2	3	18	18
	Subcontractor										8		5	24	13	8	54	40			136	9						
June 27, 2014	APCO/ArCon										9																	
	Subcontractor													8			20	32			160	16						
June 28, 2014	APCO/ArCon		4	3						4	11	4													1	3	18	18
	Subcontractor										8		5	24	13	8	54	40			136	9						
June 29, 2014	APCO/ArCon		2	3					2	2	8	3													1	3	14	7
	Subcontractor										8		5	16	8	8	38	40			48	9						
June 30, 2014	APCO/ArCon		2	3					2	4	8	3																
	Subcontractor										8		5	16	8	8	38	40			48	9						
	APCO/ArCon																								0	0	0	0
	Subcontractor																											
Total																									31	77	486	333
