USAID | WEST BANK/GAZA

MONTHLY PROGRESS REPORT

TASK ORDER NO. 13-00013

Deir Sharaf Main Pipeline Project (DST)

APCO/ArCon

February, 2015

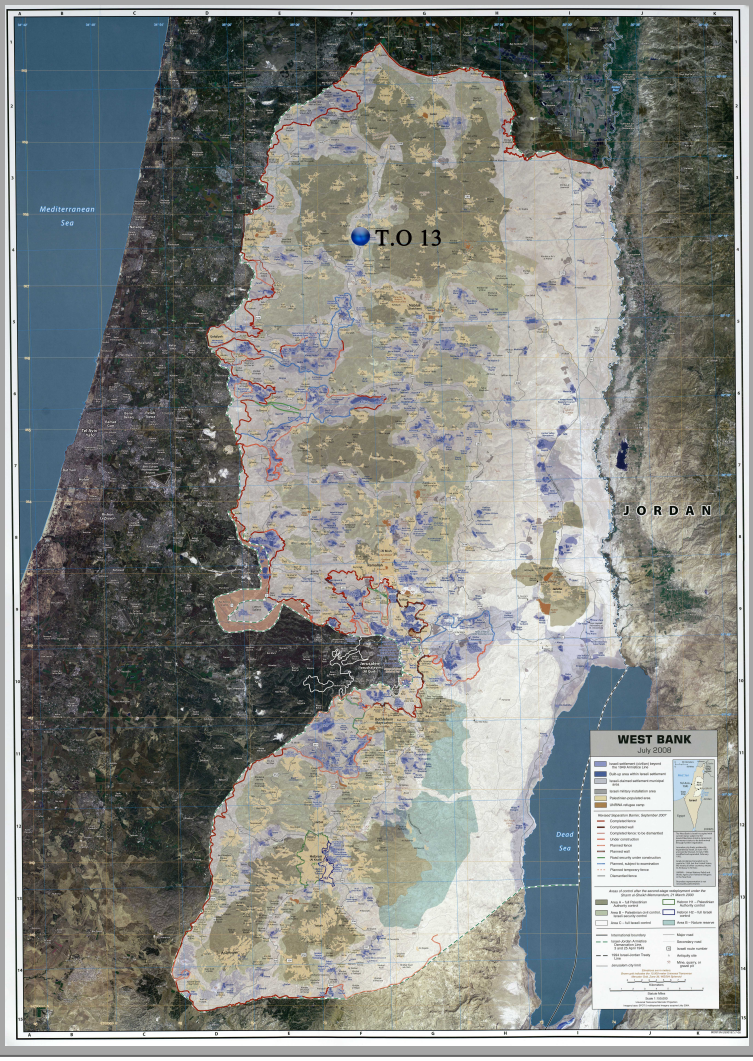

MONTHLY TASK ORDER PROGRESS REPORT

INFRASTRUCTURE NEEDS PROGRAM

Contract No. 294-I-00-12-00005
Task Order No. AID-294-TO-13-00013

From Feb. 01, 2015 to Feb. 28, 2015

DISCLAIMER

"This report is made possible by the support of the American People through the United States Agency for International Development (USAID). The contents of this report are the sole responsibility of APCO/ArCon and do not necessarily reflect the views of USAID or the United States Government."

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

USAID Contract No.:	294-I-00-12-00005
TO No.:	13-00013
Contractor:	APCO/ArCon Construction and Services
T.O Key Personnel:	Eng. Jomana Zaqzaq T.O.M Eng. Loay Kalbouneh- Q.C.M Eng. Mohammad Al Bazzour- S.E.O starting Nov. 29 Eng. Majdi Al Turabi- P.E Mr. Ata Mayyaleh - CWI

Monthly Progress Report number 15

TABLE OF CONTENTS

Task Order Overview……. 2-3
Safety …….. 3
Environmental Compliance……... 3
Traffic Control Measures……... 3
Community Outreach and Gender Consideration……. 3
Coordination ……. 4
Site Visitors…… 4
Material or Equipment Delivered to Site……... 4
Progress and Scheduling……..... 5
Activities during this Reporting Period……. 5
Planned Activities for Next Month…… 5
Indicator No. 01- Number of kilometers of transportation infrastructure constructed or repaired and water pipelines installed through USG assistance 5
Working / Non-working Days……... 6
Indicator No. 02- Generated Person-Days of Employment…... 6
Site Memos ……... 6
Procurement…… 6
Inspection Requests……... 7
Quality Control and Test Results……... 7-8
Submittals ……. 8
RFIs…… 8
Transmittals…… 8-10
Payments…… 10
Variation Order ……. 10
Variation Order Requests……... 11
Obstacles and Challenges…….. 11
Progress Photos……. 12-13
Annexes
A Materials- Equipment Receiving Log…… 14-16
B Detailed Time Schedule for the Project……. 17-37
One Month Look Ahead…… 38-40
Completed and in progress activities……. 41-50
C Progress S-Curve versus Actual…… 51-52
D Site Memos Log……. 53-55
E Inspection Requests Log…… 56-119
F Submittals Log for the Reporting Period……... 120-153
G RFI's Log for the Reporting Period……... 154-155
H Geo-MIS Data Collection Sheet……. 156-159
Generated Person-Days of Employment
I Risk Register log……. 160-162

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

TASK ORDER OVERVIEW:

Task Order Project Name	Deir Sharaf Main Pipeline (DST)
Project Description	This project is comprised of the installation of 3 water segments: 1) major segment A, new 300mm diameter main transmission pipeline approximately 13.7 kilometers in length from Deir Sharaf junction to Sanur well junction 2) minor segment B, 1.2km long 150mm diameter transmission line from Segment A to Al Fondaqumiya existing elevated reservoir 3) minor segment C, 0.1km long 150mm diameter transmission line from Segment A to Silat Ad Dahir existing reservoir. The pipeline will connect to an existing 300mm diameter pipeline at Deir Sharaf junction, and will pass by and supply water from metered turn-outs to Al Naqura, Sabastiya, Shavei Shamron, Burqa, Silat Ad Dahir, Al Fondaqumiya, and Bazzariya.
Statement of Work (SOW)	The SOW outlines trench excavation, side slope cuts, supply and installation of piping, valves, fittings and associated accessories required for complete installation and operation of transmission main. Related civil and mechanical works, concrete encasement, backfilling excavated areas, repaving, milling and reinstatement of the roadways, pipe pressure testing, pipe disinfection and cleaning, as well as other work needed to complete this project as specified in the bidding documents.
Project Location	Nablus – Jenin District (Area B and C)
Contract No.	294-I-00-12-00005
Task Order No.	AID-294-TO-13-00013
Employer	USAID
Contractor	APCO/ArCon
Engineer / CMC	Black and Veatch
Subcontractor Name	Brothers Company
Notice of Award (NOA)	Sep. 19, 2013
Notice To Proceed (NTP)	Dec. 03, 2013
Task Order Contract Value	$6,859,034
BOQ Items	$6,509,034
Day Work	$350,000
Modified BOQ Items	$6,843,844.57 (per VO#04)
Modified Day Work	$15,189.43 (per VO#04)
Start of Construction	March 26, 2014
Contractual period of Performance	450 Calendar Days
Contractual End Date	Feb. 25, 2015
Modified period of Performance	463 Calendar Days (VO#04)
Modified End Date	Mar. 10, 2015 (VO#04)
Estimated Completion Date	Mar. 10, 2015
Planned Percentage of Completion	100% (BL01)
Planned Percentage of Completion	100% (BL02)
Planned Percentage of Completion	100% (BL03)
Actual Percentage of Completion	98.9%
Total Float	0 Days

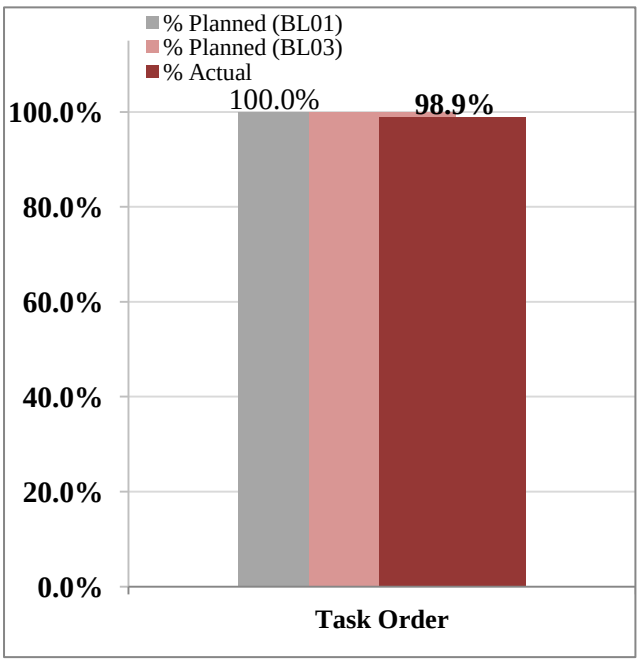

USAID | WEST BANK/GAZA
FROM THE AMERICAN PEOPLE

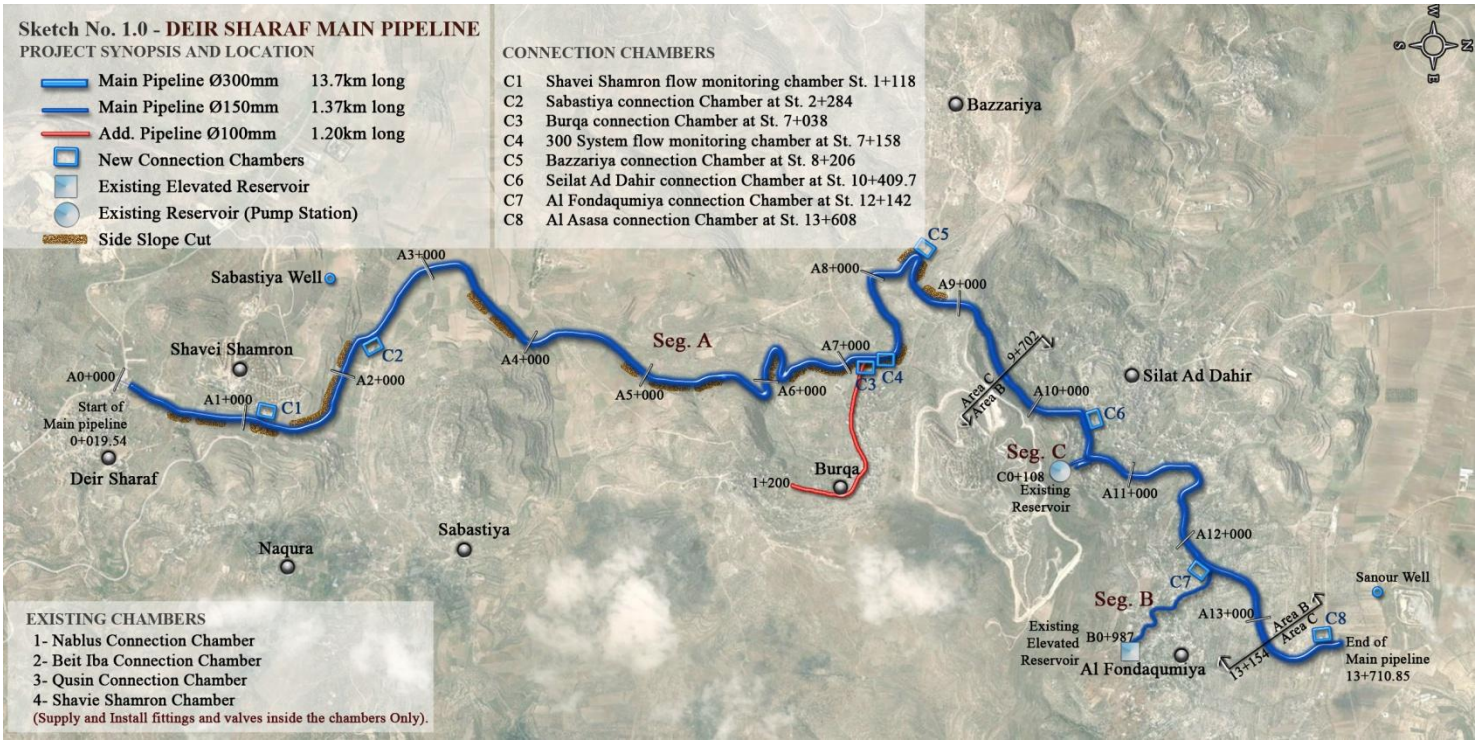

SAFETY:

During this reporting period, no accidents were reported; zero Notices of unsafe condition were issued.

ENVIRONMENTAL COMPLIANCE:

Environmental mitigation plan detailed methods that respond to special condition and construction activities that may impact on projects surroundings was prepared and submitted to CMC. Approval received on Jan. 09, 2014. Environmental mitigation plan measures were implemented during this reporting period (dust control, public and workers health and safety measures, traffic control and other measures). One Environmental Checklist (ECL) was received on February 18, 2015 for the month of January; requesting APCO to close all previous checklists and conduct general housekeeping for Burqa pipeline. During February APCO closed October and December 2014 ECLs. November checklist comments were performed and an inspection was submitted but the CMC returned it R.R and requested housekeeping activities to be executed properly. APCO will adhere to CMC recommendations and close officially pending November and January ECLs.

TRAFFIC CONTROL MEASURES:

Traffic control plan preparation was sourced out to specialty engineering firm. For road segments that are located in Area B, copies were stamped and approved by the Traffic Higher Council at the Palestinian Ministry of Transport and local councils. Stamped and approved copies were distributed to all entities that have jurisdiction over the work area. Traffic Control plan written approval for road segments in Area C was received on April 10th, 2014, copies of approval was submitted to CMC. Maatz written approval was received on April 10, 2014. Traffic Control measures were implemented on site prior starting pipeline installation.

COMMUNITY OUTREACH, PUBLIC INFORMATION AND GENDER CONSIDERATION:

Coordinations with local councils and utility owners were conducted to discuss work scope and solve obstacles and challenges when needed as detailed below:

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

COORDINATION:
During this reporting period, the following coordinations and meetings occurred :

Date	Attendees	Subject	Description
Feb. 02, 2015	PWA/ Aysar Rabaiya Black & Veatch/ Osama Al Khalili Black & Veatch/Sari Nasser Aldeen Black & Veatch/Anan Saleh Black & Veatch/ Haya Tafakji APCO/ArCon / Jomana Zaqzaq APCO/ArCon / Tahreer Mayyaleh Brothers/ Moain Salah	Bi-weekly meeting # 19	Review progress of work, discuss project issues and provide solutions where required.
Feb. 09, 2015	PWA/Aysar Rabiya PWA/Ahmad Sawaftah WBWD/Mohammad Abu Ayyash WBWD/Rasha Hamdan Black & Veatch/ Osama Al Khalili APCO/ArCon/ Jomana Zaqzaq	Coordination Meeting with PWA & WBWD	Discuss connections with Shavi Shamron inlet and outlet, Qusin and Beit Iba chambers.
Feb. 16, 2015	PWA/ Amin Wishahi Black & Veatch/ Osama Al Khalili Black & Veatch/Sari Nasser Aldeen Black & Veatch/Anan Saleh Black & Veatch/ Haya Tafakji APCO/ArCon / Jomana Zaqzaq APCO/ArCon / Tahreer Mayyaleh Brothers/ Moain Salah	Bi-weekly meeting # 20	Review progress of work, discuss project issues and provide solutions where required.
Feb. 18, 2015	USAID- Peter Riley, Mark Peters, and Sophie Taintor B&V- Dr. Daoud Al Qawasmeh, Osama Al Khalili, Sari Nasser Aldeen, Anan Saleh APCO/ArCon - Najim Saymuah, Ibrahim Al Hindi, Jomana Zaqzaq, and Tahreer Mayyaleh.	USAID progress meeting	Review progress of work.
Feb. 18, 2015	WBWD- Mohammad Abu Ayyash Mekorot representatives. B&V- Sari Naser Al Deen APCO ArCon- Loay Kalbouneh and Majdi Turabi	Coordination Meeting with Mekorot at DCL	Discuss APCO disinfection plan for installed pipeline.

SITE VISITORS:
During this reporting period, the following visits have occurred:

Date	Company	Location	Description
Task Order 13			
Feb. 09, 2015	PWA/ Aysar Rabiya Ahmad Sawaftah WBWD/Mohammad Abu Ayyash Rasha Hamdan	Office & Site	Joint site visit to discuss connections with Shavi Shamron inlet and outlet, Qusin and Beit Iba chambers.
Feb. 16, 2015	PWA/ Amin Weshahi	Office & Site	Follow-up work progress and attend Bi-weekly meeting.
Feb. 18, 2015	USAID/ Peter Riley Mark Peters Sophie Taintor	Office	Attend USAID progress meeting

MATERIAL OR EQUIPMENT DELIVERED TO SITE:

Please refer to **Annex A-** Equipment and Material receiving log.

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

PROGRESS and SCHEDULING:

% of Completion:

- Installation of steel pipe 300mm 100 %
- Installation of steel pipe 150mm 100 %
- Concrete Chambers 100%
- Concrete encasement 100%
- Asphalt reinstatement 300mm 100%
- Reinstatement concrete ditch 100%
- Asphalt reinstatement 150mm 100%
- Milling 100%
- Asphalt wearing 100%
- Mechanical works for chambers 85%

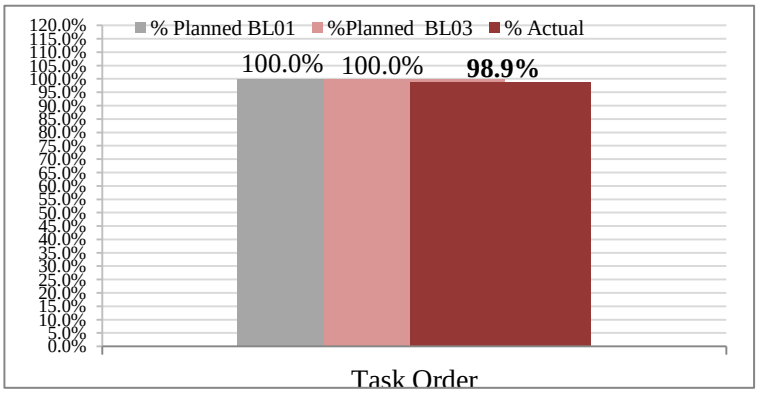

Overall percentages of completion are :

Completion%	T.O
Planned % (baseline 01)	100%
Planned % (baseline 02)	100%
Planned % (baseline 03)	100%
Actual %	98.9%
Total Float	**0Days**

Refer to **Appendix C** Progress s-curve planned versus Actual

ACTIVITIES DURING THIS REPORTING PERIOD:

- Continue survey works, submittals preparation for materials and shop drawings.
- Delivery of fittings and valves.
- Surface preparation for chambers.
- Finish the installation of fittings and valves inside the chambers.
- Complete the milling and the asphalting wearing course.
- Continue the internal finishing inside the chambers.
- Test the sewer line.
- Finish the installation of Burqa Pipeline.
- Continue the work in the acrylic paint.
- Install all the additional pre-cast manholes in Al Fandaqumia.
- Disinfection test.
- Connect to the existing lines.
- Complete the work in Scada System.
- Pre commissioning and commissioning.

PLANNED ACTIVITIES FOR NEXT MONTH:

- Continue in the Pre-commissioning and start the commissioning of the pipeline.
- Continue implementation of traffic control plan and detour.
- Finish the acrylic paint.
- Training.
- Handing Over.

INDICATOR NO. 01- Number of pipelines installed, road constructed or repaired through USG assistance:

Total Pipelines installed (100% Completed) during this reporting period	0.212 Km
Target value (Original Design)	15.05Km
Number of kilometers of pipelines installed through end of this reporting period.	**16.363** Km

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

WORKING / NON-WORKING DAYS

1	Total Period of Performance (Original)	450
2	Total Excusable delays/approved extensions	13
3	Modified Period of Performance	463
4	Modified Completion Date	March 10, 2015
5	No. of Working Days during this reporting Period	22
6	Accumulated Working Days	364
7	Total No. of non-working days (Holidays and weekends) during this reporting Period	4
8	Accumulated non-working days (Holidays and weekends)	72
9	No. of other non-working days during this month**	2
10	Accumulated other non-working days	17

** Worked stopped due to rainy weather

INDICATOR NO. 2: GENERATED PERSON-DAYS OF EMPLOYMENT:

All reported materials are up to date and meet the five quality data standards (Clause H.9).

This indicator count only local Palestinian staff whose time is charged to the USAID activity (the Contractor at the "prime" and "first tier" subcontractor level only). Neither expatriate person days of employment (i.e. those worked by American or other Third Country National staff) nor management nor administrative person days of employment (i.e. program level and other general and administrative staff shared among multiple task orders) are included. All reported person-days are calculated based on the approved Daily Joint Reports.

(Note: Totals are rounded to nearest decimal number - Person-day)

Task Order

- Target value= **13,920**
- Employment generated previously = 12,720.9 ≈ 12,721Person-Days (Audited up to Feb. 2014)
- Employment generated this month = 766.9 ≈ 767 Person-Days
- Total cumulative employment generated to-date= **13,487.8** ≈ **13,488** Person-Days
- Total Female employment generated previously= 625.6 ≈ 625 Person-Days
- Total Female employment generated this month= 43.8 ≈44 Person-Days
- Total cumulative Female employment generated to-date= **669.4** ≈ **669** Person-Days

Total Person Days	**No. of Full Time Equivalent (FTE) Jobs =** (Total Person Days / 23.8)
Generated previously = 12,721 Person-days	Generated previously = 534.5 ≈ 535
During this reporting period = 767 Person-days	During this reporting period = 32.2≈ 32
Total generated to-date = 13,488 Person-days	Total generated to-date = 566.7≈ 567

SITE MEMO:

Please see **Appendix D**- Site Memos log

PROCUREMENT:

Feb. 07, 2015	75mm Gate Valve-25 bar- 6 pieces.
Feb. 07, 2015	300mm Flow Control Valve-40 bar- 1 piece.
Feb. 07, 2015	150mm blind flange- 2 pieces.
Feb. 07, 2015	250 mm blind flange- 1 pieces.
Feb. 07, 2015	100 mm Gate Valve 20 bar- 2 pieces.

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

INSPECTION REQUEST:

Please see **Appendix E**- Inspection requests log

During this reporting period **113** inspection requests were issued and/or closed as follow:

No. of IRs	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review Not Required
113	102	11	88	0	13	1	0
%	90.3%	9.7%	77.9%	0.0%	11.5%	0.9%	0.0%

Non Compliance Report Log - NCR -

No NCRs were issued during this reporting period.

QUALITY CONTROL AND TEST RESULTS:

During this reporting period **18** Test reports were submitted and/or closed as the following:

No. of Tests	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review Not Required
18	12	6	7	0	0	0	5
%	66.7%	33.3%	38.9%	0.0%	0.0%	0.0%	27.8%

Tests Log summary table during up to this reporting period

Material Description	Test description	Number of tests	Pass	Fail	Notes (Action taken for failed tests)
Bedding material (Sumsum) & Single size	Gradation Test for Bedding Material (Sumsum)& Single Size Backfilling Material	1	1	0	
Somsom Aggregate (Bedding Material)	Somsom Aggregate Test	13	13	0	
Single Size Aggregate (Backfilling Material)	Gradation Test for Single Size Aggregate Material	12	12	0	
Concrete	7 Days concrete compressive strength	121	104	17	28 concrete strength results were submitted and passed.
	9 Days concrete compressive strength	2	2	0	
Concrete	28 Days concrete compressive strength	110	101	8	4 tests for trial batch were repeated by conducting site trial batch for foundation of GV through IR-13-00013-DST-237-A For two tests structural calculation were submitted to CMC for review and check. 45 days concrete strength was submitted for two failed submittals and passed. 1 Pending submittal.
	28 & 47 Days concrete compressive strength	2	2	0	
	Compaction core test	2	1	1	Structural calculation were submitted to CMC for review and check under SUB-13-00013-DST-138-A
	8 Days concrete compressive strength	1	1	0	

Material Description	Test description	Number of tests	Pass	Fail	Notes (Action taken for failed tests)
Base course	Base Course Comprehensive Test	15	14	0	1 Pending submittal.
	Field compaction test	15	12	1	Failed area was re-worked, re-compacted and re-tested. Test result was submitted for CMC review- TEST-13-00013-DST-026-A. 2 Pending submittals.
Fabricated elbows	Radiographic test by Morex company	11	10	1	According to Morex test results all elbows passed, the CMC requested one test report to be revised as they requested more quality assurance on tested elbows.
Asphalt	Marshall test	35	32	0	3 Pending Submittals
	Compaction degree test (core test)	7	5	2	Will be resubmitted including lab's recommendation and Jordanian specification limits.
	Asphalt Milled materials	1	1	0	
Steel	Steel reinforcement test	6	5	1	Re-submitted after removing Turkey source results as it will not be used.
Cast iron	Nondestructive loading test	1	1	0	
Metal	Manhole Rungs	1	1	0	
Selected material	Backfill material -sewer pipeline	1	1	0	
Paint	Acrylic paint (traffic paint)	1	1	0	

SUBMITTALS:

- **See Appendix F** Submittals log for this reporting period.

During this reporting period **9** submittals were submitted and/or closed as the following:

No. of SUB	No. Reviewed	No. Pending	% No Exception Noted	% Make Corrections Noted	% Amend-Resubmit	% Rejected-Resubmit	% Review Not required
9	7	2	2	5	0	0	0
%	77.8%	22.2%	22.2%	55.6%	0.0%	0.0%	0.0%

RFI:

- **See Appendix G** RFI's log for this reporting period.

TRANSMITTALS:

Outgoing / Incoming USAID Transmittals (USAID/ APCO/ArCon)

Date	Contractor Trans. No.	Sender/Recipient	Subject
February 02.2015	By Email	USAID/ APCO/ArCon	Contracting Officer's Monthly Meeting No. 14Contracting Officer's Monthly Meeting No. 14
February 02.2015	By Email	USAID/ APCO/ArCon	Revised agenda for the Monthly CO Meeting No. 14
February 03.2015	By Email	APCO/ArCon/ USAID	T.O 13- January 2015 - Monthly Report- Draft
February 06.2015	By Email	USAID/ APCO/ArCon	Rejection of Invoice number 11 Deir Sharaf Pipeline
February 07.2015	By Email	APCO/ArCon/ USAID	REMINDER: T.O 13- December 2014 - Monthly Report- COR Comments Modified
February 07.2015	By Email	APCO/ArCon/ USAID	REMINDER: T.O 13- Branding - Fittings and Valves

Date	Contractor Trans. No.	Sender/Recipient	Subject
February 07.2015	By Email	APCO/ArCon/ USAID	REMINDER: T.O 13- November 2014 - Monthly Report- Modified
February 11.2015	By Email	USAID/ APCO/ArCon	Re: Rejection of Invoice number 11 Deir Sharaf Pipeline
February 11.2015	By Email	USAID/ APCO/ArCon	Re: REMINDER: T.O 13- Branding - Fittings and Valves
February 12.2015	By Email	APCO/ArCon/ USAID	RE: Rejection of Invoice number 11 Deir Sharaf Pipeline
February 12.2015	By Email	USAID/ APCO/ArCon	Re: Rejection of Invoice number 11 Deir Sharaf Pipeline
February 16.2015	By Email	APCO/ArCon/ USAID	REMINDER: T.O 13- December 2014 - Monthly Report- COR Comments Modified
February 16.2015	By Email	APCO/ArCon/ USAID	RE: REMINDER: T.O 13- November 2014 - Monthly Report- Modified
February 16.2015	By Email	APCO/ArCon/ USAID	T.Os 13 and 15- Pending Monthly Reports
February 17.2015	By Email	USAID/ APCO/ArCon	Re: REMINDER: T.O 13- November 2014 - Monthly Report- Modified
February 17.2015	By Email	USAID/ APCO/ArCon	Re: T.O 13- December 2014 - Monthly Report- COR Comments Modified
February 17.2015	By Email	USAID/ APCO/ArCon	Re: T.O 13- January 2015 - Monthly Report- Draft
February 17.2015	By Email	APCO/ArCon/ USAID	RE: T.O 13- January 2015 - Monthly Report- COR Comments- Modified
February 19.2015	By Email	USAID/ APCO/ArCon	AID-294-TO-13-00013 / Variation Order No. 04
February 20.2015	By Email	APCO/ArCon/ USAID	RE: AID-294-TO-13-00013 / Variation Order No. 04
February 21.2015	By Email	USAID/ APCO/ArCon	Re: Preparation for inclement weather
February 22.2015	By Email	APCO/ArCon/ USAID	T.Os 13 and 15- Pending Monthly Reports
February 27.2015	By Email	APCO/ArCon/ USAID	TO#13 Deir Sharaf- Progress update and Task Order Manager leave.

Outgoing / Incoming Consultant Correspondences (B&V/ APCO/ArCon)

Date	Contractor Trans. No.	Sender/Recipient	Subject
February 02.2015	By Email	B&V/APCO/ArCon	TO 13-00013 DST: Weather Impact VO
February 02.2015	By Email	B&V/APCO/ArCon	RE: TO 13-00013 DST: RE: Radiographic Test
February 03.2015	By Email	B&V/APCO/ArCon	TO 13-00013DST : Draft MOM #19
February 03.2015	By Email	APCO/ArCon/ B&V	RE: TO 13-00013DST : Draft MOM #19
February 05.2015	By Email	APCO/ArCon/ B&V	All Task Orders- Geo-MIS Data - January 2015
February 07.2015	By Email	B&V/APCO/ArCon	FW: Rejection of Invoice number 11 Deir Sharaf Pipeline
February 07.2015	By Email	B&V/APCO/ArCon	TO 13-00013DST : Final MOM #19
February 07.2015	By Email	APCO/ArCon/ B&V	RE: Rejection of Invoice number 11 Deir Sharaf Pipeline
February 10.2015	By Email	APCO/ArCon/ B&V	Welding Schedule
February 10.2015	By Email	B&V/APCO/ArCon	RE: Welding Schedule
February 10.2015	By Email	APCO/ArCon/ B&V	FW: Coordination with Mekerot
February 10.2015	By Email	B&V/APCO/ArCon	RE: Coordination with Mekerot
February 12.2015	By Email	B&V/APCO/ArCon	TO 13-00013 DST : Progress Meeting No.20 – Agenda
February 12.2015	By Email	APCO/ArCon/ B&V	RE: TO 13-00013 DST: Variation Order #04 - Final for Signature
February 16.2015	By Email	B&V/APCO/ArCon	All Task Orders: As-Built Drawings Submittal delays
February 17.2015	By Email	APCO/ArCon/ B&V	Meeting with Mekerot
February 17.2015	By Email	B&V/APCO/ArCon	RE: Meeting with Mekerot
February 17.2015	By Email	B&V/APCO/ArCon	RE: Revised agenda for the Monthly CO Meeting No. 14
February 17.2015	By Email	B&V/APCO/ArCon	All TO: Expected rainy Weather and snow fall
February 18.2015	By Email	APCO/ArCon/ B&V	As-Built Drawings Submittal
February 19.2015	By Email	B&V/APCO/ArCon	RE: As-Built Drawings Submittal
February 19.2015	By Email	B&V/APCO/ArCon	TO 13-00013DST : Draft MOM #20
February 19.2015	By Email	APCO/ArCon/ B&V	Preparation for inclement weather

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

Date	Contractor Trans. No.	Sender/Recipient	Subject
February 21.2015	By Email	B&V/APCO/ArCon	RE: Preparation for inclement weather
February 23.2015	By Email	B&V/APCO/ArCon	TO 13-00013DST : Final MOM #20
February 24.2015	By Email	B&V/APCO/ArCon	All Task Orders: Core Tests Practice - Testing Labs
February 26.2015	By Email	APCO/ArCon/ B&V	FW: analytical report
February 26.2015	By Email	B&V/APCO/ArCon	RE: analytical report
February 26.2015	By Email	B&V/APCO/ArCon	TO 13-00013 DST : Progress Meeting No.21 - Agenda
February 26.2015	By Email	APCO/ArCon/ B&V	Training course
February 26.2015	By Email	APCO/ArCon/ B&V	Pre-commissioning of Deir Sharaf Main Pipeline
February 26.2015	By Email	B&V/APCO/ArCon	RE: analytical report
February 26.2015	By Email	B&V/APCO/ArCon	Fwd: FW: Burqa pipe line trench asphalt reinstatement
February 27.2015	By Email	B&V/APCO/ArCon	RE: Training course

PAYMENTS:

Voucher Number	Submitted Date	Amount	Retention Amount	Amount Received	Date Received
01	January 16, 2014	$ 247,963.20	$0.00	$ 247,963.20	January 31, 2014
02	April 21, 2014	$ 293,694.98	$0.00	$ 293,694.98	May 07, 2014
03	May 29, 2014	$ 438,876.10	$0.00	$ 438,876.10	June 16, 2014
04	June 19, 2014	$ 408,935.56	$0.00	$ 408,935.56	July 07, 2014
05	July 08, 2014	$ 362,241.24	$0.00	$ 362,241.24	July 23, 2014
06	August 03, 2014	$ 305,436.46	$0.00	$ 305,436.46	August 22, 2014
07	September 02, 2014	$ 525,953.60	$0.00	$ 525,953.60	September 23, 2014
08	October 08, 2014	$ 507,167.47	$0.00	$ 507,167.47	October 28, 2014
09	Nov. 19, 2014	$309,973.08	$0.00	$309,973.08	December 07, 2014
10	December 10, 2014	$553,258.80	$0.00	$553,258.80	December 19, 2014
11	February 23, 2015	$1,440,798.03	$0.00	Not received yet	
Total		**$5,394,298.52**	**$0.00**	**$3,953,500.49**	

APCO/ArCon total accrued expenditures $1,375,462.33

VARIATION ORDERS

VO No.	DESCRIPTION	VO Status (AP/PE/RE/RJ)			Date Sent to B&V	USAD Approval Date	Variation order Amount	Time Extension Days
		APCO	B&V	USAID				
01	Archeological excavation and New Definitive Quantities	AP	AP	AP	May 22, 2014	May 28, 2014	$(131,153.62)	00
02	Additional Works, Changes in Requirements & New Items, and Project New Definitive Quantities	AP	AP	AP	Dec. 18, 2014	Dec. 19, 2014	$263,369.21	00
03	New Item: Upgrading the Remote Flow Monitoring GBRS/GSM System and New Definitive Quantities	AP	AP	AP	Jan. 15, 2015	Jan. 26, 2015	$112,964.24	00
04	Installation of Cat Eyes, Project Pre-final Definitive Quantities and Time Extension.	AP	AP	AP	Feb. 12, 2015	Feb. 19, 2015	$89,630.74	13 Days

AP: Approved PE: Pending RE: Revise RJ: Rejected

USAID FROM THE AMERICAN PEOPLE | WEST BANK/GAZA

VARIATION ORDER REQUESTS:

VOR No.	DESCRIPTION	Date Sent to B&V	Variation order Amount	Time Ex.
01-A	Steel Mini guard Vs. New Jersey Concrete	May 26, 2014	$0.00 Approved.	00 Days
02-A	200mm future connection of Silat Al Daher water tank at Sta. 9+920 and Sta. 10+463 2. 250mm future connection of Sanour Cluster at Sta. 13+671.	June 24, 2014	$55,286.70 Revise-with supporting documents for prices	00 Days
03-A	New items :Change in Scope of work	Sep. 01, 2014	$252,581.54 Revise Resubmit	00 Days
03-B		Sep. 28, 2014	$242,572.36 Noted.	00 Days
03-C		Nov. 26, 2014	$138,118.41 Suspended by VOR#08-A / Price is noted.	00 Days
04-A	Trench excavation for pipeline	Sep. 23, 2014	$42,470 Revise Resubmit	00 Days
04-B		Nov. 09, 2014	$42,470 Closed under VO#02	00 Days
05-A	Additional works (new item prices)	Sep. 28, 2014	$482,000 Revise Resubmit	00 Days
05-B		Nov. 10, 2014	$477,000 Noted	00 Days
06-A	New Items: Construction of new 8" UPVC sewer pipeline and 1000 mm dia. precast concrete manhole and Time Extension	Nov. 06, 2014	$59,775 Revise Resubmit	07 Days
06-B	New Items: Construction of new 8" UPVC sewer pipeline and 1000 mm dia. precast concrete manhole and Time Extension	Dec. 03, 2014	$52,030 Closed under VO#02	07 Days
07-A	Additional Works (New items) – 1200 l.m of 4" water pipeline and gate valve.	Dec. 03, 2014	$265,214 Closed under VO#02	14 Days
08-A	New items: Change in Scope of work- new and combined chambers and new future connections	Dec. 04, 2014	To be evaluated Closed under VO#02	00 Days
09-A	New items and change in scope of work: a. Upgrading Remote Flow Monitoring GPRS/GSM system. b. Time impact analysis	Dec. 24, 2014	Option 01 $46,690 Option 02 $53,786 Closed under VO#03 and VO#04	6 weeks from start to finish
10-A	Time Extension: a. Upgrading Remote Flow Monitoring GPRS/GSM system. b. Time impact analysis	Jan. 29, 2015	$---- Closed under VO#04	14 Days
11-A	Time Extension due to rainy days and weather condition	Feb. 02, 2015	$---- Closed under VO#04	9 Days
12-A	New Items: A) Supply and install single sided cat eyes B) Time impact of new works	Feb. 08, 2015	$18,000 Closed under VO#04	10 Days

OBSTACLES AND CHALLENGES

No issues during this reporting period.

USAID | WEST BANK/GAZA

PROGRESS PHOTOS

Progress Photo- 4" pipes installation for Burqa water pipeline at Sta. 0+870.

Progress Photo- Asphalt core test for trench reinstatement second layer of Al Foundqumiya at Sta. 0+600.

Progress Photo- Asphalt wearing course for LHS shoulder of main road around Sta. 6+000.

Progress Photo- Installation for pre-cast manholes of 4" Burqa gate valve chamber at Sta. 1+150.

Progress Photo- Mechanical fittings installation for al As'asa connection chamber at Sta. 13+608.

Progress Photo- Mechanical fittings installation for Silat Al Daher connection at the end of segment C.

Progress Photo- Pressure reading at Sta. 0+019.5-Burqa.	Progress Photo- Wearing course asphalting for LHS shoulder of main road at Sta. 7+600.

A | Materials- Equipments Receiving Log

Project: Deir Sharaf Main Pipeline Project
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Equipment receiving log/February 2015

Date	Wheel excavator		Bob Cat		Welder machine		JCB		Truck 1971		Truck 1979		Truck Crane		WATER TANK 10M3		Pick up Car		Steel plate compactor		Steel Roller compactor		Asphalt Finisher		Milling Machine		Rubber Roller compactor		Asphalt Truck		Safety pick up car		Acrylic paint machine	
	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle	Quantity in use	Quantity idle
1-Feb			1		2		2		1		1		1				2																	
2-Feb			1		2		2		1		1		1				2																	
3-Feb			1		2		2		1		1		1				2																	
4-Feb			1		2		2		1		1		1		1		2																	
5-Feb			1		2		1		1		1		2				2																	
6-Feb																																		
7-Feb			1		3		1						1		1		6				1		1		1		1		5					
8-Feb			2		2		1		1		1		1		1		2				1		1				1		3					
9-Feb					2		1		1		1		1		1		2																	
10-Feb					2		1		1		1		1																					
11-Feb													1																					
12-Feb					1																													
13-Feb																																		
14-Feb																																		
15-Feb					2		1						1				2																	
16-Feb					2		1			1							2																	
17-Feb					1		1			1							1																	
18-Feb					1		1										2																	
19-Feb					1		1						1																					
20-Feb																																		
21-Feb																																		
22-Feb																	2																	
23-Feb			1		1		2		1								2				1													
24-Feb			1				1										2				2								2					
25-Feb			1		1		1										2				1								2					
26-Feb			1														2				2								2				1	
27-Feb																	1														1		1	
28-Feb																	1				1													

Project: Deir Sharaf Main Pipeline Project
USAID Contract No. 294-I-00-12-00005
Contractor: APCO/ArCon

Title: Materials Receiving Log/ February 2015

Date	Material Delivered to Site	Quantity
1-Feb	Bedding material	18 m^3
	Single size	36 m^3
	Base course	18 m^3
	Concrete B 350	1 m^3
2-Feb	Bedding material	36 m^3
	Single size	18 m^3
	Base course	36 m^3
3-Feb	Bedding material	18 m^3
	Single size	36 m^3
	Base course	36 m^3
4-Feb	Bedding material	18 m^3
5-Feb	……	……
6-Feb		
7-Feb	Asphalt ¾ ‘’	315 ton
	Pre-cast manholes	2 manhole
	3’’ GV-25 Bar	6
	12’’ FCV-40 Bar	1
	6’’ Blind flange	2
	10’’ Blind flange	1
	4’’ GV-20 Bar	2
8-Feb	Asphalt ¾ ‘’	175 ton
9-Feb	Low strength concrete	5 m^3
10-Feb	……	……
11-Feb	……	……
12-Feb	……	……
13-Feb		
14-Feb	……	……
15-Feb	……	……
16-Feb	……	……
17-Feb	……	……
18-Feb	Bedding material	18 m^3
19-Feb	……	……
20-Feb		
21-Feb	……	……
22-Feb	……	……
23-Feb	……	……
24-Feb	Asphalt ¾ ‘’	70 ton
25-Feb	Asphalt ¾ ‘’	70 ton
26-Feb	Asphalt ¾ ‘’	130 ton
27-Feb		
28-Feb	Asphalt ¾ ‘’	20 ton

B | Detailed Time Schedule for the Project

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
Deir- Sharaf Main Pipeline Project		463d		10d	03-Dec-13 A	10-Mar-15	0d	$6,843,844.57	$6,769,760.85
Milestones		463d		10d	03-Dec-13 A	10-Mar-15	0d	$0.00	$0.00
General milestone		463d		0d	03-Dec-13 A	10-Mar-15	0d	$0.00	$0.00
DST0000	Start Date NTP	0d	100%	0d	03-Dec-13 A			$0.00	$0.00
DST0010	Completion Project	0d	0%	0d		10-Mar-15	0d	$0.00	$0.00
Task Order Duration		450d		10d	03-Dec-13 A	10-Mar-15	0d	$0.00	$0.00
DST0020	Project Duration (Calendar Days)	450d	97.78%	10d	03-Dec-13 A	10-Mar-15	0d	$0.00	$0.00
DST0030	Project Duration (Working Days)	343d	97.7%	8d	03-Dec-13 A	10-Mar-15	0d	$0.00	$0.00
Pre Construction Milestones		254d		0d	08-Dec-13 A	25-Jan-15 A		$0.00	$0.00
DST0050	Start Preconstruction Submittal	0d	100%	0d	08-Dec-13 A			$0.00	$0.00
DST0060	Finish Preconstruction Submittal	0d	100%	0d		25-Jan-15 A		$0.00	$0.00
Mobilization Milestones		0d		0d	04-Dec-13 A	14-Jan-14 A		$0.00	$0.00
DST0070	Start Mobilization	0d	100%	0d	04-Dec-13 A			$0.00	$0.00
DST0080	Finish Mobilization	0d	100%	0d		14-Jan-14 A		$0.00	$0.00
Shop Drawing Milestones		296d		0d	02-Feb-14 A	27-Jan-15 A		$0.00	$0.00
DST0090	Start Shop Drawing Submittal	0d	100%	0d	02-Feb-14 A			$0.00	$0.00
DST0100	Finish Shop Drawing Submittal	0d	100%	0d		27-Jan-15 A		$0.00	$0.00
Material Milestones		334d		0d	25-Dec-13 A	03-Mar-15	6d	$0.00	$0.00
DST0105	Start Material Submittal	0d	100%	0d	25-Dec-13 A			$0.00	$0.00
DST0110	Finish Material submittal	0d	0%	0d		03-Mar-15	6d	$0.00	$0.00
Construction Milestones		256d		0d	26-Mar-14 A	02-Mar-15	3d	$0.00	$0.00
DST0115	Start Construction (Ground Breaking)	0d	100%	0d	26-Mar-14 A			$0.00	$0.00
DST0120	Finish Construction	0d	0%	0d	02-Mar-15		3d	$0.00	$0.00
Pre Construction Phase		426d		0d	03-Dec-13 A	25-Jan-15 A		$247,963.20	$247,963.20
Pre Construction Submittals		299d		0d	08-Dec-13 A	25-Jan-15 A		$0.00	$0.00
DST0170	Bank Guarantee Certificates	10d	100%	0d	08-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0160	Scheduling Qualification Submittals	10d	100%	0d	08-Dec-13 A	22-Dec-13 A		$0.00	$0.00
DST0180	Submittals Schedule	10d	100%	0d	19-Dec-13 A	04-Feb-14 A		$0.00	$0.00

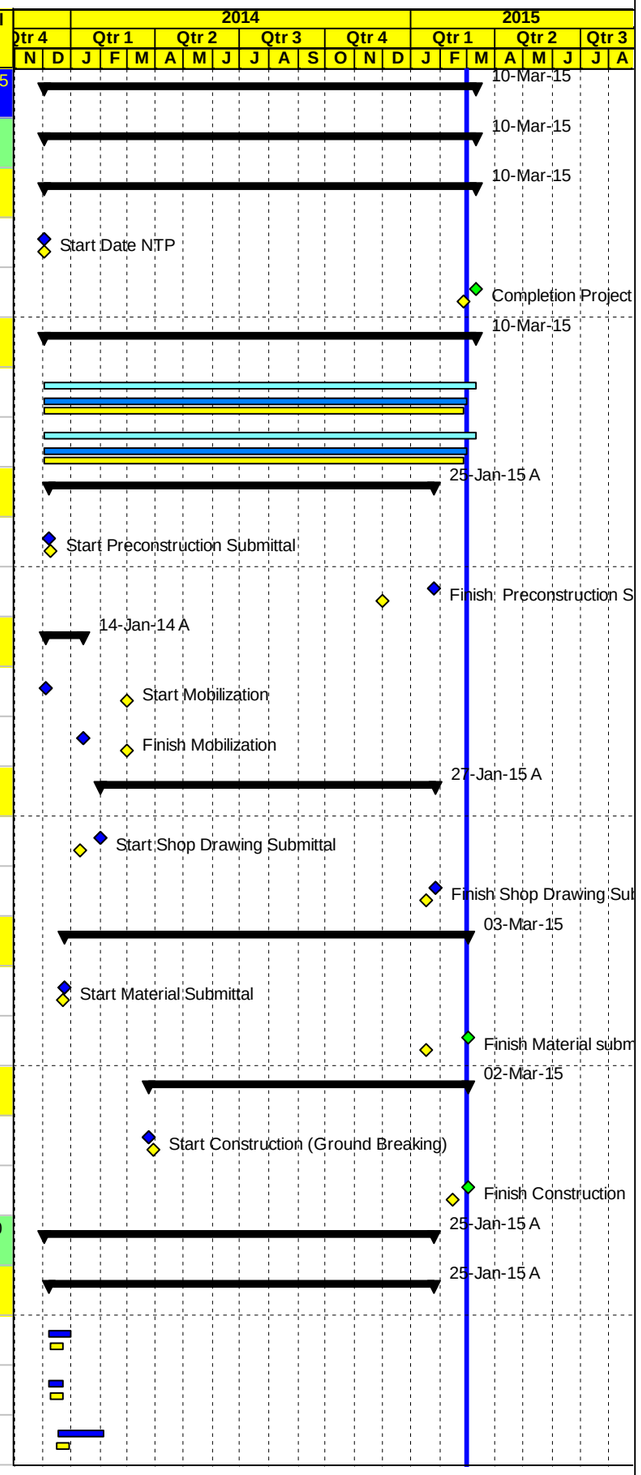

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST0240	Subcontractors' profile	10d	100%	0d	22-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0270	60-Day Plan of Operation	10d	100%	0d	22-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0280	Project Overview Bar Chart	10d	100%	0d	22-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0200	Testing Lab	10d	100%	0d	23-Dec-13 A	02-Jan-14 A		$0.00	$0.00
DST0173	Field Offices Location & Layout	10d	100%	0d	23-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0399	Safety Trench plan	10d	100%	0d	25-Dec-13 A	20-Jan-14 A		$0.00	$0.00
DST0210	Key Personnel Plan	10d	100%	0d	25-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0290	QCP-Quality Control Program	10d	100%	0d	25-Dec-13 A	13-Jan-14 A		$0.00	$0.00
DST0300	Safety Plan	10d	100%	0d	25-Dec-13 A	20-Jan-14 A		$0.00	$0.00
DST0370	Material Staging ,Storage and dumping Areas Plan	10d	100%	0d	25-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0310	USAID Branding Plan	10d	100%	0d	25-Dec-13 A	09-Jan-14 A		$0.00	$0.00
DST0230	Insurances	10d	100%	0d	25-Dec-13 A	07-Jan-14 A		$0.00	$0.00
DST0177	Field Offices Furniture & Equipment Plan	10d	100%	0d	25-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0340	Method Statement including asphalt disposal,pipeline install,formworks,curing,storm sys.,&R. mark	10d	100%	0d	29-Dec-13 A	23-Jan-14 A		$0.00	$0.00
DST0304	Environmental Mitigation Plan	10d	100%	0d	29-Dec-13 A	09-Jan-14 A		$0.00	$0.00
DST0306	CPM-Construction Schedule and S-Curve	10d	100%	0d	29-Dec-13 A	24-Feb-14 A		$0.00	$0.00
DST0350	Coordination with local Authorities Plan including list of permits & and licenses	10d	100%	0d	30-Dec-13 A	09-Jan-14 A		$0.00	$0.00
DST0204	Temporary and Permanent Project Sign Plan	10d	100%	0d	30-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0250	Existing Survey Plan	10d	100%	0d	02-Jan-14 A	13-Jan-14 A		$0.00	$0.00
DST0320	Dilapidation Survey	10d	100%	0d	02-Jan-14 A	12-Jan-14 A		$0.00	$0.00
DST0390	Traffic Control Plan Phase I	10d	100%	0d	05-Jan-14 A	16-Jan-14 A		$0.00	$0.00
DST0415	Welders qualification	10d	100%	0d	20-Jan-14 A	26-Jan-14 A		$0.00	$0.00
DST0393	Welding procedure	10d	100%	0d	23-Jan-14 A	20-Mar-14 A		$0.00	$0.00
DST0330	Risk Management Plan	10d	100%	0d	26-Jan-14 A	04-Feb-14 A		$0.00	$0.00
DST0410	Third party testing lab -Arc-Eyes	10d	100%	0d	26-Jan-14 A	30-Jan-14 A		$0.00	$0.00
DST0396	Public relation plan	10d	100%	0d	27-Jan-14 A	30-Jan-14 A		$0.00	$0.00
DST0415-new	Pipeline trenching method statement	10d	100%	0d	13-Feb-14 A	02-Apr-14 A		$0.00	$0.00
DST0416-new	Pipe Installation method statement	10d	100%	0d	16-Feb-14 A	02-Mar-14 A		$0.00	$0.00

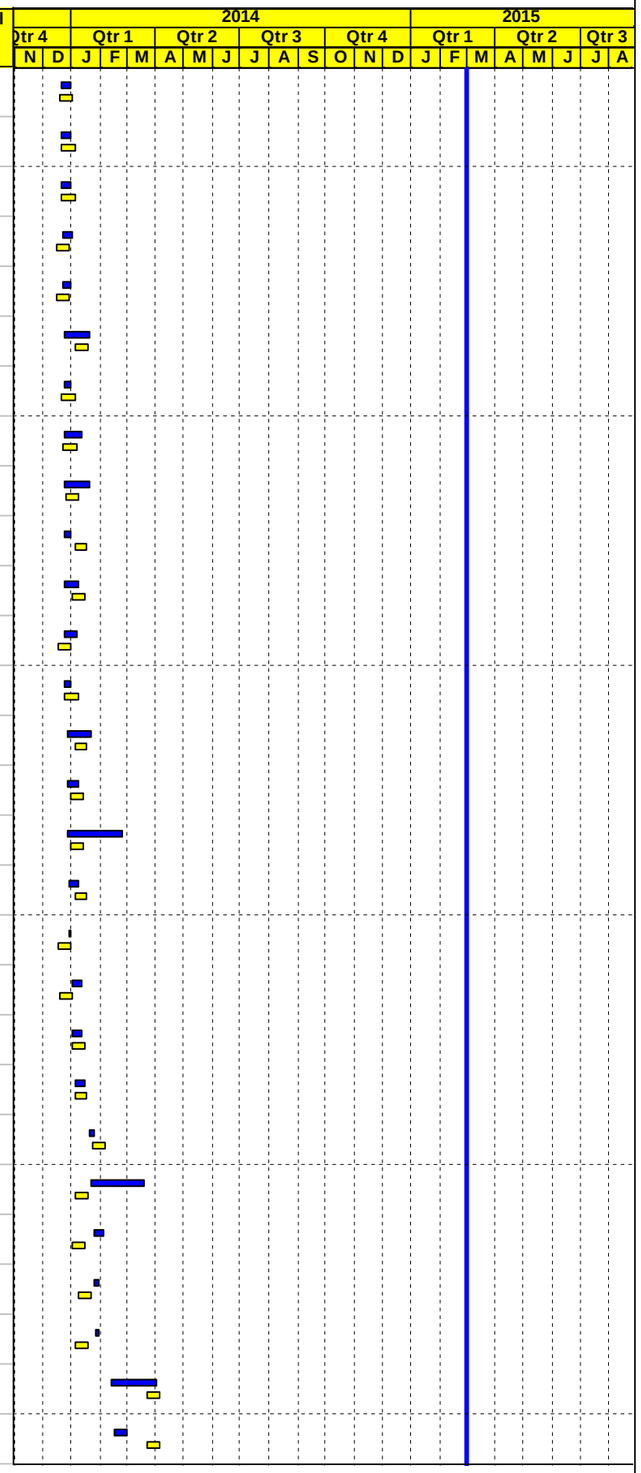

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST0418-new	Method Statement for Filling & Repair The Conical Tie Rods Holes In The Concrete	10d	100%	0d	24-Feb-14 A	13-Mar-14 A		$0.00	$0.00
DST0419-new	Radiographic Testing Safety Plan	10d	100%	0d	04-Mar-14 A	02-Apr-14 A		$0.00	$0.00
DST0420-new	8-12 inch Procedure Qualification Record (PQR)	10d	100%	0d	05-Mar-14 A	20-Mar-14 A		$0.00	$0.00
DST0422-new	Radiographic Testing (RT) Method Statement	10d	100%	0d	16-Mar-14 A	20-Mar-14 A		$0.00	$0.00
DST0423-new	Approved Temporary Traffic Plan by DCL (Area C)	10d	100%	0d	02-Apr-14 A	15-Apr-14 A		$0.00	$0.00
DST0425-new	Work Zone Traffic Control and Operations at Night (Specific Night Work Safety Plan)	10d	100%	0d	13-Jul-14 A	03-Aug-14 A		$0.00	$0.00
DST0426-new	Cleaning, washing, hydraulic test and disinfection plan	10d	100%	0d	12-Nov-14 A	08-Dec-14 A		$0.00	$0.00
DST0427-new	Second Source for Third Party Testing	10d	100%	0d	21-Jan-15 A	25-Jan-15 A		$0.00	$0.00
Mobilization		85d		0d	04-Dec-13 A	03-Feb-14 A		$247,963.20	$247,963.20
DST0420	Mobilization Total Cost (4.0%)	20d	100%	0d	04-Dec-13 A	16-Jan-14 A		$247,963.20	$247,963.20
DST0460	Start Preparation Construction Submittals (Survey plan , Shop Drawings & Materials)	8d	100%	0d	21-Dec-13 A	31-Dec-13 A		$0.00	$0.00
DST0480	Supply and install Office IT Equipments & Applience	2d	100%	0d	07-Jan-14 A	03-Feb-14 A		$0.00	$0.00
DST0470	Supply and install Office Furniture's and Supplies	2d	100%	0d	07-Jan-14 A	03-Feb-14 A		$0.00	$0.00
DST0430	Site Hand Over	1d	100%	0d	08-Jan-14 A	08-Jan-14 A		$0.00	$0.00
DST0440	Checking With CMC Existing-Bench Marks, Survey Control Points	2d	100%	0d	12-Jan-14 A	12-Jan-14 A		$0.00	$0.00
DST0490	Install Temporary Project Sign	1d	100%	0d	14-Jan-14 A	16-Jan-14 A		$0.00	$0.00
Conformed Drawings and Coordination		40d		0d	03-Dec-13 A	15-May-14 A		$0.00	$0.00
DST0495	Coordination with Israeli authorities for approval and permit area C	40d	100%	0d	03-Dec-13 A	15-May-14 A		$0.00	$0.00
DST0492	Final for Construction Drawing (Conformed)	1d	100%	0d	03-Dec-13 A	03-Dec-13 A		$0.00	$0.00
Construction Phase		441d		8d	25-Dec-13 A	08-Mar-15	2d	$6,533,890.57	$6,521,797.65
Construction Submittals		330d		2d	25-Dec-13 A	03-Mar-15	6d	$0.00	$0.00
Shop Drawing Submittals		296d		0d	02-Feb-14 A	27-Jan-15 A		$0.00	$0.00
Waterline		295d		0d	02-Feb-14 A	12-Jan-15 A		$0.00	$0.00
DST0590	Waterline 300 mm Main pipeline from Sta. A10+400 to Sta. A12+120 At RHS	21d	100%	0d	02-Feb-14 A	09-Apr-14 A		$0.00	$0.00
DST0605	Waterline 300 mm Main pipeline from Sta. A10+400 to Sta. A9+700 At RHS	21d	100%	0d	23-Mar-14 A	09-Apr-14 A		$0.00	$0.00
DST0600	Waterline 300 mm Main pipeline from Sta. A12+120 to Sta. A13+580 At LHS	21d	100%	0d	08-Apr-14 A	30-Apr-14 A		$0.00	$0.00
DST0595	Waterline 150 mm Main pipeline at Segment B	21d	100%	0d	28-Apr-14 A	21-May-14 A		$0.00	$0.00
DST0650-new	Waterline 300 mm Main pipeline From St.13+560 To St.13+725	21d	100%	0d	06-May-14 A	21-May-14 A		$0.00	$0.00

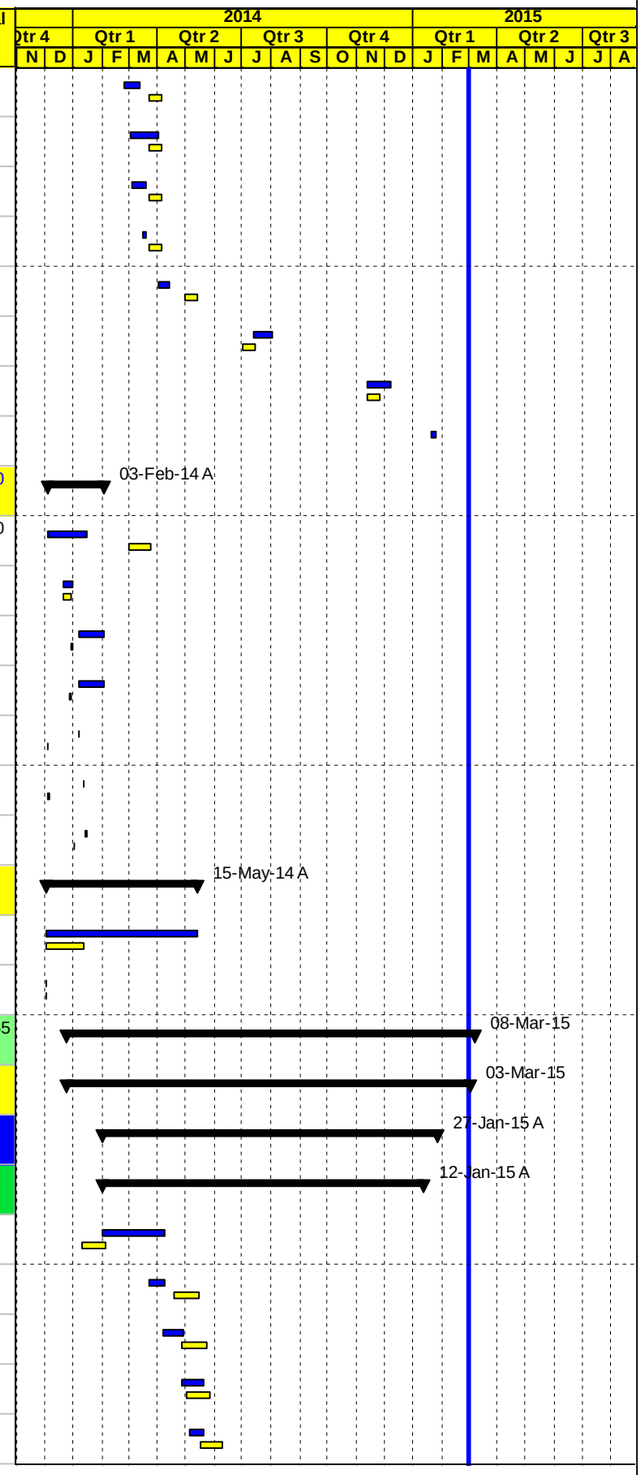

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST0655-new	Waterline 300 mm Main pipeline From St.5+000 To St.7+010	21d	100%	0d	12-May-14 A	27-May-14 A		$0.00	$0.00
DST0615	Waterline 300 mm Main pipeline from Sta. A2+900 to Sta. A5+000 At RHS	21d	100%	0d	01-Jun-14 A	12-Jun-14 A		$0.00	$0.00
DST0625	Waterline 300 mm Main pipeline from Sta. A1+100 To St. A2+900 At RHS	21d	100%	0d	10-Jun-14 A	01-Jul-14 A		$0.00	$0.00
DST0610	Waterline 300 mm Main pipeline from Sta. A7+020 to Sta. A9+700 At LHS	21d	100%	0d	14-Jul-14 A	04-Aug-14 A		$0.00	$0.00
DST0620	Waterline 300 mm Main pipeline from Sta. 0+034 to Sta. 1+250	21d	100%	0d	02-Sep-14 A	15-Sep-14 A		$0.00	$0.00
DST0660-new	Waterline 100 mm Main pipeline Burqa From St. 0+000 To St. 1+135	21d	100%	0d	30-Dec-14 A	12-Jan-15 A		$0.00	$0.00
Sewer Line		21d		0d	28-Dec-14 A	06-Jan-15 A		$0.00	$0.00
DST0665-new	8" Sewer Line From Sta. 0+000 to Sta. 0+260	21d	100%	0d	28-Dec-14 A	06-Jan-15 A		$0.00	$0.00
Rock Cutting in Slope		21d		0d	15-Jun-14 A	03-Jul-14 A		$0.00	$0.00
DST0585	Cut Slope Seg. A From Sta (1+430-1+825, 2+020-2+115,4+920-4+980,5+060-5+100,5+750-5+820,6+560-6+620, 6+650-7+740)	21d	100%	0d	15-Jun-14 A	03-Jul-14 A		$0.00	$0.00
Connection and Valves Chambers		208d		0d	27-Mar-14 A	27-Jan-15 A		$0.00	$0.00
DST0630	Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 9+700 to 12+120	21d	100%	0d	27-Mar-14 A	09-Jun-14 A		$0.00	$0.00
DST0680-new	Structural & Mechanical detail for valve chambers- From Sta. 5+000 to Sta. 7+000 & from Sta.12+000 to 13+700	21d	100%	0d	08-Jun-14 A	12-Jun-14 A		$0.00	$0.00
DST0670	Al Asasa connection chamber at Sta. A13+600 & connect to exist. Pipes	21d	100%	0d	15-Jun-14 A	06-Aug-14 A		$0.00	$0.00
DST0640	Sielat AL Dahir connection chamber at Sta. A10+420	21d	100%	0d	15-Jun-14 A	06-Aug-14 A		$0.00	$0.00
DST0645-new	Structural & Mechanical Detail for Valve Chambers for (Water Pipeline) From Sta. 2+000 to 5+000	21d	100%	0d	22-Jul-14 A	24-Nov-14 A		$0.00	$0.00
DST0646-new	Structural & Mechanical Detail for Valve Chambers for (Water Pipeline) for Seg. B	21d	100%	0d	22-Jul-14 A	12-Aug-14 A		$0.00	$0.00
DST0647-new	Structural & Mechanical Detail for Valve Chambers for (Water Pipeline) From 1+000 to 2+900 & From Sta. 7+000 to 9+000	21d	100%	0d	03-Aug-14 A	21-Aug-14 A		$0.00	$0.00
DST0710	Sabastia Connection Chamber at Sta. A2+280 & Connect to Exist.WSP	21d	100%	0d	04-Aug-14 A	28-Aug-14 A		$0.00	$0.00
DST0650	Al Fondaqumiya Connection Chamber at Sta. A12+120	21d	100%	0d	04-Aug-14 A	28-Aug-14 A		$0.00	$0.00
DST0690	Burqa Connection Chamber at Sta. A7+032 & Connect to Exist. Pipeline	21d	100%	0d	12-Aug-14 A	10-Sep-14 A		$0.00	$0.00
DST0700	Structural & Mechanical detail for Flow Water Meter connection chamber @ Sta.7+180	21d	100%	0d	12-Aug-14 A	15-Sep-14 A		$0.00	$0.00
DST0680	Bazzariya Connection Chamber at Sta. A8+230 & Connect to Exist.WSP	21d	100%	0d	12-Aug-14 A	10-Sep-14 A		$0.00	$0.00
DST0720	Structural & Mechanical Detail for Water Meter Connection Chamber at Sta. 1+156	21d	100%	0d	08-Sep-14 A	28-Oct-14 A		$0.00	$0.00
DST0740-new	Structural & Mechanical Detail for Flow Control Connection Chamber at Sta. 1+170	21d	100%	0d	09-Sep-14 A	02-Oct-14 A		$0.00	$0.00
DST0750-new	Structural & Mechanical Detail for Valve Chambers For (Water Pipeline) From Sta. 0+034 To 1+250	21d	100%	0d	14-Sep-14 A	02-Oct-14 A		$0.00	$0.00
DST0778-new	Mechanical Detail For 250 mm Washout Sta. 0+90 & AV/AR Chamber Sta. 0+365 in TO #14	21d	100%	0d	14-Sep-14 A	25-Sep-14 A		$0.00	$0.00
DST0770	Mechanical Detail for Shavi Shomron Main System Flow Monitoring Chamber at Sta. A 1+870 (TO.14)	21d	100%	0d	16-Sep-14 A	25-Sep-14 A		$0.00	$0.00

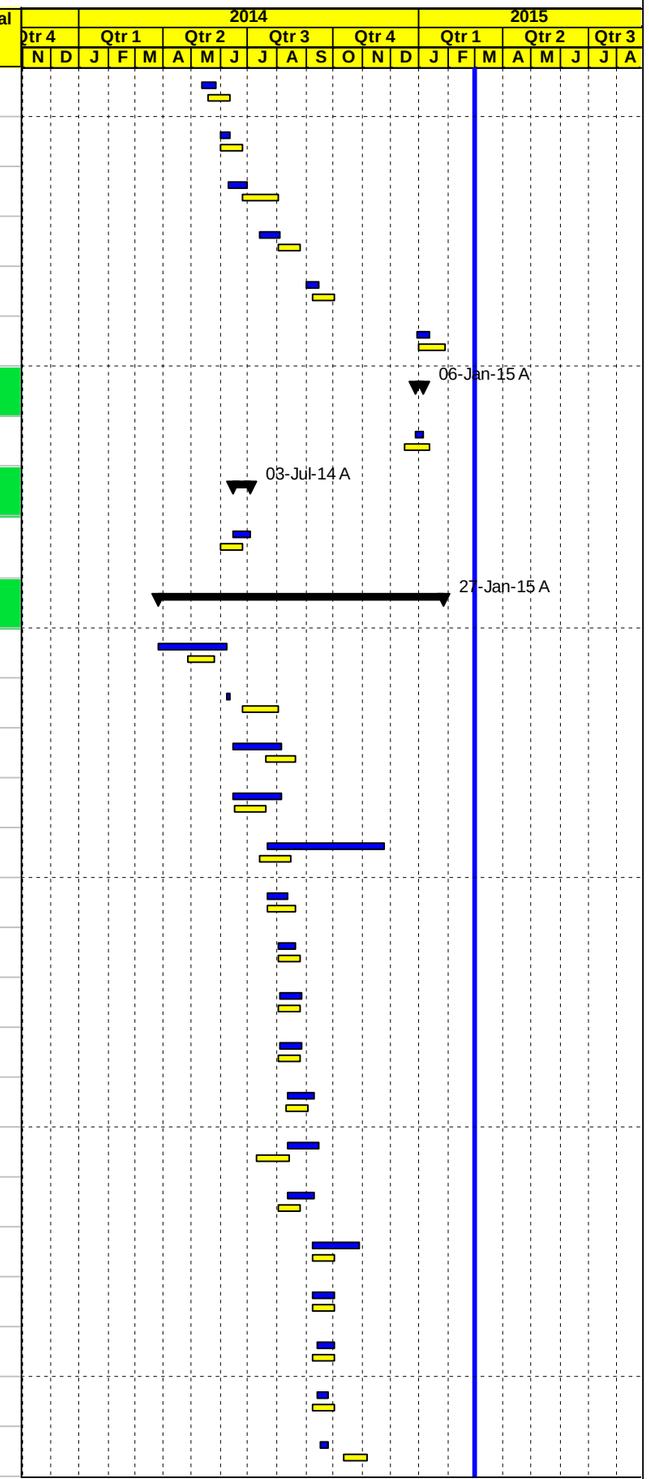

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST0760	Beit Iba Connection Chamber @ St. Seg. B 0+342	21d	100%	0d	18-Sep-14 A	02-Oct-14 A		$0.00	$0.00
DST0768	Nablus Connection Chamber @ St. B 0+040	21d	100%	0d	18-Sep-14 A	02-Oct-14 A		$0.00	$0.00
DST0780-new	Mechanical Detail For Combined Butterfly & Av/Ar Chamber Sta. 0+810 Beit Iba Road	21d	100%	0d	21-Sep-14 A	05-Nov-14 A		$0.00	$0.00
DST0764	Qusin Flow Monitoring Chamber @St. 0+184	21d	100%	0d	27-Oct-14 A	01-Dec-14 A		$0.00	$0.00
DST0785-new	Structural & Mechanical Detail for New Location of Selit Aldaher Connection	21d	100%	0d	04-Nov-14 A	18-Nov-14 A		$0.00	$0.00
DST0786-new	Mechanical Detail for 250 Mm Washout Sta. 0+038- in TO# 14	21d	100%	0d	23-Nov-14 A	30-Nov-14 A		$0.00	$0.00
DST0788-new	6"&4" G.V Al-Foundqumieh @0+990, 2*2" G.V Al-Foundqumieh @0+410 & 0+430 &2*4" G.V Bourqa @1+120 & 1+130	21d	100%	0d	18-Jan-15 A	27-Jan-15 A		$0.00	$0.00
Material Submittals including Manufacturers Qualifications , Shop Test, Product Data		330d		2d	25-Dec-13 A	03-Mar-15	6d	$0.00	$0.00
Material Submittals Pipelines including Hydraulic calculation and wiring diagrams, labeling sched		330d		2d	25-Dec-13 A	03-Mar-15	6d	$0.00	$0.00
DST0780	Steel pipeline 300 mm	21d	100%	0d	25-Dec-13 A	05-Jan-14 A		$0.00	$0.00
DST0790	Steel pipeline 150 mm	21d	100%	0d	25-Dec-13 A	05-Jan-14 A		$0.00	$0.00
DST0792	Pipe Fittings	21d	100%	0d	16-Jan-14 A	09-Feb-14 A		$0.00	$0.00
DST0797	Gate Valves PN 40	21d	100%	0d	20-Jan-14 A	26-Jan-14 A		$0.00	$0.00
DST0895	Dismantling joints	21d	100%	0d	20-Jan-14 A	28-Jan-14 A		$0.00	$0.00
DST0798	Butterfly valves	21d	100%	0d	20-Jan-14 A	26-Jan-14 A		$0.00	$0.00
DST0898	Identification Tape for water pipeline	21d	100%	0d	21-Jan-14 A	22-Jan-14 A		$0.00	$0.00
DST0810	Ball valves	21d	100%	0d	26-Jan-14 A	30-Jan-14 A		$0.00	$0.00
DST0865	Elecometer 266 Holiday detector	21d	100%	0d	26-Jan-14 A	30-Jan-14 A		$0.00	$0.00
DST0935	Heavy duty frame and cover	21d	100%	0d	27-Jan-14 A	30-Jan-14 A		$0.00	$0.00
DST0870	Combination air release valves.	21d	100%	0d	27-Jan-14 A	02-Feb-14 A		$0.00	$0.00
DST0910	Strainers.	21d	100%	0d	27-Jan-14 A	30-Jan-14 A		$0.00	$0.00
DST0874	Air Release Valves.	21d	100%	0d	27-Jan-14 A	30-Jan-14 A		$0.00	$0.00
DST0930	Pressure relief valves.	21d	100%	0d	30-Jan-14 A	04-Feb-14 A		$0.00	$0.00
DST0820	Pipe Flanges	21d	100%	0d	30-Jan-14 A	04-Feb-14 A		$0.00	$0.00
DST0975	UPVC pipe for drainage	21d	100%	0d	03-Feb-14 A	04-Feb-14 A		$0.00	$0.00
DST0970-new	Pressure Reducing Valves	21d	100%	0d	10-Feb-14 A	02-Apr-14 A		$0.00	$0.00
DST0937	Repair Pipe Cement Lining and Coating	21d	100%	0d	10-Feb-14 A	16-Apr-14 A		$0.00	$0.00
DST0970	Flow Control Valves	21d	100%	0d	10-Feb-14 A	20-Feb-14 A		$0.00	$0.00

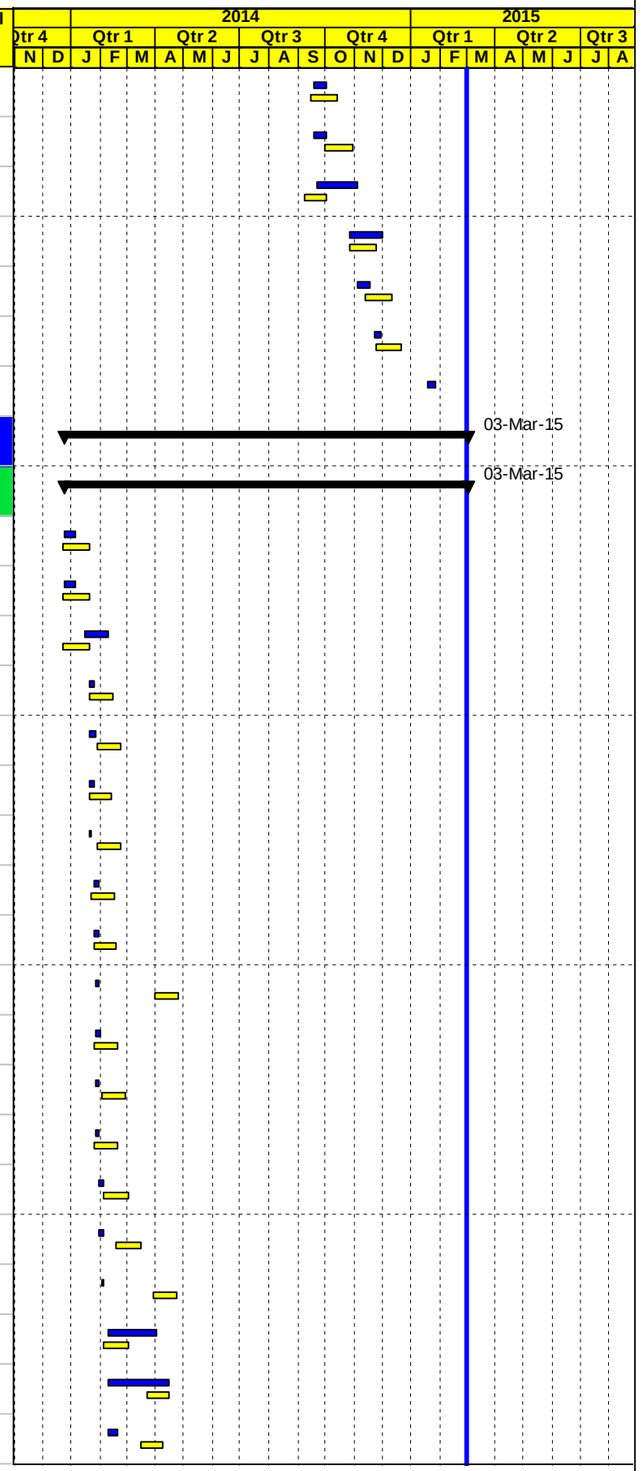

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST0795	Shrinkable Sheet	21d	100%	0d	18-Feb-14 A	23-Feb-14 A		$0.00	$0.00
DST0972-new	Washout Flap Valve	21d	100%	0d	20-Feb-14 A	25-Feb-14 A		$0.00	$0.00
DST0974-new	Check Valve	21d	100%	0d	02-Mar-14 A	03-Mar-14 A		$0.00	$0.00
DST0977-new	Finish Paint for Exposed Pipes/Fittings and Pipes/Fittings Inside Chambers	21d	100%	0d	13-Mar-14 A	30-Mar-14 A		$0.00	$0.00
DST0976-new	Bolts, Nuts& Washers	21d	100%	0d	23-Mar-14 A	05-May-14 A		$0.00	$0.00
DST0920	Electro-Magnetic Flow Meters	21d	100%	0d	21-Apr-14 A	09-Jun-14 A		$0.00	$0.00
DST0950-new	Hubbed Slip on Flanges for Welding (Alternative)	21d	100%	0d	08-May-14 A	18-May-14 A		$0.00	$0.00
DST0940	Pressure Gauges	21d	100%	0d	12-May-14 A	21-Aug-14 A		$0.00	$0.00
DST0955-new	Structural Analysis for Gate Valve Chamber Walls.	21d	100%	0d	23-Jul-14 A	04-Aug-14 A		$0.00	$0.00
DST0960-new	Adjustable Support for pipes & Fittings inside chambers	21d	100%	0d	20-Aug-14 A	16-Sep-14 A		$0.00	$0.00
DST0965-new	Ball Valve-Tyco F120 for Pressure Gauge	21d	100%	0d	27-Aug-14 A	28-Aug-14 A		$0.00	$0.00
DST0975-new	Galvanized Manhole ladder	21d	100%	0d	27-Aug-14 A	15-Oct-14 A		$0.00	$0.00
DST0980-new	Measuring Ranges for Pressure Gauges	21d	100%	0d	09-Sep-14 A	16-Sep-14 A		$0.00	$0.00
DST0990-new	Weld neck flange-DIN 2635 for 10" and 12" sizes	21d	100%	0d	06-Nov-14 A	10-Nov-14 A		$0.00	$0.00
DST0985-new	Strainer Ball Valve	21d	100%	0d	09-Nov-14 A	11-Nov-14 A		$0.00	$0.00
DST0995-new	Pipe Marker	21d	100%	0d	09-Nov-14 A	18-Nov-14 A		$0.00	$0.00
DST0999-new	Anti Seize for Stainless Steel Bolts	21d	100%	0d	17-Dec-14 A	22-Dec-14 A		$0.00	$0.00
DST0310-new	Sewer Manhole Cover 60cm clear opening	21d	90%	2d	18-Jan-15 A	03-Mar-15	6d	$0.00	$0.00
DST0300-new	FCVs Orifice Calculations	21d	100%	0d	29-Jan-15 A	03-Feb-15 A		$0.00	$0.00
DST0320-new	Gate Valve PN 25	21d	100%	0d	15-Feb-15 A	18-Feb-15 A		$0.00	$0.00
Material Submittals civil		302d		0d	15-Jan-14 A	03-Feb-15 A		$0.00	$0.00
DST1015	Bedding material	21d	100%	0d	15-Jan-14 A	20-Jan-14 A		$0.00	$0.00
DST1018	Backfilling material (Basecourse and single size)	21d	100%	0d	15-Jan-14 A	20-Jan-14 A		$0.00	$0.00
DST1100	Prime Coat	21d	100%	0d	23-Jan-14 A	26-Jan-14 A		$0.00	$0.00
DST1110	Tack Coat	21d	100%	0d	23-Jan-14 A	26-Jan-14 A		$0.00	$0.00
DST1042	Cold Bituminous material	21d	100%	0d	26-Jan-14 A	26-Jan-14 A		$0.00	$0.00
DST1130	Asphalt -Mix Design	21d	100%	0d	28-Jan-14 A	06-Feb-14 A		$0.00	$0.00
DST1010	Concrete Mix Design including Cement type	21d	100%	0d	30-Jan-14 A	26-Feb-14 A		$0.00	$0.00

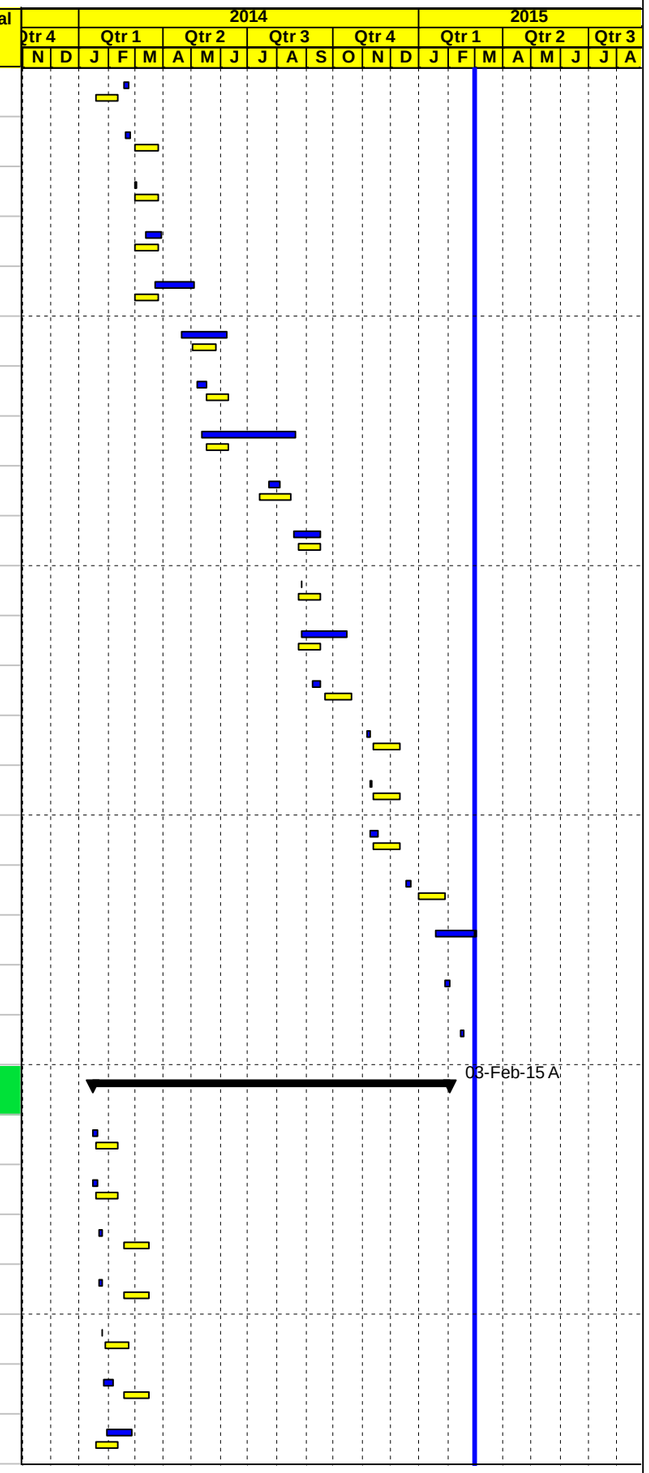

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST1030	Steel Reinforcement	21d	100%	0d	02-Feb-14 A	06-Feb-14 A		$0.00	$0.00
DST1035-new	Concrete & Plastic Supports/Spacers	21d	100%	0d	02-Mar-14 A	18-Mar-14 A		$0.00	$0.00
DST1028	Concrete Formwork Tie Rods	21d	100%	0d	04-Mar-14 A	18-Mar-14 A		$0.00	$0.00
DST1036-new	Casing (Sleeve) For Water Pipe line Crossing Main Asphalted Road & Israeli Roads	21d	100%	0d	05-Mar-14 A	16-Apr-14 A		$0.00	$0.00
DST1037-new	Stainless Steel Chocks & Materials for Filling Annular Space With Non-Shrink Grout	21d	100%	0d	08-May-14 A	27-May-14 A		$0.00	$0.00
DST1038-new	Precast Manhole for Washout , Air vent & release Manhole	21d	100%	0d	29-May-14 A	22-Jul-14 A		$0.00	$0.00
DST1040-new	Sewer UPVC Pipes (DN 8" SN 8)	21d	100%	0d	30-Dec-14 A	13-Jan-15 A		$0.00	$0.00
DST1045-new	Sewer Circular Precast Concrete Manhole (one meter internal diameter)	21d	100%	0d	30-Dec-14 A	03-Feb-15 A		$0.00	$0.00
DST1046-new	Rubber Gasket for 8" sewer UPVC pipes/ Sample	21d	100%	0d	15-Jan-15 A	20-Jan-15 A		$0.00	$0.00
Procurements		259d		0d	20-Jan-14 A	08-Dec-14 A		$0.00	$0.00
Order		134d		0d	20-Jan-14 A	19-Jun-14 A		$0.00	$0.00
DST1160	Start Order 300 mm,150 mm pipes and fittings	0d	100%	0d	20-Jan-14 A			$0.00	$0.00
DST1170	Start Order valves and other related materials	0d	100%	0d	19-Jun-14 A			$0.00	$0.00
Manufacturing		174d		0d	20-Jan-14 A	13-Nov-14 A		$0.00	$0.00
DST1190	300 mm,150 mm pipes and fittings	29d	100%	0d	20-Jan-14 A	11-Mar-14 A		$0.00	$0.00
DST1200	Valves and other related materials	70d	100%	0d	22-Jun-14 A	13-Nov-14 A		$0.00	$0.00
Delivery		204d		0d	11-Mar-14 A	08-Dec-14 A		$0.00	$0.00
DST1210	Start Delivery 300mm, 150 mm pipes and fittings	0d	100%	0d	11-Mar-14 A			$0.00	$0.00
DST1220	Start Delivery valves and other related materials	0d	100%	0d	08-Dec-14 A			$0.00	$0.00
Testing		2d		0d	16-Mar-14 A	16-Mar-14 A		$0.00	$0.00
DST1230	300 mm,150 mm pipes and fittings	2d	100%	0d	16-Mar-14 A	16-Mar-14 A		$0.00	$0.00
Construction Work		331d		8d	19-Jan-14 A	08-Mar-15	2d	$6,533,890.57	$6,521,797.65
Implement traffic control		5d		0d	19-Jan-14 A	23-Mar-14 A		$0.00	$0.00
DST1240	Start Implement traffic control and safety plan	5d	100%	0d	19-Jan-14 A	23-Mar-14 A		$0.00	$0.00
Main pipeline		321d		8d	26-Mar-14 A	08-Mar-15	2d	$6,533,890.57	$6,521,797.65
Segment A		303d		0d	26-Mar-14 A	24-Dec-14 A		$4,722,384.52	$4,722,417.10
Phase One from Sta. A9+702 to Sta. A12+900 At RHS/ Location Area(B)		243d		0d	26-Mar-14 A	18-Dec-14 A		$1,005,721.17	$1,005,743.25
300 mm Main pipeline from Sta. A9+702 to Sta. A11+300 At RHS/ Location Area(B)		237d		0d	06-Apr-14 A	18-Dec-14 A		$522,671.30	$522,671.30

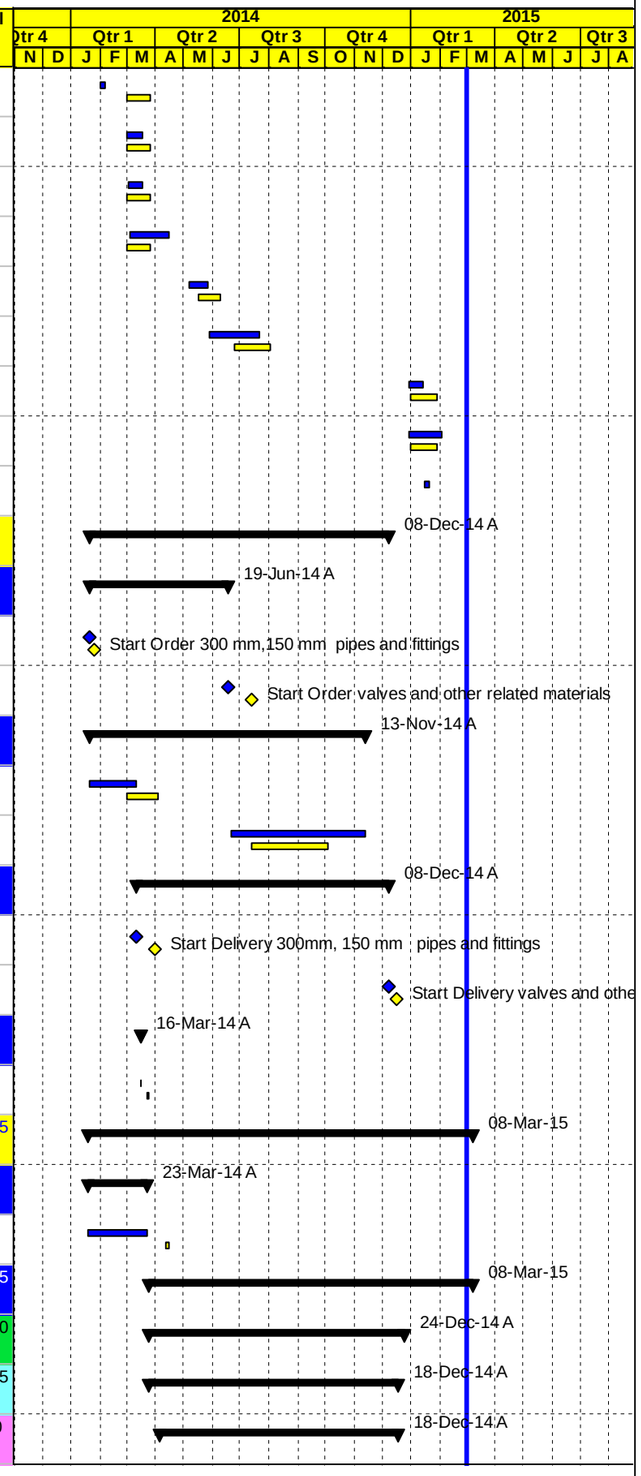

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
Safety and Remove Asphalt		78d		0d	06-Apr-14 A	18-Dec-14 A		$0.00	$0.00
DST1570	Maintain traffic control and safety plan	78d	100%	0d	06-Apr-14 A	18-Dec-14 A		$0.00	$0.00
DST1580	Remove Asphalt	6d	100%	0d	07-Apr-14 A	29-Apr-14 A		$0.00	$0.00
Pipe Installation		71d		0d	07-Apr-14 A	29-May-14 A		$319,363.38	$319,363.38
DST1590	Trench excavation for 300 mm main pipeline length approx. (1600 LM) and road crossing	18d	100%	0d	07-Apr-14 A	30-Apr-14 A		$51,136.00	$51,136.00
DST1600	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	18d	100%	0d	08-Apr-14 A	30-Apr-14 A		$224,537.83	$224,537.83
DST1620	Compact Approved Backfill material ,sub base / base course above pipeline	18d	100%	0d	08-Apr-14 A	30-Apr-14 A		$27,166.00	$27,166.00
DST1610	Casting concrete as encasement around the main pipeline from Sta. A10+326 and Sta. A10+431 (105 LM)	19d	100%	0d	20-Apr-14 A	22-Apr-14 A		$8,925.00	$8,925.00
DST1672	Future connection at Sta. A10+460 and Sta. A9+920	1d	100%	0d	29-May-14 A	29-May-14 A		$7,598.55	$7,598.55
Civil Chamber work		95d		0d	26-May-14 A	14-Dec-14 A		$110,124.15	$110,124.15
DST1630	Construct - Gate Valve chambe (Dia. 200 mm) @ Sta. A9+941	14d	100%	0d	26-May-14 A	15-Jul-14 A		$14,850.00	$14,850.00
DST1660	Construct - Combined Butterfly Valve (Dia.300) and Air Valve chamber(Dia.100mm) @ Sta. 11+187	18d	100%	0d	02-Jun-14 A	23-Jun-14 A		$46,039.47	$46,039.47
DST1645	Construct - Gate Valve chamber (Dia. 200mm) @ Sta. A10+461 (Precast)	14d	100%	0d	15-Jul-14 A	20-Jul-14 A		$14,850.00	$14,850.00
DST1640	Construct- Combination Air Valve chamber (Dia.100mm) @ Sta. A9+928 (Precast)	14d	100%	0d	08-Sep-14 A	14-Dec-14 A		$14,100.00	$14,100.00
DST1650	Construct - Wash out Valve chamber (Dia.150mm) @ A10+889	13d	100%	0d	15-Sep-14 A	01-Oct-14 A		$20,284.68	$20,284.68
Testing		135d		0d	05-May-14 A	18-Dec-14 A		$0.00	$0.00
DST1674	Radiograph Testing	2d	100%	0d	05-May-14 A	05-May-14 A		$0.00	$0.00
DST1676	Pressure Testing	2d	100%	0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
Reinstatement		74d		0d	30-Apr-14 A	13-Nov-14 A		$93,183.78	$93,183.78
DST1680	Asphalt reinstatement	4d	100%	0d	30-Apr-14 A	12-Nov-14 A		$53,085.78	$53,085.78
DST1685-new	Milling of Existing Asphalt	1d	100%	0d	28-Oct-14 A	28-Oct-14 A		$4,920.00	$4,920.00
DST1690-new	Asphalt reinstatement (wearing course)	5d	100%	0d	10-Nov-14 A	13-Nov-14 A		$35,178.00	$35,178.00
300 mm Main pipeline from Sta. A11+300 to Sta. A12+900 At RHS/ Location Area(B)		243d		0d	26-Mar-14 A	18-Dec-14 A		$483,049.86	$483,071.94
Safety and Remove Asphalt		75d		0d	26-Mar-14 A	18-Dec-14 A		$0.00	$0.00
DST1682	Maintain traffic control and safety plan	63d	100%	0d	26-Mar-14 A	18-Dec-14 A		$0.00	$0.00
DST1690	Remove Asphalt	7d	100%	0d	26-Mar-14 A	11-May-14 A		$0.00	$0.00
Pipe Installation		21d		0d	26-Mar-14 A	24-May-14 A		$305,076.86	$305,098.94
DST1700	Trench excavation for 300 mm main pipeline length approx. (1600 LM)	18d	100%	0d	26-Mar-14 A	13-May-14 A		$50,946.32	$50,968.40

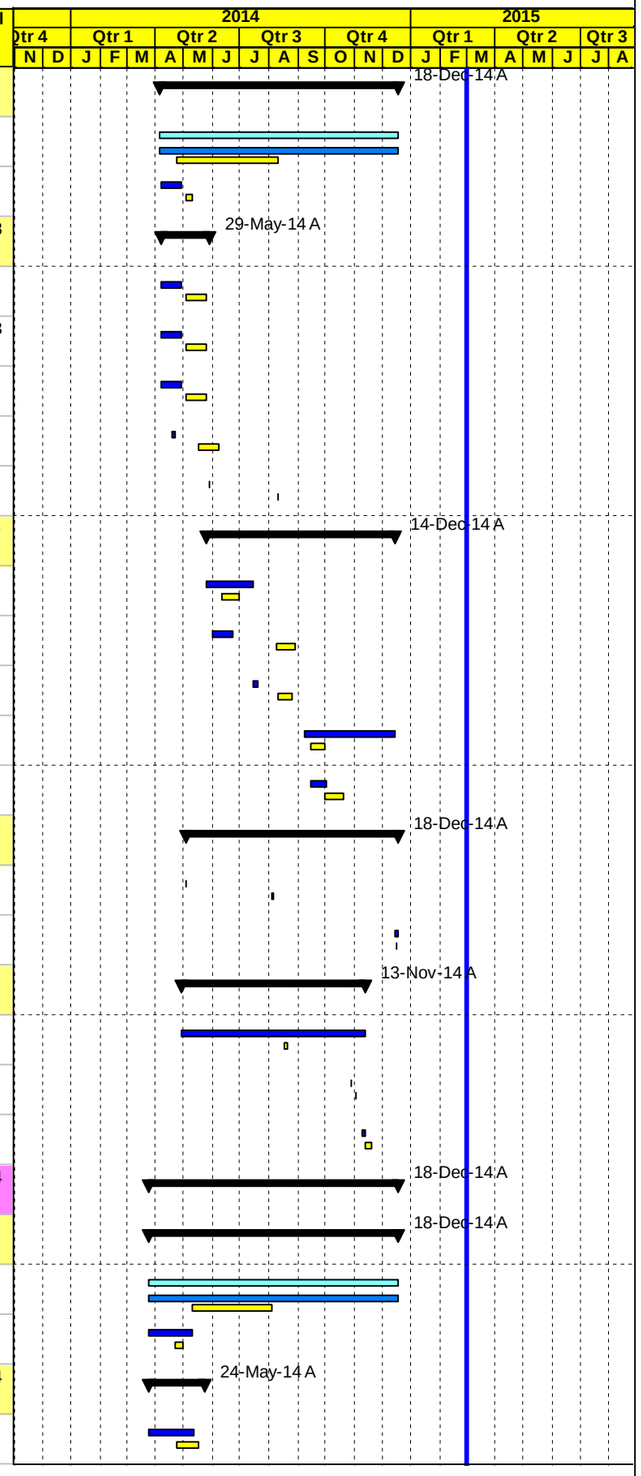

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST1710	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	18d	100%	0d	26-Mar-14 A	13-May-14 A		$223,945.82	$223,945.82
DST1730	Compact Approved Backfill material ,sub base / base course above pipeline	18d	100%	0d	26-Mar-14 A	13-May-14 A		$26,922.73	$26,922.73
DST1890-new	Road crossing from Sta. 12+562.11 to St. 12+578.42 (16.31m)	2d	100%	0d	24-May-14 A	24-May-14 A		$3,262.00	$3,262.00
Civil Chamber work		18d		0d	25-Aug-14 A	02-Dec-14 A		$93,200.00	$93,200.00
DST1750	Construct - Combination Air Valve chamber (Dia. 100mm) @ 12+500	14d	100%	0d	25-Aug-14 A	05-Nov-14 A		$14,100.00	$14,100.00
DST1760	Construct - Combination Air Valve chamber (Dia.100mm) @ 11+743	14d	100%	0d	25-Aug-14 A	02-Dec-14 A		$14,100.00	$14,100.00
DST1765-new	Al Foudqumiya Connection Chamber (Dia.100mm) at Sta. 12+142	14d	100%	0d	28-Aug-14 A	01-Oct-14 A		$65,000.00	$65,000.00
Testing		243d		0d	30-Mar-14 A	18-Dec-14 A		$0.00	$0.00
DST1772	Radiograph Testing	2d	100%	0d	30-Mar-14 A	07-May-14 A		$0.00	$0.00
DST1774	Pressure Testing	3d	100%	0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
Reinstatement		82d		0d	04-May-14 A	10-Nov-14 A		$84,773.00	$84,773.00
DST1778	Asphalt reinstatement	4d	100%	0d	04-May-14 A	02-Jun-14 A		$52,173.00	$52,173.00
DST1780-new	Milling of Existing Asphalt	1d	100%	0d	28-Oct-14 A	28-Oct-14 A		$4,000.00	$4,000.00
DST1788-new	Asphalt Reinstatement (wearing course)	5d	100%	0d	09-Nov-14 A	10-Nov-14 A		$28,600.00	$28,600.00
Phase Two 300 mm Main pipeline from Sta. A12+900 to Sta. A13+154 At LHS/ Location Area(B)		164d		0d	11-May-14 A	18-Dec-14 A		$65,164.75	$65,164.75
Safety and Remove Asphalt		38d		0d	11-May-14 A	18-Dec-14 A		$0.00	$0.00
DST1850	Maintain traffic control and safety plan	26d	100%	0d	11-May-14 A	18-Dec-14 A		$0.00	$0.00
DST1860	Remove Asphalt	3d	100%	0d	12-May-14 A	15-May-14 A		$0.00	$0.00
Pipe Installation		24d		0d	13-May-14 A	15-May-14 A		$50,262.75	$50,262.75
DST1880	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	6d	100%	0d	13-May-14 A	15-May-14 A		$35,458.00	$35,458.00
DST1890	Compact Approved Backfill material ,sub base / base course above pipeline	6d	100%	0d	13-May-14 A	15-May-14 A		$4,318.00	$4,318.00
DST1870	Trench excavation for 300 mm main pipeline length approx. (254 LM)	6d	100%	0d	13-May-14 A	15-May-14 A		$8,128.00	$8,128.00
DST1885	Casting Concrete as Encasement around the Main Pipeline or Single Size if required (from Sta. 13+055.40 to Sta. 13+083)	6d	100%	0d	15-May-14 A	15-May-14 A		$2,358.75	$2,358.75
Testing		2d		0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
DST1894	Pressure Testing	2d	100%	0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
Reinstatement		110d		0d	02-Jun-14 A	09-Nov-14 A		$14,902.00	$14,902.00
DST1898	Asphalt reinstatement	2d	100%	0d	02-Jun-14 A	02-Jun-14 A		$8,382.00	$8,382.00
DST1990-new	Milling of Existing Asphalt	1d	100%	0d	28-Oct-14 A	28-Oct-14 A		$800.00	$800.00

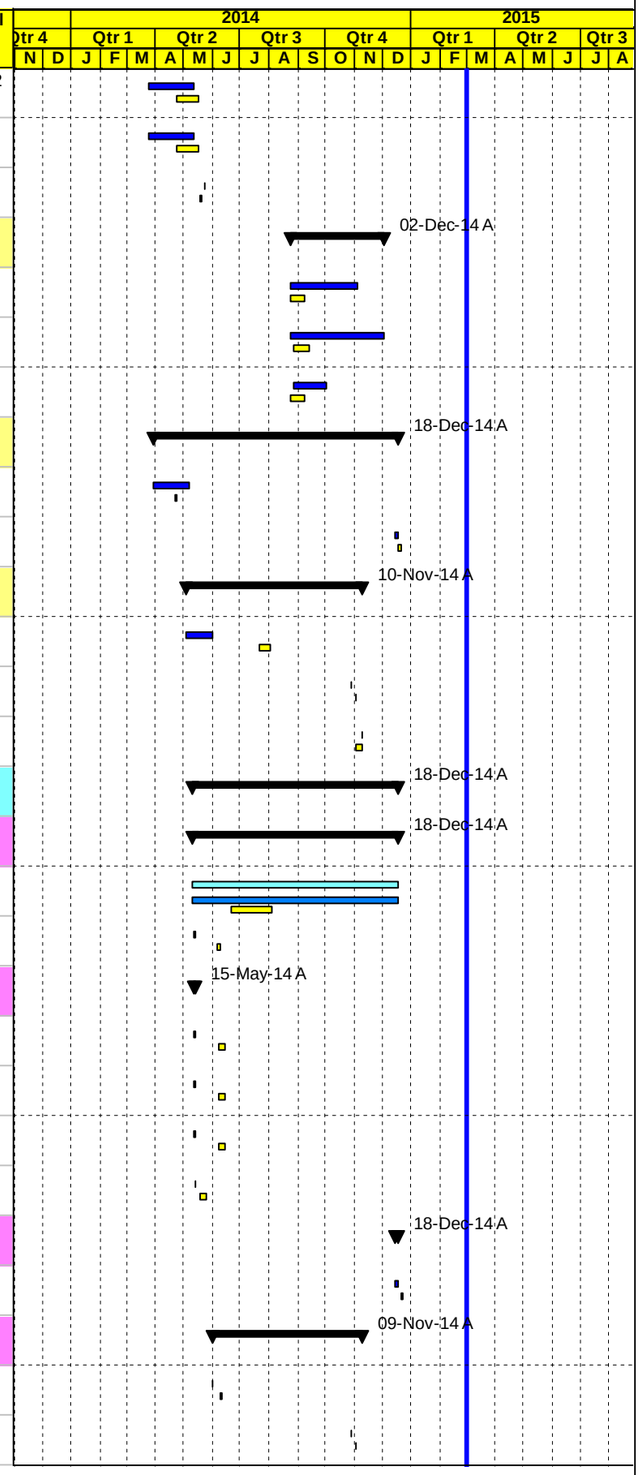

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST1999-new	Asphalt Reinstatement (wearing course)	3d	100%	0d	09-Nov-14 A	09-Nov-14 A		$5,720.00	$5,720.00
Phase Three 300 mm Main pipeline from Sta. A13+154 to Sta. A13+710 At LHS/ Location Area(C)		174d		0d	15-May-14 A	18-Dec-14 A		$277,532.71	$277,532.71
Safety and Remove Asphalt		88d		0d	15-May-14 A	18-Dec-14 A		$0.00	$0.00
DST1900	Maintain traffic control and Safety plan	88d	100%	0d	15-May-14 A	18-Dec-14 A		$0.00	$0.00
DST1910	Remove Asphalt	4d	100%	0d	15-May-14 A	22-May-14 A		$0.00	$0.00
Pipe Installation		63d		0d	15-May-14 A	24-May-14 A		$106,655.30	$106,655.30
DST1920	Trench excavation for 300 mm main pipeline length approx. (578 LM)	10d	100%	0d	15-May-14 A	24-May-14 A		$17,819.20	$17,819.20
DST1930	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	10d	100%	0d	17-May-14 A	24-May-14 A		$78,684.15	$78,684.15
DST1940	Compact Approved Backfill material ,sub base / base course above pipeline	10d	100%	0d	17-May-14 A	24-May-14 A		$9,466.45	$9,466.45
DST1938	Future connection at A13+625	1d	100%	0d	20-May-14 A	20-May-14 A		$685.50	$685.50
Civil Chamber work		43d		0d	05-Jun-14 A	02-Dec-14 A		$143,462.41	$143,462.41
DST2030	Construct - Gate Valve chamber (Dia. 250mm) at A13+617	5d	100%	0d	05-Jun-14 A	28-Aug-14 A		$28,177.73	$28,177.73
DST1960	Construct - Butterfly Valve chamber (Dia. 300mm) @ Sta. A13+700	14d	100%	0d	09-Jun-14 A	12-Jul-14 A		$35,000.00	$35,000.00
DST1970	Construct Al Asasa connection chamber (Dia. 50mm) at Sta. A13+608 & connect to exist. Pipes	14d	100%	0d	25-Jun-14 A	12-Oct-14 A		$60,000.00	$60,000.00
DST1950	Construct - Wash out Valve chamber (Dia. 150mm) @ Sta. A13+628	14d	100%	0d	13-Aug-14 A	02-Dec-14 A		$20,284.68	$20,284.68
Testing		2d		0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
DST1977	Pressure Testing	2d	100%	0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
Reinstatement		108d		0d	02-Jun-14 A	09-Nov-14 A		$27,415.00	$27,415.00
DST1979	Asphalt reinstatement	5d	100%	0d	02-Jun-14 A	29-Oct-14 A		$16,005.00	$16,005.00
DST1989-new	Milling of Existing Asphalt	1d	100%	0d	28-Oct-14 A	28-Oct-14 A		$1,400.00	$1,400.00
DST1995-new	Asphalt Reinstatement (wearing course)	3d	100%	0d	09-Nov-14 A	09-Nov-14 A		$10,010.00	$10,010.00
Phase Four from Sta. A6+983 to Sta. A2+280 At RHS/ Location Area(C)		245d		0d	25-May-14 A	24-Dec-14 A		$1,348,515.94	$1,348,515.94
300 mm Main pipeline from Sta. A6+983 to Sta. A5+200 At RHS/ Location Area(C)		162d		0d	25-May-14 A	14-Dec-14 A		$502,228.27	$502,228.27
Safety and Remove Exist. concrete ditch		68d		0d	25-May-14 A	14-Dec-14 A		$0.00	$0.00
DST2260	Maintain traffic control and safety plan	68d	100%	0d	25-May-14 A	14-Dec-14 A		$0.00	$0.00
DST2270	Remove Exist. concrete ditch	9d	100%	0d	26-May-14 A	17-Jun-14 A		$0.00	$0.00
Pipe Installation		154d		0d	26-May-14 A	17-Jun-14 A		$400,342.97	$400,342.97
DST2320	Backfilling from Sta.6+241.18 to 6+364 - 6+430.00 to 6+508.70 (201.52)	6d	100%	0d	26-May-14 A	17-Jun-14 A		$3,425.84	$3,425.84

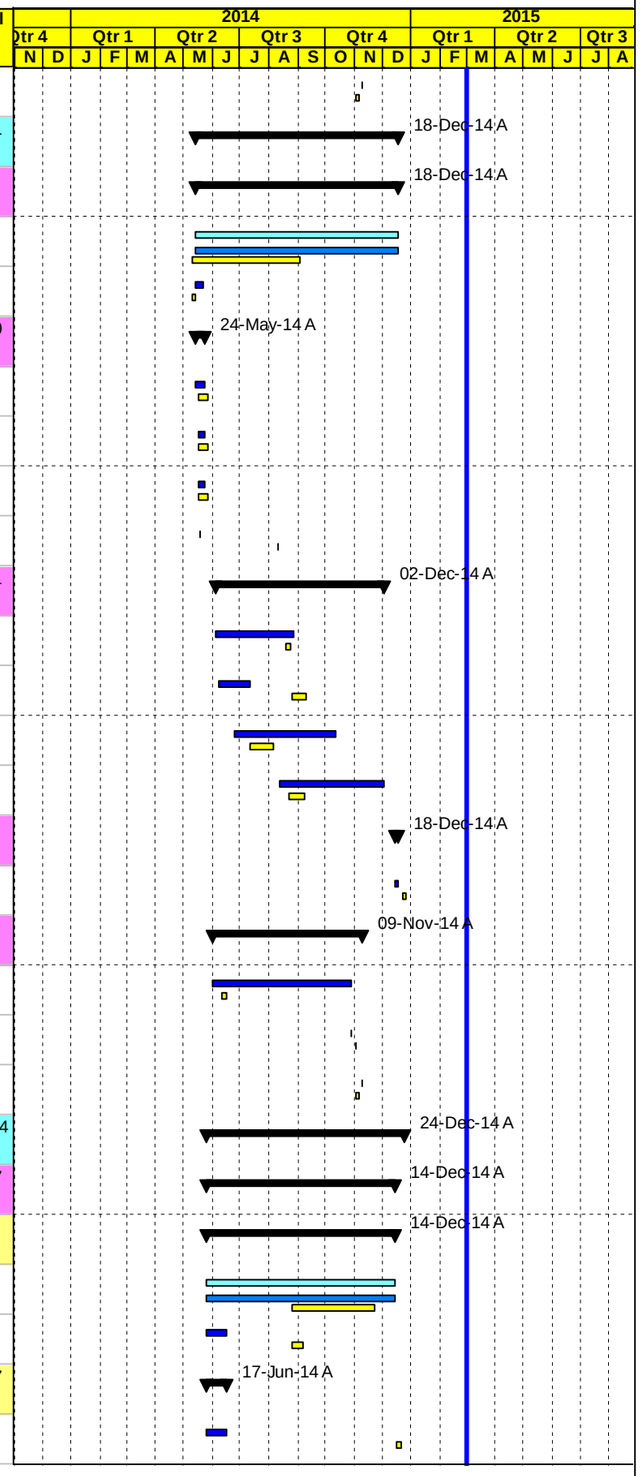

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST2290	Trench excavation for 300 mm main pipeline length approx. (1783 LM)	22d	100%	0d	26-May-14 A	17-Jun-14 A		$34,598.98	$34,598.98
DST2300	Install 300 mm schedule 20 Steel Pipe Include testing	22d	100%	0d	26-May-14 A	17-Jun-14 A		$221,092.00	$221,092.00
DST2310	Casting concrete as encasement around the main pipeline or single size if required	22d	100%	0d	26-May-14 A	17-Jun-14 A		$138,548.30	$138,548.30
DST2330	Bedding (single size aggregate) from Sta.6+289.68 to 6+364 - 6+430.00 to 6+508.70 (153.02)	6d	100%	0d	26-May-14 A	17-Jun-14 A		$2,677.85	$2,677.85
Civil Chamber work		14d		0d	31-Aug-14 A	03-Sep-14 A		$14,100.00	$14,100.00
DST2340	Construct - Combination Air Valve chamber (Dia. 100) @ Sta. A6+332	14d	100%	0d	31-Aug-14 A	03-Sep-14 A		$14,100.00	$14,100.00
Testing		2d		0d	14-Dec-14 A	14-Dec-14 A		$0.00	$0.00
DST2354	Pressure Testing	2d	100%	0d	14-Dec-14 A	14-Dec-14 A		$0.00	$0.00
Reinstatement		61d		0d	31-May-14 A	11-Aug-14 A		$87,785.29	$87,785.29
DST2356	Concrete Reinstatement	11d	100%	0d	31-May-14 A	05-Aug-14 A		$84,386.29	$84,386.29
DST2360-new	Asphalt Reinstatement (Sta. 6+508 to Sta. 6+430) 78 m	5d	100%	0d	11-Aug-14 A	11-Aug-14 A		$3,399.00	$3,399.00
300 mm Main pipeline from Sta. A5+200 to Sta. A3+880 At RHS/ Location Area(C)		200d		0d	17-Jun-14 A	14-Dec-14 A		$384,595.23	$384,595.23
Safety and Remove Exist. concrete ditch		117d		0d	17-Jun-14 A	14-Dec-14 A		$0.00	$0.00
DST2360	Maintain Traffic Control and Safety Plan	117d	100%	0d	17-Jun-14 A	14-Dec-14 A		$0.00	$0.00
DST2370	Remove Exist. concrete ditch	9d	100%	0d	17-Jun-14 A	30-Jun-14 A		$0.00	$0.00
Pipe Installation		31d		0d	17-Jun-14 A	30-Jun-14 A		$290,462.12	$290,462.12
DST2390	Trench excavation for 300 mm main pipeline length approx. (1320 LM)	18d	100%	0d	17-Jun-14 A	30-Jun-14 A		$27,302.45	$27,302.45
DST2400	Install 300 mm Steel pipe schedule 20 include testing	18d	100%	0d	17-Jun-14 A	30-Jun-14 A		$161,200.00	$161,200.00
DST2410	Casting concrete as encasement around the main pipeline or single size if required	18d	100%	0d	17-Jun-14 A	30-Jun-14 A		$93,566.30	$93,566.30
DST2420-new	Bedding (single size aggregate) from Sta. 4+081.25 to Sta. 3+918	1d	100%	0d	30-Jun-14 A	30-Jun-14 A		$3,836.35	$3,836.35
DST2425-new	Backfilling from Sta. 4+186.06 to Sta. 3+918	1d	100%	0d	30-Jun-14 A	30-Jun-14 A		$4,557.02	$4,557.02
Civil Chamber work		36d		0d	31-Aug-14 A	27-Oct-14 A		$34,384.68	$34,384.68
DST2430	Construct - Combination Air Valve chamber (Dia. 100mm) @ 5+110	14d	100%	0d	31-Aug-14 A	03-Sep-14 A		$14,100.00	$14,100.00
DST2442	Construct - Wash out Valve chamber (Dia. 150mm) @ Sta. A3+924	14d	100%	0d	29-Sep-14 A	27-Oct-14 A		$20,284.68	$20,284.68
Testing		162d		0d	19-Jun-14 A	14-Dec-14 A		$0.00	$0.00
DST2444	Radiograph Testing	2d	100%	0d	19-Jun-14 A	19-Jun-14 A		$0.00	$0.00
DST2446	Pressure Testing	2d	100%	0d	14-Dec-14 A	14-Dec-14 A		$0.00	$0.00
Reinstatement		54d		0d	05-Aug-14 A	11-Aug-14 A		$59,748.43	$59,748.43

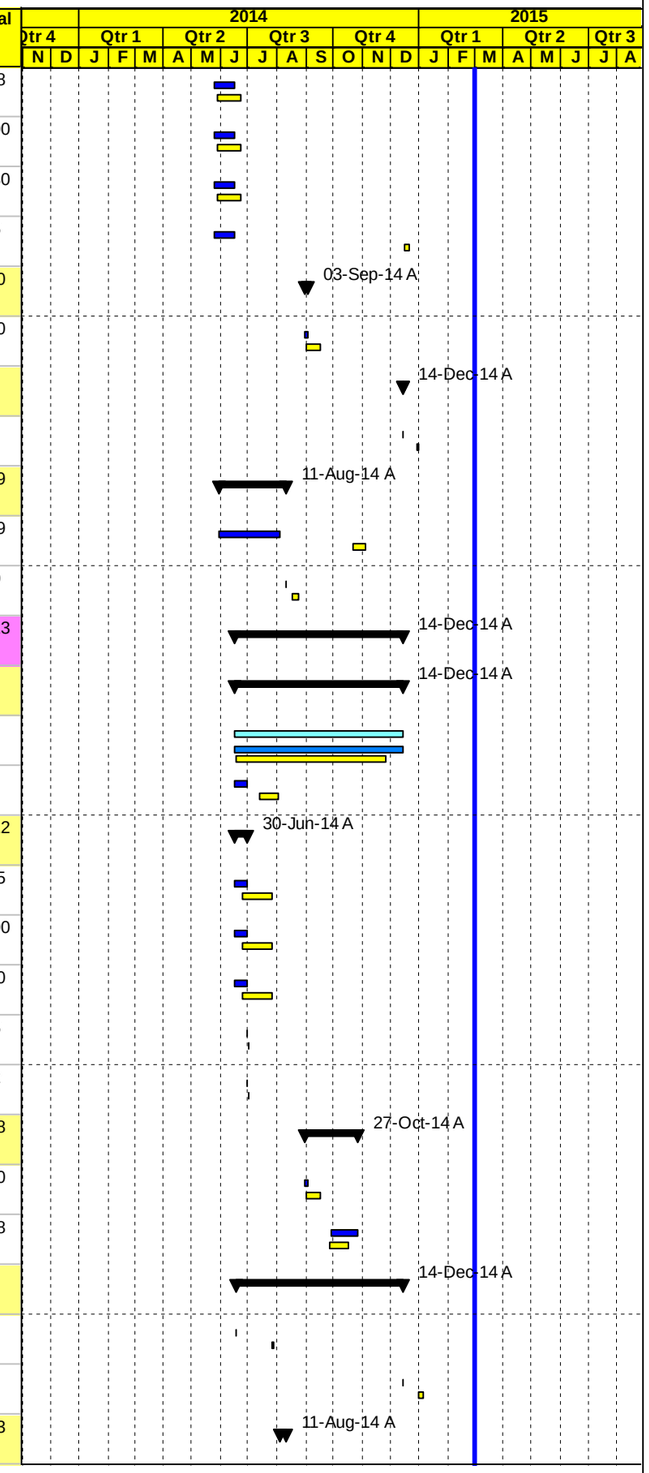

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST2448	Concrete Reinstatement	15d	100%	0d	05-Aug-14 A	11-Aug-14 A		$56,210.82	$56,210.82
DST2449-new	Asphalt Reinstatement (Sta. 3+950 to Sta. 4+080 (130 m)	15d	100%	0d	11-Aug-14 A	11-Aug-14 A		$3,537.60	$3,537.60
300 mm Main pipeline from Sta. A3+480 to Sta. A2+280 At RHS/ Location Area(C)		212d		0d	30-Jun-14 A	24-Dec-14 A		$461,692.45	$461,692.45
Safety and Remove Exist. concrete ditch		74d		0d	30-Jun-14 A	14-Dec-14 A		$0.00	$0.00
DST2450	Maintain traffic control and safety plan	74d	100%	0d	30-Jun-14 A	14-Dec-14 A		$0.00	$0.00
DST2460	Remove Exist. concrete ditch	9d	100%	0d	16-Jul-14 A	16-Jul-14 A		$0.00	$0.00
Pipe Installation		125d		0d	01-Jul-14 A	19-Jul-14 A		$272,368.30	$272,368.30
DST2480	Trench excavation for 300 mm main pipeline length approx. (1200 LM)	19d	100%	0d	01-Jul-14 A	17-Jul-14 A		$22,167.41	$22,167.41
DST2490	Install 300 mm Steel pipe schedule 20 include testing	19d	100%	0d	01-Jul-14 A	16-Jul-14 A		$148,800.00	$148,800.00
DST2500	Casting concrete as encasement around the main pipeline or single size if required	19d	100%	0d	02-Jul-14 A	16-Jul-14 A		$95,472.00	$95,472.00
DST2510-new	Bedding (single size aggregate) from Sta. 3+354 to Sta. 3+321 & Sta. 2+961 to Sta. 2+936	19d	100%	0d	03-Jul-14 A	09-Jul-14 A		$995.05	$995.05
DST2520-new	Backfilling from Sta. 3+354 to Sta. 3+324 & Sta. 2+961.86 to Sta. 2+935 (56.86m)	19d	100%	0d	03-Jul-14 A	09-Jul-14 A		$943.84	$943.84
DST2530-new	Road crossing from St.2+319.78 to St. 2+299.88 (19.9m)	5d	100%	0d	19-Jul-14 A	19-Jul-14 A		$3,990.00	$3,990.00
Civil Chamber work		132d		0d	02-Aug-14 A	24-Dec-14 A		$189,324.15	$189,324.15
DST2530	Construct - Air Valve chamber (Dia. 100mm) combined with Butterfly Valve (Dia. 300mm) @A3+350	20d	100%	0d	02-Aug-14 A	07-Sep-14 A		$46,039.47	$46,039.47
DST2540	Construct - Butterfly Valve chamber (Dia. 300mm) @ 2+952	14d	100%	0d	10-Aug-14 A	07-Sep-14 A		$35,000.00	$35,000.00
DST2520	Construct -Wash out chamber (Dia. 150mm) @2+952	14d	100%	0d	13-Aug-14 A	24-Dec-14 A		$20,284.68	$20,284.68
DST2552	Sabastiya Washout (Dia. 250mm) @ St.2+936	5d	100%	0d	13-Aug-14 A	24-Aug-14 A		$24,000.00	$24,000.00
DST2550	Construct Sabastia connection chamber (Dia. 75mm) at Sta. A2+322 & connect to exist.WSP	14d	100%	0d	01-Sep-14 A	02-Dec-14 A		$64,000.00	$64,000.00
Testing		66d		0d	14-Aug-14 A	14-Dec-14 A		$0.00	$0.00
DST2553	Radiograph Testing	2d	100%	0d	14-Aug-14 A	14-Aug-14 A		$0.00	$0.00
DST2555	Pressure Testing	2d	100%	0d	14-Dec-14 A	14-Dec-14 A		$0.00	$0.00
Reinstatement		9d		0d	14-Jul-14 A	01-Oct-14 A		$0.00	$0.00
DST2426-new	Backfilling with selected material from Sta. 3+460 to Sta. 2+340	9d	100%	0d	14-Jul-14 A	01-Oct-14 A		$0.00	$0.00
Phase Five 300 mm Main pipeline from Sta. A2+280 to Sta. A1+220 At LHS/ Location Area(C)		174d		0d	15-Jul-14 A	14-Dec-14 A		$302,982.27	$302,982.27
Safety and Remove Exist. concrete ditch		83d		0d	15-Jul-14 A	14-Dec-14 A		$0.00	$0.00
DST2560	Maintain traffic control and safety plan	83d	100%	0d	15-Jul-14 A	14-Dec-14 A		$0.00	$0.00
DST2570	Remove Exist. concrete ditch	5d	100%	0d	17-Jul-14 A	09-Aug-14 A		$0.00	$0.00

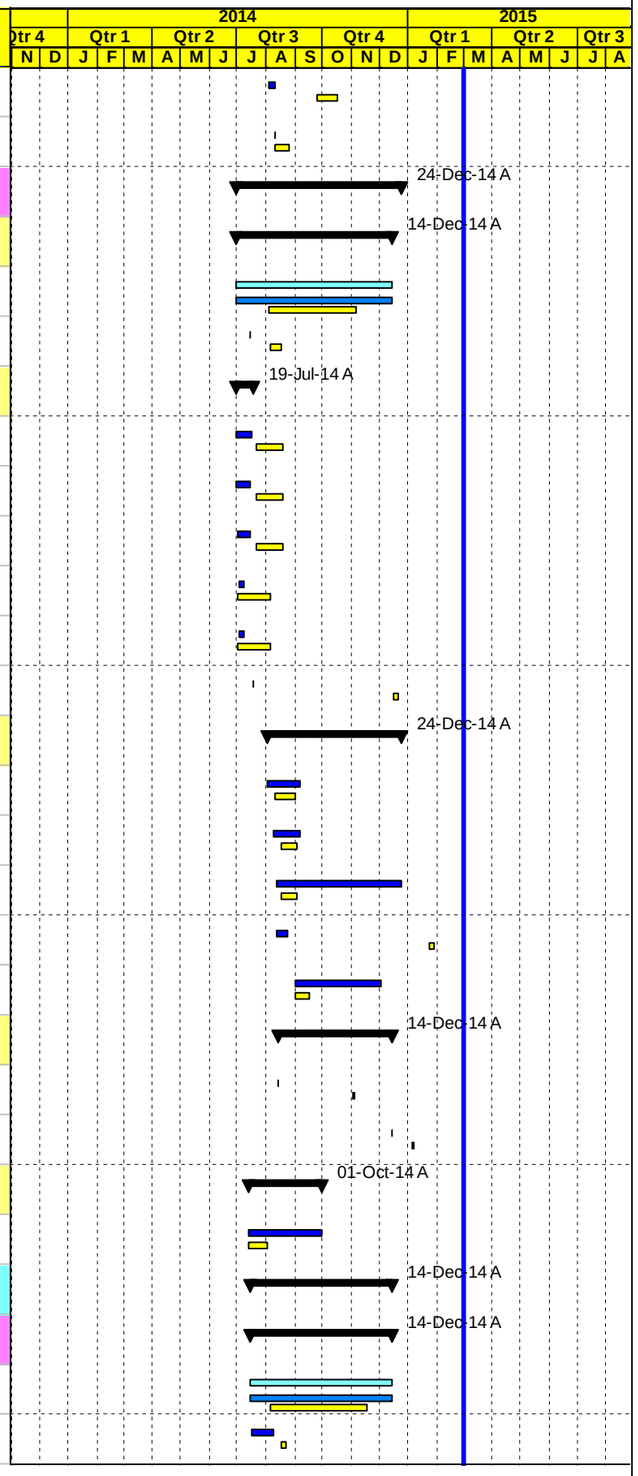

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
Pipe Installation		115d		0d	17-Jul-14 A	29-Sep-14 A		$236,476.56	$236,476.56
DST2590	Trench excavation for 300 mm main pipeline length approx. (1060 LM)	15d	100%	0d	17-Jul-14 A	09-Aug-14 A		$19,620.60	$19,620.60
DST2600	Install 300 mm schedule 20 Steel pipe include testing	15d	100%	0d	19-Jul-14 A	09-Aug-14 A		$127,991.56	$127,991.56
DST2610	Casting concrete as encasement around the main pipeline or single size if required	15d	100%	0d	20-Jul-14 A	09-Aug-14 A		$83,980.00	$83,980.00
DST2620-new	Bedding from Sta. 1+360 to 1+413 (53m)	15d	100%	0d	07-Aug-14 A	07-Aug-14 A		$927.50	$927.50
DST2630-new	Backfilling from Sta. 1+360 to 1+413 (53m)	15d	100%	0d	07-Aug-14 A	07-Aug-14 A		$850.00	$850.00
DST2645-new	Road crossing from St. 1+239 to St. 1+224.19	5d	100%	0d	08-Aug-14 A	08-Aug-14 A		$2,962.00	$2,962.00
DST2635-new	Bedding from sta.1+224.19 to Sta.1+220 (4.2m)	15d	100%	0d	29-Sep-14 A	29-Sep-14 A		$73.50	$73.50
DST2640-new	Backfilling from Sta.1+224.19 to Sta.1+221 (4.2m)	15d	100%	0d	29-Sep-14 A	29-Sep-14 A		$71.40	$71.40
Civil Chamber work		14d		0d	15-Sep-14 A	02-Dec-14 A		$14,100.00	$14,100.00
DST2650	Construct - Combination Air Valve chamber (Dia. 100) @ 1+390	14d	100%	0d	15-Sep-14 A	02-Dec-14 A		$14,100.00	$14,100.00
Testing		76d		0d	14-Aug-14 A	14-Dec-14 A		$0.00	$0.00
DST2652	Radiograph Testing	2d	100%	0d	14-Aug-14 A	14-Aug-14 A		$0.00	$0.00
DST2654	Pressure Testing	2d	100%	0d	14-Dec-14 A	14-Dec-14 A		$0.00	$0.00
Reinstatement		10d		0d	27-Aug-14 A	28-Aug-14 A		$52,405.71	$52,405.71
DST2656	Concrete Reinstatement	10d	100%	0d	27-Aug-14 A	28-Aug-14 A		$52,405.71	$52,405.71
Phase Six 300 mm Main pipeline from Sta. A9+702 to Sta. A9+030 At RHS/ Location Area(C)		148d		0d	09-Aug-14 A	18-Dec-14 A		$182,321.46	$182,321.46
Safety and Remove Exist. concrete ditch		25d		0d	09-Aug-14 A	18-Dec-14 A		$0.00	$0.00
DST1980	Maintain traffic control and safety plan	25d	100%	0d	09-Aug-14 A	18-Dec-14 A		$0.00	$0.00
DST1990	Remove Exist. concrete ditch	4d	100%	0d	10-Aug-14 A	17-Aug-14 A		$0.00	$0.00
Pipe Installation		14d		0d	10-Aug-14 A	19-Aug-14 A		$150,858.60	$150,858.60
DST2000	Trench Excavation for 300 mm Main Pipeline Length approx. (672 LM)	10d	100%	0d	10-Aug-14 A	18-Aug-14 A		$14,020.60	$14,020.60
DST2010	Install 300 mm schedule 20 Steel pipe include testing	10d	100%	0d	11-Aug-14 A	18-Aug-14 A		$83,328.00	$83,328.00
DST2060-new	Bedding from Sta. 9+691 to Sta. 9+610 (81 m)	2d	100%	0d	11-Aug-14 A	12-Aug-14 A		$1,575.00	$1,575.00
DST2064-new	Backfilling from Sta. 9+702 to Sta. 9+557 (145)	2d	100%	0d	11-Aug-14 A	12-Aug-14 A		$2,465.00	$2,465.00
DST2020	Casting Concrete as Encasement Around the Main Pipeline or Single Size if Required	10d	100%	0d	12-Aug-14 A	19-Aug-14 A		$49,470.00	$49,470.00
Testing		127d		0d	14-Aug-14 A	18-Dec-14 A		$0.00	$0.00
DST2032	Radiograph Testing	2d	100%	0d	14-Aug-14 A	14-Aug-14 A		$0.00	$0.00

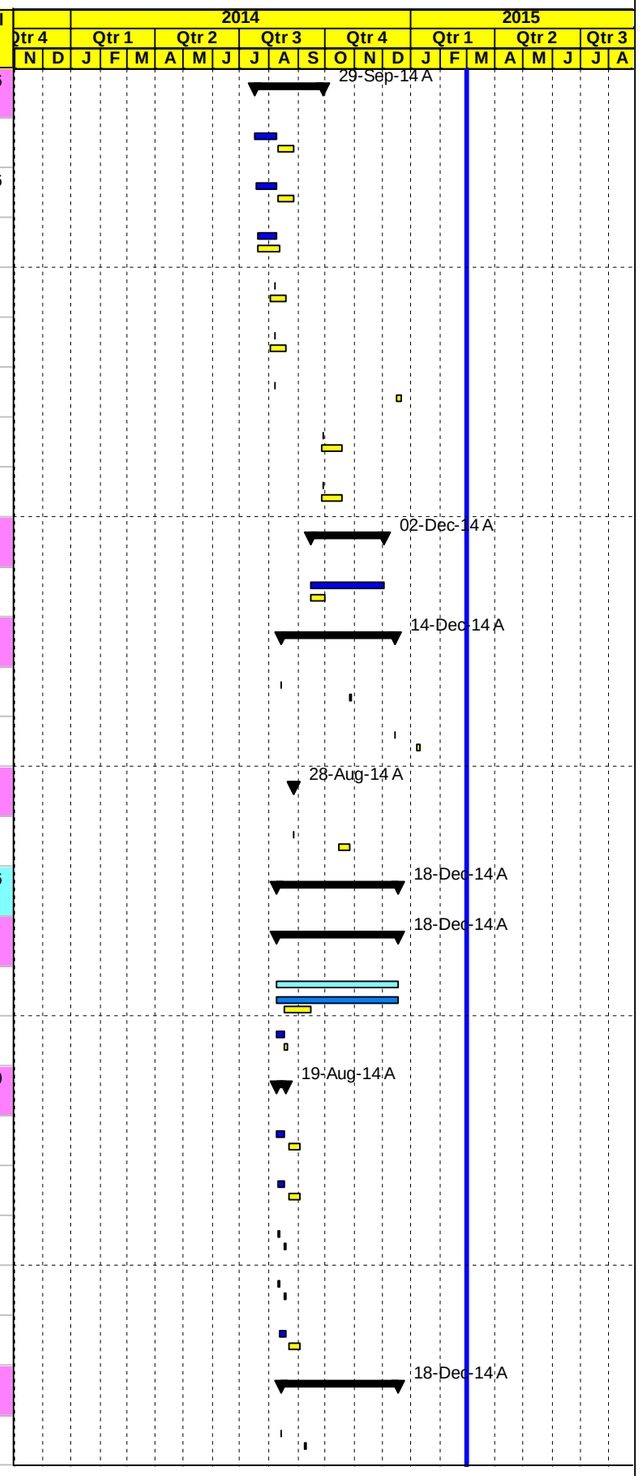

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST2034	Pressure Testing	2d	100%	0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
Reinstatement		18d		0d	01-Sep-14 A	29-Oct-14 A		$31,462.86	$31,462.86
DST2036	Concrete Reinstatement	5d	100%	0d	01-Sep-14 A	24-Sep-14 A		$25,963.74	$25,963.74
DST2040-new	Asphalt Reinstatement from Sta. 9+570 to Sta. 9+690	1d	100%	0d	29-Oct-14 A	29-Oct-14 A		$5,499.12	$5,499.12
Phase Seven 300 mm Main pipeline from Sta. A9+030 to Sta. A8+080 At LHS/ Location Area(C)		135d		0d	14-Aug-14 A	18-Dec-14 A		$322,632.00	$322,642.50
Safety and Remove Exist. concrete ditch		39d		0d	18-Aug-14 A	18-Dec-14 A		$0.00	$0.00
DST2040	Maintain traffic control and safety plan	39d	100%	0d	18-Aug-14 A	18-Dec-14 A		$0.00	$0.00
DST2050	Remove Exist. concrete ditch	5d	100%	0d	18-Aug-14 A	06-Sep-14 A		$0.00	$0.00
Pipe Installation		100d		0d	19-Aug-14 A	08-Sep-14 A		$206,276.27	$206,286.77
DST2070	Trench excav. for 300 mm Main Pipeline Approx.(950 LM)	14d	100%	0d	19-Aug-14 A	06-Sep-14 A		$18,772.61	$18,772.61
DST2080	Install 300 mm schedule 20 Steel pipe include testing	14d	100%	0d	19-Aug-14 A	06-Sep-14 A		$112,552.32	$112,552.32
DST2072-new	Road Crossing from 9+029.89 to 9+011.17(18.72m)	5d	100%	0d	19-Aug-14 A	19-Aug-14 A		$3,744.00	$3,744.00
DST2090	Casting concrete as encasement around the main pipeline or single size if required	14d	100%	0d	20-Aug-14 A	08-Sep-14 A		$60,942.45	$60,942.45
DST2075-new	Bedding from Sta. 9+005.4 to Sta. 8+814.8 (190.6 m)	14d	100%	0d	21-Aug-14 A	26-Aug-14 A		$3,325.00	$3,335.50
DST2076-new	Backfilling from Sta. 8+945.97 to Sta. 8+814.8 (131.17 m)	14d	100%	0d	21-Aug-14 A	26-Aug-14 A		$2,229.89	$2,229.89
DST2073-new	Road Crossing from Sta. 8+238.26 to Sta. 8+214.66 (23.6)	1d	100%	0d	02-Sep-14 A	02-Sep-14 A		$4,710.00	$4,710.00
Civil Chamber work		14d		0d	06-Sep-14 A	02-Dec-14 A		$74,100.00	$74,100.00
DST2120	Construct - Combination Air Valve chamber (Dia. 100mm) @ Sta.A8+885	14d	100%	0d	06-Sep-14 A	02-Dec-14 A		$14,100.00	$14,100.00
DST2130	Construct Bazzariya connection chamber (Dia. 75mm) at Sta. A8+206	14d	100%	0d	11-Sep-14 A	19-Oct-14 A		$60,000.00	$60,000.00
Testing		99d		0d	14-Aug-14 A	18-Dec-14 A		$0.00	$0.00
DST2132	Radiograph Testing	2d	100%	0d	14-Aug-14 A	14-Aug-14 A		$0.00	$0.00
DST2134	Pressure Testing	2d	100%	0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
Reinstatement		18d		0d	24-Sep-14 A	29-Oct-14 A		$42,255.73	$42,255.73
DST2136	Concrete Reinstatement	8d	100%	0d	24-Sep-14 A	29-Sep-14 A		$35,647.15	$35,647.15
DST2138-new	Asphalt reinstatement from Sta. 9+010 to Sta. 8+855	1d	100%	0d	29-Oct-14 A	29-Oct-14 A		$6,608.58	$6,608.58
Phase Eight 300 mm Main pipeline from Sta. A8+080 to Sta. A6+983 At RHS/ Location Area(C)		104d		0d	06-Sep-14 A	18-Dec-14 A		$512,164.82	$512,164.82
Safety and Remove Exist. concrete ditch		63d		0d	06-Sep-14 A	18-Dec-14 A		$0.00	$0.00
DST2140	Maintain traffic control and safety plan	63d	100%	0d	06-Sep-14 A	18-Dec-14 A		$0.00	$0.00

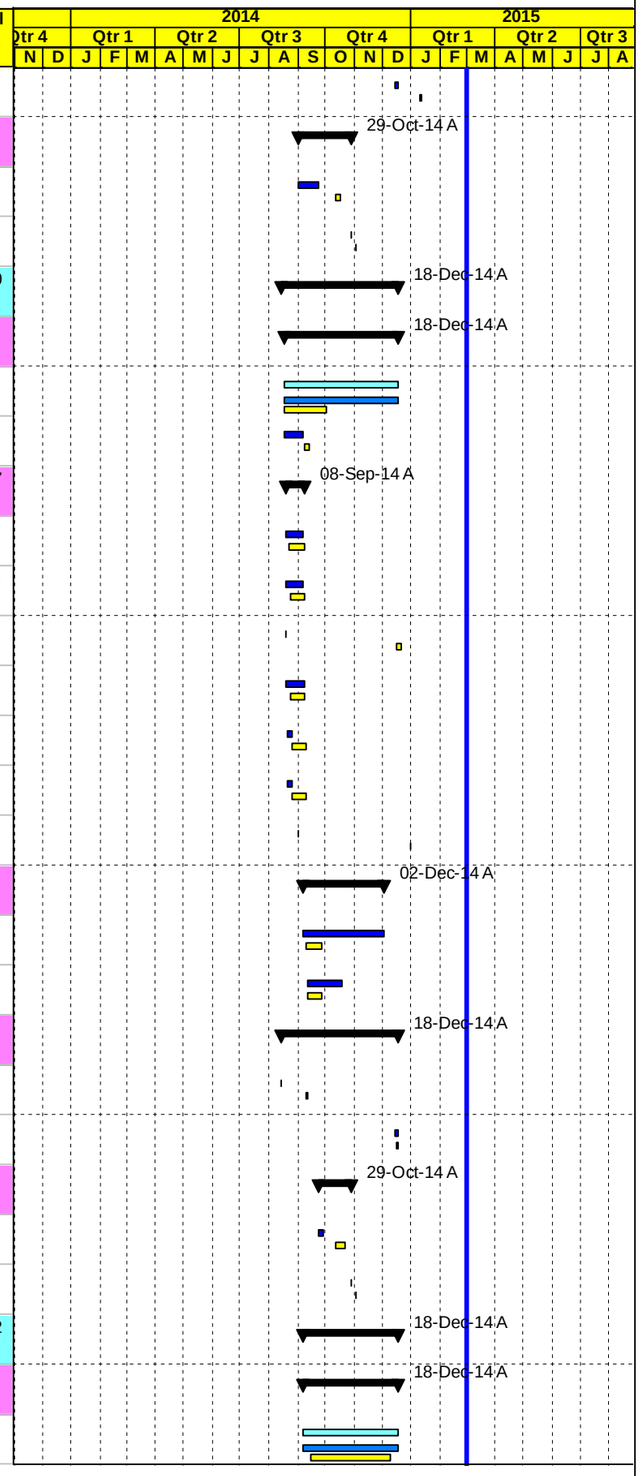

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST2150	Remove Exist. concrete ditch	9d	100%	0d	07-Sep-14 A	21-Sep-14 A		$0.00	$0.00
Pipe Installation		78d		0d	07-Sep-14 A	20-Sep-14 A		$248,672.91	$248,672.91
DST2170	Trench excavation for 300 mm main pipeline length approx. (1097 LM)	14d	100%	0d	07-Sep-14 A	20-Sep-14 A		$21,890.62	$21,890.62
DST2180	Install 300 mm Steel pipe schedule 20 include testing	14d	100%	0d	07-Sep-14 A	20-Sep-14 A		$132,604.36	$132,604.36
DST2275-new	Road Crossing from St. 8+070.64 to St. 8+053.03 (17.61)	6d	100%	0d	07-Sep-14 A	07-Sep-14 A		$3,522.00	$3,522.00
DST2190	Casting concrete as encasement around the main pipeline or single size if required	14d	100%	0d	08-Sep-14 A	20-Sep-14 A		$86,926.10	$86,926.10
DST2195-new	Backfilling from Sta. 7+444 to Sta. 7+406 & Sta. 7+395 to Sta. 7+383	14d	100%	0d	17-Sep-14 A	17-Sep-14 A		$1,572.16	$1,572.16
DST2205-new	Bedding from sta. 7+094 to Sta. 7+020.95	1d	100%	0d	20-Sep-14 A	20-Sep-14 A		$899.67	$899.67
DST2210-new	Backfilling from sta. 7+094 to Sta. 7+020.96	1d	100%	0d	20-Sep-14 A	20-Sep-14 A		$1,258.00	$1,258.00
Civil Chamber work		32d		0d	17-Sep-14 A	02-Dec-14 A		$206,324.15	$206,324.15
DST2230	Construct - Air valve chamber (Dia. 100mm)combined with Butterfly Valve(Dia. 300mm) @ Sta. A7+400	19d	100%	0d	17-Sep-14 A	02-Dec-14 A		$46,039.47	$46,039.47
DST2250	Construct-300 system flow monitoring chamber @ Sta. A7+160	12d	100%	0d	20-Sep-14 A	02-Dec-14 A		$80,000.00	$80,000.00
DST2240	Construct Burqa connection chamber (Dia. 100mm) at Sta. A7+032 & connect to exist. Pipeline	14d	100%	0d	27-Sep-14 A	25-Nov-14 A		$60,000.00	$60,000.00
DST2210	Construct - Wash out chamber (Dia. 150mm) @ Sta. A7+440	14d	100%	0d	29-Sep-14 A	21-Oct-14 A		$20,284.68	$20,284.68
Testing		54d		0d	21-Oct-14 A	18-Dec-14 A		$0.00	$0.00
DST2253	Radiograph Testing	2d	100%	0d	21-Oct-14 A	21-Oct-14 A		$0.00	$0.00
DST2254	Pressure Testing	2d	100%	0d	14-Dec-14 A	18-Dec-14 A		$0.00	$0.00
Reinstatement		40d		0d	29-Sep-14 A	30-Nov-14 A		$57,167.76	$57,167.76
DST2256	Concrete Reinstatement	14d	100%	0d	29-Sep-14 A	30-Nov-14 A		$54,728.07	$54,728.07
DST2266	Asphalt Reinstatement	1d	100%	0d	29-Oct-14 A	29-Oct-14 A		$2,439.69	$2,439.69
Phase Ten 300 mm Main pipeline from Sta. A3+880 to Sta. A3+480		122d		0d	21-Sep-14 A	14-Dec-14 A		$90,720.00	$90,720.00
Safety and Remove Exist. concrete ditch		5d		0d	21-Sep-14 A	14-Dec-14 A		$0.00	$0.00
DST2808-new	Maintain traffic Control and Safety Plan	5d	100%	0d	21-Sep-14 A	14-Dec-14 A		$0.00	$0.00
DST2809-new	Remove Exist. concrete ditch	5d	100%	0d	21-Sep-14 A	24-Sep-14 A		$0.00	$0.00
Pipe Installation		7d		0d	21-Sep-14 A	24-Sep-14 A		$90,720.00	$90,720.00
DST2810-new	Install 300 mm schedule 20 Steel pipe include testing	6d	100%	0d	21-Sep-14 A	24-Sep-14 A		$49,600.00	$49,600.00
DST2835-new	Casting concrete as encasement around the main pipeline or single size if required	6d	100%	0d	21-Sep-14 A	24-Sep-14 A		$34,000.00	$34,000.00
DST2825-new	Trench excavation for 300 mm main pipeline length approx. (400 LM) and road crossing	6d	100%	0d	21-Sep-14 A	24-Sep-14 A		$7,120.00	$7,120.00

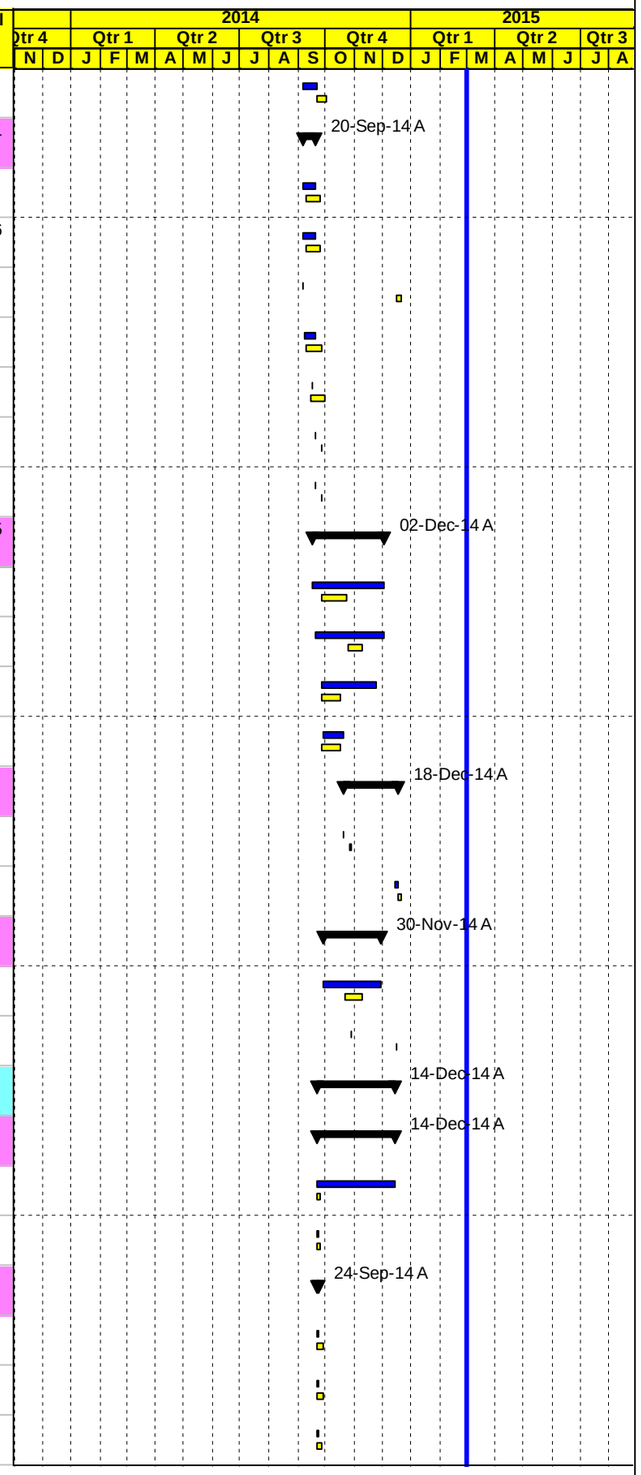

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
Testing		64d		0d	21-Oct-14 A	14-Dec-14 A		$0.00	$0.00
DST2846-new	Radiograph Testing	2d	100%	0d	21-Oct-14 A	21-Oct-14 A		$0.00	$0.00
DST2847-new	Pressure Testing	2d	100%	0d	14-Dec-14 A	14-Dec-14 A		$0.00	$0.00
Reinstatement		0d		0d			0d	$0.00	$0.00
Phase Nine 300 mm Main pipeline from Sta. A1+220 to Sta. A0+019 At RHS/ Location Area(C)		145d		0d	24-Sep-14 A	24-Dec-14 A		$611,594.84	$611,594.84
Safety and Remove Exist. concrete ditch		69d		0d	24-Sep-14 A	20-Dec-14 A		$0.00	$0.00
DST2660	Maintain Traffic Control and Safety Plan	64d	100%	0d	24-Sep-14 A	20-Dec-14 A		$0.00	$0.00
DST2670	Remove Exist. Concrete Ditch	5d	100%	0d	27-Sep-14 A	16-Oct-14 A		$0.00	$0.00
Pipe Installation		20d		0d	27-Sep-14 A	16-Oct-14 A		$259,667.96	$259,667.96
DST2690	Trench excavation for 300 mm main pipeline length approx. (1220 LM) -a	18d	100%	0d	27-Sep-14 A	16-Oct-14 A		$21,397.36	$21,397.36
DST2700	Install 300 mm schedule 20 Steel pipe include testing	19d	100%	0d	27-Sep-14 A	16-Oct-14 A		$151,900.00	$151,900.00
DST2735-new	Bedding from Sta. 1+220 to Sta. 1+032 (188m)	2d	100%	0d	29-Sep-14 A	01-Oct-14 A		$3,963.05	$3,963.05
DST2745-new	Backfilling from Sta. 1+220 to Sta. 1+032 (188m)	2d	100%	0d	29-Sep-14 A	01-Oct-14 A		$3,255.50	$3,255.50
DST2710	Casting concrete as encasement around the main pipeline or single size if required	16d	100%	0d	01-Oct-14 A	16-Oct-14 A		$75,140.00	$75,140.00
DST2747-new	Backfilling from Sta. 0+148 to Sta. 0+054.5 (93.5m)	1d	100%	0d	16-Oct-14 A	16-Oct-14 A		$2,314.55	$2,314.55
DST2746-new	Bedding from Sta. 0+148 to Sta. 0+054.5 (93.5m)	1d	100%	0d	16-Oct-14 A	16-Oct-14 A		$1,697.50	$1,697.50
Civil Chamber work		93d		0d	22-Oct-14 A	24-Dec-14 A		$306,199.78	$306,199.78
DST2740	Construct -Flow control Valve chamber (Dia. 300mm) @ Sta.A1+174	12d	100%	0d	22-Oct-14 A	16-Dec-14 A		$132,345.04	$132,345.04
DST2750	Construct - Air Valve chamber(Dia. 50mm) combined with Butterfly Valve(Dia. 300mm) @A1+162	72d	100%	0d	15-Nov-14 A	21-Dec-14 A		$44,754.74	$44,754.74
DST2757	Construct Shavei Shamron connection chamber at Sta. A1+159 & connect to exist.B.S pipe	23d	100%	0d	18-Nov-14 A	20-Dec-14 A		$80,000.00	$80,000.00
DST2730	Construct - Combination Air Valve chamber (Dia. 100mm) @ 1+107	17d	100%	0d	30-Nov-14 A	09-Dec-14 A		$14,100.00	$14,100.00
DST2760-new	Construct BFV chamber (Dia. 300mm) for outlet Shavi Shamron pipe at Sta. 1+172	24d	100%	0d	07-Dec-14 A	24-Dec-14 A		$35,000.00	$35,000.00
Testing		56d		0d	21-Oct-14 A	14-Dec-14 A		$0.00	$0.00
DST2760	Radiograph Testing	2d	100%	0d	21-Oct-14 A	21-Oct-14 A		$0.00	$0.00
DST2763	Pressure Testing	2d	100%	0d	14-Dec-14 A	14-Dec-14 A		$0.00	$0.00
Reinstatement		11d		0d	05-Nov-14 A	01-Dec-14 A		$45,727.10	$45,727.10
DST2800	Concrete Reinstatement	11d	100%	0d	05-Nov-14 A	01-Dec-14 A		$45,727.10	$45,727.10
Rock Cutting in Slope		26d		0d	28-May-14 A	09-Aug-14 A		$3,034.56	$3,034.56

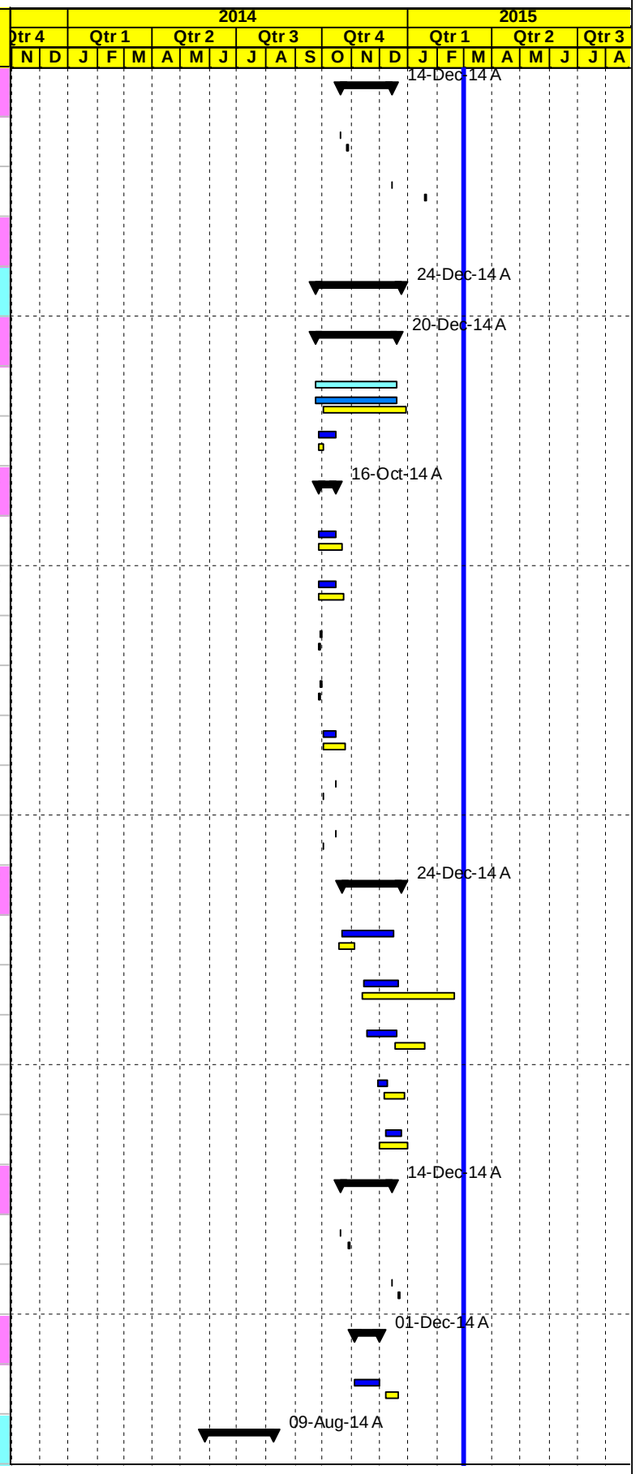

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST1330	Rock Cut Slope Seg. A From Sta (1+430-1+825, 2+020-2+115,4+920-4+980,5+060-5+100,5+750-5+820,6+560-6+620, 6+650-7+740)	26d	100%	0d	28-May-14 A	09-Aug-14 A		$3,034.56	$3,034.56
Segment B & C 150 mm Main pipeline at / Location Area(B)		90d		0d	19-Oct-14 A	27-Dec-14 A		$385,724.03	$385,724.03
Safety and Milling Asphalt		79d		0d	19-Oct-14 A	21-Dec-14 A		$0.00	$0.00
DST1790	Remove Asphalt	4d	100%	0d	19-Oct-14 A	20-Oct-14 A		$0.00	$0.00
DST1780	Maintain traffic control and safety plan	62d	100%	0d	20-Oct-14 A	21-Dec-14 A		$0.00	$0.00
Pipe Installation		32d		0d	20-Oct-14 A	19-Nov-14 A		$268,803.02	$268,803.02
Segment C		32d		0d	20-Oct-14 A	22-Oct-14 A		$23,388.38	$23,388.38
DST1834-new	Pipe encasement from Sta. 0+111.80 to Sta. 0+016	1d	100%	0d	20-Oct-14 A	22-Oct-14 A		$9,430.75	$9,430.75
DST1834	Bedding (single size aggregate) from Sta. 0+126 to Sta. 0+111.80	5d	100%	0d	20-Oct-14 A	20-Oct-14 A		$220.72	$220.72
DST1820	Trench pipes excavation for150 mm length approx. (126 LM) / Segment C	7d	100%	0d	20-Oct-14 A	22-Oct-14 A		$2,206.22	$2,206.22
DST1824	Compact Approved Backfill material ,sub base / base course above pipeline	7d	100%	0d	20-Oct-14 A	22-Oct-14 A		$1,891.05	$1,891.05
DST1822	Install 150 mm schedule 40 Steel pipe include testing	7d	100%	0d	20-Oct-14 A	22-Oct-14 A		$9,639.63	$9,639.63
Segment B		25d		0d	23-Oct-14 A	19-Nov-14 A		$245,414.64	$245,414.64
Double Trench (Sta. 1+000 to Sta. 0+426.94).		25d		0d	23-Oct-14 A	12-Nov-14 A		$192,302.50	$192,302.50
DST1800	Double Trench excavation for150 mm main pipeline length approx. (573.06 LM) / Segment B	11d	100%	0d	23-Oct-14 A	12-Nov-14 A		$14,856.14	$14,856.14
DST1810-new	Bedding (single size aggregate)	11d	100%	0d	23-Oct-14 A	12-Nov-14 A		$4,669.80	$4,669.80
DST3110	Install 150 mm schedule 40 Steel pipe include testing	11d	100%	0d	23-Oct-14 A	12-Nov-14 A		$88,251.24	$88,251.24
DST1842-new	Pipe Encasement	11d	100%	0d	23-Oct-14 A	11-Nov-14 A		$71,808.00	$71,808.00
DST1830	Compact Approved Backfill material ,sub base / base course above pipeline	11d	100%	0d	23-Oct-14 A	12-Nov-14 A		$12,717.32	$12,717.32
Single Trench (Sta. 0+426.94 to Sta. 0+007.24)		13d		0d	23-Oct-14 A	19-Nov-14 A		$53,112.14	$53,112.14
DST3070-new	Single Trench excavation for150 mm main pipeline length (432.95 lm) / Segment B	11d	100%	0d	23-Oct-14 A	19-Nov-14 A		$7,576.63	$7,576.63
DST3080-new	Bedding (single size aggregate)	11d	100%	0d	23-Oct-14 A	19-Nov-14 A		$6,724.36	$6,724.36
DST3100-new	Install 150 mm schedule 40 Steel pipe include testing	11d	100%	0d	23-Oct-14 A	19-Nov-14 A		$32,316.90	$32,316.90
DST3090-new	Compact Approved Backfill material, sub base / base course above pipeline	11d	100%	0d	23-Oct-14 A	19-Nov-14 A		$6,494.25	$6,494.25
Civil Chamber work		30d		0d	20-Nov-14 A	09-Dec-14 A		$45,528.01	$45,528.01
DST1836	Construct -Gate Valve chamber (Dia. 150mm) @ B0+653	5d	100%	0d	20-Nov-14 A	09-Dec-14 A		$14,287.79	$14,287.79
DST1828	Construct - Wash out Valve chamber (Dia. 100mm) @ Al Fonduqamiya Entrance (St. @ B0+010)	15d	100%	0d	20-Nov-14 A	25-Nov-14 A		$16,830.00	$16,830.00
DST1826	Construct -Gate Valve chamber (Dia. 150mm) @B0+384	16d	100%	0d	20-Nov-14 A	09-Dec-14 A		$14,410.22	$14,410.22

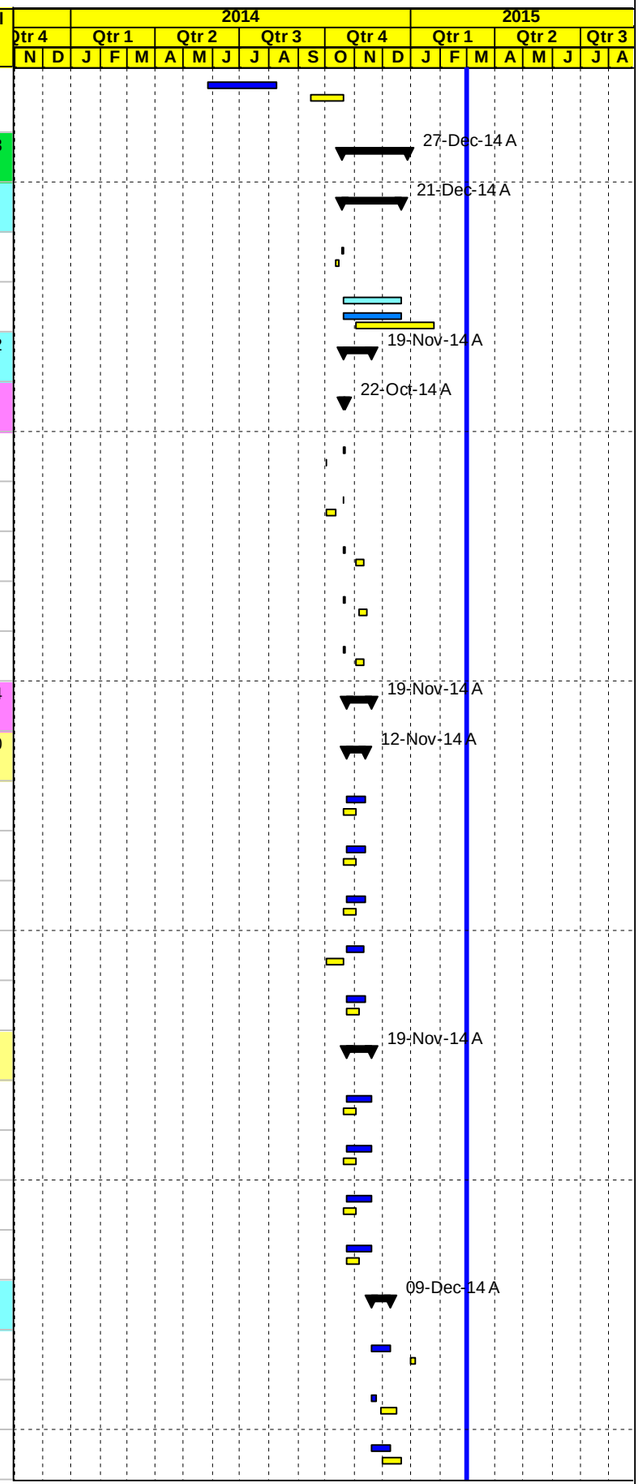

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
Testing		2d		0d	20-Dec-14 A	21-Dec-14 A		$0.00	$0.00
DST1846	Pressure Testing	2d	100%	0d	20-Dec-14 A	21-Dec-14 A		$0.00	$0.00
Reinstatement		4d		0d	25-Dec-14 A	27-Dec-14 A		$71,393.00	$71,393.00
DST1849	Asphalt Reinstatement Seg.B&C	4d	100%	0d	25-Dec-14 A	27-Dec-14 A		$71,393.00	$71,393.00
Connection Valves in TO14		3d		0d	09-Feb-15 A	17-Feb-15 A		$298,525.69	$298,525.69
DST2875	Shavei Shamron connection chamber (Dia. 300mm)	1d	100%	0d	09-Feb-15 A	10-Feb-15 A		$65,000.00	$65,000.00
DST2860	Qussin connection (Dia. 250mm) TO14	1d	100%	0d	10-Feb-15 A	11-Feb-15 A		$57,448.00	$57,448.00
DST2830	Washout chamber (Dia. 250mm)	1d	100%	0d	10-Feb-15 A	17-Feb-15 A		$18,200.00	$18,200.00
DST2840	Combined BFV and AR/AV (dia 75/300)	1d	100%	0d	11-Feb-15 A	11-Feb-15 A		$38,427.69	$38,427.69
DST2850	Beit Iba connection (Dia. 75mm)	1d	100%	0d	12-Feb-15 A	17-Feb-15 A		$65,000.00	$65,000.00
DST2870	Nablus connection (Dia. 100mm)	1d	100%	0d	12-Feb-15 A	15-Feb-15 A		$54,450.00	$54,450.00
Burqa 4" Water Pipeline		29d		0d	15-Jan-15 A	28-Feb-15 A		$224,748.23	$224,748.23
Pipeline installation		11d		0d	15-Jan-15 A	04-Feb-15 A		$145,824.00	$145,824.00
DST2879-new	Delivery steel pipeline 4"	0d	100%	0d	15-Jan-15 A			$0.00	$0.00
DST2880-new	Trench excavation 4" water pipeline Bedding, install and Backfilling approx.(1200 LM)	11d	100%	0d	17-Jan-15 A	04-Feb-15 A		$145,824.00	$145,824.00
Chambers		6d		0d	26-Jan-15 A	17-Feb-15 A		$70,004.00	$70,004.00
DST2900-new	Constuct Gate valve (PN 16 DN 150 mm)gate valve and it is chamber at Al fondaqmia elevated reservoir at Sta. 0+990	3d	100%	0d	26-Jan-15 A	17-Feb-15 A		$13,179.00	$13,179.00
DST2890-new	Constuct Gate valve chamber (PN 16 DN 50 mm) at Al fondaqmia at Sta. 0+410	3d	100%	0d	27-Jan-15 A	17-Feb-15 A		$21,362.00	$21,362.00
DST2895-new	Constuct Gate valve (PN 16 DN 100 mm) at Al fondaqmia at Sta. 0+430	3d	100%	0d	27-Jan-15 A	17-Feb-15 A		$11,221.00	$11,221.00
DST2885-new	Constuct two Gate valve chamber (PN 25 DN 100 mm) at Burqa Sta. 1+150 & Sta. 1+152	3d	100%	0d	05-Feb-15 A	08-Feb-15 A		$23,142.00	$23,142.00
DST2910-new	Connection 4" water pipeline to the existing chamber	3d	100%	0d	10-Feb-15 A	10-Feb-15 A		$1,100.00	$1,100.00
Testing		3d		0d	09-Feb-15 A	09-Feb-15 A		$0.00	$0.00
DST2912-new	Pressure Testing	3d	100%	0d	09-Feb-15 A	09-Feb-15 A		$0.00	$0.00
Reinstatement		5d		0d	25-Feb-15 A	28-Feb-15 A		$8,920.23	$8,920.23
DST2914-new	Asphalt Reinstatement	5d	100%	0d	25-Feb-15 A	28-Feb-15 A		$8,920.23	$8,920.23
Asphalt Works		40d		1d	29-Dec-14 A	01-Mar-15	3d	$651,918.52	$640,273.72
DST2920-new	Asphalt Wearing Layer 70mm Thick for Road Shoulders Including Tack coat inculding milling sta. 1+240 to sta. 8+200	21d	100%	0d	29-Dec-14 A	08-Feb-15 A		$553,470.52	$553,470.52
DST2930-new	Acrylic Paint for Road Marking	5d	90%	1d	25-Jan-15 A	01-Mar-15	4d	$80,448.00	$72,403.20

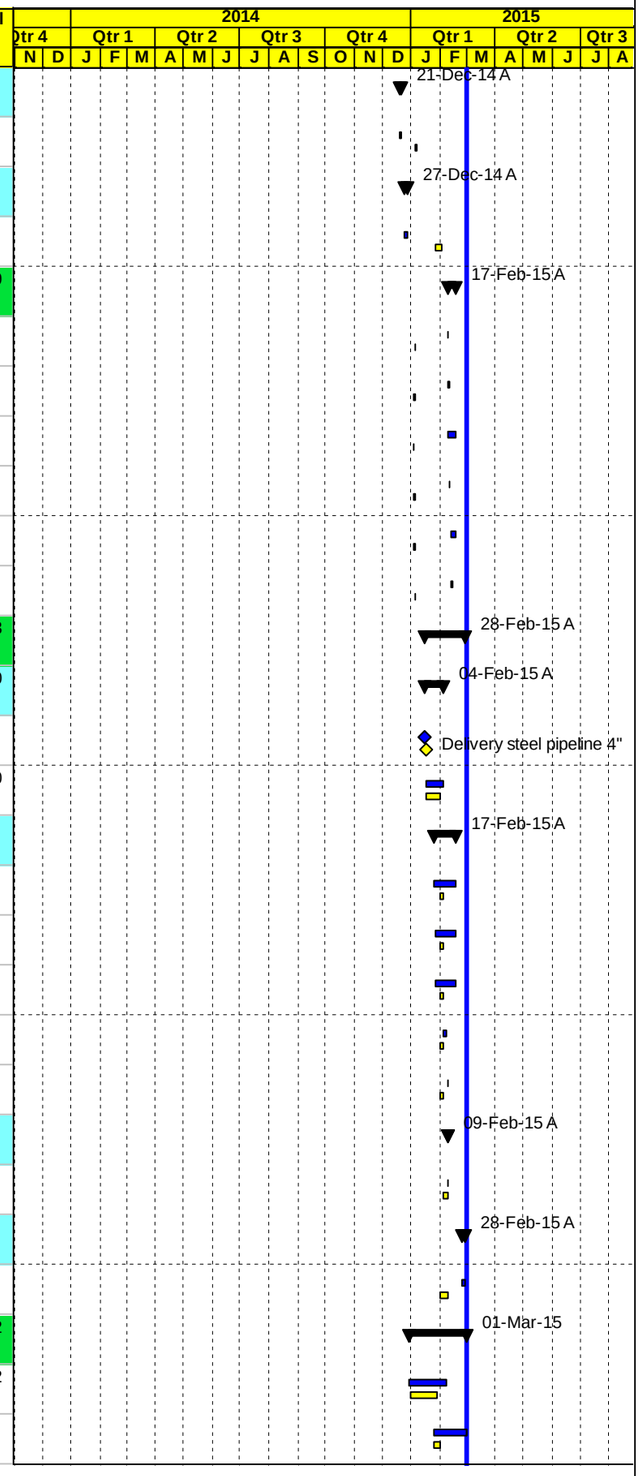

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST2934-new	Cat eyes installation LHS & RHS shoulders main line from Sta. 1+240 to Sta. 13+700	5d	80%	1d	17-Feb-15 A	01-Mar-15	3d	$18,000.00	$14,400.00
Sewer Pipeline from Sta. 0+000 Sta. 0+260		9d		0d	13-Jan-15 A	18-Jan-15 A		$50,919.20	$50,919.20
DST2940-new	Excavation 8" UPVC sewer pipelines Bedding, Install and Backfilling including precast concrete manhole (1000 dia)	8d	100%	0d	13-Jan-15 A	18-Jan-15 A		$50,419.20	$50,419.20
DST2950-new	Connection to the existing sewer manhole	1d	100%	0d	18-Jan-15 A	18-Jan-15 A		$500.00	$500.00
Main Pipeline from Sta. A0+000 to Sta. A13+732, Segment B & C Final works		127d		2d	03-Jun-14 A	03-Mar-15	8d	$132,440.38	$131,959.68
DST2886	Archeological findings	4d	100%	0d	03-Jun-14 A	05-Jun-14 A		$7,246.38	$7,246.38
DST3000-new	Finishing work for chambers internal body included ladders (Part one 18 chambers)	21d	100%	0d	23-Nov-14 A	31-Dec-14 A		$0.00	$0.00
DST2890	Mech. Work including install valves fittings, and flushing pipes (Part one 12 chambers)	16d	100%	0d	08-Dec-14 A	31-Dec-14 A		$0.00	$0.00
DST3050-new	Finishing work for chambers internal body included ladders (Part two 18 chambers)	21d	90%	2d	01-Jan-15 A	03-Mar-15	6d	$0.00	$0.00
DST2900	Mech. Work including install valves fittings, and flushing pipes (Part Two 12 chambers)	15d	100%	0d	01-Jan-15 A	28-Jan-15 A		$0.00	$0.00
DST3010-new	Pipeline Marking	10d	95%	1d	26-Jan-15 A	01-Mar-15	4d	$9,614.00	$9,133.30
DST3120	Mech. Work including install valves fittings, and flushing pipes (Part Three 12 chambers)	15d	100%	0d	29-Jan-15 A	17-Feb-15 A		$80,580.00	$80,580.00
DST1840	Connection to the existing WSP and elevated tank	2d	100%	0d	08-Feb-15 A	26-Feb-15 A		$25,000.00	$25,000.00
DST2910	Disinfection and flushing For Pipeline	3d	100%	0d	23-Feb-15 A	25-Feb-15 A		$10,000.00	$10,000.00
Upgrade the Remote Flow Monitoring GBRS/GSM System		49d		8d	25-Jan-15 A	08-Mar-15	2d	$67,230.00	$67,230.00
DST3015-new	Design Remote Flow Monitoring GBRS/GSM System	6d	100%	0d	25-Jan-15 A	27-Jan-15 A		$0.00	$0.00
DST3020-new	Order Remote Flow Monitoring GBRS/GSM System	0d	100%	0d	28-Jan-15 A			$0.00	$0.00
DST3030-new	Delivery	0d	100%	0d	01-Feb-15 A			$0.00	$0.00
DST3040-new	Installation	9d	100%	0d	01-Feb-15 A	26-Feb-15 A		$67,230.00	$67,230.00
DST3060-new	Testing Commissioning and training	6d	0%	6d	01-Mar-15	08-Mar-15	2d	$0.00	$0.00
Post Construction Phase		10d		10d	01-Feb-15 A	10-Mar-15	0d	$61,990.80	$0.00
Post Construction Submittals		0d		0d	01-Feb-15 A	10-Mar-15	0d	$0.00	$0.00
DST2930	Start preparation Operation and maintenance manual	0d	100%	0d	01-Feb-15 A			$0.00	$0.00
DST2940	Start preparation Training completion document	0d	0%	0d	10-Mar-15		0d	$0.00	$0.00
DST2950	Start preparation Warranties (to USAID)	0d	0%	0d	10-Mar-15		0d	$0.00	$0.00
DST2960	Start preparation Final Acceptance Certificate	0d	0%	0d	10-Mar-15		0d	$0.00	$0.00
DST2970	Start preparation Release of liens and waiver of debts and claims againts the government	0d	0%	0d	10-Mar-15		0d	$0.00	$0.00
DST2980	Start preparation Final payment	0d	0%	0d	10-Mar-15		0d	$0.00	$0.00

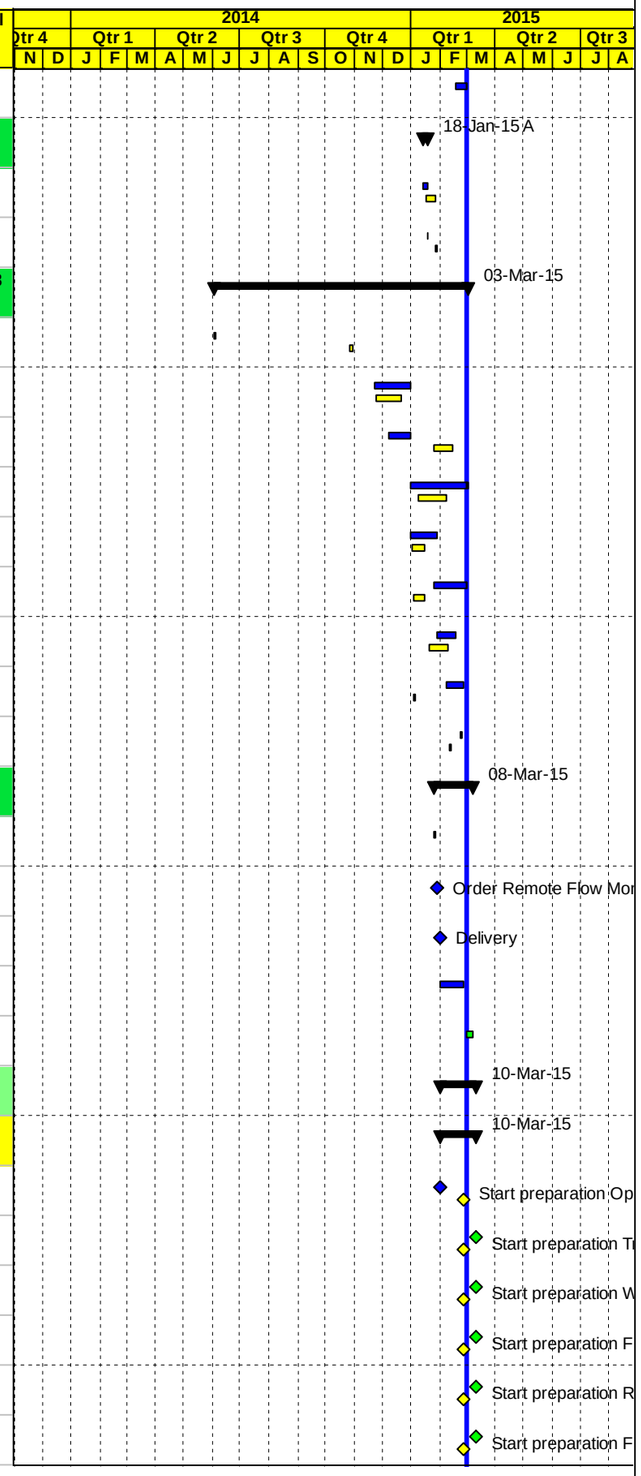

Project Baseline Bar | Baseline Milestone | Actual Level of Effort | Level of Effort
Level of effort Baseline | Actual Work | Early Bar | Summary
Milestone Early Bar | Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Updated Construction Program

February 28, 2015

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float	Budgeted Total Cost	Actual Total Cost
DST2990	Start preparation Final Report	0d	0%	0d	10-Mar-15		0d	$0.00	$0.00
DST3010	Start preparation certificate from local entities/ Authorities invloved	0d	0%	0d	10-Mar-15		0d	$0.00	$0.00
Start up, Training and commissioning		10d		10d	23-Feb-15 A	10-Mar-15	0d	$0.00	$0.00
DST3030	Pre-commissioning	5d	100%	0d	23-Feb-15 A	26-Feb-15 A		$0.00	$0.00
DST3070	Training	5d	0%	5d	01-Mar-15	05-Mar-15	0d	$0.00	$0.00
DST3020	commissioning	5d	0%	5d	06-Mar-15	10-Mar-15	0d	$0.00	$0.00
Demobilization		1d		1d	10-Mar-15	10-Mar-15	0d	$61,990.80	$0.00
DST3040	Start Demobilization and submitting close-out documents including as-built drawings	1d	0%	1d	10-Mar-15	10-Mar-15	0d	$61,990.80	$0.00
Post Construction activities		5d		5d	06-Mar-15	10-Mar-15	0d	$0.00	$0.00
DST3050	Walk through and check Punch list	5d	0%	5d	06-Mar-15	10-Mar-15	0d	$0.00	$0.00
DST3060	Start preparation as-built drawings	0d	0%	0d		10-Mar-15	0d	$0.00	$0.00

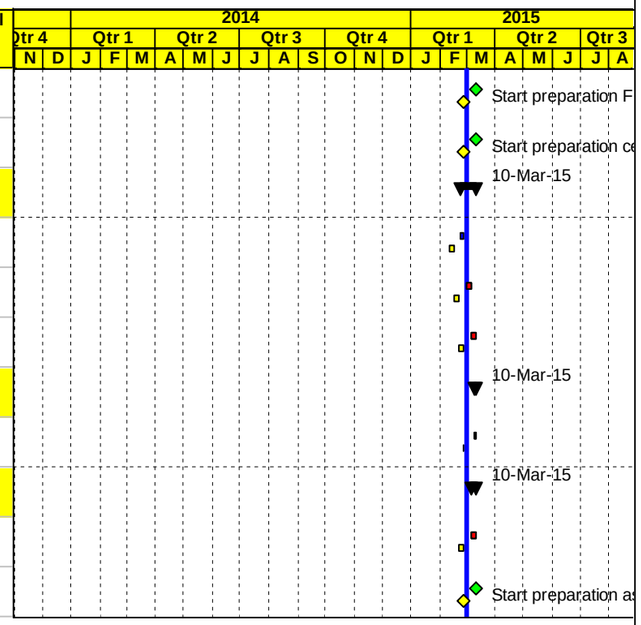

Project Baseline Bar
Level of effort Baseline
Milestone Early Bar
Baseline Milestone
Actual Work
Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

B | One Month Look ahead

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program

One Month Lookahead

TO13-Updated

Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Deir- Sharaf Main Pipeline Project		463d		03-Dec-13 A	10-Mar-15	0d
Milestones		463d		03-Dec-13 A	10-Mar-15	0d
General milestone		0d		10-Mar-15	10-Mar-15	0d
DST0010	Completion Project	0d	0%		10-Mar-15	0d
Task Order Duration		450d		03-Dec-13 A	10-Mar-15	0d
DST0020	Project Duration (Calendar Days)	450d	97.78%	03-Dec-13 A	10-Mar-15	0d
DST0030	Project Duration (Working Days)	343d	97.7%	03-Dec-13 A	10-Mar-15	0d
Pre Construction Milestones		0d				0d
Mobilization Milestones		0d				0d
Shop Drawing Milestones		0d				0d
Material Milestones		0d		03-Mar-15	03-Mar-15	6d
DST0110	Finish Material submittal	0d	0%		03-Mar-15	6d
Construction Milestones		0d		02-Mar-15	02-Mar-15	3d
DST0120	Finish Construction	0d	0%	02-Mar-15		3d
Pre Construction Phase		0d				0d
Pre Construction Submittals		0d				0d
Mobilization		0d				0d
Conformed Drawings and Coordination		0d				0d
Construction Phase		49d		01-Jan-15 A	08-Mar-15	2d
Construction Submittals		28d		18-Jan-15 A	03-Mar-15	8d
Shop Drawing Submittals		0d				0d
Waterline		0d				0d
Sewer Line		0d				0d
Rock Cutting in Slope		0d				0d
Connection and Valves Chambers		0d				0d
Material Submittals including Manufacturers Qualifications , Shop Test, Product Data		28d		18-Jan-15 A	03-Mar-15	8d
Material Submittals Pipelines including Hydraulic calculation and wiring diagrams, labeling schedule		21d		18-Jan-15 A	03-Mar-15	6d
DST0310-new	Sewer Manhole Cover 60cm clear opening	21d	90%	18-Jan-15 A	03-Mar-15	6d
Material Submittals civil		0d				0d
Procurements		0d				0d
Order		0d				0d
Manufacturing		0d				0d
Delivery		0d				0d
Testing		0d				0d
Construction Work		49d		01-Jan-15 A	08-Mar-15	2d
Implement traffic control		0d				0d
Main pipeline		49d		01-Jan-15 A	08-Mar-15	2d
Segment A		0d				0d
Segment B & C 150 mm Main pipeline at / Location Area(B)		0d				0d
Connection Valves in TO14		0d				0d
Burqa 4" Water Pipeline		0d				0d
Asphalt Works		23d		25-Jan-15 A	01-Mar-15	3d
DST2930-new	Acrylic Paint for Road Marking	5d	90%	25-Jan-15 A	01-Mar-15	4d
DST2934-new	Cat eyes installation LHS & RHS shoulders main line from Sta. 1+240 to Sta. 13+700	5d	80%	17-Feb-15 A	01-Mar-15	3d
Sewer Pipeline from Sta. 0+000 Sta. 0+260		0d				0d
Main Pipeline from Sta. A0+000 to Sta. A13+732, Segment B & C Final works		21d		01-Jan-15 A	03-Mar-15	6d
DST3050-new	Finishing work for chambers internal body included ladders (Part two 18 chambers)	21d	90%	01-Jan-15 A	03-Mar-15	6d
DST3010-new	Pipeline Marking	10d	95%	26-Jan-15 A	01-Mar-15	4d
Upgrade the Remote Flow Monitoring GBRS/GSM System		6d		01-Mar-15	08-Mar-15	2d
DST3060-new	Testing Commissioning and training	6d	0%	01-Mar-15	08-Mar-15	2d
Post Construction Phase		10d		01-Mar-15	10-Mar-15	0d
Post Construction Submittals		0d		10-Mar-15	10-Mar-15	0d

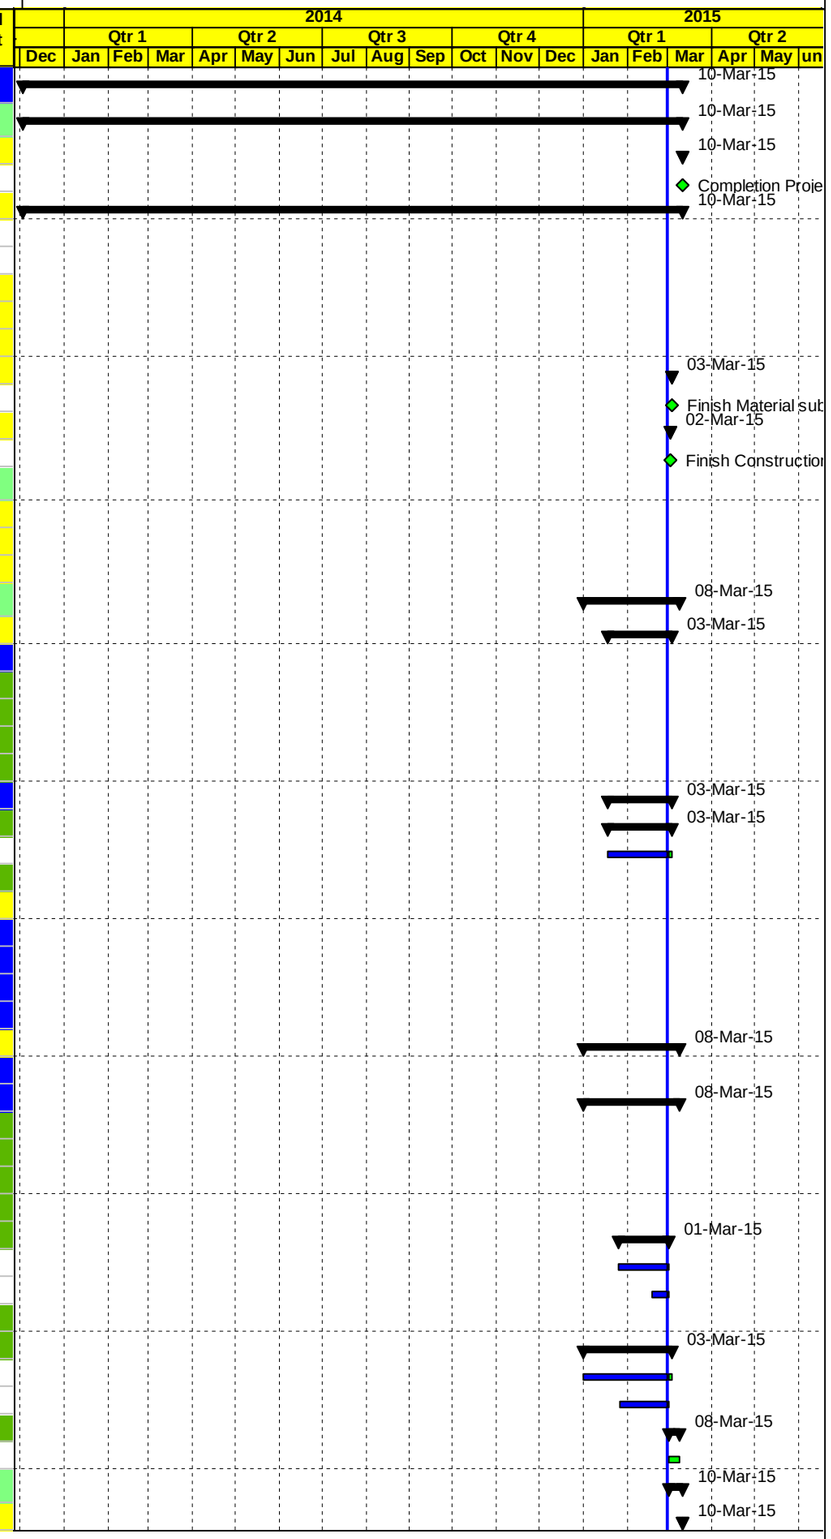

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program

One Month Lookahead

TO13-Updated

Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DST2940	Start preparation Training completion document	0d	0%	10-Mar-15		0d
DST2950	Start preparation Warranties (to USAID)	0d	0%	10-Mar-15		0d
DST2960	Start preparation Final Acceptance Certificate	0d	0%	10-Mar-15		0d
DST2970	Start preparation Release of liens and waiver of debts and claims againts the government	0d	0%	10-Mar-15		0d
DST2980	Start preparation Final payment	0d	0%	10-Mar-15		0d
DST2990	Start preparation Final Report	0d	0%	10-Mar-15		0d
DST3010	Start preparation certificate from local entities/ Authorities invloved	0d	0%	10-Mar-15		0d
Start up, Training and commissioning		10d		01-Mar-15	10-Mar-15	0d
DST3070	Training	5d	0%	01-Mar-15	05-Mar-15	0d
DST3020	commissioning	5d	0%	06-Mar-15	10-Mar-15	0d
Demobilization		1d		10-Mar-15	10-Mar-15	0d
DST3040	Start Demobilization and submitting close-out documents including as-built drawings	1d	0%	10-Mar-15	10-Mar-15	0d
Post Construction activities		5d		06-Mar-15	10-Mar-15	0d
DST3050	Walk through and check Punch list	5d	0%	06-Mar-15	10-Mar-15	0d
DST3060	Start preparation as-built drawings	0d	0%		10-Mar-15	0d

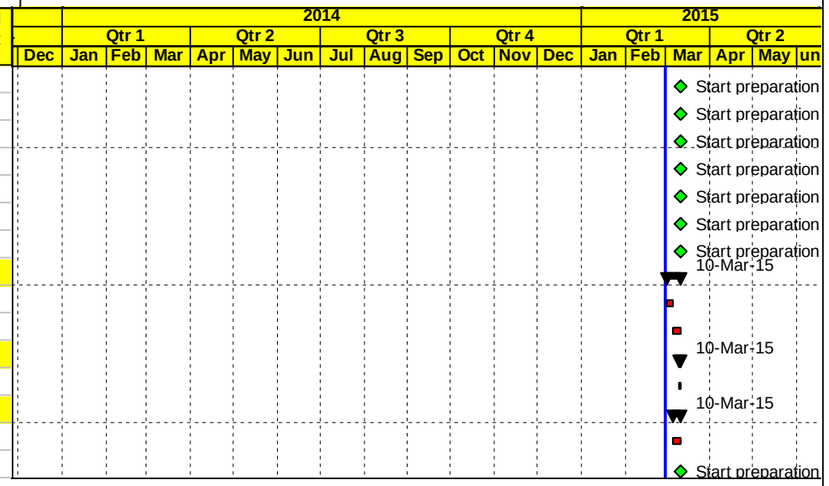

Actual Work | Early Bar | Critical Bar | Milestone | Summary

Page 2 of 2

Date	Revision	Checked	Approved
04-Mar-15			

APCO ArCon
CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Deir- Sharaf Main Pipeline Project		463d		03-Dec-13 A	10-Mar-15	0d
Milestones		450d		03-Dec-13 A	10-Mar-15	0d
General milestone		0d		03-Dec-13 A	03-Dec-13 A	
DST0000	Start Date NTP	0d	100%	03-Dec-13 A		
Task Order Duration		450d		03-Dec-13 A	10-Mar-15	0d
DST0020	Project Duration (Calendar Days)	450d	97.78%	03-Dec-13 A	10-Mar-15	0d
DST0030	Project Duration (Working Days)	343d	97.7%	03-Dec-13 A	10-Mar-15	0d
Pre Construction Milestones		254d		08-Dec-13 A	25-Jan-15 A	
DST0050	Start Preconstruction Submittal	0d	100%	08-Dec-13 A		
DST0060	Finish Preconstruction Submittal	0d	100%		25-Jan-15 A	
Mobilization Milestones		0d		04-Dec-13 A	14-Jan-14 A	
DST0070	Start Mobilization	0d	100%	04-Dec-13 A		
DST0080	Finish Mobilization	0d	100%		14-Jan-14 A	
Shop Drawing Milestones		296d		02-Feb-14 A	27-Jan-15 A	
DST0090	Start Shop Drawing Submittal	0d	100%	02-Feb-14 A		
DST0100	Finish Shop Drawing Submittal	0d	100%		27-Jan-15 A	
Material Milestones		0d		25-Dec-13 A	25-Dec-13 A	
DST0105	Start Material Submittal	0d	100%	25-Dec-13 A		
Construction Milestones		0d		26-Mar-14 A	26-Mar-14 A	
DST0115	Start Construction (Ground Breaking)	0d	100%	26-Mar-14 A		
Pre Construction Phase		426d		03-Dec-13 A	25-Jan-15 A	
Pre Construction Submittals		299d		08-Dec-13 A	25-Jan-15 A	
DST0170	Bank Guarantee Certificates	10d	100%	08-Dec-13 A	31-Dec-13 A	
DST0160	Scheduling Qualification Submittals	10d	100%	08-Dec-13 A	22-Dec-13 A	
DST0180	Submittals Schedule	10d	100%	19-Dec-13 A	04-Feb-14 A	
DST0240	Subcontractors' profile	10d	100%	22-Dec-13 A	31-Dec-13 A	
DST0270	60-Day Plan of Operation	10d	100%	22-Dec-13 A	31-Dec-13 A	
DST0280	Project Overview Bar Chart	10d	100%	22-Dec-13 A	31-Dec-13 A	
DST0200	Testing Lab	10d	100%	23-Dec-13 A	02-Jan-14 A	
DST0173	Field Offices Location & Layout	10d	100%	23-Dec-13 A	31-Dec-13 A	
DST0399	Safety Trench plan	10d	100%	25-Dec-13 A	20-Jan-14 A	
DST0210	Key Personnel Plan	10d	100%	25-Dec-13 A	31-Dec-13 A	
DST0290	QCP-Quality Control Program	10d	100%	25-Dec-13 A	13-Jan-14 A	
DST0300	Safety Plan	10d	100%	25-Dec-13 A	20-Jan-14 A	
DST0370	Material Staging ,Storage and dumping Areas Plan	10d	100%	25-Dec-13 A	31-Dec-13 A	
DST0310	USAID Branding Plan	10d	100%	25-Dec-13 A	09-Jan-14 A	
DST0230	Insurances	10d	100%	25-Dec-13 A	07-Jan-14 A	
DST0177	Field Offices Furniture & Equipment Plan	10d	100%	25-Dec-13 A	31-Dec-13 A	
DST0340	Method Statement including asphalt disposal,pipeline install,formworks,curing,storm sys.,&R. mark	10d	100%	29-Dec-13 A	23-Jan-14 A	
DST0304	Environmental Mitigation Plan	10d	100%	29-Dec-13 A	09-Jan-14 A	
DST0306	CPM-Construction Schedule and S-Curve	10d	100%	29-Dec-13 A	24-Feb-14 A	
DST0350	Coordination with local Authorities Plan including list of permits & and licenses	10d	100%	30-Dec-13 A	09-Jan-14 A	
DST0204	Temporary and Permanent Project Sign Plan	10d	100%	30-Dec-13 A	31-Dec-13 A	
DST0250	Existing Survey Plan	10d	100%	02-Jan-14 A	13-Jan-14 A	
DST0320	Dilapidation Survey	10d	100%	02-Jan-14 A	12-Jan-14 A	
DST0390	Traffic Control Plan Phase I	10d	100%	05-Jan-14 A	16-Jan-14 A	
DST0415	Welders qualification	10d	100%	20-Jan-14 A	26-Jan-14 A	
DST0393	Welding procedure	10d	100%	23-Jan-14 A	20-Mar-14 A	
DST0330	Risk Management Plan	10d	100%	26-Jan-14 A	04-Feb-14 A	
DST0410	Third party testing lab -Arc-Eyes	10d	100%	26-Jan-14 A	30-Jan-14 A	
DST0396	Public relation plan	10d	100%	27-Jan-14 A	30-Jan-14 A	
DST0415-new	Pipeline trenching method statement	10d	100%	13-Feb-14 A	02-Apr-14 A	
DST0416-new	Pipe Installation method statement	10d	100%	16-Feb-14 A	02-Mar-14 A	

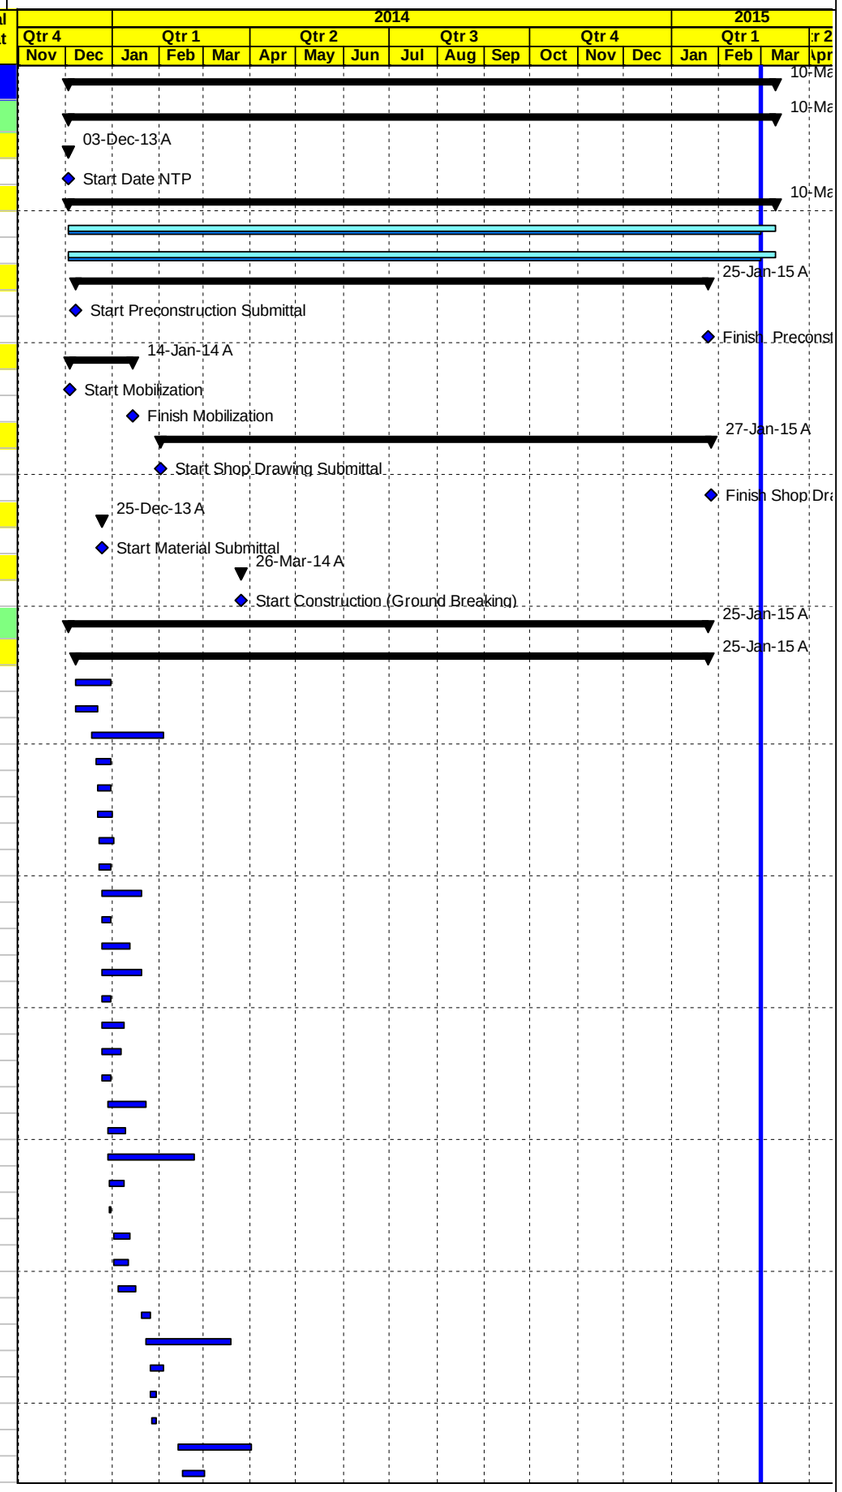

◇ Milestone Early Bar
Actual Work
◆ Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program

Completed & In Progress Activities

TO13-Updated

Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DST0418-new	Method Statement for Filling & Repair The Conical Tie Rods Holes In The Concrete	10d	100%	24-Feb-14 A	13-Mar-14 A	
DST0419-new	Radiographic Testing Safety Plan	10d	100%	04-Mar-14 A	02-Apr-14 A	
DST0420-new	8-12 inch Procedure Qualification Record (PQR)	10d	100%	05-Mar-14 A	20-Mar-14 A	
DST0422-new	Radiographic Testing (RT) Method Statement	10d	100%	16-Mar-14 A	20-Mar-14 A	
DST0423-new	Approved Temporary Traffic Plan by DCL (Area C)	10d	100%	02-Apr-14 A	15-Apr-14 A	
DST0425-new	Work Zone Traffic Control and Operations at Night (Specific Night Work Safety Plan)	10d	100%	13-Jul-14 A	03-Aug-14 A	
DST0426-new	Cleaning, washing, hydraulic test and disinfection plan	10d	100%	12-Nov-14 A	08-Dec-14 A	
DST0427-new	Second Source for Third Party Testing	10d	100%	21-Jan-15 A	25-Jan-15 A	
Mobilization		85d		04-Dec-13 A	03-Feb-14 A	
DST0420	Mobilization Total Cost (4.0%)	20d	100%	04-Dec-13 A	16-Jan-14 A	
DST0460	Start Preparation Construction Submittals (Survey plan , Shop Drawings & Materials)	8d	100%	21-Dec-13 A	31-Dec-13 A	
DST0480	Supply and install Office IT Equipments & Applience	2d	100%	07-Jan-14 A	03-Feb-14 A	
DST0470	Supply and install Office Furniture's and Supplies	2d	100%	07-Jan-14 A	03-Feb-14 A	
DST0430	Site Hand Over	1d	100%	08-Jan-14 A	08-Jan-14 A	
DST0440	Checking With CMC Existing-Bench Marks, Survey Control Points	2d	100%	12-Jan-14 A	12-Jan-14 A	
DST0490	Install Temporary Project Sign	1d	100%	14-Jan-14 A	16-Jan-14 A	
Conformed Drawings and Coordination		40d		03-Dec-13 A	15-May-14 A	
DST0495	Coordination with Israeli authorities for approval and permit area C	40d	100%	03-Dec-13 A	15-May-14 A	
DST0492	Final for Construction Drawing (Conformed)	1d	100%	03-Dec-13 A	03-Dec-13 A	
Construction Phase		435d		25-Dec-13 A	03-Mar-15	8d
Construction Submittals		330d		25-Dec-13 A	03-Mar-15	6d
Shop Drawing Submittals		296d		02-Feb-14 A	27-Jan-15 A	
Waterline		295d		02-Feb-14 A	12-Jan-15 A	
DST0590	Waterline 300 mm Main pipeline from Sta. A10+400 to Sta. A12+120 At RHS	21d	100%	02-Feb-14 A	09-Apr-14 A	
DST0605	Waterline 300 mm Main pipeline from Sta. A10+400 to Sta. A9+700 At RHS	21d	100%	23-Mar-14 A	09-Apr-14 A	
DST0600	Waterline 300 mm Main pipeline from Sta. A12+120 to Sta. A13+580 At LHS	21d	100%	08-Apr-14 A	30-Apr-14 A	
DST0595	Waterline 150 mm Main pipeline at Segment B	21d	100%	28-Apr-14 A	21-May-14 A	
DST0650-new	Waterline 300 mm Main pipeline From St.13+560 To St.13+725	21d	100%	06-May-14 A	21-May-14 A	
DST0655-new	Waterline 300 mm Main pipeline From St.5+000 To St.7+010	21d	100%	12-May-14 A	27-May-14 A	
DST0615	Waterline 300 mm Main pipeline from Sta. A2+900 to Sta. A5+000 At RHS	21d	100%	01-Jun-14 A	12-Jun-14 A	
DST0625	Waterline 300 mm Main pipeline from Sta. A1+100 To St. A2+900 At RHS	21d	100%	10-Jun-14 A	01-Jul-14 A	
DST0610	Waterline 300 mm Main pipeline from Sta. A7+020 to Sta. A9+700 At LHS	21d	100%	14-Jul-14 A	04-Aug-14 A	
DST0620	Waterline 300 mm Main pipeline from Sta. 0+034 to Sta. 1+250	21d	100%	02-Sep-14 A	15-Sep-14 A	
DST0660-new	Waterline 100 mm Main pipeline Burqa From St. 0+000 To St. 1+135	21d	100%	30-Dec-14 A	12-Jan-15 A	
Sewer Line		21d		28-Dec-14 A	06-Jan-15 A	
DST0665-new	8" Sewer Line From Sta. 0+000 to Sta. 0+260	21d	100%	28-Dec-14 A	06-Jan-15 A	
Rock Cutting in Slope		21d		15-Jun-14 A	03-Jul-14 A	
DST0585	Cut Slope Seg. A From Sta (1+430-1+825, 2+020-2+115,4+920-4+980,5+060-5+100,5+750-5+820,6+560-6+62	21d	100%	15-Jun-14 A	03-Jul-14 A	
Connection and Valves Chambers		208d		27-Mar-14 A	27-Jan-15 A	
DST0630	Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 9+700 to 12+120	21d	100%	27-Mar-14 A	09-Jun-14 A	
DST0680-new	Structural & Mechanical detail for valve chambers- From Sta. 5+000 to Sta. 7+000 & from Sta.12+000 to 13+700	21d	100%	08-Jun-14 A	12-Jun-14 A	
DST0670	Al Asasa connection chamber at Sta. A13+600 & connect to exist. Pipes	21d	100%	15-Jun-14 A	06-Aug-14 A	
DST0640	Sielat AL Dahir connection chamber at Sta. A10+420	21d	100%	15-Jun-14 A	06-Aug-14 A	
DST0645-new	Structural & Mechanical Detail for Valve Chambers for (Water Pipeline) From Sta. 2+000 to 5+000	21d	100%	22-Jul-14 A	24-Nov-14 A	
DST0646-new	Structural & Mechanical Detail for Valve Chambers for (Water Pipeline) for Seg. B	21d	100%	22-Jul-14 A	12-Aug-14 A	
DST0647-new	Structural & Mechanical Detail for Valve Chambers for (Water Pipeline) From 1+000 to 2+900 & From Sta. 7+000	21d	100%	03-Aug-14 A	21-Aug-14 A	
DST0710	Sabastia Connection Chamber at Sta. A2+280 & Connect to Exist.WSP	21d	100%	04-Aug-14 A	28-Aug-14 A	
DST0650	Al Fondaqumiya Connection Chamber at Sta. A12+120	21d	100%	04-Aug-14 A	28-Aug-14 A	
DST0690	Burqa Connection Chamber at Sta. A7+032 & Connect to Exist. Pipeline	21d	100%	12-Aug-14 A	10-Sep-14 A	
DST0700	Structural & Mechanical detail for Flow Water Meter connection chamber @ Sta.7+180	21d	100%	12-Aug-14 A	15-Sep-14 A	
DST0680	Bazzariya Connection Chamber at Sta. A8+230 & Connect to Exist.WSP	21d	100%	12-Aug-14 A	10-Sep-14 A	
DST0720	Structural & Mechanical Detail for Water Meter Connection Chamber at Sta. 1+156	21d	100%	08-Sep-14 A	28-Oct-14 A	
DST0740-new	Structural & Mechanical Detail for Flow Control Connection Chamber at Sta. 1+170	21d	100%	09-Sep-14 A	02-Oct-14 A	
DST0750-new	Structural & Mechanical Detail for Valve Chambers For (Water Pipeline) From Sta. 0+034 To 1+250	21d	100%	14-Sep-14 A	02-Oct-14 A	

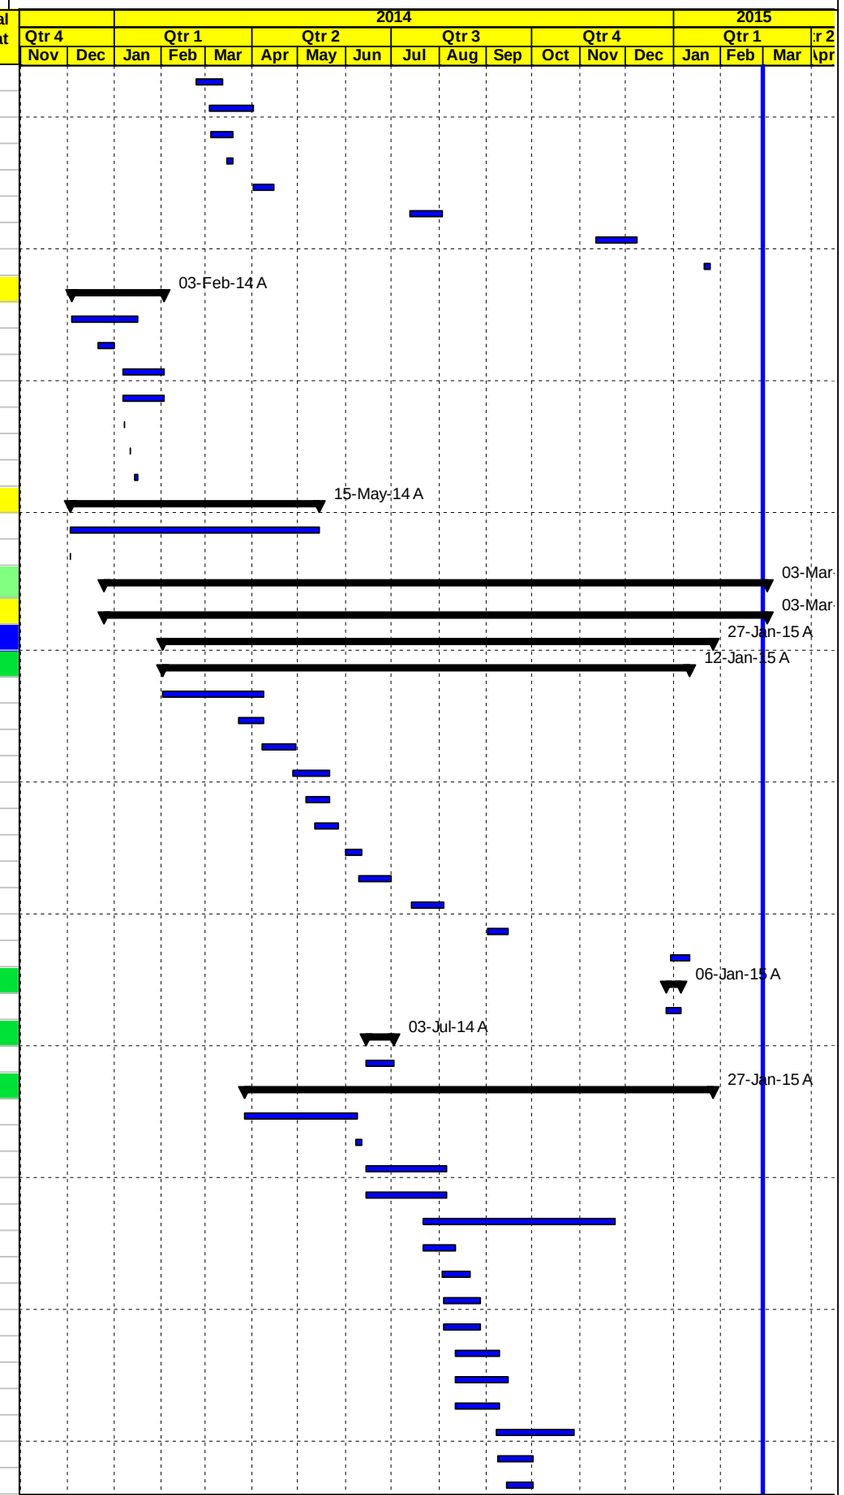

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program

Completed & In Progress Activities

TO13-Updated

Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DST0778-new	Mechanical Detail For 250 mm Washout Sta. 0+90 & AV/AR Chamber Sta. 0+365 in TO #14	21d	100%	14-Sep-14 A	25-Sep-14 A	
DST0770	Mechanical Detail for Shavi Shomron Main System Flow Monitoring Chamber at Sta. A 1+870 (TO.14)	21d	100%	16-Sep-14 A	25-Sep-14 A	
DST0760	Beit Iba Connection Chamber @ St. Seg. B 0+342	21d	100%	18-Sep-14 A	02-Oct-14 A	
DST0768	Nablus Connection Chamber @ St. B 0+040	21d	100%	18-Sep-14 A	02-Oct-14 A	
DST0780-new	Mechanical Detail For Combined Butterfly & Av/Ar Chamber Sta. 0+810 Beit Iba Road	21d	100%	21-Sep-14 A	05-Nov-14 A	
DST0764	Qusin Flow Monitoring Chamber @St. 0+184	21d	100%	27-Oct-14 A	01-Dec-14 A	
DST0785-new	Structural & Mechanical Detail for New Location of Selit Aldaher Connection	21d	100%	04-Nov-14 A	18-Nov-14 A	
DST0786-new	Mechanical Detail for 250 Mm Washout Sta. 0+038- in TO# 14	21d	100%	23-Nov-14 A	30-Nov-14 A	
DST0788-new	6"&4" G.V Al-Foundqumieh @0+990, 2*2" G.V Al-Foundqumieh @0+410 & 0+430 &2*4" G.V Bourqa @1+120	21d	100%	18-Jan-15 A	27-Jan-15 A	
Material Submittals including Manufacturers Qualifications , Shop Test, Product Data		330d		25-Dec-13 A	03-Mar-15	6d
Material Submittals Pipelines including Hydraulic calculation and wiring diagrams, labeling schedule		330d		25-Dec-13 A	03-Mar-15	6d
DST0780	Steel pipeline 300 mm	21d	100%	25-Dec-13 A	05-Jan-14 A	
DST0790	Steel pipeline 150 mm	21d	100%	25-Dec-13 A	05-Jan-14 A	
DST0792	Pipe Fittings	21d	100%	16-Jan-14 A	09-Feb-14 A	
DST0797	Gate Valves PN 40	21d	100%	20-Jan-14 A	26-Jan-14 A	
DST0895	Dismantling joints	21d	100%	20-Jan-14 A	28-Jan-14 A	
DST0798	Butterfly valves	21d	100%	20-Jan-14 A	26-Jan-14 A	
DST0898	Identification Tape for water pipeline	21d	100%	21-Jan-14 A	22-Jan-14 A	
DST0810	Ball valves	21d	100%	26-Jan-14 A	30-Jan-14 A	
DST0865	Elecometer 266 Holiday detector	21d	100%	26-Jan-14 A	30-Jan-14 A	
DST0935	Heavy duty frame and cover	21d	100%	27-Jan-14 A	30-Jan-14 A	
DST0870	Combination air release valves.	21d	100%	27-Jan-14 A	02-Feb-14 A	
DST0910	Strainers.	21d	100%	27-Jan-14 A	30-Jan-14 A	
DST0874	Air Release Valves.	21d	100%	27-Jan-14 A	30-Jan-14 A	
DST0930	Pressure relief valves.	21d	100%	30-Jan-14 A	04-Feb-14 A	
DST0820	Pipe Flanges	21d	100%	30-Jan-14 A	04-Feb-14 A	
DST0975	UPVC pipe for drainage	21d	100%	03-Feb-14 A	04-Feb-14 A	
DST0970-new	Pressure Reducing Valves	21d	100%	10-Feb-14 A	02-Apr-14 A	
DST0937	Repair Pipe Cement Lining and Coating	21d	100%	10-Feb-14 A	16-Apr-14 A	
DST0970	Flow Control Valves	21d	100%	10-Feb-14 A	20-Feb-14 A	
DST0795	Shrinkable Sheet	21d	100%	18-Feb-14 A	23-Feb-14 A	
DST0972-new	Washout Flap Valve	21d	100%	20-Feb-14 A	25-Feb-14 A	
DST0974-new	Check Valve	21d	100%	02-Mar-14 A	03-Mar-14 A	
DST0977-new	Finish Paint for Exposed Pipes/Fittings and Pipes/Fittings Inside Chambers	21d	100%	13-Mar-14 A	30-Mar-14 A	
DST0976-new	Bolts, Nuts& Washers	21d	100%	23-Mar-14 A	05-May-14 A	
DST0920	Electro-Magnetic Flow Meters	21d	100%	21-Apr-14 A	09-Jun-14 A	
DST0950-new	Hubbed Slip on Flanges for Welding (Alternative)	21d	100%	08-May-14 A	18-May-14 A	
DST0940	Pressure Gauges	21d	100%	12-May-14 A	21-Aug-14 A	
DST0955-new	Structural Analysis for Gate Valve Chamber Walls.	21d	100%	23-Jul-14 A	04-Aug-14 A	
DST0960-new	Adjustable Support for pipes & Fittings inside chambers	21d	100%	20-Aug-14 A	16-Sep-14 A	
DST0965-new	Ball Valve-Tyco F120 for Pressure Gauge	21d	100%	27-Aug-14 A	28-Aug-14 A	
DST0975-new	Galvanized Manhole ladder	21d	100%	27-Aug-14 A	15-Oct-14 A	
DST0980-new	Measuring Ranges for Pressure Gauges	21d	100%	09-Sep-14 A	16-Sep-14 A	
DST0990-new	Weld neck flange-DIN 2635 for 10" and 12" sizes	21d	100%	06-Nov-14 A	10-Nov-14 A	
DST0985-new	Strainer Ball Valve	21d	100%	09-Nov-14 A	11-Nov-14 A	
DST0995-new	Pipe Marker	21d	100%	09-Nov-14 A	18-Nov-14 A	
DST0999-new	Anti Seize for Stainless Steel Bolts	21d	100%	17-Dec-14 A	22-Dec-14 A	
DST0310-new	Sewer Manhole Cover 60cm clear opening	21d	90%	18-Jan-15 A	03-Mar-15	6d
DST0300-new	FCVs Orifice Calculations	21d	100%	29-Jan-15 A	03-Feb-15 A	
DST0320-new	Gate Valve PN 25	21d	100%	15-Feb-15 A	18-Feb-15 A	
Material Submittals civil		302d		15-Jan-14 A	03-Feb-15 A	
DST1015	Bedding material	21d	100%	15-Jan-14 A	20-Jan-14 A	
DST1018	Backfilling material (Basecourse and single size)	21d	100%	15-Jan-14 A	20-Jan-14 A	
DST1100	Prime Coat	21d	100%	23-Jan-14 A	26-Jan-14 A	

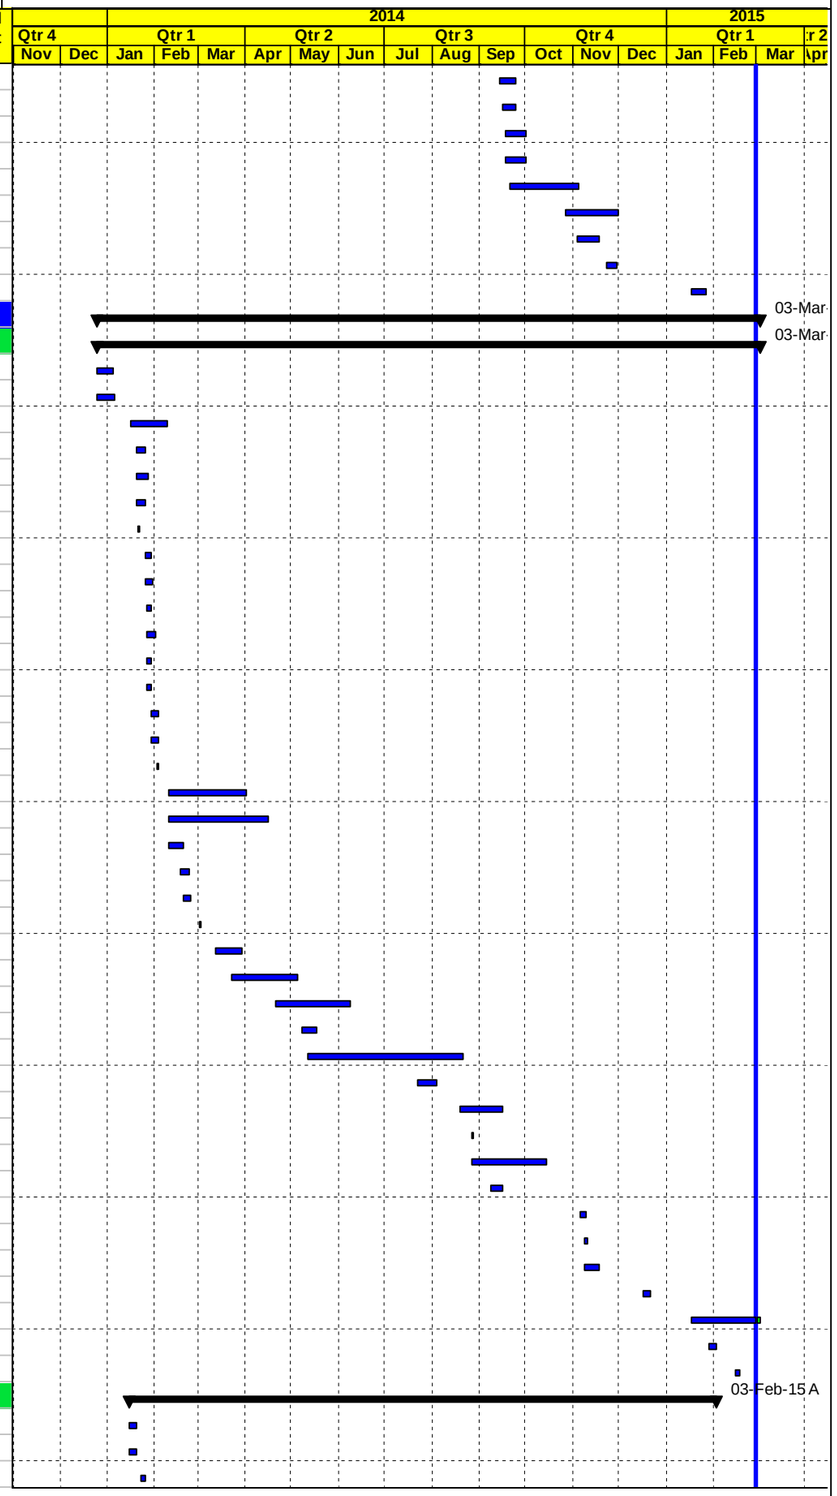

◇ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program

Completed & In Progress Activities

TO13-Updated

Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DST1110	Tack Coat	21d	100%	23-Jan-14 A	26-Jan-14 A	
DST1042	Cold Bituminous material	21d	100%	26-Jan-14 A	26-Jan-14 A	
DST1130	Asphalt -Mix Design	21d	100%	28-Jan-14 A	06-Feb-14 A	
DST1010	Concrete Mix Design including Cement type	21d	100%	30-Jan-14 A	26-Feb-14 A	
DST1030	Steel Reinforcement	21d	100%	02-Feb-14 A	06-Feb-14 A	
DST1035-new	Concrete & Plastic Supports/Spacers	21d	100%	02-Mar-14 A	18-Mar-14 A	
DST1028	Concrete Formwork Tie Rods	21d	100%	04-Mar-14 A	18-Mar-14 A	
DST1036-new	Casing (Sleeve) For Water Pipe line Crossing Main Asphalted Road & Israeli Roads	21d	100%	05-Mar-14 A	16-Apr-14 A	
DST1037-new	Stainless Steel Chocks & Materials for Filling Annular Space With Non-Shrink Grout	21d	100%	08-May-14 A	27-May-14 A	
DST1038-new	Precast Manhole for Washout , Air vent & release Manhole	21d	100%	29-May-14 A	22-Jul-14 A	
DST1040-new	Sewer UPVC Pipes (DN 8" SN 8)	21d	100%	30-Dec-14 A	13-Jan-15 A	
DST1045-new	Sewer Circular Precast Concrete Manhole (one meter internal diameter)	21d	100%	30-Dec-14 A	03-Feb-15 A	
DST1046-new	Rubber Gasket for 8" sewer UPVC pipes/ Sample	21d	100%	15-Jan-15 A	20-Jan-15 A	
Procurements		259d		20-Jan-14 A	08-Dec-14 A	
Order		134d		20-Jan-14 A	19-Jun-14 A	
DST1160	Start Order 300 mm,150 mm pipes and fittings	0d	100%	20-Jan-14 A		
DST1170	Start Order valves and other related materials	0d	100%	19-Jun-14 A		
Manufacturing		174d		20-Jan-14 A	13-Nov-14 A	
DST1190	300 mm,150 mm pipes and fittings	29d	100%	20-Jan-14 A	11-Mar-14 A	
DST1200	Valves and other related materials	70d	100%	22-Jun-14 A	13-Nov-14 A	
Delivery		204d		11-Mar-14 A	08-Dec-14 A	
DST1210	Start Delivery 300mm, 150 mm pipes and fittings	0d	100%	11-Mar-14 A		
DST1220	Start Delivery valves and other related materials	0d	100%	08-Dec-14 A		
Testing		2d		16-Mar-14 A	16-Mar-14 A	
DST1230	300 mm,150 mm pipes and fittings	2d	100%	16-Mar-14 A	16-Mar-14 A	
Construction Work		325d		19-Jan-14 A	03-Mar-15	8d
Implement traffic control		5d		19-Jan-14 A	23-Mar-14 A	
DST1240	Start Implement traffic control and safety plan	5d	100%	19-Jan-14 A	23-Mar-14 A	
Main pipeline		315d		26-Mar-14 A	03-Mar-15	8d
Segment A		303d		26-Mar-14 A	24-Dec-14 A	
Phase One from Sta. A9+702 to Sta. A12+900 At RHS/ Location Area(B)		243d		26-Mar-14 A	18-Dec-14 A	
300 mm Main pipeline from Sta. A9+702 to Sta. A11+300 At RHS/ Location Area(B)		237d		06-Apr-14 A	18-Dec-14 A	
Safety and Remove Asphalt		78d		06-Apr-14 A	18-Dec-14 A	
DST1570	Maintain traffic control and safety plan	78d	100%	06-Apr-14 A	18-Dec-14 A	
DST1580	Remove Asphalt	6d	100%	07-Apr-14 A	29-Apr-14 A	
Pipe Installation		71d		07-Apr-14 A	29-May-14 A	
DST1590	Trench excavation for 300 mm main pipeline length approx. (1600 LM) and road crossing	18d	100%	07-Apr-14 A	30-Apr-14 A	
DST1600	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	18d	100%	08-Apr-14 A	30-Apr-14 A	
DST1620	Compact Approved Backfill material ,sub base / base course above pipeline	18d	100%	08-Apr-14 A	30-Apr-14 A	
DST1610	Casting concrete as encasement around the main pipeline from Sta. A10+326 and Sta. A10+431 (105 LM)	19d	100%	20-Apr-14 A	22-Apr-14 A	
DST1672	Future connection at Sta. A10+460 and Sta. A9+920	1d	100%	29-May-14 A	29-May-14 A	
Civil Chamber work		95d		26-May-14 A	14-Dec-14 A	
DST1630	Construct - Gate Valve chambe (Dia. 200 mm) @ Sta. A9+941	14d	100%	26-May-14 A	15-Jul-14 A	
DST1660	Construct - Combined Butterfly Valve (Dia.300) and Air Valve chamber(Dia.100mm) @ Sta. 11+187	18d	100%	02-Jun-14 A	23-Jun-14 A	
DST1645	Construct - Gate Valve chamber (Dia. 200mm) @ Sta. A10+461 (Precast)	14d	100%	15-Jul-14 A	20-Jul-14 A	
DST1640	Construct- Combination Air Valve chamber (Dia.100mm) @ Sta. A9+928 (Precast)	14d	100%	08-Sep-14 A	14-Dec-14 A	
DST1650	Construct - Wash out Valve chamber (Dia.150mm) @ A10+889	13d	100%	15-Sep-14 A	01-Oct-14 A	
Testing		135d		05-May-14 A	18-Dec-14 A	
DST1674	Radiograph Testing	2d	100%	05-May-14 A	05-May-14 A	
DST1676	Pressure Testing	2d	100%	14-Dec-14 A	18-Dec-14 A	
Reinstatement		74d		30-Apr-14 A	13-Nov-14 A	
DST1680	Asphalt reinstatement	4d	100%	30-Apr-14 A	12-Nov-14 A	
DST1685-new	Milling of Existing Asphalt	1d	100%	28-Oct-14 A	28-Oct-14 A	
DST1690-new	Asphalt reinstatement (wearing course)	5d	100%	10-Nov-14 A	13-Nov-14 A	

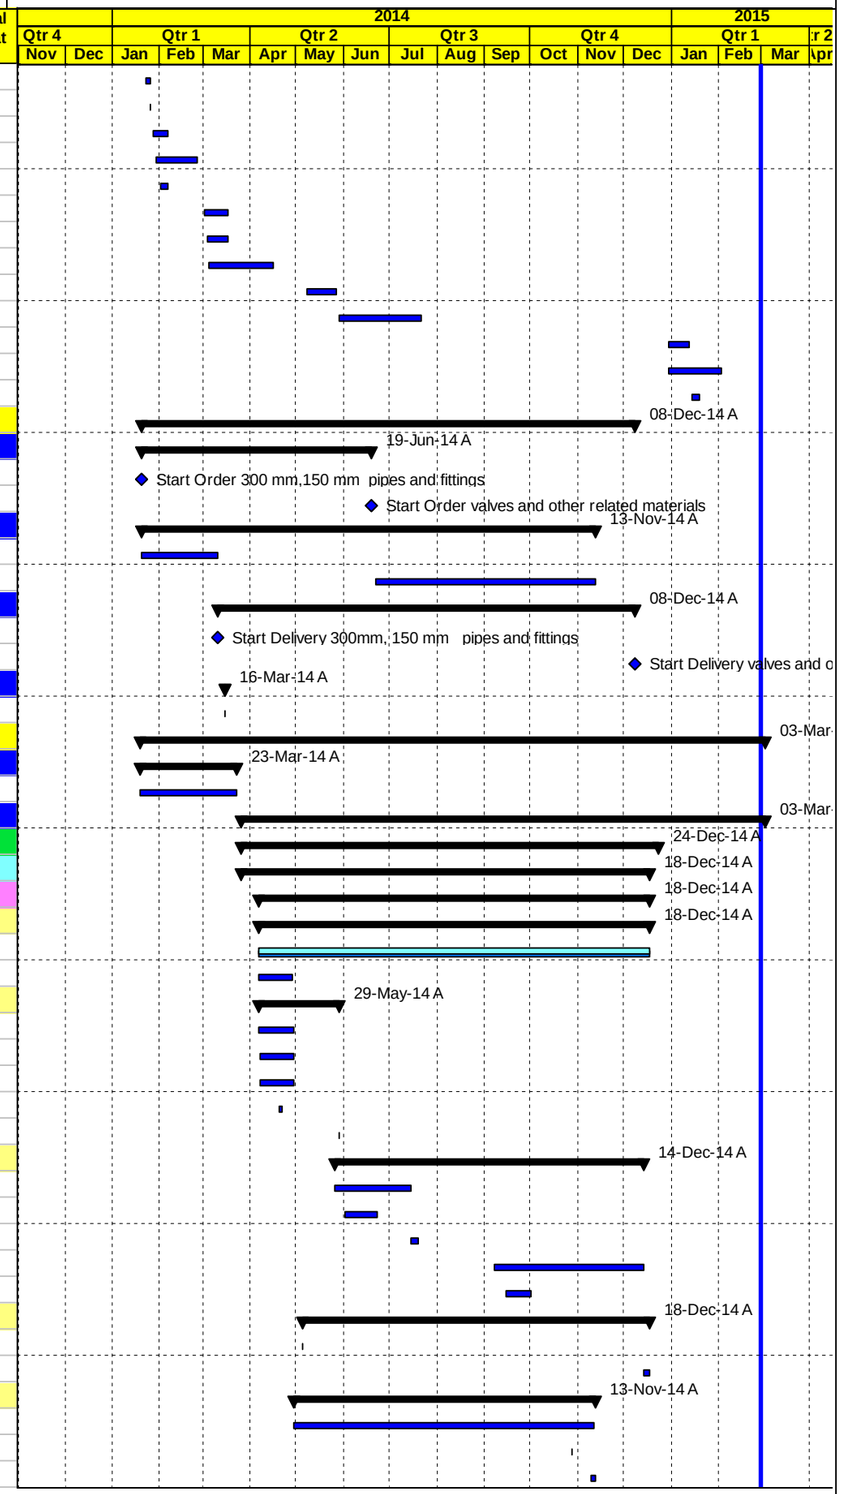

◇ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Page 4 of 10

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
300 mm Main pipeline from Sta. A11+300 to Sta. A12+900 At RHS/ Location Area(B)		243d		26-Mar-14 A	18-Dec-14 A	
Safety and Remove Asphalt		75d		26-Mar-14 A	18-Dec-14 A	
DST1682	Maintain traffic control and safety plan	63d	100%	26-Mar-14 A	18-Dec-14 A	
DST1690	Remove Asphalt	7d	100%	26-Mar-14 A	11-May-14 A	
Pipe Installation		21d		26-Mar-14 A	24-May-14 A	
DST1700	Trench excavation for 300 mm main pipeline length approx. (1600 LM)	18d	100%	26-Mar-14 A	13-May-14 A	
DST1710	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	18d	100%	26-Mar-14 A	13-May-14 A	
DST1730	Compact Approved Backfill material ,sub base / base course above pipeline	18d	100%	26-Mar-14 A	13-May-14 A	
DST1890-new	Road crossing from Sta. 12+562.11 to St. 12+578.42 (16.31m)	2d	100%	24-May-14 A	24-May-14 A	
Civil Chamber work		18d		25-Aug-14 A	02-Dec-14 A	
DST1750	Construct - Combination Air Valve chamber (Dia. 100mm) @ 12+500	14d	100%	25-Aug-14 A	05-Nov-14 A	
DST1760	Construct - Combination Air Valve chamber (Dia.100mm) @ 11+743	14d	100%	25-Aug-14 A	02-Dec-14 A	
DST1765-new	Al Foudqumiya Connection Chamber (Dia.100mm) at Sta. 12+142	14d	100%	28-Aug-14 A	01-Oct-14 A	
Testing		243d		30-Mar-14 A	18-Dec-14 A	
DST1772	Radiograph Testing	2d	100%	30-Mar-14 A	07-May-14 A	
DST1774	Pressure Testing	3d	100%	14-Dec-14 A	18-Dec-14 A	
Reinstatement		82d		04-May-14 A	10-Nov-14 A	
DST1778	Asphalt reinstatement	4d	100%	04-May-14 A	02-Jun-14 A	
DST1780-new	Milling of Existing Asphalt	1d	100%	28-Oct-14 A	28-Oct-14 A	
DST1788-new	Asphalt Reinstatement (wearing course)	5d	100%	09-Nov-14 A	10-Nov-14 A	
Phase Two 300 mm Main pipeline from Sta. A12+900 to Sta. A13+154 At LHS/ Location Area(B)		164d		11-May-14 A	18-Dec-14 A	
Safety and Remove Asphalt		38d		11-May-14 A	18-Dec-14 A	
DST1850	Maintain traffic control and safety plan	26d	100%	11-May-14 A	18-Dec-14 A	
DST1860	Remove Asphalt	3d	100%	12-May-14 A	15-May-14 A	
Pipe Installation		24d		13-May-14 A	15-May-14 A	
DST1880	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	6d	100%	13-May-14 A	15-May-14 A	
DST1890	Compact Approved Backfill material ,sub base / base course above pipeline	6d	100%	13-May-14 A	15-May-14 A	
DST1870	Trench excavation for 300 mm main pipeline length approx. (254 LM)	6d	100%	13-May-14 A	15-May-14 A	
DST1885	Casting Concrete as Encasement around the Main Pipeline or Single Size if required (from Sta. 13+055.40 to Sta	6d	100%	15-May-14 A	15-May-14 A	
Testing		2d		14-Dec-14 A	18-Dec-14 A	
DST1894	Pressure Testing	2d	100%	14-Dec-14 A	18-Dec-14 A	
Reinstatement		110d		02-Jun-14 A	09-Nov-14 A	
DST1898	Asphalt reinstatement	2d	100%	02-Jun-14 A	02-Jun-14 A	
DST1990-new	Milling of Existing Asphalt	1d	100%	28-Oct-14 A	28-Oct-14 A	
DST1999-new	Asphalt Reinstatement (wearing course)	3d	100%	09-Nov-14 A	09-Nov-14 A	
Phase Three 300 mm Main pipeline from Sta. A13+154 to Sta. A13+710 At LHS/ Location Area(C)		174d		15-May-14 A	18-Dec-14 A	
Safety and Remove Asphalt		88d		15-May-14 A	18-Dec-14 A	
DST1900	Maintain traffic control and Safety plan	88d	100%	15-May-14 A	18-Dec-14 A	
DST1910	Remove Asphalt	4d	100%	15-May-14 A	22-May-14 A	
Pipe Installation		63d		15-May-14 A	24-May-14 A	
DST1920	Trench excavation for 300 mm main pipeline length approx. (578 LM)	10d	100%	15-May-14 A	24-May-14 A	
DST1930	Bedding (single size aggregate) and install 300 mm schedule 20 Steel pipe include testing	10d	100%	17-May-14 A	24-May-14 A	
DST1940	Compact Approved Backfill material ,sub base / base course above pipeline	10d	100%	17-May-14 A	24-May-14 A	
DST1938	Future connection at A13+625	1d	100%	20-May-14 A	20-May-14 A	
Civil Chamber work		43d		05-Jun-14 A	02-Dec-14 A	
DST2030	Construct - Gate Valve chamber (Dia. 250mm) at A13+617	5d	100%	05-Jun-14 A	28-Aug-14 A	
DST1960	Construct - Butterfly Valve chamber (Dia. 300mm) @ Sta. A13+700	14d	100%	09-Jun-14 A	12-Jul-14 A	
DST1970	Construct Al Asasa connection chamber (Dia. 50mm) at Sta. A13+608 & connect to exist. Pipes	14d	100%	25-Jun-14 A	12-Oct-14 A	
DST1950	Construct - Wash out Valve chamber (Dia. 150mm) @ Sta. A13+628	14d	100%	13-Aug-14 A	02-Dec-14 A	
Testing		2d		14-Dec-14 A	18-Dec-14 A	
DST1977	Pressure Testing	2d	100%	14-Dec-14 A	18-Dec-14 A	
Reinstatement		108d		02-Jun-14 A	09-Nov-14 A	
DST1979	Asphalt reinstatement	5d	100%	02-Jun-14 A	29-Oct-14 A	
DST1989-new	Milling of Existing Asphalt	1d	100%	28-Oct-14 A	28-Oct-14 A	

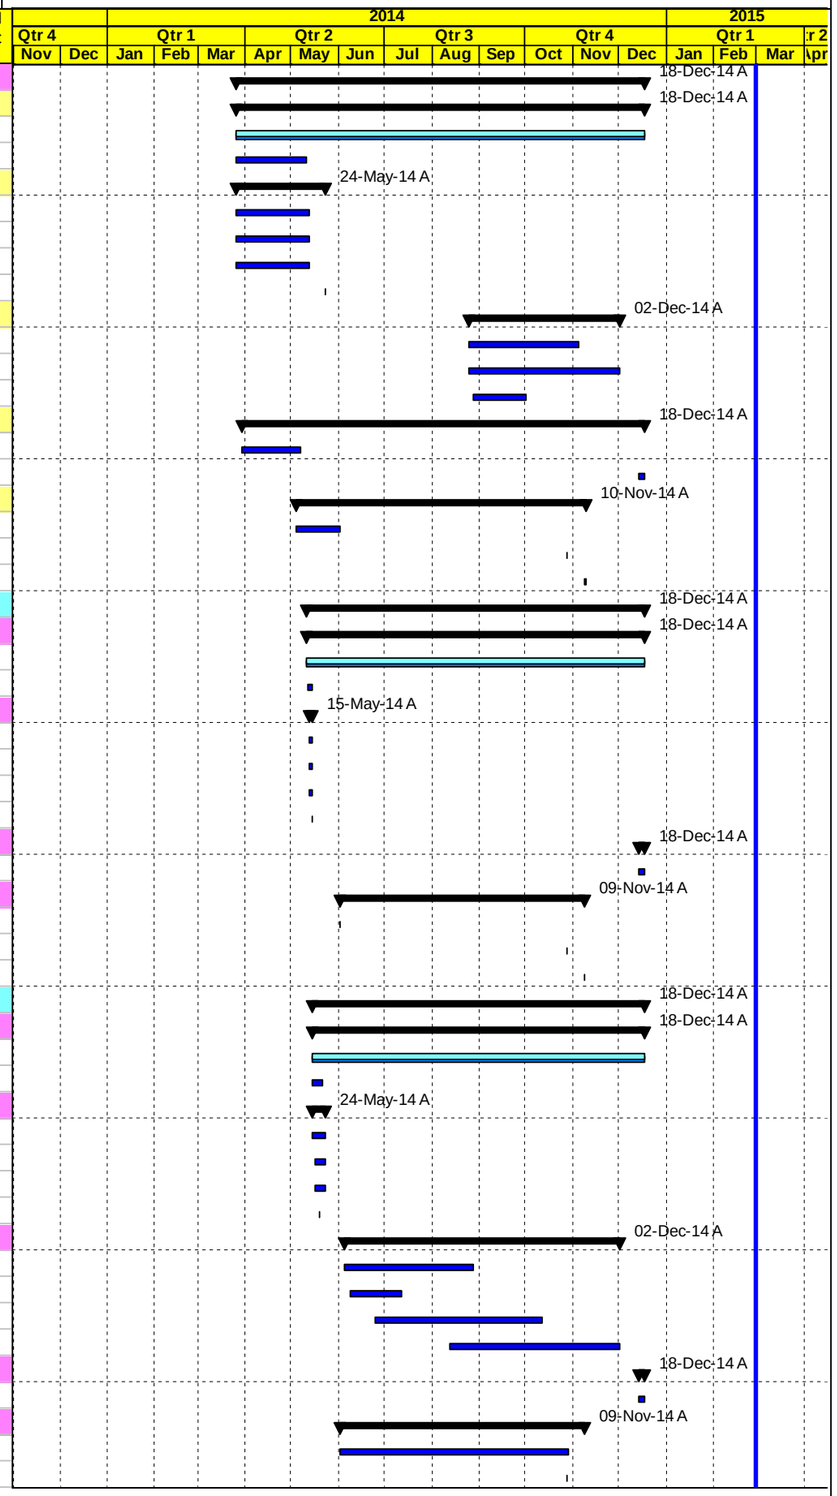

◇ Milestone Early Bar
Actual Work
◆ Milestone Actual
Actual Level of Effort
Early Bar
Critical Bar
Level of Effort
Summary

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DST1995-new	Asphalt Reinstatement (wearing course)	3d	100%	09-Nov-14 A	09-Nov-14 A	
Phase Four from Sta. A6+983 to Sta. A2+280 At RHS/ Location Area(C)		245d		25-May-14 A	24-Dec-14 A	
300 mm Main pipeline from Sta. A6+983 to Sta. A5+200 At RHS/ Location Area(C)		162d		25-May-14 A	14-Dec-14 A	
Safety and Remove Exist. concrete ditch		68d		25-May-14 A	14-Dec-14 A	
DST2260	Maintain traffic control and safety plan	68d	100%	25-May-14 A	14-Dec-14 A	
DST2270	Remove Exist. concrete ditch	9d	100%	26-May-14 A	17-Jun-14 A	
Pipe Installation		154d		26-May-14 A	17-Jun-14 A	
DST2320	Backfilling from Sta.6+241.18 to 6+364 - 6+430.00 to 6+508.70 (201.52)	6d	100%	26-May-14 A	17-Jun-14 A	
DST2290	Trench excavation for 300 mm main pipeline length approx. (1783 LM)	22d	100%	26-May-14 A	17-Jun-14 A	
DST2300	Install 300 mm schedule 20 Steel Pipe Include testing	22d	100%	26-May-14 A	17-Jun-14 A	
DST2310	Casting concrete as encasement around the main pipeline or single size if required	22d	100%	26-May-14 A	17-Jun-14 A	
DST2330	Bedding (single size aggregate) from Sta.6+289.68 to 6+364 - 6+430.00 to 6+508.70 (153.02)	6d	100%	26-May-14 A	17-Jun-14 A	
Civil Chamber work		14d		31-Aug-14 A	03-Sep-14 A	
DST2340	Construct - Combination Air Valve chamber (Dia. 100) @ Sta. A6+332	14d	100%	31-Aug-14 A	03-Sep-14 A	
Testing		2d		14-Dec-14 A	14-Dec-14 A	
DST2354	Pressure Testing	2d	100%	14-Dec-14 A	14-Dec-14 A	
Reinstatement		61d		31-May-14 A	11-Aug-14 A	
DST2356	Concrete Reinstatement	11d	100%	31-May-14 A	05-Aug-14 A	
DST2360-new	Asphalt Reinstatement (Sta. 6+508 to Sta. 6+430) 78 m	5d	100%	11-Aug-14 A	11-Aug-14 A	
300 mm Main pipeline from Sta. A5+200 to Sta. A3+880 At RHS/ Location Area(C)		200d		17-Jun-14 A	14-Dec-14 A	
Safety and Remove Exist. concrete ditch		117d		17-Jun-14 A	14-Dec-14 A	
DST2360	Maintain Traffic Control and Safety Plan	117d	100%	17-Jun-14 A	14-Dec-14 A	
DST2370	Remove Exist. concrete ditch	9d	100%	17-Jun-14 A	30-Jun-14 A	
Pipe Installation		31d		17-Jun-14 A	30-Jun-14 A	
DST2390	Trench excavation for 300 mm main pipeline length approx. (1320 LM)	18d	100%	17-Jun-14 A	30-Jun-14 A	
DST2400	Install 300 mm Steel pipe schedule 20 include testing	18d	100%	17-Jun-14 A	30-Jun-14 A	
DST2410	Casting concrete as encasement around the main pipeline or single size if required	18d	100%	17-Jun-14 A	30-Jun-14 A	
DST2420-new	Bedding (single size aggregate) from Sta. 4+081.25 to Sta. 3+918	1d	100%	30-Jun-14 A	30-Jun-14 A	
DST2425-new	Backfilling from Sta. 4+186.06 to Sta. 3+918	1d	100%	30-Jun-14 A	30-Jun-14 A	
Civil Chamber work		36d		31-Aug-14 A	27-Oct-14 A	
DST2430	Construct - Combination Air Valve chamber (Dia. 100mm) @ 5+110	14d	100%	31-Aug-14 A	03-Sep-14 A	
DST2442	Construct - Wash out Valve chamber (Dia. 150mm) @ Sta. A3+924	14d	100%	29-Sep-14 A	27-Oct-14 A	
Testing		162d		19-Jun-14 A	14-Dec-14 A	
DST2444	Radiograph Testing	2d	100%	19-Jun-14 A	19-Jun-14 A	
DST2446	Pressure Testing	2d	100%	14-Dec-14 A	14-Dec-14 A	
Reinstatement		54d		05-Aug-14 A	11-Aug-14 A	
DST2448	Concrete Reinstatement	15d	100%	05-Aug-14 A	11-Aug-14 A	
DST2449-new	Asphalt Reinstatement (Sta. 3+950 to Sta. 4+080 (130 m)	15d	100%	11-Aug-14 A	11-Aug-14 A	
300 mm Main pipeline from Sta. A3+480 to Sta. A2+280 At RHS/ Location Area(C)		212d		30-Jun-14 A	24-Dec-14 A	
Safety and Remove Exist. concrete ditch		74d		30-Jun-14 A	14-Dec-14 A	
DST2450	Maintain traffic control and safety plan	74d	100%	30-Jun-14 A	14-Dec-14 A	
DST2460	Remove Exist. concrete ditch	9d	100%	16-Jul-14 A	16-Jul-14 A	
Pipe Installation		125d		01-Jul-14 A	19-Jul-14 A	
DST2480	Trench excavation for 300 mm main pipeline length approx. (1200 LM)	19d	100%	01-Jul-14 A	17-Jul-14 A	
DST2490	Install 300 mm Steel pipe schedule 20 include testing	19d	100%	01-Jul-14 A	16-Jul-14 A	
DST2500	Casting concrete as encasement around the main pipeline or single size if required	19d	100%	02-Jul-14 A	16-Jul-14 A	
DST2510-new	Bedding (single size aggregate) from Sta. 3+354 to Sta. 3+321 & Sta. 2+961 to Sta. 2+936	19d	100%	03-Jul-14 A	09-Jul-14 A	
DST2520-new	Backfilling from Sta. 3+354 to Sta. 3+324 & Sta. 2+961.86 to Sta. 2+935 (56.86m)	19d	100%	03-Jul-14 A	09-Jul-14 A	
DST2530-new	Road crossing from St.2+319.78 to St. 2+299.88 (19.9m)	5d	100%	19-Jul-14 A	19-Jul-14 A	
Civil Chamber work		132d		02-Aug-14 A	24-Dec-14 A	
DST2530	Construct - Air Valve chamber (Dia. 100mm) combined with Butterfly Valve (Dia. 300mm) @A3+350	20d	100%	02-Aug-14 A	07-Sep-14 A	
DST2540	Construct - Butterfly Valve chamber (Dia. 300mm) @ 2+952	14d	100%	10-Aug-14 A	07-Sep-14 A	
DST2520	Construct -Wash out chamber (Dia. 150mm) @2+952	14d	100%	13-Aug-14 A	24-Dec-14 A	
DST2552	Sabastiya Washout (Dia. 250mm) @ St.2+936	5d	100%	13-Aug-14 A	24-Aug-14 A	

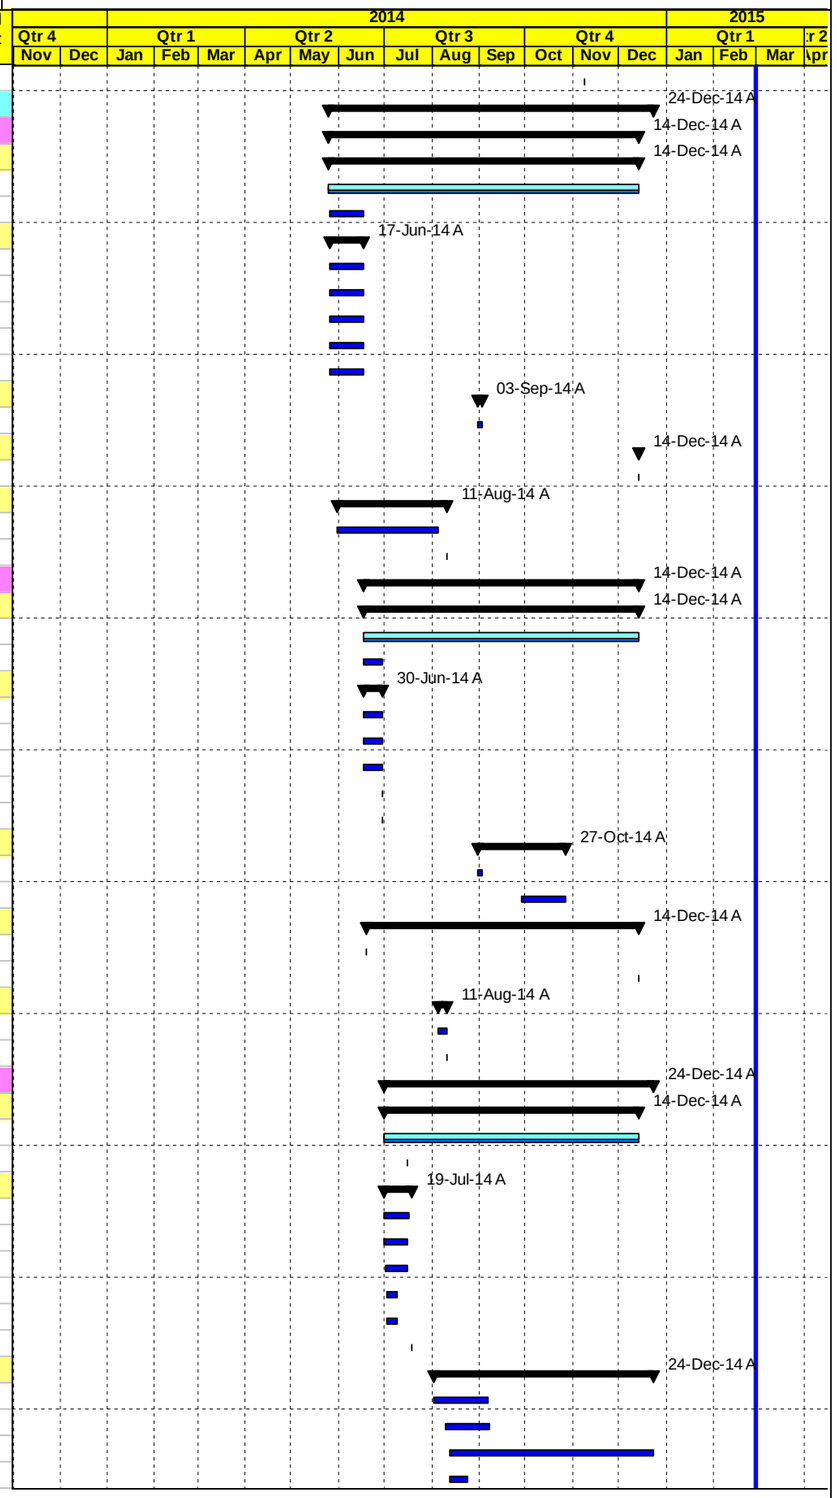

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DST2550	Construct Sabastia connection chamber (Dia. 75mm) at Sta. A2+322 & connect to exist.WSP	14d	100%	01-Sep-14 A	02-Dec-14 A	
Testing		66d		14-Aug-14 A	14-Dec-14 A	
DST2553	Radiograph Testing	2d	100%	14-Aug-14 A	14-Aug-14 A	
DST2555	Pressure Testing	2d	100%	14-Dec-14 A	14-Dec-14 A	
Reinstatement		9d		14-Jul-14 A	01-Oct-14 A	
DST2426-new	Backfilling with selected material from Sta. 3+460 to Sta. 2+340	9d	100%	14-Jul-14 A	01-Oct-14 A	
Phase Five 300 mm Main pipeline from Sta. A2+280 to Sta. A1+220 At LHS/ Location Area(C)		174d		15-Jul-14 A	14-Dec-14 A	
Safety and Remove Exist. concrete ditch		83d		15-Jul-14 A	14-Dec-14 A	
DST2560	Maintain traffic control and safety plan	83d	100%	15-Jul-14 A	14-Dec-14 A	
DST2570	Remove Exist. concrete ditch	5d	100%	17-Jul-14 A	09-Aug-14 A	
Pipe Installation		115d		17-Jul-14 A	29-Sep-14 A	
DST2590	Trench excavation for 300 mm main pipeline length approx. (1060 LM)	15d	100%	17-Jul-14 A	09-Aug-14 A	
DST2600	Install 300 mm schedule 20 Steel pipe include testing	15d	100%	19-Jul-14 A	09-Aug-14 A	
DST2610	Casting concrete as encasement around the main pipeline or single size if required	15d	100%	20-Jul-14 A	09-Aug-14 A	
DST2620-new	Bedding from Sta. 1+360 to 1+413 (53m)	15d	100%	07-Aug-14 A	07-Aug-14 A	
DST2630-new	Backfilling from Sta. 1+360 to 1+413 (53m)	15d	100%	07-Aug-14 A	07-Aug-14 A	
DST2645-new	Road crossing from St. 1+239 to St. 1+224.19	5d	100%	08-Aug-14 A	08-Aug-14 A	
DST2635-new	Bedding from sta.1+224.19 to Sta.1+220 (4.2m)	15d	100%	29-Sep-14 A	29-Sep-14 A	
DST2640-new	Backfilling from Sta.1+224.19 to Sta.1+221 (4.2m)	15d	100%	29-Sep-14 A	29-Sep-14 A	
Civil Chamber work		14d		15-Sep-14 A	02-Dec-14 A	
DST2650	Construct - Combination Air Valve chamber (Dia. 100) @ 1+390	14d	100%	15-Sep-14 A	02-Dec-14 A	
Testing		76d		14-Aug-14 A	14-Dec-14 A	
DST2652	Radiograph Testing	2d	100%	14-Aug-14 A	14-Aug-14 A	
DST2654	Pressure Testing	2d	100%	14-Dec-14 A	14-Dec-14 A	
Reinstatement		10d		27-Aug-14 A	28-Aug-14 A	
DST2656	Concrete Reinstatement	10d	100%	27-Aug-14 A	28-Aug-14 A	
Phase Six 300 mm Main pipeline from Sta. A9+702 to Sta. A9+030 At RHS/ Location Area(C)		148d		09-Aug-14 A	18-Dec-14 A	
Safety and Remove Exist. concrete ditch		25d		09-Aug-14 A	18-Dec-14 A	
DST1980	Maintain traffic control and safety plan	25d	100%	09-Aug-14 A	18-Dec-14 A	
DST1990	Remove Exist. concrete ditch	4d	100%	10-Aug-14 A	17-Aug-14 A	
Pipe Installation		14d		10-Aug-14 A	19-Aug-14 A	
DST2000	Trench Excavation for 300 mm Main Pipeline Length approx. (672 LM)	10d	100%	10-Aug-14 A	18-Aug-14 A	
DST2010	Install 300 mm schedule 20 Steel pipe include testing	10d	100%	11-Aug-14 A	18-Aug-14 A	
DST2060-new	Bedding from Sta. 9+691 to Sta. 9+610 (81 m)	2d	100%	11-Aug-14 A	12-Aug-14 A	
DST2064-new	Backfilling from Sta. 9+702 to Sta. 9+557 (145)	2d	100%	11-Aug-14 A	12-Aug-14 A	
DST2020	Casting Concrete as Encasement Around the Main Pipeline or Single Size if Required	10d	100%	12-Aug-14 A	19-Aug-14 A	
Testing		127d		14-Aug-14 A	18-Dec-14 A	
DST2032	Radiograph Testing	2d	100%	14-Aug-14 A	14-Aug-14 A	
DST2034	Pressure Testing	2d	100%	14-Dec-14 A	18-Dec-14 A	
Reinstatement		18d		01-Sep-14 A	29-Oct-14 A	
DST2036	Concrete Reinstatement	5d	100%	01-Sep-14 A	24-Sep-14 A	
DST2040-new	Asphalt Reinstatement from Sta. 9+570 to Sta. 9+690	1d	100%	29-Oct-14 A	29-Oct-14 A	
Phase Seven 300 mm Main pipeline from Sta. A9+030 to Sta. A8+080 At LHS/ Location Area(C)		135d		14-Aug-14 A	18-Dec-14 A	
Safety and Remove Exist. concrete ditch		39d		18-Aug-14 A	18-Dec-14 A	
DST2040	Maintain traffic control and safety plan	39d	100%	18-Aug-14 A	18-Dec-14 A	
DST2050	Remove Exist. concrete ditch	5d	100%	18-Aug-14 A	06-Sep-14 A	
Pipe Installation		100d		19-Aug-14 A	08-Sep-14 A	
DST2070	Trench excav. for 300 mm Main Pipeline Approx.(950 LM)	14d	100%	19-Aug-14 A	06-Sep-14 A	
DST2080	Install 300 mm schedule 20 Steel pipe include testing	14d	100%	19-Aug-14 A	06-Sep-14 A	
DST2072-new	Road Crossing from 9+029.89 to 9+011.17(18.72m)	5d	100%	19-Aug-14 A	19-Aug-14 A	
DST2090	Casting concrete as encasement around the main pipeline or single size if required	14d	100%	20-Aug-14 A	08-Sep-14 A	
DST2075-new	Bedding from Sta. 9+005.4 to Sta. 8+814.8 (190.6 m)	14d	100%	21-Aug-14 A	26-Aug-14 A	
DST2076-new	Backfilling from Sta. 8+945.97 to Sta. 8+814.8 (131.17 m)	14d	100%	21-Aug-14 A	26-Aug-14 A	
DST2073-new	Road Crossing from Sta. 8+238.26 to Sta. 8+214.66 (23.6)	1d	100%	02-Sep-14 A	02-Sep-14 A	

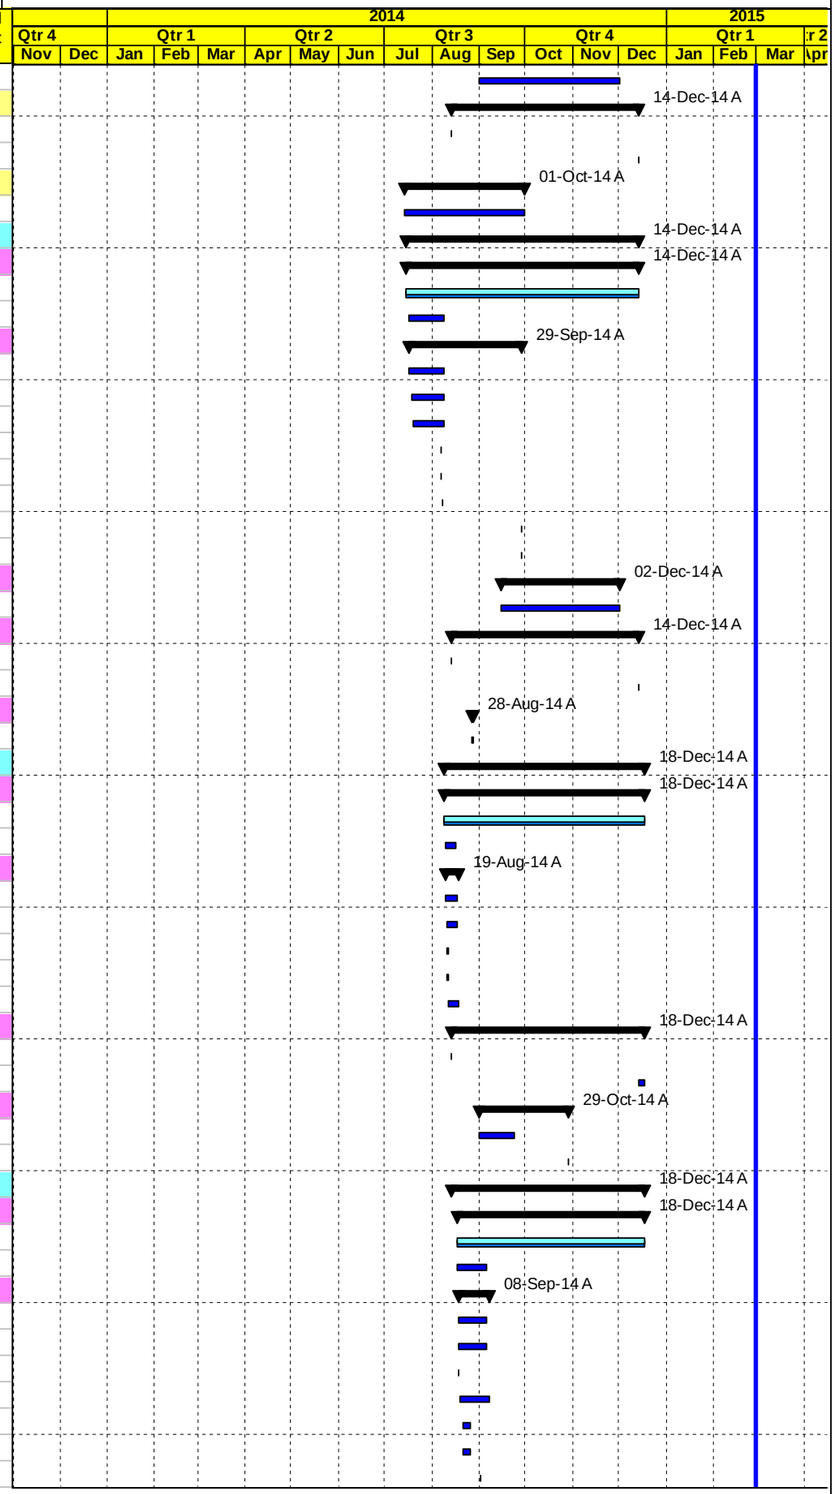

Milestone Early Bar | Actual Level of Effort | Level of Effort
Actual Work | Early Bar | Summary
Milestone Actual | Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Civil Chamber work		14d		06-Sep-14 A	02-Dec-14 A	
DST2120	Construct - Combination Air Valve chamber (Dia. 100mm) @ Sta.A8+885	14d	100%	06-Sep-14 A	02-Dec-14 A	
DST2130	Construct Bazzariya connection chamber (Dia. 75mm) at Sta. A8+206	14d	100%	11-Sep-14 A	19-Oct-14 A	
Testing		99d		14-Aug-14 A	18-Dec-14 A	
DST2132	Radiograph Testing	2d	100%	14-Aug-14 A	14-Aug-14 A	
DST2134	Pressure Testing	2d	100%	14-Dec-14 A	18-Dec-14 A	
Reinstatement		18d		24-Sep-14 A	29-Oct-14 A	
DST2136	Concrete Reinstatement	8d	100%	24-Sep-14 A	29-Sep-14 A	
DST2138-new	Asphalt reinstatement from Sta. 9+010 to Sta. 8+855	1d	100%	29-Oct-14 A	29-Oct-14 A	
Phase Eight 300 mm Main pipeline from Sta. A8+080 to Sta. A6+983 At RHS/ Location Area(C)		104d		06-Sep-14 A	18-Dec-14 A	
Safety and Remove Exist. concrete ditch		63d		06-Sep-14 A	18-Dec-14 A	
DST2140	Maintain traffic control and safety plan	63d	100%	06-Sep-14 A	18-Dec-14 A	
DST2150	Remove Exist. concrete ditch	9d	100%	07-Sep-14 A	21-Sep-14 A	
Pipe Installation		78d		07-Sep-14 A	20-Sep-14 A	
DST2170	Trench excavation for 300 mm main pipeline length approx. (1097 LM)	14d	100%	07-Sep-14 A	20-Sep-14 A	
DST2180	Install 300 mm Steel pipe schedule 20 include testing	14d	100%	07-Sep-14 A	20-Sep-14 A	
DST2275-new	Road Crossing from St. 8+070.64 to St. 8+053.03 (17.61)	6d	100%	07-Sep-14 A	07-Sep-14 A	
DST2190	Casting concrete as encasement around the main pipeline or single size if required	14d	100%	08-Sep-14 A	20-Sep-14 A	
DST2195-new	Backfilling from Sta. 7+444 to Sta. 7+406 & Sta. 7+395 to Sta. 7+383	14d	100%	17-Sep-14 A	17-Sep-14 A	
DST2205-new	Bedding from sta. 7+094 to Sta. 7+020.95	1d	100%	20-Sep-14 A	20-Sep-14 A	
DST2210-new	Backfilling from sta. 7+094 to Sta. 7+020.96	1d	100%	20-Sep-14 A	20-Sep-14 A	
Civil Chamber work		32d		17-Sep-14 A	02-Dec-14 A	
DST2230	Construct - Air valve chamber (Dia. 100mm)combined with Butterfly Valve(Dia. 300mm) @ Sta. A7+400	19d	100%	17-Sep-14 A	02-Dec-14 A	
DST2250	Construct-300 system flow monitoring chamber @ Sta. A7+160	12d	100%	20-Sep-14 A	02-Dec-14 A	
DST2240	Construct Burqa connection chamber (Dia. 100mm) at Sta. A7+032 & connect to exist. Pipeline	14d	100%	27-Sep-14 A	25-Nov-14 A	
DST2210	Construct - Wash out chamber (Dia. 150mm) @ Sta. A7+440	14d	100%	29-Sep-14 A	21-Oct-14 A	
Testing		54d		21-Oct-14 A	18-Dec-14 A	
DST2253	Radiograph Testing	2d	100%	21-Oct-14 A	21-Oct-14 A	
DST2254	Pressure Testing	2d	100%	14-Dec-14 A	18-Dec-14 A	
Reinstatement		40d		29-Sep-14 A	30-Nov-14 A	
DST2256	Concrete Reinstatement	14d	100%	29-Sep-14 A	30-Nov-14 A	
DST2266	Asphalt Reinstatement	1d	100%	29-Oct-14 A	29-Oct-14 A	
Phase Ten 300 mm Main pipeline from Sta. A3+880 to Sta. A3+480		122d		21-Sep-14 A	14-Dec-14 A	
Safety and Remove Exist. concrete ditch		5d		21-Sep-14 A	14-Dec-14 A	
DST2808-new	Maintain traffic Control and Safety Plan	5d	100%	21-Sep-14 A	14-Dec-14 A	
DST2809-new	Remove Exist. concrete ditch	5d	100%	21-Sep-14 A	24-Sep-14 A	
Pipe Installation		7d		21-Sep-14 A	24-Sep-14 A	
DST2810-new	Install 300 mm schedule 20 Steel pipe include testing	6d	100%	21-Sep-14 A	24-Sep-14 A	
DST2835-new	Casting concrete as encasement around the main pipeline or single size if required	6d	100%	21-Sep-14 A	24-Sep-14 A	
DST2825-new	Trench excavation for 300 mm main pipeline length approx. (400 LM) and road crossing	6d	100%	21-Sep-14 A	24-Sep-14 A	
Testing		64d		21-Oct-14 A	14-Dec-14 A	
DST2846-new	Radiograph Testing	2d	100%	21-Oct-14 A	21-Oct-14 A	
DST2847-new	Pressure Testing	2d	100%	14-Dec-14 A	14-Dec-14 A	
Reinstatement		0d				0d
Phase Nine 300 mm Main pipeline from Sta. A1+220 to Sta. A0+019 At RHS/ Location Area(C)		145d		24-Sep-14 A	24-Dec-14 A	
Safety and Remove Exist. concrete ditch		69d		24-Sep-14 A	20-Dec-14 A	
DST2660	Maintain Traffic Control and Safety Plan	64d	100%	24-Sep-14 A	20-Dec-14 A	
DST2670	Remove Exist. Concrete Ditch	5d	100%	27-Sep-14 A	16-Oct-14 A	
Pipe Installation		20d		27-Sep-14 A	16-Oct-14 A	
DST2690	Trench excavation for 300 mm main pipeline length approx. (1220 LM) -a	18d	100%	27-Sep-14 A	16-Oct-14 A	
DST2700	Install 300 mm schedule 20 Steel pipe include testing	19d	100%	27-Sep-14 A	16-Oct-14 A	
DST2735-new	Bedding from Sta. 1+220 to Sta. 1+032 (188m)	2d	100%	29-Sep-14 A	01-Oct-14 A	
DST2745-new	Backfilling from Sta. 1+220 to Sta. 1+032 (188m)	2d	100%	29-Sep-14 A	01-Oct-14 A	
DST2710	Casting concrete as encasement around the main pipeline or single size if required	16d	100%	01-Oct-14 A	16-Oct-14 A	

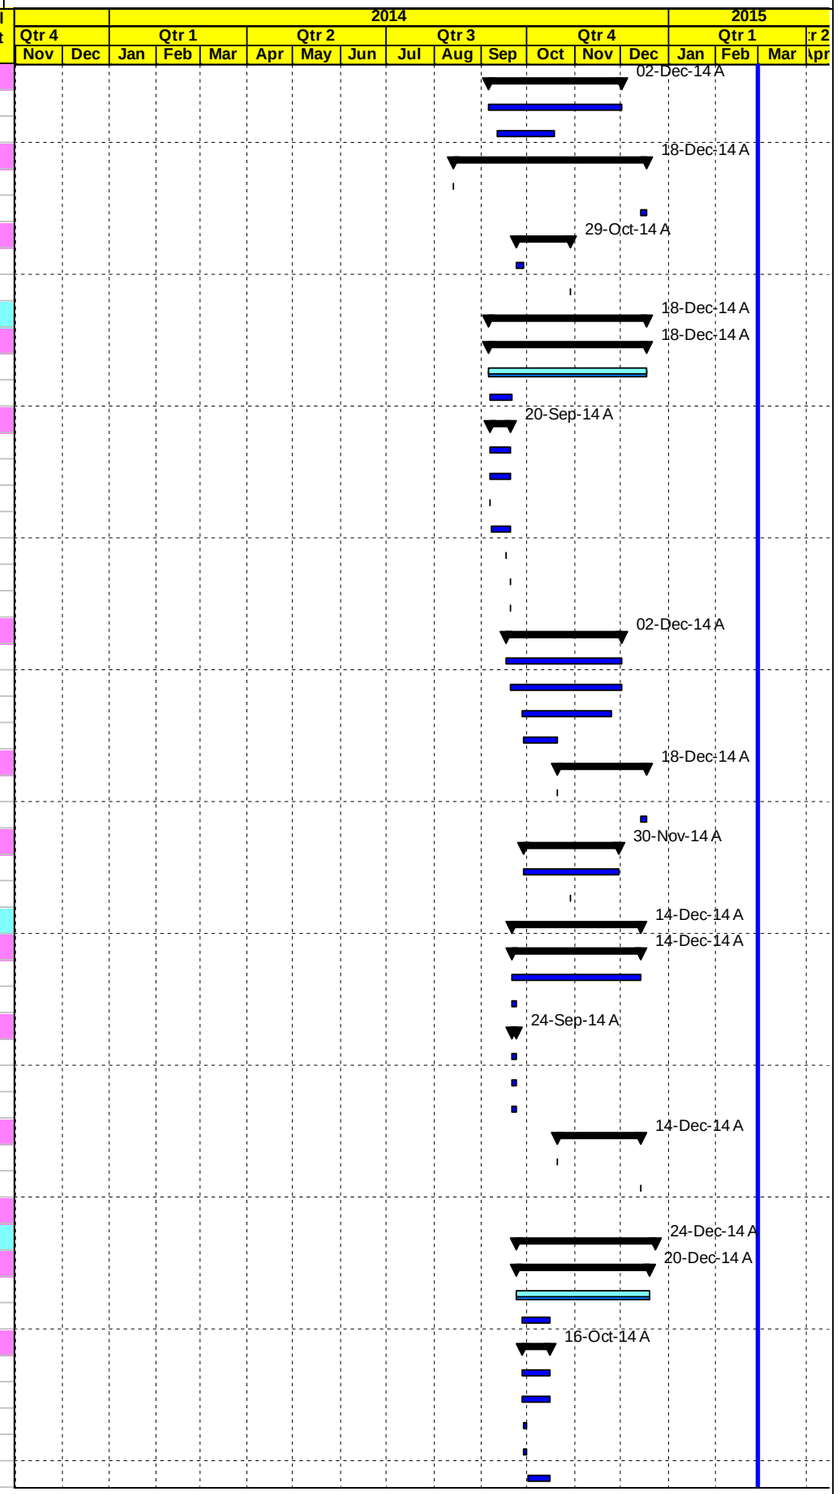

◇ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Page 8 of 10

Date	Revision	Checked	Approved
04-Mar-15			

APCO ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
DST2747-new	Backfilling from Sta. 0+148 to Sta. 0+054.5 (93.5m)	1d	100%	16-Oct-14 A	16-Oct-14 A	
DST2746-new	Bedding from Sta. 0+148 to Sta. 0+054.5 (93.5m)	1d	100%	16-Oct-14 A	16-Oct-14 A	
Civil Chamber work		93d		22-Oct-14 A	24-Dec-14 A	
DST2740	Construct -Flow control Valve chamber (Dia. 300mm) @ Sta.A1+174	12d	100%	22-Oct-14 A	16-Dec-14 A	
DST2750	Construct - Air Valve chamber(Dia. 50mm) combined with Butterfly Valve(Dia. 300mm) @A1+162	72d	100%	15-Nov-14 A	21-Dec-14 A	
DST2757	Construct Shavei Shamron connection chamber at Sta. A1+159 & connect to exist.B.S pipe	23d	100%	18-Nov-14 A	20-Dec-14 A	
DST2730	Construct - Combination Air Valve chamber (Dia. 100mm) @ 1+107	17d	100%	30-Nov-14 A	09-Dec-14 A	
DST2760-new	Construct BFV chamber (Dia. 300mm) for outlet Shavi Shamron pipe at Sta. 1+172	24d	100%	07-Dec-14 A	24-Dec-14 A	
Testing		56d		21-Oct-14 A	14-Dec-14 A	
DST2760	Radiograph Testing	2d	100%	21-Oct-14 A	21-Oct-14 A	
DST2763	Pressure Testing	2d	100%	14-Dec-14 A	14-Dec-14 A	
Reinstatement		11d		05-Nov-14 A	01-Dec-14 A	
DST2800	Concrete Reinstatement	11d	100%	05-Nov-14 A	01-Dec-14 A	
Rock Cutting in Slope		26d		28-May-14 A	09-Aug-14 A	
DST1330	Rock Cut Slope Seg. A From Sta (1+430-1+825, 2+020-2+115,4+920-4+980,5+060-5+100,5+750-5+820,6+560-	26d	100%	28-May-14 A	09-Aug-14 A	
Segment B & C 150 mm Main pipeline at / Location Area(B)		90d		19-Oct-14 A	27-Dec-14 A	
Safety and Milling Asphalt		79d		19-Oct-14 A	21-Dec-14 A	
DST1790	Remove Asphalt	4d	100%	19-Oct-14 A	20-Oct-14 A	
DST1780	Maintain traffic control and safety plan	62d	100%	20-Oct-14 A	21-Dec-14 A	
Pipe Installation		32d		20-Oct-14 A	19-Nov-14 A	
Segment C		32d		20-Oct-14 A	22-Oct-14 A	
DST1834-new	Pipe encasement from Sta. 0+111.80 to Sta. 0+016	1d	100%	20-Oct-14 A	22-Oct-14 A	
DST1834	Bedding (single size aggregate) from Sta. 0+126 to Sta. 0+111.80	5d	100%	20-Oct-14 A	20-Oct-14 A	
DST1820	Trench pipes excavation for150 mm length approx. (126 LM) / Segment C	7d	100%	20-Oct-14 A	22-Oct-14 A	
DST1824	Compact Approved Backfill material ,sub base / base course above pipeline	7d	100%	20-Oct-14 A	22-Oct-14 A	
DST1822	Install 150 mm schedule 40 Steel pipe include testing	7d	100%	20-Oct-14 A	22-Oct-14 A	
Segment B		25d		23-Oct-14 A	19-Nov-14 A	
Double Trench (Sta. 1+000 to Sta. 0+426.94).		25d		23-Oct-14 A	12-Nov-14 A	
DST1800	Double Trench excavation for150 mm main pipeline length approx. (573.06 LM) / Segment B	11d	100%	23-Oct-14 A	12-Nov-14 A	
DST1810-new	Bedding (single size aggregate)	11d	100%	23-Oct-14 A	12-Nov-14 A	
DST3110	Install 150 mm schedule 40 Steel pipe include testing	11d	100%	23-Oct-14 A	12-Nov-14 A	
DST1842-new	Pipe Encasement	11d	100%	23-Oct-14 A	11-Nov-14 A	
DST1830	Compact Approved Backfill material ,sub base / base course above pipeline	11d	100%	23-Oct-14 A	12-Nov-14 A	
Single Trench (Sta. 0+426.94 to Sta. 0+007.24)		13d		23-Oct-14 A	19-Nov-14 A	
DST3070-new	Single Trench excavation for150 mm main pipeline length (432.95 lm) / Segment B	11d	100%	23-Oct-14 A	19-Nov-14 A	
DST3080-new	Bedding (single size aggregate)	11d	100%	23-Oct-14 A	19-Nov-14 A	
DST3100-new	Install 150 mm schedule 40 Steel pipe include testing	11d	100%	23-Oct-14 A	19-Nov-14 A	
DST3090-new	Compact Approved Backfill material, sub base / base course above pipeline	11d	100%	23-Oct-14 A	19-Nov-14 A	
Civil Chamber work		30d		20-Nov-14 A	09-Dec-14 A	
DST1836	Construct -Gate Valve chamber (Dia. 150mm) @ B0+653	5d	100%	20-Nov-14 A	09-Dec-14 A	
DST1828	Construct - Wash out Valve chamber (Dia. 100mm) @ Al Fonduqamiya Entrance (St. @ B0+010)	15d	100%	20-Nov-14 A	25-Nov-14 A	
DST1826	Construct -Gate Valve chamber (Dia. 150mm) @B0+384	16d	100%	20-Nov-14 A	09-Dec-14 A	
Testing		2d		20-Dec-14 A	21-Dec-14 A	
DST1846	Pressure Testing	2d	100%	20-Dec-14 A	21-Dec-14 A	
Reinstatement		4d		25-Dec-14 A	27-Dec-14 A	
DST1849	Asphalt Reinstatement Seg.B&C	4d	100%	25-Dec-14 A	27-Dec-14 A	
Connection Valves in TO14		3d		09-Feb-15 A	17-Feb-15 A	
DST2875	Shavei Shamron connection chamber (Dia. 300mm)	1d	100%	09-Feb-15 A	10-Feb-15 A	
DST2860	Qussin connection (Dia. 250mm) TO14	1d	100%	10-Feb-15 A	11-Feb-15 A	
DST2830	Washout chamber (Dia. 250mm)	1d	100%	10-Feb-15 A	17-Feb-15 A	
DST2840	Combined BFV and AR/AV (dia 75/300)	1d	100%	11-Feb-15 A	11-Feb-15 A	
DST2850	Beit Iba connection (Dia. 75mm)	1d	100%	12-Feb-15 A	17-Feb-15 A	
DST2870	Nablus connection (Dia. 100mm)	1d	100%	12-Feb-15 A	15-Feb-15 A	
Burqa 4" Water Pipeline		29d		15-Jan-15 A	28-Feb-15 A	

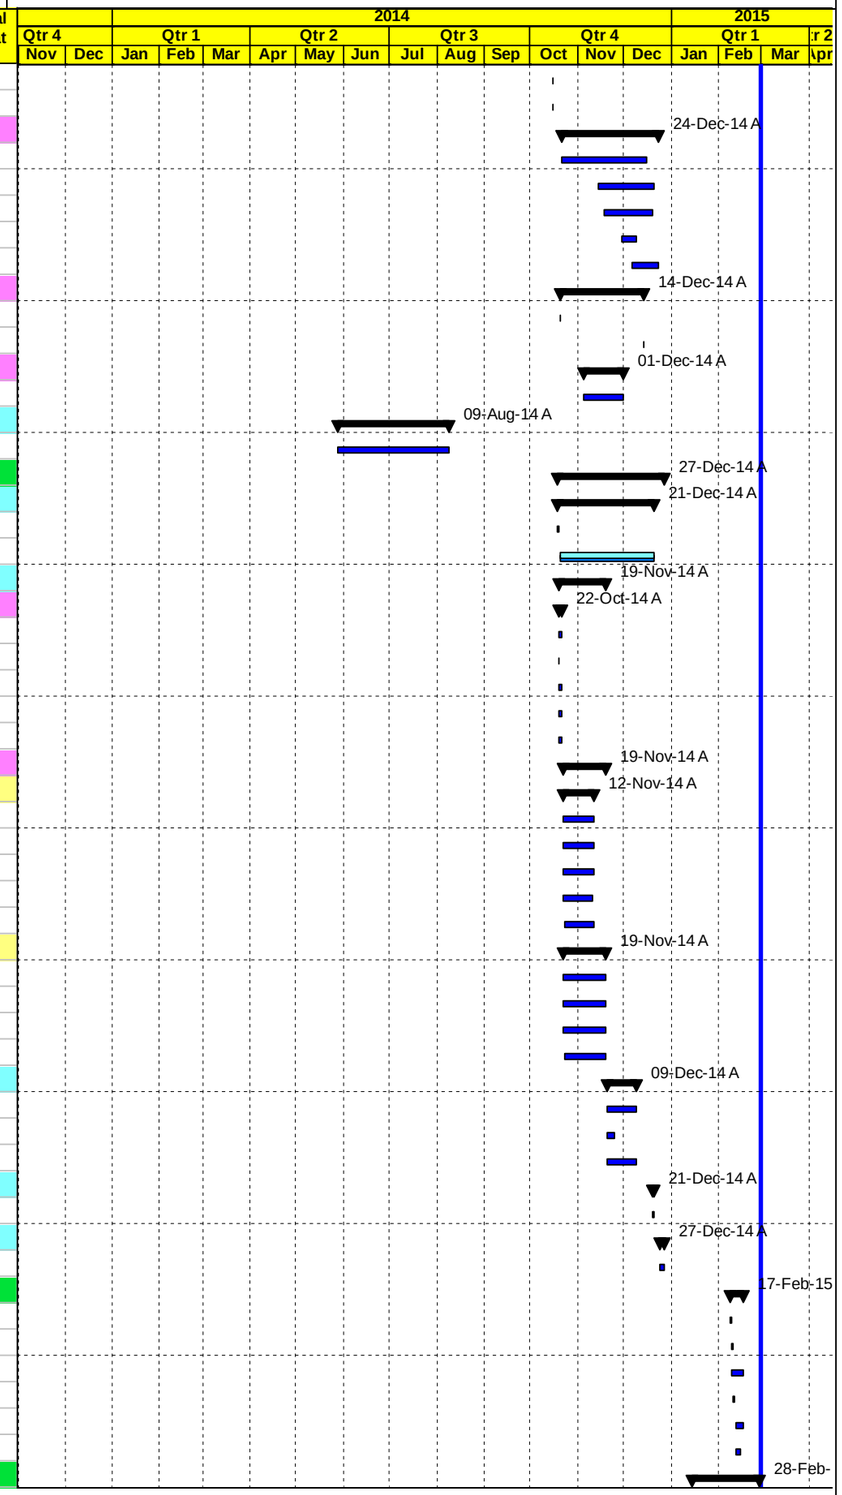

◇ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

APCO/ArCon CONSTRUCTION AND SERVICES

Construction Program
Completed & In Progress Activities

TO13-Updated
Deir- Sharaf Main Pipeline Project

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
Pipeline installation		11d		15-Jan-15 A	04-Feb-15 A	
DST2879-new	Delivery steel pipeline 4"	0d	100%	15-Jan-15 A		
DST2880-new	Trench excavation 4" water pipeline Bedding, install and Backfilling approx.(1200 LM)	11d	100%	17-Jan-15 A	04-Feb-15 A	
Chambers		6d		26-Jan-15 A	17-Feb-15 A	
DST2900-new	Constuct Gate valve (PN 16 DN 150 mm)gate valve and it is chamber at Al fondaqmia elevated reservoir at Sta. (	3d	100%	26-Jan-15 A	17-Feb-15 A	
DST2890-new	Constuct Gate valve chamber (PN 16 DN 50 mm) at Al fondaqmia at Sta. 0+410	3d	100%	27-Jan-15 A	17-Feb-15 A	
DST2895-new	Constuct Gate valve (PN 16 DN 100 mm) at Al fondaqmia at Sta. 0+430	3d	100%	27-Jan-15 A	17-Feb-15 A	
DST2885-new	Constuct two Gate valve chamber (PN 25 DN 100 mm) at Burqa Sta. 1+150 & Sta. 1+152	3d	100%	05-Feb-15 A	08-Feb-15 A	
DST2910-new	Connection 4" water pipeline to the existing chamber	3d	100%	10-Feb-15 A	10-Feb-15 A	
Testing		3d		09-Feb-15 A	09-Feb-15 A	
DST2912-new	Pressure Testing	3d	100%	09-Feb-15 A	09-Feb-15 A	
Reinstatement		5d		25-Feb-15 A	28-Feb-15 A	
DST2914-new	Asphalt Reinstatement	5d	100%	25-Feb-15 A	28-Feb-15 A	
Asphalt Works		40d		29-Dec-14 A	01-Mar-15	3d
DST2920-new	Asphalt Wearing Layer 70mm Thick for Road Shoulders Including Tack coat inculding milling sta. 1+240 to sta. 8+	21d	100%	29-Dec-14 A	08-Feb-15 A	
DST2930-new	Acrylic Paint for Road Marking	5d	90%	25-Jan-15 A	01-Mar-15	4d
DST2934-new	Cat eyes installation LHS & RHS shoulders main line from Sta. 1+240 to Sta. 13+700	5d	80%	17-Feb-15 A	01-Mar-15	3d
Sewer Pipeline from Sta. 0+000 Sta. 0+260		9d		13-Jan-15 A	18-Jan-15 A	
DST2940-new	Excavation 8" UPVC sewer pipelines Bedding, Install and Backfilling including precast concrete manhole (1000 dia	8d	100%	13-Jan-15 A	18-Jan-15 A	
DST2950-new	Connection to the existing sewer manhole	1d	100%	18-Jan-15 A	18-Jan-15 A	
Main Pipeline from Sta. A0+000 to Sta. A13+732, Segment B & C Final works		127d		03-Jun-14 A	03-Mar-15	8d
DST2886	Archeological findings	4d	100%	03-Jun-14 A	05-Jun-14 A	
DST3000-new	Finishing work for chambers internal body included ladders (Part one 18 chambers)	21d	100%	23-Nov-14 A	31-Dec-14 A	
DST2890	Mech. Work including install valves fittings, and flushing pipes (Part one 12 chambers)	16d	100%	08-Dec-14 A	31-Dec-14 A	
DST3050-new	Finishing work for chambers internal body included ladders (Part two 18 chambers)	21d	90%	01-Jan-15 A	03-Mar-15	6d
DST2900	Mech. Work including install valves fittings, and flushing pipes (Part Two 12 chambers)	15d	100%	01-Jan-15 A	28-Jan-15 A	
DST3010-new	Pipeline Marking	10d	95%	26-Jan-15 A	01-Mar-15	4d
DST3120	Mech. Work including install valves fittings, and flushing pipes (Part Three 12 chambers)	15d	100%	29-Jan-15 A	17-Feb-15 A	
DST1840	Connection to the existing WSP and elevated tank	2d	100%	08-Feb-15 A	26-Feb-15 A	
DST2910	Disinfection and flushing For Pipeline	3d	100%	23-Feb-15 A	25-Feb-15 A	
Upgrade the Remote Flow Monitoring GBRS/GSM System		31d		25-Jan-15 A	26-Feb-15 A	
DST3015-new	Design Remote Flow Monitoring GBRS/GSM System	6d	100%	25-Jan-15 A	27-Jan-15 A	
DST3020-new	Order Remote Flow Monitoring GBRS/GSM System	0d	100%	28-Jan-15 A		
DST3030-new	Delivery	0d	100%	01-Feb-15 A		
DST3040-new	Installation	9d	100%	01-Feb-15 A	26-Feb-15 A	
Post Construction Phase		10d		01-Feb-15 A	26-Feb-15 A	
Post Construction Submittals		0d		01-Feb-15 A	01-Feb-15 A	
DST2930	Start preparation Operation and maintenance manual	0d	100%	01-Feb-15 A		
Start up, Training and commissioning		5d		23-Feb-15 A	26-Feb-15 A	
DST3030	Pre-commissioning	5d	100%	23-Feb-15 A	26-Feb-15 A	
Demobilization		0d				0d
Post Construction activities		0d				0d

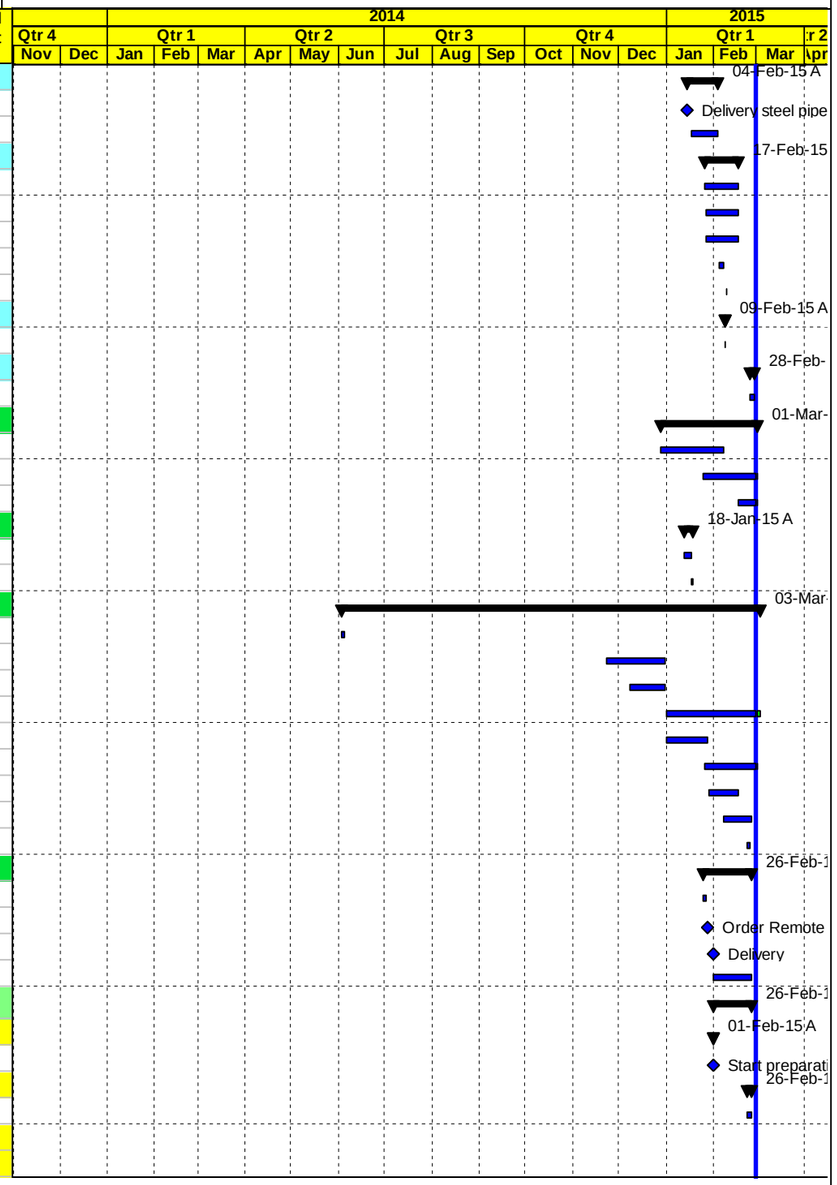

◆ Milestone Early Bar — Actual Level of Effort — Level of Effort
Actual Work — Early Bar — Summary
◆ Milestone Actual — Critical Bar

Date	Revision	Checked	Approved
04-Mar-15			

C | Progress S-Curve Versus Actual

Construction Progress S-Curve

Total Contract Value	**$**	**6,859,034**
Total Contract Value (Day Work Not Included):	**$**	**6,509,034**
Total Contract Value (VO1-BL2):	**$**	**6,377,880**
Total Contract Value (VO2-BL3):	**$**	**6,641,249.59**
Total Contract Value (VO4):	**$**	**6,843,844.57**
Project Duration :	**450 Calender Days**	
Time Extension	**13 Calender Days**	
Revised Project Duration :	**463 Calender Days**	
NTP Date:	**3-Dec-13**	

*** Day Work Not Included**

	December. 2013	January. 2014	February. 2014	March. 2014	April. 2014	May. 2014	June. 2014	July. 2014	August. 2014	September. 2014	October. 2014	November. 2014	December. 2014	January. 2015	February. 2015	March. 2015	TOTAL
Planned Value (Baseline2)	$ 193,915	$ 54,048	$ -	$ 73,274	$ 359,440	$ 487,354	$ 473,193	$ 339,393	$ 794,438	$ 702,148	$ 730,757	$ 595,252	$ 905,160	$ 445,782	$ 223,726	$ -	$6,377,880
Planned Value (CUM)	$ 193,915	$ 247,963	$ 247,963	$ 321,237	$ 680,677	$ 1,168,031	$ 1,641,224	$ 1,980,617	$ 2,775,055	$ 3,477,203	$ 4,207,960	$ 4,803,212	$ 5,708,372	$ 6,154,154	$ 6,377,880	$ 6,377,880	
% Planned	3.0%	0.8%	0.0%	1.1%	5.6%	7.6%	7.4%	5.3%	12.5%	11.0%	11.5%	9.3%	14.2%	7.0%	3.5%	0.0%	**100%**
% Planned (CUM) BL2	3.0%	3.9%	3.9%	5.0%	10.7%	18.3%	25.7%	31.1%	43.5%	54.5%	66.0%	75.3%	89.5%	96.5%	100.0%	100.0%	
Planned Value (Baseline3)	$ 193,915	$ 54,048	$ -	$ 73,274	$ 359,440	$ 487,354	$ 776,652	$ 446,376	$ 708,849	$ 930,516	$ 422,776	$ 512,146	$ 477,149	$ 966,992	$ 231,763	$ -	**$ 6,641,249.59**
Planned Value (CUM)	$ 193,915	$ 247,963	$ 247,963	$ 321,237	$ 680,677	$ 1,168,031	$ 1,944,683	$ 2,391,059	$ 3,099,908	$ 4,030,424	$ 4,453,200	$ 4,965,346	$ 5,442,495	$ 6,409,487	$ 6,641,250	$ 6,641,250	
% Planned	2.9%	0.8%	0.0%	1.1%	5.4%	7.3%	11.7%	6.7%	10.7%	14.0%	6.4%	7.7%	7.2%	14.6%	3.5%	0.0%	**100.00%**
% Planned (CUM) BL3	2.9%	3.7%	3.7%	4.8%	10.2%	17.6%	29.3%	36.0%	46.7%	60.7%	67.1%	74.8%	81.9%	96.5%	100.0%	100.0%	
Actual Value	$ 193,915	$ 54,048	$ -	$ 73,274	$ 359,440	$ 487,354	$ 776,652	$ 446,376	$ 708,849	$ 930,516	$ 422,776	$ 477,149	$ 515,440	$ 638,298	$ 685,674		**$ 6,769,760.85**
Actual Value (CUM)	$ 193,915	$ 247,963	$ 247,963	$ 321,237	$ 680,677	$ 1,168,031	$ 1,944,683	$ 2,391,059	$ 3,099,908	$ 4,030,424	$ 4,453,200	$ 4,930,349	$ 5,445,789	$ 6,084,087	$ 6,769,761		
% Actual	2.8%	0.8%	0.0%	1.1%	5.3%	7.1%	11.3%	6.5%	10.4%	13.6%	6.2%	7.0%	7.5%	9.3%	10.0%		**98.9%**
% Actual (CUM)	2.8%	3.6%	3.6%	4.7%	9.9%	17.1%	28.4%	34.9%	45.3%	58.9%	65.1%	72.0%	79.6%	88.9%	98.9%		

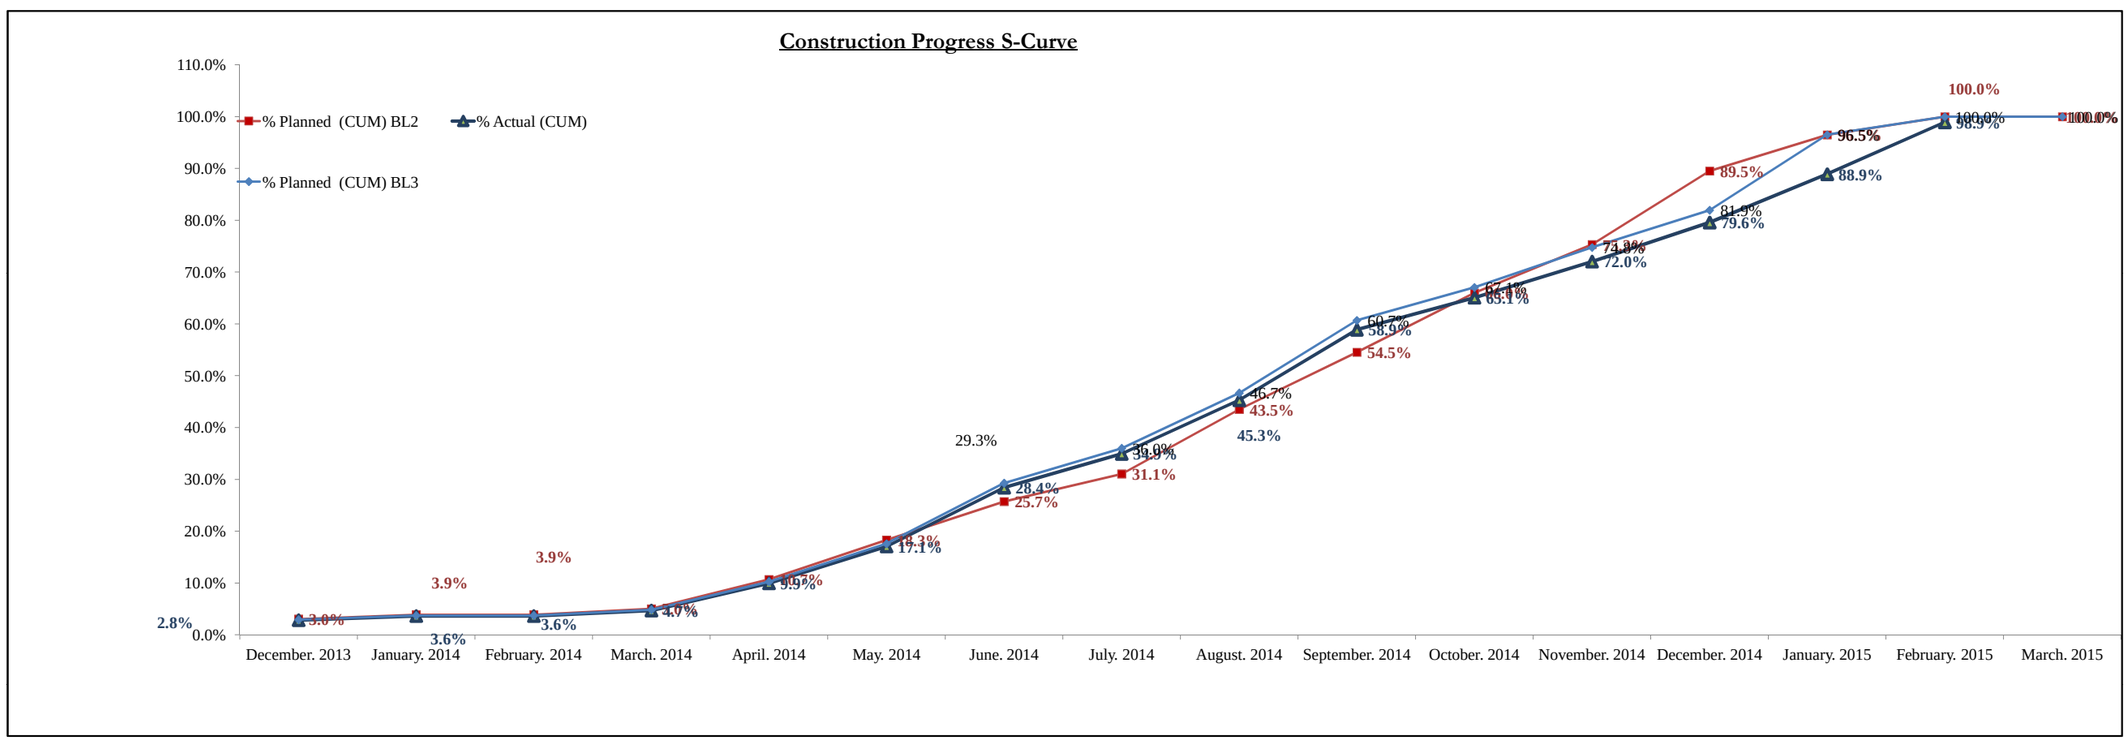

D | Site Memos Log

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project
Site Memo Log (E-C)

SUBMITTAL				TRACKING DATES			
Spec. No.	Submittal No	Subject	Project	Submitted on (M/D/Y)	Returned on (M/D/Y)	Review Days	Remarks
	SM-13-00013-DST-E-C-001	Joint walkthrough on December 24,2013	DST	01/13/14	01/14/14	1	Site Instruction
	SM-13-00013-DST-E-C-002	Mobilization Items	DST	04/15/14	04/16/14	1	Site Instruction
	SM-13-00013-DST-E-C-003	Revised List of Chambers	DST	04/23/14	04/23/14	0	Site Instruction
	SM-13-00013-DST-E-C-004	Revised Segments for Location of Cut Slopes	DST	06/03/14	06/03/14	0	Site Instruction
	SM-13-00013-DST-E-C-005	Night Shift Works	DST	07/08/14	07/08/14	0	Site Instruction
	SM-13-00013-DST-E-C-006	Concrete Compressive Strength of GV Chamber Walls	DST	07/09/14	07/09/14	0	Site Instruction
	SM-13-00013-DST-E-C-007	Concrete Compressive Strength Test Results	DST	07/22/14	07/22/14	0	Site Instruction
	SM-13-00013-DST-E-C-008	Response to Contractor's Site Memo "SM-13-00013-DST-C-E-002"	DST	07/23/14	07/23/14	0	Site Instruction
	SM-13-00013-DST-E-C-009	Asphalt Reinstatement Width - Second Layer	DST	09/11/14	09/11/14	0	Site Instruction
	SM-13-00013-DST-E-C-010	Relocation of Seilt Adaher Connection Chamber	DST	09/11/14	09/11/14	0	Site Instruction
	SM-13-00013-DST-E-C-011	Site Modification	DST	10/19/14	10/19/14	0	Site Instruction
	SM-13-00013-DST-E-C-012	Additional Sewer Lines	DST	10/22/14	10/22/14	0	Site Instruction
	SM-13-00013-DST-E-C-013	Additional Works for the 150 mm Pipeline at Al Fondaqumiya	DST	10/23/14	10/23/14	0	Site Instruction
	SM-13-00013-DST-E-C-014	Mail Server System at the West Bank Water Department (WBWD)	DST	10/28/14	10/28/14	0	Site Instruction
	SM-13-00013-DST-E-C-015	Concrete Encasement for 150mm Pipeline	DST	10/27/14	10/27/14	0	Site Instruction
	SM-13-00013-DST-E-C-016	Response to Contractor's Site Memo "SM-13-00013-DST-C-E-005"	DST	10/30/14	10/30/14	0	Site Instruction
	SM-13-00013-DST-E-C-017	Relocation of Mainline flow Monitoring chamber"PD-05" (Shavi Shamron Montoring chamber	DST	11/02/14	11/02/14	0	Site Instruction
	SM-13-00013-DST-E-C-018	Response to Contractor's Site Memo "SM-13-00013-DST-C-E-006"	DST	11/06/14	11/06/14	0	Site Instruction
	SM-13-00013-DST-E-C-019	Concrete Compressive Strength	DST	11/09/14	11/09/14	0	Site Instruction
	SM-13-00013-DST-E-C-020	Telephone Service	DST	11/11/14	11/11/14	0	Site Instruction
	SM-13-00013-DST-E-C-021	Additional Works	DST	11/12/14	11/12/14	0	Site Instruction
	SM-13-00013-DST-E-C-022	Box Culverts	DST	11/20/14	11/20/14	0	Site Instruction
	SM-13-00013-DST-E-C-023	Relocation of Air Vent	DST	12/30/14	12/30/14	0	Site Instruction
	SM-13-00013-DST-E-C-024	Letter Received from Al Fundaqomeya Village Council	DST	01/13/15	01/13/15	0	Site Instruction
	SM-13-00013-DST-E-C-025	Box Culvert at Sta. 13+640	DST	01/27/15	01/27/15	0	Site Instruction
	SM-13-00013-DST-E-C-026	Response to Contractor's Site Memo"SM-13-00013-DST-C-E-007"	DST	02/02/15	02/02/15	0	Response to Site Memo No. C-E-007
	SM-13-00013-DST-E-C-027	Response to Contractor's Site Memo"SM-13-00013-DST-C-E-008"	DST	02/02/15	02/02/15	0	Response to Site Memo No. C-E-008
	SM-13-00013-DST-E-C-028	Asphalt work for shoulders	DST	02/02/15	02/02/15	0	Site Instruction
	SM-13-00013-DST-E-C-029	Supply and install cat eyes	DST	02/02/15	02/02/15	0	Site Instruction
	SM-13-00013-DST-E-C-030	Initial Punch List for Deir Sharaf Main Pipeline Project.	DST	02/10/15	02/10/15	0	Attached

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project
Site Memo Log (C-E)

SUBMITTAL				TRACKING DATES			
Spec. No.	Submittal No	Subject	Project	Submitted on (M/D/Y)	Returned on (M/D/Y)	Review Days	Remarks
1	SM-13-00013-DST-C-E-001	Confirmation of project's walkthrough conducted on December 24,2013	DST	01/07/14	01/07/14	0	Other
2	SM-13-00013-DST-C-E-002	Reply Response to RFI #015	DST	07/01/14	07/01/14	0	Other
3	SM-13-00013-DST-C-E-003	Shavi Shamroun Connections	DST	08/06/14	08/06/14	0	Other
4	SM-13-00013-DST-C-E-004	Thanks letters	DST	09/16/14	09/16/14	0	Other
5	SM-13-00013-DST-C-E-005	Milling of Existing Asphalt	DST	09/22/14	09/22/14	0	Other
6	SM-13-00013-DST-C-E-006	Relocation of Mainline flow Monitoring chamber (Shavi Sbamron Monitoring chamber)	DST	11/04/14	11/04/14	0	Other
7	SM-13-00013-DST-C-E-007	Telephone Service	DST	11/12/14	11/12/14	0	Other
8	SM-13-00013-DST-C-E-008	Al Foundqumiya chambers	DST	02/02/15	02/02/15	0	Other

E | Inspection Requests Log

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-001-A	CMC office	01/04/14	01/05/14	01/05/14	0	C
	IR-13-00013-DST-001-B	CMC office	02/02/14	02/02/14	02/03/14	1	A
	IR-13-00013-DST-002-A	Installation for Two Temporary Signs at location as specified in SUB-13-00013-DST-020-A	01/14/14	01/14/14	01/14/14	0	C
	IR-13-00013DST-002-B	Material, fabrication and installation for Two Temporary Signs at location as specified in SUB-13-00013-DST-020-A	01/16/14	01/16/14	01/16/14	0	A
	IR-13-00013-DST-003-A	Construction facilities	01/26/14	01/26/14	01/27/14	1	C
	IR-13-00013-DST-003-B	Construction facilities	01/28/14	01/29/14	01/29/14	0	A
	IR-13-00013-DST-004-A	Storage yard	01/26/14	01/26/14	01/27/14	1	C
	IR-13-00013-DST-004-B	Storage yard	01/28/14	01/29/14	01/29/14	0	A
	IR-13-00013-DST-005-A	Traffic control signs / phase 1	01/26/14	01/27/14	01/29/14	2	A
	IR-13-00013-DST-006-A	Safety facilities concrete barrires	02/23/14	02/24/14	02/25/14	1	A
	IR-13-00013-DST-007-A	Welders training and testing	02/25/14	02/27/14	03/02/14	3	A
	IR-13-00013-DST-008-A	Pipe identification tape	03/03/14	03/04/14	03/04/14	0	A
	IR-13-00013-DST-009-A	Off shelf-12 3/4 inch OD-steel pipes ,QTY=366mm	03/03/14	03/05/14	03/05/14	0	C
	IR-13-00013-DST-009-B	Off shelf-12 3/4 inch OD-steel pipes ,QTY=366mm	03/05/14	03/06/14	03/10/14	4	A
	IR-13-00013-DST-010-A	Welders testing	03/04/14	03/05/14	03/12/14	7	C
	IR-13-00013-DST-010-B	Welders testing	03/09/14	03/11/14	03/12/14	1	A
	IR-13-00013-DST-011-A	Trial batch for B350,B250 and B150	03/06/14	03/10/14	03/11/14	1	A
	IR-13-00013-DST-012-A	Cement lining repair mock up for Fabricated Metered Bends using Fosroc Material	03/09/14	03/09/14	03/10/14	1	A
	IR-13-00013-DST-013-A	12 3/4 inch steel pipes,QTY:298.74m	03/13/14	03/16/14	03/18/14	2	A
	IR-13-00013-DST-014-A	Conduct compresseive strength at 7 days for BONYAN concrete trial batch & related aggregate sieve analysis	03/16/14	03/17/14	03/18/14	1	A
	IR-13-00013-DST-015-A	Concrete trial batch for MUASI concrete mix design	03/18/14	03/19/14	03/20/14	1	A
	IR-13-00013-DST-016-A	Trial pits for existing water pipeline in St. 10+580 & St. 10+750	03/18/14	03/19/14	03/20/14	1	A
	IR-13-00013-DST-017-A	Safety precautions and traffic control while conducting Trial pits for existing water pipeline in St. 10+580 & St. 10+750	03/19/14	03/19/14	03/20/14	1	A
	IR-13-00013-DST-018-A	12 3/4 inch OD-Sch. 20-ERW-ASTM A53,Grade B. wall thickness 6.35 mm steel pipes,QTY=2000m	03/19/14	03/20/14	03/20/14	0	A
	IR-13-00013-DST-019-A	Pipeline alignment marked on site from St. 10+400 to St. 12+120	03/20/14	03/23/14	03/25/14	2	A
	IR-13-00013-DST-020-A	Manufacturing process of external polyethylene coating & internal cement lining for 12 3/4 OD pipes,Qty =2000m	03/23/14	03/24/14	03/26/14	2	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-021-A	Concrete trial batch of BONYAN concrete mix design	03/23/14	03/24/14	03/25/14	1	A
	IR-13-00013-DST-022-A	Cement lining repair mock up for Fabricated Metered Bends using Fosroc Material (Rendroc S and FC for Fair Face finish)	03/25/14	03/25/14	03/25/14	0	A
	IR-13-00013-DST-023-A	1-Site fabricated 11 ¼ ° Elbow 12 inch-QTY=15, 90° 2- Standard Elbow-QTY=15, 45° standard Elbow-QTY=15, Reduce Tee 12x12x6-QTY=6, Reduce Tee 12x12x8-QTY=2 and Reduce Tee 12x12x10-QTY=2 3-CANUSA Shrinkable sheet, QTY=25.	03/25/14	03/26/14	03/26/14	0	D
	IR-13-00013-DST-023-B	Inspection for : 1-Site fabricated 11 ¼ ° Elbow 12 inch-QTY=15, 90° 2- Standard Elbow-QTY=15, 45° standard Elbow-QTY=15, Reduce Tee 12x12x6-QTY=6, Reduce Tee 12x12x8-QTY=2 and Reduce Tee 12x12x10-QTY=2 3-CANUSA Shrinkable sheet, QTY=25. Note: Standard fittings-FIP products.	02/15/15	02/15/15	02/15/15	0	A
	IR-13-00013-DST-024-A	compressive strength at 7 days for MUASI concrete trial batch & related aggregate sieve analysis	03/25/14	03/26/14	03/27/14	1	A
	IR-13-00013-DST-025-A	Trench excavation from St. 12+105 to St. 12+036	03/25/14	03/26/14	03/30/14	4	A
	IR-13-00013-DST-026-A	Pipeline installaion and bedding backfilling from St. 12+105 to St. 12+036	03/25/14	03/26/14	03/30/14	4	A
	IR-13-00013-DST-027-A	Trench backfilling from St. 12+105 to St. 12+036	03/25/14	03/26/14	03/30/14	4	A
	IR-13-00013-DST-028-A	Trench excavation from St. 12+036 to St. 11+960	03/27/14	03/27/14	03/30/14	3	A
	IR-13-00013-DST-029-A	Pipeline installation and bedding backfilling from St. 12+036 to St. 11+960	03/27/14	03/27/14	03/30/14	3	A
	IR-13-00013-DST-030-A	Trench backfilling from St. 12+036 to St. 11+960	03/27/14	03/27/14	03/30/14	3	A
	IR-13-00013-DST-031-A	Internal cement lining manufacture process for externally coated pipe-FIP product (12 inch,QTY=2000 m)	03/27/14	03/27/14	03/30/14	3	A
	IR-13-00013-DST-032-A	Trench excavation from St. 11+960 to St. 11+870	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00013-DST-033-A	Pipeline installation and bedding backfilling from St. 11+960 to St. 11+870	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00013-DST-034-A	Trench backfilling from St. 11+960 to St. 11+870	03/27/14	03/29/14	03/30/14	1	A
	IR-13-00013-DST-035-A	Conducting radiographic nondestructive test for fabricated bends in attendees of MOREX agency , the quantities will be as follow: 12 inch 11 ¼ bends=29 piece 6 inch 11 ¼ bends=8 piece	03/27/14	03/30/14	03/31/14	1	A
	IR-13-00013-DST-036-A	Trench excavation from St. 11+870 to St. 11+800	03/30/14	03/30/14	03/31/14	1	A
	IR-13-00013-DST-037-A	Pipeline installation and bedding from St. 11+870 to St. 11+800	03/30/14	03/30/14	03/31/14	1	A
	IR-13-00013-DST-038-A	Trench backfilling fromSt. 11+870 to St. 11+800	03/30/14	03/30/14	03/31/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-039-A	12 3/4 inch steel pipes,QTY:800 m	03/30/14	03/31/14	04/01/14	1	A
	IR-13-00013-DST-040-A	Inspection for the following FIP-fittings: Elbow 45° /12''-QTY= 1 Elbow 90°/12''-QTY=3 Tee 300x300x250-QTY=2 Tee 300x300x150-QTY=1	03/30/14	03/31/14	04/01/14	1	C
	IR-13-00013-DST-040-B	Inspection for the following FIP-fittings: Elbow 45° /12''-QTY= 1 Elbow 90°/12''-QTY=3 Tee 300x300x250-QTY=2 Tee 300x300x150-QTY=1	02/15/15	02/15/15	02/15/15	0	A
	IR-13-00013-DST-041-A	Trench excavation from St. 11+800 to St. 11+730	03/30/14	03/31/14	04/01/14	1	A
	IR-13-00013-DST-042-A	Pipe installaion and bedding from St. 11+800 to St. 11+730	03/30/14	03/31/14	04/01/14	1	A
	IR-13-00013-DST-043-A	Trench backfilling from St. 11+800 to St. 11+730	03/30/14	03/31/14	04/01/14	1	A
	IR-13-00013-DST-044-A	compressive strength at 7 days for BONYAN concrete trial batch & related aggregate sieve analysis	03/31/14	03/31/14	04/01/14	1	A
	IR-13-00013-DST-045-A	Trench excavation from St. 11+730 to St. 11+680	03/31/14	04/02/14	04/02/14	0	A
	IR-13-00013-DST-046-A	Pipeline installation and bedding from St. 11+730 to St. 11+680	03/31/14	04/02/14	04/02/14	0	A
	IR-13-00013-DST-047-A	Trench backfilling from St. 11+730 to St. 11+680	03/31/14	04/02/14	04/02/14	0	A
	IR-13-00013-DST-048-A	Trench excavation from St. 11+680 to St. 11+600	04/01/14	04/03/14	04/03/14	0	A
	IR-13-00013-DST-049-A	Pipeline installation and bedding from St. 11+680 to St. 11+600	04/01/14	04/03/14	04/03/14	0	A
	IR-13-00013-DST-050-A	Trench backfilling fromSt. 11+680 to St. 11+600	04/01/14	04/03/14	04/03/14	0	A
	IR-13-00013-DST-051-A	Inspection for : 12 ¾ inch steel pipes-FIP product, QTY: 704.07 m Shrinkable sheet-CANUCA type-WLO, QTY=58 sheet	04/01/14	04/02/14	04/03/14	1	A
	IR-13-00013-DST-052-A	Trench excavation from St. 11+600 to St. 11+500	04/02/14	04/05/14	04/07/14	2	A
	IR-13-00013-DST-053-A	Pipeline installation and bedding from St. 11+600 to St. 11+500	04/02/14	04/05/14	04/07/14	2	A
	IR-13-00013-DST-054-A	Trench backfilling from St. 11+600 to St. 11+500	04/02/14	04/05/14	04/07/14	2	A
	IR-13-00013-DST-055-A	Trench excavation from St. 11+500 to St. 11+380	04/03/14	04/06/14	04/07/14	1	A
	IR-13-00013-DST-056-A	Pipeline installation and bedding from St. 11+500 to St. 11+380	04/03/14	04/06/14	04/07/14	1	A
	IR-13-00013-DST-057-A	Trench backfilling from St. 11+500 to St. 11+380	04/03/14	04/06/14	04/07/14	1	A
	IR-13-00013-DST-058-A	Trench excavation from St. 11+380 to St. 11+330	04/06/14	04/07/14	04/09/14	2	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-059-A	Compressive strength at 28 days for BONYAN concrete first trial batch	04/06/14	04/07/14	04/09/14	2	A
	IR-13-00013-DST-060-A	Inspection for the following FIP-fittings:	04/06/14	04/07/14	04/14/14	7	A
		Elbow 45° /12''-QTY= 12					
		Elbow 90°/12''-QTY=13					
		Tee 300x300x250-QTY=2					
		Tee 300x300x200-QTY=2					
		Tee 300x300x150-QTY=4					
	IR-13-00013-DST-061-A	Pipeline installation and bedding from St. 11+380 to St. 11+330	04/06/14	04/08/14	04/09/14	1	A
	IR-13-00013-DST-062-A	Trench backfilling from St. 11+380 to St. 11+330	04/06/14	04/08/14	04/09/14	1	A
	IR-13-00013-DST-063-A	Trench excavation from St. 11+330 to St. 11+270	04/07/14	04/09/14	04/09/14	0	A
	IR-13-00013-DST-064-A	Pipeline installation and bedding from St. 11+330 to St. 11+270	04/07/14	04/09/14	04/09/14	0	A
	IR-13-00013-DST-065-A	Trench backfilling from St. 11+330 to St. 11+270	04/07/14	04/09/14	04/09/14	0	A
	IR-13-00013-DST-066-A	Trench excavation from St. 11+270 to St. 11+200	04/08/14	04/10/14	04/10/14	0	A
	IR-13-00013-DST-067-A	Pipeline installation and bedding from St. 11+270 to St. 11+200	04/08/14	04/10/14	04/10/14	0	A
	IR-13-00013-DST-068-A	Trench backfilling from St. 11+270 to St. 11+200	04/08/14	04/10/14	04/10/14	0	A
	IR-13-00013-DST-069-A	· Polyethylene coated pipes-12 inch FIP product, QTY= 326.11 m (Delivered on Apr. 06)	04/08/14	04/08/14	04/09/14	1	A
		· Polyethylene coated pipes-12 inch FIP product, QTY= 144.38 m (Delivered on Apr. 08)					
		· Epoxy coated pipes-12 inch FIP product, QTY= 36.27 m (Delivered on Apr. 06)					
		· Shrinkable sheet-CANUCA type, QTY= 29 (Delivered on Apr. 06)					
		· Shrinkable sheet-CANUCA type, QTY= 10 (Delivered on Apr. 08)					
	IR-13-00013-DST-070-A	Trench excavation from St. 11+200 to St. 11+130	04/09/14	04/12/14	04/14/14	2	A
	IR-13-00013-DST-071-A	Pipeline installation and bedding from St. 11+200 to St. 11+130	04/09/14	04/12/14	04/14/14	2	A
	IR-13-00013-DST-072-A	Trench backfilling from St. 11+200 to St. 11+130	04/09/14	04/12/14	04/14/14	2	A
	IR-13-00013-DST-073-A	Trench excavation from St. 11+130 to St. 11+030	04/10/14	04/13/14	04/14/14	1	A
	IR-13-00013-DST-074-A	Pipeline installation and bedding from St. 11+130 to St. 11+030	04/10/14	04/13/14	04/14/14	1	A
	IR-13-00013-DST-075-A	Trench backfilling from St. 11+130 to St. 11+030	04/10/14	04/13/14	04/14/14	1	A
	IR-13-00013-DST-076-A	Trench excavation from St. 11+030 to St. 10+950	04/13/14	04/14/14	04/14/14	0	A
	IR-13-00013-DST-077-A	Pipeline installation and bedding from St. 11+030 to St. 10+950	04/13/14	04/14/14	04/14/14	0	A
	IR-13-00013-DST-078-A	Trench backfilling from St. 11+030 to St. 10+950	04/13/14	04/14/14	04/14/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-079-A	Trench excavation from St. 10+950 to St. 11+870	04/13/14	04/15/14	04/16/14	1	A
	IR-13-00013-DST-080-A	Pipeline installation and bedding from St. 10+950 to St. 10+870	04/13/14	04/15/14	04/16/14	1	A
	IR-13-00013-DST-081-A	Trench backfilling from St. 10+950 to St. 10+870	04/13/14	04/15/14	04/16/14	1	A
	IR-13-00013-DST-082-A	Trench excavation from St. 10+870 to St. 10+780	04/14/14	04/16/14	04/16/14	0	A
	IR-13-00013-DST-083-A	Pipeline installation and bedding from St. 10+870 to St. 11+780	04/14/14	04/16/14	04/16/14	0	A
	IR-13-00013-DST-084-A	Trench backfilling from St. 10+870 to St. 10+780	04/14/14	04/16/14	04/16/14	0	A
	IR-13-00013-DST-085-A	Trench excavation from St. 10+780 to St. 10+700	04/14/14	04/16/14	04/17/14	1	A
	IR-13-00013-DST-086-A	Pipeline installation and bedding from St. 10+780 to St. 10+700	04/14/14	04/16/14	04/17/14	1	A
	IR-13-00013-DST-087-A	Trench backfilling from St. 10+780 to St. 10+700	04/14/14	04/16/14	04/17/14	1	A
	IR-13-00013-DST-088-A	Compressive strength at 28 days for MUWASI concrete first trial batch	04/15/14	04/16/14	04/17/14	1	A
	IR-13-00013-DST-089-A	Inspection for : 12 inch -polyethylene coated pipes /Grade B ASTM A53 ERW welded steel pipes-Borusan/ Middle East Tube Company Ltd. product., QTY= 866.2 m 12 inch-FBE primer coated pipes /Grade B ASTM A53 ERW welded steel pipes-Borusan/ Middle East Tube Company Ltd. product.QTY= 122 m Shrinkable sheet-CANUCA WLC-KLC type (Supplier Middle East Tube Company Ltd .),QTY=70 sheet	04/15/14	04/16/14	04/19/14	3	A
	IR-13-00013-DST-090-A	Trench excavation from St. 10+700 to St. 10+620	04/15/14	04/17/14	04/17/14	0	A
	IR-13-00013-DST-091-A	Pipeline installation and bedding from St. 10+700 to St. 10+620	04/15/14	04/17/14	04/17/14	0	A
	IR-13-00013-DST-092-A	Trench backfilling from St. 10+700 to St. 10+620	04/15/14	04/17/14	04/17/14	0	A
	IR-13-00013-DST-093-A	Trench excavation from St. 10+620 to St. 10+540	04/16/14	04/19/14	04/21/14	2	A
	IR-13-00013-DST-094-A	Pipeline installation and bedding from St. 10+620 to St. 10+540	04/16/14	04/19/14	04/21/14	2	A
	IR-13-00013-DST-095-A	Trench backfilling from St. 10+620 to St. 10+540	04/16/14	04/19/14	04/21/14	2	A
	IR-13-00013-DST-096-A	Trench excavation fromSt. 10+540 to St. 10+460	04/17/14	04/20/14	04/21/14	1	A
	IR-13-00013-DST-097-A	Pipeline installation and bedding from St. 10+540 to St. 10+460	04/17/14	04/20/14	04/21/14	1	A
	IR-13-00013-DST-098-A	Trench backfilling from St. 10+540 to St. 10+460	04/17/14	04/20/14	04/21/14	1	A
	IR-13-00013-DST-099-A	Trench excavation from St. 10+460 to St. 10+380	04/17/14	04/21/14	04/22/14	1	A
	IR-13-00013-DST-100-A	Pipeline installation and bedding from St. 10+460 to St. 10+380	04/17/14	04/21/14	04/22/14	1	A
	IR-13-00013-DST-101-A	Trench backfilling from St. 10+460 to St. 10+380	04/17/14	04/21/14	04/22/14	1	A
	IR-13-00013-DST-102-A	Pipeline alignment marked on site from St. 9+700 to St. 10+400	04/17/14	04/22/14	04/22/14	0	C
	IR-13-00013-DST-102-B	Pipeline alignment marked on site from St. 9+700 to St. 10+400	04/22/14	04/22/14	04/23/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-103-A	Trench excavation from St. 10+380 to St. 10+300	04/21/14	04/23/14	04/24/14	1	A
	IR-13-00013-DST-104-A	Pipeline installation and bedding from St. 10+380 to St. 10+300	04/21/14	04/23/14	04/24/14	1	A
	IR-13-00013-DST-105-A	Trench backfilling from St. 10+380 to St. 10+300	04/21/14	04/23/14	04/24/14	1	A
	IR-13-00013-DST-106-A	Trench excavation from St. 10+300 to St. 10+220	4/22/2014	4/24/2014	04/24/14	0	A
	IR-13-00013-DST-107-A	Pipeline installation and bedding from St. 10+300 to St. 10+220	04/22/14	04/24/14	04/24/14	0	A
	IR-13-00013-DST-108-A	Trench backfilling from St. 10+300 to St. 10+220	04/22/14	04/24/14	04/24/14	0	A
	IR-13-00013-DST-109-A	Trench excavation from St. 10+220 to St. 10+120	04/23/14	04/26/14	04/27/14	1	A
	IR-13-00013-DST-110-A	Pipeline installation and bedding from St. 10+220 to St. 10+120	04/23/14	04/26/14	04/27/14	1	A
	IR-13-00013-DST-111-A	Trench backfilling from St. 10+220 to St. 10+120	04/23/14	04/26/14	04/27/14	1	A
	IR-13-00013-DST-112-A	12 ¾ OD, ERW welded steel pipes- Toscelik/Tzinorot-steel Grade B sch. 20 ASTM A 53, QTY=1500 m	04/23/14	04/24/14	04/28/14	4	A
	IR-13-00013-DST-113-A	Conducting radiographic nondestructive test for fabricated bends in attendees of MOREX agency , the quantities will be as follow: · 12 inch 11 ¼ bends=36 piece · 6 inch 11 ¼ bends=8 piece	04/23/14	04/24/14	04/24/14	0	C
	IR-13-00013-DST-113-B	Conducting radiographic nondestructive test for fabricated bends in attendees of MOREX agency	04/24/14	04/24/14	04/27/14	3	A
	IR-13-00013-DST-114-A	Trench excavation from St. 10+120 to St. 10+040	04/24/14	04/27/14	04/28/14	1	A
	IR-13-00013-DST-115-A	Pipeline installation and bedding from St. 10+120 to St. 10+040	04/24/14	04/27/14	04/28/14	1	A
	IR-13-00013-DST-116-A	Trench backfilling from St. 10+120 to St. 10+040	04/24/14	04/27/14	04/28/14	1	A
	IR-13-00013-DST-117-A	Trench excavation from St. 10+040 to St. 9+940	04/24/14	04/28/14	04/29/14	1	A
	IR-13-00013-DST-118-A	Pipeline installation and bedding from St. 10+040 to St. 9+940	04/24/14	04/28/14	04/29/14	1	A
	IR-13-00013-DST-119-A	Trench backfilling from St. 10+040 to St. 9+940	04/24/14	04/28/14	04/29/14	1	A
	IR-13-00013-DST-120-A	Trench excavation from St. 9+940 to St. 10+860	04/27/14	04/29/14	04/30/14	1	A
	IR-13-00013-DST-121-A	Pipeline installation and bedding from St. 9+940 to St. 9+860	04/27/14	04/29/14	04/30/14	1	A
	IR-13-00013-DST-122-A	Trench backfilling from St. 9+940 to St. 9+860	04/27/14	04/29/14	04/30/14	1	A
	IR-13-00013-DST-123-A	Pipeline alignment marked on site from St. 12+120 to St. 13+580	04/28/14	04/29/14	04/30/14	1	C
	IR-13-00013-DST-123-B	Pipeline alignment marked on site from St. 12+120 to St. 13+580	12/09/14	12/09/14	12/09/14	0	A
	IR-13-00013-DST-124-A	Trench excavation from St. 9+860 to St. 9+780	04/29/14	05/03/14	05/04/14	1	A
	IR-13-00013-DST-125-A	Pipeline installation and bedding from St. 9+860 to St. 9+780	04/29/14	05/03/14	05/04/14	1	A
	IR-13-00013-DST-126-A	Trench backfilling from St. 9+860 to St. 9+780	04/29/14	05/03/14	05/04/14	1	A
	IR-13-00013-DST-127-A	Field compaction test for finished base course layer	04/29/14	04/29/14	04/30/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-128-A	Trench excavation from St. 9+780 to St. 9+700	04/30/14	05/03/14	05/04/14	1	A
	IR-13-00013-DST-129-A	Pipeline installation and bedding from St. 9+780 to St. 9+700	04/30/14	05/03/14	05/04/14	1	A
	IR-13-00013-DST-130-A	Trench backfilling from St. 9+780 to St. 9+700	04/30/14	05/03/14	05/04/14	1	A
	IR-13-00013-DST-131-A	Inspection to spread prime coat on finished base course layer	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00013-DST-132-A	Pipeline alignment marked on site from St. 12+100 to St. 12+400	04/30/14	04/30/14	05/04/14	4	A
	IR-13-00013-DST-133-A	Inspection for fabrication of mitered bends-12 inch	04/30/14	05/01/14	05/04/14	3	A
	IR-13-00013-DST-134-A	Inspection for fabrication of mitered bends-12 inch	04/30/14	05/02/14	05/04/14	2	A
	IR-13-00013-DST-135-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer). St. 10+360 to St. 10+760	04/30/14	04/30/14	04/30/14	0	A
	IR-13-00013-DST-136-A	Trench excavation from St. 12+105 to St. 12+185	05/04/14	05/05/14	05/05/14	0	A
	IR-13-00013-DST-137-A	Pipeline installation and bedding from St. 12+105 to St. 12+185	05/04/14	05/05/14	05/05/14	0	A
	IR-13-00013-DST-138-A	Trench backfilling from St. 12+105 to St. 12+185	05/04/14	05/05/14	05/05/14	0	A
	IR-13-00013-DST-139-A	Inspection to spread prime coat on finished base course layer	05/04/14	05/04/14	05/05/14	1	A
	IR-13-00013-DST-140-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer). St. 11+060 to St. 11+510	05/04/14	05/04/14	05/05/14	1	A
	IR-13-00013-DST-141-A	Trench excavation from St. 12+185 to St. 12+265	05/04/14	05/06/14	05/06/14	0	A
	IR-13-00013-DST-142-A	Pipeline installation and bedding from St. 12+185 to St. 12+265	05/04/14	05/06/14	05/06/14	0	A
	IR-13-00013-DST-143-A	Trench backfilling from St. 12+185 to St. 12+265	05/04/14	05/06/14	05/06/14	0	A
	IR-13-00013-DST-144-A	Inspection for 12 inch fabricated bends, QTY=30	05/04/14	05/04/14	05/08/14	4	A
	IR-13-00013-DST-145-A	Pipeline alignment marked on site from St. 12+400 to St. 12+600	05/05/14	05/05/14	05/05/14	0	A
	IR-13-00013-DST-146-A	Inspection to spread prime coat on finished base course layer	05/05/14	05/05/14	05/05/14	0	C
	IR-13-00013-DST-146-B	Inspection to spread prime coat on finished base course layer	05/05/14	05/05/14	05/06/14	1	A
	IR-13-00013-DST-147-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer).St. 11+760 to St. 11+060 St. 11+510 to St. 11+660	05/05/14	05/05/14	05/05/14	0	C
	IR-13-00013-DST-147-B	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer).St. 10+760 to St. 11+060	05/05/14	05/05/14	05/06/14	1	A
	IR-13-00013-DST-148-A	Trench excavation from St. 12+265 to St. 12+400	05/05/14	05/07/14	05/07/14	0	A
	IR-13-00013-DST-149-A	Pipeline installation and bedding from St. 12+265 to St. 12+400	05/05/14	05/07/14	05/07/14	0	A
	IR-13-00013-DST-150-A	Trench backfilling from St. 12+265 to St. 12+400	05/05/14	05/07/14	05/07/14	0	A
	IR-13-00013-DST-151-A	Inspection to spread prime coat on finished base course layer	05/06/14	05/06/14	05/06/14	0	A
	IR-13-00013-DST-152-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer).St. 11+360 to St. 11+760	05/06/14	05/06/14	05/06/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-153-A	Trench excavation from St. 12+400 to St. 12+500	05/06/14	05/08/14	05/08/14	0	A
	IR-13-00013-DST-154-A	Pipeline installation and bedding from St. 12+400 to St. 12+500	05/06/14	05/08/14	05/08/14	0	A
	IR-13-00013-DST-155-A	Trench backfilling from St. 12+400 to St. 12+500	05/06/14	05/08/14	05/08/14	0	A
	IR-13-00013-DST-156-A	Electric resistance welded black steel pipe(casing sleeve)-OD=16 inch, wall thickness= 9.52 mm, QTY=106 m , Supplier FIP	05/06/14	05/06/14	05/07/14	1	C
	IR-13-00013-DST-156-B	Epoxy coated Electric resistance welded black steel pipe(casing sleeve)-OD=12 inch, wall thickness= 9.52 mm, QTY=106 m	05/22/14	05/22/14	05/25/14	3	A
	IR-13-00013-DST-157-A	Inspection for 12 inch fabricated bends, QTY=7	05/06/14	05/06/14	05/08/14	2	A
	IR-13-00013-DST-158-A	Conducting radiographic nondestructive test for fabricated bends in attendees of MOREX agency, QTY= 30 pieces	05/06/14	05/07/14	05/08/14	1	A
	IR-13-00013-DST-159-A	Concrete trial batch- Grade B 350 of Me'mar concrete mix design	05/06/14	05/08/14	05/12/14	4	A
	IR-13-00013-DST-160-A	Inspection to spread prime coat on finished base course layer	05/07/14	05/07/14	05/08/14	1	A
	IR-13-00013-DST-161-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer).St. 11+660 to St. 12+060	05/07/14	05/07/14	05/08/14	1	A
	IR-13-00013-DST-162-A	Trench excavation from St. 12+500 to St. 12+550.71	05/07/14	05/08/14	05/08/14	0	A
	IR-13-00013-DST-163-A	Pipeline installation and bedding from St. 12+500 to St. 12+550.71	05/07/14	05/08/14	05/08/14	0	A
	IR-13-00013-DST-164-A	Trench backfilling from St. 12+500 to St. 12+550.71	05/07/14	05/08/14	05/08/14	0	A
	IR-13-00013-DST-165-A	Pipeline alignment marked on site from St. 12+600 to St. 12+800	05/07/14	05/07/14	05/12/14	5	A
	IR-13-00013-DST-166-A	Trench excavation from St. 12+587.61 to St. 12+646	05/07/14	05/10/14	05/11/14	1	A
	IR-13-00013-DST-167-A	Pipeline installation and bedding from St. 12+587.61 to St. 12+646	05/07/14	05/10/14	05/11/14	1	A
	IR-13-00013-DST-168-A	Trench backfilling fromSt. 12+587.61 to St. 12+646	05/07/14	05/10/14	05/11/14	1	A
	IR-13-00013-DST-169-A	6 inch fabrication bends, degree= 11.25°, QTY=14	05/07/14	05/10/14	05/11/14	1	C
	IR-13-00013-DST-169-B	6 inch and 12 inch fabrication bends	05/15/14	05/22/14	05/25/14	3	A
	IR-13-00013-DST-170-A	Pipeline alignment marked on site from St. 12+800 to St. 12+920	05/11/14	05/11/14	05/12/14	1	A
	IR-13-00013-DST-171-A	12 inch -polyethylene coated pipes /Grade B ASTM A53 ERW welded steel pipes-Toscelik/Middle East Tube Company Ltd. product., QTY= 660 m	05/11/14	05/11/14	05/14/14	3	A
	IR-13-00013-DST-172-A	Trench excavation from St. 12+646 to St. 12+750	05/11/14	05/12/14	05/12/14	0	A
	IR-13-00013-DST-173-A	Pipeline installation and bedding from St. 12+646 to St. 12+750	05/11/14	05/12/14	05/12/14	0	A
	IR-13-00013-DST-174-A	Trench backfilling from St. 12+646 to St. 12+750	05/11/14	05/12/14	05/12/14	0	A
	IR-13-00013-DST-175-A	Conduct internal cement lining for 12 inch mitered bends fabrication starting from May 12,2014 at time 8:00 AM, QTY=15	05/12/14	05/14/14	05/15/14	1	A
	IR-13-00013-DST-176-A	Pipeline alignment marked on site from St. 12+920 to St. 13+140	05/12/14	05/12/14	05/14/14	2	A
	IR-13-00013-DST-177-A	Trench excavation from St. 12+750 to St. 12+850	05/12/14	05/14/14	05/14/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-178-A	Pipeline installation and bedding from St. 12+750 to St. 12+850	05/12/14	05/14/14	05/14/14	0	A
	IR-13-00013-DST-179-A	Trench backfilling from St. 12+750 to St. 12+850	05/12/14	05/14/14	05/14/14	0	A
	IR-13-00013-DST-180-A	Trench excavation from St. 12+850 to St. 13+000	05/12/14	05/15/14	05/15/14	0	A
	IR-13-00013-DST-181-A	Pipeline installation and bedding from St. 12+850 to St. 13+000	05/12/14	05/15/14	05/15/14	0	A
	IR-13-00013-DST-182-A	Trench backfilling from St. 12+850 to St. 13+000	05/12/14	05/15/14	05/15/14	0	A
	IR-13-00013-DST-183-A	12 inch -polyethylene coated pipes /Grade B ASTM A53 ERW welded steel pipes-Toscelik/Middle East Tube Company Ltd. product., QTY= 660.16 m	05/13/14	05/13/14	05/14/14	1	A
	IR-13-00013-DST-184-A	Trench excavation from St. 13+000 to St. 13+080	05/14/14	05/17/14	05/18/14	1	A
	IR-13-00013-DST-185-A	Pipeline installation and bedding from St. 13+000 to St. 13+080	05/14/14	05/17/14	05/18/14	1	A
	IR-13-00013-DST-186-A	Trench backfilling from St. 13+000 to St. 13+080	05/14/14	05/17/14	05/18/14	1	A
	IR-13-00013-DST-187-A	Field compaction test for finished base course layer	05/14/14	05/14/14	05/15/14	1	A
	IR-13-00013-DST-188-A	Pipeline alignment marked on site from St. 13+140 to St. 13+580	05/15/14	05/15/14	05/18/14	3	A
	IR-13-00013-DST-189-A	Inspection to spread prime coat on finished base course layer	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00013-DST-190-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer).St. 9+690 to St. 10+050	05/15/14	05/15/14	05/15/14	0	A
	IR-13-00013-DST-191-A	Trench excavation from St. 13+080 to St. 13+200	05/15/14	05/18/14	05/18/14	0	A
	IR-13-00013-DST-192-A	Pipeline installation and bedding from St. 13+080 to St. 13+200	05/15/14	05/18/14	05/18/14	0	A
	IR-13-00013-DST-193-A	Trench backfilling from St. 13+080 to St. 13+200	05/15/14	05/18/14	05/18/14	0	A
	IR-13-00013-DST-194-A	Trench excavation from St. 13+200 to Sta. 13+280	05/18/14	05/19/14	05/19/14	0	A
	IR-13-00013-DST-195-A	Pipeline installation and bedding from St. 13+200 to Sta. 13+280	05/18/14	05/19/14	05/19/14	0	A
	IR-13-00013-DST-196-A	Trench backfilling from St. 13+200 to Sta. 13+280	05/18/14	05/19/14	05/19/14	0	A
	IR-13-00013-DST-197-A	Trench excavation from Sta. 13+280 to Sra. 13+380	05/18/14	05/20/14	05/20/14	0	A
	IR-13-00013-DST-198-A	Pipeline installation and bedding from Sta. 13+280 to Sra. 13+380	05/18/14	05/20/14	05/20/14	0	A
	IR-13-00013-DST-199-A	Trench backfilling from Sta. 13+280 to Sra. 13+380	05/18/14	05/20/14	05/20/14	0	A
	IR-13-00013-DST-200-A	Inspection for mobile traffic signs for traffic control of area C	05/18/14	05/19/14	05/20/14	1	A
	IR-13-00013-DST-201-A	Trench excavation from Sta. 13+380 to Sta. 13+480	05/19/14	05/21/14	05/21/14	0	A
	IR-13-00013-DST-202-A	Pipeline installation and bedding from Sta. 13+380 to Sta. 13+480	05/19/14	05/21/14	05/21/14	0	A
	IR-13-00013-DST-203-A	Trench backfilling from Sta. 13+380 to Sta. 13+480	05/19/14	05/21/14	05/21/14	0	A
	IR-13-00013-DST-204-A	Trench excavation from Sta. 13+480 to St. 13+580	05/20/14	05/22/14	05/22/14	0	A
	IR-13-00013-DST-205-A	Pipeline installation and bedding from Sta. 13+480 to St. 13+580	05/20/14	05/22/14	05/22/14	0	A
	IR-13-00013-DST-206-A	Trench backfilling from Sta. 13+480 to St. 13+580	05/20/14	05/22/14	05/22/14	0	A
	IR-13-00013-DST-207-A	Inspection to spread prime coat on finished base course layer St. 10+000 to St. 10+360	05/21/14	05/21/14	05/22/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-208-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer). St. 10+000 to St. 10+360	05/21/14	05/21/14	05/22/14	1	A
	IR-13-00013-DST-209-A	Pipeline alignment marked on site from St. 13+580 to St. 13+725	05/21/14	05/21/14	05/22/14	1	A
	IR-13-00013-DST-210-A	Visual inspection for delivered ductile cast iron manhole cover GGG50-EN124-D400, QTY=50 pieces	05/21/14	05/22/14	05/26/14	4	C
	IR-13-00013-DST-210-B	Visual inspection for delivered ductile cast iron manhole cover GGG50-EN124-D400(one sample)	07/08/14	07/09/14	07/15/14	6	A
	IR-13-00013-DST-211-A	Trench excavation from Sta. 13+580 to St. 13+710.58	05/21/14	05/24/14	05/25/14	1	A
	IR-13-00013-DST-212-A	Pipeline installation and bedding from Sta. 13+580 to St. 13+710.58	05/21/14	05/24/14	05/25/14	1	A
	IR-13-00013-DST-213-A	Trench backfilling from Sta. 13+580 to St. 13+710.58	05/21/14	05/24/14	05/25/14	1	A
	IR-13-00013-DST-214-A	12 inch -polyethylene coated pipes /Grade B ASTM A53 ERW welded steel pipes-Toscelik/Middle East Tube Company Ltd. product., QTY= 1986 m	05/22/14	05/26/14	05/27/14	1	C
	IR-13-00013-DST-214-B	12 inch -polyethylene coated pipes /Grade B ASTM A53 ERW welded steel pipes-Toscelik/Middle East Tube Company Ltd. product., QTY= 1781.2 m	06/12/14	06/12/14	06/15/14	3	A
	IR-13-00013-DST-215-A	Trench excavation from Sta. 12+550.71 to Sta. 12+562.11 and from Sta. 12+578.42 to Sta. 12+587.61	05/22/14	05/24/14	05/25/14	1	A
	IR-13-00013-DST-216-A	Pipes installation and bedding from Sta. 12+550.71 to Sta. 12+562.11 and from Sta. 12+578.42 to Sta. 12+587.61	05/22/14	05/24/14	05/25/14	1	A
	IR-13-00013-DST-217-A	Trench backfilling from Sta. 12+550.71 to Sta. 12+562.11 and from Sta. 12+578.42 to Sta. 12+587.61	05/22/14	05/24/14	05/25/14	1	A
	IR-13-00013-DST-218-A	Road crossing from Sta. 12+562.11 to Sta. 12+578.42 include : Excavation, pipes installation , install casing pipe , poring low concrete strength and final backfilling	05/22/14	05/24/14	05/25/14	1	A
	IR-13-00013-DST-219-A	Inspection for welding bends to 12 inch pipe	05/25/14	05/26/14	05/28/14	2	C
	IR-13-00013-DST-219-B	Inspection for welding bends to 12 inch pipe	02/15/15	02/15/15	02/16/15	1	A
	IR-13-00013-DST-220-A	Starting excavation for gate valve (200 mm) manhole at Sta. 09+941.31	05/25/14	05/26/14	05/27/14	1	A
	IR-13-00013-DST-221-A	Trench excavation from Sta. 6+983 to Sta. 6+903	05/26/14	05/28/14	05/28/14	0	A
	IR-13-00013-DST-222-A	Pipes installation from Sta. 6+983 to Sta. 6+903	05/26/14	05/28/14	05/28/14	0	A
	IR-13-00013-DST-223-A	Pipe encasement by casting concrete B 150 from Sta. 6+981 to Sta. 6+903	05/26/14	05/28/14	05/28/14	0	A
	IR-13-00013-DST-224-A	Trench excavation from Sta. 6+903 to Sta. 6+823	05/27/14	05/29/14	05/29/14	0	A
	IR-13-00013-DST-225-A	Pipes installation from Sta. 6+903 to Sta. 6+823	05/27/14	05/29/14	05/29/14	0	A
	IR-13-00013-DST-226-A	Pipe encasement by casting concrete B 150 from Sta. 6+903 to Sta. 6+823	05/27/14	05/29/14	05/29/14	0	A
	IR-13-00013-DST-227-A	Inspection for 200 mm gate valve at Sta. 9+941.31, include : · Excavation · Spread single size below base slab · Safety around the manhole	05/27/14	05/27/14	05/28/14	1	A
	IR-13-00013-DST-228-A	Trench excavation from Sta. 6+823 to Sta. 6+723	05/28/14	05/31/14	06/01/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-229-A	Pipes installation from Sta. 6+823 to Sta. 6+723	05/28/14	05/31/14	06/01/14	1	A
	IR-13-00013-DST-230-A	Pipe encasement by casting concrete B 150 from Sta. 6+823 to Sta. 6+723	05/28/14	05/31/14	06/01/14	1	A
	IR-13-00013-DST-231-A	Inspection to start excavation (location & marking) for 200 GV at Sta. 10+461	05/28/14	05/28/14	05/29/14	1	A
	IR-13-00013-DST-232-A	Trench excavation from Sta. 6+723 to Sta. 6+603	05/29/14	06/01/14	06/01/14	0	A
	IR-13-00013-DST-233-A	Pipes installation from Sta. 6+723 to Sta. 6+603	05/29/14	06/01/14	06/01/14	0	A
	IR-13-00013-DST-234-A	Pipe encasement by casting concrete B 150 from Sta. 6+723 to Sta. 6+603	05/29/14	06/01/14	06/01/14	0	A
	IR-13-00013-DST-235-A	12 inch fabrication bends, QTY=4 pieces	05/29/14	05/29/14	06/01/14	3	A
	IR-13-00013-DST-236-A	Inspection for 200 mm gate valve, include : • Excavation • Spread single size below base slab • Safety around manhole	05/29/14	05/31/14	06/01/14	1	C
	IR-13-00013-DST-236-B	Inspection for 200 mm gate valve, include : • Excavation • Safety around manhole • Spreading single size below blind layer • Drainage system for sewage water • Level • Dimension	06/17/14	06/17/14	06/17/14	0	C
	IR-13-00013-DST-236-C	Inspection for 200 mm gate valve, include : • Excavation • Safety around manhole • Spreading single size below blind layer • Drainage system for sewage water • Level • Dimension	12/09/14	12/09/14	12/09/14	0	A
	IR-13-00013-DST-237-A	Concrete casting for reinforced foundation of 200 GV at Sta. 9+941	05/31/14	05/31/14	06/01/14	1	A
	IR-13-00013-DST-238-A	Inspection to spread prime coat on finshed base course layer	05/31/14	05/31/14	06/01/14	1	A
	IR-13-00013-DST-239-A	Asphalt reinstatment over trench edges with 300 mm pipes (first Layer)	05/31/14	05/31/14	06/01/14	1	A
	IR-13-00013-DST-240-A	Trench excavation from Sta. 6+603 to Sta. 6+400	06/01/14	06/03/14	06/04/14	1	A
	IR-13-00013-DST-241-A	• Pipes installation from Sta. 6+603 to Sta. 6+400 • Bedding backfilling from Sta. 6+508.7 to Sta. 6+430	06/01/14	06/03/14	06/04/14	1	A
	IR-13-00013-DST-242-A	• Pipe encasement by casting concrete B 150 from Sta. 6+603 to Sta. 6+508.7 and from Sta. 6+430 to Sta. 6+400 • Trench backfilling from Sta. 6+508.7 Sta. 6+430	06/01/14	06/03/14	06/04/14	1	A
	IR-13-00013-DST-243-A	Field compaction test for finished base course layer St. 12+578 to St. 13+070	06/01/14	06/01/14	06/02/14	1	A
	IR-13-00013-DST-244-A	Inspection to spread prime coat on finished base course layer St. 12+578 to St. 12+835 and from St. 13+040 to St. 13+200	06/01/14	06/01/14	06/02/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-245-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer).St. St. 12+578 to St. 12+835 and from St. 13+040 to St. 13+200	06/01/14	06/01/14	06/02/14	1	A
	IR-13-00013-DST-246-A	Steel reinforcement for walls of GV 200 mm at Sta. 9+941	06/01/14	06/01/14	06/02/14	1	A
	IR-13-00013-DST-247-A	Inspection to start excavation (Location & marking) for combined air release valve with butterfly valve chamber at St. 11+187	06/01/14	06/01/14	06/02/14	1	A
	IR-13-00013-DST-248-A	Field compaction test for finished base course layer (St. 12+835 to St. 13+040 and from Sta. 13+200 to St. 13+480)	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00013-DST-249-A	Inspection to spread prime coat on finished base course layer (St. 12+835 to St. 13+040 and from Sta. 13+200 to St. 13+480)	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00013-DST-250-A	Asphalt reinstatement over trench edges with 300 mm pipes (First Layer).(St. 12+835 to St. 13+040 and from Sta. 13+200 to St. 13+480)	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00013-DST-251-A	Inspection for combined air release valve and butterfly valve chamber at Sta. 11+187, include : · Excavation · Spread single size below base slab · Safety around the manhole	06/02/14	06/02/14	06/03/14	1	A
	IR-13-00013-DST-252-A	Trench excavation from Sta. 6+400 to Sta. 6+320	06/03/14	06/05/14	06/05/14	0	A
	IR-13-00013-DST-253-A	• Pipes installation from Sta. 6+400 to Sta. 6+320 • Bedding backfilling from Sta. 6+364 to Sta. 6+320	06/03/14	06/05/14	06/05/14	0	A
	IR-13-00013-DST-254-A	• Pipe encasement by casting concrete B 150 from Sta. 6+400 to Sta. 6+364 • Trench backfilling from Sta. 6+364 to Sta. 6+320	06/03/14	06/05/14	06/05/14	0	A
	IR-13-00013-DST-255-A	Steel reinforcement and formwork shuttering for walls of 200 mm GV at Sta. 9+941	06/03/14	06/03/14	06/03/14	0	A
	IR-13-00013-DST-256-A	Trench excavation from Sta. 6+320 to Sta. 6+240	06/04/14	06/07/14	06/08/14	1	A
	IR-13-00013-DST-257-A	Pipes installation from Sta. 6+320 to Sta. 6+240 Bedding backfilling from Sta. 6+320 to Sta. 6+289.68	06/04/14	06/07/14	06/08/14	1	A
	IR-13-00013-DST-258-A	Pipe encasement by casting concrete B 150 from Sta. 6+289.68 to Sta. 6+240	06/04/14	06/07/14	06/08/14	1	A
	IR-13-00013-DST-259-A	Inspection for mock up of implemented drainage ditch from Sta. 6+975 to Sta. 6+951	06/05/14	06/08/14	06/09/14	1	C
	IR-13-00013-DST-260-A	Inspection to start excavation (Location & marking) for 250 mm Gate valve chamber at St. 13+617	06/05/14	06/07/14	06/08/14	1	A
	IR-13-00013-DST-261-A	Trench backfilling from Sta. 6+320 to Sta. 6+289.68	06/05/14	06/07/14	06/08/14	1	A
	IR-13-00013-DST-262-A	Trench excavation from Sta. 6+240 to Sta. 6+100	06/08/14	06/09/14	06/10/14	1	A
	IR-13-00013-DST-263-A	Pipes installation from Sta. 6+240 to Sta. 6+100	06/08/14	06/09/14	06/10/14	1	A
	IR-13-00013-DST-264-A	Trench backfilling from Sta. 6+289.68 to Sta. 6+241.18	06/08/14	06/09/14	06/09/14	0	A
	IR-13-00013-DST-265-A	Pipe encasement by casting concrete B 150 from Sta. 6+240 to Sta. 6+100 (including reinforced concrete fro Sta. 6+202.01 to Sta. 6+165.04	06/08/14	06/09/14	06/10/14	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-265-B	Pipe encasement by casting concrete B 150 from Sta. 6+240 to Sta. 6+100 (including reinforced concrete fro Sta. 6+202.01 to Sta. 6+165.05)	06/10/14	06/10/14	06/11/14	1	A
	IR-13-00013-DST-266-A	Inspection for 250 mm gate valve at Sta. 13+617, include : · Excavation · Spread single size below base slab · Safety around the manhole. · level	06/08/14	06/08/14	06/09/14	1	A
	IR-13-00013-DST-267-A	Formwork and steel reinforcement for foundation of combined butterfly valve and Air release valve chamber to cast concrete at Sta. 11+187	06/08/14	06/08/14	06/09/14	1	A
	IR-13-00013-DST-268-A	12 inch black steel pipes /Grade B ASTM A53 ERW welded steel pipes-Toscelik/Middle East Tube Company Ltd. product., QTY= 5000 m	06/08/14	06/09/14	06/11/14	2	C
	IR-13-00013-DST-268-B	13 inch black steel pipes /Grade B ASTM A53 ERW welded steel pipes-Toscelik/Middle East Tube Company Ltd. product., QTY= 5000 m	02/15/15	02/15/15	02/16/15	1	A
	IR-13-00013-DST-269-A	12 inch fabrication bends starting from June 09,2014 at 8:00 AM	06/08/14	06/15/14	06/15/14	0	C
	IR-13-00013-DST-269-B	12 inch fabrication bends starting from June 17,2014 at 8:00 AM	06/17/14	06/26/14	06/26/14	0	A
	IR-13-00013-DST-270-A	Steel reinforcement for walls of combined air release valve and butterfly valve at Sta. 11+187	06/08/14	06/09/14	06/09/14	0	A
	IR-13-00013-DST-271-A	Trench excavation from Sta. 6+100 to Sta. 6+000	06/09/14	06/10/14	06/11/14	1	A
	IR-13-00013-DST-272-A	Pipes installation from Sta. 6+100 to Sta. 6+000	06/09/14	06/10/14	06/11/14	1	A
	IR-13-00013-DST-273-A	Pipe encasement by casting concrete B 150 from Sta. 6+100 to Sta. 6+000	06/09/14	06/10/14	06/11/14	1	A
	IR-13-00013-DST-274-A	Trench excavation from Sta. 6+000 to Sta. 5+920`	06/09/14	06/11/14	06/11/14	0	A
	IR-13-00013-DST-275-A	Pipes installation from Sta. 6+000 to Sta. 5+920`	06/09/14	06/11/14	06/11/14	0	A
	IR-13-00013-DST-276-A	Pipe encasement by casting concrete B 150 from Sta. 6+000 to Sta. 5+920`	06/09/14	06/11/14	06/11/14	0	A
	IR-13-00013-DST-277-A	Inspection to start excavation (Location & marking) for butterfly valve chamber at St. 13+700	06/09/14	06/09/14	06/09/14	0	A
	IR-13-00013-DST-278-A	Trench excavation from Sta. 5+920 to Sta. 5+770`	06/10/14	06/12/14	06/12/14	0	A
	IR-13-00013-DST-279-A	Pipes installation from Sta. 5+920 to Sta. 5+770`	06/10/14	06/12/14	06/12/14	0	A
	IR-13-00013-DST-280-A	Pipe encasement by casting concrete B 150 from Sta. 5+920 to Sta. 5+770`	06/10/14	06/12/14	06/12/14	0	A
	IR-13-00013-DST-281-A	formwork for walls of combined air release valve and butterfly valve chamber at Sta. 11+187 to cast concrete: Level Dimension Verticality	06/10/14	06/10/14	06/11/14	1	A
	IR-13-00013-DST-282-A	Formwork and steel reinforcement for foundation of 250 mm GV at Sta. 13+617 to concrete casting	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00013-DST-283-A	Excavation for butterfly valve chamber at Sta. 13+617	06/11/14	06/11/14	06/12/14	1	C
	IR-13-00013-DST-283-B	Excavation for butterfly valve chamber at Sta. 13+700	06/12/14	06/12/14	06/12/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-284-A	Formwork and steel reinforcement for roof slab of 200 mm GV at Sta. 9+941 to cast concrete	06/11/14	06/11/14	06/12/14	1	C
	IR-13-00013-DST-284-B	Formwork and steel reinforcement for roof slab of 200 mm GV at Sta. 9+941 to cast concrete	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00013-DST-285-A	Concrete casting for concrete ditch from Sta. 6+975 to Sta. 6+750	06/11/14	06/11/14	06/12/14	1	A
	IR-13-00013-DST-286-A	Trench excavation from Sta. 5+770 to Sta. 5+620	06/11/14	06/14/14	06/15/14	1	A
	IR-13-00013-DST-287-A	Pipes installation from Sta. 5+770 to Sta. 5+620	06/11/14	06/14/14	06/11/14	-3	C
	IR-13-00013-DST-287-B	Pipes installation from Sta. 5+770 to Sta. 5+620	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00013-DST-288-A	Pipes encasement by casting concrete B 150 from Sta. 5+770 to Sta. 5+620	06/11/14	06/14/14	06/15/14	1	A
	IR-13-00013-DST-289-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 6+750 to Sta. 6+548	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00013-DST-290-A	Steel reinforcement work for walls of 250 mm GV to close the shutters of formwork	06/12/14	06/12/14	06/12/14	0	A
	IR-13-00013-DST-291-A	Steel reinforcement work and formwork for foundation of butterfly valve to cast concrete at Sta. 13+700	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00013-DST-292-A	Formwork for walls of 250 mm GV chamber at Sta. 13+617 to cast concrete : · Level · Dimensions · Verticality	06/12/14	06/14/14	06/15/14	1	A
	IR-13-00013-DST-293-A	Trench excavation from Sta. 5+620 to Sta. 5+540	06/12/14	06/15/14	06/16/14	1	A
	IR-13-00013-DST-294-A	Pipes installation from Sta. 5+620 to Sta. 5+540	06/12/14	06/15/14	06/16/14	1	A
	IR-13-00013-DST-295-A	Pipes encasement by casting concrete B 150 from Sta. 5+620 to Sta. 5+540	06/12/14	06/15/14	06/16/14	1	A
	IR-13-00013-DST-296-A	Trench excavation from Sta. 5+540 to Sta. 5+460	06/15/14	06/17/14	06/17/14	0	A
	IR-13-00013-DST-297-A	Pipes installation from Sta. 5+540 to Sta. 5+460	06/15/14	06/17/14	06/17/14	0	A
	IR-13-00013-DST-298-A	Pipe encasement by casting concrete B 150 from Sta. 5+540 to Sta. 5+460	06/15/14	06/17/14	06/17/14	0	A
	IR-13-00013-DST-299-A	Trench excavation from Sta. 5+460 to Sta. 5+360	06/16/14	06/18/14	06/18/14	0	A
	IR-13-00013-DST-300-A	Pipes installation from Sta. 5+460 to Sta. 5+360	06/16/14	06/18/14	06/18/14	0	A
	IR-13-00013-DST-301-A	Pipe encasement by casting concrete B 150 from Sta. 5+460 to Sta. 5+360	06/16/14	06/18/14	06/18/14	0	A
	IR-13-00013-DST-302-A	Inspection for walls steel reinforcement of butterfly valve at Sta. 13+700 to close the shutters	06/17/14	06/17/14	06/17/14	0	A
	IR-13-00013-DST-303-A	Trench excavation from Sta. 5+360 to Sta. 5+160	06/17/14	06/19/14	06/19/14	0	A
	IR-13-00013-DST-304-A	Pipes installation from Sta. 5+360 to Sta. 5+160	06/17/14	06/19/14	06/19/14	0	A
	IR-13-00013-DST-305-A	Pipe encasement by casting concrete B 150 from Sta. 5+360 to Sta. 5+160	06/17/14	06/19/14	06/19/14	0	A
	IR-13-00013-DST-306-A	Conducting radiographic nondestructive test for 12 inch fabricated bends & Field joints in attendees of MOREX agency	06/17/14	06/19/14	06/19/14	0	A
	IR-13-00013-DST-307-A	Steel reinforcement and formwork for roof slab of combined air release and butterfly valves to cast concrete at Sta. 11+187	06/18/14	06/18/14	06/18/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-308-A	Trench excavation from Sta. 5+160 to Sta. 4+960	06/18/14	06/21/14	06/22/14	1	A
	IR-13-00013-DST-309-A	Pipes installation from Sta. 5+160 to Sta. 4+960	06/18/14	06/21/14	06/22/14	1	A
	IR-13-00013-DST-310-A	Formwork for walls of Butterfly valve chamber at Sta. 13+700 to cast concrete : · Level · Dimensions · Verticality	06/18/14	06/18/14	06/18/14	0	A
	IR-13-00013-DST-311-A	Starting filling conical holes and surface finish for walls of combined air release and butterfly valves chamber and 200 mm gate valve at Sta. 11+187 & Sta. 9+941 using approved FOSROC material (from June 21,2014 at 8:00 AM)	06/19/14	06/24/14	06/24/14	0	A
	IR-13-00013-DST-312-A	Bedding backfilling from Sta. 5+128.10 to Sta. 5+091.24	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00013-DST-313-A	Trench backfilling from Sta. 5+128.10 to Sta. 5+091.24	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00013-DST-314-A	Pipes encasements by casting concrete B 150 from Sta. 5+160 to Sta. 5+128.10 and from Sta. 5+091.24 to Sta. 4+960	06/22/14	06/22/14	06/22/14	0	A
	IR-13-00013-DST-315-A	Trench excavation from Sta. 4+960 to Sta. 4+700	06/22/14	06/24/14	06/24/14	0	A
	IR-13-00013-DST-316-A	Pipes installation from Sta. 4+960 to Sta. 4+700	06/22/14	06/24/14	06/24/14	0	A
	IR-13-00013-DST-317-A	Pre- cast manhole for 200 mm GV at Sta. 10+461-PCP product	06/22/14	06/22/14	06/23/14	1	C
	IR-13-00013-DST-317-B	Pre- cast manhole for 200 mm GV at Sta. 10+461-PCP product	07/13/14	07/13/14	07/14/14	1	C
	IR-13-00013-DST-317-C	Pre- cast manhole for 200 mm GV at Sta. 10+461-PCP product	07/14/14	07/14/14	07/15/14	1	A
	IR-13-00013-DST-318-A	Steel reinforcement work and formwork for roof slab of butterfly valve to cast concrete at Sta. 13+700	06/23/14	06/23/14	06/23/14	0	A
	IR-13-00013-DST-319-A	Surface preparation to start painting the external face of combined air release and butterfly valves chamber at Sta. 11+187 with accepted bitumen material	06/23/14	06/23/14	06/23/14	0	A
	IR-13-00013-DST-320-A	Trench excavation from Sta. 4+700 to Sta. 4+500	06/23/14	06/25/14	06/25/14	0	A
	IR-13-00013-DST-321-A	Pipes installation from Sta. 4+700 to Sta. 4+500	06/23/14	06/25/14	06/25/14	0	A
	IR-13-00013-DST-322-A	Pipe encasement by casting concrete B 150 from Sta. 4+960 to Sta. 4+700	06/23/14	06/25/14	06/25/14	0	A
	IR-13-00013-DST-323-A	Painting the second layer for external face of combined air release and butterfly valves chamber at Sta. 11+187 with accepted bitumen material	06/23/14	06/23/14	06/23/14	0	A
	IR-13-00013-DST-324-A	Backfilling with single size around combined air release and butterfly valves chamber at Sta. 11+187	06/23/14	06/24/14	06/24/14	0	A
	IR-13-00013-DST-325-A	Trench excavation from Sta. 4+500 to Sta. 4+300	06/24/14	06/26/14	06/26/14	0	A
	IR-13-00013-DST-326-A	pipes installation from Sta. 4+500 to Sta. 4+300	06/24/14	06/26/14	06/26/14	0	A
	IR-13-00013-DST-327-A	Pipe encasement by casting concrete B 150 from Sta. 4+700 to Sta. 4+500	06/24/14	06/26/14	06/26/14	0	A
	IR-13-00013-DST-328-A	Inspection to start excavation (Location & marking) for Al Asa'sa connection chamber at Sta. 13+608	06/24/14	06/24/14	06/25/14	1	A
	IR-13-00013-DST-329-A	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.	06/24/14	07/02/14	07/02/14	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-329-B	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.	07/02/14	07/02/14	07/03/14	1	A
	IR-13-00013-DST-330-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch , Sta. 6+548 to Sta. 6+520, Sta. 6+410 to Sta. 6+340, Sta. 6+325 to Sta. 6+202.01& Sta. 6+165.05 to Sta. 5+880	06/24/14	06/25/14	06/26/14	1	A
	IR-13-00013-DST-331-A	Inspection for Al Asa'sa connection chamber to cast blind layer at Sta. 13+608, include : · Dimension of excavation · Spread single size below base slab · Safety around the manhole. · level	06/25/14	06/25/14	06/26/14	1	A
	IR-13-00013-DST-332-A	Trench excavation from Sta. 4+300 to Sta. 4+050	06/25/14	06/28/14	06/29/14	1	A
	IR-13-00013-DST-333-A	Pipes installation from Sta. 4+300 to Sta. 4+050	06/25/14	06/28/14	06/29/14	1	A
	IR-13-00013-DST-334-A	Pipe encasement by casting concrete B 150 from Sta. 4+500 to Sta. 4+300	06/25/14	06/28/14	06/29/14	1	A
	IR-13-00013-DST-335-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch (Sta. 5+880 to Sta. 5+350)	06/26/14	06/28/14	06/29/14	1	A
	IR-13-00013-DST-336-A	Trench excavation from Sta. 4+050 to Sta. 3+950	06/29/14	07/01/14	07/02/14	1	A
	IR-13-00013-DST-337-A	Pipes installation from Sta. 4+050 to Sta. 3+950	06/29/14	07/01/14	07/02/14	1	A
	IR-13-00013-DST-338-A	Pipe encasement by casting concrete B 150 from Sta. 4+300 to Sta. 4+081.25	06/30/14	06/30/14	06/30/14	0	A
	IR-13-00013-DST-339-A	Steel reinforcement work and formwork for foundation of small chamber from AlAsa'sa connection to cast concrete at Sta. 13+608	07/01/14	07/01/14	07/02/14	1	A
	IR-13-00013-DST-340-A	Trench excavation from Sta. 3+950 to Sta. 3+916.77	07/02/14	07/02/14	07/03/14	1	A
	IR-13-00013-DST-341-A	Pipes installation from Sta. 3+950 to Sta. 3+916.77	07/02/14	07/02/14	07/03/14	1	A
	IR-13-00013-DST-342-A	Bedding from Sta. 4+081.25 to Sta. 3+917	07/02/14	07/02/14	07/03/14	1	A
	IR-13-00013-DST-343-A	Trench backfilling from Sta. 4+081.25 to Sta. 3+917	07/02/14	07/02/14	07/03/14	1	A
	IR-13-00013-DST-344-A	Trench excavation from Sta. 3+461.70 to Sta. 3+300	07/02/14	07/03/14	07/03/14	0	A
	IR-13-00013-DST-345-A	Pipes installation from Sta. 3+461.70 to Sta. 3+300	07/02/14	07/03/14	07/03/14	0	A
	IR-13-00013-DST-346-A	Filling conical holes and surface finish for walls of butterfly valve chamber at Sta. 13+700 using approved FOSROC material	07/02/14	07/02/14	07/03/14	1	C
	IR-13-00013-DST-346-B	Filling conical holes and surface finish for walls of butterfly valve chamber at Sta. 13+700 using approved FOSROC material	07/09/14	07/09/14	07/09/14	0	A
	IR-13-00013-DST-347-A	Steel reinforcement for walls of first room of Al Asa'sa chamber at Sta. 13+608	07/03/14	07/03/14	07/03/14	0	A
	IR-13-00013-DST-348-A	Steel reinforcement and formwork for foundation of second room of Al Asa'sa chamber at Sta. 13+608 to cast concrete	07/03/14	07/03/14	07/03/14	0	C
	IR-13-00013-DST-348-B	Steel reinforcement and formwork for foundation of second room of Al Asa'sa chamber at Sta. 13+608 to cast concrete	07/03/14	07/05/14	07/06/14	1	A
	IR-13-00013-DST-349-A	12 inch fabrication bends starting from July 03,2014 at 10:00 AM	07/03/14	07/15/14	07/16/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-350-A	Trench excavation from Sta. 3+300 to Sta. 3+230	07/03/14	07/05/14	07/06/14	1	A
	IR-13-00013-DST-351-A	Pipes installation from Sta. 3+300 to Sta. 3+230	07/03/14	07/05/14	07/06/14	1	A
	IR-13-00013-DST-352-A	Compaction test for asphalt reinstatement over trench edges (first layer)from Sta. 9+700 to sta. 13+480	07/03/14	07/05/14	07/06/14	1	A
	IR-13-00013-DST-353-A	Formwork for walls of first room of Al asa'sa chamber at Sta. 13+608 to cast concrete : · Level · Dimensions · Verticality	07/05/14	07/05/14	07/06/14	1	A
	IR-13-00013-DST-354-A	Trench excavation from Sta. 3+230 to Sta. 3+100	07/06/14	07/08/14	07/08/14	0	A
	IR-13-00013-DST-355-A	Pipes installation from Sta. 3+230 to Sta. 3+100	07/06/14	07/08/14	07/08/14	0	A
	IR-13-00013-DST-356-A	Trench backfilling from Sta. 4+870.67to Sta. 4+821.83	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00013-DST-357-A	Pipes encasement by casting concrete B 150 from Sta. 3+461 to Sta. 3+354.05 and from Sta. 3+320.91 to Sta. 3+300	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00013-DST-358-A	Bedding from Sta. 3+354.05 to Sta. 3+320.91	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00013-DST-359-A	Backfilling from Sta. 3+354.05 to Sta. 3+320.91	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00013-DST-360-A	Pipe encasement by casting concrete B 150 from Sta. 3+300 to Sta. 3+230	07/06/14	07/06/14	07/07/14	1	A
	IR-13-00013-DST-361-A	Excavation ,Pipe installation and connection to pipe of 200 mm GV at Sta. 9+941starting from July 08,2014	07/08/14	07/10/14	07/13/14	3	A
	IR-13-00013-DST-362-A	Trench excavation from Sta. 3+100 to Sta. 2+900	07/08/14	07/09/14	07/09/14	0	A
	IR-13-00013-DST-363-A	Pipes installation from Sta. 3+100 to Sta. 2+900	07/08/14	07/09/14	07/09/14	0	A
	IR-13-00013-DST-364-A	Pipe encasement by casting concrete B 150 from Sta. 3+230 to Sta. 3+100	07/08/14	07/09/14	07/09/14	0	A
	IR-13-00013-DST-365-A	Steel reinforcement for walls of second room of Al Asa'sa chamber at Sta. 13+608	07/09/14	07/09/14	07/09/14	0	A
	IR-13-00013-DST-366-A	Trench excavation from Sta. 2+900 to Sta. 2+700	07/09/14	07/12/14	07/13/14	1	A
	IR-13-00013-DST-367-A	Pipes installation from Sta. 2+900 to Sta. 2+700	07/09/14	07/12/14	07/13/14	1	C
	IR-13-00013-DST-367-B	Pipes installation from Sta. 2+900 to Sta. 2+700	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00013-DST-368-A	Inspection to conduct core test of concrete for walls of 200 mm GV chamber at Sta. 9+941	07/09/14	07/10/14	07/10/14	0	A
	IR-13-00013-DST-369-A	Painting the external body of butterfly valve chamber at Sta. 13+700 with accepted bitumen material	07/10/14	07/10/14	07/10/14	0	C
	IR-13-00013-DST-369-B	Painting the external body of butterfly valve chamber at Sta. 13+700 with accepted bitumen material	07/13/14	07/13/14	07/13/14	0	A
	IR-13-00013-DST-370-A	Formwork for walls of second(large) room of Al asa'sa chamber at Sta. 13+608 to cast co · Level · Dimensions · Verticality	07/10/14	07/12/14	07/13/14	1	A
	IR-13-00013-DST-371-A	Bedding from Sta. 2+959.22 to Sta. 2+935.50	07/10/14	07/10/14	07/13/14	3	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-372-A	Trench backfilling from Sta. 2+959.22 to Sta. 2+935.50	07/10/14	07/10/14	07/13/14	3	A
	IR-13-00013-DST-373-A	Conduct compaction test for core samples from walls of 200 GV chamber at Sta. 9+941	07/13/14	07/13/14	07/14/14	1	C
	IR-13-00013-DST-373-B	Compaction test for core samples from walls of 200 GV chamber at Sta. 9+941(according to submitted structural analysis SUB- 13-00013-DST-138-A)	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-374-A	Inspection for Fittings (Reducer, Elbow, Saddle & Tee) , Quantities and type shown in attached certificate on origin	07/13/14	07/13/14	07/15/14	2	C
	IR-13-00013-DST-374-B	Inspection for Fittings (Reducer, Elbow, Saddle & Tee) , Quantities and type shown in attached certificate on origin	08/12/14	08/12/14	08/13/14	1	A
	IR-13-00013-DST-375-A	Backfilling with single size around butterfly valves chamber at Sta. 13+700	07/13/14	07/13/14	07/13/14	0	A
	IR-13-00013-DST-376-A	Pipe encasement by casting concrete B 150 from Sta. 3+100 to Sta. 2+959.22 & Sta. 2+935.50 to Sta. 2+900	07/13/14	07/13/14	07/13/14	0	A
	IR-13-00013-DST-377-A	Pipe encasement by casting concrete B 150 from Sta. 2+900 to Sta. 2+700	07/13/14	07/14/14	07/14/14	0	A
	IR-13-00013-DST-378-A	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A14011304 & A1401331), QTY= 658.8m	07/14/14	07/15/14	07/16/14	1	A
	IR-13-00013-DST-379-A	Painting the first layer for external body of 200 mm GV chamber at Sta. 9+941with accepted bitumen material	07/14/14	07/14/14	07/14/14	0	A
	IR-13-00013-DST-380-A	Trench excavation from Sta. 2+700 to Sta. 2+500	07/14/14	07/15/14	07/15/14	0	A
	IR-13-00013-DST-381-A	Pipes installation from Sta. 2+700 to Sta. 2+500	07/14/14	07/15/14	07/15/14	0	A
	IR-13-00013-DST-382-A	Pipe encasement by casting concrete B 150 from Sta. 2+700 to Sta. 2+500	07/14/14	07/15/14	07/15/14	0	A
	IR-13-00013-DST-383-A	Painting the second layer for external body of 200 mm GV chamber at Sta. 9+941with accepted bitumen material	07/14/14	07/15/14	07/15/14	0	A
	IR-13-00013-DST-384-A	Trench excavation from Sta. 2+500 to Sta. 2+350	07/15/14	07/16/14	07/16/14	0	A
	IR-13-00013-DST-385-A	Pipes installation from Sta. 2+500 to Sta. 2+350	07/15/14	07/16/14	07/16/14	0	A
	IR-13-00013-DST-386-A	Pipe encasement by casting concrete B 150 from Sta. 2+500 to Sta. 2+350	07/15/14	07/16/14	07/16/14	0	A
	IR-13-00013-DST-387-A	Finish of casted concrete ditch from Sta. 6+975 to Sta. 6+675	07/15/14	07/16/14	07/17/14	1	C
	IR-13-00013-DST-388-A	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A1401202,A1401226,A1401228,A1401239,A1401240,A1401246 & A1401247), QTY= 2305.80 m	07/15/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-389-A	Installation of pre cast manhole at Sta. 10+461	07/15/14	07/15/14	07/15/14	0	A
	IR-13-00013-DST-390-A	Backfilling with single size aggregate around gate valve chamber at Sta. 9+941	07/16/14	07/16/14	07/16/14	0	A
	IR-13-00013-DST-391-A	Bedding and backfilling of 200 mm pipe for connection of 200 mm GV at Sta. 9+941	07/16/14	07/16/14	07/16/14	0	A
	IR-13-00013-DST-392-A	Steel reinforcement and formwork for roof slab of Al Asa'sa connection chamber (small room) at Sta. 13+608 to cast concrete	07/16/14	07/16/14	07/17/14	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-392-B	Steel reinforcement and formwork for roof slab of Al Asa'sa connection chamber (small room) at Sta. 13+608 to cast concrete	07/23/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-393-A	Finish of casted concrete ditch from Sta. 6+675 to Sta. 6+520 and Sta. 6+410 to Sta. 6+340	07/16/14	07/17/14	07/17/14	0	C
	IR-13-00013-DST-394-A	Trench excavation from Sta. 2+350 to Sta. 2+319.78	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00013-DST-395-A	Pipes installation from Sta. 2+350 to Sta. 2+319.78	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00013-DST-396-A	Pipe encasement by casting concrete B 150 from Sta. 2+350 to Sta. 2+319.78	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00013-DST-397-A	Road crossing from Sta. 2+319.78 to Sta. 2+299.88	07/17/14	07/19/14	07/22/14	3	A
	IR-13-00013-DST-398-A	Trench excavation from Sta. 2+299.88 to Sta. 2+230	07/17/14	07/20/14	07/22/14	2	A
	IR-13-00013-DST-399-A	Pipes installation from Sta. 2+299.88 to Sta. 2+230	07/17/14	07/20/14	07/22/14	2	A
	IR-13-00013-DST-400-A	Pipe encasement by casting concrete B 150 from Sta. 2+299.88 to Sta. 2+230	07/17/14	07/20/14	07/22/14	2	A
	IR-13-00013-DST-401-A	Surface preparation to start painting the external face of pre cast chamber at Sta. 10+461 with accepted bitumen material	07/17/14	07/17/14	07/17/14	0	A
	IR-13-00013-DST-402-A	Painting the first layer for external body of pre cast chamber at Sta. 10+461 with accepted bitumen material	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00013-DST-403-A	Painting the second layer for external body of pre cast chamber at Sta. 10+461 with accepted bitumen material	07/17/14	07/19/14	07/20/14	1	A
	IR-13-00013-DST-404-A	Sand plastering for external body of mechanical fittings as surface preparation (Elbow ,Tee, Reducer ,Saddle…etc)	07/20/14	07/20/14	07/20/14	0	A
	IR-13-00013-DST-405-A	Painting with epoxy material for external body of mechanical fittings (Elbow ,Tee, Rreducer ,Saddle…etc)-Starting from July 20,2014 at 8:00 AM	07/20/14	07/22/14	07/23/14	1	A
	IR-13-00013-DST-406-A	Start finishing work for internal surface of pre cast at Sta. 10+461 from July 20,2014 At 9:00 AM	07/20/14	07/23/14	07/23/14	0	C
	IR-13-00013-DST-406-B	Finishing work for internal surface of pre cast at Sta. 10+461	08/07/14	08/10/14	08/11/14	1	A
	IR-13-00013-DST-407-A	Backfilling with single size around pre-cast manhole at sta. 10+461 ,starting from July 20,2014 at 10:00AM	07/20/14	07/21/14	07/22/14	1	C
	IR-13-00013-DST-407-B	Backfilling with single size around pre-cast manhole at sta. 10+461	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-408-A	Trench excavation from Sta. 2+230 to Sta. 2+100	07/22/14	07/23/14	07/23/14	0	A
	IR-13-00013-DST-409-A	Pipes installation from Sta. 2+230 to Sta. 2+100	07/22/14	07/23/14	07/23/14	0	A
	IR-13-00013-DST-410-A	Pipe encasement by casting concrete B 150 from Sta. 2+230 to Sta. 2+100	07/22/14	07/23/14	07/23/14	0	A
	IR-13-00013-DST-411-A	Trench excavation from Sta. 2+100 to Sta. 2+000	07/22/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-412-A	Pipes installation from Sta. 2+100 to Sta. 2+000	07/22/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-413-A	Pipe encasement by casting concrete B 150 from Sta. 2+100 to Sta. 2+000	07/22/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-414-A	Conduct internal cement lining for 12 inch mitered bends fabrication starting from July 22,2014 at time 01:30 PM	07/22/14	07/31/14	08/03/14	3	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-415-A	Inspection to start excavation (Location & marking) for the followings chambers: · Combined Air release & butterfly valves at Sta. 3+340 · Air release valve at Sta. 9+970 · Air release valve at Sta. 12+500	07/23/14	07/23/14	07/24/14	1	A
	IR-13-00013-DST-416-A	Steel reinforcement and formwork for roof slab of 250mm gate valve at Sta. 13+617 to cast concrete	07/23/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-417-A	Trench excavation from Sta. 2+000 to Sta. 1+880	07/24/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-418-A	Pipes installation from Sta. 2+000 to Sta. 1+880	07/24/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-419-A	Pipe encasement by casting concrete B 150 from Sta. 2+000 to Sta. 1+880	07/24/14	07/24/14	07/24/14	0	A
	IR-13-00013-DST-420-A	Trench excavation from Sta. 1+880 to Sta. 1+780	08/02/14	08/04/14	08/04/14	0	A
	IR-13-00013-DST-421-A	Pipes installation from Sta. 1+880 to Sta. 1+780	08/02/14	08/04/14	08/04/14	0	A
	IR-13-00013-DST-422-A	Pipe encasement by casting concrete B 150 from Sta. 1+880 to Sta. 1+780	08/02/14	08/04/14	08/04/14	0	A
	IR-13-00013-DST-423-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch (Sta. 5+581 to Sta. 5+389)	08/03/14	08/03/14	08/04/14	1	A
	IR-13-00013-DST-424-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 5+389 to Sta. 5+189 (Starting from August 04,2014 at 8:00 AM)	08/03/14	08/05/14	08/06/14	1	A
	IR-13-00013-DST-425-A	Inspection to start excavation (location & marking) for Silat Al Daher connection chamber at Sta. 10+410	08/03/14	08/03/14	08/04/14	1	C
	IR-13-00013-DST-425-B	Inspection to start excavation (location & marking) for Silat Al Daher connection chamber at Sta. 10+410	08/07/14	08/07/14	08/07/14	0	A
	IR-13-00013-DST-426-A	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A1401359,A1401396 &A1401394), QTY= 988.20 m	08/03/14	08/05/14	08/07/14	2	A
	IR-13-00013-DST-427-A	12 inch mitered bends fabrication	08/03/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-428-A	Trench excavation from Sta. 1+780 to Sta. 1+680	08/03/14	08/05/14	08/06/14	1	A
	IR-13-00013-DST-429-A	Pipes installation from Sta. 1+780 to Sta. 1+680	08/03/14	08/05/14	08/06/14	1	A
	IR-13-00013-DST-430-A	Pipe encasement by casting concrete B 150 from Sta. 1+780 to Sta. 1+680	08/03/14	08/05/14	08/06/14	1	A
	IR-13-00013-DST-431-A	Inspection for Combined AR/AV and BFV at Sta. 3+350, include : · Excavation dimensions · Spread single size below base slab · Safety around the manhole. · level	08/04/14	08/05/14	08/06/14		A
	IR-13-00013-DST-432-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 5+690.40 to Sta. 5+746	08/05/14	08/05/14	08/06/14	1	A
	IR-13-00013-DST-433-A	Conduct internal cement lining repair for the fabricated bends # (142,143,144,145 ,146,147 & 148)	08/05/14	08/05/14	08/06/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-434-A	Trench excavation from Sta. 1+680 to Sta. 1+580	08/05/14	08/07/14	08/07/14	0	A
	IR-13-00013-DST-435-A	Pipes installation from Sta. 1+680 to Sta. 1+580	08/05/14	08/07/14	08/07/14	0	A
	IR-13-00013-DST-436-A	Pipe encasement by casting concrete B 150 from Sta. 1+680 to Sta. 1+580	08/05/14	08/07/14	08/07/14	0	A
	IR-13-00013-DST-437-A	Steel reinforcement work and formwork for foundation of combined AV/AR & BFV at Sta. 3+350 to cast concrete	08/06/14	08/06/14	08/06/14	0	A
	IR-13-00013-DST-438-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 5+189 to Sta. 4+960(Starting from Aug. 06 at 9:00 AM)	08/06/14	08/07/14	08/07/14	0	A
	IR-13-00013-DST-439-A	Trench excavation from Sta. 1+580 to Sta. 1+300	08/06/14	08/09/14	08/10/14	1	A
	IR-13-00013-DST-440-A	Pipes installation from Sta. 1+580 to Sta. 1+300	08/06/14	08/09/14	08/10/14	1	A
	IR-13-00013-DST-441-A	Pipe encasement by casting concrete B 150 from Sta. 1+580 to Sta. 1+413 and from Sta. 1+360 to Sta. 1+300	08/06/14	08/09/14	08/10/14	1	A
	IR-13-00013-DST-442-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 4+960 to Sta. 4+870	08/07/14	08/07/14	08/07/14	0	A
	IR-13-00013-DST-443-A	Steel reinforcement work for walls of combined AV/AR & BFV at Sta. 3+350	08/07/14	08/07/14	08/07/14	0	A
	IR-13-00013-DST-444-A	Inspection for dimension level & single size layer for excavation of Silat Al Daher to cast rubble concrete under foundation	08/07/14	08/07/14	08/10/14	3	A
	IR-13-00013-DST-445-A	Steel reinforcement work and formwork for walls of combined AV/AR & BFV at Sta. 3+350 to cast concrete	08/07/14	08/09/14	08/10/14	1	A
	IR-13-00013-DST-446-A	Steel reinforcement and formwork for roof slab of Al Asa'sa connection chamber (large room) at Sta. 13+608 to cast concrete	08/07/14	08/09/14	08/10/14	1	A
	IR-13-00013-DST-447-A	Inspection for complete installed pre-cast manhole (Base slab, raiser rings & roof slab)	08/07/14	08/10/14	08/11/14	1	A
	IR-13-00013-DST-448-A	Inspection to start excavation (location & marking) for butterfly valve chamber at Sta. 2+952	08/10/14	08/10/14	08/11/14	1	A
	IR-13-00013-DST-449-A	Bedding from Sta. 1+413 to Sta. 1+360	08/10/14	08/10/14	08/10/14	0	A
	IR-13-00013-DST-450-A	Backfilling from Sta. 1+413 to Sta. 1+360	08/10/14	08/10/14	08/10/14	0	A
	IR-13-00013-DST-451-A	Trench excavation from Sta. 1+300 to Sta. 1+239 and from Sta. 1+224.19 to Sta. 1+213.25	08/10/14	08/10/14	08/10/14	0	A
	IR-13-00013-DST-452-A	Pipes installation from Sta. 1+300 to Sta. 1+239 and from Sta. 1+224.19 to Sta. 1+213.25	08/10/14	08/10/14	08/10/14	0	A
	IR-13-00013-DST-453-A	Main road crossing from Sta. 1+239 to Sta. 1+224.19	08/10/14	08/10/14	08/10/14	0	A
	IR-13-00013-DST-454-A	Pipe encasement by casting concrete B 150 from Sta. 1+300 to Sta. 1+239	08/10/14	08/10/14	08/10/14	0	A
	IR-13-00013-DST-455-A	Steel reinforcement and formwork for foundation of Silat Al Daher connection chamber part 1 (small room) at Sta. 10+410	08/10/14	08/10/14	08/11/14	1	D
	IR-13-00013-DST-455-B	Steel reinforcement and formwork for foundation of Silat Al Daher connection chamber part 1 (small room) at Sta. 10+411	01/26/15	01/26/15	01/27/15	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-456-A	Conduct base course field compaction test from Sta. 3+950 to Sta. 4+080 and Sta. 6+430 to Sta. 6+508	08/11/14	08/11/14	08/11/14	0	A
	IR-13-00013-DST-457-A	Trench excavation from Sta. 9+691.34 to Sta. 9+590	08/11/14	08/12/14	08/12/14	0	A
	IR-13-00013-DST-458-A	Pipes installation from Sta. 9+691.34 to Sta. 9+590	08/11/14	08/12/14	08/12/14	0	A
	IR-13-00013-DST-459-A	Bedding from Sta. 9+691.34 to Sta. 9+610	08/11/14	08/12/14	08/14/14	2	A
	IR-13-00013-DST-460-A	Trench backfilling from Sta. 9+691.34 to Sta. 9+590	08/11/14	08/12/14	08/13/14	1	A
	IR-13-00013-DST-461-A	Inspection to spread prime coat on finished base course layer from Sta. 3+950 to Sta. 4+080 and Sta. 6+430 to Sta. 6+508	08/11/14	08/11/14	08/11/14	0	A
	IR-13-00013-DST-462-A	Asphalt reinstatement over trench edges with 300 mm pipes from Sta. 3+950 to Sta. 4+080 and Sta. 6+430 to Sta. 6+508	08/11/14	08/11/14	08/11/14	0	A
	IR-13-00013-DST-463-A	Inspection for butterfly valve at Sta. 2+952 to cast blind concrete , include : · Excavation dimensions · Spread single size below base slab · Safety around the manhole. · level	08/11/14	08/11/14	08/11/14	0	A
	IR-13-00013-DST-464-A	Inspection to start excavation (location & marking) for two wash out valve chambers at Sta. 2+936 & Sta. 13+627	08/12/14	08/13/14	08/13/14	0	A
	IR-13-00013-DST-465-A	Steel reinforcement work and formwork for foundation of butterfly valve chamber at Sta. 2+952 to cast concrete	08/12/14	08/12/14	08/13/14	1	A
	IR-13-00013-DST-466-A	Conduct internal cement lining repair for the fabricated bends # (138,129,130,135,165,166,169,167,122,168,170,118,171,172,121,119,125 & 103)	08/13/14	08/13/14	08/14/14	1	A
	IR-13-00013-DST-467-A	Pipe encasement by casting concrete B 150 from Sta. 9+610 to Sta. 9+548	08/13/14	08/13/14	08/13/14	0	A
	IR-13-00013-DST-468-A	Formwork and steel reinforcement for walls of butterfly valve chamber at Sta. 2+952	08/13/14	08/13/14	08/14/14	1	A
	IR-13-00013-DST-469-A	Trench excavation from Sta. 9+590 to Sta. 9+490	08/13/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-470-A	Pipes installation from Sta. 9+590 to Sta. 9+490	08/13/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-471-A	Trench backfilling from Sta. 9+590 to Sta. 9+557	08/13/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-472-A	Inspection for complete installed pre-cast wash out manhole (Base slab, raiser rings & roof slab)	08/13/14	08/13/14	08/14/14	1	C
	IR-13-00013-DST-472-B	Inspection for complete installed pre-cast wash out manhole (Base slab, raiser rings & roof slab)	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-473-A	Formwork for walls of butterfly valve chamber at Sta. 2+952 to cast concrete : · Level · Dimensions · Verticality	08/14/14	08/14/14	08/14/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-474-A	Inspection to start excavation (location & marking) for Al Foundqumiya connection chamber at Sta. 12+142	08/14/14	08/14/14	08/14/14	0	C
	IR-13-00013-DST-474-B	Inspection to start excavation (location & marking) for Al Foundqumiya connection chamber at Sta. 12+142	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-475-A	Pipe encasement by casting concrete B 150 from Sta. 9+548 to sta. 9+490	08/14/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-476-A	Trench excavation from Sta. 9+490 to Sta. 9+390	08/14/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-477-A	Pipes installation from Sta. 9+490 to Sta. 9+390	08/14/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-478-A	Pipe encasement by casting concrete B 150 from Sta. 9+490 to Sta. 9+390	08/14/14	08/14/14	08/14/14	0	A
	IR-13-00013-DST-479-A	Trench excavation from Sta. 9+390 to Sta. 9+300	08/14/14	08/16/14	08/17/14	1	A
	IR-13-00013-DST-480-A	Pipes installation from Sta. 9+390 to Sta. 9+300	08/14/14	08/16/14	08/17/14	1	A
	IR-13-00013-DST-481-A	Pipe encasement by casting concrete B 150 from Sta. 9+390 to Sta. 9+300	08/14/14	08/16/14	08/17/14	1	A
	IR-13-00013-DST-482-A	Inspection for pre-cast wash out manhole at Sta. 2+936, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	08/16/14	08/16/14	08/18/14	2	A
	IR-13-00013-DST-483-A	Inspection for pre-cast wash out manhole at Sta. 13+627, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	08/16/14	08/16/14	08/18/14	2	A
	IR-13-00013-DST-484-A	Inspection for installing pre-cast wash out manhole at Sta. 2+936	08/16/14	08/16/14	08/18/14	2	C
	IR-13-00013-DST-484-B	Inspection for installing pre-cast wash out manhole at Sta. 2+936	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-485-A	Inspection for installing pre-cast wash out manhole at Sta. 13+627	08/16/14	08/16/14	08/18/14	2	C
	IR-13-00013-DST-485-B	Inspection for installing pre-cast wash out manhole at Sta. 13+627	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-486-A	Trench excavation from Sta. 9+300 to Sta. 9+200	08/17/14	08/17/14	08/18/14	1	A
	IR-13-00013-DST-487-A	Pipes installation from Sta. 9+300 to Sta. 9+200	08/17/14	08/17/14	08/18/14	1	A
	IR-13-00013-DST-488-A	Pipe encasement by casting concrete B 150 from Sta. 9+300 to Sta. 9+200	08/17/14	08/17/14	08/18/14	1	A
	IR-13-00013-DST-489-A	Steel reinforcement and formwork for roof slab of combined AV/AR & BFV chamber at Sta. 3+350 to cast concrete	08/17/14	08/17/14	08/18/14	1	A
	IR-13-00013-DST-490-A	Steel reinforcement and formwork for roof slab of butterfly valve chamber at Sta. 2+952 to cast concrete	08/17/14	08/17/14	08/18/14	1	A
	IR-13-00013-DST-491-A	Manufacturing process of external polyethylene coating & internal cement lining for 12 & 6 inch OD pipes	08/17/14	08/18/14	08/20/14	2	A
	IR-13-00013-DST-492-A	Surface finish preparation and filling conical holes for walls of GV chamber at Sta. 13+617 using approved FOSROC material (starting from Aug. 18,2014 at 8:30 AM)	08/18/14	08/19/14	08/20/14	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-492-B	Surface finish preparation and filling conical holes for walls of GV chamber at Sta. 13+617 using approved FOSROC material	08/21/14	08/21/14	08/21/14	0	A
	IR-13-00013-DST-493-A	Surface finish preparation and filling conical holes for walls of Al asa'sa connection(part A &B) chamber at Sta. 13+608 using approved FOSROC material (starting from Aug. 18,2014 at 8:30 AM)	08/18/14	08/19/14	08/20/14	1	C
	IR-13-00013-DST-493-B	Surface finish preparation and filling conical holes for walls of Al asa'sa connection(part A &B) chamber at Sta. 13+608 using approved FOSROC material	08/21/14	08/21/14	08/21/14	0	A
	IR-13-00013-DST-494-A	Trench excavation from Sta. 9+200 to Sta. 9+100	08/18/14	08/18/14	08/19/14	1	A
	IR-13-00013-DST-495-A	Pipes installation from Sta. 9+200 to Sta. 9+100	08/18/14	08/18/14	08/19/14	1	A
	IR-13-00013-DST-496-A	Pipe encasement by casting concrete B 150 from Sta. 9+200 to Sta. 9+100	08/18/14	08/18/14	08/19/14	1	A
	IR-13-00013-DST-497-A	Formwork and steel reinforcement for opening neck of manhole cover to cast concrete, for the followings chambers: • BFV chamber at Sta. 13+700 • 250 GV chamber at sta. 13+617 • Al Asa'sa connection chamber (part A & B) at Sta. 13+608 • Combined AV/AR & BFV at Sta. 11+187	08/18/14	08/18/14	08/19/14	1	C
	IR-13-00013-DST-497-B	Formwork and steel reinforcement for opening neck of manhole cover to cast concrete, for the followings chambers: • BFV chamber at Sta. 13+700 • 250 GV chamber at sta. 13+617 • Al Asa'sa connection chamber (part A & B) at Sta. 13+608 • Combined AV/AR & BFV at Sta. 11+187	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-498-A	Inspection for marking location of AV/AR chamber at Sta. 8+900	08/18/14	08/19/14	08/20/14	1	A
	IR-13-00013-DST-499-A	Trench excavation from Sta. 9+100 to Sta. 9+029.89	08/20/14	08/20/14	08/21/14	1	A
	IR-13-00013-DST-500-A	Pipes installation from Sta. 9+100 to Sta. 9+029.89	08/20/14	08/20/14	08/21/14	1	A
	IR-13-00013-DST-501-A	Pipe encasement by casting concrete B 150 from Sta. 9+100 to Sta. 9+029.89	08/20/14	08/20/14	08/21/14	1	A
	IR-13-00013-DST-502-A	Road crossing from Sta. 9+029.89 to Sta. 9+011.7	08/20/14	08/20/14	08/21/14	1	A
	IR-13-00013-DST-503-A	Trench excavation from Sta. 9+011.7 to Sta. 8+900	08/20/14	08/21/14	08/21/14	0	A
	IR-13-00013-DST-504-A	Pipe installation from Sta. 9+011.7 to Sta. 8+900	08/20/14	08/21/14	08/21/14	0	A
	IR-13-00013-DST-505-A	Pipe encasement by casting concrete B 150 from Sta. 9+011.7 to Sta. 9+005.40	08/20/14	08/21/14	08/21/14	0	A
	IR-13-00013-DST-506-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 4+870 to Sta. 4+720 (Starting from Aug. 21,2014 at 8:30 AM)	08/20/14	08/21/14	08/21/14	0	A
	IR-13-00013-DST-507-A	Welding & pipe installation for W.O manhole connections at Sta. 13+628 (Starting from Aug. 21,2014 at 9:30 AM)	08/21/14	08/24/14	08/25/14	1	A
	IR-13-00013-DST-508-A	Welding & pipe installation for 250 mm GV manhole connections at Sta. 13+617(Starting from Aug. 21,2014 at 9:30 AM)	08/21/14	08/24/14	08/25/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-509-A	Bedding from Sta. 9+005.40 to Sta. 8+900 (Starting from Aug. 21,2014 at 11:00 AM)	08/21/14	08/23/14	08/24/14	1	A
	IR-13-00013-DST-510-A	Backfilling from Sta. 9+011.7 to Sta. 8+900 (Starting from Aug. 21,2014 at 11:00 AM)	08/21/14	08/23/14	08/24/14	1	A
	IR-13-00013-DST-511-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 4+720 to Sta. 4+570 (Starting from Aug. 21,2014 at 11:00 AM)	08/21/14	08/23/14	08/24/14	1	A
	IR-13-00013-DST-512-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 4+570 to Sta. 4+220 (Starting from Aug. 23,2014 at 08:30 AM)	08/21/14	08/24/14	08/25/14	1	A
	IR-13-00013-DST-513-A	Trench excavation from Sta. 8+900 to Sta. 8+800	08/21/14	08/23/14	08/24/14	1	C
	IR-13-00013-DST-513-B	Trench excavation from Sta. 8+900 to Sta. 8+800	08/26/14	08/26/14	08/26/14	0	A
	IR-13-00013-DST-514-A	Pipes installation from Sta. 8+900 to Sta. 8+800	08/21/14	08/23/14	08/24/14	1	C
	IR-13-00013-DST-514-B	Pipes installation from Sta. 8+900 to Sta. 8+800	08/26/14	08/26/14	08/26/14	0	A
	IR-13-00013-DST-515-A	Start painting the external face of Al Asa'sa connection chamber at Sta. 13+608 with accepted bitumen material (Starting Aug. 21,2014 at time 3:00 PM)	08/21/14	08/23/14	08/24/14	1	A
	IR-13-00013-DST-516-A	Welding & pipe installation for W.O manhole connections at Sta. 2+936(Starting from Aug. 21,2014 at 3:00 PM)	08/21/14	08/23/14	08/24/14	1	C
	IR-13-00013-DST-516-B	Welding & pipe installation for W.O manhole connections at Sta. 2+936	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-517-A	External surface preparation using FOSROC material for W.O manhole at Sta. 2+936 (Starting Aug. 23,2014 at 8:00 AM)	08/21/14	08/24/14	08/25/14	1	A
	IR-13-00013-DST-518-A	External surface preparation using FOSROC material for W.O manhole at Sta. 13+628 (Starting Aug. 23,2014 at 8:00 AM)	08/21/14	08/24/14	08/25/14	1	A
	IR-13-00013-DST-519-A	12 inch fabrication bends starting from Aug. 24,2014 at 11:00 AM	08/24/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-520-A	Surface finish preparation for external body of combined AV/AR chamber at Sta. 3+350	08/25/14	08/25/14	08/26/14	1	A
	IR-13-00013-DST-521-A	Surface finish preparation for external body of butterfly valve chamber at Sta. 2+952	08/25/14	08/25/14	08/26/14	1	A
	IR-13-00013-DST-522-A	Finished base course layer under drainage ditch to start reinforcement work from Sta. 1+239 to Sta. 1+330 & Sta. 1+370 to Sta. 1+800	08/25/14	08/25/14	08/26/14	1	A
	IR-13-00013-DST-523-A	Conduct internal cement lining repair for the fabricated bends # (181,182,183,184,185,186,187)	08/25/14	08/25/14	08/26/14	1	A
	IR-13-00013-DST-524-A	Steel reinforcement work and finish base course layer to cast concrete for drainage ditch from Sta. 4+220 to Sta. 4+050	08/25/14	08/25/14	08/25/14	0	A
	IR-13-00013-DST-525-A	Painting the first layer for external face of Al Asa'sa connection chamber at Sta. 13+608 with accepted bitumen material	08/25/14	08/25/14	08/25/14	0	A
	IR-13-00013-DST-526-A	Location & marking for AV/AR valve chamber at Sta. 11+743	08/25/14	08/25/14	08/25/14	0	A
	IR-13-00013-DST-527-A	Surface finish preparation for internal walls of 200 mm GV at Sta. 9+941 using FOSROC material (Staring from Aug. 25,2014 at 3:00 PM)	08/25/14	08/26/14	08/27/14	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-527-B	Surface finish preparation for internal walls of 200 mm GV at Sta. 9+941	12/14/14	12/14/14	12/15/14	1	C
	IR-13-00013-DST-527-C	Surface finish preparation for internal walls of 200 mm GV at Sta. 9+941	01/25/15	01/25/15	01/25/15	0	A
	IR-13-00013-DST-528-A	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A1401589,A1401532 ,A1401526 & A15401523), QTY= 1317.6 m	08/26/14	08/27/14	08/28/14	1	A
	IR-13-00013-DST-529-A	6 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A1401568) QTY= 719.8 m	08/26/14	08/27/14	08/28/14	1	C
	IR-13-00013-DST-529-B	7 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A1401568) QTY= 719.8 m	09/23/14	09/23/14	09/23/14	0	A
	IR-13-00013-DST-530-A	Trench excavation from Sta. 8+800 to Sta. 8+700	08/26/14	08/27/14	08/27/14	0	A
	IR-13-00013-DST-531-A	Pipes installation from Sta. 8+800 to Sta. 8+700	08/26/14	08/27/14	08/27/14	0	A
	IR-13-00013-DST-532-A	Inspection for installation AV/AR pre-cast manhole at Sta. 11+743(Starting from Aug. 26,2014 at 12:00 PM)	08/26/14	08/26/14	08/27/14	1	A
	IR-13-00013-DST-533-A	Inspection for installation AV/AR pre-cast manhole at Sta. 12+514(Starting from Aug. 26,2014 at 12:00 PM)	08/26/14	08/26/14	08/27/14	1	A
	IR-13-00013-DST-534-A	Welding & pipe installation for AV/AR manhole connections at Sta. 11+743(Starting from Aug. 26,2014 at 12:00 PM)	08/26/14	08/27/14	08/28/14	1	A
	IR-13-00013-DST-535-A	Welding & pipe installation for AV/AR manhole connections at Sta. 12+514(Starting from Aug. 26,2014 at 12:00 PM)	08/26/14	08/27/14	08/28/14	1	A
	IR-13-00013-DST-536-A	Finished surface repair for fabricated bends NO. (181,182,183,184,185,186,187) using FC FOSROC material (Starting from Aug. 26,2014 at 12:00 PM)	08/26/14	08/27/14	08/28/14	1	A
	IR-13-00013-DST-537-A	Bedding from Sta. 8+900 to Sta. 8+814.8	08/26/14	08/26/14	08/26/14	0	A
	IR-13-00013-DST-538-A	Trench backfilling from Sta. 8+900 to Sta. 8+814.8	08/26/14	08/26/14	08/26/14	0	A
	IR-13-00013-DST-539-A	Formwork and steel reinforcement for drainage ditch from Sta. 1+239 to Sta. 1+330 & Sta. 1+370 to Sta. 1+800 to cast concrete (Starting Aug. 27,2014 at 8:00 AM)	08/26/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-540-A	External surface preparation for pre-cast AV/AR manhole at Sta. 11+743(Starting from Aug. 27,2014 at 9:00 AM)	08/27/14	08/27/14	08/28/14	1	A
	IR-13-00013-DST-541-A	External surface preparation for pre-cast AV/AR manhole at Sta. 12+514(Starting from Aug. 27,2014 at 9:00 AM)	08/27/14	08/27/14	08/28/14	1	A
	IR-13-00013-DST-542-A	Pipe encasement by casting concrete B 150 from Sta. 8+814.8 to Sta. 8+800	08/27/14	08/27/14	08/27/14	0	A
	IR-13-00013-DST-543-A	Pipe encasement by casting concrete B 150 from Sta. 8+800 to Sta. 8+700	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-544-A	Painting the first layer for external face of 250 mm GV chamber at sta. 13+617 with accepted bitumen material	08/27/14	08/27/14	08/27/14	0	A
	IR-13-00013-DST-545-A	Painting the first layer for external face of pre-cast AV/AR chamber at Sta. 11+743 with accepted bitumen material(Staring from Aug. 27,2014 at 3:30 PM)	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-546-A	Painting the first layer for external face of pre-cast AV/AR chamber at Sta. 12+514 with accepted bitumen material(Staring from Aug. 27,2014 at 3:30 PM)	08/27/14	08/28/14	08/28/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-547-A	Marking location of Al Foundqumiya connection chamber at Sta. 12+143 & Sabstiya connection chamber at Sta. 2+320	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-548-A	Painting the second layer for external face of 250 mm GV chamber at sta. 13+617 with accepted bitumen material(Staring from Aug. 27,2014 at 3:00 PM)	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-549-A	Painting the second layer for external face of Al Asa'sa connection chamber at sta. 13+608 with accepted bitumen material(Staring from Aug. 27,2014 at 3:00 PM)	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-550-A	Painting the second layer for external face of pre-cast AV/AR chamber at Sta. 11+743 with accepted bitumen material(Starting from Aug. 27,2014 at 4:00PM)	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-551-A	Painting the second layer for external face of pre-cast AV/AR chamber at Sta. 12+514 with accepted bitumen material (Starting from Aug. 27,2014 at 4:00PM)	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-552-A	Backfilling with single size around AV/AR manhole at Sta. 11+743(Starting from Aug. 27,2014 at 5:30 PM)	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-553-A	Backfilling with single size around AV/AR manhole at Sta. 12+514(Starting from Aug. 27,2014 at 5:30 PM)	08/27/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-554-A	Painting the first layer for external face of BFV chamber at Sta. 2+952 by accepted bitumen material (Starting from Aug. 28,2014 at 9:00 AM)	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-555-A	Painting the first layer for external face of combined AV/AR & BFV chamber at Sta. 3+350 by accepted bitumen material (Starting from Aug. 28,2014 at 9:00 AM)	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-556-A	Trench excavation from Sta. 8+700 to Sta. 8+600	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-557-A	Pipes installation from Sta. 8+700 to Sta. 8+600	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-558-A	Backfilling with single size around 250 mm GV chamber at Sta. 13+617	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-559-A	6 inch bends fabrication (Starting from Aug. 28,2014 at 9: 00 AM)	08/28/14	09/04/14	09/04/14	0	C
	IR-13-00013-DST-559-B	Continue 6 inch bends fabrication (Starting from Sep. 13,2014 at 11:00 AM)	09/13/14	09/16/14	09/16/14	0	A
	IR-13-00013-DST-560-A	Finished base course layer under daring ditch to start steel reinforcement work from Sta. 1+909 to Sta. 2+224	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-561-A	Steel reinforcement work for drainage ditch to cast concrete from Sta. 1+909 to Sta. 2+224(Starting from Aug. 28,2014 at 10:30 AM)	08/28/14	08/28/14	08/28/14	0	A
	IR-13-00013-DST-562-A	Trench excavation from Sta. 8+600 to Sta. 8+500	08/28/14	08/30/14	08/31/14	1	A
	IR-13-00013-DST-563-A	Pipes installation from Sta. 8+600 to Sta. 8+500	08/28/14	08/30/14	08/31/14	1	A
	IR-13-00013-DST-564-A	Pipe encasement by casting concrete B 150 from Sta. 8+700 Sta. 8+600	08/28/14	08/30/14	08/31/14	1	A
	IR-13-00013-DST-565-A	Starting excavation for Al Foundqumiya connection chamber at Sta. 12+143(Starting from Aug. 28,2014 at 11:00 AM)	08/28/14	08/31/14	08/31/14	0	A
	IR-13-00013-DST-566-A	Painting the second layer for external face of BFV at Sta. 2+952 with accepted bitumen material(Starting from Aug. 28,2014 at 3:00 PM)	08/28/14	08/30/14	08/31/14	1	C
	IR-13-00013-DST-566-B	Painting the second layer for external face of BFV at Sta. 2+952 with accepted bitumen material	09/02/14	09/02/14	09/03/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-567-A	Inspection for Al Foundqumeya connection chamber to cast blind layer at Sta. 12+143, include : • Dimension of excavation • Spread single size below base slab • Safety around the manhole. • level	08/30/14	08/30/14	08/31/14	1	A
	IR-13-00013-DST-568-A	Painting the second layer for external face of combined AV/AR & BFV at Sta. 3+350 with accepted bitumen material	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00013-DST-569-A	Backfilling around combined AV/AR & BFV chamber at Sta. 3+350 with single size aggregate (Starting from Aug. 31,2014 at 9:00AM)	08/31/14	09/01/14	09/02/14	1	C
	IR-13-00013-DST-569-B	Backfilling around combined AV/AR & BFV chamber at Sta. 3+350 with single size aggregate	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-570-A	Marking location of two AV/AR chambers at Sta. 5+110 & Sta. 6+332	08/31/14	08/31/14	08/31/14	0	A
	IR-13-00013-DST-571-A	Trench excavation from Sta. 8+500 to Sta. 8+400	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00013-DST-572-A	Pipe installation from Sta. 8+500 to Sta. 8+400	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00013-DST-573-A	Pipe encasement by casting concrete B 150 from Sta. 8+600 to Sta. 8+500	08/31/14	08/31/14	08/31/14	0	A
	IR-13-00013-DST-574-A	Trench excavation from Sta. 8+400 to Sta. 8+300	08/31/14	09/02/14	09/02/14	0	A
	IR-13-00013-DST-575-A	Pipe installation from Sta. 8+400 to Sta. 8+300	08/31/14	09/02/14	09/02/14	0	A
	IR-13-00013-DST-576-A	Pipe encasement by casting concrete B 150 from Sta. 8+500 to Sta. 8+400	08/31/14	09/02/14	09/02/14	0	A
	IR-13-00013-DST-577-A	Formwork and Steel reinforcement work of opening neck to cast concrete for the following chambers: • BFV at Sta. 2+952 • Combined AV/AR & BFV at Sta. 3+350	08/31/14	08/31/14	09/01/14	1	C
	IR-13-00013-DST-577-B	Formwork and Steel reinforcement work of opening neck to cast concrete for the following chambers: • BFV at Sta. 2+952 • Combined AV/AR & BFV at Sta. 3+350	09/09/14	09/09/14	09/09/14	0	A
	IR-13-00013-DST-578-A	Formwork and steel reinforcement work for foundation part A (Small room)of Al Foundqumiya connection chamber at Sta. 12+143 to cast concrete	08/31/14	08/31/14	09/01/14	1	A
	IR-13-00013-DST-579-A	Start excavation for Sabstiya connection chamber at Sta. 2+320(Starting from Sep. 01,2014 at 1:30 PM)	09/01/14	09/03/14	09/03/14	0	A
	IR-13-00013-DST-580-A	Inspection for installation of pre-cast AV/AR manhole at Sta. 5+110	09/02/14	09/03/14	09/03/14	0	A
	IR-13-00013-DST-581-A	Inspection for installation of pre-cast AV/AR manhole at Sta. 6+332	09/02/14	09/03/14	09/03/14	0	A
	IR-13-00013-DST-582-A	Marking location of AV/AR chamber at Sta. 8+885	09/02/14	09/03/14	09/03/14	0	A
	IR-13-00013-DST-583-A	Trench excavation from Sta. 8+300 to Sta. 8+239	09/02/14	09/02/14	09/03/14	1	A
	IR-13-00013-DST-584-A	Pipes installation from Sta. 8+300 to Sta. 8+239	09/02/14	09/02/14	09/03/14	1	A
	IR-13-00013-DST-585-A	Pipe encasement by casting concrete B 150 from Sta. 8+400 to Sta. 8+300	09/02/14	09/02/14	09/03/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-586-A	Formwork and steel reinforcement work for walls of Al Founqumiya connection chamber(part 1) at Sta. 12+143 to cast concrete	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-587-A	Inspection for Sabastiya connection chamber at Sta. 2+320 to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-588-A	Pipe installation of pre-cast AV/AR manhole at Sta. 5+110(Starting from Sep. 03 at 2:00 PM)	09/03/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-589-A	Pipe installation of pre-cast AV/AR manhole at Sta. 6+332(Starting from Sep. 03 at 2:00 PM)	09/03/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-590-A	Backfilling around BFV chamber at Sta. 2+952 with single size	09/03/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-591-A	Surface preparation for external body of pre-cast AV/AR manhole at Sta. 5+110	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-592-A	Surface preparation for external body of pre-cast AV/AR manhole at Sta. 6+332	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-593-A	Painting the first layer of external face of pre-cast AV/AR manhole at Sta. 5+110 with accepted bitumen material	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-594-A	Painting the first layer of external face of pre-cast AV/AR manhole at Sta. 6+332 with accepted bitumen material	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-595-A	Painting the second layer of external face of pre-cast AV/AR manhole at Sta. 5+110 with accepted bitumen material	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-596-A	Painting the second layer of external face of pre-cast AV/AR manhole at Sta. 6+332 with accepted bitumen material	09/03/14	09/03/14	09/04/14	1	A
	IR-13-00013-DST-597-A	Backfilling around pre-cast AV/AR manhole at Sta. 5+110 with single size aggregate	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-598-A	Backfilling around pre-cast AV/AR manhole at Sta. 6+332 with single size aggregate	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-599-A	Formwork and steel reinforcement work for foundation of Al Foundqumiya connection chamber part 2 at Sta. 12+143 to cast concrete	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-600-A	Formwork and steel reinforcement work for foundation of Sabstiya connection chamber part 1 at Sta. 2+320 to cast concrete	09/04/14	09/06/14	09/07/14	1	C
	IR-13-00013-DST-600-B	Formwork and steel reinforcement work for foundation of Sabstiya connection chamber part 1 at Sta. 2+320 to cast concrete	09/09/14	09/09/14	09/09/14	0	A
	IR-13-00013-DST-601-A	Road crossing from Sta. 8+238. 26 to Sta. 8+214.66	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-602-A	Trench excavation from Sta. 8+214.66 to Sta. 8+ 170	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-603-A	Pipes installation from Sta. 8+214.66 to Sta. 8+ 170	09/04/14	09/04/14	09/04/14	0	A
	IR-13-00013-DST-604-A	Trench excavation from Sta. 8+ 170 to Sta. 8+070	09/04/14	09/06/14	09/07/14	1	A
	IR-13-00013-DST-605-A	Pipes installation from Sta. 8+ 170 to Sta. 8+070	09/04/14	09/06/14	09/07/14	1	A
	IR-13-00013-DST-606-A	Pipe encasement by casting concrete B 150 from Sta. 8+300 to Sta. 8+238.26	09/07/14	09/07/14	09/07/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-607-A	Pipe encasement by casting concrete B 150 from Sta. 8+214.66 to Sta. 8+170	09/07/14	09/07/14	09/07/14	0	A
	IR-13-00013-DST-608-A	Marking location of W.O pre-cast manhole at Sta. 10+889 to start excavation	09/07/14	09/07/14	09/08/14	1	A
	IR-13-00013-DST-609-A	External formwork and steel reinforcement work for walls of Al Foundqumiya (part 2) at Sta. 12+143 to cast concrete	09/08/14	09/08/14	09/08/14	0	A
	IR-13-00013-DST-610-A	Formwork for walls of Al foundqumiya (part 2) connection chamber at Sta. 12+143 to cast concrete : • Level • Dimensions • Verticality	09/08/14	09/08/14	09/09/14	1	A
	IR-13-00013-DST-611-A	Road crossing from Sta. 8+070.64 to Sta. 8+053.03	09/08/14	09/08/14	09/08/14	0	A
	IR-13-00013-DST-612-A	Trench excavation from Sta. 8+053.03 to Sta. 7+950	09/08/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-613-A	Pipes installation from Sta. 8+053.03 to Sta. 7+950	09/08/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-614-A	Excavation work for AV/AR pre-cast manhole at Sta. 9+928	09/09/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-615-A	Formwork and steel reinforcement work for roof opening neck of GV chamber at Sta. 9+941 to cast concrete	09/09/14	09/09/14	09/10/14	1	A
	IR-13-00013-DST-616-A	Formwork and steel reinforcement work for roof slab of Al Foundqumiya connection chamber (part 1) at Sta. 12+143 to cast concrete	09/09/14	09/09/14	09/10/14	1	A
	IR-13-00013-DST-617-A	Pipe encasement by casting concrete B 150 from Sta. 8+170 to Sta. 8+070.64	09/09/14	09/09/14	09/10/14	1	A
	IR-13-00013-DST-618-A	Pipe encasement by casting concrete B 150 from Sta. 8+053.03 to Sta. 7+950	09/09/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-619-A	Trench excavation from Sta. 7+950 to Sta. 7+850	09/09/14	09/11/14	09/11/14	0	A
	IR-13-00013-DST-620-A	Pipes installation from Sta. 7+950 to Sta. 7+850	09/09/14	09/11/14	09/11/14	0	A
	IR-13-00013-DST-621-A	Installation of pre-cast AV/AR manhole at Sta. 9+928	09/10/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-622-A	Installation of pre-cast AV/AR manhole at Sta. 8+885	09/10/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-623-A	Marking location of Bizzayia connection chamber at Sta. 8+206	09/10/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-624-A	Steel reinforcement for walls of Sabstiya connection chamber (part 1) at Sta. 2+320 to close formwork shuttering	09/10/14	09/10/14	09/10/14	0	A
	IR-13-00013-DST-625-A	12 inch bends fabrication (Starting from Sep. 11,2014 at 8:00 AM)	09/10/14	09/30/14	09/30/14	0	A
	IR-13-00013-DST-626-A	Surface preparation & finishing for external body of AV/AR pre-cast manhole at Sta. 8+885	09/11/14	09/11/14	09/11/14	0	A
	IR-13-00013-DST-627-A	Surface preparation & finishing for external body of AV/AR pre-cast manhole at Sta. 9+928	09/11/14	09/11/14	09/11/14	0	A
	IR-13-00013-DST-628-A	Formwork and steel reinforcement work for walls of Sabstiya connection chamber (part 1) at Sta. 2+320 to cast concrete	09/11/14	09/11/14	09/14/14	3	A
	IR-13-00013-DST-629-A	Trench excavation from Sta. 7+850 to Sta. 7+750	09/11/14	09/11/14	09/11/14	0	A
	IR-13-00013-DST-630-A	Pipes installation from Sta. 7+850 to Sta. 7+750	09/11/14	09/11/14	09/11/14	0	A
	IR-13-00013-DST-631-A	Pipe encasement by casting concrete B 150 from Sta. 7+950 Sta. 7+850	09/11/14	09/11/14	09/11/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-632-A	Excavation work for Bizzariya connection chamber at Sta. 8+206 (Starting from Sep. 11,2014 at 10:30 AM)	09/11/14	09/14/14	09/15/14	1	A
	IR-13-00013-DST-633-A	Pipes installation for AV/AR pre-cast manhole at Sta. 8+885 (Starting from Sep. 11,2014 at 10:30 AM)	09/11/14	09/13/14	09/14/14	1	A
	IR-13-00013-DST-634-A	Pipes installation for AV/AR pre-cast manhole at Sta. 9+928(Starting from Sep. 11,2014 at 10:30 AM)	09/11/14	09/13/14	09/14/14	1	A
	IR-13-00013-DST-635-A	• 24.40 m of 3.96 mm wall thickness of 4''pipe (use for ventilation purpose) • 109.80 m of Sch. 40 wall thickness of 4'' water pipes	09/11/14	09/14/14	09/15/14	1	C
	IR-13-00013-DST-635-B	4 inch galvanized pipe-Sch. 40 for pipe chamber ventilation	10/22/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-636-A	Formwork and steel reinforcement work for foundation of Sabstiya connection chamber(part 2) at Sta. 2+320 to cast concrete	09/11/14	09/13/14	09/14/14	1	A
	IR-13-00013-DST-637-A	Trench excavation from Sta. 7+750 to Sta. 7+670	09/11/14	09/13/14	09/14/14	1	A
	IR-13-00013-DST-638-A	Pipes installation from Sta. 7+750 to Sta. 7+670	09/11/14	09/13/14	09/14/14	1	A
	IR-13-00013-DST-639-A	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A1401745, A1401698 & A1401664), QTY= 988.20 m	09/11/14	09/14/14	09/15/14	0	A
	IR-13-00013-DST-640-A	Cement lining repair for fabricated bends No. (190, 191, 192, 193, 194, 195, 196, 197& 198) Starting from Sep. 13,2014 at 8:00 AM	09/13/14	09/16/14	09/17/14	1	A
	IR-13-00013-DST-641-A	Painting first layer for external body of AV/AR pre-cast manhole at Sta. 8+885 with accepted bitumen material	09/13/14	09/13/14	09/14/14	1	A
	IR-13-00013-DST-642-A	Painting first layer for external body of AV/AR pre-cast manhole at Sta. 9+928 with accepted bitumen material	09/13/14	09/13/14	09/14/14	1	A
	IR-13-00013-DST-643-A	Conduct test pit for W.O manhole at Sta. 10+889	09/14/14	09/14/14	09/15/14	1	A
	IR-13-00013-DST-644-A	Inspection for Bizzariya connection chamber at Sta. 8+206 to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	09/14/14	09/14/14	09/15/14	1	A
	IR-13-00013-DST-645-A	Painting second layer for external body of AV/AR pre-cast manhole at Sta. 8+885 with accepted bitumen material	09/14/14	09/14/14	09/14/14	0	A
	IR-13-00013-DST-646-A	Painting second layer for external body of AV/AR pre-cast manhole at Sta. 9+928 with accepted bitumen material	09/14/14	09/14/14	09/14/14	0	A
	IR-13-00013-DST-647-A	Cement lining repair for bends No. (199,200 &201) Starting from Sep. 14,2014 at 1:30 PM	09/14/14	09/16/14	09/17/14	1	A
	IR-13-00013-DST-648-A	Marking location of AV/AR pre-cast manhole at Sta. 1+389	09/14/14	09/14/14	09/15/14	1	A
	IR-13-00013-DST-649-A	Backfilling around AV/AR pre-cast manhole at Sta. 8+885 with single size aggregate	09/15/14	09/15/14	09/15/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-650-A	Backfilling around AV/AR pre-cast manhole at Sta. 9+928 with single size aggregate	09/15/14	09/15/14	09/15/14	0	A
	IR-13-00013-DST-651-A	Pipe encasement by casting concrete B 150 from Sta. 7+850 to Sta. 7+750	09/15/14	09/15/14	09/15/14	0	A
	IR-13-00013-DST-652-A	Pipe encasement by casting concrete B 150 from Sta. 7+750 to Sta. 7+670	09/15/14	09/15/14	09/15/14	0	A
	IR-13-00013-DST-653-A	Trench excavation from Sta. 7+670 to Sta. 7+500	09/15/14	09/15/14	09/15/14	0	A
	IR-13-00013-DST-654-A	Pipes installation from Sta. 7+670 to Sta. 7+500	09/15/14	09/15/14	09/15/14	0	A
	IR-13-00013-DST-655-A	Pipe encasement by casting concrete B 150 from Sta. 7+670 to Sta. 7+500	09/15/14	09/15/14	09/15/14	0	A
	IR-13-00013-DST-656-A	Trench excavation from Sta. 7+500 to Sta. 7+400	09/15/14	09/16/14	09/16/14	0	A
	IR-13-00013-DST-657-A	Pipes installation from Sta. 7+500 to Sta. 7+400	09/15/14	09/16/14	09/16/14	0	A
	IR-13-00013-DST-658-A	Formwork and steel reinforcement work for roof slab of Al Foundqumiya connection chamber(part 2) at Sta. 12+143 to cast concrete	09/15/14	09/15/14	09/15/14	0	A
	IR-13-00013-DST-659-A	Excavation work for W.O pre-cast manhole at sta. 10+889(Starting from Sep. 15,2014 at 11:30 AM)	09/15/14	09/16/14	09/16/14	0	A
	IR-13-00013-DST-660-A	Excavation work for AV/AR pre-cast manhole at Sta. 1+389	09/15/14	09/15/14	09/16/14	1	A
	IR-13-00013-DST-661-A	Surface preparation for external walls of Al Foundqumiya connection chamber at Sta. 12+143 using FOSROC material (Starting from Sep. 16,2014 at 10:00 AM)	09/16/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-662-A	External formwork and steel reinforcement work for Sabstiya connection chamber(part 2) at Sta. 2+320 to close shutters	09/16/14	09/16/14	09/16/14	0	A
	IR-13-00013-DST-663-A	Trench excavation from Sta. 7+400 to Sta. 7+300	09/16/14	09/17/14	09/17/14	0	A
	IR-13-00013-DST-664-A	Pipes installation from Sta. 7+400 to Sta. 7+300	09/16/14	09/17/14	09/17/14	0	A
	IR-13-00013-DST-665-A	Pipe encasement by casting concrete B 150 from Sta. 7+500 to Sta. 7+400	09/16/14	09/16/14	09/16/14	0	A
	IR-13-00013-DST-666-A	Installation for AV/AR pre-cast manhole at Sta. 1+389	09/17/14	09/17/14	09/17/14	0	A
	IR-13-00013-DST-667-A	Installation for W.O pre-cast manhole at Sta. 10+889	09/17/14	09/17/14	09/17/14	0	A
	IR-13-00013-DST-668-A	Marking location for combined AV/AR & BFV chamber at Sta. 7+400	09/17/14	09/17/14	09/17/14	0	A
	IR-13-00013-DST-669-A	Trench excavation from Sta. 7+300 to Sta. 7+200	09/17/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-670-A	Pipes installation from Sta. 7+300 to Sta. 7+200	09/17/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-671-A	Pipe encasement by casting concrete B150 from Sta. 7+395 to Sta. 7+300	09/17/14	09/17/14	09/17/14	0	A
	IR-13-00013-DST-672-A	Formwork and steel reinforcement work for walls of Sabstiya connection chamber (part 2) at Sta. 2+320 to cast concrete	09/17/14	09/17/14	09/18/14	1	A
	IR-13-00013-DST-673-A	Excavation work for combined AV/AR & BFV chamber at Sta. 7+400 (starting from Sep. 17,2014 at 1:00 PM)	09/17/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-674-A	Pipes installation for AV/AR pre-cast manhole at Sta. 1+389(Starting from Sep. 17,2014 at 2:30 PM)	09/17/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-675-A	Pipes installation for W.O pre-cast manhole at Sta. 10+889(Starting from Sep. 17,2014 at 2:30 PM)	09/17/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-676-A	Formwork and steel reinforcement work for foundation of Bizzariya connection chamber (part 1) at Sta. 8+206 to cast concrete	09/18/14	09/18/14	09/18/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-677-A	Painting the first layer of external body of Al Foundqumiya connection chamber at Sta. 12+143 with accepted bitumen material	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-678-A	Surface preparation using FOSROC material for external walls of W.O pre-cast manhole at Sta. 10+889	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-679-A	Surface preparation using FOSROC material for external walls of AV/AR pre-cast manhole at Sta. 1+389	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-680-A	Painting the first layer for external body of W.O pre-cast manhole at Sta. 10+889 with accepted bitumen material	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-681-A	Painting the first layer for external body of AV/AR pre-cast manhole at Sta. 1+389 with accepted bitumen material	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-682-A	Trench backfilling from Sta. 7+444 to Sta. 7+406 & from Sta. 7+395 to Sta. 7+383	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-683-A	Trench excavation from Sta. 7+200 to Sta. 7+167.5 & from Sta. 7+150 to Sta. 7+100	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-684-A	Pipes installation from Sta. 7+200 to Sta. 7+167.5 & from Sta. 7+150 to Sta. 7+100	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-685-A	Pipe encasement by casting concrete B150 from Sta. 7+300 to Sta. 7+200	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-686-A	Painting the second layer for external body of AV/AR pre-cast manhole at Sta. 1+389 with accepted bitumen material	09/18/14	09/18/14	09/18/14	0	C
	IR-13-00013-DST-686-B	Painting the second layer for external body of AV/AR pre-cast manhole at Sta. 1+389 with accepted bitumen material	09/20/14	09/20/14	09/21/14	1	A
	IR-13-00013-DST-687-A	Painting the second layer for external body of W.O pre-cast manhole at Sta. 10+889 with accepted bitumen material	09/18/14	09/18/14	09/18/14	0	C
	IR-13-00013-DST-687-B	Painting the second layer for external body of W.O pre-cast manhole at Sta. 10+889 with accepted bitumen material	10/01/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-688-A	Painting the second layer for external body of Al Foundqumiya connection chamber at Sta. 12+143 with accepted bitumen material	09/18/14	09/18/14	09/18/14	0	A
	IR-13-00013-DST-689-A	Inspection for combined AV/AR & BFV chamber at Sta. 7+400 to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	09/18/14	09/20/14	09/21/14	1	A
	IR-13-00013-DST-690-A	Backfilling around AV/AR pre-cast manhole at Sta. 1+389 with single size aggregate	09/18/14	09/20/14	09/21/14	1	A
	IR-13-00013-DST-691-A	Backfilling around W.O pre-cast manhole at Sta. 10+889 with single size aggregate	09/18/14	09/20/14	09/21/14	1	C
	IR-13-00013-DST-691-B	Backfilling around W.O pre-cast manhole at Sta. 10+889 with single size aggregate	10/01/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-692-A	Backfilling around Al Foundqumiya connection chamber at Sta. 12+143 with single size aggregate	09/18/14	09/20/14	09/21/14	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-692-B	Backfilling around Al Foundqumiya connection chamber at Sta. 12+143 with single size aggregate	10/01/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-693-A	Trench excavation from Sta. 7+100 to Sta. 6+983	09/18/14	09/20/14	09/21/14	1	A
	IR-13-00013-DST-694-A	Pipes installation from Sta. 7+100 to Sta. 6+983	09/18/14	09/20/14	09/21/14	1	A
	IR-13-00013-DST-695-A	Marking location of flow monitoring chamber at Sta. 7+160	09/20/14	09/20/14	09/21/14	1	A
	IR-13-00013-DST-696-A	Formwork and steel reinforcement work for roof slab of Sabstiya connection chamber (part 1) at Sta. 2+320 to cast concrete	09/21/14	09/21/14	09/21/14	0	A
	IR-13-00013-DST-697-A	Pipe encasement by casting concrete B 150 from Sta. 7+200 to Sta. 7+166 & Sta. 7+149 to Sta. 7+100	09/21/14	09/21/14	09/21/14	0	A
	IR-13-00013-DST-698-A	Pipe encasement by casting concrete B 150 from Sta. 7+100 to Sta. 7+020.95 & Sta. 6+992.82 to Sta. 6+981	09/21/14	09/21/14	09/22/14	1	A
	IR-13-00013-DST-699-A	External formwork and steel reinforcement for walls of Bazzariya connection chamber (part1) at Sta. 8+206 to close shutters	09/21/14	09/21/14	09/21/14	0	A
	IR-13-00013-DST-700-A	Bedding from Sta. 7+020.95 to Sta. 6+992.82	09/21/14	09/21/14	09/21/14	0	A
	IR-13-00013-DST-701-A	Trench backfilling from Sta. 7+020.95 to Sta. 6+992.82	09/21/14	09/21/14	09/21/14	0	A
	IR-13-00013-DST-702-A	Trench excavation from Sta. 3+461.70 to Sta. 3+550	09/21/14	09/22/14	09/22/14	0	A
	IR-13-00013-DST-703-A	Pipe installation from Sta. 3+461.70 to Sta. 3+550	09/21/14	09/22/14	09/22/14	0	A
	IR-13-00013-DST-704-A	6 inch fabrication bends, QTY=11 bends (Starting from Sep. 21,2014 at 12:30 PM)	09/21/14	09/24/14	09/24/14	0	A
	IR-13-00013-DST-705-A	Formwork and steel reinforcement work for walls of Bazzariya connection chamber (part 1) at Sta. 8+206 to cast concrete	09/22/14	09/22/14	09/22/14	0	A
	IR-13-00013-DST-706-A	Inspection for flow monitoring chamber at Sta. 7+160 to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	09/22/14	09/22/14	09/22/14	0	A
	IR-13-00013-DST-707-A	Trench excavation from Sta. 3+550 to Sta. 3+700	09/22/14	09/23/14	09/23/14	0	A
	IR-13-00013-DST-708-A	Pipes installation from Sta. 3+550 to Sta. 3+700	09/22/14	09/23/14	09/23/14	0	A
	IR-13-00013-DST-709-A	Pipe encasement by casting concrete B 150 from Sta. 3+461.70 to Sta. 3+550	09/22/14	09/22/14	09/22/14	0	A
	IR-13-00013-DST-710-A	Base course preparation (leveling & compacting) to install steel reinforcement from Sta. 9+600 to Sta. 9+030	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00013-DST-711-A	Trench excavation from Sta. 3+700 to Sta. 3+800	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00013-DST-712-A	Pipes installation from Sta. 3+700 to Sta. 3+800	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00013-DST-713-A	Pipe encasement by casting concrete B 150 from Sta. 3+550 to Sta. 3+700	09/23/14	09/23/14	09/24/14	1	A
	IR-13-00013-DST-714-A	Mock up for rung steps of GV chamber at Sta. 10+460	09/23/14	09/24/14	09/25/14	1	C
	IR-13-00013-DST-715-A	Formwork and steel reinforcement work for foundation of Bazzariya connection chamber (part 2) at Sta. 8+206 to cast concrete	09/23/14	09/23/14	09/24/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-716-A	Location of air vent for W.O chamber at Sta. 10+889	09/23/14	09/24/14	09/25/14	1	A
	IR-13-00013-DST-717-A	Steel reinforcement work for drainage ditch from Sta. 9+600 to Sta. 9+030 to cast concrete (Starting from Sep. 24,2014 at 11:00AM)	09/24/14	09/25/14	09/25/14	0	A
	IR-13-00013-DST-718-A	Trench excavation from Sta. 3+800 to Sta. 3+900	09/24/14	09/24/14	09/25/14	1	A
	IR-13-00013-DST-719-A	Pipes installation from Sta. 3+800 to Sta. 3+900	09/24/14	09/24/14	09/25/14	1	A
	IR-13-00013-DST-720-A	Pipe encasement by casting concrete B 150 from Sta. 3+700 to Sta. 3+800	09/24/14	09/24/14	09/24/14	0	A
	IR-13-00013-DST-721-A	Base course preparation for drainage ditch from Sta. 8+850 to Sta. 8+500	09/24/14	09/24/14	09/25/14	1	A
	IR-13-00013-DST-722-A	Steel reinforcement for walls of Bazzariya connection chamber (part 2) at Sta. 8+206	09/25/14	09/25/14	09/25/14	0	A
	IR-13-00013-DST-723-A	Formwork and steel reinforcement for foundation of combined AV/AR & BFV at Sta. 7+400 to cast concrete	09/25/14	09/25/14	09/25/14	0	A
	IR-13-00013-DST-724-A	Trench excavation from Sta. 1+224.19 to Sta. 1+140	09/25/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-725-A	Pipes installation from Sta. 1+224.19 to Sta. 1+140	09/25/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-726-A	Formwork and steel reinforcement for drainage ditch from Sta. 8+850 to Sta. 8+500 to cast concrete (Starting from Sep. 27,2014 at 8:00 AM)	09/25/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-727-A	Formwork and steel reinforcement for walls of Bazzariya connection chamber(part 2) at Sta. 8+206 to cast concrete	09/25/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-728-A	Marking location for Burqa connection chamber at Sta. 7+032 to start excavation	09/25/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-729-A	Trench excavation from Sta. 3+900 to Sta. 3+916.77	09/27/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-730-A	Pipe installation from Sta. 3+900 to Sta. 3+916.77	09/27/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-731-A	Pipe encasement by casting concrete B 150 from Sta. 3+800 to Sta. 3+898.89	09/27/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-732-A	Bedding from Sta. 3+898.89 to Sta. 3+916.77	09/27/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-733-A	Trench backfilling from Sta. 3+898.89 to Sta. 3+916.77	09/27/14	09/27/14	09/28/14	1	A
	IR-13-00013-DST-734-A	Base course preparation for drainage ditch from Sta. 8+500 to Sta. 8+215	09/28/14	09/28/14	09/28/14	0	A
	IR-13-00013-DST-735-A	Steel reinforcement for drainage ditch from Sta. 8+500 to Sta. 8+215 to cast concrete (Starting from Sep. 28,2014 at 11:00 AM	09/28/14	09/29/14	09/29/14	0	A
	IR-13-00013-DST-736-A	Formwork and steel reinforcement work for roof slab of Sabstiya connection chamber(part 2) at Sta. 2+320 to cast concrete	09/28/14	09/28/14	09/29/14	1	A
	IR-13-00013-DST-737-A	Base course preparation for drainage ditch from Sta. 8+050 to Sta. 7+400	09/29/14	09/29/14	09/29/14	0	A
	IR-13-00013-DST-738-A	Formwork and steel reinforcement for drainage ditch from Sta. 8+050 to Sta. 7+850 to cast concrete(starting from Sep. 29,2014 at 01:00 PM)	09/29/14	09/30/14	09/30/14	0	A
	IR-13-00013-DST-739-A	Pipes installation to connect main pipeline with Al Foundqumiya connection chamber at Sta. 12+143 (Starting from Sep. 29,2014 at 11:30 AM)	09/29/14	09/30/14	10/01/14	1	A
	IR-13-00013-DST-740-A	Marking location of W.O chamber at Sta. 7+440 to start excavation	09/29/14	09/29/14	09/30/14	1	A
	IR-13-00013-DST-741-A	Formwork and steel reinforcment for walls of combined AV/AR & BFV at Sta. 7+400 to close shutters	09/29/14	09/30/14	09/30/14	0	A
	IR-13-00013-DST-742-A	Bedding form Sta. 1+224.19 to Sta. 1+140	09/30/14	09/30/14	10/01/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-743-A	Trench backfilling form Sta. 1+224.19 to Sta. 1+140	09/30/14	09/30/14	10/01/14	1	A
	IR-13-00013-DST-744-A	Trench excavation form Sta. 1+140 to Sta. 1+040	09/30/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-745-A	Pipes installation form Sta. 1+140 to Sta. 1+040	09/30/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-746-A	Formwork and steel reinforcement for drainage ditch from Sta. 7+850 to Sta. 7+750 to cast concrete	09/30/14	09/30/14	10/01/14	1	A
	IR-13-00013-DST-747-A	Formwork and steel reinforcement work for walls of combined AV/AR & BFV chamber at Sta. 7+400 to cast concrete	09/30/14	09/30/14	10/01/14	1	A
	IR-13-00013-DST-748-A	Formwork and steel reinforcement work for drainage ditch from Sta. 7+750 to Sta. 7+450 to cast concrete (Strating from Oct. 01,2014 at 9:30 AM)	10/01/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-749-A	Trench excavationfrom Sta. 1+040 to Sta. 0+960	10/01/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-750-A	Pipes installation from Sta. 1+040 to Sta. 0+960	10/01/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-751-A	Bedding from Sta. 1+140 to Sta. 1+045	10/01/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-752-A	Trench backfilling from Sta. 1+140 to Sta. 1+045	10/01/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-753-A	Marking location for pre-cast W.O manhole at Sta. 3+924 to start excavation	10/01/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-754-A	Installation for pre-cast W.O manhole at Sta. 7+440	10/01/14	10/01/14	10/02/14	1	A
	IR-13-00013-DST-755-A	Installation for pre-cast W.O manhole at Sta. 3+924	10/01/14	10/01/14	10/02/14	1	A
	IR-13-00013-DST-756-A	Pipe installation to connect main pipeline with pre-cast W.O manhole at Sta. 7+440 (Starting from Oct. 01,2014 at 12:00 PM)	10/01/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-757-A	Pipe installation to connect main pipeline with pre-cast W.O manhole at Sta. 3+924 (Starting from Oct. 01,2014 at 12:00 PM)	10/01/14	10/02/14	10/02/14	0	C
	IR-13-00013-DST-757-B	Pipe installation to connect main pipeline with pre-cast W.O manhole at Sta. 3+924	10/11/14	10/11/14	10/12/14	1	A
	IR-13-00013-DST-758-A	Surface preparation for external body of pre-cast W.O manhole at Sta. 7+440 using accepted FOSROC material(Starting from Oct. 01,2014 at 10:00 AM)	10/01/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-759-A	Formwork and steel reinforcement work for foundation of flow monitoring chamber at Sta. 7+160 to cast concrete	10/01/14	10/01/14	10/01/14	0	A
	IR-13-00013-DST-760-A	Trench excavation from Sta. 0+960 to Sta. 0+860	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-761-A	Pipes installation from Sta. 0+960 to Sta. 0+860	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-762-A	Bedding from Sta. 1+045 to Sta. 1+032	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-763-A	Trench backfilling from Sta. 1+045 to Sta. 1+032	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-764-A	Pipe encasement by casting concrete B 150 from Sta. 1+032 to Sta. 0+960	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-765-A	Trench excavation from Sta. 0+860 to 0+780	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-766-A	Pipes installation from Sta. 0+860 to 0+780	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-767-A	Formwork and steel reinforcement work for roof slab of Bazzariya connection chamber (part 1) at Sat. 8+206 to cast concrete	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-768-A	Formwork and steel reinforcement work for roof slab of Bazzariya connection chamber (part 2) at Sat. 8+206 to cast concrete	10/02/14	10/02/14	10/02/14	0	A
	IR-13-00013-DST-769-A	Trench excavation from Sta. 0+780 to Sta. 0+700	10/02/14	10/11/14	10/12/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-770-A	Pipes installation from Sta. 0+780 to Sta. 0+700	10/02/14	10/11/14	10/12/14	1	A
	IR-13-00013-DST-771-A	External formwork and steel reinforcement for walls of flow monitoring chamber at sta. 7+160 to close shutters	10/12/14	10/12/14	10/12/14	0	A
	IR-13-00013-DST-772-A	Pipe encasement by casting concrete B 150 from Sta. 0+960 to Sta. 0+860	10/12/14	10/12/14	10/12/14	0	A
	IR-13-00013-DST-773-A	Pipe encasement by casting concrete B 150 from Sta. 0+860 to Sta. 0+780	10/12/14	10/12/14	10/12/14	0	A
	IR-13-00013-DST-774-A	Pipe encasement by casting concrete B 150 from Sta. 0+780 to Sta. 0+700	10/12/14	10/12/14	10/12/14	0	A
	IR-13-00013-DST-775-A	Trench excavation from Sta. 0+700 to Sta. 0+600	10/12/14	10/13/14	10/13/14	0	A
	IR-13-00013-DST-776-A	Pipes installation from Sta. 0+700 to Sta. 0+600	10/12/14	10/13/14	10/13/14	0	A
	IR-13-00013-DST-777-A	Base course preparation for drainage ditch from Sta. 7+365 to Sta. 7+180 to install steel reinforcement	10/12/14	10/12/14	10/13/14	1	A
	IR-13-00013-DST-778-A	Concrete casting for drainage ditch from Sta. 7+365 to Sta. 7+180 (Starting from Oct. 13,2014 at 9:00 AM)	10/13/14	10/14/14	10/14/14	0	A
	IR-13-00013-DST-779-A	Surface preparation for external walls of Bazzariya connection chamber at Sta. 8+206 using accepted FOSROC material	10/13/14	10/13/14	10/14/14	1	A
	IR-13-00013-DST-780-A	Trench excavation from Sta. 0+600 to Sta. 0+500	10/13/14	10/13/14	10/14/14	1	A
	IR-13-00013-DST-781-A	Pipes installation from Sta. 0+600 to Sta. 0+500	10/13/14	10/13/14	10/14/14	1	A
	IR-13-00013-DST-782-A	Pipe encasement by casting concrete B 150 from Sta. 0+700 to Sta. 0+600	10/13/14	10/13/14	10/13/14	0	A
	IR-13-00013-DST-783-A	Welding repair for fabricated bend No. 116	10/13/14	10/13/14	10/14/14	1	A
	IR-13-00013-DST-784-A	Formwork and steel reinforcement work for roof slab of combined AV/AR & BFV chamber at Sta. 7+400 to cast concrete	10/13/14	10/14/14	10/14/14	0	A
	IR-13-00013-DST-785-A	Formwork and steel reinforcement work for walls of flow monitoring chamber at Sta. 7+160 to cast concrete	10/13/14	10/14/14	10/14/14	0	A
	IR-13-00013-DST-786-A	Excavation to cast blind layer for Burqa connection chamber at Sta. 7+032	10/13/14	10/14/14	10/14/14	0	A
	IR-13-00013-DST-787-A	Trench excavation from Sta. 0+500 to Sta. 0+400	10/13/14	10/14/14	10/15/14	1	A
	IR-13-00013-DST-788-A	Pipe installation from Sta. 0+500 to Sta. 0+400	10/13/14	10/14/14	10/15/14	1	A
	IR-13-00013-DST-789-A	Trench excavation from Sta. 0+400 to Sta. 0+300	10/15/14	10/15/14	10/15/14	0	A
	IR-13-00013-DST-790-A	Pipes installation from Sta. 0+400 to Sta. 0+300	10/15/14	10/15/14	10/15/14	0	A
	IR-13-00013-DST-791-A	Pipe encasement by casting concrete B 150 from Sta. 0+600 to Sta. 0+500	10/15/14	10/15/14	10/15/14	0	A
	IR-13-00013-DST-792-A	Pipe encasement by casting concrete B 150 from Sta. 0+500 to Sta. 0+400	10/15/14	10/15/14	10/15/14	0	A
	IR-13-00013-DST-793-A	Trench excavation from Sta. 0+300 to Sta. 0+200	10/15/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-794-A	Pipes installation from Sta. 0+300 to Sta. 0+200	10/15/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-795-A	Pipe installation to connect main pipeline with Al Asa'sa connection chamber at Sta. 13+608	10/15/14	10/15/14	10/15/14	0	A
	IR-13-00013-DST-796-A	.Pipe encasement by casting concrete B 150 from Sta. 0+400 to Sta. 0+300	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-797-A	Surface preparation for external body of pre-cast W.O manhole at Sta. 7+440 using accepted FOSROC material	10/16/14	10/16/14	10/16/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-798-A	Painting first layer for external body of pre-cast W.O manhole at Sta. 7+440 using accepted bitumen material	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-799-A	Painting first layer for external body of Bazzariya connection chamber at Sta. 8+206 using accepted bitumen material	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-800-A	Marking for milling and asphalt reinstatement from Sta. 9+700 to Sta. 11+200	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-801-A	Milling for asphalt layer from Sta. 9+700 to Sta. 10+700 (Starting from Oct. 18,2014 at 8:00 AM)	10/16/14	10/19/14	10/20/14	1	C
	IR-13-00013-DST-801-B	Milling for asphalt layer from Sta. 9+700 to Sta. 10+700	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00013-DST-802-A	Formwork and steel reinforcement for foundation of Burqa (part 1) at Sta. 7+032 to cast concrete	10/16/14	10/18/14	10/19/14	1	A
	IR-13-00013-DST-803-A	Trench excavation from Sta. 0+200 to Sta. 0+100	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-804-A	Pipes installation from Sta. 0+200 to Sta. 0+100	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-805-A	Pipe encasement by casting concrete B 150 from Sta. 0+300 to Sta. 0+200	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-806-A	Conduct connection for GV chamber at Sta. 10+461 to connect with main pipeline (Starting from Oct. 16,2014 at 8:00 AM)	10/16/14	10/18/14	10/19/14	1	A
	IR-13-00013-DST-807-A	Trench excavation from Sta. 0+000 to Sta. 0+100 (Segment. C)	10/16/14	10/19/14	10/20/14	1	A
	IR-13-00013-DST-808-A	Pipes installation from Sta. 0+000 to Sta. 0+100 (Segment. C)	10/16/14	10/19/14	10/20/14	1	A
	IR-13-00013-DST-809-A	Painting second layer for external body of pre-cast W.O manhole at Sta. 7+440 using accepted bitumen material	10/16/14	10/16/14	10/16/14	0	A
	IR-13-00013-DST-810-A	Painting second layer for external body of Bazzariya connection chamber at sta. 8+206 with accepted bitumen material	10/18/14	10/18/14	10/19/14	1	A
	IR-13-00013-DST-811-A	Backfilling with single size around Bazzariya connection chamber at Sta. 8+206	10/18/14	10/18/14	10/19/14	1	A
	IR-13-00013-DST-812-A	Marking alignment for segment C from Sta. 0+000 to 0+130	10/20/14	10/20/14	10/20/14	0	A
	IR-13-00013-DST-813-A	External formwork and steel reinforcement work for walls of Burqa connection chamber (part 1) at Sta. 7+032 to close shutters	10/20/14	10/20/14	10/20/14	0	A
	IR-13-00013-DST-814-A	Marking for milling and asphalt reinstatement from Sta. 11+200 to Sta. 11+700	10/20/14	10/20/14	10/20/14	0	A
	IR-13-00013-DST-815-A	Marking location for flow control valve chamber at Sta. 1+174 to start excavation	10/20/14	10/20/14	10/21/14	1	A
	IR-13-00013-DST-816-A	Marking alignment for segment B from Sta. 0+999 to Sta. 0+899	10/20/14	10/21/14	10/22/14	1	A
	IR-13-00013-DST-817-A	Formwork and steel reinforcement work for walls of Burqa connection chamber(part 1) at Sta. 7+032 to cast concrete	10/21/14	10/21/14	10/22/14	1	A
	IR-13-00013-DST-818-A	Formwork and steel reinforcement work for foundation of Burqa connection chamber(part 2) at Sta. 7+032 to cast concrete	10/21/14	10/21/14	10/22/14	1	A
	IR-13-00013-DST-819-A	Marking location for pre-cast AV/AR chamber at Sta. 1+107 to start excavation	10/21/14	10/21/14	10/22/14	1	A
	IR-13-00013-DST-820-A	Marking location for butterfly valve chamber at Sta. 1+167 to start excavation	10/21/14	10/21/14	10/22/14	1	A
	IR-13-00013-DST-821-A	Marking location for combined AV/AR & BFV chamber at Sta. 1+162 to start excavation	10/21/14	10/21/14	10/22/14	1	A
	IR-13-00013-DST-822-A	Marking for milling and asphalt reinstatement from Sta. 11+700 to Sta. 13+725	10/21/14	10/21/14	10/22/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-823-A	12 inch steel pipes /Grade B ASTM A53 ERW welded steel pipes- Toscelik/Middle East Tube Company Ltd. product.(Delivery No. A1401958, QTY=122 m , A1401959 ,QTY=170.8 m & A1401962,QTY=329.4 m)	10/21/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-824-A	Backfilling with single size aggregate around pre-cast W.O manhole at Sta. 7+440	10/22/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-825-A	Trench excavation for segment C from Sta. 0+100 to Sta. 0+126	10/22/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-826-A	6 " Pipe installation for segment C from Sta. 0+100 to Sta. 0+126	10/22/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-827-A	Bedding for segment C from Sta. 0+126.00 to Sta. 0+111.80	10/22/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-828-A	Pipe encasement for segment C from Sta. 0+111.80 to Sta. 0+000.00	10/22/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-829-A	Trench backfilling for segment C from Sta. 0+126 to Sta. 0+000	10/22/14	10/22/14	10/22/14	0	A
	IR-13-00013-DST-830-A	Inspection for safety measures around backfilling material stock piles on site	10/23/14	10/26/14	10/26/14	0	A
	IR-13-00013-DST-831-A	Inspection for chevrons installation at manholes	10/23/14	10/26/14	10/26/14	0	A
	IR-13-00013-DST-832-A	Formwork and steel reinforcement work for roof slab of flow monitoring chamber at Sa. 7+160 to cast concrete	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-833-A	External formwork and steel reinforcement work for walls of Burqa connection chamber(part 2) at Sta. 7+032 to close shutters	10/23/14	10/23/14	10/23/14	0	A
	IR-13-00013-DST-834-A	Inspection for delivered strainers type DOFUS VANADOKUM DIS TICARET LTD STI : DV50,DN80,DN100,DN150,DN250 & DN300	10/23/14	10/26/14	10/26/14	0	C
	IR-13-00013-DST-835-A	Trench excavation for segment B from Sta. 1+000 to Sta. 0+950 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-836-A	Pipe installation for segment B from Sta. 1+000 to Sta. 0+950 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-837-A	Pipe encasement for segment B from Sta. 1+000 to Sta. 0+950 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-838-A	Trench backfilling for segment B from Sta. 1+000 to Sta. 0+950 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-839-A	Trench excavation for segment B from Sta. 0+950 to Sta. 0+870 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-840-A	Pipe installation for segment B from Sta. 0+950 to Sta. 0+870 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-841-A	Pipe encasement for segment B from Sta. 0+950 to Sta. 0+870 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-842-A	Trench backfilling for segment B from Sta. 0+950 to Sta. 0+870 (double trench)	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-843-A	Formwork and steel reinforcement work for walls of Burqa connection chamber (part 2) at Sta. 7+032 to cast concrete	10/23/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-844-A	Milling for asphalt layer from Sta. 10+700 to Sta. 12+500 (Starting from Oct. 25,2014 at 8:00 AM)	10/23/14	10/25/14	10/26/14	1	C
	IR-13-00013-DST-844-B	Milling for asphalt layer from Sta. 10+700 to Sta. 12+500	11/10/14	11/10/14	11/10/14	0	A
	IR-13-00013-DST-845-A	Surface preparation for external body of combined AV/AR & BFV chamber at Sta. 7+400 using FOSROC material	10/23/14	10/23/14	10/23/14	0	A
	IR-13-00013-DST-846-A	Marking alignment for segment B from Sta. 0+899 to Sta. 0+640	10/25/14	10/25/14	10/26/14	1	A
	IR-13-00013-DST-847-A	Surface preparation for external body of Sabstiya connection chamber at Sta. 2+320 using FOSROC material	10/26/14	10/26/14	10/27/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-848-A	Formwork and steel reinforcement for opening necks of the following chambers to cast concrete : • GV chamber at Sta. 10+461 • AV/AR chamber at Sta. 9+924 • WO chamber at Sta. 10+891	10/26/14	10/26/14	10/27/14	1	A
	IR-13-00013-DST-849-A	Formwork and steel reinforcement for opening necks of Bazzariya connection chamber at Sta. 8+206 to cast concrete	10/27/14	10/27/14	10/27/14	0	A
	IR-13-00013-DST-850-A	Trench excavation for segment B from Sta. 0+870 to Sta. 0+830 (double trench)	10/27/14	10/28/14	10/28/14	0	A
	IR-13-00013-DST-851-A	6" pipes installation for segment B from Sta. 0+870 to Sta. 0+830 (double trench)	10/27/14	10/28/14	10/28/14	0	A
	IR-13-00013-DST-852-A	Pipe encasement for segment B from Sta. 0+870 to Sta. 0+848.55 (double trench)	10/27/14	10/28/14	10/28/14	0	A
	IR-13-00013-DST-853-A	Trench backfilling for segment B from Sta. 0+870 to Sta. 0+830 (double trench)	10/27/14	10/28/14	10/28/14	0	A
	IR-13-00013-DST-854-A	Air ventilation installation for AV/AR manhole at Sta. 9+928 & GV manhole at Sta. 9+941	10/27/14	10/27/14	10/27/14	0	A
	IR-13-00013-DST-855-A	Formwork and steel reinforcement for opening neck of combined AV/AR & BFV at Sta. 7+400 to cast concrete	10/27/14	10/27/14	10/28/14	1	A
	IR-13-00013-DST-856-A	Painting first layer for external body of combined AV/AR & BFV chamber at Sta. 7+400 with accepted bitumen material	10/27/14	10/27/14	10/28/14	1	A
	IR-13-00013-DST-857-A	Painting second layer for external body of combined AV/AR & BFV chamber at Sta. 7+400 with accepted bitumen material	10/28/14	10/28/14	10/28/14	0	A
	IR-13-00013-DST-858-A	Air ventilation pipe installation for W.O manhole at Sta. 10+889 & GV manhole at Sta. 10+461	10/28/14	10/28/14	10/28/14	0	A
	IR-13-00013-DST-859-A	Formwork and steel reinforcement for roof slab of Burqa connection chamber at Sta. 7+032 (part 1 & 2) to cast concrete	10/28/14	10/28/14	10/29/14	1	A
	IR-13-00013-DST-860-A	Backfilling around combined AV/AR & BFV chamber at Sta. 7+400 with accepted milled asphalt material	10/29/14	10/29/14	10/29/14	0	A
	IR-13-00013-DST-861-A	Bedding from Sta. 0+848.55 to Sta. 0+825.45	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00013-DST-862-A	Trench excavation for segment B from Sta. 0+830 to Sta. 0+800 (double trench)	10/29/14	10/30/14	10/30/14	0	A
	IR-13-00013-DST-863-A	6 " pipes installation for segment B from Sta. 0+830 to Sta. 0+800 (double trench)	10/29/14	10/30/14	10/30/14	0	A
	IR-13-00013-DST-864-A	Painting first layer for external body of Sabastiya connection chamber(part 1&2) at sta. 2+320 with accepted bitumen material	10/29/14	10/29/14	10/29/14	0	A
	IR-13-00013-DST-865-A	Surface preparation for external body of flow monitoring chamber at Sta. 7+160 using accepted FOSROC material	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00013-DST-866-A	Milling for asphalt layer from Sta. 12+500 to Sta. 13+480	10/29/14	10/29/14	10/29/14	0	A
	IR-13-00013-DST-867-A	Compacted base course layer to reinstate asphalt trench from Sta. 9+010 to Sta. 8+855 ,Sta. 9+570 to Sta. 9+690,Sta. 9+910 to sta. 9+950 & Sta. 13+480 to Sta. 13+700	10/29/14	10/29/14	10/29/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-868-A	Inspection to spread prime coat on finished base course layer from Sta. 9+010 to Sta. 8+855 ,Sta. 9+570 to Sta. 9+690,Sta. 9+910 to sta. 9+950 & Sta. 13+480 to Sta. 13+700	10/29/14	10/29/14	10/30/14	1	A
	IR-13-00013-DST-869-A	Conduct cement lining repair for 6 inch fabricated bends(Starting from Oct. 30,2014 at 9:30 AM)	10/30/14	11/02/14	11/03/14	1	A
	IR-13-00013-DST-870-A	Painting second layer for external body of Sabstiya connection chamber at sta. 2+320 with accepted bitumen material	10/30/14	10/30/14	10/30/14	0	A
	IR-13-00013-DST-871-A	Pipe encasement for segment B from Sta. 0+825.45 to Sta. 0+800 (double trench)	10/30/14	10/30/14	10/30/14	0	A
	IR-13-00013-DST-872-A	Trench backfilling for segment B from Sta. 0+830 to Sta. 0+800 (double trench)	10/30/14	10/30/14	10/30/14	0	A
	IR-13-00013-DST-873-A	Inspection to asphalt reinstatement from Sta. 9+010 to Sta. 8+855 ,Sta. 9+570 to Sta. 9+690,Sta. 9+910 to sta. 9+950 & Sta. 13+480 to Sta. 13+700	10/30/14	10/30/14	10/30/14	0	A
	IR-13-00013-DST-874-A	Trench excavation for segment B from Sta. 0+800 to Sta. 0+740 (double trench)	10/30/14	11/01/14	11/02/14	1	A
	IR-13-00013-DST-875-A	6” pipes installation for segment B from Sta. 0+800 to Sta. 0+740 (double trench)	10/30/14	11/01/14	11/02/14	1	A
	IR-13-00013-DST-876-A	Pipe encasement for segment B from Sta. 0+800 to Sta. 0+740 (double trench)	10/30/14	11/01/14	11/02/14	1	A
	IR-13-00013-DST-877-A	Trench backfilling for segment B from Sta. 0+800 to Sta. 0+740 (double trench)	10/30/14	11/01/14	11/02/14	1	A
	IR-13-00013-DST-878-A	Finishing work for internal body of the followings chamber : • BFV chamber at Sta. 13+700 • GV chamber at Sta. 13+617 • WO chamber at Sta. 13+628 • Al Asa’sa connection chamber at Sta. 13+608 (Starting from Nov. 01,2014 at 8:00 AM)	10/30/14	11/10/14	11/11/14	1	C
	IR-13-00013-DST-878-B	Finishing work for internal body (base slab, walls & ceiling) of BFV chamber at Sta. 13+700	11/30/14	11/30/14	12/01/14	1	C
	IR-13-00013-DST-878-C	Finishing work for internal body (base slab, walls & ceiling) of BFV chamber at Sta. 13+700	02/16/15	02/16/15	02/17/15	1	A
	IR-13-00013-DST-879-A	Hubbed slip on flanges	11/02/14	11/02/14	11/03/14	1	A
	IR-13-00013-DST-880-A	Painting first layer for external body of flow monitoring chamber at Sta. 7+160 with accepted bitumen material	11/02/14	11/02/14	11/02/14	0	A
	IR-13-00013-DST-881-A	Base course preparation for drainage ditch from Sta. 0+520 to Sta.1+032	11/02/14	11/02/14	11/02/14	0	A
	IR-13-00013-DST-882-A	Painting second layer for external body of flow monitoring chamber at Sta. 7+160 with accepted bitumen material	11/02/14	11/02/14	11/02/14	0	A
	IR-13-00013-DST-883-A	Trench excavation for segment B from Sta. 0+740 to Sta. 0+716 (double trench)	11/03/14	11/03/14	11/03/14	0	A
	IR-13-00013-DST-884-A	6” pipes installation for segment B from Sta. 0+740 to Sta. 0+716 (double trench)	11/03/14	11/03/14	11/03/14	0	A
	IR-13-00013-DST-885-A	Pipe encasement for segment B from Sta. 0+740 to Sta. 0+716 (double trench)	11/03/14	11/03/14	11/03/14	0	A
	IR-13-00013-DST-886-A	Trench backfilling for segment B from Sta. 0+740 to Sta. 0+716 (double trench)	11/03/14	11/03/14	11/03/14	0	A
	IR-13-00013-DST-887-A	Inspection for welding flanges on manholes pipes spools(8,6,4,3&2inch)(Starting from Nov. 03,2014)	11/03/14	11/06/14	11/06/14	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-887-B	Inspection for welding flanges on manholes pipes spools(8,6,4,3&2inch)	02/15/15	02/15/15	02/16/15	1	A
	IR-13-00013-DST-888-A	Formwork and steel reinforcement for drainage ditch from Sta. 0+520 to Sta. 1+032	11/04/14	11/05/14	11/05/14	0	A
	IR-13-00013-DST-889-A	Trench excavation for segment B from Sta. 0+716 to Sta. 0+680 (double trench)	11/04/14	11/05/14	11/05/14	0	A
	IR-13-00013-DST-890-A	Pipes installation for segment B from Sta. 0+716 to Sta. 0+680 (double trench)	11/04/14	11/05/14	11/05/14	0	A
	IR-13-00013-DST-891-A	Air ventilation pipe installation for AV/AR chamber at Sta. 12+514	11/05/14	11/05/14	11/05/14	0	A
	IR-13-00013-DST-892-A	Trench excavation for segment B from Sta. 0+680 to Sta. 0+650(double trench)	11/05/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-893-A	Pipes installation for segment B from Sta. 0+680 to Sta. 0+650(double trench)	11/05/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-894-A	Concrete casting for drainage ditch from Sta. 0+520 to Sta. 1+032(Starting from Nov. 05,2014 at 1:00 PM)	11/05/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-895-A	Pipe encasement from Sta. 0+200 to Sta. 0+148	11/05/14	11/05/14	11/06/14	1	A
	IR-13-00013-DST-896-A	Bedding and backfilling from Sta. 0+148 to Sta. 0+100	11/05/14	11/05/14	11/06/14	1	A
	IR-13-00013-DST-897-A	Trench excavation from Sta. 0+100 to Sta. 0+019.5	11/05/14	11/05/14	11/06/14	1	A
	IR-13-00013-DST-898-A	12'' pipes installation from Sta. 0+100 to Sta. 0+019.5	11/05/14	11/05/14	11/06/14	1	A
	IR-13-00013-DST-899-A	Bedding and backfilling from Sta. 0+100 to Sta. 0+019.5	11/05/14	11/05/14	11/06/14	1	A
	IR-13-00013-DST-900-A	Pipe encasement for segment B from Sta. 0+716 to Sta. 0+680	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-901-A	Trench backfilling for segment B from Sta. 0+716 to Sta. 0+680	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-902-A	Pipe encasement for segment B from Sta. 0+680 to Sta. 0+678	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-903-A	Bedding for segment B from Sta. 0+678 to Sta. 0+650	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-904-A	Trench backfilling for segment B from Sta. 0+680 to Sta. 0+650	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-905-A	Trench excavation for segment B from Sta. 0+650 to Sta. 0+620 (double trench)	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-906-A	6" pipes installation for segment B from Sta. 0+650 to Sta. 0+620 (double trench)	11/06/14	11/06/14	11/06/14	0	A
	IR-13-00013-DST-907-A	Milling for asphalt layer from Sta. 10+700 to Sta. 13+480(Starting from Nov. 08,2014 at 8:00 AM)	11/06/14	11/08/14	11/09/14	1	A
	IR-13-00013-DST-908-A	Trench excavation for segment B from Sta. 0+620 to Sta. 0+590 (double trench)	11/06/14	11/08/14	11/09/14	1	A
	IR-13-00013-DST-909-A	6" pipes installation for segment B from Sta. 0+620 to Sta. 0+590 (double trench)	11/06/14	11/08/14	11/09/14	1	A
	IR-13-00013-DST-910-A	External surface preparation for Burqa connection chamber at Sta. 7+032 using FOSROC material(Stating from Nov. 08,2014)	11/06/14	11/09/14	11/10/14	1	C
	IR-13-00013-DST-910-B	External surface preparation for Burqa connection chamber at Sta. 7+032 using FOSROC material	01/26/15	01/26/15	01/26/15	0	A
	IR-13-00013-DST-911-A	Conduct core test for first layer of asphalt trench reinstatement from Sta. 9+010 to Sta. 8+855 ,Sta. 9+570 to Sta. 9+690,Sta. 9+910 to sta. 9+950 & Sta. 13+480 to Sta. 13+700	11/06/14	11/08/14	11/09/14	1	A
	IR-13-00013-DST-912-A	Bedding for segment B from Sta. 0+650 to Sta. 0+620(double trench)	11/09/14	11/09/14	11/10/14	1	A
	IR-13-00013-DST-913-A	Trench backfilling for segment B from Sta. 0+650 to Sta. 0+620(double trench)	11/09/14	11/09/14	11/10/14	1	A
	IR-13-00013-DST-914-A	Bedding for segment B from Sta. 0+620 to Sta. 0+580.5(double trench)	11/09/14	11/09/14	11/10/14	1	A
	IR-13-00013-DST-915-A	Trench backfilling for segment B from Sta. 0+620 to Sta. 0+580.5(double trench)	11/09/14	11/09/14	11/10/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-916-A	Trench excavation for segment B from Sta. 0+590 to Sta. 0+500(double trench)	11/09/14	11/10/14	11/10/14	0	A
	IR-13-00013-DST-917-A	6" pipes installation for segment B from Sta. 0+590 to Sta. 0+500(double trench)	11/09/14	11/10/14	11/10/14	0	A
	IR-13-00013-DST-918-A	Spreading tack coat on asphalt layer from Sta. 13+700 to Sta. 12+500	11/09/14	11/09/14	11/10/14	1	A
	IR-13-00013-DST-919-A	Asphalt reinstatement for wearing course layer (pipeline trench second layer & wearing course layer)Sta. 13+700 to Sta. 12+500 (Starting from Nov. 09,2014 at 10:00 AM)	11/09/14	11/10/14	11/10/14	0	A
	IR-13-00013-DST-920-A	Pipe encasement for segment B from Sta. 0+580.5 to Sta. 0+500(double trench)	11/09/14	11/10/14	11/10/14	0	A
	IR-13-00013-DST-921-A	Trench backfilling for segment B from Sta. 0+580.5 to Sta. 0+500(double trench)	11/10/14	11/10/14	11/10/14	0	A
	IR-13-00013-DST-922-A	Spreading tack coat on asphalt layer from Sta. 12+500 to Sta. 11+300	11/10/14	11/10/14	11/10/14	0	A
	IR-13-00013-DST-923-A	Asphalt reinstatement for wearing course layer (pipeline trench second layer & wearing course layer) from Sta. 12+500 to Sta. 11+300 (Starting from Nov. 10,2014 at 10:30 AM)	11/10/14	11/11/14	11/11/14	0	A
	IR-13-00013-DST-924-A	Trench excavation for segment B from Sta. 0+500 to Sta. 0+450(double trench)	11/10/14	11/11/14	11/12/14	1	A
	IR-13-00013-DST-925-A	6" pipes installation for segment B from Sta. 0+500 to Sta. 0+450(double trench)	11/10/14	11/11/14	11/12/14	1	A
	IR-13-00013-DST-926-A	Pipe encasement for segment B from Sta. 0+500 to Sta. 0+457(double trench)	11/10/14	11/11/14	11/12/14	1	A
	IR-13-00013-DST-927-A	Trench backfilling for segment B from Sta. 0+500 to Sta. 0+450(double trench)	11/10/14	11/11/14	11/12/14	1	A
	IR-13-00013-DST-928-A	Spreading tack coat on asphalt layer from Sta. 11+300 to Sta. 10+400	11/11/14	11/11/14	11/12/14	1	A
	IR-13-00013-DST-929-A	Asphalt reinstatement for wearing course layer (pipeline trench second layer & wearing course layer) from Sta. 11+300 to Sta. 10+400 (Starting from Nov. 11,2014 at 11:00 AM)	11/11/14	11/12/14	11/12/14	0	A
	IR-13-00013-DST-930-A	Pipes installation to connect Burqa connection chamber at Sta. 7+032 with main pipeline (Starting from Nov. 12,2014 at 9:30 AM)	11/12/14	11/13/14	11/13/14	0	A
	IR-13-00013-DST-931-A	Spreading tack coat on asphalt layer from Sta. 10+400 to Sta. 9+700	11/12/14	11/12/14	11/13/14	1	A
	IR-13-00013-DST-932-A	Asphalt reinstatement for wearing course layer (pipeline trench second layer & wearing course layer) from Sta. 10+400 to Sta. 9+700 (Starting from Nov. 12,2014 at 10:00 AM)	11/12/14	11/13/14	11/13/14	0	A
	IR-13-00013-DST-933-A	Bedding for segment B from Sta. 0+457 to Sta. 0+450(double trench)	11/12/14	11/12/14	11/12/14	0	A
	IR-13-00013-DST-934-A	Trench excavation for segment B from Sta. 0+450 to Sta. 0+427 (double trench)	11/12/14	11/12/14	11/13/14	1	A
	IR-13-00013-DST-935-A	6'' pipes installation for segment B from Sta. 0+450 to Sta. 0+427 (double trench)	11/12/14	11/12/14	11/13/14	1	A
	IR-13-00013-DST-936-A	Bedding for segment B from Sta. 0+450 to Sta. 0+427 (double trench)	11/12/14	11/12/14	11/13/14	1	A
	IR-13-00013-DST-937-A	Trench backfilling for segment B from Sta. 0+450 to Sta. 0+427 (double trench)	11/12/14	11/12/14	11/13/14	1	A
	IR-13-00013-DST-938-A	Trench excavation for segment B from Sta. 0+427 to Sta. 0+370(Single trench)	11/12/14	11/13/14	11/13/14	0	A
	IR-13-00013-DST-939-A	6'' pipes installation for segment B from Sta. 0+427 to Sta. 0+370(Single trench)	11/12/14	11/13/14	11/13/14	0	A
	IR-13-00013-DST-940-A	Bedding for segment B from Sta. 0+427 to Sta. 0+370(Single trench)	11/12/14	11/13/14	11/13/14	0	A
	IR-13-00013-DST-941-A	Trench backfilling for segment B from Sta. 0+427 to Sta. 0+370(Single trench)	11/12/14	11/13/14	11/13/14	0	A
	IR-13-00013-DST-942-A	Trench excavation for segment B from Sta. 0+370 to Sta. 0+300(Single trench)	11/13/14	11/15/14	11/16/14	1	A
	IR-13-00013-DST-943-A	6'' pipes installation for segment B from Sta. 0+370 to Sta. 0+300(Single trench)	11/13/14	11/15/14	11/16/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-944-A	Bedding for segment B from Sta. 0+370 to Sta. 0+300(Single trench)	11/13/14	11/15/14	11/16/14	1	A
	IR-13-00013-DST-945-A	Trench backfilling for segment B from Sta. 0+370 to Sta. 0+300(Single trench)	11/13/14	11/15/14	11/16/14	1	A
	IR-13-00013-DST-946-A	Inspection for flow control valve chamber at Sta. 1+174 to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	11/13/14	11/15/14	11/16/14	1	C
	IR-13-00013-DST-946-B	Inspection for flow control valve chamber at Sta. 1+174 to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	11/17/14	11/17/14	11/17/14	0	A
	IR-13-00013-DST-947-A	Excavation for combined AV/AR & BFV chamber at Sta. 1+162 (Starting on Saturday 11/15/2014)	11/13/14	11/16/14	11/17/14	1	A
	IR-13-00013-DST-948-A	Trench excavation for segment B from Sta. 0+300 to Sta. 0+250(Single trench)	11/13/14	11/16/14	11/17/14	1	A
	IR-13-00013-DST-949-A	6'' pipes installation for segment B from Sta. 0+300 to Sta. 0+250(Single trench)	11/13/14	11/16/14	11/17/14	1	A
	IR-13-00013-DST-950-A	Bedding for segment B from Sta. 0+300 to Sta. 0+250(Single trench)	11/13/14	11/16/14	11/17/14	1	A
	IR-13-00013-DST-951-A	Backfilling for segment B from Sta. 0+300 to Sta. 0+250(Single trench)	11/13/14	11/16/14	11/17/14	1	A
	IR-13-00013-DST-952-A	Trench excavation for segment B from Sta. 0+250 to Sta. 0+150(Single trench)	11/17/14	11/18/14	11/18/14	0	A
	IR-13-00013-DST-953-A	6'' pipes installation for segment B from Sta. 0+250 to Sta. 0+150(Single trench)	11/17/14	11/18/14	11/18/14	0	A
	IR-13-00013-DST-954-A	Bedding for segment B from Sta. 0+250 to Sta. 0+150(Single trench)	11/17/14	11/18/14	11/18/14	0	A
	IR-13-00013-DST-955-A	Trench backfilling for segment B from Sta. 0+250 to Sta. 0+150(Single trench)	11/17/14	11/18/14	11/18/14	0	A
	IR-13-00013-DST-956-A	Asphalt reinstatement for 300mm pipeline trench first & second layer from Sta. 7+748 to Sta. 7+945, Sta. 7+672 to Sta. 7+665,Sta. 7+624 to Sta. 7+617,Sta. 7+470 to Sta. 7+356,Sta. 7+318 to sta. 7+314,Sta. 7+222 to Sta. 7+217,Sta. 7+208 to Sta. 7+202,Sta. 8+214 to Sta. 8+238 ,Sta. 8+070 to Sta. 8+053 & Sta. 7+021 to Sta. 6+992	11/17/14	11/17/14	11/17/14	0	A
	IR-13-00013-DST-957-A	6 inch -polyethylene coated pipes/Grade B ASTM A53 steel pipes Sch. 40-Toscelik/FIP supplier ,QTY= 305 m	11/17/14	11/17/14	11/18/14	1	A
	IR-13-00013-DST-958-A	Inspection for check weld neck flanges-DIN 2635: 10 inch weld neck flange, QTY= 19 PCS, 12 inch weld neck flange, QTY=17 PCS	11/17/14	11/17/14	11/18/14	1	C
	IR-13-00013-DST-958-B	Inspection for check weld neck flanges-DIN 2635: 10 inch weld neck flange, QTY= 19 PCS, 12 inch weld neck flange, QTY=17 PCS	02/15/15	02/15/15	02/16/15	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-959-A	Trench excavation for segment B from Sta. 0+150 to Sta. 0+050(Single trench)	11/18/14	11/19/14	11/19/14	0	A
	IR-13-00013-DST-960-A	6'' pipes installation for segment B from Sta. 0+150 to Sta. 0+050(Single trench)	11/18/14	11/19/14	11/19/14	0	A
	IR-13-00013-DST-961-A	Bedding for segment B from Sta. 0+150 to Sta. 0+050(Single trench)	11/18/14	11/19/14	11/19/14	0	A
	IR-13-00013-DST-962-A	Trench backfilling for segment B from Sta. 0+150 to Sta. 0+050(Single trench)	11/18/14	11/19/14	11/19/14	0	A
	IR-13-00013-DST-963-A	Start excavation of flow monitoring Shavi Shamron chamber(PD-05) at Sta. 1+156(Starting from Nov. 18,2014 at 10:30 AM)	11/18/14	11/20/14	11/20/14	0	A
	IR-13-00013-DST-964-A	Formwork and steel reinforcement work for foundation of flow control valve chamber at Sta. 1+174	11/19/14	11/19/14	11/19/14	0	A
	IR-13-00013-DST-965-A	Inspection for combined AV/AR & BFV chamber at Sta. 1+162 at to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	11/19/14	11/19/14	11/19/14	0	A
	IR-13-00013-DST-966-A	Trench excavation for segment B from Sta. 0+050 to Sta. 0+007.24(Single trench)	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00013-DST-967-A	6'' pipes installation for segment B from Sta. 0+050 to Sta. 0+007.24(Single trench)	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00013-DST-968-A	Bedding for segment B from Sta. 0+050 to Sta. 0+007.24(Single trench)	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00013-DST-969-A	Trench backfilling for segment B from Sta. 0+050 to Sta. 0+007.24(Single trench)	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00013-DST-970-A	Conduct 4" pipes installation for segment B wash out chamber at sta. 0+010	11/20/14	11/20/14	11/20/14	0	C
	IR-13-00013-DST-970-B	Conduct 4" pipes installation for segment B wash out chamber at sta. 0+010	11/27/14	11/27/14	11/27/14	0	A
	IR-13-00013-DST-971-A	Precast wash out manhole installation for segment B at sta. 0+010	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00013-DST-972-A	Precast 6" G.V manhole installation for segment B at sta. 0+384	11/20/14	11/20/14	11/20/14	0	A
	IR-13-00013-DST-973-A	Surface preparation for external body of 6" G.V manhole - segment B at sta. 0+384	11/20/14	11/20/14	11/20/14	0	C
	IR-13-00013-DST-973-B	Surface preparation for external body of 6" G.V manhole - segment B at sta. 0+384	01/26/15	01/26/15	01/26/15	0	A
	IR-13-00013-DST-974-A	Surface preparation for external body of 4" Wash out manhole - segment B at sta. 0+010	11/20/14	11/20/14	11/20/14	0	C
	IR-13-00013-DST-974-B	Surface preparation for external body of 4" Wash out manhole - segment B at sta. 0+010	11/25/14	11/25/14	11/26/14	1	A
	IR-13-00013-DST-975-A	Trench excavation from Sta. 7+167 to Sta. 7+149 (starting at 11/20/2014	11/20/14	11/24/14	11/25/14	1	A
	IR-13-00013-DST-976-A	12" Pipes installation from Sta. 7+167 to Sta. 7+149 (starting at 11/20/2014)	11/20/14	11/24/14	11/25/14	1	A
	IR-13-00013-DST-977-A	Pipes installation for outlet wash out chamber at sta. 7+440 (starting at 11/22/2014)	11/20/14	11/24/14	11/25/14	1	C
	IR-13-00013-DST-977-B	Pipes installation for outlet wash out chamber at sta. 7+440	01/26/15	01/26/15	01/26/15	0	A
	IR-13-00013-DST-978-A	Backfilling around 250 mm G.V chamber at sta. 13+617 (starting at 11/20/2014)	11/20/14	11/24/14	11/25/14	1	C
	IR-13-00013-DST-978-B	Backfilling around 250 mm G.V chamber at sta. 13+617	12/04/14	12/04/14	12/04/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-979-A	Backfilling around Al assasa connection chamber at sta. 13+608 (starting at 11/20/2014)	11/20/14	11/24/14	11/25/14	1	C
	IR-13-00013-DST-979-B	Backfilling around Al assasa connection chamber at sta. 13+608	12/04/14	12/04/14	12/04/14	0	A
	IR-13-00013-DST-980-A	Backfilling around Wash out chamber at sta. 13+628	11/20/14	11/24/14	11/25/14	1	C
	IR-13-00013-DST-980-B	Backfilling around Wash out chamber at sta. 13+628	12/04/14	12/04/14	12/04/14	0	A
	IR-13-00013-DST-981-A	Inspection for welding flanges on manholes pipes spools(8,6,4,3&2inch)(Starting from Nov. 22,2014)	11/22/14	11/25/14	11/26/14	1	C
	IR-13-00013-DST-981-B	Inspection for welding flanges on manholes pipes spools(8,6,4,3&2inch)(Starting from Nov. 29,2014)	11/27/14	12/15/14	12/15/14	0	A
	IR-13-00013-DST-982-A	External formwork and steel reinforcement for walls of flow control valve chamber at Sta. 1+174 to close shutters	11/23/14	11/23/14	11/23/14	0	A
	IR-13-00013-DST-983-A	formwork and steel reinforcement for walls of flow control valve chamber at Sta. 1+174 to cast concrete	11/24/14	11/24/14	11/25/14	1	A
	IR-13-00013-DST-984-A	Formwork and steel reinforcement for foundation of combined AV/AR & BFV chamber at Sta. 1+162 to cast concrete	11/24/14	11/24/14	11/25/14	1	A
	IR-13-00013-DST-985-A	Excavation work for inlet Shavi Shamron flow monitoring chamber at Sta. 1+159 to cast blind concrete	11/24/14	11/24/14	11/25/14	1	A
	IR-13-00013-DST-986-A	Painting first layer for external body of Burqa connection chamber(small room) at Sta. 7+032 wit accepted bitumen material	11/25/14	11/25/14	11/25/14	0	A
	IR-13-00013-DST-987-A	Painting second layer for external body of Burqa connection chamber(small room) at Sta. 7+032 with accepted bitumen material	11/25/14	11/25/14	11/25/14	0	A
	IR-13-00013-DST-988-A	Trench Bedding from Sta. 7+167 to Sta. 7+149	11/25/14	11/25/14	11/26/14	1	A
	IR-13-00013-DST-989-A	Painting first layer for external body of WO manhole at Sta. 0+010-seg. B using accepted bitumen material	11/25/14	11/25/14	11/26/14	1	A
	IR-13-00013-DST-990-A	Painting second layer for external body of WO manhole at Sta. 0+010-seg. B using accepted bitumen material	11/25/14	11/25/14	11/26/14	1	A
	IR-13-00013-DST-991-A	Trench Backfilling from Sta. 7+167 to Sta. 7+149	11/25/14	11/25/14	11/26/14	1	A
	IR-13-00013-DST-992-A	Base course preparation for double trench asphalt reinstatement (segment B) from sta. 0+580 to sta. 0+427. (starting 29-11-2014)	11/27/14	12/01/14	12/02/14	1	A
	IR-13-00013-DST-993-A	Formwork & steel reinforcement for drainage ditch from sta. 1+700 to sta. 1+933, from sta. 1+332 to sta. 1+368. & from sta. 0+520 to sta. 0+090 (starting 29-11-2014)	11/27/14	12/01/14	12/01/14	0	A
	IR-13-00013-DST-994-A	Back filling for Burqa connection chamber at sta. 7+032	11/27/14	11/27/14	11/27/14	0	A
	IR-13-00013-DST-995-A	Back filling for flow monitoring chamber at sta. 7+160	11/27/14	11/27/14	11/27/14	0	A
	IR-13-00013-DST-996-A	Back filling for precast washout chamber at sta. 0+010 segment B	11/27/14	11/27/14	11/27/14	0	A
	IR-13-00013-DST-997-A	External formwork and steel reinforcement work for walls of combined AV/AR & BFV chamber at Sta. 1+162 to close shutters	11/29/14	11/29/14	11/30/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-998-A	Finishing work for internal body (base slab, walls & sailing) of GV chamber at Sta. 13+617	11/30/14	11/30/14	12/01/14	1	C
	IR-13-00013-DST-999-A	Base course preparation for drainage ditch from Sta. 7+470 to Sta. 7+356, Sta. 7+185 to Sta. 7+021, Sta. 6+992 to Sta. 6+983 & at Sta. 8+214 near Bazzarya connection	11/30/14	11/30/14	11/30/14	0	A
	IR-13-00013-DST-1000-A	Formwork and steel reinforcement work for drainage ditch to cast concrete from Sta. 7+470 to Sta. 7+356, Sta. 7+185 to Sta. 7+021, Sta. 6+992 to Sta. 6+983 & at Sta. 8+214 near Bazzarya connection	11/30/14	11/30/14	11/30/14	0	A
	IR-13-00013-DST-1001-A	Pipe installation for 6" G.V manhole at Sta. 0+384 to connect with 6'' pipeline –segment B	11/30/14	11/30/14	11/30/14	0	A
	IR-13-00013-DST-1002-A	Inspection for ASHCROFT pressure gauges: Pressure gauge-PN16,QTY= 4 Pressure gauge-PN25,QTY= 8 Pressure gauge-PN40,QTY=10	11/30/14	12/01/14	12/01/14	0	A
	IR-13-00013-DST-1003-A	Formwork and steel reinforcement work for opening necks of Al Foundqumiya connection chamber at sta. 12+143 & WO manhole at Sta. 0+010-seg. B to cast concrete	11/30/14	11/30/14	12/01/14	1	A
	IR-13-00013-DST-1004-A	Formwork and steel reinforcement work for foundation of inlet Shavi Shamron flow monitoring chamber at Sta. 1+159 to cast concrete	11/30/14	12/01/14	12/01/14	0	A
	IR-13-00013-DST-1005-A	Base course preparation for drainage ditch from Sta. 1+800 to Sta. 1+933, Sta. 1+332 to Sta. 1+369,Sta. 5+772 to Sta. 5+761,Sta. 5+136 to Sta. 5+126 & Sta. 4+086 to Sta. 4+072	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00013-DST-1006-A	Formwork and steel reinforcement for drainage ditch to cast concrete from Sta. 5+772 to Sta. 5+761,Sta. 5+136 to Sta. 5+126 & Sta. 4+086 to Sta. 4+072	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00013-DST-1007-A	Base course preparation for drainage ditch from Sta. 0+520 to Sta. 0+090	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00013-DST-1008-A	Start excavation for GV chamber at Sta. 0+653 (starting from Dec. 01,2014 at 11:30 AM)	12/01/14	12/02/14	12/02/14	0	A
	IR-13-00013-DST-1009-A	Excavation work for AV/AR chamber at Sta. 1+107	12/01/14	12/01/14	12/01/14	0	A
	IR-13-00013-DST-1010-A	Pipes installation for Sabstiya connection chamber at Sta. 2+320 to connect with 300 mm main pipeline	12/01/14	12/01/14	12/02/14	1	A
	IR-13-00013-DST-1011-A	Base course preparation for double trench asphalt reinstatement (segment B) from Sta. 1+000 to Sta. 0+580	12/01/14	12/01/14	12/02/14	1	A
	IR-13-00013-DST-1012-A	Spreading prime coat over finished base course layer from Sta. B1+000 to Sta. B0+427(Starting from Dec. 02,2014 at 9:30 AM)	12/02/14	12/03/14	12/03/14	0	A
	IR-13-00013-DST-1013-A	Asphalt reinstatement over trench edges with 150 mm pipes (First Layer) from Sta. B1+000 to Sta. B0+427(Starting from Dec. 02,2014 at 11:00 AM)	12/02/14	12/03/14	12/04/14	1	A
	IR-13-00013-DST-1014-A	Installation for AV/AR pre-cast manhole at Sta. 1+107	12/02/14	12/02/14	12/03/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1015-A	Installation for GV pre-cast manhole at Sta. 0+653	12/02/14	12/02/14	12/03/14	1	A
	IR-13-00013-DST-1016-A	Formwork and steel reinforcement work for opening necks of the followings chambers to cast concrete : 1. WO at Sta. 13+628 2. AV/AR at Sta. 8+885 3. AV/AR at Sta. 11+743 4. AV/AR at Sta. 1+390 5. Flow control valve at Sta. 7+160 6. Combined AV/AR & BFV at Sta. 7+400 7. Sabastiya connection chamber at Sta. 2+320	12/02/14	12/02/14	12/03/14	1	A
	IR-13-00013-DST-1017-A	Base course preparation for single trench asphalt reinstatement (segment B) from Sta. 0+427 to Sta. 0+007	12/03/14	12/03/14	12/03/14	0	A
	IR-13-00013-DST-1018-A	Backfilling around Sabstiya connection chamber at Sta. 2+320 with single size aggregate	12/03/14	12/03/14	12/03/14	0	A
	IR-13-00013-DST-1019-A	Spreading prime coat on finished base course layer(segment B) from Sta. 0+427 to Sta. 0+007	12/03/14	12/03/14	12/04/14	1	A
	IR-13-00013-DST-1020-A	Asphalt reinstatement over trench edges with 150 mm(first layer) from Sta. 0+427 to Sta. 0+007(segment B)	12/03/14	12/03/14	12/04/14	1	A
	IR-13-00013-DST-1021-A	Pipes installation for AV/AR precast manhole at Sta. 1+107 to connect with 300 mm main pipeline	12/04/14	12/04/14	12/04/14	0	A
	IR-13-00013-DST-1022-A	Pipes installation for GV precast manhole at Sta. 0+653 to connect with 150 mm main pipeline (segment B)	12/04/14	12/06/14	12/07/14	1	A
	IR-13-00013-DST-1023-A	Formwork and steel reinforcement work for walls of combined AV/AR & BFV chamber at Sta. 1+162 to cast concrete	12/04/14	12/04/14	12/04/14	0	A
	IR-13-00013-DST-1024-A	Steel reinforcement work for walls of inlet Shavi Shamron flow monitoring chamber at Sta. 1+159 to close shutters	12/04/14	12/04/14	12/04/14	0	A
	IR-13-00013-DST-1025-A	Formwork and steel reinforcement work for roof slab of flow control valve chamber at Sta. 1+174 to cast concrete	12/04/14	12/06/14	12/07/14	1	C
	IR-13-00013-DST-1025-B	Formwork and steel reinforcement work for roof slab of flow control valve chamber at Sta. 1+174 to cast concrete	12/09/14	12/09/14	12/09/14	0	A
	IR-13-00013-DST-1026-A	External surface preparation for body of GV precast manhole at Sta. 0+653(segment B) using FOSROC material	12/06/14	12/06/14	12/07/14	1	A
	IR-13-00013-DST-1027-A	Painting first layer for external body of GV precast manhole at Sta. 0+653(segment B) using bitumen material	12/06/14	12/06/14	12/07/14	1	A
	IR-13-00013-DST-1028-A	Painting second layer for external body of GV precast manhole at Sta. 0+653(segment B) using bitumen material	12/06/14	12/06/14	12/07/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1029-A	Backfilling around GV precast manhole at Sta. 0+653(segment B) with single size aggregate	12/08/14	12/08/14	12/08/14	0	A
	IR-13-00013-DST-1030-A	Painting first layer for external body of GV precast manhole at Sta. 0+384 (segment B) using bitumen material	12/08/14	12/08/14	12/08/14	0	A
	IR-13-00013-DST-1031-A	Painting second layer for external body of GV precast manhole at Sta. 0+384 (segment B) using bitumen material	12/08/14	12/08/14	12/08/14	0	A
	IR-13-00013-DST-1032-A	Backfilling around GV precast manhole at Sta. 0+384 (segment B) with single size aggregate	12/08/14	12/08/14	12/08/14	0	A
	IR-13-00013-DST-1033-A	Formwork and steel reinforcement for walls of inlet Shavi Shamron chamber at Sta. 1+159 to cast concrete	12/08/14	12/08/14	12/09/14	1	A
	IR-13-00013-DST-1034-A	Start excavation for BFV chamber for outlet Shavi Shamron pipe at Sta. 1+172 (starting from Dec. 08,2014)	12/08/14	12/09/14	12/10/14	1	A
	IR-13-00013-DST-1035-A	Surface preparation for external body of AV/AR precast manhole at Sta. 1+107 using FOSROC material	12/08/14	12/08/14	12/09/14	1	A
	IR-13-00013-DST-1036-A	Painting first & second layer for external body of AV/AR precast manhole at Sta. 1+107 using bitumen material	12/08/14	12/08/14	12/09/14	1	A
	IR-13-00013-DST-1037-A	Quality certificate for 6'' steel pipes delivered on Oct. 21, 2014 – (delivery No. A1402022)	12/09/14	12/09/14	12/09/14	0	A
	IR-13-00013-DST-1038-A	Cleaning and washing for 300 mm pipeline from Sta. 7+180 to Sta. 0+019-segment A	12/09/14	12/09/14	12/10/14	1	C
	IR-13-00013-DST-1038-B	Cleaning and washing for 300 mm pipeline from Sta. 7+180 to Sta. 0+019-segment A(Flushing point at Sta. 0+019,Sta. 2+960 & Sta. 3+960)	12/13/14	12/13/14	12/14/14	1	A
	IR-13-00013-DST-1039-A	Backfilling around AV/AR precast manhole at Sta. 1+107 with single size aggregate	12/10/14	12/10/14	12/10/14	0	A
	IR-13-00013-DST-1040-A	Inspection for BFV chamber for outlet Shavi Shamron pipe at Sta. 1+172 to cast blind concrete, include : • Excavation dimensions • Spread single size below base slab • Safety around the manhole. • level	12/10/14	12/10/14	12/10/14	0	A
	IR-13-00013-DST-1041-A	Inspection for Torq Bolts, Nuts & Washers (see the attached sheets for dimensional & quantities)	12/10/14	12/10/14	12/11/14	1	C
	IR-13-00013-DST-1041-B	Inspection for Torq Bolts, Nuts & Washers (see the attached sheets for dimensional , quantities & quality test report)	12/21/14	12/21/14	12/22/14	1	A
	IR-13-00013-DST-1042-A	Surface preparation for external body of flow control valve chamber at Sta. 1+174 using FOSROC material	12/11/14	12/11/14	12/11/14	0	A
	IR-13-00013-DST-1043-A	Inspection for fittings	12/11/14	12/11/14	12/11/14	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1043-B	Inspection for fittings	01/20/15	01/20/15	01/22/15	2	A
	IR-13-00013-DST-1044-A	Painting first layer for external body of FCV chamber at Sta. 1+174 using bitumen material	12/11/14	12/11/14	12/11/14	0	C
	IR-13-00013-DST-1044-B	Painting first layer for external body of FCV chamber at Sta. 1+174 using bitumen material	12/13/14	12/13/14	12/14/14	1	A
	IR-13-00013-DST-1045-A	Surface preparation for external body of inlet Shavi Shamron flow monitoring chamber at sta. 1+159 (starting from Dec. 11,2014 at 11:30 AM)	12/11/14	12/15/14	12/16/14	1	C
	IR-13-00013-DST-1045-B	Surface preparation for external body of inlet Shavi Shamron flow monitoring chamber at sta. 1+159 using FOSROC material	12/17/14	12/17/14	12/17/14	0	A
	IR-13-00013-DST-1046-A	Formwork and steel reinforcement work for foundation of BFV chamber for outlet Shavi Shamron pipe at Sta. 1+172 to cast concrete	12/11/14	12/13/14	12/14/14	1	A
	IR-13-00013-DST-1047-A	Formwork and steel reinforcement work for roof slab of combined AV/AR & BFV chamber at sta. 1+162 to cast concrete	12/11/14	12/13/14	12/14/14	1	A
	IR-13-00013-DST-1048-A	Formwork and steel reinforcement work for roof slab of inlet Shavi Shamron flow monitoring chamber to cast concrete	12/11/14	12/13/14	12/14/14	1	C
	IR-13-00013-DST-1048-B	Formwork and steel reinforcement work for roof slab of inlet Shavi Shamron flow monitoring chamber to cast concrete	12/15/14	12/15/14	12/15/14	0	A
	IR-13-00013-DST-1049-A	Painting second layer for external body of FCV chamber at Sta. 1+174 using bitumen material	12/13/14	12/13/14	12/14/14	1	A
	IR-13-00013-DST-1050-A	Internal finishing work for AV/AR a chamber at Sta. 9+928	12/14/14	12/14/14	12/15/14	1	C
	IR-13-00013-DST-1051-A	Inspection for Hydraulic pressure test for segment A from Sta. 7+160 to Sta. 0+019	12/14/14	12/14/14	12/15/14	1	A
	IR-13-00013-DST-1052-A	Painting flanged manholes spools pipes with epoxy paint (starting from Dec. 16,2014)	12/16/14	12/30/14	12/31/14	1	A
	IR-13-00013-DST-1053-A	Steel reinforcement for walls of BFV chamber for Shavi Shamron oulet pipe at Sta. 1+172 to close shutters	12/16/14	12/16/14	12/16/14	0	A
	IR-13-00013-DST-1054-A	Marking for edges of trench asphalt reinstatement (second layer) at segment B from Sta. 1+000 to Sta. 0+720	12/16/14	12/16/14	12/17/14	1	A
	IR-13-00013-DST-1055-A	Marking for edges of trench asphalt reinstatement (second layer) at segment B from Sta. 0+720 to Sta. 0+680	12/16/14	12/16/14	12/17/14	1	A
	IR-13-00013-DST-1056-A	Cleaning and washing for 300 mm pipeline(segment A) from Sta. 7+180 to Sta. 13+710 &for 150 mm pipeline from Sta. 0+000 to Sta. 0+126(segment C)	12/16/14	12/16/14	12/17/14	1	A
	IR-13-00013-DST-1057-A	Formwork and steel reinforcement for opening necks of the following chambers to cast concrete : • AV/AR chamber at Sta. 5+110 • AV/AR chamber at Sta. 1+390 • AV/AR chamber at Sta. 6+332 • WO at chamber Sta. 3+960	12/16/14	12/16/14	12/17/14	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1058-A	Formwork and steel reinforcement for walls of BFV chamber for Shavi Shamron oulet pipe at Sta. 1+172 to cast concrete	12/16/14	12/17/14	12/17/14	0	A
	IR-13-00013-DST-1059-A	Backfilling around FCV chamber at Sta. 1+174 with single size aggregate	12/17/14	12/17/14	12/17/14	0	A
	IR-13-00013-DST-1060-A	Washing for 6'' supply water line from Sta. 1+000 to Sta. 0+007 (segment B)-washing point at Al Foundqumiya connection at Sta. 12+143	12/17/14	12/17/14	12/17/14	0	A
	IR-13-00013-DST-1061-A	Surface preparation for external body of combined AV/AR & BFV chamber at Sta.. 1+162 using FOSROC material	12/17/14	12/17/14	12/17/14	0	A
	IR-13-00013-DST-1062-A	Painting first layer for external body of combined AV/AR & BFV chamber at Sta. 1+162 using bitumen material	12/17/14	12/17/14	12/17/14	0	A
	IR-13-00013-DST-1063-A	Hydraulic pressure test for 300 mm pipeline(segment A) from Sta. 7+160 to Sta. 13+710 &for 150 mm pipeline from Sta. 0+000 to Sta. 0+126(segment C)	12/18/14	12/18/14	12/18/14	0	A
	IR-13-00013-DST-1064-A	Welding flanges on manholes pipes spools(starting from Dec. 18,2014)	12/18/14	12/31/14	12/31/14	0	A
	IR-13-00013-DST-1065-A	Painting second layer for external body of combined AV/AR & BFV chamber at Sta. 1+162 using bitumen material	12/18/14	12/18/14	12/18/14	0	A
	IR-13-00013-DST-1066-A	Painting first layer for external body of inlet Shavi Shamron flow monitoring chamber at Sta. 1+159 using bitumen material	12/18/14	12/18/14	12/18/14	0	A
	IR-13-00013-DST-1067-A	Painting second layer for external body of inlet Shavi Shamron flow monitoring chamber at Sta. 1+159 using bitumen material	12/18/14	12/18/14	12/18/14	0	A
	IR-13-00013-DST-1068-A	Formwork and steel reinforcement for roof slab of BFV chamber for Shavi Shamron outlet pipe at Sta. 1+172 to cast concrete	12/18/14	12/20/14	12/21/14	1	A
	IR-13-00013-DST-1069-A	Washing for 6'' returned water line from Sta. 1+000 to Sta. 0+427(segment B)	12/18/14	12/20/14	12/21/14	1	A
	IR-13-00013-DST-1070-A	Hydraulic pressure test for 6'' returned water line from Sta. 1+000 to Sta. 0+427(segment B)	12/18/14	12/20/14	12/21/14	1	A
	IR-13-00013-DST-1071-A	Hydraulic pressure test for 6'' supply water line from Sta. 1+000 to Sta. 0+007 (segment B)	12/18/14	12/20/14	12/21/14	1	A
	IR-13-00013-DST-1072-A	Formwork and steel reinforcement for opening necks of the following chambers to cast concrete : • Combined AV/AR & BFV chamber at Sta. 1+162 • Flow control valve chamber at Sta. 1+174 • Inlet Shavi Shamron flow monitoring chamber at Sta. 1+159	12/21/14	12/21/14	12/21/14	0	A
	IR-13-00013-DST-1073-A	Marking for edges of trench asphalt reinstatement (second layer) at segment B from Sta. 0+680 to Sta. 0+427	12/21/14	12/21/14	12/21/14	0	A
	IR-13-00013-DST-1074-A	Marking for edges of trench asphalt reinstatement (second layer) at segment B from Sta. 0+427 to Sta. 0+007	12/21/14	12/21/14	12/21/14	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1075-A	Formwork and steel reinforcement for openings necks for the following chambers to cast concrete : • GV precast manhole at Sta. B0+653 • GV precast manhole at Sta. B0+384 • BFV chamber at Sta. A1+172 • FCV chamber at Sta. A1+174(square opening neck)	12/22/14	12/22/14	12/22/14	0	A
	IR-13-00013-DST-1076-A	Surface preparation for external body of BFV chamber for Shavi Shamron outlet at Sta. 1+172 using FOSROC material	12/22/14	12/22/14	12/22/14	0	A
	IR-13-00013-DST-1077-A	Painting first layer for external body of BFV chamber for Shavi Shamron outlet at Sta. 1+172 using bitumen material	12/22/14	12/22/14	12/23/14	1	A
	IR-13-00013-DST-1078-A	Inspection for SITRANS F M MAG 8000 WATER METER PN40(see the attached table & quality inspection certificates)	12/23/14	12/23/14	12/24/14	1	A
	IR-13-00013-DST-1079-A	Painting second layer for external body of BFV chamber for Shavi Shamron outlet at Sta. 1+172 using bitumen material	12/23/14	12/23/14	12/23/14	0	A
	IR-13-00013-DST-1080-A	Spreading tack coat on asphalt first layer from Sta. 1+000 to Sta. 0+600(segment B)	12/24/14	12/25/14	12/25/14	0	A
	IR-13-00013-DST-1081-A	Trench asphalt reinstatement (second layer) from Sta. 1+000 to Sta. 0+600(segment B)	12/24/14	12/25/14	12/25/14	0	A
	IR-13-00013-DST-1082-A	Spreading tack coat on asphalt first layer from Sta. 0+600 to Sta. 0+300(segment B)	12/24/14	12/26/14	12/28/14	2	A
	IR-13-00013-DST-1083-A	Trench asphalt reinstatement (second layer) from Sta. 0+600 to Sta. 0+300(segment B)	12/24/14	12/26/14	12/28/14	2	A
	IR-13-00013-DST-1084-A	Spreading tack coat on asphalt first layer from Sta. 0+300 to Sta. 0+007(segment B)	12/24/14	12/27/14	12/28/14	1	A
	IR-13-00013-DST-1085-A	Trench asphalt reinstatement (second layer) from Sta. 0+300 to Sta. 0+007(segment B)	12/24/14	12/27/14	12/28/14	1	A
	IR-13-00013-DST-1086-A	Fittings installation (air release valve, gate valve & dismantling joint) for the AV/AR chambers at Sta. 12+500, Sta. 11+743,Sta. 1+390 ,Sta. 1+107,Sta. 6+332,Sta. 8+885,Sta. 5+110 & Sta. 9+928 (starting from Dec. 25,2014)	12/24/14	12/29/14	12/29/14	0	C
	IR-13-00013-DST-1087-A	Painting welded flanges inside chambers (starting from Dec. 25,2014)	12/24/14	12/30/14	12/31/14	1	A
	IR-13-00013-DST-1088-A	Pipes installation to connect inlet Shavi Shamron chamber at Sta. 1+159 with 300 mm pipeline	12/28/14	12/28/14	12/28/14	0	A
	IR-13-00013-DST-1089-A	Pipes installation to connect BFV chamber for Shavi Shamron outlet pipe at Sta. 1+172 with 300 mm pipeline	12/28/14	12/28/14	12/28/14	0	A
	IR-13-00013-DST-1090-A	Welding flanges inside chambers in segment B at the following stations : • WO chamber at Sta. B0+010 • GV chamber at Sta. B0+384 • GV chamber at Sta. B0+653 (Starting from Dec. 28,2014)	12/28/14	12/29/14	12/29/14	0	C
	IR-13-00013-DST-1091-A	Inspection for Air release valves	12/28/14	12/29/14	12/29/14	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1091-B	Inspection for Air release valves	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1091-C	Inspection for Air release valves	01/26/15	01/28/15	01/29/15	1	A
	IR-13-00013-DST-1092-A	Inspection for check valves:	12/28/14	12/29/14	12/29/14	0	C
	IR-13-00013-DST-1092-B	Inspection for check valves:	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1092-C	Inspection for check valves:	01/26/15	01/26/15	01/29/15	3	A
	IR-13-00013-DST-1093-A	Inspection for Air release valve (Model S-015-01)	12/29/14	12/29/14	12/29/14	0	C
	IR-13-00013-DST-1093-B	Inspection for Air release valve (Model S-015-01)	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1093-C	Inspection for Air release valve (Model S-015-01)	01/26/15	01/26/15	01/29/15	3	A
	IR-13-00013-DST-1094-A	Inspection for Flap valves:	12/29/14	12/30/14	12/30/14	0	A
	IR-13-00013-DST-1095-A	Milling for RHS shoulder for main road from Sta. 1+240 to Sta. 4+300	12/29/14	12/29/14	12/30/14	1	A
	IR-13-00013-DST-1096-A	Spreading tack coat on milled RHS shoulder for main road from Sta. 1+240 to Sta. 2+740	12/29/14	12/29/14	12/30/14	1	A
	IR-13-00013-DST-1097-A	Asphalt wearing course for RHS shoulder of main road from Sta. 1+240 to Sta. 2+740 (starting from Dec. 29,2014 at 11:00AM)	12/29/14	12/29/14	12/30/14	1	A
	IR-13-00013-DST-1098-A	Spreading tack coat on milled RHS shoulder for main road from Sta. 2+740 to Sta. 3+740	12/30/14	12/30/14	12/30/14	0	A
	IR-13-00013-DST-1099-A	Asphalt wearing course for RHS shoulder of main road from Sta. 2+740 to Sta. 3+740 (starting from Dec. 30,2014 at 11:00AM)	12/30/14	12/30/14	12/31/14	1	A
	IR-13-00013-DST-1100-A	Inspection for Flow Control Valves	12/30/14	01/04/15	01/06/15	2	C
	IR-13-00013-DST-1101-A	Inspection for Pressure Reducing Control Valves	12/30/14	01/04/15	01/06/15	2	C
	IR-13-00013-DST-1102-A	Inspection for Pressure Relief Valves	12/30/14	01/04/15	01/06/15	2	C
	IR-13-00013-DST-1103-A	Welding flanges inside WO chamber at Sta. 0+010-segment B	12/30/14	12/31/14	12/31/14	0	A
	IR-13-00013-DST-1104-A	Fitting installation for WO chamber at Sta. 0+010-segment B	12/30/14	12/31/14	12/31/14	0	A
	IR-13-00013-DST-1105-A	Welding flanges inside Al Foundqumiya connection chamber at Sta. 12+143	12/30/14	12/31/14	12/31/14	0	A
	IR-13-00013-DST-1106-A	Spreading tack coat on milled RHS shoulder for main road from Sta. 3+740 to Sta. 4+300	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00013-DST-1107-A	Asphalt wearing course for RHS shoulder of main road from Sta. 3+740 to Sta. 4+300 (starting from Dec. 31,2014 at 11:00AM)	12/31/14	12/31/14	12/31/14	0	A
	IR-13-00013-DST-1108-A	Fittings installation for Al Foundqumiya connection chamber at Sta. 12+143	12/31/14	12/31/14	12/31/14	0	C
	IR-13-00013-DST-1109-A	Acrylic painting for RHS & LHS shoulder of main road from Sta. 7+370 to Sta. 8+200 (Starting from Feb. 26,2015 at 10:00 AM)	02/26/15	02/26/15	02/26/15	0	C
	IR-13-00013-DST-1109-B	Acrylic painting for RHS & LHS shoulder of main road from Sta. 7+370 to Sta. 8+200	02/28/15	02/28/15		PE	
	IR-13-00013-DST-1110-A	Milling for LHS shoulder for main road from Sta. 1+240 to Sta. 4+300	12/31/14	12/31/14	01/01/15	1	A
	IR-13-00013-DST-1111-A	Spreading tack coat on milled LHS shoulder for main road from Sta. 4+300 to Sta. 3+800	12/31/14	12/31/14	01/01/15	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1112-A	Asphalt wearing course for LHS shoulder of main road from Sta. 4+300 to Sta. 3+800 (starting from Dec. 31,2014 at 2:00PM)	12/31/14	12/31/14	01/01/15	1	A
	IR-13-00013-DST-1113-A	Spreading tack coat on milled LHS shoulder for main road from Sta. 3+800 to Sta. 2+600	12/31/14	01/01/15	01/01/15	0	A
	IR-13-00013-DST-1114-A	Asphalt wearing course for LHS shoulder of main road from Sta. 3+800 to Sta. 2+600	12/31/14	01/01/15	01/01/15	0	A
	IR-13-00013-DST-1115-A	Spreading tack coat on milled LHS shoulder for main road from Sta. 2+600 to Sta. 1+240	12/31/14	01/02/15	01/03/15	1	A
	IR-13-00013-DST-1116-A	Asphalt wearing course for LHS shoulder of main road from Sta. 2+600 to Sta. 1+240	12/31/14	01/02/15	01/03/15	1	A
	IR-13-00013-DST-1117-A	Disinfection for 6'' returned water line from Sta. 1+000 to Sta. 0+427(segment B) (starting from Feb. 26,2015)	02/26/15	03/02/15		PE	
	IR-13-00013-DST-1118-A	Milling for RHS shoulder for main road from Sta. 4+300 to Sta. 5+500	12/31/14	12/31/14	01/01/15	1	D
	IR-13-00013-DST-1118-B	Milling for RHS shoulder for main road from Sta. 4+300 to Sta. 5+500	01/02/14	01/02/15	01/03/15	1	A
	IR-13-00013-DST-1119-A	Spreading tack coat on milled RHS shoulder for main road from Sta. 4+300 to Sta. 5+500	12/31/14	01/03/15	01/03/15	0	A
	IR-13-00013-DST-1120-A	Asphalt wearing course for RHS shoulder of main road from Sta. 4+300 to Sta. 5+500	12/31/14	01/03/15	01/03/15	0	A
	IR-13-00013-DST-1121-A	Mechanical fittings installation inside 250 mm GV chamber at Sta. 13+617	01/05/15	01/05/15	01/06/15	1	A
	IR-13-00013-DST-1122-A	Mechanical fittings installation inside 200 mm GV chamber at Sta. 10+461	01/05/15	01/05/15	01/06/15	1	A
	IR-13-00013-DST-1123-A	Mechanical fittings installation inside 200 mm GV chamber at Sta. 9+941	01/05/15	01/05/15	01/06/15	1	A
	IR-13-00013-DST-1124-A	Inspection for Froged flange (Hubbed slip-on) & Welded Neck flange	01/11/15	01/12/15	01/13/15	1	C
	IR-13-00013-DST-1125-A	Mechanical fittings installation for WO chamber at Sta. 13+628(150 mm gate valve and 150 mm dismantling joint)	01/12/15	01/12/15	01/13/15	1	C
	IR-13-00013-DST-1126-A	Mechanical fittings installation for WO chamber at Sta. 10+889(150 mm gate valve and 150 mm dismantling joint)	01/12/15	01/12/15	01/13/15	1	A
	IR-13-00013-DST-1127-A	Mechanical fittings installation for WO chamber at Sta. 3+924(150 mm gate valve and 150 mm dismantling joint)	01/12/15	01/12/15	01/13/15	1	A
	IR-13-00013-DST-1128-A	Internal finishing work(floor, ceiling & walls) for combined AV/AR & BFV chamber at Sta. 1+162	01/12/15	01/13/15	01/14/15	1	C
	IR-13-00013-DST-1129-A	Internal finishing work(floor, ceiling & walls) for BFV Shavi Shamron outlet chamber at Sta. 1+172	01/12/15	01/13/15	01/14/15	1	C
	IR-13-00013-DST-1130-A	Internal finishing work(floor, ceiling & walls) for inlet Shavi Shamron chamber at Sta. 1+159	01/12/15	01/13/15	01/14/15	1	C
	IR-13-00013-DST-1131-A	Internal finishing work(floor, ceiling & walls) for flow control valve chamber at Sta. 1+174	01/12/15	01/13/15	01/14/15	1	C
	IR-13-00013-DST-1132-A	Internal finishing work(floor, ceiling & walls) for AV/AR chamber at Sta. 1+107	01/12/15	01/13/15	01/14/15	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1133-A	Mechanical fittings installation for WO chamber at Sta. 7+440(150 mm gate valve and 150 mm dismantling joint)	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00013-DST-1134-A	Inspection for alignment of sewer pipeline and manholes location from Sta. 0+000 to Sta. 0+250	01/13/15	01/13/15	01/13/15	0	A
	IR-13-00013-DST-1135-A	Material inspection for sewer precast manholes	01/13/15	01/13/15	01/13/15	0	C
	IR-13-00013-DST-1135-B	Material inspection for sewer precast manholes	02/15/15	02/15/15	02/16/15	1	A
	IR-13-00013-DST-1136-A	Material inspection for UPVC sewer pipes	01/13/15	01/13/15	01/13/15	0	A
	IR-13-00013-DST-1137-A	Milling for RHS shoulder of main road from Sta. 5+500 to Sta. 7+300	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00013-DST-1138-A	Spreading tack coat on milled RHS shoulder of main road from Sta. 5+500 to Sta. 6+500	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00013-DST-1139-A	Asphalt wearing course for RHS shoulder of main road from Sta. 5+500 to Sta. 6+500	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00013-DST-1140-A	Excavation for sewer pipeline from MH-01 to MH-02	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00013-DST-1141-A	Installation for sewer UPCV pipes from MH-01 to MH-02	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00013-DST-1142-A	Bedding for sewer pipeline from MH-01 to MH-02	01/13/15	01/13/15	01/14/15	1	A
	IR-13-00013-DST-1143-A	Backfilling for sewer pipeline from MH-01 to MH-02	01/13/15	01/13/15	01/14/15	1	C
	IR-13-00013-DST-1143-B	Backfilling for sewer pipeline from MH-01 to MH-02	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1144-A	Installation for MH-01 & MH-02	01/13/15	01/13/15	01/14/15	1	C
	IR-13-00013-DST-1144-B	Installation for MH-01 & MH-02	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-1145-A	Internal finishing work(floor, ceiling & walls) for Bazzariya connection chamber at Sta. 8+206	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1146-A	Internal finishing work(floor, ceiling & walls) for Al Asa'sa connection chamber at Sta. 13+608	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1147-A	Internal finishing work(floor, ceiling & walls) for GV chamber at 13+617	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1148-A	Internal finishing work(floor, ceiling & walls) for BFV chamber at Sta. 13+700	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1149-A	Internal finishing work(floor, ceiling & walls) for WO chamber at Sta. 13+628	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1150-A	Internal finishing work(floor, ceiling & walls) for Al Foundqumiya connection chamber at Sta. 12+143	01/14/15	01/15/15	01/15/15	0	C
	IR-13-00013-DST-1151-A	Excavation for sewer pipeline from MH-02 to MH-03	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00013-DST-1152-A	Installation for MH-03	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1152-B	Installation for MH-03	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-1153-A	Installation for sewer UPCV pipes from MH-02 to MH-03	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00013-DST-1154-A	Bedding for sewer pipeline from MH-02 to MH-03	01/14/15	01/14/15	01/15/15	1	A
	IR-13-00013-DST-1155-A	Backfilling for sewer pipeline from MH-02 to MH-03	01/14/15	01/14/15	01/15/15	1	C
	IR-13-00013-DST-1155-B	Backfilling for sewer pipeline from MH-02 to MH-03	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1156-A	Spreading tack coat on milled RHS shoulder of main road from Sta. 6+500 to Sta. 7+250	01/15/15	01/15/15	01/15/15	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1157-A	Asphalt wearing course for RHS shoulder of main road from Sta. 6+500 to Sta. 7+250	01/15/15	01/15/15	01/15/15	0	A
	IR-13-00013-DST-1158-A	Excavation for sewer pipeline from MH-03 to MH-04	01/15/15	01/15/15	01/15/15	0	A
	IR-13-00013-DST-1159-A	Installation for MH-04	01/15/15	01/15/15	01/15/15	0	C
	IR-13-00013-DST-1159-B	Installation for MH-04	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-1160-A	Installation for sewer UPCV pipes from MH-03 to MH-04	01/15/15	01/15/15	01/15/15	0	A
	IR-13-00013-DST-1161-A	Bedding for sewer pipeline from MH-03 to MH-04	01/15/15	01/15/15	01/15/15	0	A
	IR-13-00013-DST-1162-A	Backfilling for sewer pipeline from MH-03 to MH-04	01/15/15	01/15/15	01/15/15	0	C
	IR-13-00013-DST-1162-B	Backfilling for sewer pipeline from MH-03 to MH-04	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1163-A	Excavation for sewer pipeline from MH-04 to MH-05 to MH-06	01/15/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1164-A	Installation for MH-05 & MH-06	01/15/15	01/17/15	01/18/15	1	C
	IR-13-00013-DST-1164-B	Installation for MH-05 & MH-06	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-1165-A	Installation for sewer UPCV pipes from MH-04 to MH-05 to MH-06	01/15/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1166-A	Bedding for sewer pipeline from MH-04 to MH-05 to MH-06	01/15/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1167-A	Backfilling for sewer pipeline from MH-04 to MH-05 to MH-06	01/15/15	01/17/15	01/18/15	1	C
	IR-13-00013-DST-1167-B	Backfilling for sewer pipeline from MH-04 to MH-05 to MH-06	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1168-A	Marking alignment of 4" Burqa water pipeline from Sta. 0+000 to Sta. 0+300	01/15/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1169-A	Trench excavation for Burqa water pipeline from Sta. 0+000 to Sta. 0+100 (Starting from Jan. 17,2015)	01/15/15	01/18/15	01/19/15	1	A
	IR-13-00013-DST-1170-A	4 " pipes installation for Burqa water pipeline from Sta. 0+000 to Sta. 0+100 (Starting from Jan. 17,2015)	01/15/15	01/18/15	01/19/15	1	A
	IR-13-00013-DST-1171-A	Bedding for Burqa water pipeline from Sta. 0+000 to Sta. 0+100 (Starting from Jan. 17,2015)	01/15/15	01/18/15	01/19/15	1	A
	IR-13-00013-DST-1172-A	Backfilling for Burqa water pipeline from Sta. 0+000 to Sta. 0+100 (Starting from Jan. 17,2015)	01/15/15	01/18/15	01/19/15	1	A
	IR-13-00013-DST-1173-A	Welding flanges inside combined AV/AR & BFV chamber at Sta. 7+400	01/15/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1174-A	Excavation for sewer pipeline from MH-06 to MH-07	01/17/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1175-A	Installation for MH-07	01/17/15	01/17/15	01/18/15	1	C
	IR-13-00013-DST-1175-B	Installation for MH-07	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-1176-A	Installation for sewer UPCV pipes from MH-06 to MH-07	01/17/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1177-A	Bedding for sewer pipeline from MH-06 to MH-07	01/17/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1178-A	Backfilling for sewer pipeline from MH-06 to MH-07	01/17/15	01/17/15	01/18/15	1	C
	IR-13-00013-DST-1178-B	Backfilling for sewer pipeline from MH-06 to MH-07	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1179-A	Excavation for sewer pipeline from MH-07 to MH-08	01/17/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1180-A	Installation for MH-08	01/17/15	01/17/15	01/18/15	1	C
	IR-13-00013-DST-1180-B	Installation for MH-08	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-1181-A	Installation for sewer UPCV pipes from MH-07 to MH-08	01/17/15	01/17/15	01/18/15	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1182-A	Bedding for sewer pipeline from MH-07 to MH-08	01/17/15	01/17/15	01/18/15	1	A
	IR-13-00013-DST-1183-A	Backfilling for sewer pipeline from MH-07 to MH-08	01/17/15	01/17/15	01/18/15	1	C
	IR-13-00013-DST-1183-B	Backfilling for sewer pipeline from MH-07 to MH-08	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1184-A	Internal finishing work(floor, ceiling & walls) for WO chamber at Sta. 7+440	01/18/15	01/18/15	01/19/15	1	C
	IR-13-00013-DST-1185-A	Internal finishing work(floor, ceiling & walls) for combined AV//AR & BFV chamber at Sta. 7+400	01/18/15	01/18/15	01/19/15	1	C
	IR-13-00013-DST-1186-A	Internal finishing work(floor, ceiling & walls) for flow monitoring chamber at Sta. 7+160	01/18/15	01/18/15	01/19/15	1	C
	IR-13-00013-DST-1187-A	Internal finishing work(floor, ceiling & walls) for Burqa connection chamber at Sta. 7+032	01/18/15	01/18/15	01/19/15	1	C
	IR-13-00013-DST-1188-A	Internal finishing work(floor, ceiling & walls) for combined AV/AR & BFV chamber at Sta. 3+350	01/18/15	01/19/15	01/19/15	0	C
	IR-13-00013-DST-1189-A	Milling for LHS shoulder of main road from Sta. 4+300 to Sta. 7+370	01/18/15	01/18/15	01/19/15	1	A
	IR-13-00013-DST-1190-A	Excavation for sewer pipeline from MH-08 to MH-09 to MH-10 to MH-11(starting from Jan. 18,2015)	01/18/15	01/19/15	01/19/15	0	A
	IR-13-00013-DST-1191-A	Installation for MH-09 & MH-10	01/18/15	01/19/15	01/19/15	0	C
	IR-13-00013-DST-1191-B	Installation for MH-09 & MH-10	02/10/15	02/10/15	02/10/15	0	A
	IR-13-00013-DST-1192-A	Installation for sewer UPCV pipes from MH-08 to MH-09 to MH-10 to MH-11	01/18/15	01/19/15	01/19/15	0	A
	IR-13-00013-DST-1193-A	Bedding for sewer pipeline from MH-08 to MH-09 to MH-10 to MH-11	01/18/15	01/19/15	01/19/15	0	A
	IR-13-00013-DST-1194-A	Backfilling for sewer pipeline from MH-08 to MH-09 to MH-10 to MH-11	01/18/15	01/19/15	01/19/15	0	C
	IR-13-00013-DST-1194-B	Backfilling for sewer pipeline from MH-08 to MH-09 to MH-10 to MH-11	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1195-A	Spreading tack coat on milled LHS shoulder of main road from Sta. 7+370 to Sta. 6+300	01/19/15	01/19/15	01/20/15	1	A
	IR-13-00013-DST-1196-A	Asphalt wearing course for LHS shoulder of main road from Sta. 7+370 to Sta. 6+300(staring from Jan. 19,2015 at 11:00 AM)	01/19/15	01/19/15	01/20/15	1	A
	IR-13-00013-DST-1197-A	Trench excavation for Burqa water pipeline from Sta. 0+100 to Sta. 0+250	01/19/15	01/20/15	01/20/15	0	A
	IR-13-00013-DST-1198-A	4'' pipes installation for Burqa water pipeline from Sta. 0+100 to Sta. 0+250	01/19/15	01/20/15	01/20/15	0	A
	IR-13-00013-DST-1199-A	Bedding for Burqa water pipeline from Sta. 0+100 to Sta. 0+250	01/19/15	01/20/15	01/20/15	0	A
	IR-13-00013-DST-1200-A	Backfilling for Burqa water pipeline from Sta. 0+100 to Sta. 0+250	01/19/15	01/20/15	01/20/15	0	A
	IR-13-00013-DST-1201-A	Trench excavation for Burqa water pipeline from Sta. 0+250 to Sta. 0+350	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00013-DST-1202-A	4'' pipes installation for Burqa water pipeline from Sta. 0+250 to Sta. 0+350	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00013-DST-1203-A	Bedding for Burqa water pipeline from Sta. 0+250 to Sta. 0+350	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00013-DST-1204-A	Backfilling for Burqa water pipeline from Sta. 0+250 to Sta. 0+350	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00013-DST-1205-A	Spreading tack coat on milled LHS shoulder from Sta. 6+300 to Sta. 5+800	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00013-DST-1206-A	Asphalt wearing course for LHS shoulder from Sta. 6+300 to Sta. 5+800	01/20/15	01/20/15	01/21/15	1	A
	IR-13-00013-DST-1207-A	Marking alignment for Burqa water pipeline from Sta. 0+300 to Sta. 0+700 (starting from Jan. 20,2015)	01/20/15	01/20/15	01/21/15	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1208-A	Inspection for Butterfly valves	01/20/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1209-A	Inspection for Ball valves	01/20/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1210-A	Trench excavation for Burqa water pipeline from Sta. 0+350 to Sta. 0+450	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1211-A	4'' pipes installation for Burqa water pipeline from Sta. 0+350 to Sta. 0+450	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1212-A	Bedding for Burqa water pipeline from Sta. 0+350 to Sta. 0+450	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1213-A	Backfilling for Burqa water pipeline from Sta. 0+350 to Sta. 0+450	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1214-A	Welding flanges inside BFV of Shavi Shamron outlet chamber at Sta. 1+172	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1215-A	Welding flanges inside combined AV/AR & BFV chamber at Sta. 1+162	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1216-A	Spreading tack coat on milled LHS shoulder from Sta. 5+800 to Sta. 4+300	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1217-A	Asphalt wearing course for LHS shoulder from Sta. 5+800 to Sta. 4+300	01/21/15	01/21/15	01/22/15	1	A
	IR-13-00013-DST-1218-A	Trench excavation for Burqa water pipeline from Sta. 0+450 to Sta. 0+600	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00013-DST-1219-A	4'' pipes installation for Burqa water pipeline from Sta. 0+450 to Sta. 0+600	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00013-DST-1220-A	Bedding for Burqa water pipeline from Sta. 0+450 to Sta. 0+600	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00013-DST-1221-A	Backfilling for Burqa water pipeline from Sta. 0+450 to Sta. 0+600	01/22/15	01/22/15	01/22/15	0	A
	IR-13-00013-DST-1222-A	Trench excavation for Burqa water pipeline from Sta. 0+600 to Sta. 0+800	01/22/15	01/24/15	01/25/15	1	A
	IR-13-00013-DST-1223-A	4'' pipes installation for Burqa water pipeline from Sta. 0+600 to Sta. 0+800	01/22/15	01/24/15	01/25/15	1	A
	IR-13-00013-DST-1224-A	Bedding for Burqa water pipeline from Sta. 0+600 to Sta. 0+800	01/22/15	01/24/15	01/25/15	1	A
	IR-13-00013-DST-1225-A	Backfilling for Burqa water pipeline from Sta. 0+600 to Sta. 0+800	01/22/15	01/24/15	01/25/15	1	A
	IR-13-00013-DST-1226-A	Mechanical fittings installation for BFV chamber at Sta. 2+952(starting from Jan. 24,2015 at 8:00AM)	01/22/15	01/25/15	01/26/15	1	C
	IR-13-00013-DST-1227-A	Mechanical fittings installation for BFV chamber at Sta. 13+700(starting from Jan. 24,2015 at 8:00AM)	01/22/15	01/25/15	01/26/15	1	C
	IR-13-00013-DST-1228-A	Mechanical fittings installation for combined AV/AR & BFV chamber at Sta. 11+187 (starting from Jan. 24,2015 at 8:00AM)	01/22/15	01/25/15	01/26/15	1	C
	IR-13-00013-DST-1229-A	Mechanical fittings installation for combined AV/AR & BFV chamber at Sta. 7+400 (starting from Jan. 24,2015 at 8:00AM)	01/22/15	01/25/15	01/26/15	1	C
	IR-13-00013-DST-1230-A	Epoxy painting for internal walls of GV chamber at Sta. 9+941 (Starting from Jan. 22,2015 at 2:00 PM)	01/22/15	01/24/15	01/25/15	1	A
	IR-13-00013-DST-1231-A	Marking alignment for Acrylic paint for RHS shoulder of main road from Sta. 1+240 to Sta. 7+250	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1232-A	Marking alignment for Burqa water pipeline from Sta. 0+700 to Sta. 1+000	01/25/15	01/25/15	01/26/15	1	A
	IR-13-00013-DST-1233-A	Marking alignment for Acrylic paint for LHS shoulder of main road from Sta. 1+240 to Sta. 7+370	01/26/15	01/26/15	01/26/15	0	A
	IR-13-00013-DST-1234-A	Acrylic painting for RHS shoulder of main road from Sta. 1+240 to Sta. 7+250	01/26/15	01/26/15	01/26/15	0	C
	IR-13-00013-DST-1235-A	Asphalt wearing course for RHS shoulder of main road from Sta. 7+250 to Sta. 7+370	01/26/15	01/26/15	01/26/15	0	A
	IR-13-00013-DST-1236-A	Acrylic painting for RHS shoulder of main road from Sta. 7+250 to Sta. 7+370	01/26/15	01/26/15	01/26/15	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1237-A	Formwork and steel reinforcement for Sialt Al Daher concrete pad to cast concrete	01/26/15	01/26/15	01/27/15	1	A
	IR-13-00013-DST-1238-A	Acrylic painting for LHS shoulder of main road from Sta. 1+240 to Sta. 7+370	01/27/15	01/27/15	01/28/15	1	C
	IR-13-00013-DST-1239-A	Marking location for 6 " GV chamber for Al Foundqumiya at Sta. 0+990 to start excavation	01/27/15	01/27/15	01/27/15	0	A
	IR-13-00013-DST-1240-A	Marking location for 4 " GV chamber for Al Foundqumiya at Sta. 0+990 to start excavation	01/27/15	01/27/15	01/27/15	0	A
	IR-13-00013-DST-1241-A	Marking location for 2 " GV chamber for Al Foundqumiya at Sta. 0+410 to start excavation	01/27/15	01/27/15	01/27/15	0	A
	IR-13-00013-DST-1242-A	Marking location for 2 " GV chamber for Al Foundqumiya at Sta. 0+430 to start excavation	01/27/15	01/27/15	01/27/15	0	A
	IR-13-00013-DST-1243-A	Trench excavation for Burqa water pipeline from Sta. 0+800 to Sta. 0+900	01/29/15	01/31/15	02/01/15	1	A
	IR-13-00013-DST-1244-A	4'' pipes installation for Burqa water pipeline from Sta. 0+800 to Sta. 0+900	01/29/15	01/31/15	02/01/15	1	A
	IR-13-00013-DST-1245-A	Bedding for Burqa water pipeline from Sta. 0+800 to Sta. 0+900	01/29/15	01/31/15	02/01/15	1	A
	IR-13-00013-DST-1246-A	Backfilling for Burqa water pipeline from Sta. 0+800 to Sta. 0+900	01/29/15	01/31/15	02/01/15	1	A
	IR-13-00013-DST-1247-A	Welding flanges inside Al Asa'sa connection chamber at Sta. 13+608 (Starting from Jan. 31,2015)	01/29/15	02/02/15	02/03/15	1	C
	IR-13-00013-DST-1247-B	Welding flanges inside Al Asa'sa connection chamber at Sta. 13+608	02/15/15	02/15/15	02/15/15	0	A
	IR-13-00013-DST-1248-A	Mechanical fittings installation for FCV chamber at Sta. 1+174(Starting from Jan. 31,2015)	01/29/15	02/02/15	02/03/15	1	C
	IR-13-00013-DST-1249-A	Mechanical fittings installation for combined AV/AR & BFV chamber at Sta. 11+187(Starting from Jan. 31,2015)	01/29/15	02/02/15	02/03/15	1	C
	IR-13-00013-DST-1250-A	Marking location for Sabastiya GV chamber around Sta. 2+952 to start excavation	01/31/15	01/31/15	02/01/15	1	A
	IR-13-00013-DST-1251-A	Trench excavation for Burqa water pipeline from Sta. 0+900 to Sta. 1+000	02/01/15	02/02/15	02/02/15	0	A
	IR-13-00013-DST-1252-A	4'' pipes installation for Burqa water pipeline from Sta. 0+900 to Sta. 1+000	02/01/15	02/02/15	02/02/15	0	A
	IR-13-00013-DST-1253-A	Bedding for Burqa water pipeline from Sta. 0+900 to Sta. 1+000	02/01/15	02/02/15	02/02/15	0	A
	IR-13-00013-DST-1254-A	Backfilling for Burqa water pipeline from Sta. 0+900 to Sta. 1+000	02/01/15	02/02/15	02/02/15	0	A
	IR-13-00013-DST-1255-A	Washout outlet concrete retaining wall at Sta. 7+440 & Sta. 13+628	02/01/15	02/01/15	02/01/15	0	A
	IR-13-00013-DST-1256-A	Installation for precast Sabastiya GV chamber around Sta. 2+952	02/01/15	02/01/15	02/01/15	0	A
	IR-13-00013-DST-1257-A	Marking alignment for Burqa pipeline from Sta. 1+000 to Sta. 1+200	02/02/15	02/02/15	02/02/15	0	A
	IR-13-00013-DST-1258-A	Trench excavation for Burqa water pipeline from Sta. 1+000 to Sta. 1+100	02/02/15	02/03/15	02/04/15	1	A
	IR-13-00013-DST-1259-A	4'' pipes installation for Burqa water pipeline from Sta. 1+000 to Sta. 1+100	02/02/15	02/03/15	02/04/15	1	A
	IR-13-00013-DST-1260-A	Bedding for Burqa water pipeline from Sta. 1+000 to Sta. 1+100	02/02/15	02/03/15	02/04/15	1	A
	IR-13-00013-DST-1261-A	Backfilling for Burqa water pipeline from Sta. 1+000 to Sta. 1+100	02/02/15	02/03/15	02/04/15	1	A
	IR-13-00013-DST-1262-A	1. Re-plant cypress tree at Sta. 1+156 2. Removing and storing the material at Sta. 12+130 3. Open the culverts that affected by the project construction 4. Re-installing the traffic sign at Sta. 1+100	02/03/15	02/04/15	02/04/15	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1263-A	1. Fixing the gate of the Kindergartner 2. Re-plant cypress tree at Sta. 1+160 3. Removing and storing material at Sta. 12+130 4. Housekeeping along pipeline from Sta. 0+000 to Sta. 0+600 5. Removing concrete barriers at Sta. 0+450-segment B	02/03/15	02/04/15	02/04/15	0	C
	IR-13-00013-DST-1264-A	1. Re-installing traffic sign at Sta. 0+450 2. Re-plant cypress tree at Sta. 1+150	02/03/15	02/04/15	02/04/15	0	A
	IR-13-00013-DST-1265-A	Excavation for Burqa water pipeline from Sta. 1+100 to Sta. 1+146	02/04/15	02/05/15	02/05/15	0	A
	IR-13-00013-DST-1266-A	4'' pipes installation for Burqa water pipeline from Sta. 1+100 to Sta. 1+146	02/04/15	02/05/15	02/05/15	0	A
	IR-13-00013-DST-1267-A	Bedding for Burqa water pipeline from Sta. 1+100 to Sta. 1+146	02/04/15	02/05/15	02/05/15	0	A
	IR-13-00013-DST-1268-A	Backfilling for Burqa water pipeline from Sta. 1+100 to Sta. 1+146	02/04/15	02/05/15	02/05/15	0	A
	IR-13-00013-DST-1269-A	Welding flanges for combined AV/AR & BFV chamber at Sta. 0+810 in TO 14 (Starting from Feb. 07,2015)	02/05/15	02/08/15	02/09/15	1	C
	IR-13-00013-DST-1270-A	Welding flanges for WO chamber at Sta. 0+090 in TO 14 (Starting from Feb. 07,2015)	02/05/15	02/08/15	02/09/15	1	C
	IR-13-00013-DST-1271-A	Mechanical fittings installation for Silat Al Daher connection at the end of segment C (Starting from Feb. 07,2015)	02/05/15	02/09/15	02/09/15	0	C
	IR-13-00013-DST-1272-A	Milling for RHS shoulder for main road from Sta. 7+370 to Bazzariya connection chamber at Sta. 8+206	02/05/15	02/07/15	02/08/15	1	A
	IR-13-00013-DST-1273-A	Spreading tack coat on milled RHS shoulder for main road from Sta. 7+370 to Bazzariya connection chamber at Sta. 8+206	02/05/15	02/07/15	02/08/15	1	A
	IR-13-00013-DST-1274-A	Asphalt wearing course for RHS shoulder for main road from Sta. 7+370 to Bazzariya connection chamber at Sta. 8+206 (starting from Feb. 07,2015 at 11:00 AM)	02/05/15	02/08/15	02/08/15	0	A
	IR-13-00013-DST-1275-A	Milling for LHS shoulder for main road from Sta. 7+370 to Bazzariya connection chamber at Sta. 8+206	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00013-DST-1276-A	Marking location for Burqa GV chamber at Sta. 1+150 to start excavation	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00013-DST-1277-A	Marking location for Burqa GV chamber at Sta. 1+152 to start excavation	02/07/15	02/07/15	02/08/15	1	A
	IR-13-00013-DST-1278-A	Spreading tack coat on milled LHS shoulder for main road from Sta. 7+370 to Bazzariya connection chamber at Sta. 8+206	02/08/15	02/08/15	02/08/15	0	A
	IR-13-00013-DST-1279-A	Asphalt wearing course for LHS shoulder for main road from Sta. 7+370 to Bazzariya connection chamber at Sta. 8+206	02/08/15	02/08/15	02/09/15	1	A
	IR-13-00013-DST-1280-A	Installation for precast Burqa GV manhole at Sta. 1+150	02/08/15	02/08/15	02/08/15	0	A
	IR-13-00013-DST-1281-A	Installation for precast Burqa GV manhole at Sta. 1+152	02/08/15	02/08/15	02/08/15	0	A
	IR-13-00013-DST-1282-A	Trench excavation from Sta. 0+019.45 to Sta. 0+015.95 to connect pipeline in TO 13 with pipeline in TO14	02/08/15	02/08/15	02/08/15	0	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1283-A	12'' pipes installation from Sta. 0+019.45 to Sta. 0+015.95 to connect pipeline in TO 13 with pipeline in TO14	02/08/15	02/08/15	02/08/15	0	A
	IR-13-00013-DST-1284-A	Cleaning and washing for 4'' Burqa pipeline from Sta. 0+000 to Sta. 1+146	02/08/15	02/08/15	02/08/15	0	A
	IR-13-00013-DST-1285-A	Hydraulic pressure test for 4'' Burqa pipeline PN 25 from Sta. 0+019 to Sta. 1+146 at lowest point Sta. 0+019 (Start reading at 10:00 AM)	02/09/15	02/09/15	02/10/15	1	A
	IR-13-00013-DST-1286-A	Welding flanges for flow monitoring chamber at Sta. 0+340-segment B TO14	02/09/15	02/09/15	02/09/15	0	A
	IR-13-00013-DST-1287-A	Mechanical fittings installation for 4'' Burqa GV chambers at Sta. 1+150 & Sta. 1+152	02/09/15	02/09/15	02/09/15	0	D
	IR-13-00013-DST-1288-A	Trench excavation, pipes installation ,bedding & backfilling for Burqa connections as follow: 1. Connection to Burqa balance tank pipeline 2. Connection to upper Burqa reservoir pipeline 3. Connection new Burqa pipeline to 4'' GV chambers at Sta. 1+150 & Sta. 1+152	02/09/15	02/09/15	02/10/15	1	A
	IR-13-00013-DST-1289-A	Trench excavation from Sta. 0+125.19 to Silat Al Daher connection-segment C	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1290-A	6'' pipes installation from Sta. 0+125.19 to Silat Al Daher connection-segment C	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1291-A	Bedding from Sta. 0+125.19 to Silat Al Daher connection-segment C	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1292-A	Backfilling from Sta. 0+125.19 to Silat Al Daher connection-segment C	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1293-A	Trench excavation for 4'' Burqa pipeline from Sta. 0+019.5 to Burqa connection chamber at Sta. 7+032	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1294-A	Pipes installation for 4'' Burqa pipeline from Sta. 0+019.5 to Burqa connection chamber at Sta. 7+032	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1295-A	Bedding for 4'' Burqa pipeline from Sta. 0+019.5 to Burqa connection chamber at Sta. 7+032	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1296-A	Backfilling for 4'' Burqa pipeline from Sta. 0+019.5 to Burqa connection chamber at Sta. 7+032	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1297-A	Internal finishing work for combined AV/AR & BFV chamber at Sta. 11+187	02/10/15	02/10/15	02/11/15	1	A
	IR-13-00013-DST-1298-A	300 mm pipe bedding & backfilling from Sta. 0+019.54 to Sta. 0+016	02/12/15	02/12/15	02/12/15	0	A
	IR-13-00013-DST-1299-A	Trench excavation, pipes installation, pipes bedding & backfilling for connection of Al funduqumia 4" & 6" gate valves chamber at sta. 1+000 with Reservoir existing pipes lines.	02/12/15	02/14/15	02/15/15	1	C
	IR-13-00013-DST-1299-B	Trench excavation, pipes installation, pipes bedding & backfilling for connection of Al funduqumia 4" & 6" gate valves chamber at sta. 1+000 with Reservoir existing pipes lines.	02/17/15	02/17/15	02/18/15	1	A
	IR-13-00013-DST-1300-A	Trench excavation, pipes installation, pipes bedding & backfilling for connection of sabstaya 10 "gate valve with 8" sabstya existing pipe line.	02/12/15	02/14/15	02/15/15	1	A
	IR-13-00013-DST-1301-A	Mechanical Fittings installation for Bitiba Connection chamber in To# 14, starting on 02/14/2015	02/12/15	02/15/15	02/15/15	0	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1302-A	Welding flanges inside Bitiba Connection chamber in To# 14	02/15/15	02/15/15	02/15/15	0	A
	IR-13-00013-DST-1303-A	Finishing work for internal body (base slab, walls & ceiling) of GV chamber at Sta. 13+617	02/16/15	02/16/15	02/17/15	1	A
	IR-13-00013-DST-1304-A	Installation for precast 6 " GV manhole for Al Foundqumiya at Sta. 0+990	02/16/15	02/16/15	02/17/15	1	A
	IR-13-00013-DST-1305-A	Installation for precast 4 " GV manhole for Al Foundqumiya at Sta. 0+990	02/16/15	02/16/15	02/17/15	1	A
	IR-13-00013-DST-1306-A	Installation for two precast 2 " GV manholes of Al Foundqumiya at Sta. 0+410 & Sta. 0+430	02/16/15	02/16/15	02/17/15	1	A
	IR-13-00013-DST-1307-A	Trench excavation, pipes installation, pipes bedding & backfilling for connection of Sabstaya 10 "gate valve around Sta. 2+960 & BFV chamber at Sta. 2+952 with Sabastiya well pipeline	02/16/15	02/16/15	02/17/15	1	A
	IR-13-00013-DST-1308-A	Cat eyes installation for RHS shoulder of main road from Sta. 1+240 to Sta. 7+370	02/17/15	02/17/15	02/18/15	1	A
	IR-13-00013-DST-1309-A	Sewer pipeline leakage test from MH-01 to MH-02 & from MH-02 to MH-03	02/17/15	02/17/15	02/18/15	1	A
	IR-13-00013-DST-1310-A	Trench excavation, pipes installation, pipes bedding & backfilling for connection of Shavi Shamron flow monitoring chamber at Sta. 1+159 with inlet Shavi Shamron existing pipeline	02/18/15	02/18/15	02/18/15	0	A
	IR-13-00013-DST-1311-A	Trench excavation, pipes installation, pipes bedding & backfilling for connection of BFV chamber at Sta. 1+172 with outlet Shavi Shamron existing pipeline	02/18/15	02/18/15	02/18/15	0	A
	IR-13-00013-DST-1312-A	Sewer pipeline leakage test from MH-03 to MH-04	02/18/15	02/18/15	02/18/15	0	A
	IR-13-00013-DST-1313-A	Disinfection for All project pipelines(starting from Feb. 21,2015 at 8:00 AM)	02/19/15	02/22/15	02/23/15	1	C
	IR-13-00013-DST-1313-B	Disinfection for All project pipelines except 6'' returned water line from Sta. 1+000 to Sta. 0+427(segment B)	02/23/15	02/26/15	02/26/15	0	A
	IR-13-00013-DST-1314-A	Cat eyes installation for LHS shoulder of main road from Sta. 7+360 to Sta. 4+200	02/22/15	02/22/15	02/22/15	0	A
	IR-13-00013-DST-1315-A	Trench excavation, pipes installation, pipes bedding & backfilling to connect main pipeline with Al Naqura existing chamber	02/22/15	02/22/15	02/22/15	0	A
	IR-13-00013-DST-1316-A	Pipes installation to connect Silat Al Daher with reservoir existing inlet pipe	02/22/15	02/22/15	02/22/15	0	A
	IR-13-00013-DST-1317-A	Sewer pipeline leakage test from MH-04 to MH-05	02/22/15	02/22/15	02/22/15	0	A
	IR-13-00013-DST-1318-A	Sewer pipeline leakage test from MH-05 to MH-06	02/22/15	02/22/15	02/22/15	0	A
	IR-13-00013-DST-1319-A	Sewer pipeline leakage test from MH-06 to MH-07	02/22/15	02/22/15	02/22/15	0	A
	IR-13-00013-DST-1320-A	Cat eyes installation for LHS shoulder of main road from Sta. 4+200 to Sta. 1+240	02/23/15	02/23/15	02/23/15	0	A
	IR-13-00013-DST-1321-A	Conduct base course field compaction test for Burqa pipeline from Sta. 1+200 to Sta. 0+650	02/24/15	02/24/15	02/24/15	0	C
	IR-13-00013-DST-1322-A	Conduct base course field compaction test for Burqa pipeline from Sta. 0+650 to Sta. 0+000	02/26/15	02/26/15	02/26/15	0	A
	IR-13-00013-DST-1323-A	Spreading prime coat on finished compacted base course for Burqa pipeline from Sta. 0+000 to Sta. 1+200	02/26/15	02/26/15	02/26/15	0	A
	IR-13-00013-DST-1324-A	Asphalt first layer for Burqa pipeline from Sta. 0+000 to Sta. 1+200	02/26/15	02/26/15	02/26/15	0	C
	IR-13-00013-DST-1325-A	Flushing for 6'' returned water line from Sta. 1+000 to Sta. 0+427(segment B)	02/26/15	02/28/15		PE	

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-12-00005
TASK ORDER #13, Deir Sharaf Main Pipe Line
Inspection Request Log

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Date Inspection Required	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	IR-13-00013-DST-1326-A	Pre-commissioning for Deir Sharaf main pipeline (starting from Feb. 26,2015 at 06:00 PM)	02/26/15	03/05/15		PE	
	IR-13-00013-DST-1327-A	Spreading tack coat for Burqa pipeline from Sta. 0+000 to Sta. 1+200	02/28/15	02/28/15		PE	
	IR-13-00013-DST-1328-A	Asphalt second layer for Burqa pipeline from Sta. 0+000 to Sta. 1+200	02/28/15	02/28/15		PE	
	IR-13-00013-DST-1329-A	Asphalt reinstatement around Al Foundqumiya chambers as followings: • 6'' & 4'' GV chambers at Sta. 0+990 • 2'' chamber t Sta. 0+430 • 2'' chamber at Sta. 0+410	02/28/15	02/28/15		PE	
	IR-13-00013-DST-1330-A	Trench asphalt reinstatement from Sta. 1+174 to Sta. 1+100	02/28/15	02/28/15		PE	
	IR-13-00013-DST-1331-A	Acrylic painting for center of main road from Sta. 1+240 to Sta. 8+200	02/28/15	02/28/15		PE	
	IR-13-00013-DST-1332-A	Cat eyes installation for RHS & LHS shoulders of main road from Sta. 7+370 to Sta. 8+200	02/28/15	02/28/15		PE	
	IR-13-00013-DST-1333-A	Acrylic painting for RHS,LHS shoulders & center of main road from Sta. 8+200 to Sta. 13+700	02/28/15	02/28/15		PE	

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

F | Submittals Log for the Reporting Period

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, DER SHARAF WATER PIPELINE
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Returne Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00013-DST-001-A	Scheduling Qualification Submittal	DST	P	12/08/13	01/07/14	12/22/13	14	A
	SUB-13-00013-DST-002-A	Bank Guarantee	DST	P	12/08/13	01/07/14	12/31/13	23	E
	SUB-13-00013-DST-003-A	Submittals Schedule	DST	P	12/19/13	01/18/14	01/07/14	19	C
	SUB-13-00013-DST-003-B	Submittals Schedule	DST	P	01/23/14	02/22/14	02/04/14	12	B
	SUB-13-00013-DST-004-A	Subcontracting Plan	DST	P	12/22/13	01/21/14	12/31/13	9	E
	SUB-13-00013-DST-005-A	60-Day Schedule of Operation	DST	P	12/22/13	01/21/14	12/31/13	9	B
	SUB-13-00013-DST-006-A	Overview Bar chart & Master Plan	DST	P	12/22/13	01/21/14	12/31/13	9	A
	SUB-13-00013-DST-007-A	Testing Labs	DST	P	12/23/13	01/22/14	01/02/14	10	B
	SUB-13-00013-DST-008-A	CMC Field Office Location and Layout	DST	P	12/23/13	01/22/14	12/31/13	8	B
	SUB-13-00013-DST-009-A	Insurances: Contractors all Risk Insurance, Amendment No. 1, Commercial General Liability, Vehicle Insurance, and Workmen's Compensation Policy, 2013.	DST	P	12/25/13	01/24/14	01/07/14	13	E
	SUB-13-00013-DST-010-A	Proposed Dumping Site, Storage and Staging Area	DST	P	12/25/13	01/24/14	12/31/13	6	B
	SUB-13-00013-DST-011-A	Field Offices Furniture and Equipment List	DST	P	12/25/13	01/24/14	12/31/13	6	B
	SUB-13-00013-DST-012-A	Branding Plan	DST	P	12/25/13	01/24/14	01/09/14	15	E
	SUB-13-00013-DST-013-A	Quality Control Plan (QCP)	DST	P	12/25/13	01/24/14	01/13/14	19	B
	SUB-13-00013-DST-014-A	Steel Pipes and Fittings, 6" to 12" - Middle East Tube Company Ltd, BOQ items 2.1.1 and 2.1.2	DST	M	12/25/13	01/24/14	01/05/14	11	B
	SUB-13-00013-DST-015-A	Key Personnel Plan	DST	P	12/25/13	01/24/14	12/31/13	6	E
	SUB-13-00013-DST-016-A	Safety Plan	DST	P	12/25/13	01/24/14	01/13/14	19	C
	SUB-13-00013-DST-016-B	Safety Plan	DST	P	01/16/14	02/15/14	01/20/14	4	B
	SUB-13-00013-DST-017-A	Security System	DST	P	12/29/13	01/28/14	01/05/14	7	C
	SUB-13-00013-DST-017-B	Security System	DST	P	01/16/14	02/15/14	01/16/14	0	B
	SUB-13-00013-DST-018-A	Method Statement	DST	P	12/29/13	01/28/14	01/09/14	11	C
	SUB-13-00013-DST-018-B	Method Statement	DST	P	01/21/14	02/20/14	01/23/14	2	B
	SUB-13-00013-DST-019-A	Construction Time Schedule	DST	P	12/29/13	01/28/14	01/07/14	9	C
	SUB-13-00013-DST-019-B	Original CPM Construction Schedule	DST	P	01/23/14	02/22/14	02/04/14	12	C
	SUB-13-00013-DST-019-C	Original CPM Construction Schedule	DST	P	02/16/14	03/18/14	02/25/14	9	A
	SUB-13-00013-DST-020-A	Temporary and Permanent Sign -text and fabrication	DST	P	12/30/13	01/29/14	12/31/13	1	B
	SUB-13-00013-DST-021-A	Coordination with Local Authorities Plan and List of Permits and Licenses	DST	P	12/30/13	01/29/14	01/09/14	10	B
	SUB-13-00013-DST-022-A	Environmental Mitigation Plan	DST	P	12/30/13	01/29/14	01/09/14	10	B
	SUB-13-00013-DST-023-A	Dilapidation Survey - Segments A, B and C	DST	P	01/02/14	02/01/14	01/12/14	10	B
	SUB-13-00013-DST-024-A	FIP Deir Sharaf_Fittings &heat shrinkable sheet	DST	M	01/05/14	02/04/14	01/13/14	8	B
	SUB-13-00013-DST-025-A	Survey Plan from Sta.A0+000 to Sta.A13+720 -Segment A	DST	P	01/02/14	02/01/14	01/13/14	11	B
	SUB-13-00013-DST-026-A	Traffic Control Plan Phase I	DST	P	01/05/14	02/04/14	01/16/14	11	B
	SUB-13-00013-DST-027-A	Bedding and Backfilling Material Source- Abu Khanfa Crusher	DST	M	01/15/14	02/14/14	01/20/14	5	B
	SUB-13-00013-DST-028-A	Bedding and Backfilling Material Source- Abu Shusha Crusher	DST	M	01/15/14	02/14/14	01/20/14	5	B
	SUB-13-00013-DST-029-A	Bedding and Backfilling Material Source- Al Ashaqar Crusher	DST	M	01/15/14	02/14/14	01/20/14	5	B
	SUB-13-00013-DST-030-A	Avrot Pipe Fittings_up to 12 inch	DST	M	01/16/14	02/15/14	01/23/14	7	C
	SUB-13-00013-DST-030-B	Avrot Pipe Fittings_up to 12 inch	DST	M	02/04/14	03/06/14	02/09/14	5	B
	SUB-13-00013-DST-031-A	Butterfly Valves- Venessa- PN 40-BOQ items No. 3.2.2,3.2.4,3.2.5,3.3.1 and 3.3.2	DST	M	01/20/14	02/19/14	01/26/14	6	B
	SUB-13-00013-DST-032-A	Gate Valves PN 40- Raphael Valves Industries- TMS-BOQ items No. 3.1.1,2-3.2.1,2,3,6,7,8,9,10,11-3.4.1,2 and 3.5.1,2,3	DST	M	01/20/14	02/19/14	01/26/14	6	B
	SUB-13-00013-DST-033-A	Dismantling Joint PN 40- Unijoint -BOQ items No. 3.1.1,2-3.2.1,2,3,4,5,6,7,8,9,10,11-3.3.1,2-3.4.1,2-3.5.1,2,3 and 3.6.1	DST	M	01/20/14	02/19/14	01/28/14	8	B
	SUB-13-00013-DST-034-A	Proposed Welders for welders qualification test - CVs	DST	P	01/20/14	02/19/14	01/26/14	6	B
	SUB-13-00013-DST-035-A	Proposed Storage & Staging Yard	DST	P	01/21/14	02/20/14	01/22/14	1	B
	SUB-13-00013-DST-036-A	Identification Tape for water pipeline	DST	M	01/21/14	02/20/14	01/22/14	1	B
	SUB-13-00013-DST-037-A	Welding Procedure for 3”-12”	DST	P	01/23/14	02/22/14	01/26/14	3	C
	SUB-13-00013-DST-037-B	Welding Procedure for 3”-12”	DST	P	03/16/14	04/15/14	03/20/14	4	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, DER SHARAF WATER PIPELINE
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Returne Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00013-DST-038-A	Water Quality Testing Lab-Scientific Center Co. for Food & Drug Analysis	DST	P	01/23/14	02/22/14	01/26/14	3	C
	SUB-13-00013-DST-038-B	Water Quality Testing Lab-Birzeit University Testing Laboratories	DST	P	11/09/14	12/09/14	11/18/14	9	B
	SUB-13-00013-DST-039-A	Prime Coat Emulsion -Pazkar Ltd.-item No. 3.01	DST	M	01/23/14	02/22/14	01/26/14	3	B
	SUB-13-00013-DST-040-A	Tack Coat Emulsion -Pazkar Ltd.-item No. 3.02	DST	M	01/23/14	02/22/14	01/26/14	3	B
	SUB-13-00013-DST-041-A	Cold Bituminous material (Nito proof 230) as external isolation for concrete chambers	DST	M	01/26/14	02/25/14	01/26/14	0	B
	SUB-13-00013-DST-042-A	Tyco ball valves 150mm -item No. 3.3.1 and 3.3.2	DST	M	01/26/14	02/25/14	01/30/14	4	B
	SUB-13-00013-DST-043-A	Tyco Ball Valves- DN 50&80 -item No. 3.2.1,3,6,7,8,9,10,11 and 3.6.1	DST	M	01/26/14	02/25/14	01/30/14	4	B
	SUB-13-00013-DST-044-A	Risk Management Program	DST	P	01/26/14	02/25/14	02/04/14	9	B
	SUB-13-00013-DST-045-A	Elecometer 266 Holiday detector	DST	M	01/26/14	02/25/14	01/30/14	4	E
	SUB-13-00013-DST-046-A	Third party testing lab -Arc-Eyes	DST	P	01/26/14	02/25/14	01/30/14	4	B
	SUB-13-00013-DST-047-A	Combination Air Release Valve-PN 40-DN50-ARI-D015-item No.3.2.1,3,6,7,8,9,10	DST	M	01/27/14	02/26/14	02/02/14	6	B
	SUB-13-00013-DST-048-A	Air Release Valve-PN 40-DN25-ARI-S015-item No. 3.2.11	DST	M	01/27/14	02/26/14	01/30/14	3	B
	SUB-13-00013-DST-049-A	Combination Air Release Valve Non Slam -PN 40-DN100-ARI-D-065 NS-item No. 3.4.1,2	DST	M	01/27/14	02/26/14	02/02/14	6	B
	SUB-13-00013-DST-050-A	Manhole cover & frame (clear opening 750 mm)	DST	M	01/27/14	02/26/14	01/30/14	3	B
	SUB-13-00013-DST-051-A	Cost break down	DST	P	01/27/14	02/26/14	02/23/14	27	D
	SUB-13-00013-DST-051-B	Cost break down	DST	P	04/03/14	05/03/14	04/16/14	13	E
	SUB-13-00013-DST-052-A	Strainer-Bermad_PN 40-item No. 3.2.1,2,3,4,5,6,7,8,9,10,11	DST	M	01/27/14	02/26/14	01/30/14	3	B
	SUB-13-00013-DST-053-A	Public Relation Plan	DST	P	01/27/14	02/26/14	01/30/14	3	E
	SUB-13-00013-DST-054-A	1/2" Asphalt wearing course JMF	DST	M	01/28/14	02/27/14	02/06/14	9	C
	SUB-13-00013-DST-055-A	3/4" Asphalt wearing course JMF	DST	M	01/28/14	02/27/14	02/06/14	9	B
	SUB-13-00013-DST-056-A	Flanged Coupling Adaptor- UniJoint-item No. 3.3.1 & 3.3.2	DST	M	01/29/14	02/28/14	02/04/14	6	D
	SUB-13-00013-DST-056-B	Flanged Coupling Adaptor- UniJoint-item No. 3.3.1 & 3.3.2	DST	M	12/08/14	01/07/15	12/11/14	3	E
	SUB-13-00013-DST-057-A	Concrete Mix Ready -Bonyan Ready mix plant	DST	M	01/30/14	03/01/14	02/06/14	7	B
	SUB-13-00013-DST-058-A	Concrete Mix Ready -Muwasi Ready mix plant	DST	M	01/30/14	03/01/14	02/06/14	7	B
	SUB-13-00013-DST-059-A	Branding Plan-Approved Flyer Text (Arabic & English)	DST	P	01/30/14	03/01/14	02/05/14	6	E
	SUB-13-00013-DST-060-A	Pipe Flanges- ISO/DIN Flanges	DST	M	01/30/14	03/01/14	02/04/14	5	B
	SUB-13-00013-DST-061-A	Pressure Relief Valve- Bermad- 83Q - item No. 3.2.1,3,6,7,8,9,10,11	DST	M	01/30/14	03/01/14	02/04/14	5	B
	SUB-13-00013-DST-062-A	Method statement for Repairing pipes cement mortar lining	DST	M	02/02/14	03/04/14	02/20/14	18	C
	SUB-13-00013-DST-062-B	Method statement for Repairing pipes cement mortar lining	DST	M	04/02/14	05/02/14	04/16/14	14	B
	SUB-13-00013-DST-063-A	Shop Drawings: 12" Main Pipeline: Plan, Profile and Cross Section from Sta.10+400 to Sta.12+120	DST	S	02/02/14	03/04/14	02/12/14	10	C
	SUB-13-00013-DST-063-B	Shop Drawings: 12" Main Pipeline: Plan, Profile and Cross Section from Sta.10+400 to Sta.12+120	DST	S	02/25/14	03/27/14	03/12/14	15	C
	SUB-13-00013-DST-063-C	Shop Drawings: 12" Main Pipeline: Plan, Profile and Cross Section from Sta.10+400 to Sta.12+120	DST	S	03/23/14	04/22/14	04/09/14	17	A
	SUB-13-00013-DST-064-A	UPVC Pipes Manufactures Data Sheet(UPVC 12" SN 8)	DST	M	02/02/14	03/04/14	02/04/14	2	B
	SUB-13-00013-DST-065-A	Reinforcement Steel Manufactures Data Sheets (Israeli & Turkey products)	DST	M	02/02/14	03/04/14	02/06/14	4	B
	SUB-13-00013-DST-066-A	Chambers Formwork Design Calculation	DST	S	02/05/14	03/07/14	02/12/14	7	E
	SUB-13-00013-DST-067-A	Field Offices Furniture and Equipment List Amendment (For Submittal No.: SUB-13-00013-DST-011-A)	DST	P	02/05/14	03/07/14	02/12/14	7	B
	SUB-13-00013-DST-068-A	Proposed Welders for welders qualification test - CVs	DST	P	02/10/14	03/12/14	02/16/14	6	C
	SUB-13-00013-DST-068-B	Proposed Welders for welders qualification test - CVs	DST	P	02/24/14	03/26/14	02/27/14	3	B
	SUB-13-00013-DST-069-A	Pressure Reducing Valves PN 40- Bermad- Specification Ref: 15217: 2.1&2.2 and 15200, BOQ itemd 3.2.1, 3.2.3, 3.2.6, 3.2.7, 3.2.8, 3.2.9, and 3.2.10	DST	M	02/10/14	03/12/14	02/16/14	6	C
	SUB-13-00013-DST-069-B	Pressure Reducing Valves PN 40- Bermad- Specification Ref: 15217: 2.1&2.2 and 15200, BOQ itemd 3.2.1, 3.2.3, 3.2.6, 3.2.7, 3.2.8, 3.2.9, and 3.2.10	DST	M	03/16/14	04/15/14	04/02/14	17	B
	SUB-13-00013-DST-070-A	Flow Control Valves PN 40- Bermad-Specification Ref: 15217: 2.1&2.2 and 15200,BOQ item 3.2.1, 3.2.3, 3.2.6, 3.2.7, 3.2.8, 3.2.9, 3.2.10,3.2.11 and 3.6.1	DST	M	02/10/14	03/12/14	02/20/14	10	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, DER SHARAF WATER PIPELINE
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Returne Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00013-DST-070-B	Manufacturer "Bermad" sizing of Deir Sharaf Flow Control Valves **-For Engineering Record**	DST	M	06/17/14	07/17/14	07/01/14	14	C
	SUB-13-00013-DST-070-C	Manufacturer "Bermad" sizing of Deir Sharaf Flow Control Valves **-For Engineering Record**	DST	M	09/02/14	10/02/14	09/16/14	14	B
	SUB-13-00013-DST-071-A	Mitered Bends Fabrication	DST	M	02/13/14	03/15/14	02/20/14	7	B
	SUB-13-00013-DST-072-A	Hijjawi Construction Labs –modified Accreditation Schedule Certificate-Amendment for Submittal No.:SUB-13-00013-DST-007-A)	DST	P	02/13/14	03/15/14	02/20/14	7	B
	SUB-13-00013-DST-073-A	GMT Labs' profile & Accreditation certificate for Manhole cover testing	DST	P	02/13/14	03/15/14	02/20/14	7	B
	SUB-13-00013-DST-074-A	Pipeline trenching method statement	DST	P	02/13/14	03/15/14	03/03/14	18	C
	SUB-13-00013-DST-074-B	Pipeline trenching method statement	DST	P	03/23/14	04/22/14	04/02/14	10	B
	SUB-13-00013-DST-075-A	Pipe Installation method statement	DST	P	02/16/14	03/18/14	03/02/14	14	B
	SUB-13-00013-DST-076-A	Heat Shrinkable Sleeve &Tape (CANUSA) for steel pipes-BOQ item No. 2.1.1 and 2.1.2	DST	M	02/18/14	03/20/14	02/23/14	5	B
	SUB-13-00013-DST-077-A	Galvanized Malleable Iron Fittings up to 2"- Modgal	DST	M	02/18/14	03/20/14	02/20/14	2	B
	SUB-13-00013-DST-078-A	3 inch Procedure Qualification Record (PQR)	DST	M	02/20/14	03/22/14	02/26/14	6	B
	SUB-13-00013-DST-079-A	28 days concrete strength results for Concrete Mix design _BONYAN READY -MIX PLANT)	DST	M	02/20/14	03/22/14	02/26/14	6	A
	SUB-13-00013-DST-080-A	28 days concrete strength results for Concrete mix design _MUWASI READY -MIX PLANT)	DST	M	02/20/14	03/22/14	02/26/14	6	A
	SUB-13-00013-DST-081-A	Flange Gaskets_Klinger	DST	M	02/20/14	03/22/14	02/25/14	5	C
	SUB-13-00013-DST-081-B	Flange Gaskets_Reinz AFM34 FDA	DST	M	03/09/14	04/08/14	03/10/14	1	C
	SUB-13-00013-DST-081-C	Flange Gaskets_Reinz AFM 34	DST	M	05/19/14	06/18/14	05/28/14	9	C
	SUB-13-00013-DST-081-D	Flange Gaskets_Reinz AFM 34	DST	M	12/08/14	01/07/15	12/11/14	3	A
	SUB-13-00013-DST-082-A	Wash out Flap Valves-ARI -BOQ item No. 3.5.1 and 3.5.2	DST	M	02/20/14	03/22/14	02/25/14	5	B
	SUB-13-00013-DST-083-A	Concrete Curing methods	DST	M	02/24/14	03/26/14	03/13/14	17	B
	SUB-13-00013-DST-084-A	Method Statement for Filling & Repair The Conical Tie Rods Holes In The Concrete	DST	M	02/24/14	03/26/14	03/13/14	17	B
	SUB-13-00013-DST-085-A	Check Valve- B.O.Q- item No. 3.2.1, 3.2.2, 3.2.3, 3.2.4, 3.2.5, 3.2.6, 3.2.7, 3.2.8, 3.2.9, 3.2.10	DST	M	03/02/14	04/01/14	03/03/14	1	B
	SUB-13-00013-DST-086-A	Concrete & Plastic Supports/Spacers sample for plastic is attached	DST	M	03/02/14	04/01/14	03/18/14	16	B
	SUB-13-00013-DST-087-A	Concrete Formwork Tie Rods For Manholes' walls/Sample	DST	M	03/04/14	04/03/14	03/18/14	14	B
	SUB-13-00013-DST-088-A	Radiographic Testing Safety Plan	DST	P	03/04/14	04/03/14	03/16/14	12	C
	SUB-13-00013-DST-088-B	Radiographic Testing Safety Plan	DST	P	03/25/14	04/24/14	04/02/14	8	B
	SUB-13-00013-DST-089-A	Casing (Sleeve) For Water Pipe line Crossing Main Asphalted Road & Israeli Roads	DST	M	03/05/14	04/04/14	03/18/14	13	D
	SUB-13-00013-DST-089-B	Casing (Sleeve) For Water Pipe line Crossing Main Asphalted Road & Israeli Roads	DST	M	03/30/14	04/29/14	04/16/14	17	B
	SUB-13-00013-DST-090-A	Updated Construction Schedule & S-Curve-February 28, 2014	DST	SCH	03/05/14	04/04/14	03/16/14	11	B
	SUB-13-00013-DST-091-A	Concrete Formwork Chamfers For Exterior Corners Members	DST	M	03/05/14	04/04/14	03/18/14	13	A
	SUB-13-00013-DST-092-A	Certificate for Welder –Emad abu Zaineh-Amendment (For Submittal No.SUB-13-00013-DST-068-B)	DST	P	03/05/14	04/04/14	03/19/14	14	C
	SUB-13-00013-DST-092-B	Certificate for Welder –Emad abu Zaineh-Amendment (For Submittal No.SUB-13-00013-DST-068-B)	DST	P	08/07/14	09/06/14	08/12/14	5	A
	SUB-13-00013-DST-093-A	Proposed Welders for welders qualification test - CVs	DST	P	03/05/14	04/04/14	03/10/14	5	B
	SUB-13-00013-DST-094-A	6 inch and over Procedure Qualification Record (PQR)	DST	P	03/05/14	04/04/14	03/09/14	4	C
	SUB-13-00013-DST-094-B	6 inch and over Procedure Qualification Record (PQR) and Welding Procedure Specification (WPS).	DST	P	03/16/14	04/15/14	03/20/14	4	B
	SUB-13-00013-DST-095-A	8-12 inch Procedure Qualification Record (PQR)	DST	P	03/05/14	04/04/14	03/09/14	4	C
	SUB-13-00013-DST-095-B	8-12 inch Procedure Qualification Record (PQR)	DST	P	03/16/14	04/15/14	03/20/14	4	A
	SUB-13-00013-DST-096-A	Supply of water pipes and fittings -FIP Co.	DST	M	03/09/14	04/08/14	03/12/14	3	C
	SUB-13-00013-DST-096-B	Supply of water pipes and fittings -FIP Co.	DST	M	03/16/14	04/15/14	03/19/14	3	B
	SUB-13-00013-DST-097-A	Mill certificate & Technical reports for 12" pipe- ERW inspected on Mar,6.2014 at Middle East Factory	DST	M	03/11/14	04/10/14	03/20/14	9	B
	SUB-13-00013-DST-098-A	Finish paint for exposed pipes/fittings and pipes/fittings inside chambers_ FOSROC_Nitocote EP405	DST	M	03/13/14	04/12/14	03/20/14	7	C
	SUB-13-00013-DST-098-B	Finish paint for exposed pipes/fittings and pipes/fittings inside chambers_ FOSROC_Nitocote EP405	DST	M	03/23/14	04/22/14	03/30/14	7	B
	SUB-13-00013-DST-099-A	Radiographic Testing (RT) Method Statement	DST	P	03/16/14	04/15/14	03/20/14	4	B
	SUB-13-00013-DST-100-A	Steel ASTM A 53-Gr B , ERW Welded Pipes- Borusan/Tzinorot -B.O.Q-Item No. 2.1.1 **(Pipe on shelf)**	DST	M	03/27/14	04/26/14	04/02/14	6	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, DER SHARAF WATER PIPELINE
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Returne Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00013-DST-100-B	Steel ASTM A 53-Gr B , ERW Welded Pipes- Borusan/Tzinorot -B.O.Q-Item No. 2.1.1 **(Pipe on shelf)**	DST	M	04/10/14	05/10/14	04/14/14	4	B
	SUB-13-00013-DST-101-A	Steel ASTM A 53-Gr B , ERW Welded Pipes- Toscelik /Tzinorot- B.O.Q item No. 2.1.1, 2.1.2	DST	M	03/16/14	04/15/14	03/20/14	4	C
	SUB-13-00013-DST-101-B	Steel ASTM A 53-Gr B , ERW Welded Pipes- Toscelik /Tzinorot- B.O.Q item No. 2.1.1, 2.1.2	DST	M	04/03/14	05/03/14	04/13/14	10	B
	SUB-13-00013-DST-102-A	Galvanized steel pipes_Pecker	DST	M	03/20/14	04/19/14	03/24/14	4	B
	SUB-13-00013-DST-103-A	Bolts, Nuts& washers-Factor for Mechanical Chamber.	DST	M	03/23/14	04/22/14	03/30/14	7	C
	SUB-13-00013-DST-103-B	Bolts, Nuts& washers-Factor for Mechanical Chamber.	DST	M	04/02/14	05/02/14	04/09/14	7	C
	SUB-13-00013-DST-103-C	Bolts, Nuts& washers-Factor for Mechanical Chamber.	DST	M	04/28/14	05/28/14	05/05/14	7	B
	SUB-13-00013-DST-104-A	Shop Drawings: 12" Main Pipeline: Plan, Profile and Cross Section from Sta.9+700 to Sta.10+403	DST	S	03/23/14	04/22/14	04/09/14	17	B
	SUB-13-00013-DST-105-A	Welders Test results and Performance Qualification Certificate.Mr. Yahia Kadous and Mr. Nabil Ali	DST	P	04/15/14	05/15/14	04/28/14	13	B
	SUB-13-00013-DST-106-A	Welders Performance Qualification Certificate	DST	P	03/27/14	04/26/14	04/13/14	17	C
	SUB-13-00013-DST-106-B	Welders Performance Qualification Certificate- RT-Negative Films are attached	DST	P	08/07/14	09/06/14	08/12/14	5	A
	SUB-13-00013-DST-107-A	Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 9+700 to 12+120	DST	S	03/27/14	04/26/14	04/14/14	18	C
	SUB-13-00013-DST-107-B	Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 9+700 to 12+120	DST	S	04/28/14	05/28/14	05/14/14	16	C
	SUB-13-00013-DST-107-C	Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 9+700 to 12+120	DST	S	05/28/14	06/27/14	06/09/14	12	B
	SUB-13-00013-DST-108-A	Approved Temporary Traffic Plan by DCL (Area C)	DST	P	04/02/14	05/02/14	04/15/14	13	B
	SUB-13-00013-DST-109-A	Updated Construction Schedule & S-Curve-March 31,2014	DST	SCH	04/06/14	05/06/14	04/15/14	9	B
	SUB-13-00013-DST-110-A	Shop Drawings: 12" Main Pipeline Plan,Profile From St.12+120 To St.13+580	DST	S	04/08/14	05/08/14	04/17/14	9	B
	SUB-13-00013-DST-110-B	Shop Drawings: 12" Main Pipeline Plan,Profile From St.12+120 To St.13+580-**For Engineering Record**	DST	S	04/28/14	05/28/14	04/30/14	2	A
	SUB-13-00013-DST-111-A	Electro-Magnetic water meter-Siemens- PN 40- B.O.Q- item No. 3.2.1,DN 80-50, 3.2.2,DN 250-150, 3.2.3 DN 100-80, 3.2.4, 3.2.5 DN 300, 3.2.6 DN 80, 3.2.7 DN 100-80, 3.2.8 DN 80, 3.2.9 DN 150-100, 3.2.10 DN 100 & 3.2.11 DN50.	DST	M	04/21/14	05/21/14	05/06/14	15	C
	SUB-13-00013-DST-111-B	Electro-Magnetic water meter-Siemens- PN 40- B.O.Q- item No. 3.2.1,DN 80-50, 3.2.2,DN 250-150, 3.2.3 DN 100-80, 3.2.4, 3.2.5 DN 300, 3.2.6 DN 80, 3.2.7 DN 100-80, 3.2.8 DN 80, 3.2.9 DN 150-100, 3.2.10 DN 100 & 3.2.11 DN50.	DST	M	06/09/14	07/09/14	06/09/14	0	B
	SUB-13-00013-DST-112-A	Shop Drawings: 12" Main Pipeline Plan,Profile For Segment" B" From St.0+000 To St.0+998	DST	S	04/28/14	05/28/14	05/21/14	23	B
	SUB-13-00013-DST-112-B	Shop Drawings: 6" Main Pipeline Plan,Profile For Segment" B" From St.0+000 To St.0+998-**For Engineering Record**	DST	S	08/06/14	09/05/14	08/20/14	14	A
	SUB-13-00013-DST-113-A	Concrete Mix Design for Me'mar Ready-mix Plant	DST	M	04/30/14	05/30/14	05/05/14	5	B
	SUB-13-00013-DST-114-A	Updated Construction Schedule & S-Curve-April 30,2014	DST	SCH	05/04/14	06/03/14	05/14/14	10	B
	SUB-13-00013-DST-115-A	Shop Drawings: 12" Main Pipeline Plan,Profile From St.13+560 To St.13+725	DST	S	05/06/14	06/05/14	05/21/14	15	B
	SUB-13-00013-DST-116-A	Hubbed slip on flanges for welding (Alternative)	DST	M	05/08/14	06/07/14	05/18/14	10	B
	SUB-13-00013-DST-117-A	Stainless Steel Chocks & Materials for Filling Annular Space With Non-Shrink Grout	DST	M	05/08/14	06/07/14	05/27/14	19	B
	SUB-13-00013-DST-118-A	Pressure Gauge- Ashcroft 1279	DST	M	05/12/14	06/11/14	05/18/14	6	C
	SUB-13-00013-DST-118-B	Pressure Gauge- Ashcroft 1279	DST	M	08/20/14	09/19/14	08/21/14	1	B
	SUB-13-00013-DST-119-A	Shop Drawings: 12" Main Pipeline Plan,Profile From St.5+000 To St.7+010	DST	S	05/12/14	06/11/14	05/27/14	15	B
	SUB-13-00013-DST-119-B	Shop Drawings: 12" Main Pipeline Plan,Profile From St.5+000 To St.7+010 -**For Engineering Record**	DST	S	06/05/14	07/05/14	06/09/14	4	A
	SUB-13-00013-DST-120-A	Testing Labs-Renewed Accreditation Certificate and Schedule (For Hijjawi Construction Labs-Amendment for Submittal No.:SUB-13-00013-DST-007-A) & (SUB-13-00013-DST-072-A)	DST	P	05/22/14	06/21/14	05/28/14	6	A
	SUB-13-00013-DST-121-A	Strainer- alternative-Dier Sharaf - PN 40 - B.O.Q-item No. 3.2.1, 3.2.2, 3.2.3, 3.2.4, 3.2.5, 3.2.6, 3.2.7, 3.2.8, 3.2.9, 3.2.10, 3.2.11	DST	M	06/01/14	07/01/14	06/05/14	4	B
	SUB-13-00013-DST-122-A	Precast Manhole for Washout , Air vent & release Manhole –Palestinian Construction Products LTD.	DST	M	05/29/14	06/28/14	06/11/14	13	C
	SUB-13-00013-DST-122-B	Precast Manhole for Washout , Air vent & release Manhole –Palestinian Construction Products LTD.	DST	M	6/24/2014	07/24/14	07/22/14	28	B
	SUB-13-00013-DST-123-A	Shop Drawings: 12" Main Pipeline Plan,Profile From St.2+900 To St.5+000	DST	S	06/01/10	07/01/10	06/12/14	1472	B
	SUB-13-00013-DST-124-A	Revised Construction Schedule & S-Curve (May 31, 2014)	DST	SCH	06/05/14	07/05/14	06/22/14	17	B
	SUB-13-00013-DST-124-B	Revised Construction Schedule & S-Curve (May 31, 2014)-F**or Engineering Record**	DST	SCH	06/29/14	07/29/14	07/07/14	8	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, DER SHARAF WATER PIPELINE
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Returne Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00013-DST-125-A	Pressure Reducing Valves_ Asasa chamber_ PN 40_Bermad	DST	M	06/17/14	07/17/14	06/26/14	9	B
	SUB-13-00013-DST-126-A	Shop Drawings: Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 5+000 to Sta. 7+000 & from Sta.12+000 to 13+700	DST	S	06/08/14	07/08/14	06/12/14	4	B
	SUB-13-00013-DST-127-A	Shop Drawings: 12" Main Pipeline Plan,Profile From St.1+100 To St.2+900	DST	S	06/10/14	07/10/14	07/01/14	21	B
	SUB-13-00013-DST-128-A	Project Grid Elevation for Cut Slope Area from Sta. 00+000 To Sta. 06+770	DST	S	06/15/14	07/15/14	07/03/14	18	B
	SUB-13-00013-DST-129-A	Shop Drawings: Structural & Mechanical detail for SELIT ALDAHER & ALASASA Connection Chambers	DST	S	06/15/14	07/15/14	07/02/14	17	C
	SUB-13-00013-DST-129-B	**Structural & Mechanical detail for:** - SELIT ALDAHER Chamber at Sta.10+420 -ALASASA Connection Chamber at Sta.13+600.	DST	S	07/23/14	08/22/14	08/06/14	14	B
	SUB-13-00013-DST-130-A	Pressure Gauge-Wika- (Alternative)	DST	M	06/19/14	07/19/14	07/01/14	12	C
	SUB-13-00013-DST-130-B	Pressure Gauge-Wika- (Alternative)	DST	M	12/08/14	01/07/15	12/11/14	3	E
	SUB-13-00013-DST-131-A	Updated Construction Schedule & S-Curve-June 30,2014	DST	SCH	07/06/14	08/05/14	07/10/14	4	B
	SUB-13-00013-DST-132-A	Stainless Steel Bolts (Alternative)	DST	M	07/13/14	08/12/14	08/03/14	21	D
	SUB-13-00013-DST-132-B	Stainless Steel Bolts (Alternative)	DST	M	12/08/14	01/07/15	12/11/14	3	E
	SUB-13-00013-DST-133-A	Work Zone Traffic Control and Operations at Night (Specific Night Work Safety Plan)	DST	P	07/13/14	08/12/14	08/03/14	21	E
	SUB-13-00013-DST-134-A	Shop Drawings: 12" Main Pipeline Plan,Profile From St.7+020 to St.9+700	DST	S	07/14/14	08/13/14	08/04/14	21	B
	SUB-13-00013-DST-135-A	Drainage Proposal for gate valve Sta. 10+461.	DST	S	07/14/14	08/13/14	07/20/14	6	B
	SUB-13-00013-DST-136-A	Shop Drawings: Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 2+000 to 5+000	DST	S	07/22/14	08/21/14	08/12/14	21	C
	SUB-13-00013-DST-136-B	Shop Drawings: Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 2+000 to 5+000	DST	S	09/24/14	10/24/14	10/15/14	21	C
	SUB-13-00013-DST-136-C	Shop Drawings: Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 2+000 to 5+000	DST	S	11/17/14	12/17/14	11/24/14	7	A
	SUB-13-00013-DST-137-A	Structural & Mechanical detail for valve chambers for (Water Pipeline) for Seg. B	DST	S	07/22/14	08/21/14	08/12/14	21	B
	SUB-13-00013-DST-138-A	Structural analysis for gate valve chamber walls.	DST	M	07/23/14	08/22/14	08/04/14		B
	SUB-13-00013-DST-139-A	Structural & Mechanical detail for valve chambers for (Water Pipeline) From Sta. 1+000 to 2+900 & From Sta. 7+000 to Sta.9+000	DST	S	08/03/14	09/02/14	08/21/14	18	B
	SUB-13-00013-DST-140-A	**Structural & Mechanical detail for:** Al-Foundqumieh & Sabastiya connection chamber.	DST	S	08/04/14	09/03/14	08/12/14	8	C
	SUB-13-00013-DST-140-B	**Structural & Mechanical detail for:** Al-Foundqumieh & Sabastiya connection chamber.	DST	S	08/27/14	09/26/14	08/28/14	1	B
	SUB-13-00013-DST-141-A	Updated Construction Schedule & S-Curve-July 31,2014	DST	SCH	08/05/14	09/04/14	08/14/14	9	B
	SUB-13-00013-DST-142-A	Shop Drawings: Structural & Mechanical detail for Bizzariya connection chamber @ Sta.8+230	DST	S	08/12/14	09/11/14	08/25/14	13	C
	SUB-13-00013-DST-142-B	Shop Drawings: Structural & Mechanical detail for Bizzariya connection chamber @ Sta.8+230	DST	S	09/04/14	10/04/14	09/10/14	6	B
	SUB-13-00013-DST-143-A	Shop Drawings: Structural & Mechanical detail for Burqa connection chamber @ Sta.7+032	DST	S	08/12/14	09/11/14	08/25/14	13	C
	SUB-13-00013-DST-143-B	Shop Drawings: Structural & Mechanical detail for Burqa connection chamber @ Sta.7+032	DST	S	09/04/14	10/04/14	09/10/14	6	B
	SUB-13-00013-DST-144-A	Shop Drawings: Structural & Mechanical detail for Flow Water Meter connection chamber @ Sta.7+180	DST	S	08/12/14	09/11/14	08/28/14	16	C
	SUB-13-00013-DST-144-B	Structural & Mechanical detail for Flow Water Meter connection chamber @ Sta.7+180	DST	S	09/04/14	10/04/14	09/15/14	11	B
	SUB-13-00013-DST-145-A	Adjustable support for pipes & Fittings inside chambers	DST	M	08/19/14	09/18/14	08/28/14	9	C
	SUB-13-00013-DST-145-B	Adjustable support for pipes & Fittings inside chambers	DST	M	09/10/14	10/10/14	09/16/14	6	B
	SUB-13-00013-DST-146-A	Ball Valve-Tyco F120 for Pressure Gauge	DST	M	08/27/14	09/26/14	08/27/14	0	B
	SUB-13-00013-DST-147-A	Galvanized Manhole ladder	DST	M	08/27/14	09/26/14	08/31/14	4	C
	SUB-13-00013-DST-147-B	Manhole Ladder steps	DST	M	09/04/14	10/04/14	09/11/14	7	C
	SUB-13-00013-DST-147-C	Manhole Ladder steps- EYAR Plastic Industries Co.	DST	M	09/24/14	10/24/14	10/15/14	21	B
	SUB-13-00013-DST-148-A	Shop Drawings: 12" Main Pipeline: Plan, Profile and Cross Section from Sta. 0+034 to Sta. 1+250	DST	S	09/02/14	10/02/14	09/15/14	13	B
	SUB-13-00013-DST-149-A	Fasteners- TorqBolt	DST	M	09/04/14	10/04/14	09/11/14	7	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, DER SHARAF WATER PIPELINE
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Returne Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00013-DST-150-A	Updated Construction Schedule and S Curve (August 31, 2014)	DST	SCH	09/07/14	10/07/14	09/15/14	8	B
	SUB-13-00013-DST-151-A	Shop Drawings: Structural & Mechanical Detail for Water Meter Connection Chamber at Sta. 1+156	DST	S	09/08/14	10/08/14	09/22/14	14	C
	SUB-13-00013-DST-151-B	Shop Drawings: Structural & Mechanical Detail for Water Meter Connection Chamber at Sta. 1+156	DST	S	10/16/14	11/15/14	10/28/14	12	B
	SUB-13-00013-DST-152-A	Measuring ranges for pressure gauges	DST	M	09/09/14	10/09/14	09/16/14	7	B
	SUB-13-00013-DST-153-A	Shop Drawings: Structural & Mechanical Detail for Flow Control Connection Chamber at Sta. 1+170	DST	S	09/09/14	10/09/14	09/18/14	9	C
	SUB-13-00013-DST-153-B	Shop Drawings: Structural & Mechanical Detail for Flow Control Connection Chamber at Sta. 1+170	DST	S	09/24/14	10/24/14	10/02/14	8	B
	SUB-13-00013-DST-154-A	Shop Drawings: Structural & Mechanical Detail For valve Chambers For (Water Pipeline) From Sta. 0+034 To 1+250	DST	S	09/14/14	10/14/14	09/22/14	8	C
	SUB-13-00013-DST-154-B	Shop Drawings: Structural & Mechanical Detail For valve Chambers For (Water Pipeline) From Sta. 0+034 To 1+250	DST	S	09/28/14	10/28/14	10/02/14	4	B
	SUB-13-00013-DST-155-A	**Mechanical Detail For Beit Iba Connection Chambers in TO#14:** 1. Beit Iba Connection Chamber @ St. Seg. B 0+342 2. Nablus Connection Chamber @ St. B 0+040	DST	S	09/25/14	10/25/14	10/2/2014	7	A
	SUB-13-00013-DST-156-A	Mechanical Detail For 250 mm Washout Sta. 0+90 & AV/AR Chamber Sta. 0+365 in TO #14	DST	S	09/14/14	10/14/14	09/25/14	11	B
	SUB-13-00013-DST-157-A	Shop Drawings: Mechanical Detail for Shavi Shomron Main System Flow Monitoring Chamber at Sta. A 1+870 (TO.14)	DST	S	09/16/14	10/16/14	09/25/14	9	B
	SUB-13-00013-DST-158-A	Shop Drawings: Mechanical Detail For Combined Butterfly & Av/Ar Chamber @Sta. 0+810 Beit Iba Road.	DST	S	09/21/14	10/21/14	10/13/14	22	C
	SUB-13-00013-DST-158-B	Shop Drawings: Mechanical Detail For Combined Butterfly & Av/Ar Chamber @Sta. 0+810 Beit Iba Road.	DST	S	10/16/14	11/15/14	10/28/14	12	C
	SUB-13-00013-DST-158-C	Shop Drawings: Mechanical Detail For Combined Butterfly & Av/Ar Chamber @Sta. 0+810 Beit Iba Road.	DST	S	10/30/14	11/29/14	11/05/14	6	A
	SUB-13-00013-DST-159-A	Bolts and Nuts Sample - Torq Bolt Inc.	DST	M	10/12/14	11/11/14	10/15/14	3	B
	SUB-13-00013-DST-160-A	Updated Construction Schedule & S-Curve-September 30,2014	DST	SCH	10/12/14	11/11/14	10/27/14	15	B
	SUB-13-00013-DST-161-A	Shop Drawings: Mechanical Detail for Qusin Flow Monitoring Chamber Sta. 0+184	DST	S	10/27/14	11/26/14	11/06/14	10	C
	SUB-13-00013-DST-161-B	Shop Drawings: Mechanical Detail for Qusin Flow Monitoring Chamber Sta. 0+184-in TO# 14	DST	S	11/24/14	12/24/14	12/01/14	7	B
	SUB-13-00013-DST-162-A	DIN Steel Flanges	DST	M	10/29/14	11/28/14	11/03/14	5	D
	SUB-13-00013-DST-162-B	DIN Steel Flanges	DST	M	12/08/14	01/07/15	12/11/14	3	E
	SUB-13-00013-DST-163-A	Shop Drawings: Structural & Mechanical Detail for New Location of Selit Aldaher Connection	DST	S	11/04/14	12/04/14	11/18/14	14	B
	SUB-13-00013-DST-164-A	Updated Construction Schedule & S-Curve-October 31,2014	DST	SCH	11/06/14	12/06/14	11/18/14	12	B
	SUB-13-00013-DST-165-A	Weld neck flange-DIN 2635 for 10" and 12" sizes	DST	M	11/06/14	12/06/14	11/10/14	4	A
	SUB-13-00013-DST-166-A	Strainer ball valve- B.O.Q- item No. 3.2.1, 3.2.2, 3.2.3, 3.2.4, 3.2.5, 3.2.6, 3.2.7, 3.2.8, 3.2.9, 3.2.10, 3.2.11	DST	M	11/09/14	12/09/14	11/11/14	2	B
	SUB-13-00013-DST-167-A	3/4 inch Asphalt Wearing Course-Palestine Co. -Hijjawi lab	DST	M	11/10/14	12/10/14	11/11/14	1	B
	SUB-13-00013-DST-168-A	Pipe marker- B.O.Q- item No.7	DST	M	11/10/14	12/10/14	11/18/14	8	B
	SUB-13-00013-DST-169-A	Cleaning, washing, hydraulic test and disinfection plan	DST	P	11/12/14	12/12/14	11/20/14	8	C
	SUB-13-00013-DST-169-B	Cleaning, washing, hydraulic test and disinfection plan	DST	P	11/25/14	12/25/14	11/30/14	5	C
	SUB-13-00013-DST-169-C	Cleaning, washing, hydraulic test and disinfection plan	DST	P	12/02/14	01/01/15	12/08/14	6	B
	SUB-13-00013-DST-170-A	Shop Drawings: Mechanical Detail for 250 mm Washout Sta. 0+038- in TO# 14	DST	S	11/23/14	12/23/14	11/30/14	7	A
	SUB-13-00013-DST-171-A	Rock Cut Grid Elevation from Sta. 00+000 to Sta. 06+780	DST	S	12/01/14	12/31/14	12/22/14	21	E
	SUB-13-00013-DST-172-A	Updated Construction Schedule & S-Curve-November 30, 2014	DST	SCH	12/08/14	01/07/15	12/22/14	14	B
	SUB-13-00013-DST-173-A	Anti Seize for Stainless Steel Bolts-FIP Co.	DST	M	12/17/14	01/16/15	12/22/14	5	B
	SUB-13-00013-DST-174-A	Shop Drawings: 8" Sewer Line From Sta. 0+000 to Sta. 0+260	DST	S	12/28/14	01/27/15	01/06/15	9	B
	SUB-13-00013-DST-175-A	Shop Drawings: Burqa 4"Water Pipeline: Plan, Profile & Typical Section from Sta.0+000 to Sta.1+135- Deir Sharaf Main Pipeline	DST	S	12/30/14	01/29/15	01/12/15	13	B
	SUB-13-00013-DST-176-A	Sewer UPVC Pipes Manufactures Data Sheet (DN 8" SN 8) -Royal Product	DST	M	12/30/14	01/29/15	01/06/15	7	C
	SUB-13-00013-DST-176-B	Sewer UPVC Pipes Manufactures Data Sheet (DN 8" SN 8) -Royal Product	DST	M	01/12/15	02/11/15	01/13/15	1	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, DER SHARAF WATER PIPELINE
Submittals Register Log

SUBMITTAL					TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Project	DV	Submitted on (M/D/Y)	Returne Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	SUB-13-00013-DST-177-A	Sewer Circular Precast Concrete Manhole (one meter internal diameter) - PCP Product.	DST	M	12/30/14	01/29/15	01/06/15	7	C
	SUB-13-00013-DST-177-B	Sewer Circular Precast Concrete Manhole (one meter internal diameter) - PCP Product.	DST	M	01/28/15	02/27/15	02/03/15	6	A
	SUB-13-00013-DST-178-A	Revised Construction Schedule & S-Curve-December 31, 2014	DST	SCH	01/04/15	02/03/15	01/13/15	9	B
	SUB-13-00013-DST-178-B	Revised Construction Schedule & S-Curve-December 31, 2014- **For Engineering Record**	DST	SCH	01/20/15	02/19/15	02/01/15	12	B
	SUB-13-00013-DST-179-A	Shop Drawings: Structural & Mechanical Detail For: **1.** 6"&4" G.V for Al-Foundqumieh @ Sta. 0+990 **2.** 2*2" G.V for Al-Foundqumieh @ Sta. 0+410 & 0+430 **3.** 2*4" G.V for Bourqa @ Sta. 1+120 & 1+130	DST	S	01/18/15	02/17/15	01/27/15	9	B
	SUB-13-00013-DST-180-A	Rubber Gasket for 8" sewer UPVC pipes/ Sample	DST	M	01/15/15	02/14/15	01/20/15	5	A
	SUB-13-00013-DST-181-A	Check Valve DN 50, PN 40_ARI -NR-034 - BOQ item No. 3.2.11	DST	M	01/18/15	02/17/15	01/21/15	3	B
	SUB-13-00013-DST-182-A	Sewer Manhole Cover 60cm clear opening	DST	M	01/18/15	02/17/15	01/27/15	9	C
	SUB-13-00013-DST-183-A	Second Source for Third Party Testing – Radiographic Testing Company – Gabi Shoef LTD. N.D.T. and Quality Control.	DST	P	01/21/15	02/20/15	01/25/15	4	A
	SUB-13-00013-DST-184-A	FCVs Orifice Calculations. - BOQ item No. 3.2.1, 3.2.3, 3.2.6, 3.2.7, 3.2.8, 3.2.9, 3.2.10, 3.2.11, 3.6.1	DST	M	01/29/15	02/28/15	02/03/15	5	A
	SUB-13-00013-DST-185-A	Operation and Maintenance Manual (O&M) of Deir Sharaf Main Pipeline- All Sections	DST	PC	02/01/15	03/03/15	02/10/15	9	B
	SUB-13-00013-DST-186-A	Updated Construction Schedule & S-Curve-January 31, 2015	DST	SCH	02/05/15	03/07/15	02/17/15	12	B
	SUB-13-00013-DST-187-A	Acrylic paint.	DST	M	02/10/15	03/12/15	02/19/15	9	B
	SUB-13-00013-DST-188-A	Gate Valve PN 25- Raphael Valves Industries.	DST	M	02/15/15	03/17/15	02/18/15	3	B
	SUB-13-00013-DST-189-A	Date sheets 2", 4" and 6" Flanged Dismantling joints type Kruazs (PN 25, PN 40)	DST	M	02/16/15	03/18/15		PE	
	SUB-13-00013-DST-190-A	Draft As Built Drawings: Deir Sharaf 12" Main Pipeline: Plan, Profile and Typical Section from Sta. 0+015 to Sta. 1+520	DST	AS	02/24/15	03/26/15		PE	

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

P= Preconstruction - S= Shop drawings - M= Materials - O= Others - SCH= Schedule - PC= Post construction - AS= As Built

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-001-A	Gradation Test for Bedding Material (Sumsum)& Single Size Backfilling Material were taken from stock piles Material near St. 12+100 & from Jaba' Storage yard stockpiles- Source Al ashqar crusher – Location from sta. 12+105 to sta. 12+066/**Reports NO. M/1403/284, M/1403/285, M/1403/286**	03/30/14	04/29/14	04/14/14	15	B
	TEST-13-00013-DST-002-A	Gradation Test for Single Size Aggregate Material were taken from Stock Piles near St. 11+990 - Source Al Ashqar Crusher /**Reports NO. M/1403/305**	04/01/14	05/01/14	04/14/14	13	B
	TEST-13-00013-DST-003-A	7 Days concrete compressive strength For trial batch mix of grade B150,B250 & B350–Source MUASI Ready-Mix Plant/**Reports NO. M/1403/202, M/1403/202a, M/1403/202b**	04/01/14	05/01/14	04/24/14	23	B
	TEST-13-00013-DST-004-A	7 days concrete compressive strength for the first trial mix of grade B150, B250 & B350 –Source BONYAN Ready-Mix Plant/**Reports NO. M/1403/126a, M/1403/127, M/1403/128**	04/01/14	05/01/14	04/24/14	23	B
	TEST-13-00013-DST-005-A	7 days concrete compressive strength for the second trial mix of grade B250 & B350 –Source BONYAN Ready-Mix Plant/**Reports NO. M/1403/261, M/1403/261a**	04/02/14	05/02/14	04/24/14	22	B
	TEST-13-00013-DST-006-A	Base Course Comprehensive Test From Stock Piles At Sta. 12+120 For Trench Backfilling Final layer –Alashqar Crusher/**Reports NO. M/1403/283**	04/02/14	05/02/14	04/14/14	12	B
	TEST-13-00013-DST-007-A	Base Course Comprehensive Test From Stock Piles At Sta. 11+690 For Trench Backfilling Final layer –Alashqar Crusher /**Reports NO. M/1404/13**	04/07/14	05/07/14	04/14/14	7	B
	TEST-13-00013-DST-008-A	Single Size Aggregate Test From Stock Piles At Sta. 11+500 For Trench Backfilling/**Reports NO. M/1404/52**	04/07/14	05/07/14	04/14/14	7	B
	TEST-13-00013-DST-009-A	Somsom Aggregate Test From Stock Piles at Sta. 11+500 For Trench Bedding /**Reports NO. M/1404/51**	04/07/14	05/07/14	04/14/14	7	B
	TEST-13-00013-DST-010-A	Gradation Test for Bedding Material (Sumsum)were taken from stock piles Material near St. 11+050 –Source Alashqar Crusher/**Reports NO. M/1404/126**	04/13/14	05/13/14	04/14/14	1	B
	TEST-13-00013-DST-011-A	Single Size Aggregate Test From Stock Piles At Sta. 10+900 For Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1404/153**	04/15/14	05/15/14	04/16/14	1	B
	TEST-13-00013-DST-012-A	Base Course Comprehensive Test From Stock Piles At Sta. 11+120 For Trench Backfilling Final layer –Alashqar Crusher/**Reports NO. M/1404/125**	04/15/14	05/15/14	04/16/14	1	B
	TEST-13-00013-DST-013-A	28 Days concrete compressive strength For trial batch mix of grade B150,B250 & B350–Source MUASI Ready-Mix Plant/**Reports NO. M/1403/202c, M/1403/202d, M/1403/202e**	04/23/14	05/23/14	04/24/14	1	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-013-B	29 Days concrete compressive strength For trial batch mix of grade B150,B250 & B350–Source MUASI Ready-Mix Plant/**Reports NO. M/1403/202c, M/1403/202d, M/1403/202e**	02/11/15	03/13/15	02/23/15	12	E
	TEST-13-00013-DST-014-A	Base Course Comprehensive Test From Stock Piles At Sta. 10+670 For Trench Backfilling Final layer –Alashqar Crusher/**Reports NO. M/1404/204**	04/24/14	05/24/14	04/27/14	3	A
	TEST-13-00013-DST-015-A	28 days concrete compressive strength for the second trial mix of grade B250 & B350 –Source BONYAN Ready-Mix Plant/**Reports NO. M/1403/261b & M/1403/261c**	04/24/14	05/24/14	04/27/14	3	C
	TEST-13-00013-DST-016-A	Fabrication elbows Radiographic test results by Morex company(Examination date Mar. 30, 2014, 11 ¼ elbow 12 inch, Quantity: 22 pieces)	04/28/14	05/28/14	05/27/14	29	B
	TEST-13-00013-DST-017-A	28 days concrete compressive strength for the first trial mix of grade B150, B250 & B350 –Source BONYAN Ready-Mix Plant/**Reports NO. M/1403/127a**	04/28/14	05/28/14	05/08/14	10	C
	TEST-13-00013-DST-018-A	Single Size Aggregate Test From Stock Piles At Sta. 10+250 For Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1404/299**	04/29/14	05/29/14	05/08/14	9	A
	TEST-13-00013-DST-019-A	Somsom Aggregate Test From Stock Piles at Sta. 10+250 For Trench Bedding - Source Al Ashqar Crusher/**Reports NO. M/1404/300**	04/29/14	05/29/14	05/08/14	9	A
	TEST-13-00013-DST-020-A	Fabrication elbows Radiographic test results by MOREX company(Examination date Apr. 27, 2014, 11 ¼ elbow 12 inch(QTY=21 pieces) and 6 inch (QTY=7 pieces	04/29/14	05/29/14	05/28/14	29	B
	TEST-13-00013-DST-021-A	Field compaction test at Sta. 10+700 , Sta. 10+560 & Sta. 10+410 /**Report No. M/1404/381**	04/30/14	05/30/14	05/08/14	8	A
	TEST-13-00013-DST-022-A	Base Course Comprehensive Test From Stock Piles At Sta. 10+140 For Trench Backfilling Final layer –Source Al Ashqar Crusher/**Reports NO. M/1404/318**	05/04/14	06/03/14	05/08/14	4	A
	TEST-13-00013-DST-023-A	Single Size Aggregate Test From Stock Piles At Sta. 9+800 For Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1404/388**	05/04/14	06/03/14	05/08/14	4	A
	TEST-13-00013-DST-024-A	Somsom Aggregate Test From Stock Piles at Sta. 9+800 For Trench Bedding - Source Al Ashqar Crusher/**Reports NO. M/1404/387**	05/04/14	06/03/14	05/08/14	4	A
	TEST-13-00013-DST-025-A	Field compaction test at Sta. 10+795 , Sta. 10+985 ,Sta. 11+300, Sta. 11+435 & Sta. 11+580/**Report No. M/1404/11**	05/04/14	06/03/14	05/08/14	4	C
	TEST-13-00013-DST-025-B	Field compaction test at Sta. 10+795 , Sta. 10+985 ,Sta. 11+300, Sta. 11+435 & Sta. 11+580/**Report No. M/1405/31**	12/16/14	01/15/15	12/30/14	14	A
	TEST-13-00013-DST-026-A	Field compaction test at Sta. 10+800 , Sta. 10+970 & Sta. 11+570/**Report No. M/1404/31**	05/05/14	06/04/14	05/14/14	9	A
	TEST-13-00013-DST-027-A	Base Course Comprehensive Test From Stock Piles At Sta. 9+940 , Sta. 10+000 & Sta. 9+980 For Trench Backfilling Final layer –Source Al Ashqar Crusher/**Reports NO. M/1404/376**	05/05/14	06/04/14	05/14/14	9	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-028-A	Marshall Test for ¾ ‘’ Asphalt Binder Course from Sta. 10+360 to Sta. 10+760 –Source Developed Company/**Reports NO. M/1404/389**	05/06/14	06/05/14	05/18/14	12	A
	TEST-13-00013-DST-029-A	Field compaction test at Sta. 11+750, Sta. 11+880 & Sta. 12+030/**Report No. M/1404/46**	05/06/14	06/05/14	05/14/14	8	A
	TEST-13-00013-DST-030-A	Single Size Aggregate Test From Stock Piles At Sta. 12+380 For Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1404/64**	05/11/14	06/10/14	05/14/14	3	A
	TEST-13-00013-DST-031-A	Marshall Test for ¾ ‘’ Asphalt Binder Course from Sta. 11+060 to Sta. 11+360 **/Reports NO. M/1404/16**	05/11/14	06/10/14	05/18/14	7	A
	TEST-13-00013-DST-032-A	Marshall Test for ¾ ‘’ Asphalt Binder Course from Sta. 10+760 to Sta. 11+060/**Reports NO. M/1404/37**	05/11/14	06/10/14	05/18/14	7	A
	TEST-13-00013-DST-033-A	Marshall Test for ¾ ‘’ Asphalt Binder Course from Sta. 11+360 to Sta. 11+660/**Reports NO. M/1404/65**	05/11/14	06/10/14	05/18/14	7	A
	TEST-13-00013-DST-034-A	Somsom Aggregate Test From Stock Piles at Sta. 12+380 For Trench Bedding - Source Al Ashqar Crusher/**Reports NO. M/1404/64a**	05/11/14	06/10/14	05/14/14	3	A
	TEST-13-00013-DST-035-A	Fabrication elbows Radiographic test films by Morex company(Examination date Mar. 30, 2014, 11 ¼ elbow 12 inch, Quantity: 22 pieces)	05/12/14	06/11/14	05/28/14	16	B
	TEST-13-00013-DST-036-A	Fabrication elbows Radiographic test films by MOREX company(Examination date Apr. 27, 2014, 11 ¼ elbow 12 inch(QTY=21 pieces) and 6 inch (QTY=7 pieces)	05/12/14	06/11/14	05/28/14	16	B
	TEST-13-00013-DST-037-A	Marshall Test for ¾ ‘’ Asphalt Binder Course from Sta. 11+660 to Sta. 12+080/**Reports NO. M/1404/78**	05/14/14	06/13/14	05/27/14	13	A
	TEST-13-00013-DST-038-A	Base Course Comprehensive Test From Stock Piles at Sta. 12+590 for Trench Backfilling Final layer –Source Al Ashqar Crusher/**Reports NO. M/1404/106**	05/15/14	06/14/14	05/27/14	12	A
	TEST-13-00013-DST-039-A	Field compaction test at Sta. 9+730, Sta. 9+870 & Sta. 10+000 and retest at Sta. 9+870 & Sta. 9+904/**Report No. M/1405/160 & M/1405/167**	05/18/14	06/17/14	05/27/14	9	A
	TEST-13-00013-DST-040-A	Somsom Aggregate Test From Stock Piles at Sta. 12+850 For Trench Bedding - Source Al Ashqar Crusher/**Reports NO. M/1405/163**	05/19/14	06/18/14	05/27/14	8	A
	TEST-13-00013-DST-041-A	Single Size Aggregate Test From Stock Piles At Sta. 12+380 For Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1404/64**	05/19/14	06/18/14	05/28/14	9	A
	TEST-13-00013-DST-042-A	7 days concrete compressive strength for the first trial mix of grade B350 –Source Me'mar Ready-Mix Plant /**Reports NO. M/1405/139**	05/19/14	06/18/14	05/29/14	10	B
	TEST-13-00013-DST-043-A	Marshall Test for ¾ ‘’ Asphalt Binder Course from Sta. 9+690 to Sta. 9+904 and from Sta. 9+960 to Sta. 10+000/**Reports NO. M/1405/168**	05/20/14	06/19/14	05/28/14	8	A
	TEST-13-00013-DST-044-A	Field compaction test at Sta. 10+130, Sta. 10+210 & Sta. 10+300 /**Report No. M/1405/247**	05/21/14	06/20/14	05/28/14	7	A
	TEST-13-00013-DST-045-A	Base Course Comprehensive Test From Stock Piles at Sta. 12+850 for Trench Backfilling Final layer –Source Al Ashqar Crusher/**Reports NO. M/1405/161**	05/21/14	06/20/14	05/28/14	7	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-046-A	Somsom Aggregate Test From Stock Piles at Sta. 13+490 For Trench Bedding - Source Al Ashqar Crusher/**Reports NO. M/1405/245**	05/25/14	06/24/14	05/28/14	3	A
	TEST-13-00013-DST-047-A	Single Size Aggregate Test From Stock Piles At Sta. 13+490 For Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1405/246**	05/25/14	06/24/14	05/28/14	3	A
	TEST-13-00013-DST-048-A	Base Course Comprehensive Test From Stock Piles at Sta. 13+490 for Trench Backfilling Final layer –Source Al Ashqar Crusher/**Reports NO. M/1405/244**	05/28/14	06/27/14	06/03/14	6	A
	TEST-13-00013-DST-049-A	Marshall Test for ¾ '' Asphalt Binder Course from Sta. 10+000 to Sta. 10+360 **/Reports NO. M/1405/260**	05/29/14	06/28/14	06/03/14	5	A
	TEST-13-00013-DST-050-A	Field compaction test at Sta. 12+300, Sta. 12+400 , Sta. 12+500 & Sta. 12+150/**Report No. M/1405/396, M/1405/401**	06/01/14	07/01/14	06/04/14	3	A
	TEST-13-00013-DST-051-A	Steel reinforcement Test for 200 mm GV at Sta. 9+941/**Report No. M/1405/369**	06/02/14	07/02/14	06/04/14	2	A
	TEST-13-00013-DST-052-A	Field compaction (compacted base course) test at Sta. 13+260, Sta. 13+390 ,Sta. 13+160 , Sta. 12+645, Sta. 12+750, Sta. 12+850 ,Sta. 12+960 & Sta. 13+070 and retest at Sta. 12+870 Sta. 12+930 & Sta. 12+990 /**Report No. M/1405/1, M/1405/2**	06/02/14	07/02/14	06/11/14	9	A
	TEST-13-00013-DST-053-A	Marshall Test for ¾ '' Asphalt Binder Course from Sta. 12+080 to Sta. 12+510 **/Reports NO. M/1405/400**	06/04/14	07/04/14	06/15/14	11	A
	TEST-13-00013-DST-054-A	7 days concrete compressive strength for the trial mix of grade B150 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1405/344**	06/04/14	07/04/14	06/15/14	11	B
	TEST-13-00013-DST-055-A	8 days concrete compressive strength for the trial mix of grade B150–Source MUWASI Ready-Mix Plant /**Reports NO. M/1405/373**	06/04/14	07/04/14	06/15/14	11	B
	TEST-13-00013-DST-056-A	Marshall Test for ¾ '' Asphalt Binder Course from Sta. 12+835 to Sta. 13+040 & Sta. 13+210 to Sta. 13+480/**Reports NO. M/1406/23**	06/08/14	07/08/14	06/15/14	7	A
	TEST-13-00013-DST-057-A	Marshall Test for ¾ '' Asphalt Binder Course from Sta. 12+510 to Sta. 12+835 & Sta. 13+040 to Sta. 13+210/**Reports NO. M/1406/6**	06/08/14	07/08/14	06/15/14	7	A
	TEST-13-00013-DST-058-A	Steel reinforcement Test /**Report No. M/1406/22 & M/1406/22a**	06/08/14	07/08/14	06/19/14	11	C
	TEST-13-00013-DST-058-B	Steel reinforcement Test /**Report No. M/1406/22 & M/1406/22a**	07/02/14	08/01/14	07/07/14	5	A
	TEST-13-00013-DST-059-A	7 days concrete compressive strength for foundation of 200 mm GV at Sta. 9+941 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/3**	06/08/14	07/08/14	06/19/14	11	B
	TEST-13-00013-DST-060-A	7 days concrete compressive strength for walls of 200 mm GV chamber at Sta. 9+941 of grade B350 –Source MUWASI Ready-Mix Plant/**Reports NO. M/1406/52**	06/10/14	07/10/14	06/19/14	9	B
	TEST-13-00013-DST-061-A	7 days concrete compressive strength for pipe encasement from Sta. 6+740 to Sta. 6+640 of grade B150 –Source MUWASI Ready-Mix Plant/**Reports NO. M/1405/402**	06/10/14	07/10/14	06/19/14	9	A

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-062-A	7 days concrete compressive strength of concrete for ditches at Sta. 6+970 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/61**	06/15/14	07/15/14	06/19/14	4	A
	TEST-13-00013-DST-063-A	7 days concrete compressive strength for pipe encasement at Sta. 6+080 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/110**	06/16/14	07/16/14	06/19/14	3	A
	TEST-13-00013-DST-064-A	7 days concrete compressive strength for foundation of combined air release valve and butterfly valve at Sta. 11+187 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/111**	06/16/14	07/16/14	06/19/14	3	A
	TEST-13-00013-DST-065-A	Fabrication elbows Radiographic test results & films by Morex company(Examination date May 11, 2014, 11 ¼ elbow 12 inch, Quantity: 25 pieces & one on field)	06/19/14	07/19/14	07/10/14	21	A
	TEST-13-00013-DST-066-A	7 days concrete compressive strength for reinforced pipes encasement from Sta. 6+202 to Sta. 6+165 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/148**	06/19/14	07/19/14	06/22/14	3	A
	TEST-13-00013-DST-067-A	7 days concrete compressive strength for reinforced pipes encasement from Sta. 5+850 to Sta. 5+790 and from 5+580 to Sta. 5+780 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/168 & M/1406/169**	06/19/14	07/19/14	06/22/14	3	A
	TEST-13-00013-DST-068-A	7 days concrete compressive strength for drainage ditch from Sta. 6+975 to Sta. 6+750 of grade B250 –Source MUWASI Ready-Mix Plant/**Reports NO. M/1406/166**	06/19/14	07/19/14	06/22/14	3	A
	TEST-13-00013-DST-069-A	7 days concrete compressive strength for combined air release and butterfly valves walls at Sta. 11+187 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/167**	06/19/14	07/19/14	06/22/14	3	B
	TEST-13-00013-DST-070-A	7 days concrete compressive strength for foundation of 250 mm GV at Sta. 13+617 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/165**	06/19/14	07/19/14	06/24/14	5	C
	TEST-13-00013-DST-070-B	8 days concrete compressive strength for foundation of 250 mm GV at Sta. 13+617 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/165**	02/09/15	03/11/15	02/15/15	6	E
	TEST-13-00013-DST-071-A	Fabrication elbows Radiographic test results & films by Morex company(Examination date June 19, 2014, 11 ¼ elbow 12 inch, Quantity: 14 pieces & 5 joints on field)	06/23/14	07/23/14	07/10/14	17	A
	TEST-13-00013-DST-072-A	7 days concrete compressive strength for base slab of butterfly valve at Sta. 13+700 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/202**	06/24/14	07/24/14	07/07/14	13	B
	TEST-13-00013-DST-073-A	7 days concrete compressive strength for wall of 250 mm GV chamber at Sta. 13+617 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/219**	06/24/14	07/24/14	07/07/14	13	B

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-074-A	7 days concrete compressive strength for concrete ditch from Sta. 6+750 to Sta. 6+530 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/1**95	06/24/14	07/24/14	07/07/14	13	A
	TEST-13-00013-DST-075-A	28 days concrete compressive strength for trial mix of grade B 350 –Source Me'mar Ready-Mix Plant /**Reports NO. M/1406/139a**	06/24/14	07/24/14	07/07/14	13	C
	TEST-13-00013-DST-076-A	28 days concrete compressive strength for foundation of 200 mm GV at Sta. 9+941 of grade B 350 –Source Me'mar Ready-Mix Plant/**Reports NO. M/1406/3a**	06/29/14	07/29/14	07/07/14	8	A
	TEST-13-00013-DST-077-A	28 days concrete compressive strength for Pipe encasement from Sta. 6+740 to Sta. 6+640 of grade B 150 –Source Me'mar Ready-Mix Plant /**Reports NO. M/1406/402a**	06/29/14	07/29/14	07/07/14	8	A
	TEST-13-00013-DST-078-A	7 days concrete compressive strength for Pipe encasement from Sta. 5+338 to Sta. 5+253 & from Sta. 5+253 to Sta. 5+153 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/248 & Reports NO. M/1406/269**	07/02/14	08/01/14	07/07/14	5	A
	TEST-13-00013-DST-079-A	7 days concrete compressive strength for roof slab for combined chamber at Sta. 11+187 and walls of butterfly chamber at Sta. 13+700 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/268**	07/02/14	08/01/14	07/07/14	5	A
	TEST-13-00013-DST-080-A	28 days concrete compressive strength for pipe encasement from Sta. 6+921.56 to Sta. 6+846 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1405/373a**	07/02/14	08/01/14	07/09/14	7	A
	TEST-13-00013-DST-081-A	Steel reinforcement Test – Source Alas'sa connection chamber/**Reports NO. M/1406/417**	07/02/14	08/01/14	07/09/14	7	A
	TEST-13-00013-DST-082-A	28 days concrete compressive strength for walls of GV chamber at Sta. 9+941 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/52a**	07/02/14	08/01/14	07/15/14	13	C
	TEST-13-00013-DST-082-B	29 days concrete compressive strength for walls of GV chamber at Sta. 9+941 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/52a**	02/01/15	03/03/15	02/15/15	14	E
	TEST-13-00013-DST-083-A	28 days concrete compressive strength for pipe encasement from Sta. 6+981 to Sta. 6+921.56 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1405/344a**	07/07/14	08/06/14	07/10/14	3	A
	TEST-13-00013-DST-084-A	7days concrete compressive strength for roof slab of butterfly chamber at Sta. 13+700 of grade B 350 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1406/336**	07/07/14	08/06/14	07/10/14	3	A
	TEST-13-00013-DST-085-A	Somsom Aggregate Test From Stock Piles at Sta. 4+000 near Al Masaudyeh For Trench Bedding - Source Source Al Ashqar Crusher/**Reports NO. M/1406/418**	07/07/14	08/06/14	07/10/14	3	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-086-A	28 days concrete compressive strength for pipe encasement from Sta. 6+223 to Sta. 6+202 & Sta. 6+165 to Sta. 6+055 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/110a**	07/08/14	08/07/14	07/15/14	7	A
	TEST-13-00013-DST-087-A	7 days concrete compressive strength for pipe encasement from Sta. 4+871 to Sta. 4+612 & Sta. 4+460 to Sta. 4+342 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/335 & M/1406/372**	07/08/14	08/07/14	07/15/14	7	A
	TEST-13-00013-DST-088-A	28 days concrete compressive strength for Concrete ditch(Mock up) from Sta. 6+970 to Sta. 6+951 of grade B 250 –Source MUWASI Ready-Mix Plant / **Reports NO. M/1406/61a**	07/08/14	08/07/14	07/15/14	7	A
	TEST-13-00013-DST-089-A	7 days concrete compressive strength for concrete ditch from Sta. 6+020to Sta. 5+575 of grade B 250 –Source MUWASI Ready-Mix Plant / **Reports NO. M/1406/383**	07/08/14	08/07/14	07/15/14	7	A
	TEST-13-00013-DST-090-A	28 days concrete compressive strength for foundation of combined air release and butterfly valves at Sta. 11+187 of grade B 250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/111a**	07/08/14	08/07/14	07/15/14	7	A
	TEST-13-00013-DST-091-A	28 days concrete compressive strength for pipe encasement from Sta. 6+202 to Sta. 6+165 ,Sta. 5+580 to Sta. 5+780 & Sta. 5+580 to Sta. 5+790 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/148a, M/1406/168a & M/1406/169a**	07/13/14	08/12/14	07/16/14	3	A
	TEST-13-00013-DST-092-A	28 days concrete compressive strength for combined AR/AV and BVF chamber walls at Sta. 11+187 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/167a**	07/13/14	08/12/14	07/16/14	3	A
	TEST-13-00013-DST-093-A	28 days concrete compressive strength for drainage ditch fro Sta. 6+975 to Sta. 6+750 of grade B 250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/166a**	07/13/14	08/12/14	07/16/14	3	A
	TEST-13-00013-DST-094-A	28 days concrete compressive strength for foundation of 250 mm GV at Sta. 13+617 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/165a**	07/13/14	08/12/14	07/16/14	3	C
	TEST-13-00013-DST-094-B	29 days concrete compressive strength for foundation of 250 mm GV at Sta. 13+617 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/165a**	02/09/15	03/11/15	02/15/15	6	E
	TEST-13-00013-DST-095-A	7 days concrete compressive strength for foundation of small room of Al Asa'sa connection chamber at Sta. 13+608 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/26**	07/13/14	08/12/14	07/17/14	4	C
	TEST-13-00013-DST-095-B	7 days concrete compressive strength for foundation of small room of Al Asa'sa connection chamber at Sta. 13+608 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/26**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-096-A	7 days concrete compressive strength pipe encasement from Sta. 3+461 to Sta. 3+354 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/28**	07/13/14	08/12/14	07/17/14	4	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-097-A	7 days concrete compressive strength for drainage concrete ditch from Sta. 6+410 to Sta. 6+340 , Sta. 6+325 to Sta. 6+202 & Sta. 6+165 to Sta. 6+020 of grade B 250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/373**	07/13/14	08/12/14	07/17/14	4	A
	TEST-13-00013-DST-098-A	Compaction degree test & thickness for first layer of asphalted trench from Sta. 9+690 to Sta. 13+481 –Material Source Development Co. /**Reports NO. M/1407/36**	07/13/14	08/12/14	07/17/14	4	C
	TEST-13-00013-DST-098-B	Compaction degree test & thickness for first layer of asphalted trench from Sta. 9+690 to Sta. 13+481 –Material Source Development Co. /**Reports NO. M/1407/36aa**	08/06/14	09/05/14	08/18/14	12	A
	TEST-13-00013-DST-099-A	28 days concrete compressive strength for Base slab of butterfly valve at Sta. 13+700 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/202a**	07/15/14	08/14/14	07/20/14	5	A
	TEST-13-00013-DST-100-A	7 days concrete compressive strength for foundation of large room of Al Asa'sa connection chamber at Sta. 13+608 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/49**	07/15/14	08/14/14	07/20/14	5	C
	TEST-13-00013-DST-100-B	7 days concrete compressive strength for foundation of large room of Al Asa'sa connection chamber at Sta. 13+608 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/49**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-101-A	7 days concrete compressive strength for walls of small room of Al Asa'sa connection chamber at Sta. 13+608of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/50**	07/15/14	08/14/14	07/20/14	5	B
	TEST-13-00013-DST-102-A	28 days concrete compressive strength for concrete ditch from Sta. 6+750 to Sta. 6+530 of grade B 250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/195a**	07/15/14	08/14/14	07/24/14	9	A
	TEST-13-00013-DST-103-A	28 days concrete compressive strength for wall of 10'' GV chamber at Sta. 13+617 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/219a**	07/15/14	08/14/14	07/24/14	9	A
	TEST-13-00013-DST-104-A	Compaction core test for walls of 200 mm GV at Sta. 9+941 /**Reports NO. M/1407/102**	07/15/14	08/14/14	07/24/14	9	C
	TEST-13-00013-DST-104-B	Compaction core test for walls of 200 mm GV at Sta. 9+941 /**Reports NO. M/1407/103**	02/01/15	03/03/15	02/15/15	14	E
	TEST-13-00013-DST-105-A	28 days concrete compressive strength for pipe encasement from Sta. 5+338 to Sta. 5+253 & from Sta. 5+253 to Sta. 5+153 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/248a & M/1406/269a**	07/20/14	08/19/14	08/06/14	17	B
	TEST-13-00013-DST-106-A	7 days concrete compressive strength for foundation of butterfly valve chamber at Sta. 2+952 of grade B350 –Source MUWASI Ready-Mix Plant	08/21/14	09/20/14	08/27/14	6	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-107-A	7 days concrete compressive strength for pipe encasement from Sta. 3+100 to Sta. 3+060 of grade B 150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/84**	07/20/14	08/19/14	08/06/14	17	B
	TEST-13-00013-DST-108-A	7 days concrete compressive strength for walls of Al Asa'sa connection B (large room) at Sta. 13+608 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/133**	07/22/14	08/21/14	08/06/14	15	B
	TEST-13-00013-DST-109-A	28 days concrete compressive strength for roof slab of butterfly chamber at Sta. 13+700 of grade B 350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/336a**	07/22/14	08/21/14	08/06/14	15	B
	TEST-13-00013-DST-110-A	7 days concrete compressive strength for pipe encasement near Sabastia junction of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/203**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-111-A	28 days concrete compressive strength for pipe encasement from Sta. 4+871 to Sta. 4+612 , Sta. 4+460 to Sta.4+342 & Sta. 3+461 to Sta. 3+354 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/372a, M/1407/28a & M/1406/335a**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-112-A	28 days concrete compressive strength for concrete ditch from Sta. 6+020 to Sta. 5+575 , Sta. 6+410 to Sta. 6+340 ,Sta. 6+325 to Sta. 6+202 & Sta. 6+165 to Sta. 6+020 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/373a, & M/1406/383a**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-113-A	28 days concrete compressive strength for foundation of small room of Al-Assa'sa connection chamber at Sta. 13+608 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/26a**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-114-A	28 days concrete compressive strength for foundation of large room of Al-Assa'sa connection chamber at Sta. 13+608 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/49a**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-115-A	28 days concrete compressive strength for walls of small room of Al-Assa'sa connection chamber at Sta. 13+608 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/50a**	08/03/14	09/02/14	08/07/14	4	A
	TEST-13-00013-DST-116-A	9 days concrete compressive strength for roof slab of 250mm GV and small room of Alassa'sa connection chamber of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/274**	08/03/14	09/02/14	08/13/14	10	A
	TEST-13-00013-DST-117-A	9 days concrete compressive strength for pipe encasement from Sta. 1+950 to Sta. 1+890 grade B150 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1407/275**	08/03/14	09/02/14	08/13/14	10	A
	TEST-13-00013-DST-118-A	28 & 47 days concrete compressive strength for roof slab of combined chamber at Sta. 11+187 and walls of butterfly valve chamber of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/268a**	08/06/14	09/05/14	08/13/14	7	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-119-A	28 days concrete compressive strength for pipe encasement from Sta. 3+100 to Sta. 3+060 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/84a**	08/10/14	09/09/14	08/18/14	8	A
	TEST-13-00013-DST-120-A	Nondestructive loading test for ductile cast iron manhole cover(Dia. 750 mm)-GMT lab	08/10/14	09/09/14	08/18/14	8	A
	TEST-13-00013-DST-121-A	Field compaction test for base course layer from Sta. 3+950 to Sta. 4+080 & Sta. 6+508 to Sta. 6+430 /**Reports NO. M/1408/95**	08/11/14	09/10/14	08/18/14	7	A
	TEST-13-00013-DST-122-A	28 days concrete compressive strength for roof slab of 200 mm GV at Sta. 9+941 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1406/202a**	08/12/14	09/11/14	08/18/14	6	A
	TEST-13-00013-DST-123-A	7 days concrete compressive strength for ditch from Sta. 5+395 to Sta. 5+120 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/48**	08/17/14	09/16/14	08/21/14	4	C
	TEST-13-00013-DST-124-A	7 days concrete compressive strength for walls of combined AV/AR & BFV at Sta. 3+350of grade B350 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/88**	08/17/14	09/16/14	08/21/14	4	B
	TEST-13-00013-DST-125-A	7 days concrete compressive strength for foundation of combined AV/AR & BFV at Sta. 3+350 of grade B350 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/56**	08/17/14	09/16/14	08/21/14	4	B
	TEST-13-00013-DST-126-A	Single Size Aggregate test From Stock Piles at Sta. 9+660 for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1408/119**	08/17/14	09/16/14	08/21/14	4	A
	TEST-13-00013-DST-127-A	Somsom Aggregate test From Stock Piles at Sta. 9+660 for Trench Bedding - Source Al Ashqar Crusher/**Reports NO. M/1408/120**	08/17/14	09/16/14	08/21/14	4	A
	TEST-13-00013-DST-128-A	7 days concrete compressive strength for pipe encasement from Sta. 1+350 to Sta. 1+275 , Sta. 1+670 to Sta. 1+710 & Sta. 5+120 to Sta. 4+900 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/76, M/1408/36 & M/1408/57**	08/17/14	09/16/14	08/21/14	4	C
	TEST-13-00013-DST-128-B	7 days concrete compressive strength for pipe encasement from Sta. 1+350 to Sta. 1+275 & Sta. 1+670 to Sta. 1+710 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/76, M/1408/36**	08/24/14	09/23/14	08/27/14	3	A
	TEST-13-00013-DST-129-A	Fabrication Bends Radiographic test results by Morex company(Examination date Aug. 14, 2014, bends 12 inch, Quantity: 28 pieces	08/18/14	09/17/14	09/01/14	14	C
	TEST-13-00013-DST-129-B	Fabrication Bends Radiographic test results by Morex company	10/15/14	11/14/14	10/23/14	8	A
	TEST-13-00013-DST-130-A	7 days concrete compressive strength for ditch from Sta. 5+580 to Sta. 5+395 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/37**	08/19/14	09/18/14	08/24/14	5	C
	TEST-13-00013-DST-130-B	7 days concrete compressive strength for ditch from Sta. 5+580 to Sta. 5+395 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/37**	10/01/14	10/31/14	10/23/14	22	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-131-A	7 days concrete compressive strength for roof slab of Al Asa'sa connection chamber(part B) at Sta. 13+608 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/106**	08/19/14	09/18/14	08/24/14	5	A
	TEST-13-00013-DST-132-A	28 days concrete compressive strength for pipe encasement from Sta. 2+369 to Sta. 2+320 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/203a**	08/19/14	09/18/14	08/24/14	5	A
	TEST-13-00013-DST-133-A	Base Course Comprehensive Test From Stock Piles at Sta. 9+600 for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1408/135**	8/19/2014	09/18/14	08/24/14	5	A
	TEST-13-00013-DST-134-A	7 days concrete compressive strength for drainage ditch from Sta. 5+120 to Sta. 4+900 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/57**	08/21/14	09/20/14	08/27/14	6	A
	TEST-13-00013-DST-135-A	28 days concrete compressive strength for roof slab of 250 mm GV and small room of Al Asa'sa connection chamber at sta. 13+608 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1407/274A**	08/24/14	09/23/14	08/27/14	3	A
	TEST-13-00013-DST-136-A	7 days concrete compressive strength Pipe encasement from Sta. 9+548 to Sta. 9+358 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/173+175**	08/24/14	09/23/14	08/27/14	3	A
	TEST-13-00013-DST-137-A	7 days concrete compressive strength for walls of butterfly valve chamber at Sta. 2+952 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/174**	08/24/14	09/23/14	08/27/14	3	A
	TEST-13-00013-DST-138-A	7 days concrete compressive strength for roof slab of butterfly valve chamber at Sta. 2+952 and for combined AV/AR & BFV chamber at Sta. 3+350 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/196**	08/28/14	09/27/14	09/08/14	11	A
	TEST-13-00013-DST-139-A	7 days concrete compressive strength for pipe encasement from Sta. 9+240 to Sta. 9+141 of grade B150 –Source MUWASI Ready-Mix Plant/**Reports NO. M/1408/197**	08/28/14	09/27/14	09/08/14	11	A
	TEST-13-00013-DST-140-A	28 days concrete compressive strength for pipe encasement from Sta. 1+950 to Sta. 1+890 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/275a**	08/28/14	09/27/14	09/10/14	13	A
	TEST-13-00013-DST-141-A	7 days concrete compressive strength for drainage ditch from Sta. 4+860 to Sta. 4+560 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/253**	09/01/14	10/01/14	09/08/14	7	A
	TEST-13-00013-DST-142-A	7 days concrete compressive strength for drainage ditch from Sta. 4+000 to Sta. 4+490 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/290 +291**	09/02/14	10/02/14	09/08/14	6	C
	TEST-13-00013-DST-142-B	7days concrete compressive strength for drainage ditch from Sta. 4+000 to Sta. 4+490 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/290 +291a**	12/16/14	01/15/15	12/30/14	14	A

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-143-A	28 days concrete compressive strength for drainage ditch from Sta. 5+580 to Sta. 5+395 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/37a**	09/02/14	10/02/14	09/08/14	6	A
	TEST-13-00013-DST-144-A	28 days concrete compressive strength for pipe encasement from Sta. 1+670 to Sta. 1+710 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/36a**	09/02/14	10/02/14	09/08/14	6	A
	TEST-13-00013-DST-145-A	28 days concrete compressive strength for ditch from Sta. 5+395 to Sta. 5+120 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/48a**	09/04/14	10/04/14	09/10/14	6	C
	TEST-13-00013-DST-146-A	7 days concrete compressive strength for ditch from Sta. 1+400 to Sta. 1+280 & Sta. 1+620 to Sta. 1+700 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/342+343**	09/04/14	10/04/14	09/10/14	6	A
	TEST-13-00013-DST-147-A	28 days concrete compressive strength for ditch from Sta. 5+120 to Sta. 4+900 of grade B250 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/57a**	09/04/14	10/04/14	09/17/14	13	A
	TEST-13-00013-DST-148-A	28 days concrete compressive strength for foundation of combined AV/AR & BFV chamber at Sta. 3+350 of grade B350 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/56a**	09/07/14	10/07/14	09/17/14	10	A
	TEST-13-00013-DST-149-A	Reinforcing steel bars used for pre-cast manhole from PCP Co./**Reports NO. M/1409/20**	09/07/14	10/07/14	09/17/14	10	A
	TEST-13-00013-DST-150-A	Reinforcing steel bars used for Al Foundqumiya connection chamber at Sta. 12+143/**Reports NO. M/1409/4**	09/07/14	10/07/14	09/17/14	10	A
	TEST-13-00013-DST-151-A	28 days concrete compressive strength for pipe encasement from Sta. 1+350 to Sta. 1+275 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/76a**	09/07/14	10/07/14	09/17/14	10	A
	TEST-13-00013-DST-152-A	7 days concrete compressive strength for pipe encasement from Sta. 8+700 to Sta. 8+630 of grade B150 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/365**	09/07/14	10/07/14	09/18/14	11	A
	TEST-13-00013-DST-153-A	7 days concrete compressive strength for ditch from Sta. 1+720 to Sta. 2+060 & Sta. 2+120 to Sta. 2+200 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/363+364**	09/07/14	10/07/14	09/18/14	11	A
	TEST-13-00013-DST-154-A	28 days concrete compressive strength for walls of Al Asa'sa connection chamber at Sta. 13+608 of grade B350 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1407/133a**	09/10/14	10/10/14	09/22/14	12	B
	TEST-13-00013-DST-155-A	7 days concrete compressive strength for pipe encasement from Sta. 8+324 to Sta. 8+246 of grade B150 –Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/25**	09/10/14	10/10/14	09/18/14	8	A
	TEST-13-00013-DST-156-A	28 days concrete compressive strength for foundation of butterfly valve chamber at Sta. 2+952 of grade B350 –Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/142a**	09/10/14	10/10/14	09/18/14	8	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-157-A	7 days concrete compressive strength for Base slab for pre-cast manholes produced by PCP Factory(1.5 m) of grade B350 **/Reports NO. M/1409/24**	09/10/14	10/10/14	09/18/14	8	A
	TEST-13-00013-DST-158-A	28 days concrete compressive strength for walls of combined AV/AR & BFV at Sta. 3+350 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/88a**	09/10/14	10/10/14	09/18/14	8	A
	TEST-13-00013-DST-159-A	28 days concrete compressive strength for roof slab of Al Asa'sa connection chamber (part B)at Sta. 13+608 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/106a**	09/10/14	10/10/14	09/18/14	8	A
	TEST-13-00013-DST-160-A	7 days concrete compressive strength for base slab of Al Foundqumiya connection chamber (part 1) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/395**	09/10/14	10/10/14	09/18/14	8	A
	TEST-13-00013-DST-161-A	7 days concrete compressive strength for foundation of large room of Al Foundqumiya connection chamber at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/47**	09/14/14	10/14/14	09/23/14	9	A
	TEST-13-00013-DST-162-A	28 days concrete compressive strength for pipe encasement from Sta. 9+548 to Sta. 9+358 of grade B150- Source MUWASI Ready-Mix Plant/**Reports NO. M/1408/173a+175a**	09/14/14	10/14/14	09/23/14	9	A
	TEST-13-00013-DST-163-A	28 days concrete compressive strength for walls of butterfly valve chamber at Sta. 2+952 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/174a**	09/14/14	10/14/14	09/23/14	9	A
	TEST-13-00013-DST-164-A	7 days concrete compressive strength for walls part 1 of Al Foundqumiya connection chamber at sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/53**	09/14/14	10/14/14	09/23/14	9	A
	TEST-13-00013-DST-165-A	28 days concrete compressive strength for pipe encasement from Sta. 9+240 to Sta. 9+141 of grade B150- Source MUWASI Ready-Mix Plant/**Reports NO. M/1408/197a**	09/14/14	10/14/14	09/23/14	9	A
	TEST-13-00013-DST-166-A	28 days concrete compressive strength for roof slab of butterfly valve at Sta. 2+952 & combined AV/AR & BFV at Sta. 3+350 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/196a**	09/14/14	10/14/14	09/23/14	9	A
	TEST-13-00013-DST-167-A	7 days concrete compressive strength for foundation for Al Foundqumiya connection chamber(part 2) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/10**1	09/21/14	10/21/14	09/29/14	8	A
	TEST-13-00013-DST-168-A	7 days concrete compressive strength for pipe encasement from Sta. 7+695 to Sta. 7+605 of grade B150- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/179**	09/21/14	10/21/14	09/29/14	8	A
	TEST-13-00013-DST-169-A	7 days concrete compressive strength for roof slab of Al Foundqumiya connection chamber(part A) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/120**	09/21/14	10/21/14	09/29/14	8	A

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-170-A	7 days concrete compressive strength for walls of Sabstiya connection chamber (part A) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/158**	09/21/14	10/21/14	09/29/14	8	A
	TEST-13-00013-DST-171-A	7 days concrete compressive strength for base slab of Sabstiya connection chamber (part A) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/119**	09/21/14	10/21/14	09/29/14	8	A
	TEST-13-00013-DST-172-A	7 days concrete compressive strength for pipe encasement from Sta. 7+975 to Sta. 7+912 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/118**	09/21/14	10/21/14	09/29/14	8	A
	TEST-13-00013-DST-173-A	7 days concrete compressive strength for foundation of Sabstiya connection chamber (part 2)at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/178**	09/21/14	10/21/14	09/29/14	8	A
	TEST-13-00013-DST-174-A	28 days concrete compressive strength for drainage ditch from Sta. 4+860 to Sta. 4+560 of grade B250- Source MUWASI Ready-Mix Plant/**Reports NO. M/1409/253a**	09/21/14	10/21/14	09/29/14	8	A
	TEST-13-00013-DST-175-A	28 days concrete compressive strength for drainage ditch from Sta. 1+400 to Sta. 1+280 & from Sta. 1+620 to Sta. 1+700 of grade B250- Source MUWASI Ready-Mix Plant **/Reports NO. M/1408/342+343a**	09/28/14	10/28/14	10/01/14	3	A
	TEST-13-00013-DST-176-A	28 days concrete compressive strength for pipe encasement from Sta. 8+700 to Sta. 8+630 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/365a**	09/28/14	10/28/14	10/01/14	3	A
	TEST-13-00013-DST-177-A	28 days concrete compressive strength for drainage ditch from Sta. 4+000 to Sta. 4+490 of grade B250- Source MUWASI Ready-Mix Plant/**Reports NO. M/1408/290+291a**	09/28/14	10/28/14	10/01/14	3	A
	TEST-13-00013-DST-178-A	28 days concrete compressive strength for drainage ditch from Sta. 1+720 to sta. 2+060 & Sta. 2+120 to Sta. 2+200 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/363 + 364a**	09/28/14	10/28/14	10/01/14	3	A
	TEST-13-00013-DST-179-A	7 days concrete compressive strength for walls of Sabstiya connection chamber at Sta. 2+320 & base slab of Bazzariya connection chamber at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/256**	09/28/14	10/28/14	10/01/14	3	A
	TEST-13-00013-DST-180-A	7 days concrete compressive strength for roof slab of part 2 of Al Foundqumiya connection chamber at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/217**	09/28/14	10/28/14	10/01/14	3	A
	TEST-13-00013-DST-181-A	7 days concrete compressive strength for pipe encasement from sta. 7+500 to Sta. 7+417 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/218**	09/28/14	10/28/14	10/01/14	3	A
	TEST-13-00013-DST-182-A	7 days concrete compressive strength for pipe encasement from Sta. 7+215 to Sta. 7+166 & from Sta. 7+149 to Sta. 7+094 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/257**	10/01/14	10/31/14	10/15/14	14	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-183-A	7 days concrete compressive strength for walls of Bazzariya connection chamber (part 1)at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/361**	10/01/14	10/31/14	10/15/14	14	A
	TEST-13-00013-DST-184-A	7 days concrete compressive strength for pipe encasement from Sta. 3+461 to Sta. 3+530 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/300**	10/01/14	10/31/14	10/15/14	14	A
	TEST-13-00013-DST-185-A	7 days concrete compressive strength for roof slab of Sabastiya connection chamber (part1) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/299**	10/01/14	10/31/14	10/15/14	14	A
	TEST-13-00013-DST-186-A	28 days concrete compressive strength for base slab of Al Foundqumiya connection chamber (part 1) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1408/395a**	10/01/14	10/31/14	10/15/14	14	A
	TEST-13-00013-DST-187-A	28 days concrete compressive strength for pipe encasement from Sta. 8+324 to Sta. 8+246 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/25a**	10/01/14	10/31/14	10/15/14	14	A
	TEST-13-00013-DST-188-A	28 days concrete compressive strength for base slab of pre-cast manholes produced(1.5 m) by PCP factory of grade B350/**Reports NO. M/1409/24a**	10/01/14	10/31/14	10/15/14	14	A
	TEST-13-00013-DST-189-A	7 days concrete compressive strength for base slab of Bazzariya connection chamber (part2) at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/325**	10/01/14	10/31/14	10/15/14	14	A
	TEST-13-00013-DST-190-A	7 days concrete compressive strength for foundation of combined AV/AR & BFV at Sta. 7+400 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/385**	10/02/14	11/01/14	10/15/14	13	A
	TEST-13-00013-DST-191-A	28 days concrete compressive strength for foundation of Al Foundqumiya connection chamber (large room) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/47a**	10/02/14	11/01/14	10/15/14	13	A
	TEST-13-00013-DST-192-A	7 days concrete compressive strength for drainage ditch from Sta. 8+850 to Sta. 8+214 & Sta. 8+060 to Sta. 7+450 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/399, M/1409/422, M/1409/423 & M/1410/31**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-193-A	7 days concrete compressive strength for drainage ditch from sta. 9+350 to sta. 9+550 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/360**	10/12/14	11/11/14	10/20/14	8	C
	TEST-13-00013-DST-193-B	7 days concrete compressive strength for drainage ditch from sta. 9+350 to sta. 9+550 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/360aa**	12/10/14	01/09/15	12/18/14	8	A
	TEST-13-00013-DST-194-A	7 days concrete compressive strength for drainage ditch from sta. 9+030 to sta. 9+350 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/368**	10/12/14	11/11/14	10/20/14	8	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-194-B	8 days concrete compressive strength for drainage ditch from sta. 9+030 to sta. 9+350 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/368**	10/23/14	11/22/14	10/29/14	6	A
	TEST-13-00013-DST-195-A	7 days concrete compressive strength for roof slab of Bazzariya connection chamber (part 1+ 2) at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/20**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-196-A	7 days concrete compressive strength for foundation of flow monitoring chamber at Sta. 7+160 of grade B350- Source MUWASI Ready-Mix Plant/**Reports NO. M/1410/16**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-197-A	7 days concrete compressive strength for walls of Bazzariya connection chamber (part 2) at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/386**	10/12/14	11/11/14	10/20/14	8	C
	TEST-13-00013-DST-197-B	7 days concrete compressive strength for walls of Bazzariya connection chamber (part 2) at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/386a**	12/16/14	01/15/15	12/30/14	14	A
	TEST-13-00013-DST-198-A	7 days concrete compressive strength for roof slab of Sabastiya connection chamber (part 2) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/398**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-199-A	7 days concrete compressive strength for walls of combined AV/AR & BFV chamber at Sta. 7+400 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/445**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-200-A	28 days concrete compressive strength for walls of Al Foundqumiya connection chamber(part 1) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/53a**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-201-A	28 days concrete compressive strength for base slab of Sabastiya connection chamber (part A) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/119a**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-202-A	28 days concrete compressive strength for walls of Al Foundqumiya connection chamber(part 2) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/101a**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-203-A	28 days concrete compressive strength for walls of Sabastiya connection chamber (part A) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/158a**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-204-A	28 days concrete compressive strength for roof slab of Al Foundqumiya connection (part A) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/120a**	10/12/14	11/11/14	10/16/14	4	A
	TEST-13-00013-DST-205-A	28 days concrete compressive strength for pipe encasement from Sta. 7+975 to Sta. 7+912 & Sta. 8+095 to Sta. 8+070.6 of grade B150- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/118a**	10/12/14	11/11/14	10/16/14	4	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-206-A	Base Course Comprehensive Test From Stock Piles at Sta. 1+180 for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1408/414**	10/12/14	11/11/14	10/22/14	10	A
	TEST-13-00013-DST-207-A	Single size aggregate Test From Stock Piles at Sta. 1+180 for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1408/415**	10/12/14	11/11/14	10/22/14	10	A
	TEST-13-00013-DST-208-A	Sumsum aggregate Test From Stock Piles at Sta. 1+180 for Trench Bedding-Source Al Ashqar Crusher/**Reports NO. M/1408/416**	10/12/14	11/11/14	10/22/14	10	A
	TEST-13-00013-DST-209-A	28 days concrete compressive strength for pipe encasement from Sta. 7+695 to Sta. 7+605 & Sta. 7+500 to Sta. 7+417 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/179a, M/1409/218a**	10/19/14	11/18/14	10/23/14	4	A
	TEST-13-00013-DST-210-A	28 days concrete compressive strength for foundation of Sabastiya connection chamber (part 2) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/178a**	10/19/14	11/18/14	10/23/14	4	A
	TEST-13-00013-DST-211-A	28 days concrete compressive strength for roof slab of Al Foundqumiya connection chamber (part 2) at Sta. 12+143 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/217a**	10/19/14	11/18/14	10/23/14	4	A
	TEST-13-00013-DST-212-A	28 days concrete compressive strength for walls of Sabastiya connection (part B) at Sta. 2+300 & base slab of Bazzariya connection chamber (part A) at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/256a**	10/19/14	11/18/14	10/23/14	4	A
	TEST-13-00013-DST-213-A	28 days concrete compressive strength for pipe encasement from Sta. 7+215 to Sta. 7+166 & from Sta. 7+149 to Sta. 7+094 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/257a**	10/19/14	11/18/14	10/23/14	4	A
	TEST-13-00013-DST-214-A	Manhole Rungs Test /**Reports NO. M/1410/113**	10/19/14	11/18/14	10/23/14	4	A
	TEST-13-00013-DST-215-A	Fabrication Bends Radiographic test results &films by Morex company(Examination date Sep. 29, 2014, bends 6 inch, Quantity: 5 pieces	10/22/14	11/21/14	10/29/14	7	A
	TEST-13-00013-DST-216-A	Fabrication Bends Radiographic test films by Morex company(Examination date: June 19,2014 & Aug. 14, 2014)	10/22/14	11/21/14	10/29/14	7	A
	TEST-13-00013-DST-217-A	28 days concrete compressive strength for base slab of Bazzariya connection chamber (part 2) at sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/325a**	10/22/14	11/21/14	10/29/14	7	A
	TEST-13-00013-DST-218-A	28 days concrete compressive strength for roof slab of Sabastiya connection chamber (part 1)at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/299a**	10/22/14	11/21/14	10/29/14	7	A
	TEST-13-00013-DST-219-A	7 days concrete compressive strength for pipe encasement from Sta. 0+715 to Sta. 0+557 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/60**	10/22/14	11/21/14	10/29/14	7	A
	TEST-13-00013-DST-220-A	7 days concrete compressive strength for walls of flow monitoring chamber at Sta. 7+160 grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/93a**	10/22/14	11/21/14	10/29/14	7	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-221-A	7 days concrete compressive strength for roof slab of combined AV/AR & BFV chamber at Sta. 7+400 grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/93**	10/22/14	11/21/14	10/29/14	7	A
	TEST-13-00013-DST-222-A	28 days concrete compressive strength for drainage ditch from Sta. 9+030 to Sta. 9+350 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/368a**	10/23/14	11/22/14	10/29/14	6	A
	TEST-13-00013-DST-223-A	28 days concrete compressive strength for pipe encasement from Sta. 3+461 to Sta. 3+530 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/300a**	10/23/14	11/22/14	10/29/14	6	A
	TEST-13-00013-DST-224-A	28 days concrete compressive strength for walls of Bazzariya connection chamber (part 1)at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/361a**	10/23/14	11/22/14	10/29/14	6	A
	TEST-13-00013-DST-225-A	Asphalt milling materials to be used around chambers /**Reports NO. M/1410/121**	10/23/14	11/22/14	10/29/14	6	A
	TEST-13-00013-DST-226-A	7 days concrete compressive strength for base slab of Burqa connection chamber(part1) at Sta. 7+032 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/129**	11/02/14	12/02/14	11/05/14	3	A
	TEST-13-00013-DST-227-A	7 days concrete compressive strength for drainage ditch from Sta. 7+360 to Sta. 7+180 of grade B250- Source MUWASI Ready-Mix Plant/**Reports NO. M/1410/73**	11/02/14	12/02/14	11/05/14	3	A
	TEST-13-00013-DST-228-A	7 days concrete compressive strength for pipe encasement from Sta. 0+230 to Sta. 0+148 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/114**	11/02/14	12/02/14	11/05/14	3	A
	TEST-13-00013-DST-229-A	28 days concrete compressive strength for foundation of combined AV/AR & BFV chamber at Sta. 7+400 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/385a**	11/02/14	12/02/14	11/05/14	3	A
	TEST-13-00013-DST-230-A	28 days concrete compressive strength for walls of Bazzariya connection chamber (part 2) at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/386a**	11/02/14	12/02/14	11/05/14	3	A
	TEST-13-00013-DST-231-A	28 days concrete compressive strength for roof slab of Sabastiya connection chamber (part 2) at Sta. 2+320 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/398a**	11/02/14	12/02/14	11/05/14	3	A
	TEST-13-00013-DST-232-A	28 days concrete compressive strength for drainage ditch from Sta. 9+350 to Sta. 9+550 ,Sta. 8+850 to Sta. 8+500, Sta. 8+500-Sta. 8+214 & Sta. 8+060 to Sta. 7+800 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/360a, M/1409/399a, M/1409/422a & M/1409/423a**	11/02/14	12/02/14	11/05/14	3	C
	TEST-13-00013-DST-232-B	29 days concrete compressive strength for drainage ditch from Sta. 9+350 to Sta. 9+550 , of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1409/360aa**	12/10/14	01/09/15	12/18/14	8	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-233-A	28 days concrete compressive strength for walls of combined AV/AR & BFV chamber at Sta. 7+400 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1409/445a**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-234-A	28 days concrete compressive strength for foundation of flow monitoring chamber at Sta. 7+160 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/16a**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-235-A	28 days concrete compressive strength for drainage ditch from Sta. 7+800 to Sta. 7+450 of grade B250- Source MUWASI Ready-Mix Plant/**Reports NO. M/1410/31a**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-236-A	28 days concrete compressive strength for roof slab of Bazzariya connection chamber (part1&2) at Sta. 8+206 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/20a**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-237-A	7 days concrete compressive strength for walls of Burqa connection chamber(part2) at Sta. 7+032 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/208**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-238-A	7 days concrete compressive strength for walls (part1) & base slab (part2)for Burqa connection chamber at Sta. 7+032 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/163**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-239-A	7 days concrete compressive strength for roof slab of flow monitoring chamber at Sta. 7+160 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/208a**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-240-A	Marshall Test for ¾ '' Asphalt Binder Course from Sta. 13+480 to Sta. 13+680, from Sta. 9+010 to Sta. 8+855 **/Reports NO. M/1410/254**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-241-A	Field compaction test(compacted base course) at Sta. 8+885,Sta. 8+950,Sta. 9+610,Sta. 9+940,Sta. 13+500 & Sta. 13+600 and retest at Sta. 9+650 & Sta. 9+680 **/Reports NO. M/1410/252 & M/1410/253**	11/04/14	12/04/14	11/12/14	8	A
	TEST-13-00013-DST-242-A	Compaction degree & thickness for first layer of asphalted trench(core test) at Sta. 8+900 ,Sta. 9+680,Sta. 9+675,Sta. 9+665,Sta. 9+928 & Sta. 13+500 –Material Source Development Co./**Reports NO. M/1411/72**	11/09/14	12/09/14	11/19/14	10	A
	TEST-13-00013-DST-243A	7 days concrete compressive strength for roof slab of Burqa connection chamber (part 2) at Sta. 7+032 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/270**	11/11/14	12/11/14	11/19/14	8	A
	TEST-13-00013-DST-244-A	7 days concrete compressive strength for roof slab of Burqa connection chamber (part 1) at Sta. 7+032 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/271**	11/11/14	12/11/14	11/19/14	8	A
	TEST-13-00013-DST-245-A	7 days concrete compressive strength for 6'' pipe encasement at Sta. 0+758 to Sta. 0+717of grade B150- Source MUWASI Ready-Mix Plant t/**Reports NO. M/1411/28**	11/11/14	12/11/14	11/19/14	8	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-245-B	8 days concrete compressive strength for 6'' pipe encasement at Sta. 0+758 to Sta. 0+717of grade B150- Source MUWASI Ready-Mix Plant t/**Reports NO. M/1411/28a**	12/10/14	01/09/15	12/24/14	14	A
	TEST-13-00013-DST-246-A	28 days concrete compressive strength for Concrete ditch from Sta. 7+360 to Sta. 7+180 & 45 days concrete compressive strength Sta. 9+350 to Sta. 9+550 grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/73a & NO. M/1410/360aa**	11/11/14	12/11/14	11/24/14	13	A
	TEST-13-00013-DST-247-A	28 days concrete compressive strength for 6 '' pipe encasement from Sta. 0+715 to Sta. 0+557 grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/60a**	11/11/14	12/11/14	11/24/14	13	A
	TEST-13-00013-DST-248-A	Marshall Test for ¾ '' Asphalt Binder Course from Sta. 9+580 to Sta. 9+700 & Sta. 9+912 to Sta. 9+950 (first layer) AND from Sta. 9+550 to Sta. 9+950 (second layer) /**Reports NO. M/1410/283**	11/11/14	12/11/14	11/24/14	13	A
	TEST-13-00013-DST-249-A	Marshall Test for ¾ '' Asphalt Wearing Course from Sta. 13+700 to Sta. 12+450/**Reports NO. M/1411/87**	11/11/14	12/11/14	11/24/14	13	A
	TEST-13-00013-DST-250-A	Base Course Comprehensive Test from Stock Piles at Sta. 0+780 (segment B) for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1411/25**	11/11/14	12/11/14	11/24/14	13	A
	TEST-13-00013-DST-251-A	Single size aggregate test from stock piles from Sta. 0+200 to Sta. 0+100 (segment B) for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1411/202**	11/23/14	12/23/14	11/25/14	2	A
	TEST-13-00013-DST-252-A	Bedding aggregate test from Stock Piles from Sta. 0+200 to Sta. 0+100 (segment B) for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1411/203**	11/23/14	12/23/14	11/25/14	2	A
	TEST-13-00013-DST-253-A	28 days concrete compressive strength for roof slab of combined chamber at Sta. 7+400 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/93b**	11/23/14	12/23/14	11/25/14	2	A
	TEST-13-00013-DST-254-A	28 days concrete compressive strength for walls of flow monitoring chamber at Sta. 7+160 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/93c**	11/23/14	12/23/14	11/25/14	2	A
	TEST-13-00013-DST-255-A	28 days concrete compressive strength for base slab of Burqa connection chamber (part 1) at Sta. 7+023 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/129a**	11/23/14	12/23/14	11/25/14	2	A
	TEST-13-00013-DST-256-A	28 days concrete compressive strength for concrete encasement for 12'' pipes from Sta. 0+230 to Sta. 0+148 of grade B150- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/114a**	11/23/14	12/23/14	11/25/14	2	A
	TEST-13-00013-DST-257-A	28 days concrete compressive strength for walls (part1) & base slab (part 2) of Burqa connection chamber at Sta. 7+032 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/163a**	11/23/14	12/23/14	11/25/14	2	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-258-A	7 days concrete compressive strength for drainage ditch from Sta. 0+980 to Sta. 0+500 of grade B250- Source MUWASI Ready-Mix Plant/ **Reports NO. M/1411/67**	11/23/14	12/23/14	11/25/14	2	A
	TEST-13-00013-DST-259-A	Marshall Test for ¾ '' Asphalt Wearing Course & trench second layer from Sta. 13+700 to Sta. 12+450-Source Abu Sukar Co. /**Reports NO. M/1411/88**	11/23/14	12/23/14	12/02/14	9	A
	TEST-13-00013-DST-260-A	Marshall Test for ¾ '' Asphalt Wearing Course & trench second layer from Sta. 12+450 to Sta. 11+350-Source Abu Sukar Co. **/Reports NO. M/1411/99**	11/23/14	12/23/14	12/02/14	9	A
	TEST-13-00013-DST-261-A	Marshall Test for ¾ '' Asphalt Wearing Course & trench second layer from Sta. 11+350 to Sta. 10+450-Source Abu Sukar Co. /**Reports NO. M/1411/112**	11/23/14	12/23/14	12/02/14	9	A
	TEST-13-00013-DST-262-A	Marshall Test for ¾ '' Asphalt Wearing Course & trench second layer from Sta. 10+400 to Sta. 10+000 & from Sta. 10+080 to Sta. 9+900-Source Abu Sukar Co. /**Reports NO. M/1411/132**	11/23/14	12/23/14	12/02/14	9	A
	TEST-13-00013-DST-263-A	Marshall Test for ¾ '' Asphalt Wearing Course & trench second layer from Sta. 10+080 to Sta. 10+000 & from Sta. 9+900 to Sta. 9+660-Source Abu Sukar Co. /**Reports NO. M/1411/155**	11/23/14	12/23/14	12/02/14	9	A
	TEST-13-00013-DST-264-A	7 days concrete compressive strength for walls of FCV chamber at sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/295**	12/09/14	01/08/15	12/14/14	5	A
	TEST-13-00013-DST-265-A	7 days concrete compressive strength for base slab of FCV chamber at sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/236**	12/09/14	01/08/15	12/14/14	5	C
	TEST-13-00013-DST-265-B	8 days concrete compressive strength for base slab of FCV chamber at sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/236a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-266-A	7 days concrete compressive strength for base slab of combined AV/AR & BFV chamber at Sta. 1+162 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/286**	12/09/14	01/08/15	12/14/14	5	A
	TEST-13-00013-DST-267-A	28 days concrete compressive strength for walls of Burqa connection chamber (part 2) at Sta. 7+032 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/208a**	12/09/14	01/08/15	12/14/14	5	A
	TEST-13-00013-DST-268-A	28 days concrete compressive strength for roof slab of Burqa connection chamber (part 2) at St. 7+032 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/270a**	12/09/14	01/08/15	12/14/14	5	A
	TEST-13-00013-DST-269-A	28 days concrete compressive strength for roof slab of Burqa connection chamber (part 1) at St. 7+032 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1410/271a**	12/09/14	01/08/15	12/14/14	5	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-270-A	28 days concrete compressive strength for roof slab of flow monitoring chamber at Sta. 7+180 of grade B350- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/208b**	12/09/14	01/08/15	12/14/14	5	A
	TEST-13-00013-DST-271-A	28 days concrete compressive strength for 6'' pipe encasement from Sta. 0+757 to Sta. 0+717(segment B) of grade B150- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/28a**	12/09/14	01/08/15	12/14/14	5	A
	TEST-13-00013-DST-272-A	28 days concrete compressive strength for drainage ditch from Sta. 0+980 to Sta. 0+500 of grade B250- Source MUWASI Ready-Mix Plant **/Reports NO. M/1410/67a**	12/09/14	01/08/15	12/14/14	5	A
	TEST-13-00013-DST-273-A	7 days concrete compressive strength for drainage ditch from Sta. 1+332 to Sta. 1+369 & Sta. 1+806 to Sta. 1+933 of grade B250- Source MUWASI Ready-Mix Plant **/Reports NO. M/1411/323**	12/10/14	01/09/15	12//18/2014	8	C
	TEST-13-00013-DST-273-B	8 days concrete compressive strength for drainage ditch from Sta. 1+332 to Sta. 1+369 & Sta. 1+806 to Sta. 1+933 of grade B250- Source MUWASI Ready-Mix Plant **/Reports NO. M/1411/323a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-274-A	7 days concrete compressive strength for drainage ditch at sta. 8+200 near Bazzariya connection from Sta. 7+470 to sta. 7+356 ,Sta. 7+185 to Sta. 7+021,Sta. 6+992 to Sta. 6+983 & Sta. 5+772 to Sta. 5+761 of grade B250- Source MUWASI Ready-Mix Plant **/Reports NO. M/1411/322**	12/10/14	01/09/15	12//18/2014	8	C
	TEST-13-00013-DST-274-B	8 days concrete compressive strength for drainage ditch at sta. 8+200 near Bazzariya connection from Sta. 7+470 to sta. 7+356 ,Sta. 7+185 to Sta. 7+021,Sta. 6+992 to Sta. 6+983 & Sta. 5+772 to Sta. 5+761 of grade B250- Source MUWASI Ready-Mix Plant **/Reports NO. M/1411/322**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-275-A	Marshall Test for ¾ '' Asphalt trench first layer –segment B from Sta. Sta. 1+000 to Sta. 0+384-Source Development Co. **/Reports NO. M/1412/22**	12/10/14	01/09/15	12//18/2014	8	A
	TEST-13-00013-DST-276-A	Marshall Test for ¾ '' Asphalt trench first layer –segment B from Sta. Sta. 0+007 to Sta. 0+384-Source Development Co. **/Reports NO. M/1412/43**	12/10/14	01/09/15	12//18/2014	8	A
	TEST-13-00013-DST-277-A	Field compaction test & retest for base course layer at Sta. 0+330 ,Sta. 0+200 & Sta. 0+075-segment B/**Reports NO. M/1412/23 & M/1412/29**	12/10/14	01/09/15	12//18/2014	8	A
	TEST-13-00013-DST-278-A	Field compaction test for base course layer at Sta. 0+900 ,Sta. 0+730 & Sta. 0+500-segment B/**Reports NO. M/1411/6**	12/10/14	01/09/15	12//18/2014	8	A
	TEST-13-00013-DST-279-A	Base Course Comprehensive Test From Stock Piles at sta. 0+200 to sta. 0+100 –segment B for Trench Backfilling-Source Al Ashqar Crusher/**Reports NO. M/1411/201**	12/10/14	01/09/15	12//18/2014	8	A
	TEST-13-00013-DST-280-A	7 days concrete compressive strength for drainage ditch from Sta. 1+800 to Sta. 1+900 of grade B250- Source MUWASI Ready-Mix Plant/**Reports NO. M/1412/35**	12/11/14	01/10/15	12/24/14	13	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-280-B	8 days concrete compressive strength for drainage ditch from Sta. 1+800 to Sta. 1+900 of grade B250- Source MUWASI Ready-Mix Plant/**Reports NO. M/1412/35a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-281-A	7 days concrete compressive strength for drainage ditch from Sta. 0+520 to Sta. 0+090of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/34**	12/11/14	01/10/15	12/24/14	13	A
	TEST-13-00013-DST-282-A	7 days concrete compressive strength for base slab of inlet Shavi Shamron flow monitoring chamber at Sta. 1+159 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/33**	12/11/14	01/10/15	12//18/2014	8	A
	TEST-13-00013-DST-283-A	Compaction degree & thickness for first layer of asphalted trench(core test) at Sta. B0+030 ,Sta. B0+280,Sta. B0+490 ,Sta. B0+700,Sta. B0+905,Sta. B0+910 & Sta. B 0+900–Material Source Development Co./**Reports NO. M/1412/99**	12/14/14	01/13/15	12/30/14	16	A
	TEST-13-00013-DST-284-A	Compaction degree & thickness for wearing course & second layer of asphalted trench(core test) from Sta. 9+660 to Sta. 12+400 & from Sta. 13+200 to Sta. 13+710–Material Source Development Co. &Abu Sukar Co. /**Reports NO. M/1412/24**	12/16/14	01/15/15	12/30/14	14	C
	TEST-13-00013-DST-284-B	Compaction degree & thickness for wearing course & second layer of asphalted trench(core test) from Sta. 9+660 to Sta. 12+400 & from Sta. 13+200 to Sta. 13+710–Material Source Development Co. &Abu Sukar Co. /**Reports NO. M/1412/24 & M/1502/32**	02/10/15	03/12/15	02/23/15	13	A
	TEST-13-00013-DST-285-A	7 days concrete compressive strength for foundation of BFV chamber at Sta. 1+172 & roof slab of combined chamber AV/AR & BFV at Sta. 1+162 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/221**	12/23/14	01/22/15	01/11/15	19	A
	TEST-13-00013-DST-286-A	7 days concrete compressive strength for walls of combined AV/AR & BFV chamber at Sta. 1+162 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/69**	12/23/14	01/22/15	01/11/15	19	A
	TEST-13-00013-DST-287-A	28 days concrete compressive strength for base slab of combined AV/AR & BFV chamber at Sta. 1+162 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/286a**	12/23/14	01/22/15	01/11/15	19	A
	TEST-13-00013-DST-288-A	7 days concrete compressive strength for roof slab of flow control valve chamber at Sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/143**	12/23/14	01/22/15	01/11/15	19	C
	TEST-13-00013-DST-288-B	7 days concrete compressive strength for roof slab of flow control valve chamber at Sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/143a**	01/12/15	02/11/15	01/20/15	8	A
	TEST-13-00013-DST-289-A	7 days concrete compressive strength for walls of inlet Shavi Shamron chamber at Sta. 1+159 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/142**	12/23/14	01/22/15	01/11/15	19	C

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-289-B	8 days concrete compressive strength for walls of inlet Shavi Shamron chamber at Sta. 1+159 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/142a**	01/12/15	02/11/15	01/20/15	8	A
	TEST-13-00013-DST-290-A	7 days concrete compressive strength for walls of BFV chamber (Shavi Shamron outlet chamber) at Sta. 1+172 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/302**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-291-A	7 days concrete compressive strength for roof slab of BFV chamber (Shavi Shamron outlet chamber) at Sta. 1+172 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/362**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-292-A	28 days concrete compressive strength for base slab for inlet Shavi Shamron flow monitoring chamber at Sta. 1+159 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/33a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-293-A	28 days concrete compressive strength for base slab of FCV chamber at Sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/236a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-294-A	28 days concrete compressive strength for walls of FCV chamber at Sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/295a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-295-A	28 days concrete compressive strength for drainage ditches from Sta. 1+800 to Sta. 1+900 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/35a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-296-A	28 days concrete compressive strength for drainage ditches from Sta. 7+470 to Sta. 7+356 ,Sta. 7+185 to Sta. 7+021, Sta. 6+992 to Sta. 6+983 , Sta. 5+772 to Sta. 5+761 & near Bazzariya at Sta. 8+200 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/322a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-297-A	28 days concrete compressive strength for drainage ditches from Sta. 0+520 to Sta. 0+090 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/34a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-298-A	28 days concrete compressive strength for drainage ditches at Sta. 1+350 ,Sta. 1+322 tpo Sta. 1+369 & Sta. 1+806 to Sta. 1+933 of grade B250- Source MUWASI Ready-Mix Plant /**Reports NO. M/1411/323a**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-299-A	Marshall Test for ¾ '' Asphalt reinstatement from Sta. 1+000 to Sta. 0+520 (segment B) -Source Development Co./**Reports NO. M/1412/435**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-300-A	Marshall Test for ¾ '' Asphalt reinstatement from Sta. 0+520 to Sta. 0+007(segment B) -Source Development Co./**Reports NO. M/1412/450**	01/04/15	02/03/15	01/11/15	7	A
	TEST-13-00013-DST-301-A	Marshall Test for ¾ '' asphalt RHS shoulders from Sta. 1+240 to Sta. 2+600- Source Abu Sukar Co./**Reports NO. M/1412/491**	01/12/15	02/11/15	01/20/15	8	A
	TEST-13-00013-DST-302-A	Marshall Test for ¾ '' asphalt RHS shoulders from Sta. 2+600 to Sta. 4+050 - Source Abu Sukar Co./**Reports NO. M/1412/504**	01/12/15	02/11/15	01/20/15	8	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-303-A	Marshall Test for ¾ '' asphalt LHS shoulders from Sta. 3+400 to Sta. 2+180 - Source Abu Sukar Co./**Reports NO. M/1501/2**	01/12/15	02/11/15	01/20/15	8	A
	TEST-13-00013-DST-304-A	Marshall Test for ¾ '' asphalt RHS shoulders from Sta. 4+300 to Sta. 5+250 & LHS shoulders from Sta. 2+180 to Sta. 1+240 -Source Abu Sukar Co./**Reports NO. M/1501/4**	01/12/15	02/11/15	01/20/15	8	A
	TEST-13-00013-DST-305-A	28 days concrete compressive strength for roof slab of flow control valve chamber at Sta. 1+174 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/143a**	01/12/15	02/11/15	01/20/15	8	A
	TEST-13-00013-DST-306-A	28 days concrete compressive strength for walls of inlet Shavi Shamroon chamber at Sta. 1+159 of grade B350- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/142a**	01/12/15	02/11/15	01/20/15	8	A
	TEST-13-00013-DST-307-A	Marshall Test for ¾ '' asphalt RHS shoulders from Sta. 4+050 to Sta. 4+300 & LHS shoulders from Sta. 4+300 to Sta. 3+400 -Source Abu Sukar Co./**Reports NO. M/1412/521**	01/13/15	02/12/15	01/27/15	14	A
	TEST-13-00013-DST-308-A	28 days concrete compressive strength for foundation of BFV chamber at Sta. 1+172 & roof slab of combined AV/AR & BFV chamber at Sta. 1+162- Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/221a**	01/15/15	02/14/15	01/27/15	12	A
	TEST-13-00013-DST-309-A	28 days concrete compressive strength for walls of combined AV/AR & BFV chamber at Sta. 1+162 - Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/69a**	01/15/15	02/14/15	01/27/15	12	A
	TEST-13-00013-DST-310-A	28 days concrete compressive strength for roof slab of inlet Shavi Shamron chamber at Sta. 1+159 - Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/261a**	01/15/15	02/14/15	01/27/15	12	A
	TEST-13-00013-DST-311-A	28 days concrete compressive strength for walls of BFV Shavi Shamron outlet at Sta. 1+172 chamber - Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/302a**	01/15/15	02/14/15	01/27/15	12	A
	TEST-13-00013-DST-312-A	28 days concrete compressive strength for roof slab of BFV outlet Shavi Shamron chamber at Sta. 1+172 of grade B 350 - Source MUWASI Ready-Mix Plant /**Reports NO. M/1412/362a**	01/18/15	02/17/15	01/27/15	9	A
	TEST-13-00013-DST-313-A	Somsom aggregate test from stock Piles at Sta. 0+200(sewer line) for trench bedding/**Reports NO. M/1501/70**	01/18/15	02/17/15	01/28/15	10	A
	TEST-13-00013-DST-314-A	Backfill material test for sewer line from stock pile /**Reports NO. M/1501/69**	01/20/15	02/19/15	01/28/15	8	A
	TEST-13-00013-DST-315-A	Marshall Test for ¾ '' asphalt RHS shoulders from Sta. 5+250 to Sta. 6+440 - Source Abu Sukar Co./**Reports NO. M/1501/59**	01/20/15	02/19/15	01/28/15	8	A
	TEST-13-00013-DST-316-A	Marshall Test for ¾ '' asphalt RHS shoulders from Sta. 6+440 to Sta. 7+300 - Source Abu Sukar Co./**Reports NO. M/1501/68**	01/20/15	02/19/15	01/28/15	8	A

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-TO-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project (DST)

SUBMITTAL			TRACKING DATES				Approval Status
Spec. No.	Submittal No	Description	Submitted on (M/D/Y)	Return Date AS Contract	Returned on (M/D/Y)	Review Days	(A,B,C,D,E)
	TEST-13-00013-DST-317-A	Fabrication Bends Radiographic test results by Morex company(Examination date Oct. 21, 2014, bends 6 inch, QTY: 5 pieces & field joint 12 inch ,QTY: 6 pieces	01/20/15	02/19/15	01/25/15	5	A
	TEST-13-00013-DST-318-A	Somsom aggregate test from stock Piles at Sta. 0+100(Burqa pipeline) for trench bedding/**Reports NO. M/1501/107**	01/25/15	02/24/15	01/28/15	3	A
	TEST-13-00013-DST-319-A	Single size aggregate test from stock Piles at Sta. 0+100(Burqa pipeline) for trench backfilling/**Reports NO. M/1501/108**	01/25/15	02/24/15	01/28/15	3	A
	TEST-13-00013-DST-320-A	Marshall Test for ¾ '' asphalt LHS shoulders from Sta. 7+370 to Sta. 6+250 - Source Abu Sukar Co./**Reports NO. M/1501/124**	01/25/15	02/24/15	02/15/15	21	A
	TEST-13-00013-DST-321-A	Marshall Test for ¾ '' asphalt LHS shoulders from Sta. 6+250 to Sta. 5+800 - Source Abu Sukar Co./**Reports NO. M/1501/130**	01/25/15	02/24/15	02/15/15	21	A
	TEST-13-00013-DST-322-A	Acrylic Paint Test /**Reports NO. M/1501/204**	01/27/15	02/26/15	02/03/15	7	A
	TEST-13-00013-DST-323-A	Base Course Comprehensive Test from Stock Piles in site (Trench Backfilling for Burqa pipeline-Source Al Ashqar Crusher/**Reports NO. M/1501/106**	02/01/15	03/03/15	02/15/15	14	A
	TEST-13-00013-DST-324-A	7 days concrete compressive strength for Silat Al Daher connection pad at the end of segment C of grade B 350 - Source MUWASI Ready-Mix Plant **/Reports NO. M/1501/242**	02/09/15	03/11/15	02/15/15	6	A
	TEST-13-00013-DST-325-A	Compaction degree & thickness for second layer of asphalted trench(core test) for Al Foundqumiya -segment B–Material Source Development Co. &Abu Sukar Co./**Reports NO. M/1502/10**	02/10/15	03/12/15	02/23/15	13	A
	TEST-13-00013-DST-326-A	Marshall Test for ¾ '' asphalt LHS shoulders from Sta. 4+300 to Sta. 5+800 - Source Abu Sukar Co./**Reports NO. M/1501/145**	02/17/15	03/19/15		PE	
	TEST-13-00013-DST-327-A	Marshall Test for ¾ '' asphalt LHS shoulders from Sta. 7+600 to Sta. 7+355- Source Abu Sukar Co./**Reports NO. M/1501/105**	02/17/15	03/19/15		PE	
	TEST-13-00013-DST-328-A	Field compaction test at Sta. 1+090, Sta. 0+930 ,Sta. 0+760 & Sta. 0+590/**Reports NO. M/1502/246**	02/25/15	03/27/15		PE	
	TEST-13-00013-DST-329-A	Marshall Test for ¾ '' asphalt RHS shoulders from Sta. 7+370 to Sta. 8+200- Source Abu Sukar Co./**Reports NO. M/1502/92**	02/26/15	03/28/15		PE	
	TEST-13-00013-DST-330-A	28 days concrete compressive strength for Silat Al Daher connection pad at the end of segment C of grade B 350 - Source MUWASI Ready-Mix Plant **/Reports NO. M/1501/242a**	02/26/15	03/28/15		PE	
	TEST-13-00013-DST-331-A	Field compaction test at Sta. 0+430, Sta. 0+150,Sta. 0+030 & Sta. 0+030 to Sta. 0+025/**Reports NO. M/1502/273 & M/1502/260**	02/26/15	03/28/15		PE	

DV = Division A= No Exceptions Noted B = Make Corrections Noted C = Amend-Resubmit D= Rejected-Resubmit E= Review Not Required

G | RFI's Log for the Reporting Period

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM INPII
CONTRACT NO. AID-294-I-00-12-00005
TASK ORDER #13, Deir Sharaf Main Pipeline Project
RFIs log - DST

SUBMITTAL				TRACKING DATES			Approved By
Spec. No.	Submittal No	Description	DV	Submitted on (M/D/Y)	Returned on (M/D/Y)	Review Days	
	RFI-13-00013-DST-001	Hydraulic characteristics of flow control valves, Deir Sharaf Main Pipeline Project (DST),Task order # 13	DST	12/05/13	12/22/13	17	Talal Attalah
	RFI-13-00013-DST-002	Pressure rating for fittings and valves located downstream of pressure reducing valves in water meter connection chambers/ Deir Sharaf Main Pipeline Project –task order #13	DST	12/19/13	01/05/14	17	Talal Attalah
	RFI-13-00013-DST-003	Using Steel mini guard around trenches instead off concrete barrier	DST	02/04/14	02/16/14	12	Talal Attalah
	RFI-13-00013-DST-004	Marking tape above the water pipe in the drainage ditch	DST	02/09/14	02/27/14	18	Talal Attalah
	RFI-13-00013-DST-005	250 mm washout chamber	DST	02/13/14	03/03/14	18	Talal Attalah
	RFI-13-00013-DST-006	250 mm Gate valve	DST	02/13/14	03/02/14	17	Talal Attalah
	RFI-13-00013-DST-007	Using steel mini guard around trenches instead of concrete barrier	DST	02/20/14	03/12/14	20	Talal Attalah
	RFI-13-00013-DST-008	Milling of Existing Asphalt	DST	02/26/14	03/11/14	13	Talal Attalah
	RFI-13-00013-DST-009	Existing Concrete and Stone Walls_ Deir Sharaf Project	DST	03/02/14	03/05/14	3	Talal Attalah
	RFI-13-00013-DST-010	200 and 250 mm Future Connections	DST	03/02/14	03/25/14	23	Talal Attalah
	RFI-13-00013-DST-011	Location for valve and connection chambers at Deir Sharaf Main Pipeline Task Order #13	DST	03/25/14	04/23/14	29	Talal Attalah
	RFI-13-00013-DST-012	Using Steel Mini Guard Instead Of Concrete Barrier from Sta. 9+702 to Sta. 12+120.	DST	03/25/14	04/09/14	15	Talal Attalah
	RFI-13-00013-DST-013	The thickness of asphalt over trench with 300 mm pipes	DST	04/02/14	04/21/14	19	Talal Attalah
	RFI-13-00013-DST-014	Concrete ditch/ Deir Sharaf Main Pipeline Project –task order #13	DST	05/08/14	05/14/14	6	Talal Attalah
	RFI-13-00013-DST-015	Base Course Under Concrete Ditches / Deir Sharaf Main Pipeline Project –task order #13	DST	06/03/14	06/29/14	26	Talal Attalah
	RFI-13-00013-DST-017	Dismantling joint for Qussin Chamber/task order #13	DST	06/25/14	07/02/14	7	Talal Attalah
	RFI-13-00013-DST-018	Flow Control Valve at Deir Sharaf Main Pipeline Project- task order #13	DST	07/03/14	07/17/14	14	Talal Attalah
	RFI-13-00013-DST-019	Propeller water meter as alternative than electro-magnetic water meters for bypass lines / Deir Sharaf Main Pipeline Project –task order #13	DST	07/14/14	07/24/14	10	Talal Attalah
	RFI-13-00013-DST-020	CMC response to RFI # 18 regarding FCV at Deir Sharaf Main Pipeline Project –task order #13	DST	07/22/14	08/03/14	12	Talal Attalah
	RFI-13-00013-DST-021	Design working pressure - Dial ranges table	DST	09/07/14	09/11/14	4	Osama Al Khalili

H | Geo-MIS DATA COLLECTION SHEET
Generated Person Days of Employment

USAID WEST BANK/ GAZA

INFRASTRUCTURE NEEDS PROGRAM INPII

CONTRACT NO. AID-294-I-00-12-00005

TASK ORDER NO. AID-294-TO-13-00013

Deir Sharaf Main Pipeline Project (DST)

Temproray Job Days Summary Report

Task Order Name: Deir Sharaf Main Pipeline Project

PERIOD FROM: December 03, 2013

CONTRACTOR: APCO/ArCon

PERIOD TO: February 28, 2015

Date		Site Staff Job Days**					Total Job Days	No of Full Time Equivalent (FTE) Jobs in the Month*	Notes of Comments	Females Working Hours	Female Working Days
Month	Year	Management	Engineers	Skilled Labor	Unskilled Labor	Other					
October	2012						0	0			
November	2012						0	0			
December	2012						0	0			
January	2013						0	0			
February	2013						0	0			
March	2013						0	0			
April	2013						0	0			
May	2013						0	0			
June	2013						0	0			
July	2013						0	0			
August	2013						0	0			
September	2013						0	0			
Total of FY 2013							0	0			
October	2013						0	0			
November	2013						0	0			
December	2013	23.0	7.0	46.0	0.0	0.0	76.0	3.2		184	23.0
January	2014	90.0	55.0	31.5	53.0	0.0	229.5	9.6		360	45.0
February	2014	95.0	90.9	25.0	48.0	1.0	259.9	10.9		384	48.0
March	2014	120.4	113.8	108.4	109.6	0.5	452.7	19.0		432	54.0
April	2014	167.6	128.4	627.4	312.0	2.6	1238.0	52.0		400	50.0
May	2014	166.6	126.6	637.5	314.5	0.0	1245.3	52.3		387	48.4
June	2014	151.1	117.4	735.0	371.4	0.0	1374.9	57.8		384	48.0
July	2014	94.6	73.1	307.4	155.0	0.0	630.1	26.5		281	35.1
August	2014	154.4	119.8	845.8	408.8	0.0	1528.6	64.2		397	49.6
September	2014	151.9	123.1	935.1	381.4	0.0	1591.5	66.9		396	49.5
Total of FY 2014							8626.4	362.5		3605	450.6
October	2014	109.4	84.9	644.6	236.6	0.0	1075.5	45.2		288	36.0
November	2014	127.0	106.1	599.0	254.4	0.0	1086.5	45.7		352	44.0
December	2014	122.8	107.9	546.6	160.8	0.0	938.0	39.4		408	51.0
January	2015	122.6	99.6	582.6	189.6	0.0	994.5	41.8		352	44.0
February	2015	117.0	72.8	435.1	142.0	0.0	766.9	32.2		350	43.8
March	2015						0.0	0.0			
April	2015						0.0	0.0			
May	2015						0.0	0.0			
June	2015						0.0	0.0			
July	2015						0.0	0.0			
August	2015						0.0	0.0			
September	2015						0.0	0.0			
Total of FY 2015							4861.4	204.3		1750	218.8

Note :

* No of Full Time Equivalent (FTE) Jobs in the Month = Total Job Days / Avg. Days in the Month(23.8)

** This data collection sheet is for Palestinian staff only , experts and foreign employee shall not be included.

Numbers are rounded to the nearest decimal number.

Daily Work Force /February 2015
Project: **Deir Sharaf Main Pipeline Project**
Contract No. AID-294-I-00-12-00005

APCO/ArCon CONSTRUCTION AND SERVICES

Daily Work Force /February 2015

Date	Name of Contractor /Subcontractor	Total Working Hours: Management				Engineers			Skilled							Unskilled				Man-days			
		Task Order Manager(F)	Quality Control Manager	CWI	Safety & Environmental Compliance Officer	Project Manager / Engineer	Office Engineer(F)	Office Engineer	Foreman	Surveyor	Equipment Operator	Skilled Labor	Carpenter	Welder	Steel Fixer	Unskilled Labor	Flagmen	Security Guard	Office Boy	Total Management	Total Engineers	Total Skilled	Total Unskilled
February 1, 2015	APCO/ArCon	8	10	10	8	8	8											8	8	6	3	30	6
	Subcontractor		11			11			18		66	137		22		32							
February 2, 2015	APCO/ArCon	8	8	9	8	9	8											8	8	6	4	31	8
	Subcontractor		11			11			22		66	140		20		50							
February 3, 2015	APCO/ArCon	8	10	10	8	8	8											8	8	6	3	30	8
	Subcontractor		10			11			20		60	140		20		50							
February 4, 2015	APCO/ArCon	8	10	10	8	8	8											8	8	6	3	23	8
	Subcontractor		10			10			20		56	90		20		50							
February 5, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	22	6
	Subcontractor		8			8			16		48	96		16		32							
February 6, 2015	APCO/ArCon																			0	0	0	0
	Subcontractor																						
February 7, 2015	APCO/ArCon	8	8	10	8	10	8											8	8	6	4	46	11
	Subcontractor		10			10			30		130	190		20		70							
February 8, 2015	APCO/ArCon	8	8	9	8	8	8											8	8	5	3	39	12
	Subcontractor		10			10			20		68	206		18		80							
February 9, 2015	APCO/ArCon	8	8	11	8	11	8											8	8	6	4	22	8
	Subcontractor		11			11			22		45	84		22		44							
February 10, 2015	APCO/ArCon	8	8	9	8	8	8											8	8	5	3	22	7
	Subcontractor		8			9			18		32	108		18		36							
February 11, 2015	APCO/ArCon		8	8	8	8	3											8	8	3	2	9	2
	Subcontractor					8			16		8	50											
February 12, 2015	APCO/ArCon	8	8	8	8	8												8	8	4	2	8	2
	Subcontractor					8			16			40		8									
February 13, 2015	APCO/ArCon																			0	0	0	0
	Subcontractor																						
February 14, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	1	2
	Subcontractor		8			8			8														
February 15, 2015	APCO/ArCon	8	9	9	8	8	8											8	8	5	3	14	5
	Subcontractor		8			8			16		9	72		18		27							
February 16, 2015	APCO/ArCon	8	8	9	8	9	8											8	8	5	3	15	6
	Subcontractor		9			9			18		16	72		16		32							

Date	Name of Contractor /Subcontractor	Total Working Hours: Management				Engineers			Skilled							Unskilled				Man-days			
		Task Order Manager (F)	Quality Control Manager	CWI	Safety & Environmental Compliance Officer	Project Manager / Engineer	Office Engineer (F)	Office Engineer	Foreman	Surveyor	Equipment Operator	Skilled Labor	Carpenter	Welder	Steel fixer	Unskilled Labor	Flagmen	Security Guard	Office Boy	Total Management	Total Engineers	Total Skilled	Total Unskilled
February 17, 2015	APCO/ArCon	8	9	9	9	9	8											8	8	6	3	16	5
	Subcontractor		9			9			18		18	81		9		27							
February 18, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	12	4
	Subcontractor		8			8			16		8	64		8		16							
February 19, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	4	3	11	2
	Subcontractor					8			16		16	48		8									
February 20, 2015	APCO/ArCon																			0	0	0	0
	Subcontractor																						
February 21, 2015	APCO/ArCon		3			3	3											3	3	0	2	0	1
	Subcontractor					8																	
February 22, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	8	6
	Subcontractor		8			8			16			48				32							
February 23, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	23	7
	Subcontractor		8			8			16		32	128		8		40							
February 24, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	14	8
	Subcontractor		8			8			16		32	64				48							
February 25, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	17	7
	Subcontractor		8			8			16		32	80		8		40							
February 26, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	8	7
	Subcontractor		8			8			16			48				40							
February 27, 2015	APCO/ArCon																			0	0	7	0
	Subcontractor											56											
February 28, 2015	APCO/ArCon	8	8	8	8	8	8											8	8	5	3	6	4
	Subcontractor		8			8			16			32				16							
	APCO/ArCon																			0	0	0	0
	Subcontractor																						
	APCO/ArCon																			0	0	0	0
	Subcontractor																						
	APCO/ArCon																			0	0	0	0
	Subcontractor																						
Total																				117	73	435	142

USAID WEST BANK/ GAZA
INFRASTRUCTURE NEEDS PROGRAM
TASK ORDER NO: AID-294-TO-12-00013

Deir Sharaf Main Pipeline Project
Geo-MIS DATA COLLECTION SHEET

CONTRACTOR: APCO/ArCon

PERIOD FROM: Feb. 01, 2015
PERIOD TO: Feb. 28, 2015

DATE	Deir Sharaf Main Pipeline Project					SubTotal						SubTotal
	Management	Engineers	Skilled labor	Unskilled labor	Other		Management	Engineers	Skilled labor	Unskilled labor	Other	
February 1, 2015	5.9	3.4	30.4	6.0		45.6						
February 2, 2015	5.5	3.5	31.0	8.3		48.3						
February 3, 2015	5.8	3.4	30.0	8.3		47.4						
February 4, 2015	5.8	3.3	23.3	8.3		40.5						
February 5, 2015	5.0	3.0	22.0	6.0		36.0						
February 6, 2015	0.0	0.0	0.0	0.0		0.0						
February 7, 2015	5.5	3.5	46.3	10.8		66.0						
February 8, 2015	5.4	3.3	39.0	12.0		59.6						
February 9, 2015	5.8	3.8	21.6	7.5		38.6						
February 10, 2015	5.1	3.1	22.0	6.5		36.8						
February 11, 2015	3.0	2.4	9.3	2.0		16.6						
February 12, 2015	4.0	2.0	8.0	2.0		16.0						
February 13, 2015	0.0	0.0	0.0	0.0		0.0						
February 14, 2015	5.0	3.0	1.0	2.0		11.0						
February 15, 2015	5.3	3.0	14.4	5.4		28.0						
February 16, 2015	5.3	3.3	15.3	6.0		29.8						
February 17, 2015	5.5	3.3	15.8	5.4		29.9						
February 18, 2015	5.0	3.0	12.0	4.0		24.0						
February 19, 2015	4.0	3.0	11.0	2.0		20.0						
February 20, 2015	0.0	0.0	0.0	0.0		0.0						
February 21, 2015	0.4	1.8	0.0	0.8		2.9						
February 22, 2015	5.0	3.0	8.0	6.0		22.0						
February 23, 2015	5.0	3.0	23.0	7.0		38.0						
February 24, 2015	5.0	3.0	14.0	8.0		30.0						
February 25, 2015	5.0	3.0	17.0	7.0		32.0						
February 26, 2015	5.0	3.0	8.0	7.0		23.0						
February 27, 2015	0.0	0.0	7.0	0.0		7.0						
February 28, 2015	5.0	3.0	6.0	4.0		18.0						
	0.0	0.0	0.0	0.0		0.0						
	0.0	0.0	0.0	0.0		0.0						
	0.0	0.0	0.0	0.0		0.0						
Sub Total of February	117.0	72.8	435.1	142.0	0.0	**766.9**						

Feb, 2015	**Total Job Days**	**No of Full Time Equivalent (FTE) Jobs**
	766.9	32.2

I | RISK REGISTER LOG

Risk Register Log

PROBABILITY CATEGORIES			
Description		Prob	Scale Value
H	Probable	>70%	3
M	Could happen	30-70%	2
L	Improbable	<30%	1

			PROBABILITY		
			Low/Improbable	Medium/Could Happen	High/Probable
			1	2	3
IMPACT	High/ Critical	3	3	6	9
	Medium/ Serious	2	2	4	6
	Low/ Marginal	1	1	2	3

IMPACT CATEGORIES			
Description		Guide Scenario	Scale Value
H	Critical	Impact that involves significant delay, rework, modification or reassessment.	3
M	Serious	Impact or setback that causes delay, additional work and reassessment but containable.	2
L	Marginal	Impact has some effect causing rework or reassessment but easily handled.	1

- Key/ Critical Risks - closely monitor, manage & develop fallback plans
- Intermediate Risks - monitor and manage to mitigate
- Minor Risks

Risk Event	What is it that you are working to avoid or reduce the likelihood or impact of occurring? Risks are future events that could interfere with achievement of objectives.
Risk Cause	What are the triggers, sources or circumstances that could act alone or together to increase the likelihood of the Risk Event occurring? There are usually multiple causes leading to a Risk Event.
Risk Impact	If this Risk Event did occur, how would it impact objectives? What are the longer-term or cumulative consequences?
Risk Owner	Who will take the lead on this mitigation?

T.O 13- Risk Register Log

RISK IDENTIFICATION							RISK ASSESSMENT					RISK RESPONSE			MONITORING & CONTROLLING	
REF	CATEGORY	RISK	RISK CAUSE	IMPACT/ CONSEQUENCE	RAISED BY	DATE RAISED	PROBLTY.	IMPACT	RISK RATING	COST IMPACT	SCHEDULE IMPACT	RESPONSE STRATEGY	RESPONSE PLAN	RISK OWNER	STATUS	NOTES
1	Design	No Risks during this reporting period.							0							
2	Construction								0							
3	Owner								0							
4	USAID								0							
5	Contractor								0							
6	External								0							
7	Procurement								0							
8	Skills								0							
9	Complexity								0							
10	Resources								0							
11	Communications								0							
									0							
