

Integrated Community Development Fund

Quarterly Report to USAID/Bolivia Integrated Alternative Development Office

July - September 2010

Award N°: 511-A-00-05-00153-00

September 2010

Contact:

Treena Bishop
Team Leader ICDF

Calle 11 # 480
Esq. Sánchez Bustamante
Calacoto
La Paz, Bolivia
Tel/Fax: (+591) 2 – 2793206
E-mail: tbishop@acdivoca.org.bo

ACDI/VOCA is the implementer of the Integrated Community Development Fund,
financed by USAID.

La Paz Office:

Calle 11 # 480 Esq. Sánchez
Bustamante, Calacoto
La Paz, Bolivia
Tel/Fax: (591-2) 279-3206
info@acdivocabolivia.org

La Asunta Office:

Av. Oswaldo Natty s/n
La Asunta – Sud Yungas
Cel.: 767-65965

Palos Blancos Office:

Esquina Plaza Principal
Colonia Brecha Area 2
Palos Blancos, Bolivia
Tel/Fax: (2) 873-1613 – (2)
873-1614

Coroico Office:

Calle Tomás Manning
s/n frente Convento
Madres Clarisas
Coroico - Bolivia
Tel/Fax: (2) 289-5568

Washington, DC Office:

50 F Street NW, Suite 1075
Washington, DC 20001
Tel: (202) 638-4661
<http://www.acdivoca.org>

TABLE OF CONTENTS

I. EXECUTIVE SUMMARY	5
II. ICDF IN NUMBERS	11
III. SUMMARY OF ACTIVITIES	18
A. COMMUNITY DEVELOPMENT	18
B. ECONOMIC DEVELOPMENT	25
C. CROSS-CUTTING ACTIVITIES	31
IV. PERFORMANCE INDICATORS RESULTS	34
A. Intermediate Result 1	40
B. Intermediate Result 2	43
C. Cross-cutting Indicators	46
V. LOOKING BACK – A REVIEW OF THE QUARTER.....	47
VI. LOOKING FORWARD	47
VII. FINANCIAL INFORMATION	¡Error! Marcador no definido.
VIII. ANNEXES.	49
ANNEX I - Budget Pipeline Report	¡Error! Marcador no definido.
ANNEX II. Success Stories.....	51
ANNEX III Project Status Report (Matrix).....	57

This Quarterly Progress Report is made possible by the generous support of the American people through the United States Agency for International Development (USAID). The contents are the responsibility of ACDI/VOCA and do not necessarily reflect the views of USAID or the United States Government.

LIST OF ACRONYMS

CA	COOPERATIVE AGREEMENT
CC	CROSS-CUTTING INDICATOR
CCVV	CAMINOS VECINALES
CT	TECHNICAL COMMITTEE (<i>Comité Técnico</i> in Spanish)
DRNMA	DEPARTMENT OF NATURAL RESOURCES AND ENVIRONMENT
ICDF	INTEGRATED COMMUNITY DEVELOPMENT FUND
IL	IMPLEMENTATION LETTER
IR	INTERMEDIATE RESULT
LOP	LIFE OF PROJECT
M&E	PERFORMANCE MONITORING AND EVALUATION
NBI	UNSATISFIED BASIC NEEDS INDEX
PMP	PERFORMANCE MONITORING PLAN
PSB	THE PLURINATIONAL STATE OF BOLIVIA
RAI	INDUSTRIAL ENVIRONMENTAL REGISTRY (<i>Registro Ambiental Industrial</i> in Spanish)
RFRA	REQUEST FOR REVISED APPLICATION
SO	STRATEGIC OBJECTIVE
TC	TROPICS OF COCHABAMBA

UAC-CP	UNIDAD ACADÉMICA CAMPESINA DE CARMEN PAMPA
UCB	CATHOLIC UNIVERSITY OF BOLIVIA
USAID	UNITED STATES AGENCY FOR INTERNATIONAL DEVELOPMENT
USG	UNITED STATES GOVERNMENT
VCDI	VICE MINISTRY FOR COCA AND INTEGRATED DEVELOPMENT
YCADF	YUNGAS COMMUNITY ALTERNATIVE DEVELOPMENT FUND

I. EXECUTIVE SUMMARY

Through Cooperative Agreement (CA) No. 511-A-00-05-00153-00, dated August 1, 2005, USAID/Bolivia awarded ACDI/VOCA the Integrated Community Development Fund (ICDF) program for a period of five years. This agreement was later modified to include civil society and municipal strengthening activities. Pursuant to the terms of Modification 7 approved by USAID/Bolivia, ICDF methodology was subsequently adjusted to more directly respond to the diverse development needs as well as support the policies and strategy of the Plurinational State of Bolivia (PSB) as outlined in Implementation Letter (IL) No. 043. The modification also provided for a restructuring of the program to reflect two components: economic and community development. In Modification 14, funding was added to the agreement allowing the ICDF to respond to urgent needs identified by the Vice Ministry of Coca and Integrated Development (VCDI), such as school furniture, culverts for road maintenance, tubing to expand and improve existing potable water systems and hospital equipment.

During the first quarter of the 2010 fiscal year, ACDI/VOCA responded to a Request for Revised Application (RFRA) in order to include new activities and/or broaden the reach of activities already in implementation. The proposal reflected the RFRA's strong emphasis in the region of La Asunta and the implementation of primarily community development activities. The RFRA was approved in December 2009, resulting in Modification 15.

In June of 2010, the ICDF responded to another RFRA resulting in Modification 16, which was approved by USAID in July 2010. This modification extends the ICDF's life of project (LOP) by three months, or until December 31, 2010, and provides additional funds for new project activities. New projects to be implemented under Modification 16 include the provision of school furniture and educational material, healthcare equipment, and health center and school renovation or construction. A number of new projects to be implemented with this additional funding were in the process of being identified at the close of the quarter. A technical committee (CT for its acronym in Spanish) meeting will be held in the first half of October in which these projects will be considered.

On August 27, 2010, ACDI/VOCA submitted its response to RFRA 511-10-008. The revised application consists of a two-year extension and additional funding to expand the ICDF's activities, including to geographic regions in which the ICDF has not previously worked. ACDI/VOCA expects that USAID's response to this application will be issued in the coming quarter. The decision will significantly shape the main activities of the next reporting period.

Throughout the aforementioned series of methodological and geographical adjustments, the ICDF has maintained its primary goal of supporting the joint efforts of the U.S. government (USG) and the PSB to establish a sustainable economy in Bolivia's coca-producing regions. The ICDF's

strategy is to meet basic human needs and alleviate poverty by improving social and economic conditions in the Yungas of La Paz and, formerly, the Tropics of Cochabamba (TC).

This report covers the fourth quarter of the 2010 USG fiscal year, encompassing activities carried out between July 1 and September 30, 2010. At the close of the quarter, the total number of small-grant development projects under the ICDF was 625, including 349 community development projects and 276 economic development projects. During the quarter, five new projects were added. At the end of the quarter, five projects were in the design phase, two were under procurement, and 76 were in implementation. Fifty-two ICDF projects were concluded during this reporting period. Of these, 40 were community development projects and 12 were from the economic development portfolio. To date, 542 subaward projects have been completed.

During the reporting period, the ICDF accomplished multiple key activities contributing to its overall objectives. Highlights include:

- The VCDI called for one CT in which a variety of projects and other aspects related to the implementation of the ICDF were discussed. One result of this CT was that five projects were approved. An additional coordinating meeting was held to discuss ideas for new projects, which based on the feedback received, will be further developed and presented for consideration during the first CT of the next reporting period.
- Forty projects within the community development included a new dormitory for the *Unidad Académica* which will house 170 female students and 18 projects in La Asunta, Palos Blancos and Coroico.
- The final designs for the following projects were
 - Coripata Bus Terminal in the municipality of
 - Alto Remolinos potable water system in the
 - San Miguel de Huachi potable water system in
 - San Joaquin potable water system in the
 - Cotapata sewage system in the municipality of
 - San Agustín sewage system in the municipality
 - Five school bathrooms for different schools in the municipality of La Asunta.



component were completed. These *Campesina* Carmen Pampa (UAC-CP), that expanded in the municipalities of

completed:

Coripata
municipality of Palos Blancos
the municipality of Palos Blancos
municipality of Coroico
La Asunta
of Coripata

- The ICDF broke ground on the construction of the following projects:
 - Cotapata town square in the municipality of La Asunta
 - Housing for healthcare personnel in Los Olivos, Palos Blancos
 - Teacher housing in La Cascada, Palos Blancos
 - Bajo Inicua potable water system, in the municipality of Palos Blancos.
- On July 3rd and 4th, the second cervical cancer prevention and early detection campaign was carried out in La Asunta. Volunteer healthcare personnel from the Bolivian Cancer Foundation conducted the campaign, during which approximately 160 women were screened for cancer and trained in cancer prevention and early detection. The results of the exams have been sent to the La Asunta hospital, where the attending physician will follow up with participants.
- On July 10th, volunteer veterinarian, Dr. Daniel Miller, arrived in Bolivia where he worked for three weeks in the Alto Beni region of the Yungas with dairy and beef farmers. The primary objective of Dr. Miller's visit was to provide specialized technical assistance in bovine disease prevention and control and general bovine health and herd management.



One of the 300 families from La Asunta enjoying their new stove

- The project, "Improving Family Quality of Life through the Kitchen," was completed this quarter. As a result, 300 families from the municipality of La Asunta are now trained in the construction and use of improved, ecological stoves. This project will have a significant positive impact on participating families' by reducing the risk of respiratory illnesses and lowering their firewood consumption.

of plantain. They sold their fruit for an average price markets of La Asunta and Caranavi.

- The ICDF conducted trainings on coffee processing producers in La Asunta. Samples of producers' coffee

- Plantain producers in the municipality of La Asunta harvested a total of more than 2,300 heads of 45 Bs. (US\$ 6.35) in the local



techniques for different groups of were sent to the Bolivian Federation

of Export-Quality Coffee Producers' (FECAFEB's) quality control laboratory. The samples were given a grade between 80 and 84, which ranks ICDF-assisted producers' crops as specialty coffee. The FECAFEB sent the samples to potential specialty coffee buyers in Japan and Canada who are scheduled to visit Bolivia during October. In addition, the coffee census was concluded, the results of which will be presented to stakeholders at the beginning of the next reporting period.

- Activities to promote horticulture production in La Asunta continued, with the objective of meeting an unsatisfied local demand for vegetables within the municipality. The first harvest of tomatoes, lettuce and cucumbers was sold successfully in local markets.
- Amaranth promotion activities in the municipalities of Coroico and Irupana were concluded. A total of 85 hectares of amaranth was established by 180 producers from 19 different communities. Preliminary activities for a second phase of amaranth production promotion that will encompass the municipality of Coripata as well as Coroico and Irupana began. The ICDF expects approximately 220 producers to participate in this second phase.
- On July 2nd, the ICDF team participated in an event organized by the United States Embassy in celebration of the U.S. Independence Day. Several producers who participate in Integrated Alternative Development (IAD) programs had the opportunity to showcase their products during the event.
- At the request of the VCDI, the ICDF, together with a small fair in the Sapecho community located in Participating producers of honey, stevia, eggs, show the results of their labor to Ms. Nemesia Achacollo, Minister of Rural Development and Land, Germán Loza, Vice Minister for Development and Felipe Cáceres, Vice Minister
- On August 12th, Mr. Russell Crandall, Director together with Germán Loza, Vice Minister for Felipe Cáceres, Vice Minister of Social Defense, Accompanying this delegation were John Chargé de Affairs, Rebecca Latorraca, Director of USAID/Bolivia's Integrated



Minister of Rural Development, Nemesia Achacollo, accompanied by other PSB representatives, tastes bakery products

with the ARCo project, organized a fair in the municipality of Palos Blancos. Bread and handicrafts were able to showcase their products to Nemesia Achacollo, the Minister of Rural Development and Land, Germán Loza, Vice Minister for Development and Felipe Cáceres, Vice Minister of Social Defense.

for Andean Affairs at the White House, Coca and Integrated Development and visited the Alto Beni region. Accompanying this delegation were John Chargé de Affairs, Rebecca Latorraca, Director of USAID/Bolivia's Integrated Alternative Development office and

representatives from the Narcotics Affairs Sector (NAS) and the Embassy of Brazil. The group visited the Martín Cárdenas School dormitory, which was constructed under the ICDF. At the school, the delegation toured the dormitory and spoke with students about their experiences of living and studying there. All of the guests visited a series of stands showcasing various integrated development supported products organized by the ICDF and ARCo projects. Producers from twelve different sectors participated.

- On September 3rd, the provision of equipment to five Alternative Education Centers (CEAs) was handed over in an event attended by Germán Loza, Vice Minister for Coca and Integrated Development, Mary Norris, Director of USAID/Bolivia's Integrated Alternative Development office, Cesar Guedes, Country Representative of the United Nations Office on Drugs and Crime (UNODC), the mayors of Coroico, Coripata, Irupana and Chulumani, the District Director of Education of Chulumani, local authorities and students. The implementation of this project was coordinated with the UNODC's, Bol- I80 project. The ICDF's role included the provision of kitchen equipment, tailoring and sewing machines, and books to the CEAs of Coroico, Chulumani, Coripata, Irupana and Palos Blancos.
- On September 18th, the municipal government of La Asunta organized the Second Ecological Product Fair of La Asunta, where producers assisted by the ICDF in honey, stevia, plantain, coffee and horticulture production, as well as those assisted by the ARCo project, showcased their work. This fair was attended by representatives of the VCDI, USAID, the mayor's office of La Asunta, the Federation of La Asunta and other local authorities as well as the general population of La Asunta. At the end of the fair, prizes provided by the ARCo project and the mayor's office were awarded. ICDF-assisted plantain producers won the first prize, stevia producers came away with the second prize, ICDF-supported beekeepers received the third prize, ARCo-assisted annatto producers won the fourth prize and an independent handicrafts producer earned the fifth prize.
- The new dormitory for the UAC-CP was inaugurated on September 29th. The event took place in the presence of Maruja Machaca, Representative of the VCDI, Rebecca Latorraca, Director a.i. of USAID/Bolivia, Ángel Miranda Huanca, the Municipal Mayor of Coroico, Clemente Mamani Condonera, President of the *Mancomunidad de Municipios de los Yungas de La Paz* (MMYLP), Padre Freddy Villar, Director of the UAC-CP, the UAC-CP student body and faculty and invited guests. The dormitory consists of a three-story infrastructure that contains 17 rooms designed to house a total the opportunity to speak with students and people who come from different to study at this important institution of
- The ICDF handed over school furniture in



Delivery of school furniture – Coroico

the municipalities of Yanacachi,

Chulumani, La Asunta, Coroico and Coripata on different occasions during the month of September. In total, more than 4,000 pieces of furniture were delivered to the schools with the goal of improving the quality of education for approximately 2,815 students from various communities throughout the mentioned municipalities.

- In late September, ACDI/VOCA Bolivia Catherine Gibbons, Technical Managing and direct supervisor of the ICDF team. Ms. majority of the ICDF team and had meetings understand in greater detail the unique implemented and the level of impact being



Delivery of school furniture – Coripata

received a week-long visit from Ms. Director for Community Development Gibbons visited various projects, met the with different stakeholders in order to context under which the ICDF is made.

II. ICDF IN NUMBERS

The VCDI convened one CT during the present reporting period. During this meeting, five new projects were approved; four of which are under the community development portfolio. The following table shows a breakdown of newly approved projects by portfolio and sub-portfolio.

Table 1. Projects approved during July– September 2010 quarter by portfolio and sub-portfolio

Portfolio	Sub-Portfolio	Total
Community Development	Potable Water	1
	Education	1
	Community Infrastructure	1
	Other	1
Community Development Subtotal		4
Economic Development	Agriculture	1
Economic Development Subtotal		1
Total		5

Two of the newly approved projects will be implemented in the municipality of Palos Blancos, one in the municipality of Irupana, and two will have a regional impact.

Table 2. Projects approved during July– September 2010 quarter by municipality, portfolio and sub-portfolio

Municipality	Project	Portfolio	Sub-portfolio
Irupana, Coroico and Coripata	Assistance to producers and development of the organic amaranth value chain in the Yungas of La Paz	Economic Development	Agriculture
Palos Blancos	Final design and construction of a covered multipurpose sports and recreation court for the Santa Ana de Mosevenes School	Community Development	Education
	Final design and construction of the Brecha I (Luz, Porvenir and Calama) potable water system	Community Development	Potable Water
Yungas Various	Institutional strengthening of the Vice Ministry for Coca and Integrated Development (VCDI)	Community Development	Community Strengthening
	Regional diagnostic study of new areas of intervention	Community Development	Various

The ICDF has a total of 625 projects in its portfolio (56 percent under community development, with the remaining 44 percent under economic development). Currently, seven projects are in the final design or acquisitions stage and 76 are being implemented. With 52 projects concluded during the reporting period, the total number of completed projects is now 542. Table 3 delineates the total number of ICDF projects by status and component.

Table 3. Number of projects by implementation status and by component

State of Project	Community Development	Economic Development	Total
Final Design	5	0	5
Acquisitions	2	0	2
Implementation	44	32	76
Completed	298	244	542
TOTAL	349	276	625

Fifty-two projects were concluded in the Yungas of La Paz. Forty of these were community development projects, while 12 belong to the economic development portfolio. Table 4 shows a breakdown of projects by status and region and Chart 1 demonstrates the distribution of projects by implementation status.

Table 4. Number of projects by implementation status and by region

State of Project	TC	Yungas	Total
Final Design		5	5
Acquisitions		2	2
Implementation		76	76
Completed	100	442	542
TOTAL	100	525	625

Chart 1 – Distribution of ICDF projects by implementation status

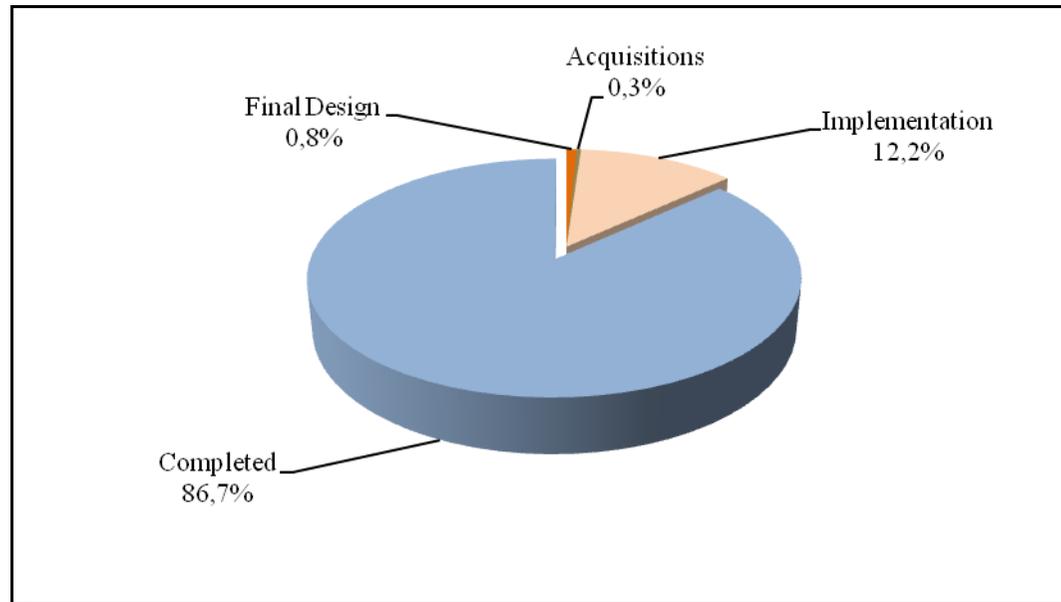


Chart 2 shows the number of new projects added to the ICDF portfolio each month compared with the number of projects completed during the same time period. Five new projects were added this quarter and 52 projects were concluded. ICDF presently has 83 active projects, which it expects to conclude by the end of the 2010 calendar year.

Chart 2. Cumulative number of ICDF sub-grant included in the portfolio and number of completed projects

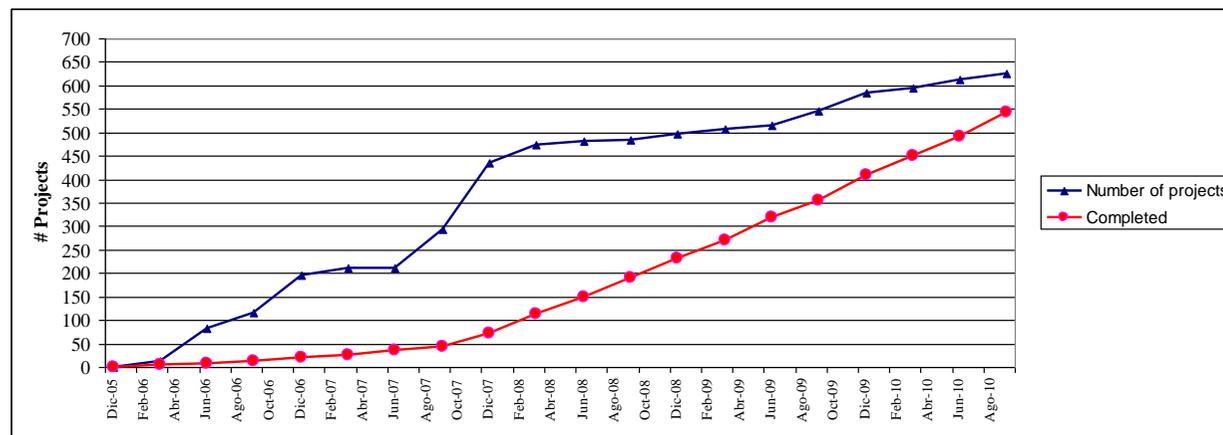


Table 5 shows a breakdown of the distribution of projects by region, municipality and portfolio. The municipality of La Asunta has the most projects, followed by Palos Blancos. Ten percent of both community and economic development projects in the Yungas benefit more than one municipality.

Table 5. Distribution of projects by region, municipality and portfolio

Region	Municipality	Community Development	Economic Development	Total
Yungas	Alto Beni	22	43	65
	Chulumani	30	15	45
	Coripata	35	15	50
	Coroico	33	7	40
	Irupana	14	2	16
	La Asunta	60	56	116
	Palos Blancos	52	42	94
	Yanacachi	19	31	50
	Various – Yungas	31	18	49
Subtotal Yungas		296	229	525

TC	Chimoré	8	6	14
	Entre Ríos	5	6	11
	Puerto Villarroel	19	12	31
	Shinahota	12	10	22
	Villa Tunari	5	7	12
	Various – TC	3	6	9
	Omereque	0	0	0
	Yapacani	1	0	1
Subtotal TC		53	47	100
Total		349	276	625

Chart 3 demonstrates the breakdown of community development projects by sector. The number of projects in the sub-portfolios of education and potable water is notable. This increase is attributed to the high impact activities that provided furniture and/or equipment for the expansion of access to healthcare, potable water and education in multiple municipalities that were added to the ICDF community development portfolio in late 2009 and during the second quarter of 2010. Chart 4 demonstrates the breakdown of economic development projects by sector.

Chart 3 – Number of community development projects by sector sub-portfolio


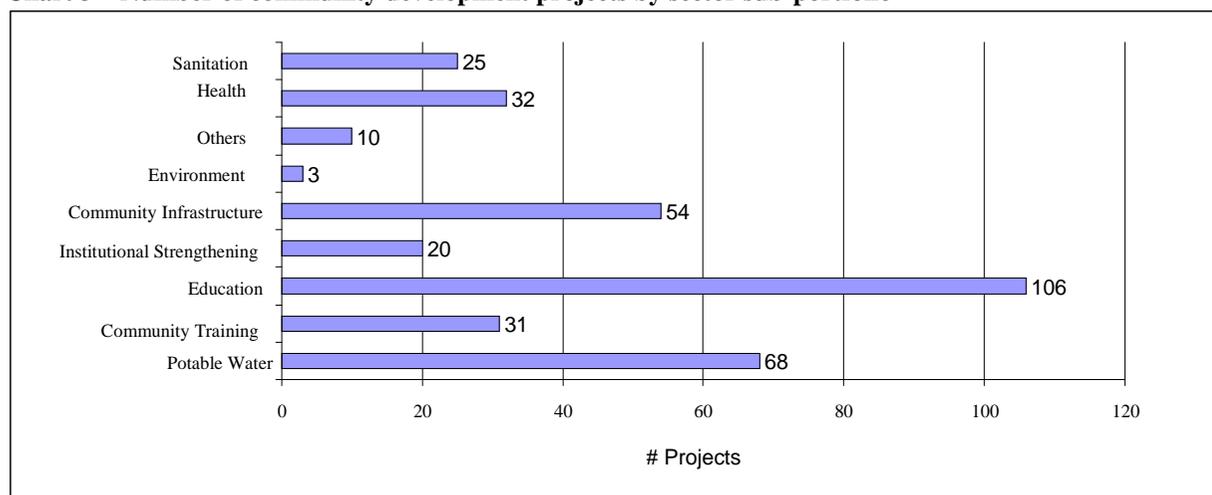


Chart 4 – Number of economic development projects by sector sub- portfolio

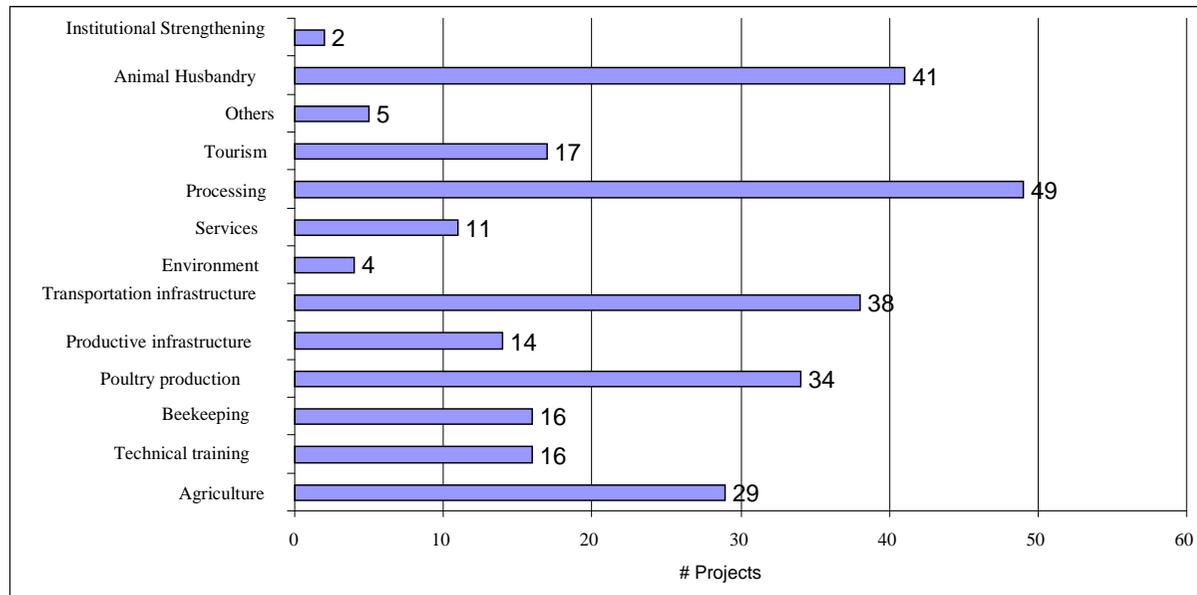

III. SUMMARY OF ACTIVITIES

A. COMMUNITY DEVELOPMENT

A total of 40 community development projects were concluded in the Yungas. These are presented by region and municipality in the following table:

Table 8: Community development projects completed during the July– September 2010 quarter

MUNICIPALITY	PROJECT
Chulumani	Provision of School Furniture for schools in the municipality of Chulumani.
	Refurbishment of the Cuchumpaya potable water system
Coripata	Provision of School Furniture for schools in the municipality of Coripata
	Final design of the San Agustín sewage system
	Furniture Provision for two schools: Charobamba and Huirí Nogalani
	Furniture Provision for two schools: El Choro Grande and Milliguaya
Coroico	Furniture Provision for schools in the municipality of Coroico
	Provision of piping for the expansion of the potable water system of Tocaña
	Final design and construction of the San Cristóbal potable water system
	Final design and construction of the Santiago Grande potable water system
	Expansion of the Marca potable water system
	Expansion of the San Gerónimo potable water system
	Refurbishment of the Santa Ana potable water system
	Expansion of the Chiquiña potable water system
	Expansion of the Calabatea de Ayacucho potable water system
	Expansion of the Chicaparque – Yolosita potable water system
Construction of a Student Dormitory for the UAC-CP	
La Asunta	Provision of School Furniture for schools in the Federation of La Asunta
	Provision of School Furniture for schools in the Federation of Chamaca
	Provision of School Furniture for schools in the population of La Asunta
	Cancer Prevention and Early Detection Campaign in La Asunta
	Design of the San Gabriel pedestrian bridge

MUNICIPALITY	PROJECT
	Construction of school bathrooms for the La Asunta School
	Refurbishment of the Santa Rosa potable water system
	Expansion of the 21 de Agosto potable water system
	Refurbishment of the Santa Felipe potable water system
	Refurbishment of the Cajones potable water system
	Refurbishment of the Yanamayo potable water system
	Rehabilitation of hydroelectric energy system in Chamaca
	Improving Family Quality of Life through the Kitchen
Palos Blancos	Final Design for a Potable Water System for the community of Alto Remolinos
	Provision of basic hospital equipment for the Palos Blancos Hospital
	Refurbishment of the Palos Blancos potable water system
	Refurbishment of the Los Olivos potable water system
Yungas, Various	Support of the 2010 Inter-Yungas Soccer Championship
	Institutional strengthening of Yungas Alternative Education Centers (CEAs)
	Provision of equipment for the Association of Yungas Municipalities (MMYLP)
	Leadership and project management training for public servants
Yanacachi	Provision of School Furniture for schools in the municipality of Yanacachi
	Design and construction of flood prevention infrastructure along the Chajro River

Almost half of the concluded projects this quarter fall under the sub-component of potable water. These projects include the refurbishment and expansion of potable water systems in different municipalities in the Yungas.

1. Inaugurations

Provision of equipment to CEAs of the Yungas

On September 3rd, equipment was handed over to five Alternative Education Centers (CEAs) in an event attended by Germán Loza, Vice Minister for Coca and Integrated Development, Mary Norris, Director of USAID/Bolivia's Integrated Alternative Development office, Cesar Guedes, Country Representative of the United Nations Office on Drugs and Crime (UNODC), the mayors of Coroico, Coripata, Irupana and Chulumani, the District Director of Education of Chulumani, local authorities and students. The implementation of this project was coordinated with the UNODC's Bol- I80 project. ICDF provided kitchen equipment, tailoring and sewing machines, and books in accordance with the

expressed needs of the CEAs of Coroico, Chulumani, Coripata, Irupana and Palos Blancos. The UNODC's Bol-I80 project will work with CEA instructors to strengthen their teaching skills. More than 900 students in total are benefiting from this project.

School Furniture

During the month of September, events were held to hand-over school furniture, including chairs, tables, desks and bookcases, to five municipalities. The details of these are as follows:

- A total of 170 pieces of school furniture was transferred to the municipality of Yanacachi. The Municipality assigned this furniture to the Machacamarca School, which is the only school in the municipality that provides education for children from kindergarten to high school. The Machacamarca School has a student population of approximately 200, with students coming from more than 10 different nearby communities.
- A total of 582 pieces of school furniture was handed over for distribution to the municipality of Chulumani. It is estimated that more than 250 students will benefit.
- A total of 2,157 pieces of school furniture were transferred to the municipality of La Asunta. This furniture will benefit over 1,000 students attending 50 different schools in communities across the municipality.
- More than 700 pieces of school furniture were handed over to the municipality of Coroico. In coordination with the District Director of Education, the Municipality has distributed the new furniture to 21 schools.
- A total of 489 pieces of school furniture was delivered to the municipality of Coripata. The furniture has been delivered to 13 schools and will benefit almost 250 students.

In total, more than 3,500 pieces of furniture were purchased for these five municipalities with the goal of improving the quality of education for approximately 1,800 students from various communities. In the past, due to an inadequate quantity of furniture, many students had to share old fashioned benches. In accordance with Ministry of Education guidelines, the new furniture provided affords each student her or his own chair and learning space. Due to logistical problems, all of the school furniture could not be delivered to the municipalities at the time of the events; the delivery of the remaining pieces was handled afterwards.



Delivery of School Furniture – Coripata

CP, the UAC-CP student body and faculty and invited guests. The dormitory consists of a three-story infrastructure that contains 17 rooms designed to house a total of 170 female students that were previously living in overcrowded dorm rooms. Those in attendance had the opportunity to speak with students and learn about the lives of the many young people who come from different municipalities and departments in Bolivia to study at this important institution of higher education.



The UAC- CP Dormitory

The new dormitory for the UAC-CP was inaugurated on September 29th. The event took place in the presence of Maruja Machaca, Representative of the VCDI, Rebecca Latorraca, Director a.i. of USAID/Bolivia, Ángel Miranda Huanca, the Municipal Mayor of Coroico, Clemente Mamani Condonera, President of the MMYLP, Padre Freddy Villar, Director of the UAC-

The delegation that visited the UAC-CP came away with a much better understanding of the importance of this institution, which provides university-level training in subjects such as veterinary medicine, primary education, nursing, and tourism. As part of the inauguration a group of education majors performed a skit in which they depicted a typical student's family: The parents wanted the best for their daughter; they wanted her to receive a university education which would not only help her to obtain a job in the future, but that would provide her with practical skills. However, this family was also faced with serious financial challenges. After completing her application, the daughter was admitted to the UAC-CP. She then applied for a scholarship which she received. She attends the university, studies education, lives in the dormitory, and after graduation, returns to her community where she will live and work. Both she and her parents are extremely happy and proud of her accomplishments.



Student skit at the UAC-CP

The UAC-CP also makes a significant contribution to the surrounding communities. It engages the local producers in various agricultural activities such as pig farming, coffee production and sausage making. It also boasts a botanical garden which is open to the public, provides recycling services for plastic bags and containers and manages a small health post that provides medical care to its students, in addition to families from 13 communities. The health post is staffed by personnel appointed by the Ministry of Health, as well as nursing students who are able to gain valuable experience while working at the health post.



Former dormitory room at the UAC-CP



New student dormitory room at the

2. Health and Cross-cutting Activities

Cervical Cancer Prevention and Early Detection Campaign

At the beginning of July, the second cervical cancer prevention and early detection campaign was realized in La Asunta. Volunteer healthcare personnel from the Bolivian Cancer Foundation conducted the campaign, during which approximately 160 women were screened for cancer and participated in cancer awareness and prevention trainings. The results of the exams have been sent to the La Asunta hospital, where the attending physician will follow up with participants.

During the last two years, the ICDF has conducted three cancer prevention and early detection campaigns. In total, approximately 550 women have participated in the municipalities of La Asunta and Palos Blancos, in many cases accompanied by their male partners, who also attended the training sessions. The ICDF will undertake a similar campaign in the municipality of Palos Blancos during the upcoming reporting period.

Improving Family Quality of Life through the Kitchen



Community member building his ecological stove

The project, “Improving Family Quality of Life through the Kitchen,” was completed. As a result, 300 families from the municipality of La Asunta were trained in the construction and use of improved, ecological stoves. This project will have a significant positive impact on participating families’ by reducing the risk of respiratory illnesses and by decreasing their consumption of firewood. In addition to covering proper stove use and maintenance, the trainings provided information of basic household hygiene and family nutrition. Due to the success of this project and the enthusiastic interest expressed by community members, the ICDF will present a second phase of this project to the CT for approval during the upcoming quarter.

3. Scholarship Programs, Yungas: Unidad Académica Campesina Carmen Pampa (UAC-CP)

The UAC-CP is a non-profit university located 111 km. northeast of La Paz, in the North Yungas Province of the department of La Paz. The university is located in the community of Carmen Pampa, which is 13 km from Coroico, the capital of the province. It offers higher education to the rural regions of tropical northern Bolivia and to the youth from the marginalized areas of the City of La Paz. It was created by an inter-institutional agreement between the Catholic University of Bolivia (UCB), the Dioceses of Coroico, the Franciscan Missionary Sisters and Villa Nilo Sub Central, the local governing body of the indigenous people, on October 4, 1993. The UAC-CP offers bachelor degrees to a student body of approximately 700 students in agronomy, nursing, veterinary medicine, animal husbandry and primary education. It also offers an associate degree in tourism. Each program includes both academic coursework and opportunities for hands-on practice in the respective career tracks.

The ICDF continued to assist UAC-CP students by funding 50 regular study scholarships during the first semester of 2010. During this period, the ICDF technical team and UAC-CP staff met to discuss the scholarship program as well as to develop a proposal for the two year extension period requested by USAID. At present, the UAC-CP scholarship program has been extended through December 31, 2010, providing 50 students with scholarships for the second semester of 2010.

B. ECONOMIC DEVELOPMENT

1. Concluded Economic Development Projects

A total of twelve economic development projects were completed in the Yungas region during the present reporting period. The names of these projects are listed in table nine.

Table 9. Economic development projects completed during the July-September 2010 quarter

MUNICIPALITY	PROYECT
Chulumani	Soil Recovery through Agroforestry systems in the <i>Zona Tradicional</i>
	Laydi Egg Farm
Coripata	Final design of the Coripata bus terminal
Coroico	Tourism Promotion in Coroico: the 2010 Coroico Cultural Festival
	Design of access to the vehicular suspension bridge
La Asunta	Provision of Transportation Infrastructure for the community of Bolívar IV
	Provision of Transportation Infrastructure for the community of Bolívar III
	Provision of Transportation Infrastructure for the community of Bolívar II
	Plantain production promotion
Palos Blancos	Provision of Transportation Infrastructure for the communities of Liquimuni and Bajo Inicua
	Modernization of the Cacique industrial dairy processing plant
Yungas Various	Modernization of the meteorological network of the Yungas

Plantain Production Promotion

Among the economic development projects concluded this quarter, plantain promotion in the municipality of La Asunta is particularly outstanding. Through the use of Farmer Field School (FFS) methodologies, approximately 80 producers in six communities received technical assistance and were trained in crop management, harvest, processing, marketing, sales and accounting. Over the last three months, plantain producers in the municipality of La Asunta harvested a total of more than 2,300 heads of plantain. They sold their fruit for an average price of 45 Bs. (US\$ 6.35) in the local markets of La Asunta and Caranavi. With ICDF assistance participating producers formed six associations in the communities of Santa Lucia, Santa Teresita, San Pablo, Alto Olivos, Bolívar III and Bolívar IV. Representatives from each association have

begun organizing the formation of a combined association that will be called the Association of Ecological Plantain Producers of La Asunta (APEPLA).



Evaluation meeting with members of a plantain association in La Asunta municipality



Plantain sales in the local market

As part of the close-out of this project, six evaluation workshops were conducted in the six associations. The workshops focused on evaluating three main aspects: 1) the FFS technical assistance methodology; 2) markets; and, 3) the status of the FOGs – products versus payments. The results of the evaluation were positive: in particular, the FFS methodology was felt to be appropriate, and the plant varieties selected were deemed suitable. Another issue discussed during these workshops was market prospects, and the conclusion reached was that there are various market opportunities to be explored. Although there is a significant demand in the local market (La Asunta), it is always a good idea to identify other buyers. Also, on September 18th, producers participated in the Second Ecological Product Fair of La Asunta, where they won first prize for their plantains and plantain chips, which they had on display.

Meteorological Stations

With the installation of nine new meteorological stations, the ICDF concluded the project, “Improving the Meteorological Network of the Yungas of La Paz”. The stations consist of temperature, humidity, solar radiation and wind sensors, barometers, data loggers, batteries, solar panels and cabinets. All of the stations are protected by fencing, support towers and lightning rods. The nine stations were constructed in the following locations:

	Municipality	Community	Institution
1	Yanacachi	Sakahuaya	Hidroeléctrica Boliviana S.A.
2	Chulumani	Chulumani	Universidad Mayor de San Andres (UMSA)
3	La Asunta	La Asunta	La Asunta Hospital
4	Irupana	Vila Vila	Community Area
5	Palos Blancos	Sapecho	UMSA
6	Alto Beni	Suapi, Km. 73	Martín Cárdenas School
7	Alto Beni	Bella Vista	Community Church House
8	Coroico	Carmen Pampa	UAC- CP
9	Coripata	Dorado Chico	Home of Juan Tórrrez, ICDF-assisted pig farmer

The institutions that have offered their property for the stations are not involved in their operation, but have signed written documents certifying that they agree to house and protect the stations. Six of the nine stations automatically send meteorological information to the National Meteorological and Hydrology Service (SENAMHI), while the other three store information that is later collected by SENAMHI personnel since the stations do not have access to a cellular signal. Once they do have access to a cellular signal the stations will be able to upload the information automatically. The new fully-equipped stations will be inaugurated during the upcoming reporting period.

Participation in Product Fairs



Together with ARCo-assisted producers, ICDF-assisted producers participated in four different productive fairs: the celebration of the U.S. Independence Day, a small fair in the population of Sapecho in the municipality of Palos Blancos, a fair at the Martin Cardenas technical high school, also in Palos Blancos and the Second Ecological Product Fair of La Asunta, organized by the municipal government of La Asunta. All fairs were attended by national and local authorities.

One of the most interesting fairs was held at the Martin Cardenas School in the municipality of Palos Blancos, where producers, students and authorities were able to engage in interesting discussions about market potential and the future. The students expressed their appreciation for being able to live and study at the prestigious agricultural school, while producers shared their experiences and highlighted their successes. Products showcased at these fairs included stevia, amaranth, poultry, eggs, plantain, flowers, baked goods, dairy, citrus juice and handicrafts.



Producer of fruit juice at the Sapecho mini-fair.

2. Economic Development Projects in the Yungas

Based on experience gained from working nearly ten years in the Yungas, ACDI/VOCA understands the geographical, social and economic diversity that characterizes the region. The ICDF strategy in the Yungas has been designed to reflect this diversity and follow the guidelines set by the PSB and USAID. The ICDF is currently working in three different areas of the Yungas: La Asunta, the *Zona Tradicional* and Alto Beni/Palos Blancos.

2.1. La Asunta

Plantain: As mentioned, plantain promotion activities were successfully concluded during the reporting period. Six producer associations were formed, and producers and community members have great expectations for expanding and improving plantain production in the municipality.



Preparing the bee hives



Honey harvest

Beekeeping: The ICDF continued to provide training and technical assistance using FFS methodologies. More than 60 new apiaries were established in the communities of Villa Camacho, Incahuara, Puerto Aroma II and Floriati-Lagunillas. Beekeepers from the communities of Villa Camacho, Incahuara and Puerto Aroma made an exchange visit to experienced beekeepers in the municipality of Caranavi. The harvest began, and producers obtained an average of 22 kg per hive, or a total of more than 9,000 kg of honey for all ICDF-assisted producers in La Asunta. Producers sold their honey in local markets for an average price of 40 Bs. (US\$5.65) per kg.

Coffee: The ICDF conducted trainings on coffee crop recovery, crop management, construction and management of compost and organic fertilizer to different groups of coffee producers in La Asunta. The ICDF also trained producers from Villa Camacho, Chorobamba and Bolívar II in processing. Subsequently, samples of producers' coffee were sent to the Bolivian Federation of Export-Quality Coffee Producers' (FECAFEB's) quality control laboratory. The samples were given a grade between 80 and 84, which ranks ICDF-assisted producers' crops as

specialty coffee. The FECAFEB sent the samples to potential specialty coffee buyers in Japan and Canada that are scheduled to visit Bolivia during October.

The coffee census was concluded; results will be presented to different VCDI and USAID, during the next reporting period. Finally, as part of 30,000 forest-variety seedlings were transplanted to coffee parcels as shade cover. This not only encourages sustainability coffee production additional future economic opportunities.

Stevia: A new nursery was constructed in Ríó Ebenay, which has a later be transplanted to plots in the communities of Villa Esperanza, Incahuara. Stevia producers from the *Central Bolívar* participated in producers throughout the municipality sold their dry stevia leaves in price of Bs. 92 (US\$13) per kg.

horticulture production continued, with the objective of meeting an (lettuce, cabbage, tomato, parsley, celery, etc.) in the municipality of La been transplanted to the plots of the 10 participating families in the Pablo, Islani, Chorobamba and Villa Camacho. The first harvest of successfully in local markets.

2.2. Zona Tradicional

Amaranth: Preliminary activities for the second phase of amaranth second phases, the ICDF estimates that as many as 220 producers will participate from the municipalities of Coripata, Coroico and Irupana.

Forest Management Strategy: Workshops were held throughout the five participating municipalities in the Yungas to assess the needs and opinions of different stakeholders. Producers from the Yungas visited different forested, agriculture-producing zones of Cochabamba to see the forest management activities taking place there. At present, the company hired to compose the forest management strategy is working on the final version of the document.



Stevia producer shows the harvest



Fresh, ecological tomatoes

stakeholders, including the Municipality, the the coffee promotion activities approximately part of a long-term plan to improve or renew the but provides 190 coffee producers with

capacity to house 350,000 seedlings that will Miraflores, Villa Litoral, Palestina and trainings on post-harvest and processing. Stevia markets in the city of La Paz for an average

Horticulture: Activities to promote unsatisfied market demand for vegetables Asunta. The majority of seedlings have communities of Pichari, Flor de Mayo, San tomatoes, lettuce and cucumbers was sold

promotion activities took place. During this

2.3. Alto Beni and Palos Blancos

The ICDF provided follow-up technical assistance and training to poultry producers in the region, as well as to microenterprises that have received ICDF support in the past. Work continued on the administrative closeout of recently completed projects in the municipalities of Alto Beni and Palos Blancos.

C. CROSS-CUTTING ACTIVITIES

Volunteer Consultant Technical Assistance

The volunteer-based technical assistance program supports the ICDF's main goal of improving quality of life and helping establish diversified sustainable economies in the Yungas of La Paz. With the expertise of its international consultants, the program constitutes an important channel through which the ICDF can provide its clients with specialized technical assistance that is not readily available locally. ICDF volunteer consultants supply producers with demand-driven assistance in different areas. In agriculture, this includes assistance in production, post-harvest handling, value-added processing and marketing. In addition to providing technical support in agriculture, the volunteer consultants give important assistance in institutional strengthening, as well as in developing sectors of Bolivia's economy that have shown high potential for growth within the ICDF's target regions.

Concluded Volunteer Consultancies

The ICDF saw one volunteer assignment in dairy cattle health to its conclusion during the current reporting period.

Technical Assistance in Beef and Dairy Cattle Health

Agricultural production in the Alto Beni Region of La Paz is well diversified. This includes cacao, citrus, coffee, banana, rice and yucca, as well as poultry, livestock and sheep. The market activity of dairy cattle producers involves satisfying the high demand for cheese, as well as for fresh milk from the area's yoghurt and flavored-milk processing plants. Alto Beni beef and dairy cattle farmers have identified many issues adversely affecting their productive potential. These include deficiencies in cattle feed, poor management of productive cycles, health issues and other problems with general herd administration. Producers feel that health issues are the main factor preventing an increase in productivity.

To assist in the development of a health strategy for disease prevention and treatment for Alto Beni meat and dairy producers, the ICDF secured the technical assistance of Dr. Daniel Miller as a volunteer consultant. Dr. Miller has a background in veterinary medicine who demonstrated his ability to provide expert assistance to small-scale dairy cattle farmers in Bolivia during prior volunteer consultancies including one conducted under the USAID/Bolivia funded Yungas Community Alternative Development Fund (YCADF) project.



Dr. Miller examines a dairy cow

Since Dr. Miller's earlier visits, the ICDF provided several producers in the municipalities of Palos Blancos and Alto Beni with an improved breed of cattle specifically chosen because they can be used for both dairy and beef production. Unfortunately, despite its being appropriate for the climate and more useful for the producers, most local veterinarians are unfamiliar with this cattle breed. For this reason the ICDF sought out the expertise of Dr. Miller who spent approximately three weeks in the field working closely with Alto Beni meat and dairy producers as part of his consultancy. Dr. Miller's main objective was to train local cattle farmers in disease prevention and control, as well as in proper livestock management practices.

During his time in the field, Dr. Miller visited approximately 30 small-scale cattle farmers on their land,

where he, with the help of the producers, examined their cows and administered vaccinations and minor treatment when necessary. Dr. Miller was able to demonstrate the proper way of administering vaccinations to producers and ICDF field technicians. These producers are now able to replicate such treatments as needed in their herds.

One of the main health issues encountered in dairy cattle in the Alto Beni Region is Mastitis an infectious disease caused by a highly contagious bacteria. Mastitis enters the udders of dairy cattle through ducts in the teat and can severely reduce milk production. Dr. Miller trained producers in the best ways to identify infected cows during the milking process. He also provided training in the proper ways to prevent the spread of mastitis and for providing treatment when possible.

Dr. Miller also provided training in the best ways to prevent and treat external and internal parasites, as well as papillomas. In addition, he provided ample training on calf care and the specifics of dietary needs for cows and bulls of all ages. The anticipated result of the theoretical and practical training provided during this volunteer consultancy is an improvement in the volume and quality of dairy and meat produced by Alto Beni cattle farmers.

During his three weeks in the field, Dr. Miller gave four formal trainings which were attended by a total of 147 people. These included three presentations at technical schools and universities as well as a workshop focused on artificial insemination in the Alto Beni region. Dr. Miller concluded his fieldwork with a presentation and workshop at the *Unidad Academica Campesina de Carmen Pampa* (UAC-CP), where 61 veterinary students participated.

II.3 Performance Monitoring and Evaluation (M&E)

During this quarter, the ICDF monitoring and evaluation team conducted field visits to completed projects, which primarily fall under the community development portfolio. Jointly with USAID, the ICDF M&E team conducted a data quality assessment utilizing a random sample of indicators presented, sources of verification and supporting documents successfully concluding this review. In coordination with the ARCo project, some suggestions were presented for the structure of a project database for use by USAID and the VCDI. Some data collection forms have been improved based on suggestions by USAID's M&E officer that allow for the comparison of economic development project information.

IV. PERFORMANCE INDICATORS RESULTS

The ICDF activities are divided into two portfolios: economic development and community development. These two programmatic areas support the USG and PSB's policies and provide the VCDI with the necessary tools to facilitate sustainable development in the Yungas and previously the Tropics of Cochabamba. The following table summarizes the ICDF's performance indicator targets per programmatic pillar.

Table 10. ICDF performance indicators and annual (calendar year) targets¹

Indicator		Unit	Calendar Year Targets					Total LOP
			05 -06	07	08	09	10	
Overall Indicators								
SO 1.1	Percentage of population below poverty line as measured by the Unsatisfied Basic Needs Index	Percentage Yungas	70%*		65%			60%
		Percent TC	75%*		70%			65%
SO 1.2	Total number of families (and their communities) with increased access to public goods, services and jobs.	Families	3,499	15,204	7,229	4,154	3,448	33,534
* Percentages for '05 and '06 are baseline reference numbers								
Community Development								
IR 1.1	Number of social infrastructure and related works completed	Infrastructures	14	23	201	140	110	488
CC 1.1	Number of people who received training within the framework of an ICDF activity.	Trainees	2,582	21,514	9,249	3,488	3,075	39,908
Economic Development								
IR 2.1	Incremental sales from economic initiatives supported by ICDF	\$US (thousands)	0	0	902	2,580	609	4,091

IR 2.2	Number of new, licit equivalent jobs directly attributable to <u>all</u> ICDF-supported initiatives	Equivalent jobs	40	94	1,550	1,275	979	3,938	
IR 2.3	Number of hectares of agricultural licit crops that have been developed or expanded with ICDF support.	Hectares	0	0	175	1,251	160	1,586	
Cross-cutting Indicators									
CC 1.1	Percent of counterpart by component	CD	10%	10%	10%	10%	10%	10%	10%
		ED	20%	20%	20%	20%	20%	20%	20%
CC 1.2	Percent of relevant sub-grant initiatives that are still “functioning well” one year after completion	Sub – grants	n/a	95%	95%	95%	95%	95%	

¹ The reformulated targets were approved in Modification 16.

The main objective of the ICDF is to support the joint USG-PSB efforts to establish a sustainable economy in Bolivia’s coca-producing and associated areas by addressing basic human needs, alleviating poverty and improving social and economic conditions through the implementation of subaward projects identified through participatory methodologies. This objective primarily responds to USAID/Bolivia’s Intermediate Result (IR) 5.3:

To improve basic public services and social conditions in the Tropics of Cochabamba and in the Yungas region of La Paz, Bolivia.

Two indicators monitor this IR: 1) the index of unsatisfied basic needs; and, 2) the number of families benefited. Due to the departure of IAD from the TC, the ICDF did not evaluate the NBI indicator in this region, nor is it planned to do so in the future. Also, given that the PSB plans to conduct the national census and measure the NBI in 2011, the next NBI indicator measurement will be done by means of the national census. Thus this indicator was measured on only one occasion during the LOP of the ICDF, using the baseline established in the NBI study published in 2005. The number of families’ indicator is monitored on a quarterly basis.

Table 11. ICDF performance indicators and calendar year results for LOP (2005-2010)

Indicator	Results By Calendar Year					Results		
	Aug 05 Dec 06	2007	2008	2009	Jan Sept 2010	LOP Target	Total Achieved	Percent of Target Achieved
NBI				52%		60%	52%	
Number of Families	3,499	15,204	7,229	4,161	2,465	33,534	32,558	97%
Number of Infrastructures	14	23	201	141	115	488	494	101%
Number of Trainees	2,582	21,514	9,249	4,049	2,183	39,908	39,577	99%
Incremental Sales Value (000 USD)	0	0	902	2,603	589	4,090	4,094	100%
Equivalent Employment	40	94	1,550	1,277	576	3,938	3,537	90%
Number of Hectares	0	0	175	1,256	192	1,586	1,623	102%

The ICDF has met the majority of established targets for its LOP according to Modification 16. In the case of number of infrastructures and related projects, incremental sales and number of hectares, the targets have been surpassed. With the results that will be achieved during the next quarter, it is expected that the LOP targets will be surpassed in all the ICDF indicators. Below is a more detailed account of the performance indicator achievements for the LOP as well as the current reporting period.

Table 12. Summary of ICDF performance indicators targets and results for the 2010 fiscal year and July-September 2010 quarter

Indicator	TOTAL FY 2010		Percent of Target Achieved	July - September 2010		Target Oct - Dec 2010
	Target	Result		Target	Result	
Number of Families	2768	3,372	122%	318	1,044	632
Number of Infrastructures	115	156	136%	10	38	14
Number of Trainees	1,165	3,064	263%	165	425	892
Incremental Sales Value (000 USD)	1258	1,261	100%	60	140	0
Equivalent Employment	763	828	109%	95	279	186
Number of Hectares	180	217	121%	55	57	0

SO 1.2 Indicator: Number of families

Title of the performance indicator: Total number of families (and their communities) with increased access to public goods, services or jobs.

Measurement unit: Number of families benefited by ICDF supported activities

The total number of families who have benefited in both regions during the ICDF's LOP is 32,558. This means that 97% of the LOP target has been reached to date. The table below shows the distribution of this number of families between municipalities and the two ICDF components.

Table 13. Distribution of families benefited during LOP by portfolio and municipality (2005 – 2010)

Region	Municipality	Community Development	Economic Development	Overall Total
Tropics of Cochabamba	Chimore	888	180	1,068
	Entre Rios	791	631	1,422

Region	Municipality	Community Development	Economic Development	Overall Total
	Puerto Villarroel	1,352	620	1,972
	Shinaota	1,858	1,300	3,158
	Various TC	38	3,667	3,705
	Villa Tunari	1,085	441	1,526
	Yapacani	407		407
Total TC		6,419	6,839	13,258
Yungas	Alto Beni	3,980	555	4,535
	Chulumani	2,114	69	2,183
	Coripata	3,499	11	3,510
	Coroico	1,095	79	1,174
	Irupana	221	0	221
	La Asunta	1,422	352	1,774
	Palos Blancos	2,189	182	2,371
	Various Yungas	2,429	327	2,756
	Yanacachi	669	107	776
Total Yungas		17,618	1,682	19,300
Total		24,037	8,521	32,558

During the reporting period, 1,044 families in the Yungas were benefited. Most of these families participated in community development projects, as is evident in the following table.

Table 14. Number of families benefited by projects concluded by component and municipality (July - September 2010)

Municipality	Community Development	Economic Development	Total
Chulumani	24	51	75
Coripata	26		26
Coroico	247		247
La Asunta	520	87	607

Palos Blancos	35	1	36
Yungas Various	46		46
Yanacachi	7		7
TOTAL	905	139	1,044

In the municipality of Coroico, the project that accounts for the largest number of beneficiary families is the completion of the girls' dormitory block on the Leahy campus of the UAC Carmen Pampa. This dormitory has the capacity to house 170 female students in comfortable accommodation.



Family shows their new stove

In La Asunta, 300 improved stoves have been installed in an equal number of homes. These are reducing the risk of respiratory diseases, especially among women. Also in this municipality, 87 families have benefited from the plan to support plantain production.

The target for this quarter has been surpassed because the UAC-CP dormitory project was scheduled to be completed during the previous quarter. In addition, the number of beneficiary families has increased because of the conclusion of the potable water and sanitation projects during FY 2010. Currently, 122 percent of the target for the fiscal year has been achieved.

Table 15. Number of families benefiting from projects completed in the July-September 2010 quarter, by portfolio and sub-portfolio

PORTFOLIO	SUB-PORTFOLIO	Number of beneficiary families
Community Development	Potable Water	90
	Education	396
	Community Infrastructure	5
	Others	300
	Health	114
Total Community Development		905
Economic Development	Agriculture	87
	Environment	50
	Livestock farming	1
	Processing	1
Total Economic Development		139
Total		1,044

A. Intermediate Result 1

The ICDF's intermediate result 1 (IR 1):

Community development in the Yungas and in the TC is strengthened; social and productive infrastructure is constructed, expanded and/or equipped.

IR 1.1 Indicator: Complementary infrastructure and related projects

Title of the performance indicator: infrastructures and related projects completed.

Measurement Unit: Number of complementary infrastructures and other projects concluded by the ICDF.


The LOP target for infrastructures and related projects has been surpassed due to the fact that the projects prioritized during the last quarter, principally rehabilitations and expansions of potable water projects have a lower average cost than many past ICDF projects.

Table 17. Number of completed infrastructure projects by municipality and portfolio (Jul – Sep 2010)

MUNICIPALITY	PORTFOLIO		Total
	Community Development	Economic Development	
Chulumani	2	1	3
Coripata	3		3
Coroico	10		10
La Asunta	10	3	13
Palos Blancos	3	2	5
Various YUN	2	1	3
Yanacachi	1		1
Total general	31	7	38

In the municipalities of Coroico and La Asunta, 13 potable water projects and six education projects were implemented. The chart below details the number of projects by type, including four transportation infrastructure projects.

Chart 6 – Number of infrastructure projects by type in the Yungas (Sep – Jul 2010)

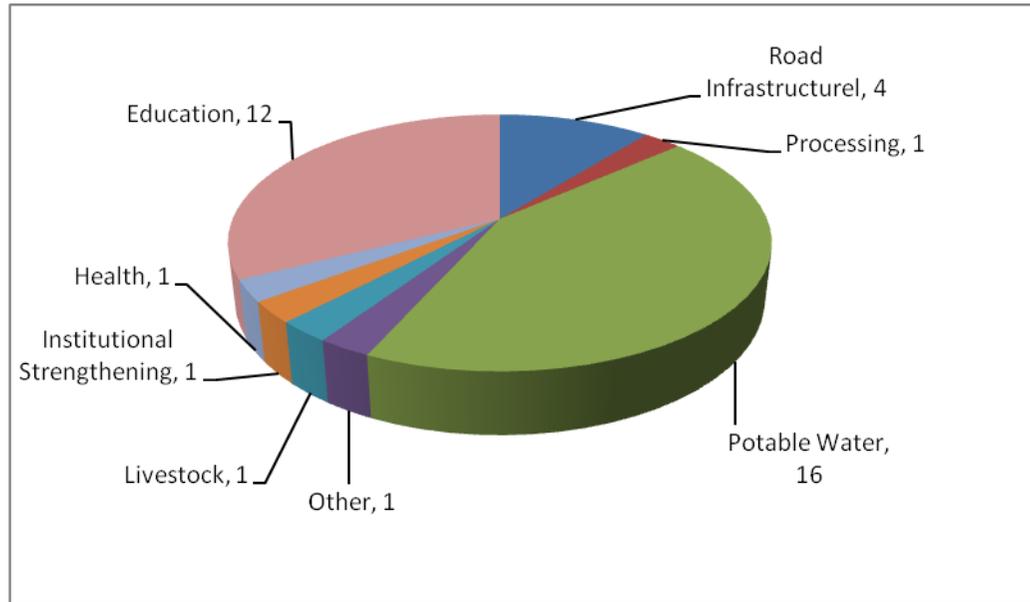

IR 1.3 Indicator: Trainees

Title of the performance indicator: People who received training within the framework of an ICDF activity.

Unit of Measure: Number of trainees

The ICDF has achieved 99 percent of the LOP target for number of trainees, with the current number of trainees at 39,577 people. The municipalities with the highest number of trainees are Palos Blancos, Alto Beni and La Asunta, where a significant number of users of potable water and sanitation systems implemented in these regions have been trained.

All ICDF community development projects include a training component in which beneficiaries learn to maintain, administer and operate infrastructure, services and/or equipment that they have acquired under the program. The different types of training offered include operation and maintenance, health and hygiene practices, basic accounting as well as administrative skills. Under the same principles, training is offered within the economic development projects in the areas of production and business management. In addition, the ICDF project portfolio also includes a number of subawards where training and/or institutional strengthening activities are not just a complementary component, but the focus of the project.

The ICDF surpassed the target for the FY 2010, given the large number of trainings conducted in the light of 28 projects of potable water systems. These trainings were conducted in several communities.

The majority of trainees for this quarter correspond to participants in the “Improving Family Quality of Life through the Kitchen” project in the municipality of La Asunta. Through this project, 300 community members received theoretical and practical training on maintenance, the use of the ecological stoves and themes related to the families’ alimentation. The community members’ active participation in building the stoves will ensure that they themselves will be able to make any repairs that may be required. The training also included good hygiene practices in food preparation.

B. Intermediate Result 2

The ICDF’s intermediate result 2 (IR.2):

Economic initiatives are promoted in the Yungas region of La Paz and in the Tropics of Cochabamba by the creation of job opportunities in these regions.

IR 2.1 Indicator: Incremental sales

Title of the performance indicator: Increases in sales generated by economic initiatives supported by the ICDF.

Unit of Measure: U.S. Dollars x 1,000

To date, 100 percent of the LOP target for incremental sales has been achieved. Around sixty percent of the sales are generated by agriculture related projects, such as through the production of heart of palm in the TC and various crops such as stevia, plantain and lily flowers in the Yungas. Significant sales have also resulted from microenterprises that have received ICDF assistance.



Plantain harvest in La Asunta



During the quarter, important sales were registered for microenterprises in Alto Beni and Palos Blancos, especially in citrus processing, dairy processing and poultry production. In total, US\$140,000 was reported for this period. The target for this indicator was surpassed by more than US\$80,000, attributable to the fact that plantain in La Asunta was sold at an average of Bs. 45 a bunch as opposed to the originally projected Bs. 30.

IR 2.2 Indicator: Equivalent employment

Title of the performance indicator: Equivalent employment directly attributed to initiatives supported by the ICDF.

Unit of Measure: Equivalent employment

The ICDF has achieved 90 percent of the LOP target for this indicator, with 3,537 equivalent jobs created to date.

Table 21. Breakdown of equivalent jobs created by portfolio and sub-portfolio (July – September 2010)¹

Portfolio	Sub-portfolio	Equivalent Employment
Community Development	Potable Water	19
	Education	167
Total Community Development		185
Economic Development	Agriculture	85
	Environment	4
	Animal Husbandry	1
	Processing	4
Total Economic Development		94
Overall Total		279

During FY 2010, the ICDF surpassed the 109 percent expected in generating equivalent jobs, mostly in community development activities such as construction and rehabilitation of more potable water systems.

Most of the equivalent jobs generated by economic development activities for this reporting period correspond to plantain production in La Asunta. The remaining jobs were in the workdays created by potable water and education projects. During the upcoming quarter, the ICDF

¹ Based on the recommendation of the RIG audit, the equivalent employment indicator has been meticulously reevaluated. The numbers presented in the table reflect this reevaluation.

expects to achieve LOP target for equivalent jobs, with the completion of the Nogalani school classroom, the Miliguaya potable water system, the Coroico Landfill, and jobs generated by various microenterprises.

IR 2.3 Indicator: Number of hectares of licit agricultural crops

Title of the performance indicator: Hectares of alternative crops or hectares under forest management plans targeted by IAD programs.

Unit of Measure: Hectares

The ICDF verified the establishment of 50 hectares of plantain in the communities of San Pablo, Santa Teresita, Bolívar III, Bolívar IV and Alto Olivos, all in the municipality of La Asunta. At present, all of the hectares that were established as part of plantain promotion activities have been verified by supervisors using georeferencing technology. In the *Zona Tradicional*, a total of seven hectares of agroforestry crops forming part of the soil recuperation project were verified, made up of different plants such as citrus trees and grains, these plots aid in the soil recovery. With the establishment of 57 hectares verified, the target for the quarter was surpassed, and the overall LOP target was also surpassed.

The producers of plantain and amaranth achieved more hectares than expected since both products have significant market demands, which encouraged more producers to be involved with the production.

C. Cross-cutting Indicators

The ICDF implements projects whose results contribute to both IRs. These results are reported by way of two cross-cutting indicators: 1) counterpart contribution; and, 2) projects that are “working well” after one year.

In compliance with the ICDF PMP, “counterpart contribution” is a yearly indicator and as such is reported in the January - March reporting period. The indicator “projects working well after one year” is to be reported every six months and therefore will be reported in the next quarterly report.

V. LOOKING BACK – A REVIEW OF THE QUARTER

The following activities were planned for the July – September reporting period:

- Completion of the landfill site in Coroico. This project could not be completed during the quarter because the construction firm had to halt activities until some concerns about the landfill site in the community of San Joaquin were resolved. The municipal government of Coroico led the negotiations with the community. After a series of meetings, a final agreement was reached and the work was re-initiated.
- Completion of the sewage system in the community of Paraíso in the municipality of Irupana. This project has been delayed due to some technical setbacks. The sewage system includes an anaerobic treatment plant. This type of treatment plant is much more efficient but it also requires more time to construct. It is envisaged that this project will be completed during the first weeks of the next quarter.
- Although the construction work on the projects listed below has been completed, they are not reported as completed projects because the provisional delivery by the construction firm has not yet taken place. This technical/administrative activity is scheduled for the first weeks of the next quarter.
 - Potable water system in Millaguaya, Coripata
 - Construction of the Nogalani School in Coripata

The following activities were carried out as planned:

- Modernization of the Yungas Meteorological Network.
- The provision of furniture to several schools in every municipality in the Yungas region.
- Development of a forestry strategy for the Yungas.

VI. LOOKING FORWARD

It is planned that all projects currently in the design, procurement and implementation phases will be completed in the coming quarter. Three of the most interesting projects to be completed are:

- The sanitary landfill for the municipality of Coroico
- The potable water system in Millaguaya, Coripata

- Construction of the Nogalani School in Coripata



Coroico school children sing a song during the hand over of school furniture

VII. ANNEXES

ANNEX II. Success Stories

Volunteer Expert in Bovine Health Shares Knowledge, Dedication and Friendship with Alto Beni Producers and Cattle Alike

When Dr. Daniel Miller and *Don* Justo Aguilar were reunited after seven years, the hearty hug and broad smiles the two men shared spoke volumes: time and distance had not diminished their friendship and mutual affection at all.

Later, standing inside the Alto Beni Milk Producers Association (APROLAB) dairy processing plant, of which Mr. Aguilar is president, the veterinarian recalls, “When I came to Bella Vista seven years ago, it was to help see if the idea for this plant was feasible.” In 2003, Dr. Miller, United States-born veterinarian and volunteer expert in bovine health, stayed in the Alto Beni community of Bella Vista for three weeks as part of assistance provided by the Yungas Community Alternative Development Fund (YCADF), a project led by the Plurinational State of Bolivia, financed by USAID/Bolivia and implemented by ACDI/VOCA. Working with APROLAB producers, Dr. Miller developed a manual for the diagnosis of dairy cattle diseases in the zone and trained producers and local animal-health promoters to manage the health problems that most seriously compromise milk production levels. After Dr. Miller’s first assignment, the YCADF financed the construction of the processing plant, with associates contributing their labor.



Dr. Daniel Miller and *Don* Justo Aguilar inside APROLAB.

Since then, the Integrated Community Development Fund (ICDF), a project led by the Plurinational State of Bolivia’s Vice Ministry for Coca and Integrated Development (VCDI), financed by USAID/Bolivia and implemented by ACDI/VOCA, has provided several producers, in the municipalities of Palos Blancos and Alto Beni, with an improved breed of cattle specifically because they can be used for both dairy and beef production. Unfortunately, despite its being appropriate for the climate and more useful for the producers, most local veterinarians are unfamiliar with this cattle breed, which is why the ICDF again sought out the expertise of Dr. Miller.

This time around, Dr. Miller provided assistance throughout the municipalities of Alto Beni and Palos Blancos. During the first of his three weeks in the field, he visited approximately 30 small-scale cattle farms. He trained the farmers how to examine their cows and how to administer vaccinations and minor treatments when necessary.

On one such occasion, Dr. Miller followed a producer for almost a mile in the rain in order to reach her herd of 20 cows. Once among the animals, he immediately noticed a black and white heifer that had a number of inflamed abscesses on her thigh. After taking a closer look, he explained in Spanish to producer Julia Choque that her cow had been infected by what is locally known as *boro*, a moth that lays its eggs on mosquitoes that then pass the larvae to the cows; the larvae burrows under the cow’s skin, and inflammation and infection commonly result. After Dr. Miller gave the cow an anti-parasitic to kill the larvae and a dose of antibiotics to treat the abscess, a very grateful

Ms. Choque admitted, “I thought it was some type of worm.” Now she knows what to look for and will not only be able to appropriately treat this problem in the future, but also share her knowledge with her cattle-raising neighbors.

Dr. Miller’s kind way with animals is evident to all who see him in action. After he took care of her heifer, Ms. Choque asked the doctor to have a look at her bull, who “has gotten thinner lately.” Dr. Miller examined the intimidating animal diagnosing a stomach parasite, and then quickly administered an anti-parasite injection demonstrating to the ICDF agronomist and Ms. Choque the most appropriate technique. After doing so, he explained that the common practice of using nose clamps is unnecessary. When the producer expressed her surprise at his ability to work with the bull without using the nose clamps, he simply stated, “I don’t like to use those; they depend on hurting the animal and I think they’re cruel.” Clearly the bull’s cooperation was his way of showing his appreciation for this human treatment.

During his three weeks in the Alto Beni region in July of 2010, Dr. Miller gave four formal trainings which were attended by a total of 147 people, including one session at the *Unidad Académica Campesina de Carmen Pampa (UAC-CP)*, where 61 veterinary students participated. The subjects of these training were common issues observed in the zone such as ticks and mastitis, a condition caused by a bacterial infection of the udders that reduces dairy-cattle’s milk production and can even make the milk produced undrinkable. An important breakthrough of sorts was Dr. Miller’s discovery that the producers in the Alto Beni region were not aware of Bracken fern (*helecho macho* locally), a plant that causes hematuria, or blood in the urine, when consumed by cattle. Now that they are informed, producers can dig up the harmful fern and prevent the formation of tumors, weight loss or even the death of their cattle. Dr. Miller also conducted one artificial insemination workshop, where participants had the opportunity to learn to identify the internal reproductive organs of a female cow.



Dr. Miller gives a training on bovine health in Los Tigres, Alto Beni.

Volunteer experts are an integral part of the ICDF’s economic development activities. To date, the ICDF has received 15 experts in diverse fields such as lily flower production, citrus pest management, organic sugar production, ethno-ecotourism and agroforestry.

With Help from the ICDF, Carpenters in Palos Blancos Break Into Local and International Markets

In San Antonio, across the river from the population of Palos Blancos, there is rarely a slow day in Callisaya's carpentry workshop. "With the heavy rains of late, I haven't been able to go look for wood. Usually this place is full of the young men that help me cut and polish the wood that ends up as hard wood floor panels in the city of La Paz and El Alto." When asked if his business has proven to be profitable, he answers affirmatively. "Even after paying all the taxes and fees in accordance with the regulations for taking wood from these forests, I still make a pretty reasonable profit being able to support my family." All of the wood used by ICDF-supported carpenters is registered

with the National Forest Service.

One must carefully navigate the cabinets, tables, windows and doors stacked all over Juan Ramos's carpentry workshop. Mr. Ramos, who is now a community leader, puts down his work, but the two other carpenters that are his employees maintain their diligent focus. One rounds off what will become curtain railings while the other cuts wood for window frames. Mr. Ramos explains, "Since I received the workshop through the project about two years ago, I've had to hire more help and expand the physical size of the workshop. Now,



Juan Ramos uses the wood polishing machine that formed part of his project with the ICDF. At left, his employees, a fellow carpenter, makes curtain rods.

three of us work here (full-time), and my son helps when he's on vacation from the university. There's a lot of demand for our products locally."

About a kilometer up the road from Juan Ramos, carpenter Victor Hugo Serna employs six people from the area. Beneath the ample covered roof that constitutes the open-air workshop, the men working are surrounded by a variety of citrus and banana trees. "What you see right here is wood that we finish and then sell to a company that exports to China. We also make some tables and other furniture, but this is where most of our business comes from."



Carpenter Dionicio Callisaya next to a stack of wood floor tiles.

Each of these men won microenterprise grants through the Integrated Community Development Fund (ICDF), a project led by the Plurinational State of Bolivia's Vice Ministry for Coca and Integrated Development (VCDI), financed by USAID/Bolivia and implemented by ACDI/VOCA. Within its economic development portfolio, the ICDF supports more than 150 small businesses initiatives in the Yungas of La Paz.

Through co-financing on carpentry machines and technical assistance, the ICDF helps small business owners like Mr. Ramos and Mr. Serna start and expand their businesses, generating income, creating jobs and providing much needed services in these rural areas. All small business owners that receive ICDF support commit to providing a cash cost-share worth 35 percent of the equipment provided and 10 percent of the cost of technical assistance.



Victor Hugo Serna in the carpentry workshop assisted by the ICDF. The wood behind him is exported to China.

Clean water is synonymous with health in Puerto Rico, La Asunta

For the 146 families who live in the community of Puerto Rico in the municipality of La Asunta in the region of the Yungas of La Paz, access to clean drinking water was something they had longed for. They found the solution to their problem in the support provided by the Integrated Community Development Fund, a USAID-funded Integrated Alternative Development program, implemented in close coordination with the Plurinational State of Bolivia.



Remedios Mendoza using her standpipe – one of the 146 domestic connections in the Puerto Rico water system.

Remedios Mendoza, a member of the community’s water committee, describes what life was like before: “It used to be a major problem for us Many years ago, the river was more or less clean, but in the last few years it had become very polluted When the river rose in the rainy season, the water was very muddy, but we still had to bring all the water we needed from the river. We used the river for washing and it was our source of drinking water as well. This caused major health problems – people were always getting stomach upsets, diarrhea...”

Children were especially vulnerable to health problems caused by the use of water from the river, and this was one of the things that most concerned Remedios, mother of three children. The lack of a nearby water source also made daily life difficult for women and older people. “I used to carry about twenty liters of water a day up from the river – that’s what I needed for cooking..... It was a long way – we had to walk for fifteen to twenty minutes.... Some women had to walk a lot further than that, depending on where their house was. I used to feel so sorry for the older people carrying all that water...”

The health worker who runs the Puerto Rico health post, Leonicio Zarate Flores has seen for himself the positive impact that clean water has had on the community’s health: “Before, the rates of acute diarrheal diseases were going up every year, causing severe dehydration in children and in older people too. Now that we have clean water, the rates of diarrheal diseases have gone down as a direct consequence – we’ve seen that in the children and also in older people.” He affirms that personal hygiene practices have also improved in many families in the community of Puerto Rico.

The ID Program actively promotes community participation throughout the project implementation process. This includes an important training component to transfer the capabilities and skills required to manage and maintain the water system. The training provided also places great emphasis on raising the community’s environmental awareness, focusing primarily on the rational use of water and protecting the water source.

Don Roberto, a plumber who was trained as part of the project and a member of the committee that operates the water system, describes the training events in which most of the community participated: “We are very grateful... they’ve given us [technical] assistance so that this water system will last a good many years. We didn’t know about maintenance, how to keep the system clean, regulations and all that. We needed that training so we could operate the system properly and make sure it doesn’t deteriorate. It’s a great system – a model system we might say... We’d never seen such a good water system before anywhere. We’re also proud that everyone in the community contributed,” Roberto adds, referring to the counterpart contribution provided by the community.

Remedios explains: “They told us we had to make a counterpart contribution equivalent to twenty percent... Part of that we provided in cash and the rest in labor: we had to carry sand and stones from the community to the water source – a distance of about five kilometers, and uphill all the way... We did all the work we promised to do... We got the whole community organized and we did the work in groups – it was a good way to do it.”

Thanks to the clean drinking water system, life has changed for the families in Puerto Rico: their health has improved, and their community organization is stronger. Now the community is confident that it can take forward new projects for the benefit of everyone who lives there.

ANNEX III Project Status Report (Matrix)

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
1	YE0424	Economico	Agricola	Alto Beni	Santa Elena	Provision de motodeshierbadoras	CONCLUIDO	4.588
2	YE0386	Economico	Pecuario	Alto Beni	Florida	Granja Avícola Quispe/Quispe - Parrilleros	CONCLUIDO	1.752
3	YE0363	Economico	Transformacion	Alto Beni	San Antonio	Apicultura "Cuba"	CONCLUIDO	3.963
4	YE0283	Economico	Pecuario	Alto Beni	Colonia Villa Prado,Pista Suapi	Agropecuaria "ALBORTA"	CONCLUIDO	15.883
5	YE0280	Economico	Pecuario	Alto Beni	Sararia	Crianza de Pollos Parrilleros - "AJNO"	CONCLUIDO	19.067
6	YE0279	Economico	Transformacion	Alto Beni	Bella Vista	Artesanias / Capinteria - Inucua	CONCLUIDO	14.193
7	YE0277	Economico	Pecuario	Alto Beni	Nuevo Suapi Kilometro 73	Agropecuaria "MARTIN CARDENAS"	CONCLUIDO	8.220
8	YE0276	Economico	Transformacion	Alto Beni	San Antonio	Carpintería Industrial "Callisaya"	CONCLUIDO	14.193
9	YE0272	Economico	Pecuario	Alto Beni	Colonia Boopi	Producción de Huevos - "SAN ANTONIO"	CONCLUIDO	7.176
10	YE0270	Economico	Transformacion	Alto Beni	Colonia Entre Rios Km. 52	Implementación de una Planta Procesadora de Alimentos Balanceados	CONCLUIDO	8.764
11	YE0269	Economico	Transformacion	Alto Beni	Comunidad Villa El Porvenir	Planta Deshidratadora de Frutas - "APAVIP"	CONCLUIDO	7.442
12	YE0265	Economico	Servicios	Alto Beni	San Antonio	Materiales Didácticos - "JULI"	CONCLUIDO	8.585
13	YE0260	Economico	Pecuario	Alto Beni	Illimani	Porcinocultura - FLORES	CONCLUIDO	2.600
14	YE0257	Economico	Pecuario	Alto Beni	Colonia Los Tigres	Centro Ecológico de Investigación Agropecuaria El Pahuichi - "CEINAP"	CONCLUIDO	17.709
15	YE0256	Economico	Pecuario	Alto Beni	Santa Rosa	Comercialización de Carne y Piel de Cuye	CONCLUIDO	1.571

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
16	YE0255	Economico	Pecuario	Alto Beni	San Antonio	Producción de Pollos Parrilleros - "GRANJA NINA"	CONCLUIDO	19.067
17	YE0251	Economico	Pecuario	Alto Beni	Colonia Ingavi,Santa Rosa	Mejoramiento del Hato Ganadero Lechero - "INGAVI - COBIJA"	CONCLUIDO	14.687
18	YE0250	Economico	Pecuario	Alto Beni	Bella Vista,Colonia Forestal	Mejoramiento del Hato Ganadero Lechero "LA FORESTAL"	CONCLUIDO	14.687
19	YE0249	Economico	Servicios	Alto Beni	San Antonio	Implementación de Microempresa Metalmecánica	CONCLUIDO	10.661
20	YE0242	Economico	Pecuario	Alto Beni	Colonia Apostol Santiago (I),Sapecho	Producción y Comercialización de Cerdos "APOSTOL SANTIAGO"	CONCLUIDO	15.883
21	YE0240	Economico	Transformacion	Alto Beni	Colonia Ingavi,Santa Rosa	Elaboración de Derivados Lácteos "TICOLAC"	CONCLUIDO	19.746
22	YE0238	Economico	Pecuario	Alto Beni	Colonia Illimani,San Antonio	Pollos Parrilleros Illimani San Antonio	CONCLUIDO	19.067
23	YE0237	Economico	Pecuario	Alto Beni	San Antonio	Crianza de Ovinos de Pelo	CONCLUIDO	7.352
24	YE0231	Economico	Transformacion	Alto Beni	Bella Vista	Apicultura "APAAB"	CONCLUIDO	7.781
25	YE0158	Economico	Agricola	Alto Beni	Colonia Piquendo	Producción y comercialización de frejol negro	CONCLUIDO	8.929
26	YE0157	Economico	Transformacion	Alto Beni	Santa Rosa	Transformación y comer. Curcuma	CONCLUIDO	6.095
27	YC0152	Economico	Varios	Alto Beni	Colonia Collasuyo,San Antonio,Sararia	Reforzamiento al Funcionamiento del Modelo de Gestión y Productivo de los Internados de San Antonio, Sararia y Nueva Kollasuyo	CONCLUIDO	17.930
28	YC0146	Comunitario	Infraestructura comunitaria	Alto Beni	Piquendo	Conclusión sede social Piquendo	CONCLUIDO	22.491
29	YR0143	Comunitario	Agua Potable	Alto Beni	Varios	Diseño: Sistema de Agua Potable (11 comunidades)	CONCLUIDO	21.986
30	YC0134	Comunitario	Educación	Alto Beni	Km 73 - Suapi	Ampliación Colegio Martín Cárdenas	CONCLUIDO	182.403

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
31	YR0131	Economico	Transformacion	Alto Beni	Colonia Piquendo, Colonia Villa Camacho	Implementación planta procesadora de frutas	CONCLUIDO	3.500
32	YR0118	Economico	Agricola	Alto Beni	San Antonio	Provisión Motodeshierbadoras (146)	CONCLUIDO	42.924
33	YR0117	Economico	Agricola	Alto Beni	Piquendo	Provisión Motodeshierbadoras (22)	CONCLUIDO	6.468
34	YR0116	Economico	Agricola	Alto Beni	Villa Camacho	Provisión Motodeshierbadoras (38)	CONCLUIDO	11.172
35	YR0115	Economico	Agricola	Alto Beni	Pajonal I	Provisión Motodeshierbadoras (21)	CONCLUIDO	6.174
36	YR0114	Economico	Agricola	Alto Beni	Ocampo	Provisión Motodeshierbadoras (32)	CONCLUIDO	9.408
37	YR0113	Economico	Agricola	Alto Beni	Nueva Esperanza	Provisión Motodeshierbadoras (22)	CONCLUIDO	6.468
38	YR0112	Economico	Agricola	Alto Beni	Nueva Collasuyo	Provisión Motodeshierbadoras (26)	CONCLUIDO	7.644
39	YR0111	Economico	Agricola	Alto Beni	Ingavi - Cobija	Provisión Motodeshierbadoras (20)	CONCLUIDO	5.880
40	YR0110	Economico	Agricola	Alto Beni	Expontánea Illimani	Provisión Motodeshierbadoras (11)	CONCLUIDO	3.234
41	YR0109	Economico	Agricola	Alto Beni	Entre Rios - Playa Azul	Provisión Motodeshierbadoras (16)	CONCLUIDO	4.704
42	YR0108	Economico	Agricola	Alto Beni	Apóstol Santiago	Provisión Motodeshierbadoras (20)	CONCLUIDO	5.880
43	YR0100	Comunitario	Agua Potable	Alto Beni	Central Provenir	Diseno: Sistema de Agua Potable - Central Porvenir	CONCLUIDO	10.750
44	YR0099	Comunitario	Agua Potable	Alto Beni	Colke Alta	Sistema de Agua Potable	CONCLUIDO	191.302
45	YR0098	Comunitario	Agua Potable	Alto Beni	Nuevo Amanecer	Sistema de Agua Potable	CONCLUIDO	26.539
46	YR0097	Comunitario	Agua Potable	Alto Beni	Villa Santiago	Complementación Agua Potable	CONCLUIDO	31.775
47	YR0094	Economico	Infraestructura Productiva	Alto Beni	Colonia San Luis	Imp. beneficiadoras de cacao	CONCLUIDO	88.428

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
48	YR0093	Economico	Infraestructura Productiva	Alto Beni	Colonia Brecha "T"	Imp. beneficiadoras de cacao	CONCLUIDO	57.755
49	YE0081	Comunitario	Educación	Alto Beni	Caserio N°9	Const. aulas, viviendas y bat.banios	CONCLUIDO	52.446
50	YR0080	Comunitario	Salud	Alto Beni	Puerto Carmen	Equipamiento mini hospital	CONCLUIDO	24.700
51	YR0075	Comunitario	Educación	Alto Beni	Colonia Belen	Diseño: Construcción escuela y batería de baños	CONCLUIDO	119
52	YR0068	Comunitario	Infraestructura comunitaria	Alto Beni	Central San Antonio	Sala de reunión central San Antonio	CONCLUIDO	80.731
53	YR0067	Comunitario	Salud	Alto Beni	Kollasuyo	Conclusión posta sanitaria	CONCLUIDO	2.164
54	YR0066	Comunitario	Salud	Alto Beni	Mercedes	Construcción posta sanitaria	CONCLUIDO	48.023
55	YR0065	Comunitario	Infraestructura comunitaria	Alto Beni	Puente Alto Beni	Construcción de sala de reuniones	CONCLUIDO	36.023
56	YR0064	Comunitario	Salud	Alto Beni	Sararia	Construcción centro de salud	CONCLUIDO	50.442
57	YR0063	Comunitario	Educación	Alto Beni	Sararia	Construcción complejo educativo Sararia	CONCLUIDO	169.983
58	YR0062	Comunitario	Educación	Alto Beni	Colonia Palmar Suapi	Const. Unidad Educativa Palmar Suapi	CONCLUIDO	52.488
59	YE0021	Comunitario	Educación	Alto Beni	Km 73 - Poblacion Suapi	Cont. bloque de talleres UE Martín Cárdenas	CONCLUIDO	45.454
60	YR0016	Comunitario	Agua Potable	Alto Beni	Varios	Megaproyecto Agua Potable (Fase II) - Area I	CONCLUIDO	447.277
61	YC0008A	Comunitario	Saneamiento	Alto Beni	Colonia Boopi,Sararia	Implementación de UHF's (201 UHF's)	CONCLUIDO	458.700
62	YE0235	Economico	Transformacion	Alto Beni	Bella Vista	Planta Procesadora de Derivados Lácteos "APROLAB"	EJECUCION	22.406
63	YE0234	Economico	Transformacion	Alto Beni	Colonia Belen	Elaboración y Comercialización de derivados Citricolas "ASOPROCID"	EJECUCION	39.463
64	TE0443	Economico	Pecuario	Chimore	Varios	Apoyo campaña de vacunacion contra Fiebre Aftosa - Chimore	CONCLUIDO	2.500

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
65	TC0425	Comunitario	Educación	Chimore	Nueva Vida	Equipamiento del Internado Unidad Educativa comunidad indígena Nueva Vida	CONCLUIDO	43.425
66	TE0420	Economico	Infraestructura Productiva	Chimore	Senda 2	Mejoramiento y conclusion ambientes de UNABANA	CONCLUIDO	9.000
67	TE0315	Economico	Transformacion	Chimore	Nueva Vida	Construccion de Cartonera para Empacadora de Banano	CONCLUIDO	6.000
68	TC0294	Comunitario	Educación	Chimore	Estano Palmito	Dotación de mobiliario escolar - Unidad Educativa Estaño Palmito	CONCLUIDO	1.344
69	TE0293	Economico	Capacitacion productiva	Chimore	Varios	Capacitacion en adminstración, contabilidad básica y elaboración de perfil de proyectos- Federaciones de varones y de Mujeres, Trópico de Cochabamba	CONCLUIDO	6.000
70	TE0222	Economico	Infraestructura Productiva	Chimore	Nueva Esperanza	Centro de Acopio de Flores y Capacitacion para Mujeres	CONCLUIDO	14.700
71	TR0171	Economico	Infraestructura Productiva	Chimore	Chimore	Diseño Construcción y equip. taller artesanal	CONCLUIDO	6.680
72	TC0148	Comunitario	Educación	Chimore	Chimore	Mejoramiento infraestructura TAC	CONCLUIDO	108.890
73	TR0124	Comunitario	Educación	Chimore	Puerto Victoria	Construcción aula multigrado y batería baños	CONCLUIDO	5.197
74	TR0123	Comunitario	Educación	Chimore	Monte Sinai	Construcción 2 aulas, baños y mobiliario	CONCLUIDO	7.564
75	TR0122	Comunitario	Educación	Chimore	Betania	Construcción 2 aulas, baños y mobiliario	CONCLUIDO	7.564
76	TR0121	Comunitario	Salud	Chimore	Trinidadcito (# 1)	Diseño: Construcción posta salud y equipamiento	CONCLUIDO	44.925
77	TC0003	Comunitario	Infraestructura comunitaria	Chimore	Varios	Iluminación 7 Canchas Polifuncionales	CONCLUIDO	18.291
78	YC0647	Comunitario	Educación	Chulumani	Chulumani	Equipamiento de mobiliario para establecimientos educativos en el Municipio de Chulumani.	CONCLUIDO	17.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
79	YC0549	Comunitario	Salud	Chulumani	Chulumani	Equipamiento de mobiliario clínico para 3 establecimientos de salud.	CONCLUIDO	10.000
80	YC0538	Comunitario	Agua Potable	Chulumani	Cuchumpaya	Refacción Sistema de agua potable - Cuchumpaya	CONCLUIDO	9.500
81	YC0537	Comunitario	Agua Potable	Chulumani	Quilasa	Refacción Sistema de agua potable - Quilasi	CONCLUIDO	2.800
82	YC0536	Comunitario	Agua Potable	Chulumani	Bajo Loa	Refacción Sistema de agua potable Bajo Loa	CONCLUIDO	6.200
83	YC0535	Comunitario	Agua Potable	Chulumani	Comunidad Huayrapata	Refacción Sistema de agua potable Huayrapata	CONCLUIDO	6.800
84	YC0511	Comunitario	Educación	Chulumani	Chulumani	Refacción de la Batería de Baños de la U.E. Pre-escolar Chulumani.	CONCLUIDO	8.000
85	YC0468	Comunitario	Capacitacion comunitaria	Chulumani	Huancane	Capacitación Jóvenes en D. Humano y Liderazgo - U.E San Cristobal Huancane - Chulumani	CONCLUIDO	9.764
86	YC0467	Comunitario	Capacitacion comunitaria	Chulumani	Chulumani	Capacitación Jóvenes en D. Humano y Liderazgo - U.E Miguel Mercado -	CONCLUIDO	9.764
87	YE0378	Economico	Medio ambiente	Chulumani	Varios	Recuperación de suelos (40 has) de ex cicales en la Zona Tradicional	CONCLUIDO	98.500
88	YE0356	Economico	Pecuario	Chulumani	Rio Blanco	Producción de Pollos Parrilleros "Nido"	CONCLUIDO	15.052
89	YE0354	Economico	Transformacion	Chulumani	Comunidad El Colpar	Panadería "Umalinda"	CONCLUIDO	8.324
90	YE0353	Economico	Transformacion	Chulumani	Rio Blanco	Producción de Miel de Abejas "RIO BLANCO"	CONCLUIDO	1.990
91	YE0351	Economico	Pecuario	Chulumani	Pasto Pata	Producción de Pollos Parrilleros "AVERANGA"	CONCLUIDO	17.000
92	YE0350	Economico	Transformacion	Chulumani	Rio Blanco	Panadería "JHONNY"	CONCLUIDO	9.183
93	YE0349	Economico	Transformacion	Chulumani	Rio Blanco	Producción de miel y jalea "ESCOBAR"	CONCLUIDO	7.139
94	YE0347	Economico	Pecuario	Chulumani	Rio Blanco	Producción de Cerdos "Flores"	CONCLUIDO	16.502

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
95	YE0344	Economico	Agricola	Chulumani	Chulumani	Manejo y Producción de Mangos "San Rafael"	CONCLUIDO	4.018
96	YE0342	Economico	Transformacion	Chulumani	Rio Blanco	Venta de Pollos Broaster y Salchipapería "Angélica"	CONCLUIDO	2.479
97	YE0340	Economico	Pecuario	Chulumani	Comunidad El Colpar	Propucción de Gallinas de Postura "LOZA"	CONCLUIDO	15.852
98	YE0339	Economico	Transformacion	Chulumani	Rio Blanco	Heladería "Los Manzanales"	CONCLUIDO	10.432
99	YE0334	Economico	Pecuario	Chulumani	Rio Blanco	Producción de Cerdos "Torrez"	CONCLUIDO	11.040
100	YE0333	Economico	Transformacion	Chulumani	Rio Blanco	Carnicería "GUTIERREZ"	CONCLUIDO	6.495
101	YC0308	Comunitario	Educación	Chulumani	Chorrillo	Diseno: Polifuncional, y .Vivienda para un maestro	CONCLUIDO	500
102	YC0307	Comunitario	Infraestructura comunitaria	Chulumani	Palma Pampa	Diseno: Centro de Capacitación- Palma Pampa	CONCLUIDO	1.250
103	YC0306	Comunitario	Infraestructura comunitaria	Chulumani	Colpar	Construcción Plaza Principal - El Colpar	CONCLUIDO	38.858
104	YC0305	Comunitario	Educación	Chulumani	Rio Blanco	Conclusión Obra fina 1er piso Colegio Bartolina Sisa de Rio Blanco (Fase 2)	CONCLUIDO	50.292
105	YC0303	Comunitario	Agua Potable	Chulumani	Rio Blanco	Sistema de Agua Potable Rio Blanco	CONCLUIDO	126.239
106	YR0144	Comunitario	Agua Potable	Chulumani	Colopampa	Agua potable	CONCLUIDO	70.597
107	YR0087	Comunitario	Educación	Chulumani	El Colpar	Conclusión Vivienda Maestros y batería baños	CONCLUIDO	41.615
108	YE0082	Economico	Servicios	Chulumani	Chulumani	Apoyo a las empresas constructoras que se adjudicaron proyectos en la Feria a la Inversa del Municipio de Chulumani	CONCLUIDO	58.653
109	YC0058	Comunitario	Educación	Chulumani	Huancane - Huancane	Obra Fina Aulas (10) - Colegio S. Cristóbal	CONCLUIDO	48.417

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
110	YC0048	Comunitario	Infraestructura comunitaria	Chulumani	Huancane - Tongobaya	Centro de Capacitación	CONCLUIDO	15.320
111	YC0043	Comunitario	Educación	Chulumani	Chulumani - Chulumani	Refacción UE Kinder Chulumani	CONCLUIDO	37.155
112	YC0042	Comunitario	Educación	Chulumani	Rio Blanco - Rio Blanco	Const. Segunda Fase UE Bartolina Sisa Río Blanco	CONCLUIDO	24.998
113	YC0041	Comunitario	Saneamiento	Chulumani	Chulumani - Zona Junin	Baterías de Baño (obra gruesa) Zona Junin	CONCLUIDO	46.114
114	YC0040	Comunitario	Saneamiento	Chulumani	Chulumani - Zona Cancha	Mejoramiento Mingitorio cerca cancha Chulumani	CONCLUIDO	10.695
115	YC0039	Comunitario	Educación	Chulumani	Tajma - Villa Remedios	Const. Baño para la Escuela Villa Remedios	CONCLUIDO	12.678
116	YC0038	Comunitario	Saneamiento	Chulumani	Ocobaya - Ocobaya	Mejoramiento Mingitorio Ocobaya	CONCLUIDO	13.676
117	YC0037	Comunitario	Infraestructura comunitaria	Chulumani	Huancane - Huancane	Empedrado calle al Colegio Huancane	CONCLUIDO	17.083
118	YC0036	Comunitario	Infraestructura comunitaria	Chulumani	Cutusuma - Montequilla	Centro de Capacitación Productiva Montequilla	CONCLUIDO	20.696
119	YC0024	Comunitario	Saneamiento	Chulumani	Tajma - Tajma	Sistema de Alcantarillado Sanitario	CONCLUIDO	74.935
120	YC0023	Comunitario	Educación	Chulumani	Ocobaya - Ocobaya	Conclusión Colegio de Ocobaya	CONCLUIDO	18.564
121	YC0022	Comunitario	Educación	Chulumani	Chulumani	Refacción Colegio Miguel Mercado	CONCLUIDO	43.265
122	YC0015	Comunitario	Infraestructura comunitaria	Chulumani	Chulumani	Equipamiento Mob. Municipio Chulumani	CONCLUIDO	20.000
123	YC0648	Comunitario	Educación	Coripata	Coripata	Equipamiento de mobiliario para establecimientos educativos en el Municipio de Coripata	CONCLUIDO	17.000
124	YC0635	Comunitario	Saneamiento	Coripata	Comunidad San Agustín	Diseño Final del Sistema de Alcantarillado Sanitario de San Agustín	CONCLUIDO	8.000
125	YC0614	Comunitario	Educación	Coripata	El Choro	Equipamiento mobiliario para 2 U.E. (El Choro Milluguaya).	CONCLUIDO	3.500

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
126	YE0599	Economico	Infraestructura vial	Coripata	Comunidad Anacuri, Comunidad Auquisamaña	Construcción de alcantarillas: Tramo Coripata – Pte Chacon y Anaruri - Auquisanana	CONCLUIDO	10.800
127	YC0546	Comunitario	Salud	Coripata	Coripata	Equipamiento clínico complejo para el hospital básico de Coripata	CONCLUIDO	25.000
128	YC0515	Comunitario	Infraestructura comunitaria	Coripata	Coripata	Dotación de mobiliario para el centro social de ADEPCOCA – Regional Coripata.	CONCLUIDO	10.300
129	YE0497	Economico	Turismo	Coripata	Municipal	Diseño final terminal de buses Coripata	CONCLUIDO	10.000
130	YC0484	Comunitario	Educación	Coripata	Trinidad Pampa	Conclusión de la Unidad Educativa Franz Tamayo	CONCLUIDO	75.600
131	YC0472	Comunitario	Capacitacion comunitaria	Coripata	Arapata	Capacitación Jóvenes en D. Humano y Liderazgo - U.E Rosemary Barrientos- Arapata- Coripata	CONCLUIDO	9.764
132	YC0471	Comunitario	Capacitacion comunitaria	Coripata	Coripata	Capacitación Jóvenes en D. Humano y Liderazgo - U.E Eduardo Abaroa- Coripata	CONCLUIDO	9.764
133	YC0427	Comunitario	Educación	Coripata	Marquirivi	Construccion de 2 Viviendas y Bateria de Baños Marquirivi	CONCLUIDO	22.175
134	YC0426	Comunitario	Infraestructura comunitaria	Coripata	Auquisamaña	Conclusion Obra Fina Iglesia Auquisamaña	CONCLUIDO	26.135
135	YE0355	Economico	Transformacion	Coripata	San Jose de Peri	Carnicería "Santa Rita"	CONCLUIDO	5.286
136	YE0352	Economico	Transformacion	Coripata	Huaycuni	Panadería "JULIA"	CONCLUIDO	9.183
137	YE0348	Economico	Pecuario	Coripata	Municipal	Producción de Gallinas de Postura "LAYDI"	CONCLUIDO	15.852
138	YE0346	Economico	Transformacion	Coripata	San Jose de Peri	Panadería "San José"	CONCLUIDO	7.882
139	YE0345	Economico	Pecuario	Coripata	San Jose de Peri	Producción de miel de abejas "NINA"	CONCLUIDO	4.668
140	YE0343	Economico	Servicios	Coripata	San José de Peri	Comidería "DOÑA JUAQUINA"	CONCLUIDO	7.836

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
141	YE0341	Economico	Transformacion	Coripata	San José de Peri	Taller de Confección Pollería "ALBERTA"	CONCLUIDO	2.390
142	YE0338	Economico	Transformacion	Coripata	Arapata	Carpintería "Juan de la Cruz"	CONCLUIDO	4.052
143	YE0337	Economico	Pecuario	Coripata	Comunidad Anacuri	Producción de Cerdos "Choque"	CONCLUIDO	16.502
144	YE0336	Economico	Servicios	Coripata	San José de Peri	Snack "DOÑA LUPE"	CONCLUIDO	1.807
145	YE0335	Economico	Pecuario	Coripata	San José de Peri	Producción de Pollos Parrileros "DOÑA MARTHA"	CONCLUIDO	14.681
146	YC0311	Comunitario	Educación	Coripata	Huaycuni	Conclusión Centro de Capacitación - Huaycuni	CONCLUIDO	107.644
147	YC0310	Comunitario	Educación	Coripata	San Jose de Peri	Conclusión Centro de Capacitación - San José de Peri - 1ra fase	CONCLUIDO	106.530
148	YC0309	Comunitario	Infraestructura comunitaria	Coripata	Comunidad Anacuri	Construcción complejo deportivo turístico	CONCLUIDO	185.592
149	YR0145	Comunitario	Infraestructura comunitaria	Coripata	Santa Rosa	Obra fina iglesia	CONCLUIDO	41.386
150	YR0142	Comunitario	Infraestructura comunitaria	Coripata	Santa Rosa (Arapata)	Polifuncional Santa Rosa de Lima	CONCLUIDO	25.640
151	YR0141	Comunitario	Infraestructura comunitaria	Coripata	Tabacal	Refacción casa de hacienda para albergue	CONCLUIDO	121.298
152	YR0140	Comunitario	Agua Potable	Coripata	Machacamarca	Agua potable	CONCLUIDO	95.628
153	YR0139	Comunitario	Infraestructura comunitaria	Coripata	Machacamarca	Obra fina sede social	CONCLUIDO	78.633
154	YR0103	Comunitario	Infraestructura comunitaria	Coripata	Anacuri	Obra fina iglesia	CONCLUIDO	44.303
155	YC0083	Comunitario	Fortalecimiento comunitario	Coripata	Coripata	Apoyo al interyungueño de fútbol 2006	CONCLUIDO	2.680
156	YR0077	Comunitario	Infraestructura comunitaria	Coripata	Arapata	Construcción Mercado Central	CONCLUIDO	116.098
157	YC0045	Comunitario	Educación	Coripata	Dorado Grande	Construcción aulas UE Dorado Grande	CONCLUIDO	32.550

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
158	YC0044	Comunitario	Educación	Coripata	Santa Getrudis	Construcción aulas UE Santa Gertrudis	CONCLUIDO	17.950
159	YC0030	Comunitario	Educación	Coripata	San Agustín	UE San Agustín	CONCLUIDO	85.654
160	YC0029	Comunitario	Educación	Coripata	Huayrapata	Diseño: UE Félix Ballivián - Huayrapata	CONCLUIDO	3.575
161	YC0028	Comunitario	Salud	Coripata	San Juan	Centro de Salud - San Juan	CONCLUIDO	36.767
162	YC0011	Comunitario	Salud	Coripata	Arapata	Ampliación Centro de Salud - Arapata	CONCLUIDO	18.585
163	YE0010	Comunitario	Infraestructura comunitaria	Coripata	Coripata	Sede Social - Sindical (ADEPCOCA)	CONCLUIDO	66.949
164	YC0616	Comunitario	Educación	Coripata	Comunidad Nogalani	Diseño y construcción obra fina 8 aulas en la U.E. de la comunidad de Nogalani	EJECUCION	69.000
165	YC0540	Comunitario	Agua Potable	Coripata	Dorado Grande	Construcción sistema de agua potable Dorado Chico – Dorado Grande.	EJECUCION	18.000
166	YC0539	Comunitario	Agua Potable	Coripata	Comunidad San Felix	Construcción sistema de agua potable San Félix – Dorado Chico – Dorado Grande.	EJECUCION	20.000
167	YC0507	Comunitario	Agua Potable	Coripata	Milluhuaya Bajo	Construcción del sistema de agua potable en Milluguaya	EJECUCION	109.300
168	YR0175	Economico	Transformacion	Coripata	Anacuri	Cortadora piedra laja	EJECUCION	26.845
169	YR0174	Economico	Servicios	Coripata	Comunidad Anacuri	Clasificadora de áridos	EJECUCION	65.428
170	YC0623	Comunitario	Agua Potable	Coroico	Comunidad San Joaquin	Diseño y construcción del sistema de agua potable San Joaquín.	ADJUDICACION	50.000
171	YC0649	Comunitario	Educación	Coroico	Coroico	Equipamiento de mobiliario para establecimientos educativos en el Municipio de Coroico	CONCLUIDO	25.000
172	YE0644	Economico	Turismo	Coroico	Coroico	Apoyo al sector turístico: Festival cultural Coroico 2010	CONCLUIDO	3.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
173	YC0643	Comunitario	Agua Potable	Coroico	Comunidad Tocaña	Dotación de Tubería para la extensión de la línea de aducción del sistema de agua de la comunidad de Tocaña.	CONCLUIDO	6.500
174	YE0634	Economico	Pecuario	Coroico	Coroico	Apoyo al segundo encuentro de la Asociación de Avicultores de La Paz	CONCLUIDO	2.200
175	YC0594	Comunitario	Agua Potable	Coroico	Comunidad San Cristobal	Diseño y construcción del Sistema de agua potable San Cristóbal.	CONCLUIDO	30.000
176	YC0593	Comunitario	Agua Potable	Coroico	Comunidad Santiago Grande	Diseño: Sistema de agua potable Santiago Grande	CONCLUIDO	62.000
177	YC0591	Comunitario	Educación	Coroico	Coroico	Diseño de 20 viviendas, batería de baños, cocina y comedor para maestros en la U.E. San Pedro de Coroico	CONCLUIDO	6.000
178	YC0590	Comunitario	Agua Potable	Coroico	Comunidad Marca	Ampliación Sistema de agua potable Marca	CONCLUIDO	1.200
179	YC0587	Comunitario	Agua Potable	Coroico	Comunidad San Geronimo	Ampliación del Sistema de agua potable San Gerónimo	CONCLUIDO	5.200
180	YC0586	Comunitario	Agua Potable	Coroico	Comunidad Santa Ana	Refacción del Sistema de Agua Potable Santa Ana	CONCLUIDO	6.200
181	YC0585	Comunitario	Agua Potable	Coroico	Comunidad Chiquiña	Construcción aducción sistema de agua potable de Chiquiña	CONCLUIDO	2.700
182	YC0584	Comunitario	Agua Potable	Coroico	Comunidad Calabatea	Ampliación del Sistema de agua potable Calabatea de Ayacucho.	CONCLUIDO	3.200
183	YC0583	Comunitario	Agua Potable	Coroico	Comunidad Chicaparque	Ampliación del Sistema de agua potable Chicaparque - Yolosita	CONCLUIDO	3.600
184	YC0541	Comunitario	Salud	Coroico	Coroico	Equipamiento complementario del hospital básico de Coroico	CONCLUIDO	30.000
185	YC0516	Comunitario	Educación	Coroico	Carmen Pampa	Provisión de materiales para la construcción de comedor de la UAC-CP	CONCLUIDO	28.000
186	YE0514	Economico	Turismo	Coroico	Coroico	Apoyo al sector turístico: Festival Cultural Coroico 2009	CONCLUIDO	5.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
187	YC0466	Comunitario	Capacitacion comunitaria	Coroico	Coroico	Capacitación Jóvenes en D. Humano y Liderazgo - U.E Reyes Ortíz - Coroico	CONCLUIDO	9.764
188	YC0465	Comunitario	Capacitacion comunitaria	Coroico	Cruz Loma	Capacitación Jóvenes en D. Humano y Liderazgo - U.E Téc. Humanístico Cruz Loma- Coroico	CONCLUIDO	9.764
189	YC0460	Comunitario	Capacitacion comunitaria	Coroico	Varios	Capacitación en Enfermería - Becas Magíster UAC-CP	CONCLUIDO	7.280
190	YE0199	Economico	Infraestructura vial	Coroico	Charobamba	Diseno de acceso al Puente vehicular colgante	CONCLUIDO	20.168
191	YC0192	Comunitario	Fortalecimiento comunitario	Coroico	Coroico	Apoyo Festival Folklorico Internacional Coroico 2007	CONCLUIDO	5.000
192	YC0172	Economico	Turismo	Coroico	Comunidad Tocaña	Desarrollo turístico comunitario	CONCLUIDO	14.000
193	YC0169	Comunitario	Salud	Coroico	Tocaña	Conclusión obra fina posta de salud	CONCLUIDO	20.875
194	YC0168	Comunitario	Educación	Coroico	Carmen Pampa	Intervención en UAC-CP "Construcción del bloque de dormitorios Leahy"	CONCLUIDO	280.000
195	YC0162	Comunitario	Fortalecimiento comunitario	Coroico	Coroico	Fort. institucional (PDM Alcaldía Coroico)	CONCLUIDO	15.725
196	YC0147	Comunitario	Infraestructura comunitaria	Coroico	Carmen Pampa	Canalización río Nilo - Carmen Pampa	CONCLUIDO	81.638
197	YC0137	Economico	Turismo	Coroico	Comunidad Tocaña	Construcción obras complem. centro cultural	CONCLUIDO	60.333
198	YC0104	Comunitario	Infraestructura comunitaria	Coroico	Coroico	Reposición obras piscina y fortalec. municipal	CONCLUIDO	51.373
199	YR0101	Comunitario	Infraestructura comunitaria	Coroico	Coroico	Polifuncional deportivo de Coroico	CONCLUIDO	99.960
200	YR0057	Comunitario	Saneamiento	Coroico	Suapi	Sistema de Alcantarillado Sanitario	CONCLUIDO	92.074
201	YR0056	Comunitario	Salud	Coroico	Comunidad Kilo Kilo Alto	Construcción Centro de Salud de Santa Rosa de Quilo Quilo	CONCLUIDO	106.585

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
202	YR0055	Comunitario	Infraestructura comunitaria	Coroico	Santa Rosa de Quilo Quilo	Plaza	CONCLUIDO	50.592
203	YR0054	Comunitario	Saneamiento	Coroico	Santa Rosa de Quilo Quilo	Sistema de Alcantarillado Sanitario	CONCLUIDO	76.981
204	YC0034	Comunitario	Educación	Coroico	Chiquina	Diseño: Escuela Multigrado Chiquina	CONCLUIDO	75
205	YE0012B	Comunitario	Otros	Coroico	Comunidad Yolosa	Apoyo a Actividades de Rescate (FEJUVE)	CONCLUIDO	10.842
206	YE0592	Economico	Turismo	Coroico	Comunidad San Felix	Mejoramiento del sitio turístico de la comunidad de San Félix	EJECUCION	21.000
207	YC0589	Comunitario	Agua Potable	Coroico	Coroico	Refacción una sección de la red de agua potable - Coroico Urbano	EJECUCION	3.600
208	YC0588	Comunitario	Agua Potable	Coroico	Comunidad Cochuma	Rehabilitación del sistema de agua de Cochuna - Coroico	EJECUCION	8.000
209	YC0485	Comunitario	Saneamiento	Coroico	Comunidad San Joaquin	Relleno Sanitario - Coroico	EJECUCION	200.000
210	TE0446	Economico	Pecuario	Entre Rios	Varios	Apoyo campaña de vacunacion contra Fiebre Aftosa - Entre Ríos	CONCLUIDO	33.000
211	TE0302	Economico	Transformacion	Entre Rios	Valle Sacta	Apoyo a AUPAII VII	CONCLUIDO	6.500
212	TE0301	Economico	Pecuario	Entre Rios	Entre Ríos,Manco Kapac,Río Blanco	Apoyo a laproducción pecuaria	CONCLUIDO	6.000
213	TE0300	Economico	Agricola	Entre Rios	El Palmar,Los Amigos,San Miguel	Apoyo a la producción de Piña	CONCLUIDO	20.000
214	TE0299	Economico	Agricola	Entre Rios	Machu Pijchu	Apoyo a la producción de Banano	CONCLUIDO	4.000
215	TC0211	Comunitario	Salud	Entre Rios	Entre Ríos	Diseño Hospital 2do. Nivel Entre Ríos - Fase 1	CONCLUIDO	37.000
216	TR0198	Comunitario	Agua Potable	Entre Rios	Sindicato Ira Volcan	Conclusión sistema de agua potable	CONCLUIDO	21.500
217	TR0178	Comunitario	Agua Potable	Entre Rios	Varios	Construcción Sistema Agua Potable 4 centrales	CONCLUIDO	82.000
218	TR0170	Comunitario	Educación	Entre Rios	Barrio Imperial	Cubierta e iluminación UE Octavio Pastrana	CONCLUIDO	64.655

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
219	TC0005	Comunitario	Infraestructura comunitaria	Entre Rios	Bulo Bulo	Conclusión Plaza Principal - Bulo Bulo	CONCLUIDO	19.778
220	YC0615	Comunitario	Educación	Irupana	Churubamba	Equipamiento mobiliario para 2 U.E. Churubamba y Huiiri Nogalani	CONCLUIDO	5.500
221	YE0598	Economico	Infraestructura vial	Irupana	Irupana, Varios	Construcción de alcantarillas en caminos comunales de Irupana	CONCLUIDO	14.600
222	YC0527	Comunitario	Agua Potable	Irupana	Comunidad Silala	Refacción y mejoramiento del Sistema de Agua Potable - Silala	CONCLUIDO	1.900
223	YC0526	Comunitario	Agua Potable	Irupana	Comunidad Uquina	Refacción y mejoramiento del Sistema de Agua Potable - Uquina	CONCLUIDO	2.100
224	YC0525	Comunitario	Agua Potable	Irupana	Yuni Grande	Refacción y mejoramiento del Sistema de Agua Potable - Yuni Grande	CONCLUIDO	2.480
225	YC0524	Comunitario	Agua Potable	Irupana	Comunidad Santa Ana	Refacción y mejoramiento del Sistema de Agua Potable Santa Ana	CONCLUIDO	5.600
226	YC0502	Comunitario	Agua Potable	Irupana	Chicaloma	Diseño y Construcción Tanque de Almacenamiento de Agua de la Población de Chicaloma.	CONCLUIDO	24.000
227	YC0464	Comunitario	Capacitacion comunitaria	Irupana	Irupana	Capacitación Jóvenes en Desarrollo Humano y Liderazgo - U.E 5 de Mayo- Irupana	CONCLUIDO	9.764
228	YC0463	Comunitario	Capacitacion comunitaria	Irupana	Chicaloma	Capacitación Jóvenes en Desarrollo Humano y Liderazgo - U.E Chicaloma- Irupana	CONCLUIDO	9.764
229	YR0078	Comunitario	Educación	Irupana	Chicaloma	Refacción Unidad Educativa Chicaloma	CONCLUIDO	151.701
230	YR0061	Comunitario	Infraestructura comunitaria	Irupana	Chicaloma	Plaza Población Chicaloma	CONCLUIDO	77.884
231	YR0059	Comunitario	Saneamiento	Irupana	Chicaloma	Sistema de Alcantarillado Sanitario	CONCLUIDO	257.396
232	YE0658	Economico	Agricola	Irupana	Irupana	Desarrollo de proveedores en la cadena de amaranto orgánico de alta calidad en Yungas de La Paz	EJECUCION	98.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
233	YC0645	Comunitario	Educación	Irupana	Irupana	Equipamiento de mobiliario para establecimientos educativos en el Municipio de Irupana	EJECUCION	17.000
234	YC0506	Comunitario	Saneamiento	Irupana	Irupana	Construcción del sistema de alcantarillado de Paraíso	EJECUCION	110.000
235	YC0652	Comunitario	Educación	La Asunta	La Asunta	Equipamiento de mobiliario para establecimientos educativos Federación La Asunta	CONCLUIDO	25.000
236	YC0651	Comunitario	Educación	La Asunta	Chamaca	Equipamiento de mobiliario para establecimientos educativos Federación Chamaca	CONCLUIDO	25.000
237	YC0650	Comunitario	Educación	La Asunta	La Asunta	Equipamiento de mobiliario para establecimientos educativos del Centro poblado de La Asunta	CONCLUIDO	25.000
238	YC0642	Comunitario	Infraestructura comunitaria	La Asunta	La Asunta	Equipamiento de los centros de capacitación de las Centrales de La Asunta y El Progreso en el Municipio de La Asunta	CONCLUIDO	3.500
239	YC0629A	Comunitario	Salud	La Asunta	La Asunta	Campaña de capacitación y prevención de cáncer uterino en La Asunta	CONCLUIDO	5.000
240	YC0620	Comunitario	Infraestructura comunitaria	La Asunta	Santa Lucía	Diseño puente peatonal en San Gabriel	CONCLUIDO	8.000
241	YC0619	Comunitario	Infraestructura comunitaria	La Asunta	San Gabriel	Construcción de un bote con motor fuera de borda	CONCLUIDO	6.000
242	YC0617	Comunitario	Educación	La Asunta	La Asunta	Construcción de la obra fina de 16 viviendas y batería de baños UE de La Asunta.	CONCLUIDO	24.000
243	YE0602	Economico	Infraestructura vial	La Asunta	La Asunta, Varios	Construcción de alcantarillas en los caminos vecinales de la Bolívar IV	CONCLUIDO	9.540
244	YE0601	Economico	Infraestructura vial	La Asunta	La Asunta, Varios	Construcción de alcantarillas en los caminos vecinales de la Bolívar III	CONCLUIDO	9.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
245	YE0600	Economico	Infraestructura vial	La Asunta	La Asunta, Varios	Construcción de alcantarillas en los caminos vecinales de la Bolívar II	CONCLUIDO	9.000
246	YC0579	Comunitario	Salud	La Asunta	La Asunta	Campaña de detección de Cáncer en mujeres.	CONCLUIDO	5.000
247	YE0568	Economico	Infraestructura vial	La Asunta	Alto Charobamba, Chamaca, Tunquini	Construcción de alcantarillas tramo Villa Victoria - Palmeras	CONCLUIDO	22.500
248	YE0565	Economico	Infraestructura vial	La Asunta	Colonia 21 de Agosto	Construcción de alcantarillas tramo Nogalani - 21 de Agosto	CONCLUIDO	20.340
249	YE0564	Economico	Infraestructura vial	La Asunta	Siguani Grande	Construcción de alcantarillas tramo Siguaní Grande - Quillabamba	CONCLUIDO	22.500
250	YE0563	Economico	Infraestructura vial	La Asunta	Colonia Incahuara	Construcción de alcantarillas tramo 10 de Febrero - Churubamba - Incahuara de Canaan	CONCLUIDO	22.500
251	YE0562	Economico	Infraestructura vial	La Asunta	Santa Lucia	Construcción de alcantarillas tramo Santa Lucia - Chispanito	CONCLUIDO	21.420
252	YE0561	Economico	Infraestructura vial	La Asunta	Central Simon Bolivar	Construcción de alcantarillas en los caminos de la Central Bolívar	CONCLUIDO	22.500
253	YC0559	Economico	Infraestructura vial	La Asunta	Comunidad Pichari	Construcción de alcantarillas tramo Pichari - Nogalani - 10 de Febrero	CONCLUIDO	22.500
254	YC0558	Economico	Infraestructura vial	La Asunta	Comunidad San Pedro Zona "C"	Construcción de alcantarillas tramo San Pedro C - La Florida	CONCLUIDO	9.000
255	YC0532	Comunitario	Agua Potable	La Asunta	Santa Rosa	Refacción del Sistema de agua potable Santa Rosa	CONCLUIDO	10.500
256	YC0531	Comunitario	Agua Potable	La Asunta	Colonia 21 de Agosto	Complementación del Sistema de Agua Potable 21 de Agosto	CONCLUIDO	12.500
257	YC0530	Comunitario	Agua Potable	La Asunta	San Felipe	Refacción del Sistema de agua potable San Felipe	CONCLUIDO	9.800
258	YC0529	Comunitario	Agua Potable	La Asunta	Comunidad Cajones	Refacción del Sistema de agua potable Cajones	CONCLUIDO	4.600
259	YC0528	Comunitario	Agua Potable	La Asunta	Yanamayu	Refacción del Sistema de agua potable Yanamayo	CONCLUIDO	7.300
260	YC0512	Comunitario	Infraestructura comunitaria	La Asunta	Central Simon Bolivar	Rehabilitación de la hidroeléctrica de Chamaca	CONCLUIDO	5.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
261	YC0510	Comunitario	Educación	La Asunta	Central Simon Bolivar	Construcción de vivienda de maestros en Bolívar IV	CONCLUIDO	27.268
262	YC0509	Comunitario	Educación	La Asunta	Central Simon Bolivar	Construcción de vivienda de maestros en Bolívar III	CONCLUIDO	13.640
263	YC0508	Comunitario	Educación	La Asunta	La Asunta	Construcción de vivienda de maestros en Bolívar II	CONCLUIDO	12.445
264	YC0494	Comunitario	Agua Potable	La Asunta	Cotapata	Sistema de agua potable - Cotapata	CONCLUIDO	107.958
265	YC0493	Comunitario	Agua Potable	La Asunta	La Asunta	Sistema de agua potable - Puerto Rico	CONCLUIDO	94.103
266	YC0492	Comunitario	Otros	La Asunta	La Asunta	Mejorando la calidad de vida de la familia desde la cocina	CONCLUIDO	22.000
267	YE0489	Economico	Agricola	La Asunta	La Asunta	Plan Platano	CONCLUIDO	98.000
268	YE0486	Comunitario	Infraestructura comunitaria	La Asunta	La Asunta	Restablecimiento de la energía eléctrica en La Asunta	CONCLUIDO	30.000
269	YC0483	Comunitario	Educación	La Asunta	Incahuara	Construcción Unidad Educativa y Vivienda para Maestro	CONCLUIDO	36.000
270	YC0482	Comunitario	Educación	La Asunta	Iro de Julio	Construcción Unidad Educativa y Vivienda para Maestro	CONCLUIDO	36.000
271	YC0479	Comunitario	Otros	La Asunta	La Asunta	Estrategia de Comunicación La Asunta	CONCLUIDO	150.000
272	YC0478	Comunitario	Capacitación comunitaria	La Asunta	Santa Rosa	Capacitación a Jóvenes en Desarrollo Humano y Liderazgo - U.E Santa Rosa - La Asunta	CONCLUIDO	9.764
273	YC0477	Comunitario	Capacitación comunitaria	La Asunta	La Calzada, Nueva Union, San Jorge, Tica Pata	Capacitación a Jóvenes en D. Humano y Liderazgo - U.E Mercedes- La Calzada - La Asunta	CONCLUIDO	9.764
274	YC0476	Comunitario	Capacitación comunitaria	La Asunta	Charia	Capacitación a Jóvenes en Desarrollo Humano y Liderazgo - U.E Charia - La Asunta	CONCLUIDO	9.764

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
276	YC0474	Comunitario	Capacitacion comunitaria	La Asunta	Comunidad Alto Asunta, Comunidad Barbarito, Comunidad Cajones, Comunidad Floriaty, Comunidad Lagunillas, Comunidad Rio Seco, Comunidad Villa Esperanza	Capac.a Jóvenes en Desarrollo Humano y Liderazgo - U.E René Barrientos Ortuño - La Asunta	CONCLUIDO	9.764
277	YC0473	Comunitario	Capacitacion comunitaria	La Asunta	Cotapata, La Esperanza, Los Olivos, San Pablo, Sanandita	Capacitación a Jóvenes en D. Humano y Liderazgo - U.E Cotapata - La Asunta	CONCLUIDO	9.764
278	YC0459	Comunitario	Capacitacion comunitaria	La Asunta	Chamaca	Formacion de Formadores en Desarrollo Humano y Liderazgo a Jóvenes en Los Yungas de La Paz	CONCLUIDO	9.764
279	YC0458	Comunitario	Capacitacion comunitaria	La Asunta	La Asunta	Capacitación en Desarrollo Humano y Liderazgo a Jóvenes de Fed. La Asunta - La Asunta	CONCLUIDO	9.764
280	YC0457	Comunitario	Capacitacion comunitaria	La Asunta	Chorobamba, Yanamayu	Capacitación a Jóvenes en Desarrollo Humano y Liderazgo - U.E Yanamuyu I-II - La Asunta	CONCLUIDO	9.764
281	YE0377	Economico	Transformacion	La Asunta	Cuchumpaya	Apicultura "San Gabriel"	CONCLUIDO	3.963
282	YE0376	Economico	Servicios	La Asunta	Progreso - San San Unido	Salon de Peinados y Peluquería "Chura"	CONCLUIDO	6.055
283	YE0375	Economico	Servicios	La Asunta	Puerto Mejillones	Transporte en bote de Carga y Pasajeros "Titanic"	CONCLUIDO	8.059
284	YE0374	Economico	Transformacion	La Asunta	Comunidad Porvenir 20 de Mayo	Heladería "Jeremy"	CONCLUIDO	13.060
285	YE0373	Economico	Transformacion	La Asunta	Progreso - San San Unido	Jugos Naturales "Erika"	CONCLUIDO	5.419
286	YE0372	Economico	Transformacion	La Asunta	Cuchumpaya	Apicultura "Mamani"	CONCLUIDO	3.963
287	YE0371	Economico	Pecuario	La Asunta	Cotapata, San Pablo	Pollos parrilleros "FICO"	CONCLUIDO	13.515
288	YE0370	Economico	Transformacion	La Asunta	Progreso - Cuchumpaya	Jugos naturales "Silvia"	CONCLUIDO	5.419

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
289	YE0369	Economico	Pecuario	La Asunta	Comunidad Porvenir 20 de Mayo	Pollos parrilleros "Doña Isabel"	CONCLUIDO	15.466
290	YE0368	Economico	Transformacion	La Asunta	La Asunta	Taller de Carpintería "Alex"	CONCLUIDO	21.131
291	YE0367	Economico	Transformacion	La Asunta	Cotapata,La Asunta	Panaderia "INTEGRAL"	CONCLUIDO	5.920
292	YE0366	Economico	Transformacion	La Asunta	Cotapata	Taller de Carpintería CORFAV	CONCLUIDO	9.941
293	YE0365	Economico	Pecuario	La Asunta	Comunidad Barbarito	Producción de pollos parrilleros "ROCO"	CONCLUIDO	8.911
294	YE0364	Economico	Transformacion	La Asunta	Comunidad Porvenir 20 de Mayo	Corte y Confección "Gloria"	CONCLUIDO	5.982
295	YE0362	Economico	Transformacion	La Asunta	La Asunta	Taller de Carpintería "Quispe"	CONCLUIDO	18.531
296	YE0361	Economico	Transformacion	La Asunta	Progreso - Cuchumpaya	Taller de Confecciones de ropa de vestir "Yola"	CONCLUIDO	5.981
297	YE0360	Economico	Pecuario	La Asunta	Cuchumpaya	Granja gallinas ponedoras "Río Seco"	CONCLUIDO	15.076
298	YE0359	Economico	Transformacion	La Asunta	Comunidad Porvenir 20 de Mayo	Apicultura "Meza"	CONCLUIDO	3.963
299	YE0358	Economico	Transformacion	La Asunta	La Asunta	Panaderia "ESTHER"	CONCLUIDO	4.230
300	YE0332B	Economico	Turismo	La Asunta	La Asunta	Promocion de Apoyo Turistico en La Asunta "Hotel 20 de Septiembre"	CONCLUIDO	8.000
301	YE0332A	Economico	Turismo	La Asunta	La Asunta	Promoción de Desarrollo Turístico en La Asunta "HOTEL ERIKA"	CONCLUIDO	15.000
302	YC0331	Comunitario	Salud	La Asunta	San Gabriel	Diseno: Posta Sanitaria San Gabriel - Central Pto Rico Histórico	CONCLUIDO	44.228
303	YC0330	Comunitario	Educación	La Asunta	Cotapata,La Esperanza,Los Olivos,San Pablo,Sanandita	Dotación 7 Computadoras para Colegio y Generador E.Eléctrica - Central Cotapata	CONCLUIDO	18.500
304	YC0329	Comunitario	Educación	La Asunta	San Pablo	Construcción Multifuncional San Pablo - Central Cotapata	CONCLUIDO	19.525

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
305	YC0328	Comunitario	Educación	La Asunta	San Antonio	Construcción Aula Multigrado San Antonio- Central Pto.Unido	CONCLUIDO	21.204
306	YC0327	Comunitario	Educación	La Asunta	Porvenir 20 de Mayo	Construcción Aula Multigrado Villa El Porvenir- Central Pto.Unido	CONCLUIDO	21.204
307	YE0295	Economico	Capacitacion productiva	La Asunta	La Asunta	Intercambio de Productores Lideres - La Asunta	CONCLUIDO	35.700
308	YE0229	Economico	Pecuario	La Asunta	La Asunta	Producción de Pollos Parrilleros "Donato"	CONCLUIDO	1.135
309	YE0227	Economico	Medio ambiente	La Asunta	La Asunta	Parcelas agroforestales familiares - La Asunta	CONCLUIDO	42.500
310	YC0189	Comunitario	Capacitacion comunitaria	La Asunta	La Asunta	Capacitación bachilleres	CONCLUIDO	2.400
311	YR0086	Comunitario	Educación	La Asunta	Porvenir 20 de Mayo	Construcción Unidad Educativa El Porvenir	CONCLUIDO	31.439
312	YE0085	Economico	Infraestructura vial	La Asunta	Porvenir 20 de Mayo	Puente Peatonal Colgante	CONCLUIDO	26.644
313	YR0084	Economico	Infraestructura vial	La Asunta	Cuchumpaya	Puente Peatonal Colgante	CONCLUIDO	79.274
314	YC0618	Comunitario	Salud	La Asunta	La Asunta	Diseño final del Centro de Salud de La Asunta	DISEÑO	14.000
315	YE0641	Economico	Infraestructura vial	La Asunta	Puerto Aroma	Diseño y provisión de materiales para la construcción del puente colgante peatonal en la Comunidad Puerto Aroma.	EJECUCION	25.000
316	YE0639	Economico	Infraestructura vial	La Asunta	Siguani Grande	Conclusión del Puente Colgante Peatonal - Siguaní Chico	EJECUCION	25.000
317	YC0633	Comunitario	Infraestructura comunitaria	La Asunta	Cotapata	Diseño y construcción de la plaza central en la Comunidad de Cotapata	EJECUCION	27.500
318	YC0627	Comunitario	Saneamiento	La Asunta	Cotapata	Elaboración del Diseño final del sistema de alcantarillado sanitario para el centro poblado de Cotapata.	EJECUCION	10.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
319	YC0626	Comunitario	Educación	La Asunta	La Asunta	Construcción de 12 aulas para la UE René Barrientos Ortuño de La Asunta	EJECUCION	111.000
320	YE0624	Economico	Capacitación productiva	La Asunta	La Asunta	Asistencia técnica comercial a la iniciativas productivas del FCDI	EJECUCION	53.000
321	YC0605F	Comunitario	Saneamiento	La Asunta	Rene Barrientos Ortuno	Construcción batería de baños en la U. E. de Rene Barrientos Ortuno	EJECUCION	30.000
322	YC0605E	Comunitario	Saneamiento	La Asunta	Bolivar III	Construcción batería de baños en la U. E. de Bolivar III	EJECUCION	9.500
323	YC0605D	Comunitario	Saneamiento	La Asunta	Bolivar II	Construcción batería de baños en la U. E. de Bolivar II	EJECUCION	9.500
324	YC0605C	Comunitario	Saneamiento	La Asunta	Yanamayu	Construcción batería de baños en la U. E. de Yanamayu	EJECUCION	25.500
325	YC0605B	Comunitario	Saneamiento	La Asunta	Santa Rosa	Construcción batería de baños en la U. E. de Santa Rosa	EJECUCION	23.500
326	YC0605A	Comunitario	Saneamiento	La Asunta	La Calzada	Mejoramiento de baños en colegios y escuelas en La Asunta - La Calzada	EJECUCION	22.000
327	YE0573	Economico	Agrícola	La Asunta	La Asunta	Incremento de la base productiva del cultivo de Stevia en el municipio de La Asunta	EJECUCION	50.000
328	YE0571	Economico	Transformación	La Asunta	La Asunta	Consolidar la calidad del café a través del co-financiamiento de despulpadoras individuales	EJECUCION	56.000
329	YE0570	Economico	Transformación	La Asunta	La Asunta	Implementación/equipamiento de centros de acopio y procesamiento apícola	EJECUCION	45.000
330	YC0543	Comunitario	Salud	La Asunta	La Asunta	Equipamiento de mobiliario clínico y complementario del Centro de Salud de La Asunta	EJECUCION	80.000
331	YC0513	Comunitario	Agua Potable	La Asunta	Central Simon Bolivar	Diseño del sistema de agua potable para la Central Bolívar	EJECUCION	10.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
332	YE0495	Economico	Infraestructura vial	La Asunta	Santa Lucia	Puente del Desarrollo	EJECUCION	89.725
333	YE0491	Economico	Agricola	La Asunta	La Asunta	Plan Apicola	EJECUCION	40.000
334	YE0490	Economico	Pecuario	La Asunta	La Asunta	Plan Avicola	EJECUCION	15.000
335	YE0488	Economico	Agricola	La Asunta	La Asunta	Plan Estevia	EJECUCION	220.000
336	YE0487	Economico	Agricola	La Asunta	La Asunta	Plan Cafe	EJECUCION	105.000
337	YE0332C	Economico	Turismo	La Asunta	La Asunta	Promocion de Desarrollo Turistico en La Asunta "HOTEL BELLA VISTA"	EJECUCION	15.000
338	YE0284	Economico	Capacitacion productiva	La Asunta	La Asunta	Formacion tecnica de jovenes en La Asunta	EJECUCION	80.000
339	YC0008B	Comunitario	Saneamiento	Palos Blancos	Varios	Implementación de UHF's (259/97 UHF's)	CONCLUIDO	497.400
340	YR0135	Comunitario	Agua Potable	Palos Blancos	Inicua	Sistema de Agua Potable Pauca a Inicua	CONCLUIDO	357.644
341	YR0119	Comunitario	Agua Potable	Palos Blancos	Varios	Megaproyecto Agua Potable - Sapecho	CONCLUIDO	339.915
342	YR0153	Comunitario	Educación	Palos Blancos	Inicua	Construcción 20 viviendas	CONCLUIDO	189.953
343	YR0092	Comunitario	Agua Potable	Palos Blancos	Covendo	Sistema de Agua Potable (Megaproyecto)	CONCLUIDO	159.081
344	YR0076	Comunitario	Educación	Palos Blancos	San Miguel de Huachi	Complejo Educativo Fase II	CONCLUIDO	152.697
345	YR0089	Comunitario	Agua Potable	Palos Blancos	Colonia Simayuni, Los Andes, Tucupi	Sistema de Agua Potable	CONCLUIDO	151.338
346	YR0090	Comunitario	Agua Potable	Palos Blancos	Covendo, Villa Concepcion	Sistema de Agua Potable	CONCLUIDO	137.342
347	YR0106	Comunitario	Agua Potable	Palos Blancos	Bologna, Belen	Sistema de Agua Potable	CONCLUIDO	88.747
348	YR0052	Comunitario	Educación	Palos Blancos	Tucupi	Construcción 8 aulas UE 13 de mayo	CONCLUIDO	87.503

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
349	YE0603	Economico	Infraestructura vial	Palos Blancos	Comunidad Inicua Bajo	Construcción de alcantarillas en los caminos de las comunidades Liquimuni y Bajo Inicua	CONCLUIDO	22.500
350	YC0013	Comunitario	Educación	Palos Blancos	Varios	Mobiliario Escuelas Municipio P. Blancos	CONCLUIDO	70.307
351	YR0053	Comunitario	Salud	Palos Blancos	Tucupi	Const. 4 viviendas y amp. centro salud	CONCLUIDO	66.462
352	YR0136	Comunitario	Agua Potable	Palos Blancos	Varias	Diseno: Sistema de Agua Potable Hoyada Kollasuyo (17 Colonias)	CONCLUIDO	61.074
353	YR0069	Comunitario	Infraestructura comunitaria	Palos Blancos	Popoy	Sede Social Múltiple	CONCLUIDO	57.135
354	YR0088	Comunitario	Agua Potable	Palos Blancos	Colonia Simay	Mejoramiento Sistema de Agua Potable	CONCLUIDO	52.572
355	YR0120	Comunitario	Agua Potable	Palos Blancos	Varios	Sistema de Agua Potable	CONCLUIDO	50.225
356	YR0091	Comunitario	Agua Potable	Palos Blancos	Colonia Cogotay	Sistema de Agua Potable	CONCLUIDO	50.203
357	YE0423	Economico	Agricola	Palos Blancos	Brecha D	Provision de motodeshierbadoras	CONCLUIDO	3.670
358	YE0286	Economico	Medio ambiente	Palos Blancos	Varios	Parcelas agro forestales en Alto Beni	CONCLUIDO	35.000
359	YE0282	Economico	Transformacion	Palos Blancos	Brecha Mejillones H,Palos Blancos	Implementación de Colmenas - "LUCANA"	CONCLUIDO	7.704
360	YE0281	Economico	Transformacion	Palos Blancos	San Pedro,Sapecho	Implementación de Apiario - "SAN PEDRO"	CONCLUIDO	3.234
361	YE0278	Economico	Pecuario	Palos Blancos	Colonia Illimani	Mejoramiento del Hato Lechero - "ILLIMANI"	CONCLUIDO	14.687

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
362	YE0275	Economico	Transformacion	Palos Blancos	Sapecho	Carpinteria Industrial "Ramos"	CONCLUIDO	14.193
363	YE0274	Economico	Pecuario	Palos Blancos	Tarapaca	Agropecuaria "ICHUTA"	CONCLUIDO	15.883
364	YE0273	Economico	Transformacion	Palos Blancos	Sapecho	Deshidratado Frutas Tropicales	CONCLUIDO	8.164
365	YE0271	Economico	Pecuario	Palos Blancos	Brecha B	Granja de Producción de Huevos - "TORRICO"	CONCLUIDO	19.067
366	YE0268	Economico	Transformacion	Palos Blancos	Palos Blancos	Artesanías - "ARTMOS"	CONCLUIDO	7.403
367	YE0267	Economico	Transformacion	Palos Blancos	Palos Blancos	Procesamiento de Frutas - "MOCEFRU"	CONCLUIDO	18.541
368	YE0266	Economico	Turismo	Palos Blancos	Palos Blancos	Circuitos Turísticos guiados por Mocetenes	CONCLUIDO	14.382
369	YE0264	Economico	Pecuario	Palos Blancos	Colonia Charcas 1	Porcinocultura - "VILLEGAS"	CONCLUIDO	15.883
370	YE0262	Economico	Transformacion	Palos Blancos	Colonia Villazon	Implementación de Apiarios - "DORADO"	CONCLUIDO	3.234
371	YE0261	Economico	Transformacion	Palos Blancos	Colonia Colorado,Colonia Santa Ana	Implementación de Colmenas - San Martín de Agua Rica	CONCLUIDO	3.234
372	YE0259	Economico	Transformacion	Palos Blancos	Inicua	Carpinteria Industrial "Hinojosa"	CONCLUIDO	14.193
373	YE0258	Economico	Pecuario	Palos Blancos	Wiñay Marca	Mejoramiento del Hato Ganadero Lechero - "WIÑAY MARCA"	CONCLUIDO	14.687
374	YE0254	Economico	Pecuario	Palos Blancos	Brecha Mejillones H,Palos Blancos	Producción de Pollos Parrilleros - "GRANJA PATI"	CONCLUIDO	19.067
375	YE0253	Economico	Transformacion	Palos Blancos	Sapecho	Implementación de Colmenas - "ECOTOP"	CONCLUIDO	7.704
376	YE0252	Economico	Agricola	Palos Blancos	Sapecho	Semilla Híbrida de Cacao y Cítricos	CONCLUIDO	12.680
377	YE0248	Economico	Transformacion	Palos Blancos	Sapecho	Peladora de Arroz y Silos	CONCLUIDO	8.773

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
378	YE0247	Economico	Pecuario	Palos Blancos	Brecha B,Sapecho	Mejoramiento del Hato y Comercialización de Leche "DELGADILLO"	CONCLUIDO	14.687
379	YE0246	Economico	Turismo	Palos Blancos	Colonia Puerto Santa Ana	Circuito Etnoecoturismo en el río La Paz y Beni	CONCLUIDO	14.382
380	YE0245	Economico	Pecuario	Palos Blancos	El Sillar	Mejoramiento del Hato Ganadero Lechero "ILLAMPU"	CONCLUIDO	14.687
381	YE0244	Economico	Transformacion	Palos Blancos	Palos Blancos	Elaboración de Derivados de Estevia - "IPAN"	CONCLUIDO	4.018
382	YE0243	Economico	Transformacion	Palos Blancos	Popoy	Implementación de una Planta Procesadora de Embutidos	CONCLUIDO	15.827
383	YE0241	Economico	Pecuario	Palos Blancos	Brecha J.Popoy	Producción y Comercialización de Cerdos	CONCLUIDO	15.883
384	YE0239	Economico	Turismo	Palos Blancos	Palos Blancos	Complementación del Hotel Magdalena	CONCLUIDO	15.276
385	YE0236	Economico	Transformacion	Palos Blancos	Palos Blancos	Transformación y Comercialización de Productos Medicinales Naturales	CONCLUIDO	11.596
386	YE0233	Economico	Servicios	Palos Blancos	Sapecho	Acopio y Venta de Áridos	CONCLUIDO	4.224
387	YE0230	Economico	Transformacion	Palos Blancos	Palos Blancos	Modernización de la Planta Industrial de Derivados Lácteos "CACIQUE"	CONCLUIDO	46.801
388	YR0071	Comunitario	Infraestructura comunitaria	Palos Blancos	Santa Ana - urbano	Construcción Casa de Gobierno	CONCLUIDO	34.034
389	YC0542	Comunitario	Salud	Palos Blancos	Palos Blancos	Equipamiento complementario hospital básico de Palos Blancos	CONCLUIDO	30.000
390	YC0582	Comunitario	Educación	Palos Blancos	Inicua	Equipamiento al Proyecto OSCAR	CONCLUIDO	28.500
391	YC0166	Comunitario	Fortalecimiento comunitario	Palos Blancos	Palos Blancos	Apoyo a interinstitucional Alto Beni "IIAB"	CONCLUIDO	27.000
392	YE0161	Economico	Transformacion	Palos Blancos	Sapecho	Carpintería industrial	CONCLUIDO	12.751

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
393	YE0160	Economico	Transformacion	Palos Blancos	Brecha J	Implementación de colmenas ADAEPAB	CONCLUIDO	7.287
394	YE0159	Economico	Servicios	Palos Blancos	Sapecho	Tarjetas artesanales	CONCLUIDO	2.637
395	YE0156	Economico	Pecuario	Palos Blancos	Sapecho	Producción pollos parrilleros - Granja Adriana	CONCLUIDO	4.703
396	YE0155	Economico	Transformacion	Palos Blancos	Palos Blancos	Apoyo en Iniciativas de Negocio en la implementación de 4 Inict. de Neg. en transformación y comercialización, en la región de los Yungas	CONCLUIDO	26.569
397	YE0154	Economico	Transformacion	Palos Blancos	Varios	Apoyo implementación 3 pastelerías	CONCLUIDO	31.574
398	YR0070	Comunitario	Educación	Palos Blancos	Brecha H	Construcción viviendas y bat.baños UE Mejillones	CONCLUIDO	26.542
399	YR0079	Comunitario	Salud	Palos Blancos	Comunidad Cocochi	Equipamiento mini hospital	CONCLUIDO	25.400
400	YC0182	Comunitario	Fortalecimiento comunitario	Palos Blancos	Alto Beni	Fortalecimiento estra. comunicación Alto Beni	CONCLUIDO	25.000
401	YC0163	Comunitario	Fortalecimiento comunitario	Palos Blancos	Varios	Fort. institucional (PDM Alcaldía P. Blancos)	CONCLUIDO	21.580
402	YR0095	Economico	Infraestructura Productiva	Palos Blancos	Colonia Nueva California	Imp. beneficiadoras de cacao	CONCLUIDO	29.442
403	YC0181	Comunitario	Educación	Palos Blancos	Palos Blancos	Computadora Braile UE para no videntes	CONCLUIDO	16.538
404	YR0073	Comunitario	Educación	Palos Blancos	Santa Ana - urbano	Const. baterías de baños - UE Santa Ana	CONCLUIDO	12.532
405	YC0462	Comunitario	Capacitacion comunitaria	Palos Blancos	Palos Blancos	Capacitación Jovenes en Desarrollo Humano y Liderazgo - U.E Palos Blancos B- Alto Beni	CONCLUIDO	9.764
406	YC0461	Comunitario	Capacitacion comunitaria	Palos Blancos	Sapecho	Capacitación Jovenes en Desarrollo Humano y Liderazgo - U.E Sapecho B- Alto Beni	CONCLUIDO	9.764

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
407	YC0534	Comunitario	Agua Potable	Palos Blancos	Palos Blancos	Refacción sistema de agua potable Palos Blancos	CONCLUIDO	8.500
408	YR0072	Comunitario	Educación	Palos Blancos	Santa Ana de Mosetenes	Construcción viviendas de maestros	CONCLUIDO	8.467
409	YC0637	Comunitario	Agua Potable	Palos Blancos	Colonia Alto Remolino	Estudio a Diseño Final del Sistema de Agua Potable para la Comunidad de Alto Remolinos	CONCLUIDO	6.000
410	YC0288	Comunitario	Infraestructura comunitaria	Palos Blancos	Palos Blancos	Diseño: Enlosetado Av. Principal de Palos Blancos	CONCLUIDO	3.471
411	YC0533	Comunitario	Agua Potable	Palos Blancos	Colonia Los Olivos	Refacción Sistema de agua potable Los Olivos	CONCLUIDO	1.800
412	YC0186	Comunitario	Educación	Palos Blancos	Brecha H	Dotación Escuela Técnica Sup.	CONCLUIDO	1.765
413	YR0074	Comunitario	Educación	Palos Blancos	Delicias	Diseño: Aulas, viviendas y bat. baños UE	CONCLUIDO	1.000
414	YC0662	Comunitario	Agua Potable	Palos Blancos	Brecha I	Ajuste del diseño final y construcción del sistema de agua potable en la Comunidad de Brecha I (Luz, Porvenir y Calama)	DISEÑO	85.000
415	YC0661	Comunitario	Educación	Palos Blancos	Santa Ana de Mosetenes	Diseño final de construcción de una cubierta para la cancha polifuncional de la Unidad Educativa de Santa Ana de Mosetenes	DISEÑO	35.000
416	YC0523	Comunitario	Agua Potable	Palos Blancos	Colonia Batallas	"Construcción de obra de toma y aducción para el sistema de agua potable de la comunidad de Batallas"	DISEÑO	18.000
417	YC0607	Comunitario	Agua Potable	Palos Blancos	Comunidad Inicua Bajo	Diseño y construcción del sistema de agua potable de Muchani – Inicua Bajo	EJECUCION	120.000
418	YC0632	Comunitario	Educación	Palos Blancos	Comunidad La Cascada	Construcción de 16 viviendas para maestros distrito educativo La Cascada	EJECUCION	64.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
419	YE0263	Economico	Transformacion	Palos Blancos	Sapecho	Planta Procesadora de Jugos Naturales - "EL PARAISO"	EJECUCION	50.133
420	YE0239A	Economico	Turismo	Palos Blancos	Palos Blancos	Complementacion "HOTEL RICMAN"	EJECUCION	8.220
421	YE0232	Economico	Transformacion	Palos Blancos	Brecha Mejillones H,Palos Blancos	Producción de Jugo y Concentrados de Cítricos	EJECUCION	47.578
422	YC0519	Comunitario	Agua Potable	Palos Blancos	Colonia San Pedro	Construcción de la red de distribución de agua Potable y conexiones domiciliarias de la comunidad de San Pedro	EJECUCION	28.000
423	YC0653	Comunitario	Educación	Palos Blancos	Palos Blancos	Equipamiento de mobiliario para establecimientos educativos en las Áreas V y VI del Municipio de Palos Blancos	EJECUCION	25.000
424	YC0521	Comunitario	Agua Potable	Palos Blancos	Sapecho	Construcción de la red de distribución de agua Potable y conexiones domiciliarias de la población de Tupiza A	EJECUCION	21.000
425	YC0611	Comunitario	Salud	Palos Blancos	Palos Blancos	Campaña de prevención de leishmaniasis	EJECUCION	20.000
426	YC0654	Comunitario	Educación	Palos Blancos	Palos Blancos	Equipamiento de mobiliario para establecimientos educativos en el Área II del Municipio de Palos Blancos	EJECUCION	19.000
427	YC0621	Comunitario	Salud	Palos Blancos	Comunidad Los Olivos	Diseño y construcción de vivienda para médico y enfermera "Comunidad los Olivos"	EJECUCION	14.000
428	YC0631	Comunitario	Educación	Palos Blancos	Muchane	Conclusión de un aula y vivienda de maestro en la Unidad Educativa Muchane	EJECUCION	12.500
429	YC0629B	Comunitario	Salud	Palos Blancos	Sapecho	Campaña de capacitación y prevención de cáncer uterino en La Asunta y Palos Blancos	EJECUCION	5.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
430	TE0298	Economico	Agricola	Pojo	Izarsama,Manco Kapac	Apoyo a la Producción Apícola	CONCLUIDO	20.000
431	TE0453	Economico	Infraestructura vial	Puerto Villarroel	1° de Mayo	Apoyo a la cadena productiva de plátano y banano (Puente Argentino)	CONCLUIDO	20.200
432	TE0452	Economico	Infraestructura vial	Puerto Villarroel	1° de Mayo	Apoyo a la cadena productiva de plátano y banano (Puente 6)	CONCLUIDO	21.000
433	TE0445	Economico	Pecuario	Puerto Villarroel	Varios	Apoyo campaña de vacunacion contra Fiebre Aftosa - Puerto Villarroel	CONCLUIDO	29.000
434	TC0440	Comunitario	Fortalecimiento comunitario	Puerto Villarroel	Libertad	Dotación de mobiliario, equipamiento, menaje cocina y capacitación a educadoras	CONCLUIDO	15.900
435	TE0434	Economico	Otros	Puerto Villarroel	Comunidad Indigena Yuqui - Via Recuate	Generación de ingresos para familias afectadas por inundaciones y establecimiento de plantaciones forestales y prácticas de agroforesteria	CONCLUIDO	11.000
436	TC0432	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Puerto Villarroel	Construcción defensivos para inundaciones y drenaje en el Centro Poblado de Puerto Villarroel	CONCLUIDO	30.000
437	TC0431	Comunitario	Fortalecimiento comunitario	Puerto Villarroel	Varias	Dotación de víveres – Central Puerto Villarroel	CONCLUIDO	20.000
438	TC0430	Comunitario	Fortalecimiento comunitario	Puerto Villarroel	Capernaun,Comunidad Indigena Yuqui - Via Recuate,Puerto Las Flores,Santa Isabel,Tres Bocas	Dotación de menaje de cocina y víveres – Comunidades indígenas	CONCLUIDO	12.000
439	TE0316	Economico	Pecuario	Puerto Villarroel	Nueva Estrella	Actividades Complementarias de Potenciamiento a proyectos Piscícolas	CONCLUIDO	1.000
440	TE0224	Economico	Infraestructura vial	Puerto Villarroel	Santa Fe	Construcción del Puente sobre el río Chua Mayu (San Isidro)Santa Fe	CONCLUIDO	18.500

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
441	TC0220	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Jose Maria Linares	Diseno: Construcción Centro Multifuncional COMUNIDAD José María Linares	CONCLUIDO	8.000
442	TE0219	Economico	Infraestructura Productiva	Puerto Villarroel	Mariposas	Contrucción Mercado de Frutas en Centro Poblado de Mariposas	CONCLUIDO	14.000
443	TC0218	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Puerto Villarroel	Construcción oficinas y escenario en la Sede de la Central Puerto Villarroel	CONCLUIDO	5.850
444	TC0217	Comunitario	Educación	Puerto Villarroel	Senda 6	Construcción viviendas para maestros Unidad Educativa Hernán Siles de Senda 6	CONCLUIDO	14.000
445	TE0215	Economico	Infraestructura Productiva	Puerto Villarroel	Tamborada A-3	Intalación de 700 m de cable vía y una Compuerta "Tamborada A-3"	CONCLUIDO	6.533
446	TE0214	Economico	Infraestructura Productiva	Puerto Villarroel	Valle Ivirza	Dotación de máquinas de coser, mobiliario y curso de capacitación -Central de Mujeres Valle Ivirza	CONCLUIDO	2.851
447	TE0213	Economico	Infraestructura Productiva	Puerto Villarroel	Tamborada A-3	Construcción Empacadora de Banano y Piña en Tamborada A-3 (Tipo B)	CONCLUIDO	7.500
448	TC0209	Comunitario	Educación	Puerto Villarroel	Israel	Dotación de mobiliario escolar para 6 aulas "Unidad Educativa Israel"	CONCLUIDO	3.783
449	TC0208	Comunitario	Infraestructura comunitaria	Puerto Villarroel	1° de Mayo	Refacción y Ampliación Sede Central 1° de Mayo en Valle Tunari	CONCLUIDO	4.500
450	TE0206	Economico	Infraestructura Productiva	Puerto Villarroel	Puerto Villarroel	Dotación de máquinas industriales de coser y mobiliario- (FSMCT)	CONCLUIDO	10.000
451	TC0204	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Puerto Villarroel	Dotación de mobiliario y equipamiento - FSCCT	CONCLUIDO	10.009
452	TC0203	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Ivirza	Dotación de mobiliario - Central Valle Ivirza	CONCLUIDO	2.486
453	TC0202	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Ivirgarzama	Dotación de mobiliario y equipamiento - Central de Comunidades de Ivirgarzama	CONCLUIDO	4.475
454	TR0132	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Ivirgarzama	Construcción Guardería	CONCLUIDO	49.508

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
455	TR0129	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Puerto Villarroel	Complejo deportivo recreacional	CONCLUIDO	66.250
456	TR0128	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Puerto Villarroel	Mercado Municipal	CONCLUIDO	59.240
457	TR0127	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Puerto Villarroel	Calle peatonal	CONCLUIDO	12.500
458	TR0126	Comunitario	Educación	Puerto Villarroel	Senda 5 (# 1)	Mobiliario UE San Francisco de Asis	CONCLUIDO	3.004
459	TR0125	Comunitario	Educación	Puerto Villarroel	Poblado Valle Sacta (# 1)	Mobiliario Colegio Juan Pablo II	CONCLUIDO	8.260
460	TC0004	Comunitario	Infraestructura comunitaria	Puerto Villarroel	Poblado de Ivirgarzama	Diseño: Construcción Parque Infantil	CONCLUIDO	282
461	TE0001E	Comunitario	Educación	Puerto Villarroel	German Busch	Refacción Galpón Unidad Educativa "German Bush B"	CONCLUIDO	7.227
462	TE0444	Economico	Pecuario	Shinahota	Varios	Apoyo campaña de vacunacion contra Fiebre Aftosa - Shinahota	CONCLUIDO	3.000
463	TC0419	Comunitario	Educación	Shinahota	Villa Barrientos	Mobiliario Escolar, UE Mcal. Sucre	CONCLUIDO	3.360
464	TC0417	Comunitario	Educación	Shinahota	Shinahota	Mobiliario Escolar, UE G. Busch A	CONCLUIDO	3.290
465	TC0415	Comunitario	Educación	Shinahota	Lauca E±e	Mobiliario Escolar, Demetrio Canelas	CONCLUIDO	2.940
466	TE0414	Economico	Infraestructura vial	Shinahota	Villa Victoria	Apoyo a la cadena productiva de piña, banano y palmito (Puente Villa Victoria 8,5 m)	CONCLUIDO	17.500
467	TE0413	Economico	Infraestructura vial	Shinahota	Dorado Chico	Apoyo a la cadena productiva de banano (Puente Dorado Chico)	CONCLUIDO	18.500
468	TE0412	Economico	Infraestructura vial	Shinahota	Bolivar	Apoyo a las cadenas productivas de banano, palmito y cítricos Puente Bolívar	CONCLUIDO	9.000
469	TE0411	Economico	Infraestructura vial	Shinahota	Arenales	Apoyo a la producción de cultivos anuales (Puente Arenales 11 m)	CONCLUIDO	18.600
470	TE0321	Economico	Infraestructura vial	Shinahota	Dorado Chico	Mejoramiento de Camino Dorado Chico - Florida	CONCLUIDO	18.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
471	TE0317	Economico	Agricola	Shinahota	2? Valle Hermoso,Simon Bolivar,Tercero Valle Hermoso	Apoyo a la cadena productiva de piña	CONCLUIDO	25.000
472	TC0205	Comunitario	Infraestructura comunitaria	Shinahota	Shinahota	Dotación de mobiliario y equipamiento - Federación única de Centrales Unidas	CONCLUIDO	10.903
473	TR0177	Economico	Infraestructura Productiva	Shinahota	Shinahota	Diseño Carpintería Comunitaria	CONCLUIDO	7.900
474	TR0130	Comunitario	Infraestructura comunitaria	Shinahota	Poblado de Shinaota (# 1)	Diseño final "Terminal de buses" - Shinaota	CONCLUIDO	16.800
475	TE0018	Economico	Infraestructura vial	Shinahota	San Luis	Reposición Terraplén Puente Méndez	CONCLUIDO	4.071
476	TC0007	Comunitario	Infraestructura comunitaria	Shinahota	Varios	Construcción Defensivos de Oroyas	CONCLUIDO	12.743
477	TC0006	Comunitario	Educación	Shinahota	4 de Abril, Monte Rico, San Luis	"Mobiliario escolar, tres Unidades Educativas"	CONCLUIDO	4.922
478	TE0001D	Comunitario	Educación	Shinahota	Centro Urbano Shinaota	Galpón Metálico Nucleo Educativo "German Bush A"	CONCLUIDO	19.657
479	TE0421	Economico	Infraestructura vial	Tiraque	Florida Tropical, San Francisco, San Isidro, Santa Rosa, Villa Victoria	Apoyo a la cadena productiva de cítricos (Incremento de ventas y empleos)	CONCLUIDO	12.000
480	TE0001A	Comunitario	Educación	Tiraque	4 de Abril	Refacción Unidad Educativa "4 de Abril"	CONCLUIDO	3.634
481	TC0194	Comunitario	Capacitacion comunitaria	Varios TC	Varios	Apoyo a pequeñas iniciativas democráticas de la Sociedad Civil	CONCLUIDO	8.000
482	TC0179	Comunitario	Capacitacion comunitaria	Varios TC	Varios	Formación de líderes CAF/IDEA	CONCLUIDO	9.928
483	TE0149	Comunitario	Otros	Varios TC	Varios	Apoyo inundaciones Yapacani (Sta. Cruz)	CONCLUIDO	30.000
484	TC0499	Economico	Capacitacion productiva	Varios TC	Varios	Fortalecimiento de las capacidades institucionales y técnicas de UNAPAL	CONCLUIDO	80.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
485	TE0498	Economico	Capacitacion productiva	Varios TC	Varios	Fortalecimiento de las capacidades institucionales para la prevención de brotes de fiebre aftosa en el Trópico de Cochabamba.	CONCLUIDO	75.000
486	TE0439	Economico	Capacitacion productiva	Varios TC	Varios	Cursos de capacitación en costura industrial para las federaciones TC	CONCLUIDO	19.600
487	TE0201	Economico	Agricola	Varios TC	Varios	Generación de Empleos y Ventas en la Cadena de Palmito el el Trópico de Cochabamba - Coordinadora de las 6 federaciones del Trópico de Cbba.	CONCLUIDO	422.651
488	TE0176	Economico	Pecuario	Varios TC	Chimor?,Entre Rios (Ene Alto),Puerto Villarroel,Shinahota,Villa Tunari	Campaña vacunación contra la fiebre aftosa 13vo y 14vo Ciclo	CONCLUIDO	122.000
489	TE0150	Economico	Infraestructura vial	Varios TC	Shinahota,Villa Tunari	Construcción de atracaderos para pontones	CONCLUIDO	38.271
490	TE0422	Economico	Agricola	Varios TC	2 de Marzo,Bustillo,Unificado,Urbanizacion Valle Ivirza,Valle Hermoso,Villa Verde	Generación de empleos y venta en la cadena productiva de Palmito UNAGRUP II	CONCLUIDO	50.000
491	YC0610	Comunitario	Medio ambiente	Varios YUN	Varios	Campaña de limpieza y concientización en el manejo de residuos sólidos en Yungas	ADJUDICACION	80.000
492	YE0636	Economico	Capacitacion productiva	Varios YUN	Varios	Curso en gestión microempresarial para el sector de costura	CONCLUIDO	11.500
493	YC0656	Comunitario	Varios	Varios YUN	Varios	Apoyo al campeonato Interyungueño de Fútbol 2010	CONCLUIDO	6.872
494	YC0625	Comunitario	Educación	Varios YUN	Varios	Fortalecimiento institucional y equipamiento de los Centros Técnicos Humanísticos Agropecuarios (CETHAs)	CONCLUIDO	58.000
495	YE0596	Economico	Otros	Varios YUN	Varios	Modernización de la red meteorológica de los Yungas	CONCLUIDO	70.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
496	YE0595	Economico	Capacitacion productiva	Varios YUN	Varios	Jóvenes emprendedores yungueños en la "Semana Mundial del Emprededurismo	CONCLUIDO	16.500
497	YC0597	Comunitario	Fortalecimiento comunitario	Varios YUN	Varios	Fortalecimiento y equipamiento técnico de la MMYLP	CONCLUIDO	28.500
498	YE0577	Economico	Capacitacion productiva	Varios YUN	Varios	Capacitación y equipamiento en corte y confección	CONCLUIDO	24.000
499	YE0576	Economico	Agricola	Varios YUN	Varios	Consolidación de Proveedores en la Cadena de Amaranto Orgánico de Alta Calidad en los Yungas de La Paz	CONCLUIDO	80.000
500	YE0569	Economico	Infraestructura vial	Varios YUN	Varios	Construcción de alcantarillas tramo Chorrillo - San Lorenzo	CONCLUIDO	18.000
501	YE0567	Economico	Infraestructura vial	Varios YUN	Varios	Construcción de alcantarillas tramo Chamaca - Tunquini - Alto Charobamba	CONCLUIDO	22.500
502	YE0566	Economico	Infraestructura vial	Varios YUN	Varios	Construcción de alcantarillas tramo Cotapata - San Felipe - 10 de febrero	CONCLUIDO	22.500
503	YE0560	Economico	Infraestructura vial	Varios YUN	Varios	Construcción de alcantarillas tramo Puerto Rico - San Fernando - Cuarta Bolívar	CONCLUIDO	20.340
504	YC0581	Comunitario	Educación	Varios YUN	Varios	Equipamiento con material didáctico y deportivos a unidades educativas de Yungas.	CONCLUIDO	23.500
505	YC0580	Comunitario	Capacitacion comunitaria	Varios YUN	Varios	Concurso de Dibujos & Cuentos, Tema "Medio Ambiente" con enfoque en "Agua"	CONCLUIDO	8.500
506	YC0557	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 3 establecimientos educativos - Chulumani	CONCLUIDO	10.000
507	YC0556	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 6 establecimientos educativos - Yanacachi	CONCLUIDO	6.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
508	YC0555	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 4 establecimientos educativos. Irupana	CONCLUIDO	15.000
509	YC0554	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 7 establecimientos educativos. Coripata	CONCLUIDO	25.000
510	YC0553	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 14 establecimientos educativos. Fed. Chamaca	CONCLUIDO	46.000
511	YC0552	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 14 establecimientos educativos. Fed. La Asunta	CONCLUIDO	38.000
512	YC0551	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 14 establecimientos educativos – Palos Blancos	CONCLUIDO	30.000
513	YC0550	Comunitario	Educación	Varios YUN	Varios	Equipamiento mobiliario para 10 establecimientos educativos - Coroico	CONCLUIDO	32.000
514	YC0547	Comunitario	Salud	Varios YUN	Varios	Equipamiento de mobiliario clínico y administrativo para cuatro establecimientos de salud de Irupana	CONCLUIDO	20.000
515	YC0545	Comunitario	Salud	Varios YUN	Varios	Equipamiento de mobiliario clínico y equipos básicos para establecimientos de salud de La Asunta (Fed. La Asunta)	CONCLUIDO	30.000
516	YE0518	Economico	Capacitacion productiva	Varios YUN	Varios	Capacitación: Gestión empresarial con enfoque de genero	CONCLUIDO	12.000
517	YC0544	Comunitario	Salud	Varios YUN	Varios	Equipamiento de mobiliario clínico y equipos básicos para establecimientos de salud de La Asunta (Fed. Chamacas)	CONCLUIDO	20.000
518	YC0501	Comunitario	Capacitacion comunitaria	Varios YUN	Varios	Fortalecimiento de las capacidades de liderazgo y gerencia de funcionarios públicos	CONCLUIDO	15.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
519	YC0496	Comunitario	Salud	Varios YUN	Caranavi,Palos Blancos	Plan de emergencia / Equipamiento para el control dengue.	CONCLUIDO	17.000
520	YE0197	Economico	Pecuario	Varios YUN	Varios	Censo Avícola en los Yungas	CONCLUIDO	16.000
521	YE0195	Economico	Capacitacion productiva	Varios YUN	Varios	Intercambio de lideres productivos	CONCLUIDO	55.700
522	YC0287	Comunitario	Fortalecimiento comunitario	Varios YUN	Varios	Procesos de priorizacion de proyectos en de la IL-43	CONCLUIDO	5.000
523	YC0200	Comunitario	Saneamiento	Varios YUN	Palos Blancos,San Antonio,Sapecho	Monitoreo alcantarillado Alto Beni	CONCLUIDO	1.000
524	YE0185	Economico	Capacitacion productiva	Varios YUN	Varios	Intercambio Academico Zamorano - UAC/CP	CONCLUIDO	54.400
525	YE0183	Economico	Otros	Varios YUN	Varios	Elaboración de 109 planes de negocio en Alto Beni	CONCLUIDO	95.000
526	YC0190	Comunitario	Fortalecimiento comunitario	Varios YUN	Varios	Apoyo actividades deportivas Yungas	CONCLUIDO	8.000
527	YC0173	Comunitario	Agua Potable	Varios YUN	Arapata,Coripata,San Antonio,Sapecho	Sostenibilidad sistemas de agua y alcantarillado	CONCLUIDO	49.983
528	YC0167	Comunitario	Otros	Varios YUN	Varios	Plan de visibilidad	CONCLUIDO	40.000
529	YC0164	Comunitario	Capacitacion comunitaria	Varios YUN	Chamaca,Chulumani,Comunidad Cajones,Irupana,La Asunta,Villa Barrientos	Formación de lideres CAF/IDEA	CONCLUIDO	39.564
530	YE0133	Comunitario	Otros	Varios YUN	Varios	Equipo móvil para emergencias	CONCLUIDO	14.022
531	YC0107	Comunitario	Medio ambiente	Varios YUN	Varios	Gestión Microcuencas del Cerro Uchumachi y pueblos de Coripata y Arapata	CONCLUIDO	14.000
532	YC0105	Comunitario	Saneamiento	Varios YUN	Varios	Fortalecimiento CAPYS de sistemas SERVIR	CONCLUIDO	36.492
533	YC0102	Comunitario	Medio ambiente	Varios YUN	Varios	Protección y conservación de microcuencas FCDI	CONCLUIDO	58.000

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
534	YR0096	Economico	Infraestructura Productiva	Varios YUN	Varios	Imp. beneficiadoras de cacao	CONCLUIDO	24.723
535	YC0035	Comunitario	Otros	Varios YUN	Varios	Estrategia autosostenibilidad de la Mancomunidad de Los Yungas	CONCLUIDO	22.500
536	YC0019	Comunitario	Agua Potable	Varios YUN	Varios	Evaluación Técnica SAP SERVIR	CONCLUIDO	12.000
537	YC0017	Comunitario	Educación	Varios YUN	Varios	Mobiliario Escuelas Municipio Coripata	CONCLUIDO	25.428
538	YE0012A	Comunitario	Otros	Varios YUN	Varios	Apoyo a Actividades de Rescate (Municipio)	CONCLUIDO	557
539	YC0008B2	Comunitario	Saneamiento	Varios YUN	Zona Tradicional	Implementación de UHFs	CONCLUIDO	78.000
540	YC0522	Comunitario	Agua Potable	Varios YUN	Varios	Diseño Final y construcción del la red de distribución de agua potable y conexiones domiciliarias de la Población de Tupiza B.	DISEÑO	19.000
541	YE0657	Economico	Pecuario	Varios YUN	Varios	Apoyo al sector avícola de los Yungas de La Paz	EJECUCION	45.000
542	YC0660	Comunitario	Varios	Varios YUN	Varios	Diagnostico regional de las nuevas áreas de intervención	EJECUCION	33.000
543	YC0659	Comunitario	Fortalecimiento comunitario	Varios YUN	Varios	Fortalecimiento institucional del Viceministerio de Coca y Desarrollo Integral -VCDI	EJECUCION	50.400
544	YC0655	Comunitario	Varios	Varios YUN	Varios	Fondo de para la elaboración de diseños de proyectos	EJECUCION	50.000
545	YC0640	Comunitario	Saneamiento	Varios YUN	Varios	Diagnóstico integral de saneamiento básico en el Municipio de La Asunta	EJECUCION	8.800
546	YE0612	Economico	Agricola	Varios YUN	Varios	Fortalecimiento de las capacidades de control sanitario de SENASAG – Yungas	EJECUCION	20.000
547	YC0622	Comunitario	Varios	Varios YUN	Varios	Transferencia de capacidades a CCVV	EJECUCION	29.500

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
548	YC0613	Comunitario	Otros	Varios YUN	Varios	Fortalecimiento del VCDI para la generación de propuestas de proyectos de desarrollo integral	EJECUCION	25.000
549	YC0609	Comunitario	Infraestructura comunitaria	Varios YUN	Varios	Parques recreativos para niños en los Yungas	EJECUCION	63.000
550	YC0608	Comunitario	Educación	Varios YUN	Varios	Equipamiento de bibliotecas de centros de educación técnica y superior.	EJECUCION	25.000
551	YE0575	Economico	Agricola	Varios YUN	Varios	Creación de una base productiva hortícola en Yungas de La Paz	EJECUCION	15.000
552	YE0574	Economico	Capacitacion productiva	Varios YUN	Varios	Estudios de mercado y capacitación en costos, mercadeo y marketing	EJECUCION	20.000
553	YE0572	Economico	Transformacion	Varios YUN	Varios	Equipamiento y complementación de tres plantas procesadoras de cítricos	EJECUCION	40.000
554	YC0578	Comunitario	Salud	Varios YUN	Varios	Campana de salud dental en niños y jóvenes.	EJECUCION	15.800
555	YE0517	Economico	Medio ambiente	Varios YUN	Varios	Estrategia Forestal para la Zona Tradicional	EJECUCION	45.000
556	YC0520	Comunitario	Agua Potable	Varios YUN	Varios	Construcción de la red de distribución de agua potable y conexiones domiciliarias de la comunidad de Villa El Carmen	EJECUCION	24.000
557	YC0504	Comunitario	Capacitacion comunitaria	Varios YUN	Varios	Capacitación y enseñanza a jóvenes yungueños en el idioma ingles	EJECUCION	10.000
558	YE0228	Economico	Turismo	Varios YUN	Varios	Senalizacion caminera/turistica de Yungas	EJECUCION	65.300
559	YC0357	Comunitario	Otros	Varios YUN	Varios	Plan de visibilidad de las actividades del FCDI y del Programa de Desarrollo Alternativo Integral	EJECUCION	50.000
560	YE0184	Economico	Capacitacion productiva	Varios YUN	Varios	Jóvenes emprendedores	EJECUCION	55.700

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
561	YC0193	Comunitario	Capacitacion comunitaria	Varios YUN	Varios	Apoyo a pequeñas Iniciativas Democráticas de la Sociedad Civil en Yungas	EJECUCION	9.000
562	YC0165	Comunitario	Capacitacion comunitaria	Varios YUN	Varios	Capacitación funcionarios públicos de los Yungas	EJECUCION	27.000
563	YC0138	Economico	Capacitacion productiva	Varios	Varios	Jóvenes Líderes Becarios a Zamorano	EJECUCION	154.833
564	TC0500	Comunitario	Salud	Villa Tunari		Plan de emergencia - Equipamiento para el control de dengue del Trópico de Cochabamba	CONCLUIDO	13.000
565	TE0442	Economico	Pecuario	Villa Tunari	Varios	Apoyo campaña de vacunacion contra Fiebre Aftosa - Villa Tunari	CONCLUIDO	26.000
566	TE0438	Economico	Turismo	Villa Tunari	Villa Tunari	Mejoramiento de los atractivos, actividades y servicios turísticos existentes	CONCLUIDO	1.000
567	TE0436	Economico	Turismo	Villa Tunari	Villa Tunari	Construcción señalización urbana Villa Tunari	CONCLUIDO	3.600
568	TE0435	Economico	Turismo	Villa Tunari	Villa Tunari	Fortalecimiento de la Unidad de Turismo de la Alcaldía de Villa Tunari	CONCLUIDO	2.780
569	TE0322	Economico	Infraestructura vial	Villa Tunari	Santibanez A	Mantenimiento del camino 5 Esquinas - Santibáñez	CONCLUIDO	11.100
570	TE0291	Economico	Infraestructura vial	Villa Tunari	5 Esquinas	Contrucción del Puente Vehicular sobre el rio el Conde Arroyo 2 en 5 Esquinas	CONCLUIDO	17.400
571	TC0223	Comunitario	Educación	Villa Tunari	Simon Bolivar	Construcción Cancha Múltiple U.E. Simón Bolivar	CONCLUIDO	6.400
572	TC0187	Comunitario	Fortalecimiento comunitario	Villa Tunari	Villa Tunari	Fortalecimiento al Desarrollo Turístico de Villa Tunari	CONCLUIDO	24.444
573	TE0151	Economico	Infraestructura vial	Villa Tunari	Carretera Cbba - Sta Cruz	Restitución paso vehicular Km. 121	CONCLUIDO	60.447
574	TC0047	Comunitario	Educación	Villa Tunari	Eterazama	Diseño: Escuela Mixta Eterazama	CONCLUIDO	300
575	TC0046	Comunitario	Educación	Villa Tunari	Uriuta	Diseño: Unidad Educativa Uriuta	CONCLUIDO	303

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
576	TC0002	Comunitario	Educación	Villa Tunari	Varios	"Mobiliario escolar para Unidades Educativas: primaria y secundaria"	CONCLUIDO	18.683
577	TE0001C	Comunitario	Educación	Villa Tunari	San Isidro	Refacción Núcleo Educativo "San Isidro"	CONCLUIDO	3.667
578	TE0001B	Comunitario	Educación	Villa Tunari		Refacción Núcleo Educativo "Ibuelo"	CONCLUIDO	7.150
579	YC0646	Comunitario	Educación	Yanacachi	Yanacachi	Equipamiento de mobiliario para establecimientos educativos en el Municipio de Yanacachi	CONCLUIDO	6.000
580	YC0548	Comunitario	Salud	Yanacachi	Yanacachi	Equipamiento de mobiliario clínico y equipo básico para el puesto de salud de Chakala	CONCLUIDO	5.000
581	YC0503	Comunitario	Infraestructura comunitaria	Yanacachi	Chajro	Diseño: Muros Defensivos en el Río Chajro	CONCLUIDO	25.000
582	YC0470	Comunitario	Capacitacion comunitaria	Yanacachi	La Chojlla	Capacitación Jóvenes en D. Humano y Liderazgo - U.E Jorge Zalles- Chojlla	CONCLUIDO	9.764
583	YC0469	Comunitario	Capacitacion comunitaria	Yanacachi	Yanacachi	Capacitación Jóvenes en D. Humano y Liderazgo - U.E Félix Ernesto Moscoso - Yanacachi	CONCLUIDO	9.764
584	YE0408	Economico	Pecuario	Yanacachi	La Chojlla	Granja Porcina "APPLC"	CONCLUIDO	35.651
585	YE0407	Economico	Pecuario	Yanacachi	Chajro	Granja Avícola "CACERES"	CONCLUIDO	7.598
586	YE0406	Economico	Pecuario	Yanacachi	Ticuniri	Granja Avícola "MACHACA"	CONCLUIDO	13.970
587	YE0405	Economico	Pecuario	Yanacachi	Sirupaya	Granja Porcina "PORFIRIA"	CONCLUIDO	17.351
588	YE0404	Economico	Pecuario	Yanacachi	Sirupaya	Granja Avícola "APAZA"	CONCLUIDO	16.535
589	YE0403	Economico	Pecuario	Yanacachi	Comunidad Chaco	Granja Porcina "Calixto"	CONCLUIDO	1.572
590	YE0402	Economico	Pecuario	Yanacachi	Comunidad Sacahuaya	Granja Avícola "ROJAS"	CONCLUIDO	10.459
591	YE0401	Economico	Pecuario	Yanacachi	Comunidad Chaco	Granja Porcina "Aquice"	CONCLUIDO	1.572

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
592	YE0400	Economico	Pecuario	Yanacachi	Comunidad La Florida	Granja Porcina "FLORIDA"	CONCLUIDO	17.351
593	YE0399	Economico	Pecuario	Yanacachi	Comunidad Chaco	Granja Porcina "Chaco"	CONCLUIDO	1.572
594	YE0398	Economico	Pecuario	Yanacachi	Villa (villorrio) Aspiazu	Granja Avícola "YUNGAS"	CONCLUIDO	7.598
595	YE0397	Economico	Pecuario	Yanacachi	Florida	Granja Avícola "Ochoa"	CONCLUIDO	14.100
596	YE0396	Economico	Pecuario	Yanacachi	La Chojlla	Granja Avícola "APPP"	CONCLUIDO	17.351
597	YE0395	Economico	Pecuario	Yanacachi	Comunidad Chaco	Granja Avícola "Patty"	CONCLUIDO	1.572
598	YE0394	Economico	Pecuario	Yanacachi	Comunidad Pichu	Granja Avícola "Loza"	CONCLUIDO	1.572
599	YE0393	Economico	Pecuario	Yanacachi	Yanacachi	Granja Avícola "Cirilo"	CONCLUIDO	1.572
600	YE0392	Economico	Pecuario	Yanacachi	Ticuniri	Granja Avícola "Poma"	CONCLUIDO	14.558
601	YE0391	Economico	Pecuario	Yanacachi	Ticuniri	Granja Avícola Tapia - Parrilleros	CONCLUIDO	1.572
602	YE0390	Economico	Pecuario	Yanacachi	Machacamarca	Granja Avícola "ISIDORO"	CONCLUIDO	16.051
603	YE0389	Economico	Pecuario	Yanacachi	Ticuniri	Granja Avícola "Azucena"	CONCLUIDO	12.670
604	YE0388	Economico	Pecuario	Yanacachi	Ticuniri	Granja Avícola "Marilena"	CONCLUIDO	4.800
605	YE0387	Economico	Pecuario	Yanacachi	Florida	Granja Avícola "Chalco"	CONCLUIDO	13.320
606	YE0385	Economico	Pecuario	Yanacachi	Machacamarca	Granja Avícola "Yupanqui"	CONCLUIDO	1.572
607	YE0384	Economico	Pecuario	Yanacachi	Villa (villorrio) Aspiazu	Granja Avícola "Daniel"	CONCLUIDO	12.670
608	YE0383	Economico	Pecuario	Yanacachi	Chacala	Granja Avícola "COSTAS"	CONCLUIDO	12.930
609	YE0382	Economico	Pecuario	Yanacachi	Florida	Granja Avícola Daza- Parrilleros	CONCLUIDO	7.598

#	Código	Componente	Sub Componente	Municipio	Colonia/Comunidad	Proyecto	Estado	Monto Total
610	YE0381	Economico	Pecuario	Yanacachi	Yanacachi	Apoyo a la Asociacion de Productores de Pollos y Cerdos de Yanacachi	CONCLUIDO	14.610
611	YE0380	Economico	Pecuario	Yanacachi	Comunidad Chaguara	Granja Avícola "Adrian"	CONCLUIDO	7.598
612	YC0060	Comunitario	Educación	Yanacachi	Santa Rosa	Construcción Escuela Multigrado Santa Rosa	CONCLUIDO	18.897
613	YC0051	Comunitario	Agua Potable	Yanacachi	Santa Rosa de Lima	Ampliación Agua Potable	CONCLUIDO	32.130
614	YC0050	Comunitario	Agua Potable	Yanacachi	Chacala	Mejoramiento Sistema Agua Potable	CONCLUIDO	11.031
615	YC0049	Comunitario	Agua Potable	Yanacachi	Iquicolo	Instalación Red Matriz Agua Potable	CONCLUIDO	9.491
616	YC0033	Comunitario	Saneamiento	Yanacachi	Villa Aspiazu	Sistema de Alcantarillado Sanitario	CONCLUIDO	74.585
617	YC0032	Comunitario	Saneamiento	Yanacachi	Yanacachi	Sistema de Alcantarillado Sanitario	CONCLUIDO	86.659
618	YC0031	Comunitario	Saneamiento	Yanacachi	Mina Chojlla	Sistema de Alcantarillado Sanitario	CONCLUIDO	147.167
619	YC0027	Comunitario	Educación	Yanacachi	Suquimilamilani	Construcción de Aulas y Viviendas p/maestro	CONCLUIDO	20.999
620	YC0026	Comunitario	Educación	Yanacachi	Machacamarca	Construcción Viviendas p/ Profesores N Escolar	CONCLUIDO	16.960
621	YC0025	Comunitario	Educación	Yanacachi	Motoncoro	Construcción Aulas Multigrado Motoncoro	CONCLUIDO	7.041
622	YC0020	Economico	Servicios	Yanacachi	Yanacachi	Telecentro para Municipio	CONCLUIDO	98.825
623	YC0014	Comunitario	Educación	Yanacachi	Varios	Mobiliario Escuelas Municipio Yanacachi	CONCLUIDO	8.835
624	YC0009	Comunitario	Salud	Yanacachi	Yanacachi	Vivienda Centro de Salud Kollana Uta	CONCLUIDO	14.905
625	YE0379	Economico	Agricola	Yanacachi	Estancia Chacala	Generación de Empleos y Ventas en la Cadena de Flores del Municipio de Yanacachi	EJECUCION	145.000
