



USAID |
FROM THE AMERICAN PEOPLE

AFGHANISTAN

IDEA-NEW
New ideas for agriculture

Biweekly Report: November 16-30, 2010

Incentives Driving Economic Alternatives—North, East and West (IDEA-NEW)

Eggs from the women's poultry project, Argo, Badakshan



Table of Contents

Acronyms	5
Map of IDEA-NEW Activities	6
Background	7
Major Accomplishments to Date	8
Job Creation:	8
Agriculture Productivity and Agribusiness:	8
Rural Job Creation	8
USG and GIROA Coordination:	9
Afghan First	9
Biweekly Highlights	10
Community-Constructed Infrastructure (CCI):	10
Agriculture Productivity and Agribusiness	11
Rural Job Creation	11
Building Capacity	12
USG & GIROA Coordination	12
Key Problems/Constraints	13
Afghan First	13
Biweekly Update: Eastern Region	14
Job Creation	14
Community-Constructed Infrastructure (CCI):	14
Voices from the Field	15
Ongoing CCI Photos, East: November 1-15, 2010	17
Agricultural Productivity Job Creation	18
Rural Job Creation:	20
Agricultural Sales/ Trade Corridor Market Development	23
Building Capacity	23
USG & GIROA Coordination	24
Key Problems/Constraints	25
Afghan First	25
Biweekly Update: Western Region	26
Job Creation	26

Ongoing CCI Photos, Western Region: November 16-30, 2010.....	27
Building Capacity of Community Institutions	28
Biweekly Update: Northern Region	29
Job Creation.....	29
Community-Constructed Infrastructure (CCI):.....	29
Agriculture and Rural Infrastructure:.....	29
Flood Protection and Irrigation	29
Power	30
Farm to Market Infrastructure.....	31
Voices from the Field.....	31
Agriculture Productivity and Agribusiness	32
Sustainable Agricultural Production	32
Livestock.....	33
Rural Enterprise Development.....	34
Women Income Generation	35
Contracts and Grants	35
Afghan First	36
USG & GIRA Coordination	36
Constraints and Problems:	36
 Biweekly Update: Northeast Region	 37
Job Creation.....	37
Community-Constructed Infrastructure (CCI):.....	37
Agriculture Productivity Job Creation	40
USG & GIRA Coordination	42
Afghan First	42
Constraints	42
Biweekly Monitoring & Evaluation Data	44
Performance Indicators.....	44
Impact Evaluation	44
Field Missions.....	44


ANNEX I: Performance Indicator Table	46
ANNEX II: CCI Project Data by Region.....	46
ANNEX III: Farmer Training Summary.....	47
ANNEX IV: Biweekly Sales Data	49
Annex V: Non-CCI Project List.....	50
Annex VI: IDEA-NEW Biweekly Grants Update	50
Annex VII: Cooperative Agreement Information.....	51
Project Contact Information	51

|

Acronyms

AAP	Annual Activity Plan	IPM	Integrated Pest Management
ADP	Alternative Development Program	ISAF	International Security Assistance Force
AGE	Anti-Government Elements	IVR	Interactive Voice Response
ACCI	Afghanistan Chamber of Commerce and Industries	JDA	Joint Development Associates
AISA	Afghanistan Investment Support Agency	LOP	Life of Project
ANDS	Afghanistan National Development Strategy	MAIL	Ministry of Agriculture, Irrigation and Livestock
ASAP	Accelerating Sustainable Agriculture Program	m	Meter
ASMED	Afghanistan Small and Medium Enterprise Development	M&E	Monitoring and Evaluation
CCI	Community Constructed Infrastructure	MCN	Ministry of Counter Narcotics
CDC	Community Development Council	MHP	Micro-Hydro Power
CDF	Commercial Demonstration Farm	MRRD	Ministry of Rural Rehabilitation and Development
CNAT	Counter Narcotics Advisory Team	MPW	Ministry of Public Works
CNTF	Counter Narcotics Trust Fund	MoWA	Ministry of Women’s Affairs
COIN	Counter Insurgency	NRM	Natural Resource Management
DAI	Development Alternatives, Inc.	NSP	National Solidarity Program
DCA	Dutch Committee for Afghanistan	NTA	Nangarhar Talc Association
DDA	District Development Authority	NVDA	Nangarhar Valley Development Authority
DoPW	Department of Public Works	PDC	Provincial Development Council
DOWA	Department of Women’s Affairs	PRT	Provincial Reconstruction Team
EMS	Environmental Management System	RCC	Reinforced Cement Concrete
FTE	Full-time Equivalent	RMHC	Rabia Mariam Handicraft Co.
GDA	Global Development Alliance	SDF	Small Demonstration Farm
GIRoA	Government of Islamic Republic of Afghanistan	TCN	Third-Country National
ha	Hectare	TIMER	Technology Innovations for Market-Led Economic Rehabilitation
ICARDA	International Center for Agricultural Research in the Dry Areas	USAID	United States Agency for International Development
IDEA-NEW	Incentives Driving Economic Alternatives—North, East and West	USDA	United States Department of Agriculture
IP	Implementing Partner	USG	United States’ Government

Map of IDEA-NEW Activities

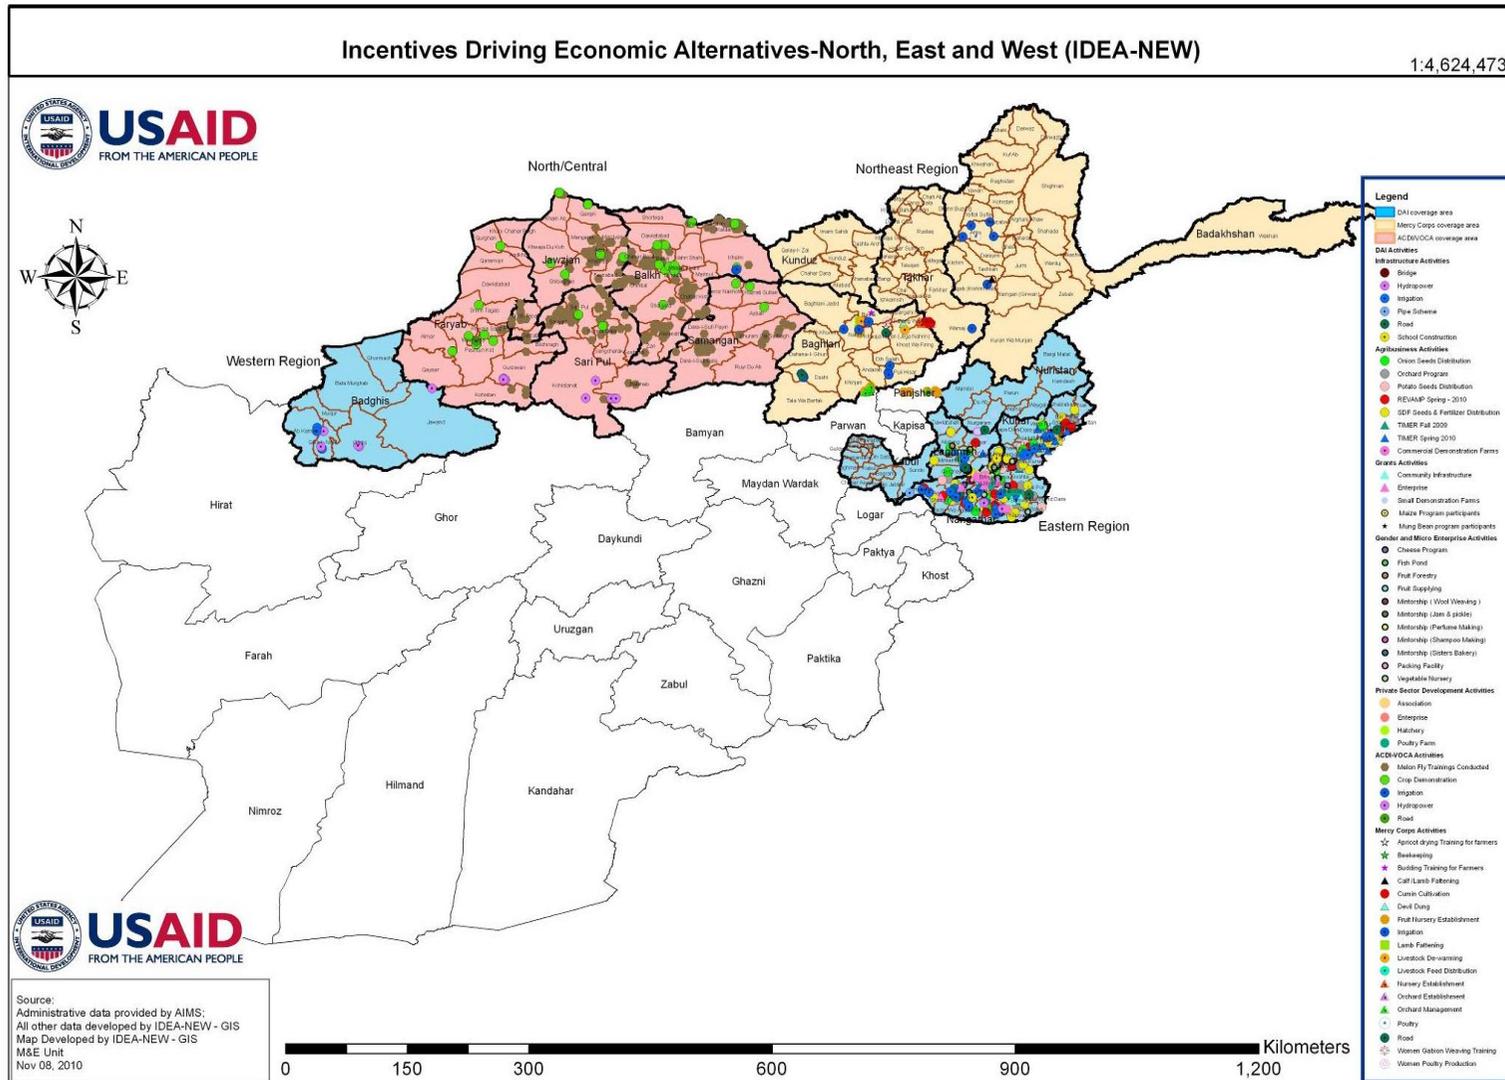

Background

IDEA-NEW, a USAID-funded initiative in Afghanistan, began in March 2009. Activities target instability/insurgency locales and buffer zones to curb narco-trafficking, and at the same time, increase job creation, strengthen Afghan leadership and promote economic growth.

The program responds rapidly to community-identified needs through Community Constructed Infrastructure (CCI) projects that foster trust and infuse communities with cash and income. IDEA-NEW then builds upon those gains in order to maintain the long term focus of sustainable growth in the agriculture and rural development sectors. The program is predominately centered in the Eastern Region, but also addresses interrelated issues of instability and economic development in select areas of the country's Northern, Northeastern and Western Regions.

Major emphasis is on: *Job Creation, Agricultural Sales and Capacity Building*. IDEA-NEW provides support and linkages to overall US government counter-insurgency (COIN) priorities through local-level agricultural and private sector development, and by engaging local government to respond to the needs of its constituencies in these sectors.

Partners

Three partners implement IDEA-NEW: Development Alternatives, Inc. (DAI), ACDI/VOCA and Mercy Corps. DAI works in the East and West, ACDI/VOCA in the North and Mercy Corps in the Northeast.

Regions

East Region activities are implemented in the Provinces of Nangarhar, Kunar, Laghman and Nuristan. The program works closely with provincial- and district-level governments and within local communities, capitalizing on the successes of previous USAID projects in the area, which built strong relations among local stakeholders, and have given IDEA-NEW the ability to scale-up rapidly. In its second year of operations in the east, IDEA-NEW is undertaking work in 39 of the region's 50 districts.

West Region activities are implemented in the Province of Badgis. **North region activities** are implemented in the Province of Faryab, Sari Pul, Jawzjan, Balkh, Samangan. **Northwestern region activities** are implemented in the Provinces of Badakshan, Takhar, Kunduz and Baghlan.



Major Accomplishments to Date

Job Creation:

Since July 2009, IDEA-NEW has created a total of 27,700 Full-Time Equivalent (FTE) jobs, in the sectors of agriculture, community-constructed infrastructure (CCI) and rural business development.

- IDEA-NEW has paid USD 3.8 million in wages to over 25,935 people on CCI projects to date.
- IDEA-NEW has completed 65 CCI projects in its areas of operation including roads, irrigation and micro-hydro power, and as of November 2010, was actively working on 53 more.

Agriculture Productivity and Agribusiness:

- Established more than 250 commercial and small-sized resource farms used as training grounds, where farmers are trained in collaboration with MAIL on modern crop techniques like raised beds and staggered planting. Some 227,705 people have been trained on these farms and through other agriculture- and livestock training programs.
- 5,881 hectares of cropland have been planted to high-yielding annual and perennial horticulture varieties.
- A total of 4,721 hectares of cropland have been brought under irrigation in IDEA-NEW targeted area.
- The project multiplied two MAIL-certified varieties of mung-bean for distribution to more than 15,000 farmers.
- More than 30,000 farmers in Eastern Region have participated in voucher distribution programs for improved vegetable varieties. Thirteen thousand farmers participating in this program from Spring 2010 increased their revenues over 2009 by more than \$3.4 million collectively.
- More than 8 million kgs of onions exported to Pakistan by Afghan traders for export revenues of USD 2.8 million.
- 581,889 livestock are under increased management/care as a result of IDEA-NEW interventions; this has included deworming and other activities in close concert with local paravets.

Rural Job Creation

- Assisted entrepreneurs to start more than 1,751 rural enterprises for men and women throughout the program.

Building Capacity

- Partnering with MAIL provincial and district offices, a total of 103,917 MAIL staff and farmers were trained on melon-fly control in the West, North and Northeast regions. An impact study completed in November 2009 showed IDEA-NEW's melon fly training program is increasing participant farmers' yields by 113% and sales by 46%.
- A total of 2,000 women and 1,023 men have received business skills training.
- A total of 843 government line staff members have received training and capacity building related to their jobs.
- Established six Ag Retail Associations across the Northern Provinces, who are working with 117 Ag Retailers to increase sales.

- Provided technical assistance and training to 12 associations in its areas of operation, including for fruit growers, talc miners, beekeepers, women's handicrafts and others.

USG and GIROA Coordination:

- Livestock De-worming Campaign in Faryab was implemented in concert with US Army Special Forces, MAIL, USAID's Accelerating Sustainable Agriculture Program's Veterinary Field Units and local, private para-veterinarians. In total 266,605 animals were de-wormed in 14 of Faryab's Districts.
- Collaborating with MAIL and the Nangarhar PRT to cultivate eight varieties of wheat breeder seeds through MAIL's Nangarhar Valley Development Authority (NVDA) on 100 hectares of government-owned land in Farm-E-Ghaziabad of Nangarhar. The project is expected to provide 250-300 tons of foundation seeds for wheat seed production enterprises and companies, including village-based seed enterprises operating throughout the Province. These companies will replicate the foundation seeds and produce more than 6,000 tons of certified wheat seeds for farmers across Nangarhar Province in 2010.
- Collaboration with USAID's ASMED project to strengthen the poultry value chain by establishing a feed mill in Surobi District of Kabul Province.
- Facilitated a plenary workshop for MAIL in 2010 in which all 34 Provincial Directorates participated. The program kicked off a national Agriculture Extension Program for the country, and has been followed up by regional level Agriculture Extension and the Planning, Budgeting, Implementation and Organization of Agriculture Projects that have been held across the country.

Afghan First

- A total of 97% of IDEA-NEW project staff members are Afghans. IDEA-NEW also prioritizes local procurement, and has procured over USD 8.1 million from Afghan vendors since June 2009.
- In December 2010, IDEA-NEW facilitated contracts with a private Afghan company to supply major international produce buyer Supreme. IDEA-NEW is working with producers throughout the country to grow according to global GAP standards and provide continuous supply of needed vegetables.

Biweekly Highlights

November 16-30, 2010

Community-Constructed Infrastructure (CCI):

IDEA-NEW worked on 62 community-constructed infrastructure (CCI) projects throughout its areas of operation. It paid USD 129,607 in wages and generated 17,583 person days representing 260 full-time equivalent (FTE) jobs

To date, the project has paid USD 4.3 million in wages and created 743,271 person-days for more than 26,673 persons, representing 2,858 FTE jobs.

A total of 62 projects were active: 13 CCI projects were active in the eastern region, 16 in the northeast, 15 in north and 18 in the west.

The following CCI projects finished in the reporting period:

- **Shapoola Canal Intake Improvement, Debala District, Nangarhar province:** The project is located in the Transitional zone of Debala District in Nangarhar Province and classified as a priority project for implementation in IDEA-NEW Annual Work Plan Three.
- **Khulm River Gabion Protection Wall Extension, Jawzjan province:** IDEA-NEW North completed 975 meters of the gabion protection wall, saving a large area of land from the recent floods on the Khulm River this summer.
- **Mazar Almond Market concrete Platform:** The Mazar-e-Sharif Balkh Dry Fruits Processing Association (MBDFA) developed a market area granted by the Mazar City municipality. IDEA-NEW provided a concrete surface in the market on which produce can be stacked and dried in clean conditions. The market houses 158 shops.
- **Dasht-e-Flood Road Rehabilitation Project - Burka District, Baghlan Province:** This road is 8km long and connects farming families to Burka and Aliabad district centers.
- **Khoja Hafiz Gabion Protection Wall - Yangi Qala, Takhar:** This project was conducted in response to villagers' requests for flood protection. Male and female gabion weavers constructed 3,750 gabion boxes to form two dikes 107m and 360m long, respectively. A total of 2,500 residents of Yangi Qala are now protected from the threat of flood.

New CCI projects started in the biweekly period:

- **Sarkho Malakan Kariz project, Nazian District, Nangarhar Province:** The project will rehabilitate about 800 m long underground kariz channel for supplying the water to agricultural lands inside the villages.

- **Farman Khail School Boundary Wall project, Qarghaei District, Laghman Province:** The new boundary wall is being built only on land where no boundary wall exists and on land that is in the legal area of the school. The property measures 780 meters long, covering a polygon shaped area of 33,722 square meters.
- **Ali Khail School Boundary Wall project, Alishang District, Laghman Province:** The project is located in Alishang District and will construct a boundary wall on the school's land. The project will help Alishang district families permit their daughters go to school.
- **Shirgar School Boundary Wall project, Mehterlam District, Laghman Province:** This project will rehabilitate a 227 meter boundary wall and install main and sub entrance gates.

Agriculture Productivity and Agribusiness

- 305 farmers were trained during 20 field days in different districts of Nangarhar, Laghman and Kunar Provinces.
- A total of 314 farmers were trained during 18 field days on urea application, thinning, IPM and irrigation in different districts of Nangarhar, Laghman and Kunar Provinces. To date, 817 out of 2,100 have been trained.
- The cleaning process of foundation seed was completed in NVADA and a total of 10.95 out of 12.8 metric tons seed was obtained with 20% wastage.
- Some 949 (or 79%) of 1,200 farmers received training on demineralizing soil preparation, irrigation, fertilizer application, pest management, and harvest and post harvest activities and training for the remaining 21 percent stopped due to the worsening security conditions in the Hesarak District of Nangarhar Province.
- Thirty-two farmers received technical assistance on water management and preparing basins around the planted trees in various districts of the eastern region for their forestry plots planted in Spring 2010.
- In Nahrin, Burka and Bano districts of Baghlan, 58 farmers were trained on orchard and nursery irrigation systems and compost preparation.
- Some 39 individual wooden timber farmers in Badakshan were trained on bending and packaging wooden timber cuttings for the next season. Farmers were also trained on using animal manure, and compost preparation and application.

Rural Job Creation

- Zamarak broiler breeder farm located in Bihsud district, Nangahar province, produced 17,900 fertile eggs during the reporting period and 8,640 fertile eggs were moved to the hatchery in Saroobi to produce day old broiler chicks.

- A total of 6,000 broiler day old chicks were produced in Saroobi hatchery which used fertile eggs from the IDEA-NEW supported breeder farm in Jalalabad, Nangarhar. These chicks were sold to the poultry farmers in Nangarhar province.
- Support continued to 24 commercial layer farms directly established with IDEA-NEW support in the Eastern Region. Through which 118,439 table eggs were produced and supplied to the local market which generated about 532,975 Afs to the owners.
- 10,500 saplings of Eucalyptus worth USD 1,141.30 which were produced in three GME established women nursery marketed to ADT team in Laghman Province.

Building Capacity

- 719 farmers were trained on modern techniques in various districts of the eastern region.
- 90 trays (11,520 seedlings) of broccoli and red cabbage seedlings shifted from Farmankhail greenhouse located in Qarghaee District to the old CPFs of Alishang District in Laghman province.
- GME developed a health education, hygiene and sanitation training which will be provided to resident of Faizullah Khan area of Ghanikhaill District, Nangarhar province.
- English and Computer classes were continued by Afghanistan Institute of Business Management (AIBM) in both Laghman and Nangarhar Provinces.
- Nangarhar Talc Producers & Traders Association exported 2,250 metric tons of talc to Pakistan generating 37,500 AFN to the association.
- Spinghar Poultry Farmers Association (SPFA) continued operation with IDEA-NEW assistance. The association distributed two membership cards to new poultry farmers and received 550 Afs as membership fees. SPFA also sold 55 bags of poultry feed and earned 4,400 Afs net profit.
- Business planning and management training continued to 180 youth school girls in Laghman and Nangarhar provinces. Currently, trainees worked on a business plan.
- Refresher training for 95 paravets to upgrade and expand their skills has been undertaken in this reporting period. The trainees received training on business skills, poultry and dairy health.
- Training completed for Large Ruminant Herd Health Package which began with 73 VFU staff and 10 government veterinarians in Balkh, Faryab, Jawzjan and Sari Pul provinces

USG & GIROA Coordination

- IDEA-NEW Agriculture Project Integration Senior Officer Participated in Program Design Team, Research and Extension project meeting in MAIL hall in which MAIL wanted AKIS to be involved in it as Research and Extension.

- A meeting was held between FGA (Fruit Growers Association), ACE (Agriculture Credit Enhancement) and IDEA-NEW. The purpose of the meeting was to discuss the opportunity of loan from ACE to FGA.
- A watershed meeting with Pacheer wa agam elders was conducted and discussed the process of direct seeding of forestry seed. It was decided that eight teams will be made monitored by a supervisor and each team will include 11 members to carry on the activity of direct seeding.
- Takhar staff attended the PDC (Provincial Development Committee) Meeting, hosted by the governor of Takhar, Abd. Jabar Taqwa. Representatives from all NGOs in Takhar were in attendance and discussed new projects and opportunities for coordination.

Key Problems/Constraints

- Infrastructure project which was stopped due to abduction of IDEA-NEW staff was resumed in Kunar Province.
- During the reporting period, security condition of Hesarak District is still insecure. All engineers are coordinating activities very closely with community elders.
- The insecurity in Chimal district has caused the cancellation of project visit there.
- Security continues to make monitoring challenging. We currently have no way to independently monitor our projects in Burka, Nahrin and Khost districts in Baghlan.

Afghan First

- Locally purchased materials for DAI (East and West) from November 16-30, 2010 were \$372,524.29 USD.
- Locally purchased materials for ACDI/VOCA (Northern) from November 15-30 were \$80,900 USD.
- Locally purchased materials for Mercy Corps (Northeast) from November 15-30 were \$115,842.36 USD.

Biweekly Update: Eastern Region

Eastern region activities are implemented in the Provinces of Nangarhar, Kunar, Laghman and Nuristan. The program works closely with provincial- and district-level governments and within local communities, capitalizing on the successes of previous USAID projects in the area, which built strong relations among local stakeholders, and have given IDEA-NEW the ability to scale-up rapidly. In its second year of operations in the east, IDEA-NEW is undertaking work in 39 of the region's 50 districts.

Job Creation

Community-Constructed Infrastructure (CCI):

During the reporting period, IDEA-NEW worked on 13 CCI projects in the eastern region, generating 7,891 person days worth USD 48,047 in wages, and employed 746 males and 10 females. One project completed in Nangarhar Province and four others started in Nangarhar and Laghman Provinces. Please also see Annex II for more detail on all CCI projects.

NOVEMBER 16-30, 2010: CCI SUMMARY CHART—EASTERN REGION

Province	Total				Male	Female			Total			
	Approved Projects	Completed Projects	Active Projects	Stopped Projects	Person Days	Person days	Male Wages	Female Wages	Person Days	Total Wages	Males Worked	Females Worked
Kunar	7	5	0	2	0	0	0	0	0	0	0	0
Laghman	5	1	3	1	822	41	5331	182	863	5513	94	7
Nangarhar	36	21	10	5	6981	47	42325	209	7028	42534	652	3
Nuristan	1	1	0	0	0	0	0	0	0	0	0	0
TOTAL	49	28	13	8	7,803	88	47,656	391	7,891	48,047	746	10

Project completed in the reporting period:

CCI-080808, Shapoola Canal Intake Improvement, Debala District, Nangarhar province

The project is located in the Transitional zone of Debala District in Nangarhar Province, it started on April 05, 2010 and was completed on November 16, 2010. It was classified as a priority project for implementation in IDEA-NEW Annual Work Plan Three.

The irrigation system is fed from an existing canal intake locally constructed on Akakhail Wash. It was in poor condition and consistently damaged by floods. The system is designed to irrigate 92.05 jeribs of land serving the farms of about 500 families and flowing through different villages in the District of Dehala. The main crops grown in this system are wheat, corn, cotton and seasonal vegetables.

The project constructed a 50-meter long stone masonry and RCC intake (weir) structure with a total length of 515 meter canal retaining walls. The weir structure will provide sufficient water for the irrigated land under the system. The canal and agricultural lands in the same area will be protected by the canal retaining walls and weir's wing walls. The main work involved is excavation for structure foundations, construction of stone masonry retaining walls and RCC.

Voices from the Field

During an interview ██████████ and ██████████ community elders of this completed project and agriculture land owners, appreciated the work done by IDEA-NEW and thanked IDEA-NEW staffs for presenting standard work in this remote area.

"I am very happy that after 30 years our canal is reconstructed and now we see canal full of water and our dream came true. In 30 years, our canal intake was completely damaged by floods. I appreciate IDEA NEW work and its staff who has worked very honestly and closely with community.

IDEA-NEW staffs work on this project was transparent and they coordinated each single issue with village elders and Shura leaders. Before we were unable to irrigate the land coming under this canal and now the current improved system can irrigate the whole area of this canal and also the poor people financially benefited during implementing the project."

-- ██████████, *Community Elder*



Photos (above / below): Before and after photos of CCI-080808, Shapoola Canal Intake Improvement, Dehala District, Nangarhar. Hectares irrigated: 18.41



Projects started in the reporting period:**Sarkho Malakan Kariz project, Nazian District, Nangarhar Province**

The irrigation system is fed from an existing underground kariz locally constructed. It is in a poor condition and is consistently damaged by floods. The system is designed to irrigate over 700 jeribs of land serving the farms of about 600 families and flowing through four different villages. The main crops grown on this system are wheat, corn, cotton and seasonal vegetables.

The project will rehabilitate about 800 m long underground kariz channel for supplying the water to agricultural lands inside the villages. The parts of the canal that are damaged by seasonal flood and need to be improved by stone masonry and RCC slabs that prevent land and water losses during irrigation.

Farman Khail School Boundary Wall project, Qarghaei District, Laghman Province

The Farman Khail School was established at its present location many years ago. Since it does not have proper boundary walls, is difficult for girls to go to school there. Thus, the community requested that IDEA-NEW build a boundary wall.

The new boundary wall is being built only on land where no boundary wall exists and on land that is in the legal area of the school. The property measures 780 meters long, covering a polygon shaped area of 33,722 square meters.

Ali Khail School Boundary Wall project, Alishang District, Laghman Province

The project is located in Alishang District and will construct a boundary wall on the school's land. The project will help Alishang district families permit their daughters go to school. The property measure 780 meters long covering a polygon shaped area of 9,953 square meters.

Shirgar School Boundary Wall project, Mehterlam District, Laghman Province

This project is located in Laghman Province and will rehabilitate a 227 meter boundary wall and install main and sub entrance gates. The project will not only protect students from direct environmental threats, such as seasonal winds during classes but will also encourage families send their girls to attend the school due to the increased level of safety. In addition, local people from the community will have job opportunities during its construction.

Ongoing CCI Photos, East: November 1-15, 2010



*Koshtal MHP project,
Achin District, Nangarhar Province
Project Progress = 90%*



*Nahri Karim Canal improvement project
Qarghayie District, Laghman Province
Project Progress: 73%*



*Garigal canal intake improvement
Chowki District, Kunar Province
Project Progress = 75%*



*Alikhail School Boundary project
Mehterlam District, Laghman Province
Project Progress = 3%*



*Marko School Boundary Wall
Shinwar District, Nangarhar Province
Project Progress = 99%*



*Ragha Canal improvement,
Hesarak District, Nangarhar Province
Project Progress = 52%*

Agricultural Productivity Job Creation

Mung Bean Seed Multiplication and Distribution:

No updates in the reporting period.

Regional Nursery Development Program:

Some 12 citrus nurseries were supervised and checked in Qarghaee and Mehtarlam districts of Laghman Province. Activities at the nurseries included removing plastic from the budded parts of seedlings, labeling the different varieties, plowing, and weed control. One of the 12 GME section green houses located in Batikot District of Nangarhar Province was selected for citrus seed planting and seedlings production; to date a total of five green houses were selected. In addition, 36,000 seeds (Volkameriana variety) were planted in one green house located in the Behsood District of Nangarhar Province; and three GME green house operators were trained on nursery establishment, raised bed preparation, sowing, and irrigation in Behsood District of Nangarhar Province.

Technology Innovations for Market-Led Economic Rehabilitation (TIMER) Voucher Program:

The Technology Innovations for Market-Led Economic Rehabilitation (TIMER) Program addresses the needs of subsistence farmers in their efforts to increase productivity and produce marketable surpluses by providing a package of improved seed varieties with marketable attributes, fertilizer, and technical assistance. Under USAID’s ADP/E program, the project was shown to increase farmer’s yields by between 60-125% and had a cost/benefit ratio of 1:4. A similar impact study was conducted in the January-March 2010 quarter under IDEA-NEW with similar results; see Impact Studies on page 56 below.

Crops planted in fall 2010:

305 farmers were trained during 20 field days in different districts of Nangarhar, Laghman and Kunar Provinces. To date, 2,836 out of 5,625 farmers have been trained on different Lead Production Farms (LPFs) and Small Demonstration Farms (SDF) modern techniques. In addition, 13 field nurseries were established in various districts of the eastern region which was the final establishments for Fall 2010. To date, a total of 93 field nurseries have been established.

Additional activities include: field lay-out, seeding and transplanting for cauliflower, cabbage, broccoli, carrots, spinach, red radish, white radish and turnip continued in eastern region. To date, 28 SPFs have been established and 95 out of 125 SDFs have been laid-out and transplanted.

Crops to be planted in spring 2011:

Preparations have begun for the coming Spring season, RFQs were distributed to the national and international seed suppliers and eight quotations have been received and are under review.



Photo: IDEA-NEW field technician trains practically to seed volkameriana citrus in Behsud District of Nangarhar Province.



Photo: IDEA-NEW field technician trains farmers on harvesting of turnips in Asadabad District of Kunar Province.

Onion Production Program:

Selection of new onion SPFs Fall season 2010 was completed in various districts of the region for licit crop production. A total of 100 farmers were selected in Nangarhar and Laghman provinces and 95 out of 100 nurseries were established.

Training activities for onion growers also have been started in the target area on field nursery establishment and management of onion demo plots. To date, 363 out of 4,500 farmers have been trained in various districts of Nangarhar Province.

Potato Program:

No updates in the reporting period.

Regional Vegetable Marketing Program (REVAMP) Voucher Program:

REVAMP helps orchard farmers to grow vegetables as an interim cash crop until their trees begin to bear fruit.

Crops planted in summer and fall 2010:

A total of 314 farmers were trained during 18 field days on urea application, thinning, IPM and irrigation in different districts of Nangarhar, Laghman and Kunar Provinces. To date, 817 out of 2,100 have been trained. Besides, 16 REVAMP demo plot owners received free tool packages in Rodat, Darinoor, Behsood, and Batikot districts of Nangarhar and Qarghaee and Mehterlam districts of Laghman provinces. The packages included three meter measuring tape, hoe, two kg nylon string, shovel, trowel, shovel for making ridges, water cane, sickle and wheelbarrow.

In addition, 84 REVAMP beneficiaries having 18 Ha land cultivated with vegetables received technical assistance on land lay out, sowing, irrigation, weed control and thinning activities.

Wheat Breeder Seed Cultivation:

The cleaning process of foundation seed was completed in NVADA and a total of 10.95 out of 12.8 metric tons seed was obtained with 20 % wastage. The 10.95 metric tons will be distributed with a 50% subsidy to the registered seed production companies in future particularly those companies that legally merit foundation seed planting.

Staple Crops Program—Yellow Maize

Some 949 (or 79%) of 1,200 farmers received training on demoinsturizing soil preparation, irrigation, fertilizer application, pest management, and harvest and post harvest activities and training for the remaining 21 percent stopped due to the worsening security conditions in the Hesarak District of Nangarhar Province.

Orchard Program:

Field technicians randomly checked 290 fruit growers for implementation of the agricultural practices recommended during the field days in Nangahar, Laghman and Kunar provinces. Besides, 259 farmers having 259 Jeribs of land in total were selected for new orchard establishment that will plant in Spring 2011. To date, a total of 806 Jeribs of land were selected for the Spring 2011 planting season.



Photo: A view of carrots plot supported by IDEA-NEW in Daria Noor District of Nangarhar Province.

FIELD Program:

Thirty-two farmers received technical assistance on water management and preparing basins around the planted trees in various districts of the eastern region for their forestry plots planted in Spring 2010. Also, 22 farmers, having 22 Jeribs land, have requested to establish the forestry plots in Spring 2011. To date, 98 farmers have been selected for the FIELD program.

Watershed Program

Seed collection was completed in Pacheer Wa Agam and around 60 kg walnut, 60 kg quercus and 10 kg pine nut seeds were collected. There are plans to reforest 100 hectares of deforested area by direct seeding in Pacheer wa agam and Noorgal districts of Nangarhar Province. Besides, four areas were also selected for direct seed reforestation in Mazar Dara Valley Noorgal District.

Rural Job Creation:**Poultry Value Chain/Breeder Farm Development:**

Zamarak broiler breeder farm located in Bihsud District produced 17,900 fertile eggs during the reporting period and 8,640 fertile eggs were moved to the hatchery in Saroobi to produce day old broiler chicks. These breeders are now 56 weeks old.

In addition, IDEA-NEW established four new commercial broiler poultry farms in Bihsud District, Nangarhar Province. IDEA-NEW distributed 1,000 broiler chicks and 50 bags feed free of cost to each farm and the poultry farmers contributed building construction, equipment etc. The chicks distributed were from the local hatchery in Saroobi District which hatches locally produced fertile eggs.

Support also continued to Hidayat Brakat Broiler Breeder Farm located in Nangarhar province. These chicks are now three weeks old. Required vaccines were given by IDEA-NEW poultry specialists and beak trimming was completed. Chicks were healthy and are growing normally. These chicks will start producing fertile eggs in 22 weeks.

Poultry Value Chain/Hatcheries' Development

A total of 6,000 broiler day old chicks were produced in Saroobi hatchery which used fertile eggs from the IDEA-NEW supported breeder farm in Jalalabad, Nangarhar. These chicks were sold to the poultry farmers in Nangarhar province.

Poultry Value Chain/Commercial Poultry Farms

Support continued to 24 commercial layer farms directly established with IDEA-NEW support in the Eastern Region. The prime objective of this program is to create jobs, promote the viable poultry sub-sector and supply table eggs to the local market. During the reporting period, a total of 118,439 table eggs were produced and supplied to the local market which generated about 532,975 Afs to the owners of these poultry farms.



Photo: A mountainous sight of Pacheer wa Agam District of Nangarhar Province where reforestation is planned.



Photo: A view of broiler farm in Behsud District of Nangarhar Province.

Poultry Value Chain/Women’s Smallholder Poultry Farms

During the reporting period, GME provided technical training to the new and existing poultry farms. In addition, site consultation and field observation of 50 established and 45 newly established women-owned poultry farms were conducted by GME technical team in the eastern region. New farms were also selected in Batikot, Surkhrod and Kama districts of Nangarhar and the Metarlam district of Laghman Provinces.

Textile Value Chain/ Processing Facility:

During the biweekly period, the facility processed the following quantities of products, which were woven by individual textile companies and weavers from Rodat and Behsud Districts of Nangarhar Province.

Product	Quantity	Processing Description
Nylon and woolen shawls	1,668	Pressed
Scarves	336	Pressed & dyed

Textile Value Chain/Textile Weavers’ Support:

A small textile factory established in Kama district will start operation and production soon. The machinery was completely installed and employees require training to learn the electrical weaving machines operation which is a new technology for them and will start in coming biweekly with IDEA-NEW support.

Textile Value Chain/Fiber Distribution Center:

No updates in the reporting period.

Livestock Value Chain/Women-Owned Dairy Processing Centers:

GME technical team visited Spinghar cheese centers located in Surkhrod, Kama, Batikot, Shega districts of Nangarhar and Husain Abad in Laghman provinces. Total cheese marketed in the reporting period was 232.7 kg worth USD 834.67.

Vegetable Value Chain/Women-Owned Greenhouses:

Site consultancy and technical assistance was continued to 22 greenhouses in the eastern region. GME applied a raised bed system on seven greenhouses for citrus cultivation and 428 kg cucumbers from different greenhouses located in Laghman worth USD 249.34 were marketed.

Vegetable Value Chain/Women-Owned Packing Facility:

Currently, 15 women are employed by the packing facility, providing packing services for vegetables of the eastern region. The facility provided its packing services to 281 kg of vegetables worth USD 318 under the brand of "Pride of the Eastern Region". Vegetables were shipped to Kabul supermarkets. The packing facility is also in the process of being privatized through a private trader. The private trader is planning to sell to Supreme, a large supplier to ANA, ANP, International Coalition Forces and others in Afghanistan, and will put the packhouse on a path to sustainability.



Photo: A woman holds a basin full of table eggs collected from poultry farm in Mehterlam District of Laghman Province.



Photo: Women package mint in Surkhrod District of Nangarhar Province.

Fruit and Nut Value Chain/Women-Owned Tree Nurseries

Herb project implemented under Kitchen Garden demo farms. Dill, Parsley, Coriander and Mint were cultivated. In addition, GME observed and monitored 20 women nurseries located in Khogiani District. The conditions of observed nurseries were in good condition. Moreover, 10,500 saplings of Eucalyptus worth USD 1,141.30 which were produced in three GME established women nursery marketed to ADT team in Laghman Province.

Besides, 30 woman operators of fruit and forestry nurseries received the final payment from IF HOPE worth USD 2173.91. Around 5,000 saplings of citrus sapling remained in the women owned nursery in Samarkhail District which will be sold to fruit growers association in future.

Fisheries Value Chain/Women-Owned Fish Farms

GME team is engaged to develop a business plan for fish production in the eastern region.

Micro-Enterprise Development/Women’s Mentorship Program:

No updates in the reporting period.

Other Rural Job Creation:

Women operators of GME established kitchen garden enables to harvest different products from their vegetable small demo farms in Barikab and Behsud distracts. During the reporting period, 2,350 kg red radish and spinach worth 20,825AFN were marketed to local district markets.

Shamshad vermicelli factory restarted operation again after a period of one month in Jalalabad; it was stopped due to negative competition of imported Pakistani products. The factory hired 10 employees and currently produces about 1.5 tons vermicelli a day.

“IDEA-NEW did a good job but what hurt me and other local small enterprises is the negative competition from the neighboring countries. Afghanistan is obviously a good market and they want to retain it. It is also our understanding that some companies have distributing agents who don’t care bringing the costs down dramatically when they see a local factory start production and taking the market share. I do request and look forward to GIROA support to protect the local industries. They create jobs, add value to the local products and even contribute in stability.”

- ██████████, Shamshad Vermicelli Factor Owner



Photo: A women operator arranges cheese produced in Surkhrod District of Nangarhar Province.



Photo: Women package mint in Surkhrod District of Nangarhar Province.

Agricultural Sales/ Trade Corridor Market Development

Local, National and Export Market Facilitation:

- Vegetable growers in the eastern region received technical assistance in harvest and postharvest management, and were linked to local markets. Please see the sales table in Annex III for details.
- Local traders continued supplying fresh fruit and vegetables to high value markets (supermarkets and institutional clients) in Kabul.
- Nothing facilitated in the export market during reporting period.

Market Information System (MIS):

- During the reporting period, nine live Karkila Aw Maldari (agriculture and livestock) radio shows were aired on Sharq Radio (91.3 FM) in Nangarhar Province, Kawoon Ghag Radio(89.3 FM) in Laghman Province and Kunar Radio (105.2 FM) in Kunar Province. A total of 28 listeners called the shows asking different questions about their orchard, vegetable and livestock problems, and received answers from the show's agriculture expert.
- Three radios were handed over to individuals who answered respective questions relating agriculture and livestock in Nangarhar Province as part promotion to the radio show.
- Malomat continued sending weekly price reports to donors, partners, individuals and BBC for broadcast on GiD. During the reporting period more than 150 individuals received weekly price reports.
- Radio show resumed in Kunar Province as the situation got normal.

Building Capacity

Resource Centers / Model Farms:

Training activities for Fall and Winter seasons continued and 719 farmers were trained on modern techniques in various districts of the eastern region. To date 3,314 farmers out of 6,075 have been trained in Fall season 2010 in four provinces of the eastern region and process of the training will be continue till final target in different stage of the crops. Please refer to the farmer training summary in Annex III for district breakdowns and type of training.

In addition, tools distribution has been continued to SPF farmers for Fall and Winter season, 2010. During the reporting period, 19 plots owner received tools in Marwara, Asmar, Assadabad, Shigal districts of Kunar Province. In addition, land preparation, applying of animal manure, DAP, lay-out and transplanting were continued for fall season in different districts



Photo: A view of carrots plot supported by IDEA-NEW in Daria Noor District of Nangarhar Province.



Photo: A farmer arranges cabbage harvested in Asadabad District of Kunar Province.

of Nangarhar, Laghman and Nooristan provinces. As per vegetable production plan the fifth planting of the cool season crops (Brussels sprout, Broccoli, Cauliflower, Lettuces etc.) was finished in all 16 CPFs plots.

Fencing process was continued in CPFs of Kama and Surkhrud District and will be finished in coming days under Global GAP (Good Agriculture Practices) program. Moreover, 90 trays (11,520 seedlings) of broccoli and red cabbage seedlings shifted from Farmankhail greenhouse located in Qarghaee District to the old CPFs of Alishang District in Laghman province.

Community Institution Capacity Building:

GME developed a health education, hygiene and sanitation training which will be provided to resident of Faizullah Khan area of Ghanikhail District, Nangarhar province. The training will help to raise awareness of how to keep clean drinking water for shallow wells. It will also assist to decrease the borne diseases of that area and the beneficiaries will have better access to clean drinking water.

English and Computer classes were continued by Afghanistan Institute of Business Management (AIBM) in both Laghman and Nangarhar Provinces.

Support continued with Nangarhar Talc Producers & Traders Association (NTPTA). During the reporting period NTPTA exported 2,250 metric tons of talc to Pakistan generating 37,500 AFN to the association. Association membership increased to 54 and will continue to grow as memberships haven't yet to be distributed to many miners in Shirzad, Khogyani and Shinwar districts.

Spinghar Poultry Farmers Association (SPFA) continued operation with IDEA-NEW assistance. The association distributed two membership cards to new poultry farmers and received 550 Afs as membership fees. SPFA also sold 55 bags of poultry feed and earned 4,400 Afs net profit.

Taraqi Saba Program:

Business planning and management training continued to 180 youth school girls in Laghman and Nangarhar provinces. Currently, trainees worked on a business plan.

USG & GIRoA Coordination

- IDEA-NEW Agriculture Project Integration Senior Officer participated in Program Design Team, Research and Extension project meeting in MAIL hall in which MAIL wanted AKIS to be involved in it as Research and Extension.
- Meeting held with deputy governor, Mr. Qalanderzai, and facilitated Laghman market shops distribution to Laghman and Nangarhar traders through Laghman authorized team.



Photo: Cabbage being grown in Batikot District of Nangarhar Province under IDEA-NEW's commercial production farm program that is helping raise standards with an eye to meeting Global GAP.



Photo: Female students gathered during Taraqi Saba Training at Bibi Aisha High School in Jalalabad, Nangarhar Province.

- In following to AKIS previous meeting IDEA-NEW liaison Officer participated in MAIL extension team meeting in order to select different pilot projects in 50 districts of Afghanistan for AKIS model projects implementation.
- Met with FAO and ASAP representatives in Badam Bagh station for selecting the venue and study tour for IDEA/NEW and its partners.
- During the reporting period, Provincial Development Committee (PDC) meeting held in Laghman Province in which decision was made on further cooperation of the organisations.
- Based on final decision of senior staff meeting regarding restarting IDEA-NEW projects in Kunar Province, Sadat, liaison officer, arranged a meeting between various districts of Kunar Province elders and IDEA-NEW senior staffs in IDEA-NEW office hall. They promised to support and take care the live of staffs working on the site.
- A meeting was held between FGA (Fruit Growers Association), ACE (Agriculture Credit Enhancement) and IDEA-NEW. The purpose of the meeting was to discuss the opportunity of loan from ACE to FGA.
“We consider this an opportunity and we will discuss this issue among all the board members and will get back to ACE and IDEA-NEW in about one week,” said Ghulam Sidiq director of FGA.
 During the meeting ACE folks from Kabul including CoP (Chief of Party) were also present and provided a brief presentation about their program.
- Meeting arranged among Shamshad Feed mill representatives, farmers’ groups representatives, PSD and AH responsible staff signed the contract in which the feed mill team will purchase yellow maize grain with high price than of the local market in order to encourage farmers to sell yellow maize on feed mill.
- A watershed meeting with Pachir Wa Agam elders was conducted and discussed the process of direct seeding of forestry seed. It was decided that eight teams will be made monitored by a supervisor and each team will include 11 members to carry on the activity of direct seeding (Nanaghar province).
- Kunar nursery growers board had a meeting with Root of Peace organization in which nursery grower Manager was selected to watch closely certain nurseries.



Photo: IDEA-NEW Agriculture Project Integration Senior Officer and other government officials in meeting held in Laghman market hall.



Photo: Various districts elders of Kunar Province in a meeting held in IDEA-NEW office hall request to resume CCI projects in Kunar Province.

Key Problems/Constraints

- Infrastructure project which was stopped due to abduction of IDEA-NEW staff was resumed in Kunar Province.
- During the reporting period, security condition of Hesarak District is still insecure. All engineers are coordinating activities very closely with community elders.

Afghan First

Locally purchased materials for DAI (East and West) from November 16-30, 2010 were \$372,524.29 USD.

Biweekly Update: Western Region

Job Creation

IDEA-NEW implements community-constructed infrastructure (CCI) projects throughout the western region, which serve a two-fold purpose: to restore and build productive infrastructure, and to inject cash into local economies in unstable and insecure areas helping to reduce communities' reliance on illegal activities, including narcotics and insurgency.

During the reporting period, IDEA-NEW continued working on 18 CCI projects (nine MHP projects, seven irrigation, one wholesale market and one construction skill training) in Badghis which generated 7,676 person days worth 49,847 wages and 675 individuals worked. Six more projects have been surveyed and are under designs which are expected to start in future. Please see Annex II for more detail on all CCI projects.



Photo: A view of Wholesale Market constructed with support of IDEA-NEW in Qalai Now District, Badghis Province.

SUMMARY TABLE: CCI PROJECTS WESTERN REGION: NOVEMBER 16-31, 2010

Province	Total Approved Projects	Completed Projects	Active Projects	Stopped Projects	Male person days	Male wages	Total person days	Total wages	Male worked
Badghis	26	3	18	5	7,676	49,847	7,676	49,847	675
TOTAL	26	3	18	5	7,676	49,847	7,676	49,847	675


Ongoing CCI Photos, Western Region: November 16-30, 2010



Ferestan Canal, Abkarmari District, Badghis
Progress : 62%



Qulmali Canal Imp., Abkamari District, Badghis
Progress: 65%

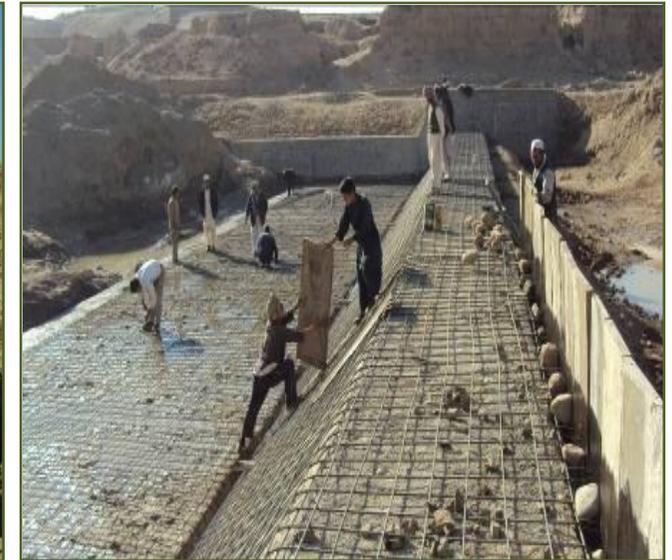

Zaemat Canal Intak, Abkamari District, Badghis
Progress: 85%

Building Capacity of Community Institutions

Training provided to 10 individuals on masonry, 12 on molding, 17 on reinforcement and 10 others on carpentry skills in various districts of Badghis Province.

USG & GIRoA Coordination

No updates in the reporting period.

Key Problems/Constraints

No updates in the reporting period.

Afghan First

Locally purchased materials for DAI (East and West) from November 16-30, 2010 were \$372,524.29 USD.

Biweekly Update: Northern Region

Job Creation

Community-Constructed Infrastructure (CCI):

Irrigation, Farm to Market Roads and Micro-Hydro Power projects

Agriculture and Rural Infrastructure:

During the reporting period, IDEA-NEW worked on fifteen CCI projects in the northern region. Please see Annex II for more detail on all CCI projects.

Province	Total Approved Projects	Completed Projects	Active Projects	Stopped Projects	Male	Female	Male	Female
					Person Days this period	Person Days this period	Wages this period (AFN)	Wages this period (AFN)
Balkh	5	4	1	0	286	0	0	0
Samangan	2	2	0	0	0	0	0	0
Jawzjan	1	0	1	0	208	0	Paid by IP	0
Sari Pul	6	1	5	0	0	0	0	0
Faryab	18	10	8	0	0	0	0	0
Total	32	17	15	0	494	0	0	0

Flood Protection and Irrigation

Construction of Mardian Water Reservoir:

Many villages in the northern part of the region suffer from severe lack of water during the summer. The irrigation canals, which they rely on dry up and since the groundwater is saline, they cannot use wells. At present they rely on storing water in ponds, which is inefficient, as there is seepage into the sandy soil, and unhygienic, as the ponds are open to animals. Concrete cisterns provide efficient clean water storage, but are very expensive. IDEA-NEW is evaluating the possibility of using ponds with High Density Polyethylene liners and covers as a less expensive alternative. Mardian district centre in Jawzjan has been selected for the pilot project, holding 3 million liters of clean potable water for 300 families, who will

draw it off through a hand-pump. Because of security considerations, it was decided that this project should be implemented under a subcontract rather than by the IDEA-NEW Infrastructure team as Cash for Work project.

Following the excavation and shaping of the pond during the previous biweekly period, the workers compacted the ground surface for laying the base course. The work progress in this project has reached 51 percent. A total of 208 person days of job created in this project in this biweekly reporting period. The project has been monitored and supervised by the infrastructure engineers.

Khulm River Gabion Protection Wall Extension:

IDEA-NEW completed 975 meters of the gabion protection wall, saving a large area of land from the recent floods on the Khulm River this summer. It also proved to be beneficial to farmers and orchard owners in Khulm district, Jawzjan province. At the request of the community representatives and local government, IDEA-NEW agreed to extend the project and strengthen an additional 550 meters of the riverbank.

The Khulm River Gabion Protection Extension Project protects dwellings and agricultural land on both sides of the Khulm River. The locations to be protected are approximately 3km upstream and 3km downstream from Khulm district center. The total length of riverbank to be protected is 550 meters. The gabion protection walls will be constructed in six different points where the banks are assessed to be weak.

This will protect 500 hectares of agricultural land from floods. It will also help the irrigation system in the Khulm River basin by providing stable river banks and improving water management. The project is expected to create 7,148 person days of employment (27.49 FTEs) for 500 families from Khwaja Assad, Qala Arab Bik, Oymahoot, Tailee, and Mirhazar villages in Khulm district.

Recent work at the site has been slow due to the shortage of woven gabion boxes. The laborers completed backfilling 200 meters. A total of 286 person days (1.10 FTE) of employment has been created. Overall progress to date remains 70%.

Power

Five Micro Hydro Power Units in Sari Pul:

IDEA-NEW began construction of five MHP plants in Balkhab district of Sari Pul province in September 2009. Construction was not completed before the winter and was damaged by the exceptional floods that took place earlier this year. The floods also delayed the resumption of work. Following an assessment of the damage, plans have been made to repair and reinforce the structures constructed by the local communities under an agreement with the IP Remote Hydro Light.



Photo: Laborer compacting the soil around a pond.

The design and extra budget was approved. The percentages of completed works in each of these five MHPs remain as it was in the previous biweekly report, but significant progress is expected in the next biweekly reporting period: Hoosh 88%; Parawshan 95%; Chaila 88%; Khamshorak 68%; and Dahna Wa Takhshar 70%.

Eight Micro Hydro Power Units in Faryab:

IDEA-NEW had previously signed a sub-grant to the International Assistance Mission (IAM) to provide the electrical equipment for the construction of eight MHP projects in Qaysar and Kohistan districts of Faryab province. However, the deteriorating security situation in those districts has obliged IAM to withdraw. IDEA-NEW has therefore signed a modification to the agreement to allow the same number of installations to be made in Pashtun Kot district. These MHPs will produce 75.4 KW power and they are being built in eight different communities of Pashtun Kot district and will serve 1,250 households.

No specific report has been received from the IP in this reporting period. Therefore, the progress percentage remains as it was in previous biweekly report. The progress in installing the equipment is as follows: Hazara Qala MHP 31.57%, Nawabad Beqlarsai MHP 24.26%, Kata Qala Shora-e-Bazar MHP 40.6%, Kata Qala Shora-e-Madrasa MHP 17%, Kata Qala Haji Basir MHP 21%, Ibrahimabad Micro Hydro Power 20.21%, Qalai Niasbeq-Payan 24.73% and Qalai Niasbeq-Bala 25.53%.

Farm to Market Infrastructure

Mazar Almond Market concrete Platform:

The Mazar-e-Sharif Balkh Dry Fruits Processing Association (MBDFA) is developing a market area granted by the Mazar City municipality. IDEA-NEW is providing a concrete surface in the market on which produce can be stacked and dried in clean conditions. The market houses 158 shops. The MBDFA members (shop owners) need to process the fruits by laying them in the open and exposing them to sunlight. At present they cannot do so because the ground, which is bare earth, is dirty and unhygienic. The dry fruits that are processed in this market are grown in Balkh and its neighboring provinces. The main types of produce sold in this market are almond, pistachio, walnut, apricot and, dried plums.

The completion ceremony is scheduled for December 11, 2010.

Voices from the Field

██████████ a local unskilled labor on Mardian Water Pond project said, “It has been about a month that I am working here in my community and making good income. I am happy from my work, because I get 300AFN per day. I am also happy because this water pond will resolve the water problem of our community.”



Photo: ██████████, shaping the pond in Mardian district (JW).

Agriculture Productivity and Agribusiness

Sustainable Agricultural Production

New Almond Orchard Establishment in Balkh Province

IDEA-NEW, working through a commercial nursery, has planted 100 hectares of new almond orchards in Chimtal district of Balkh province. Under the terms of the contract, 50% of the price was paid on completion of planting in March and 50% withheld until October, when final payment would depend on sapling survival.

Monitoring of the survival of the saplings was planned to be completed in October, but because of security constraints in this district only 49.6 ha orchards, containing 16,314 trees have been visited in previously biweekly reporting period. In this biweekly an additional 16 ha orchards containing 4,018 trees have been visited. The report indicates that on average 93% of all visited trees were alive.

Trellis post installation:

Grapes are a major crop in northern Afghanistan, but the traditional methods of cultivation, by which vines are grown on the ground, have low yields, produce poorer quality and suffer more from disease relative to modern methods of vineyard management. IDEA-NEW is seeking to improve yields and quality by introducing trellising. Four trellis post manufacturers have been established in the region (see below) and demonstration vineyards set up where existing vines are being trained onto trellises. Agricultural retailers have been trained to supervise the setting up of trellising systems and will be paid a fee by IDEA-NEW for every jerib in which a system has been correctly installed.

Following the signing of two MoUs with agriculture retailers in Feroz Nakhchir district of Samangan and Maymana City of Faryab province for trellising program, the field activities for the operations of trellising program are going on in both Feroz Nakhchir and Maymana City. IDEA-NEW agriculture development program staff not only was supervising the agriculture retailers on their initial measuring and layout, but also provided them with technical advice. A total of 2,006 concrete posts have been transported to eight vineyards for trellising. In addition to that, the team surveyed three vineyards in Khwaja Sabz Posh and Pashtun Kot districts of Faryab province. Altogether 238 concrete posts have been requested for trellising the vineyards in these plots.



Photo: View of live trees in Chimtal district (BL)



Photo: Vineyard owner in Feroz Nakhchir is installing the concrete post following the direction of Agriculture Retailer (SM)

Livestock

Establishing Village Milk Processing Centers with Balkh Livestock and Dairy Union (BLDU)

The following activities were implemented by this project.

Meeting with women dairy farmers:

The Women Master Trainer of BLDU held meeting with 50 women of Jui-Zindan village of Aybak and Ghaznigak village of Hazrati Sultan districts of Samangan province to start the Livestock Management, Milking Hygiene Training Courses. In these meetings the methodology of training was demonstrated to the village women trainers.

The courses are planned to start in next biweekly reporting period.

TA in Cattle Health Care (Cattle Infertility Campaign):

The declining fertility in dairy cattle is a major problem facing the Afghan farming sector. Among the factors that can change or overcome this problem are improved genotype, nutrition and animal health care. A key question, therefore, concerns the extent to which each of these contributes to the problem of poor conception rates. Other issues - including management practices, reproductive infections also cannot be ignored.

For this reason, BLDU started Infertility campaigns with the objectives of reducing the infertility percentage in 10 target villages. To date 6 villages had been covered, of which 2 villages have been done in this biweekly reporting period. The campaign will continue throughout the month of December to cover all the 10 target villages. The animals treated and pregnancy tests performed in two target villages is summarized in the following table.

INFERTILITY CAMPAIGN

Province	District	Village	Cows treated	Cows pregnancy tested	Infertility Percentage
Samangan	Aybak	Jui Zindan	8	26	23%
Samangan	Hazrati Sultan	Ghaznigak	22	41	34%
Total	2	2	30	67	57%



Photo: BLDU staff testing a cow for pregnancy in Hazarti Sultan district (SM)

Animal Health and Production

Under a two year project, Strengthening Animal Health and Production, implemented for IDEA-NEW by the Dutch Committee for Afghanistan (DCA), the followings activities have been accomplished during the month of November:

Capacity Building:

The six month training course for 15 new paravets (13 males and 3 Females) commenced in July and continued during this reporting period. The course will finish in January 2011. Refresher training for 95 paravets to upgrade and expand their skills has been undertaken in this reporting period. The trainees received training on business skills, poultry and dairy health.

DCA, with USAID funding, has developed Herd Health training packages to be delivered by paravets to enable livestock owners to raise the productivity of their animals. The training for the Large Ruminant Herd Health Package which had begun with 73 VFU staff and 10 government veterinarians in Balkh, Faryab, Jawzjan and Sari Pul provinces completed in November. An impact evaluation of the Small Ruminant Herd Health Package was undertaken with 29 livestock owners in 19 districts.

Rural Enterprise Development

Agricultural Retailing Development:

IDEA-NEW continues to support six non-profit provincial agricultural retailers' associations established in Northern Afghanistan that were officially registered by the Afghan Ministry of Justice. These associations will serve the farmers through 117 Agricultural Retailing shops operating in the five Northern provinces. This support includes upgrading shop premises and training of shop-keepers to conform to internationally accepted guidelines for the storage, sale and handling of pesticides.

Trellis Post Production:

The trellis post maker in Maymana City signed his 2nd PO, started concrete post production and completed casting 240 concrete posts.

The post maker in Feroz Nakhchir district of Samangan signed the 5th PO for production of 740 concrete posts and completed casting 450 concrete posts. The quality control assessment of manufactured posts has been conducted and the finding has been reported satisfactory.

The first purchase order was signed with Qaysar concrete post maker for production of 700 trellis posts.



Photo: Concrete post production continues in Feroz Nakhchir district (SM)

Laser Land Leveling:

The second phase of laser land leveling operations started with participating agricultural cooperatives in Balkh, Jawzjan, Sari Pul and Faryab provinces. Altogether the agricultural cooperatives collectively managed to level 20 jeribs of local farmers' lands.

Establishment of 25 Maintenance and Repair Workshops for Two-Wheel Tractors:

During this biweekly reporting period, the contractor held two rounds of three day long workshops for seven mechanics of Balkh province and four mechanics of Samangan province with the objective of enabling them to maintain and repair the two-wheeled tractors. The trainees will work as the skilled service providers in their villages and districts and will repair local farmers' tractors.

In-kind Grant Distribution:

The allocated 10,000 liter dormant oil has been distributed to Bawar, Balkh Bastan, Kawsar, Bahar and Khurasan agriculture retailers associations. The trellising equipment such as augers, pliers, measuring tape, steel cutters have been granted to Bawar agriculture retailing association of Faryab for trellising program in the province.

Women Income Generation

Wool Spinning wheel project:

During this reporting period, RMHC has established a training center in Aqcha district of Jawzjan province, where 100 women will be trained the use of spinning wheels. Additionally, RMHC has been continuing its survey of trainees in Jawzjan and Sari Pul province. The contractor has also placed request order for making 100 spinning wheels for Aqcha trainees.

This training will be conducted in two shifts: one in the morning and one in the afternoon. Each session will last four hours.

Contracts and Grants

Sub-agreement was signed with an Afghan woman owned company in Mazar for training of 500 women in five provinces on Wool Spinning using spinning wheels and giving 500 wool spinning wheels as in-kind grants to the beneficiaries. The project start date is December 1, 2010

ACDI VOCA head office approved the following trellis post procurements through IDEA NEW trained trellis post makers:

- Feroz Nakhchir 12,000 Nos - \$ [REDACTED]
 - Maymana 12,000 Nos - \$ [REDACTED]
 - Qaysar 12,000 Nos - \$ [REDACTED]
- (Total 36,000 trellis posts - \$ [REDACTED]).

Trellis posts are currently being manufactured by these three suppliers. The posts are given to farmers at discounted prices. IDEA NEW is helping the trellis farmers to install these trellis posts in their grape farms and providing them with agriculture extension services to make the trellising successful.



Photo: Local mechanics learn how to fix two-wheeled tractors (JW)



Photo: Dormant oil distribution to agriculture retailers (SP)

IDEA NEW received 2,500 Nos Felco 5 pruning shears and 2,200 Nos Felco 611 pruning saws. These tools would be given as in-kind grants to the six agriculture retailers associations shortly. Agriculture retailers associations would sell these tools to farmers through agriculture retailers (Ag Depots).

Awaiting USAID/AO approval for the 2-Year Farmer Training on Improved Agronomy and Small Scale Mechanization project. ACDI VOCA signed a Letter of Authorization (LOA) with the sub-grantee for a value, not to exceed \$65,000 adequate to finance the work for two months. USAID approved 2011 and 2012 Workplan. The above project is an integral part of the Workplan.

Procurement of the ice cream making equipment from an Indian vendor was approved. The beneficiary is Balkh Livestock Dairy Union (BLDU). Quotes were invited for air-freighting the equipment to Kabul

Afhan First

Expenses incurred in Afghanistan during the biweekly period:

- Procurements - \$80,900
- Total expenses in Afghanistan - \$141,100

USG & GIRoA Coordination

Coordination with local government:

During this biweekly reporting period, IDEA-NEW program received a total of 39 infrastructure project applications of which 32 requisitions came from Sari Pul Directorate of Agriculture, Irrigation and Livestock, six project proposals from Balkh Directorate of Economy and one project application from Samangan province.

Constraints and Problems:

The insecurity in Chintal district, Balkh province has caused the cancellation of project visit there.

Biweekly Update: Northeast Region

Job Creation

Community-Constructed Infrastructure (CCI):

During the reporting period, IDEA-NEW worked on 15 active CCI projects in the northeastern region, employing 326 workers generating 1,522 person days and disbursing \$31,713 in wages. Please see Annex II for more detail on all CCI projects.

NOVEMBER 16-30, 2010: CCI SUMMARY CHART—NORTHEASTERN REGION

Province	Total Approved Projects	Completed Projects	Active Projects	Stopped Projects	Male Person Days this period	Female Person days this period	Male Wages this period	Female Wages this period	Total Person Days	Total Wages
Badakhshan	19	13	4	2	-	-	-	-	-	-
Baghlan	32	29	5	1	537	-	4,671	-	-	-
Takhar	11	6	5	-	985	-	27,042	-	-	-
Kunduz	2	-	2	-	-	-	-	-	-	-
TOTAL	64	48	16	3	1,522	-	31,713	-	1,522	31,713

Projects started during the bi-weekly period:

No updates in the reporting period.

Projects completed during the bi-weekly period:**Dasht-e-Flood Road Rehabilitation Project - Burka District, Baghlan Province**

This road is 8km long and connects farming families to Burka and Aliabad district centers. In addition to cutting, filling, compacting and gravelling of the road surface, workers also excavated 3.5km of side ditches and build 15 culverts alongside the road. 3,000 Burka families will benefit from better access to markets and services along this improved road.

Khoja Hafiz Gabion Protection Wall - Yangi Qala, Takhar


This project was conducted in Khoja Hafiz village in Yangi Qala in response to villagers' requests for flood protection. In recent years, the flood path of a nearby river had begun to direct floodwater into population centers, damaging crops and houses. Male and female gabion weavers constructed 3,750 gabion boxes to form two dikes 107m and 360m long, respectively. A total of 2,500 residents of Yangi Qala are now protected from the threat of flood.



Photos: Before and after shots of the Khoja Hafiz gabion wall in Yangi Qala, Takhar



Ongoing CCI Photos, Northwest: November 16-30, 2010, 2010

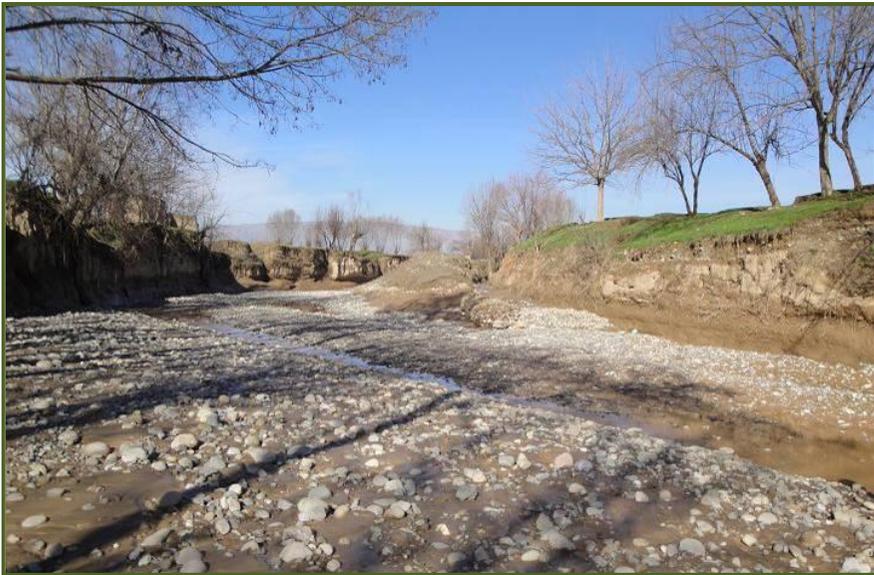

*Photos above and below:
Before and after photos of the Khoja
Mukhar canal intake, Taloqan, Takhar*



*Photo right:
Zardew canal in
Shuhada district, Badakhshan*



*Photo right:
Khustak gabion wall,
Jurm district, Badakhshan*

Agriculture Productivity Job Creation

Fruit Nursery Project

In Faizabad and Baharak districts of Badakhshan province, seven beneficiaries received training on grafting. An additional 20 farmers in Baharak, Shuhada and Warduj districts were trained on how to prepare compost.

Orchard Establishment Project

In Nahrin, Burka and Bano districts of Baghlan, 58 farmers were trained on orchard and nursery irrigation systems and compost preparation.

Commercial Vegetable Cultivation

The commercial cauliflower harvest has been completed; yield data is forthcoming. Currently, one farmer is piloting cauliflower in low plastic greenhouses that will be harvested mid-winter in Takhar.

System of Rice Intensification (SRI)

During the reporting period, the SRI project was completed. Under this project, a total of 42 lead farmers established demonstration plots on 1,423 jeribs in Kishem district. IDEA-NEW undertook this project to address declining rice productivity experienced by farmers using traditional wet paddy production methods. IDEA-NEW trained farmers in the SRI method, which uses fewer seeds and less water, but more labor, to increase rice yields. SRI is particularly appropriate for smallholders like our Badakhshan beneficiaries, who cannot afford to spend money on extra seed or fertilizer to increase yield, but have plenty of household labor. The 42 lead farmers received weeders, land markers and animal manure for fertilizer. Beneficiaries received comprehensive technical training and the lead farmer plots were also used to hold trainings for indirect beneficiaries in the area. Yield data is forthcoming.

Timber Production:

Some 39 individual wooden timber farmers in Badakhshan were trained on bending and packaging wooden timber cuttings for the next season. Farmers were also trained on using animal manure, and compost preparation and application.

Strawberry Runners Project:

This project in Takhar is completed and the five beneficiaries have covered the plants to protect them over the winter. Farmers who planted the strawberries have not commented very positively about continuing or expanding the planting of this crop. The plants did not produce as many strawberries as the farmers hoped, and therefore they did not generate as much income as other crops would on the same land. For next year, farmers will probably switch to another commercial crop that is a more efficient producer.

Women's Poultry Project

Badakhshan: In the completed women's poultry project, a sample of 10 women from the initial group of 120 women in Badakhshan found the project to be a strong income generator. Several indicators point to the sustainability of this



Photo: A farmer with his rice crop in Kishem, Bakakhshan



Photo: Farmers learning how to prepare compost, Baharak, Badakhshan

project—most of the women have more than 40 chickens, indicating that they purchased more birds once they recognized the good income generation opportunities from the project.

Key elements of the training such as disease control and feed blending ensure that egg production is maximized (compared to raising local variety chickens or just feeding them kitchen scraps). Also, this project has quite substantial start-up costs for the women because they have to build the coop, (anecdotally about 10,000Afs (\$222). Yield data from the sample of 10 beneficiaries tells us women with an average of 60 pullets that over the 10 months of the project produced on average 6,840 eggs, which generated revenue of 34,200Afs. Accounting for feed costs, the women made about 28,600 (\$636) profit or 18,600 (\$413) accounting for the 10,000Afs cost of building the coop. Of course, the families probably consumed some of the eggs, so these figures are just representative of possible income.

Beekeeping

In the beekeeping project, price data for the first batch of 79 beekeepers in Badakhshan suggests healthy profits. On average, farmers surveyed had 5 beehives (no contribution for the hives or kits), produced an average of 214kg of honey which generated average revenue of 74,917Afs (\$1,664) over the past year. After expenses due to the cooperative (about 7,280Afs), farmers take home 67,638Afs or \$1,503. A kilo of honey sells for about 350Afs (less 20Afs if farmer sells through the cooperative).

Lamb and Calf Fattening Project:

This project, conducted in Takhar, is now complete. Livestock staff worked with 200 families and 1,000 one to two year old calves in Bangi and Baharak. Prior to the project intervention, the beneficiaries had very little knowledge technical issues such as feeding and veterinary care. The project distributed 150kg of balanced feed per participant three times and calves gained an average of 40.96kg over 90 days. VFUs also vaccinated and dewormed the calves, and farmers were taught the benefits of paying for regular veterinary care.

A follow up training was conducted in Baghlan for the lamb fattening project by our Livestock Officers in 7 CDCs of 4 districts (Puli Khumri, Dushi, Burka and Nahrin) during which the lamb owners were received training on feeding, hygiene and veterinary care. Paravets have raised the awareness of livestock owners about importance of good feeding, hygiene and maintaining good relationship with their local clinics.

Feed and Veterinary Support for Milch Animals:

Badakhshan: 460 animals belonging to 250 beneficiaries were vaccinated against Black Quarter Disease by paravets under supervision of Livestock Officers in 15 villages of Kishem district. This vaccine helps to increase the resistance of milch (ie, milk-producing) animals to bacterial disease. 20,700 kg animal feed was distributed to these beneficiaries in Kishem District market through the IDEA-NEW voucher system on a cost-contribution basis. Beneficiaries with two cows received 90 kg; owners of one cow received 45kg. An additional 340 animals belonging to 210 beneficiaries were also vaccinated against Foot and Mouth Disease and de-wormed by paravets.



Photo: Kickoff ceremony for the new Shori super passage in Farkhar, Takhar



Photo: Handover ceremony for the Khuja Muktar canal intake in Taloqan, Takhar



Photo: Extra large cucumber from the commercial vegetable project in Baghlan.

USG & GIRoA Coordination

Takhar staff attended the PDC (Provincial Development Committee) Meeting, hosted by the governor of Takhar, Abd. Jabar Taqwa. Representatives from all NGOs in Takhar were in attendance and discussed new projects and opportunities for coordination.

In Farkhar, Takhar, the newly started Shori Super Passage project was inaugurated with the Takhar governor, head of provincial council, water management director and heads of local Shoras in attendance. In Taloqan, Takhar, the Khuja Mukhtar canal was handed over to local authorities. Present were representatives and directors from all MAIL offices in Takhar province, as well as the Director of the Water Management Department, related infrastructure sector directors, head of the Takhar provincial council, heads of five local Shuras and village elders. In Baghlan, staff held a meeting with the provincial governor to discuss the Karkar gabion project and local flood control measures.

Community mobilization staff met with Zaman Khail CDC in Baghlan to discuss with the community plans for upcoming projects in the area.

Afghan First

Locally purchased materials for IDEA-NEW Northeast were \$115,842.36 in the reporting period.

Constraints

Security continues to make monitoring challenging. We currently have no way to independently monitor our projects in Burka, Nahrin and Khost districts in Baghlan.



Photo: Feed distribution through the voucher system in Kishem, Badakhshan



Photo: Cauliflower pilot plots are monitored in Puli Khumri, Baghlan

Voices from the Field

Beneficiary Name: [REDACTED], 36

Project Name: Women's Poultry

From (CDC/District): Argo, Badakhshan

1. What kinds of things did you learn in the poultry training?


"We learned many things through this training such as vaccinations, treatment of disease, mixing feed and cleaning coops."

2. What do you plan to do with the extra income from selling eggs?

"Every day we are purchasing goods for the home like sugar, tea and bread with the money. We want MC to continue to support us and extend the training."

3. Will you plan to continue raising chickens in the future?

"Yes actually I have planned with my husband for us to increase our flock to 200 chickens. We will build a bigger coop and maybe try to raise some birds from chicks. This is a good way to make money and it does not require that much extra work."



Biweekly Monitoring & Evaluation Data

Performance Indicators

Outputs are tracked through 25 Performance Indicators. Regional implementing partners use the same forms to capture data, and it is reported into a central database. Depending on the indicator, results are reported on a biweekly, quarterly or annual frequency. There are 16 biweekly indicators, seven quarterly indicators and two annual indicators. The tables below give the results for the reporting period by partner as well as by the program as a whole, and are charted against “targets” by Fiscal Year.

Impact Evaluation

Output indicators by themselves are not a basis for rigorous performance measurement; IDEA-NEW also conducts impact evaluation for some of its largest projects. With the flexibility to conduct specific impact assessment at regular intervals, this plan serves to measure program effectiveness and give management the right information to make better-informed decisions about IDEA-NEW’s work, as well as give USAID Afghanistan a clear picture of IDEA-NEW’s outcomes and impacts over the life of its project.

The project also conducted a baseline household study in July 2009, and will follow up at intervals to assess household impacts in areas where IDEA-NEW is working. This will be done on a biennial basis, and will include those items measured in the household economic baseline. The baseline report, which gives a full economic picture of households in provinces where it was implemented, is available by request.

Field Missions

Finally, Field Missions are undertaken to provide contextual information, as well as quality assurance/quality control. On infrastructure projects, engineers assess construction quality and project progress, and laborers are asked if their wages are paid in a fair and transparent way. For non-infrastructure, overall quality, transparency and effectiveness are assessed. All field missions are conducted to inform program managers about areas of improvement. All missions also review environmental compliance with USAID, and ensure that GPS grid points for projects are captured. For irrigation and road projects, the areas irrigated and length of road are captured to ensure the highest accuracy for performance indicators. Approximately six to eight missions are conducted weekly.

Some explanations on indicators

All definitions and data collection methods for all indicators below are available at request. Some answers to common questions:

1. Full-time equivalent (FTE) jobs: These are calculated in two ways. For CCI projects, 260 labor days = 1 FTE. For agriculture projects, .25 ha under licit cultivation = 1 FTE. For enterprises, a new employee reported by an IDEA-NEW assisted business to be “full time” = 1 FTE. Existing employees at the start of IDEA-NEW intervention does not count. There is a one-month lag time for CCI wage reporting.

2. Increased sales of licit farm- and non-farm products are tracked in different ways. Farm product sales are tracked through surveys of key agricultural interventions programs involving 10,000 people or more. Non-farm products are tracked through bi-annual sales reports from assisted enterprises; only increases over the baseline are reported.
3. All data reported to USAID has “back-up” documentation, including training sign-in sheets, contracts, export documentation and enterprise forms that detail sales and employee information.

ANNEX I: Performance Indicator Table

November 15-30, 2010

MC/ IDEA-NEW Reporting Period: Nov 16 - Nov 30, 2010

Sr. No	PERFORMANCE INDICATORS	Added this period		MC Total to Date	LOP Targets		MC Targets By Fiscal Year				MC Achievements By Fiscal Year			MC Achievements By Province				By Gender	
					MC	IDEA-NEW	FY'09	FY'10	FY'11	FY'12	FY'09	FY'10	FY'11	Bdk-shan	Baghlan	Kunduz	Takhar	Male	Female
1	Number of families benefiting directly from USG interventions in Afghanistan	Previous Period	14,136	103,123	75,000	275,000	500	23,000	119,896	79,931	9,175	81,640	12,308	32,221	31,496	3,854	28,525		
		Current Period	7,037											759	702	-	5,576		
		Total of Two periods	21,173											32,980	32,188	3,854	34,101		
2	# of KM of roads rehabilitated or built	Previous Period	-	42	200	500	-	120	46.4	31.0	-	31	12	9	23	-	11		
		Current Period	-											-	-	-			
		Total of Two periods	-											9	23	-	11		
3	# of KM of irrigation system rehabilitated or built	Previous Period	-	5	50	350	-	75	151.2	100.8	-	5	-	1	3	-	1		
		Current Period	-											-	-	-			
		Total of Two periods	-											1	3	-	1		
4	Wages (\$) paid through community constructed infrastructure projects to local community member	Previous Period	108,892	1,688,847	4,000,000	10,000,000	-	1,300,000	1,754,012	1,169,341	-	1,462,758	226,089	632,075	746,478	40,563	238,018	1,588,242	68,892
		Current Period	31,713											-	4,671	-	27,042	31,713	-
		Total of Two periods	140,606											632,075	751,149	40,563	265,060	1,619,955	68,892
5	# of person days of labor on CCI projects by local community members	Previous Period	14,948	242,124	1,000,000	2,600,000	-	288,889	292,335	194,890	-	210,573	31,552	96,903	99,346	5,675	35,791	225,045	12,669
		Current Period	4,410											-	537	-	3,873	4,410	-
		Total of Two periods	19,358											96,903	99,883	5,675	39,664	229,455	12,669
6	# of local community members employed on CCI projects	Previous Period	-	15,423	15,385	30,000	-	5,778	2,210	1,473	-	15,423	-	7,370	4,736	221	3,096	14,447	976
		Current Period	-											-	-	-	-		
		Total of Two periods	-											7,370	4,736	221	3,096	14,447	976
7	# of individuals who have received USG-supported agricultural and livestock productivity training	Previous Period	4,383	42,636	50,000	375,000	202	10,250	17,365	11,576	9,144	23,246	10,246	12,503	6,847	3,800	18,173	40,880	443
		Current Period	1,313											611	702	-	-	1,313	-
		Total of Two periods	5,696											13,114	7,549	3,800	18,173	42,193	443
8	# of persondays of USG-supported agriculture productivity training	Previous Period	3,287	32,115	25,000	125,000	-	20,500	8,682	5,788	-	25,595	6,520	7,051	3,878	1,425	19,105	30,582	877
		Current Period	656											305	351	-	-	656	-
		Total of Two periods	3,943											7,356	4,229	1,425	19,105	31,238	877
9	# of hectares of alternative crops targeted by USG cultivation	Previous Period	-	96	5,000	40,000	350	1,590	2,501	1,667	-	73	23	34	-	-	62		
		Current Period	-											-	-	-			
		Total of Two periods	-											34	-	-	62		
10	# of livestock under increased technology and management	Previous Period	-	114,711	50,000	500,000	66,200	10,200	30,556	20,370	1,709	113,002	-	59,374	40,737	-	14,600		
		Current Period	-											-	-	-			
		Total of Two periods	-											59,374	40,737	-	14,600		
11	Number of individuals receiving agricultural and livestock inputs	Previous Period	208	16,822	30,000	115,000	60	8,650	31,612	21,074	-	15,245	1,577	9,834	4,170	-	2,230	14,985	1,249
		Current Period	588											148	-	440	348	240	
		Total of Two periods	796											9,982	4,170	-	2,670	15,333	1,489
12	# of hectares under improved irrigation in USG assisted areas	Previous Period	-	2,509	5,000	10,000	480	1,090	7,592	5,061	-	2,509	-	251	1,394	-	864		
		Current Period	-											-	-	-			
		Total of Two periods	-											251	1,394	-	864		
13	# of people receiving business and vocational skills training	Previous Period	-	1,392	300	1,000	-	200	2,865	1,910	-	907	485	52	1,169	37	134	518	874
		Current Period	-											-	-	-			
		Total of Two periods	-											52	1,169	37	134	518	874
14	# of person days of business and vocational skills training	Previous Period	975	5,795	3,000	240,000	-	2,000	1,433	955	-	4,431	1,364	137	5,246	111	301	2,039	3,756
		Current Period	-											-	-	-			
		Total of Two periods	975											137	5,246	111	301	2,039	3,756
15	# of government line staff trained	Previous Period	-	308	100	500	-	30	457	304	31	277	-	242	21	17	28	291	17
		Current Period	-											-	-	-			
		Total of Two periods	-											242	21	17	28	291	17
16	# of person days of government line staff trained	Previous Period	-	983	1,000	5,000	-	300	228	152	-	983	-	880	24	30	49	908	75
		Current Period	-											-	-	-			
		Total of Two periods	-											880	24	30	49	908	75

Sr. No	PERFORMANCE INDICATORS	Added this period		MC Total to Date	LOP Targets		MC Targets By Fiscal Year				MC Achievements By Fiscal Year			MC Achievements By Province				By Gender	
					MC	IDEA-NEW	FY'09	FY'10	FY'11	FY'12	FY'09	FY'10	FY'11	Bdk-shan	Baghlan	Kunduz	Takhar	Male	Female
17	# of families directly benefiting from infrastructure projects including roads, market centers, cold chain and storage facilities projects	Previous Period	9,545	41,965	20,000	75,000	300	23,000	67,598	45,066	-	41,965	-	9,590	19,279	-	7,960		
		Current Period	5,136											-	-	5,136			
		Total of Two periods	14,681														9,590		
18	# of farmers under new, licit contracts	Previous Period	-	-	3,000	10,000	50	800	4,959	3,306	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-														-	-	
19	Total \$US value of international exports of targeted agricultural commodities as a result of USG assistance	Previous Period	-	-	800,000	5,000,000	-	100,000	74,000	111,000	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-														-	-	
20	# of off-farm new micro and SMEs receiving IDEA-NEW technical assistance	Previous Period	-	1,020	100	300	10	40	170	113	-	1,020	-	499	241	-	280		
		Current Period	1,020											-	-	-			
		Total of Two periods	1,020														499		
21	# of associations assisted as a result of USG assistance	Previous Period	-	-	80	75	-	30	174	116	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-														-	-	
22	# of full time equivalent jobs created by USG sponsored alternative development or alternative livelihood activities	Previous Period	325	2,123	7,500	5,000	480	4,020	11,495	7,663	-	2,123	-	233	246	5	66	526	24
		Current Period	1,572											-	-	5	486	1,278	294
		Total of Two periods	1,897														956	604	
23	\$ value of direct investment leveraged in local business	Previous Period	-	-	150,000	500,000	5,000	30,000	411,384	617,076	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-														-	-	
24	Increased sales of licit farm and non-farm products in USG-assisted areas over previous year	Previous Period	-	-	0	0	-	25%	0	0	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-														-	-	
25	Increased production of licit farm products in USG-assisted areas over previous year	Previous Period	-	-	0	0	-	-	0	0	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-														-	-	

MC/ IDEA-NEW
Reporting Period: Nov 16 - Nov 30, 2010

Sr. No	PERFORMANCE INDICATORS	Added this period		MC Total to Date	LOP Targets		MC Targets By Fiscal Year				MC Achievements By Fiscal Year			MC Achievements By Province				By Gender	
					MC	IDEA-NEW	FY'09	FY'10	FY'11	FY'12	FY'09	FY'10	FY'11	Bdk-shan	Baghlan	Kunduz	Takhar	Male	Female
1	Number of families benefiting directly from USG interventions in Afghanistan	Previous Period	14,136	103,123	75,000	275,000	500	23,000	119,896	79,931	9,175	81,640	12,308	32,221	31,486	3,854	28,525		
		Current Period	7,037											759	702	-	5,576		
		Total of Two periods	21,173											32,980	32,188	3,854	34,101		
2	# of KM of roads rehabilitated or built	Previous Period	-	42	200	500	-	120	46.4	31.0	-	31	12	9	23	-	11		
		Current Period	-											-	-	-			
		Total of Two periods	-											9	23	-	11		
3	# of KM of irrigation system rehabilitated or built	Previous Period	-	5	50	350	-	75	151.2	100.8	-	5	-	1	3	-	1		
		Current Period	-											-	-	-			
		Total of Two periods	-											1	3	-	1		
4	wages (\$) paid through community constructed infrastructure projects to local community member	Previous Period	108,892	1,688,847	4,000,000	10,000,000	-	1,300,000	1,754,012	1,169,341	-	1,462,758	226,089	632,075	746,478	40,563	238,018	1,588,242	68,892
		Current Period	31,713											-	4,671	-	27,042	31,713	-
		Total of Two periods	140,606											632,075	751,149	40,563	265,060	1,619,955	68,892
5	# of person days of labor on CCI projects by local community members	Previous Period	14,948	242,124	1,000,000	2,600,000	-	288,889	292,335	194,890	-	210,573	31,552	96,903	99,346	5,675	35,791	225,045	12,669
		Current Period	4,410											-	537	-	3,873	4,410	-
		Total of Two periods	19,358											96,903	99,883	5,675	39,664	229,455	12,669
6	# of local community members employed on CCI projects	Previous Period	-	15,423	15,385	30,000	-	5,778	2,210	1,473	-	15,423	-	7,370	4,736	221	3,096	14,447	976
		Current Period	-											-	-	-	-		
		Total of Two periods	-											7,370	4,736	221	3,096	14,447	976
7	# of individuals who have received USG-supported agricultural and livestock productivity training	Previous Period	4,383	42,636	50,000	375,000	202	10,250	17,365	11,576	9,144	23,246	10,246	12,503	6,847	3,800	18,173	40,880	443
		Current Period	1,313											611	702	-	-	1,313	-
		Total of Two periods	5,696											13,114	7,549	3,800	18,173	42,193	443
8	# of persondays of USG-supported agriculture productivity training	Previous Period	3,287	32,115	25,000	125,000	-	20,500	8,682	5,788	-	25,595	6,520	7,051	3,878	1,425	19,105	30,582	877
		Current Period	656											305	351	-	-	656	-
		Total of Two periods	3,943											7,356	4,229	1,425	19,105	31,238	877
9	# of hectares of alternative crops targeted by USG cultivation	Previous Period	-	96	5,000	40,000	350	1,590	2,501	1,667	-	73	23	34	-	-	62		
		Current Period	-											-	-	-			
		Total of Two periods	-											34	-	-	62		
10	# of livestock under increased technology and management	Previous Period	-	114,711	50,000	500,000	66,200	10,200	30,556	20,370	1,709	113,002	-	59,374	40,737	-	14,600		
		Current Period	-											-	-	-			
		Total of Two periods	-											59,374	40,737	-	14,600		
11	Number of individuals receiving agricultural and livestock inputs	Previous Period	208	16,822	30,000	115,000	60	8,650	31,612	21,074	-	15,245	1,577	9,834	4,170	-	2,230	14,985	1,249
		Current Period	588											148	-	440	348	240	
		Total of Two periods	796											9,982	4,170	-	2,670	15,333	1,489
12	# of hectares under improved irrigation in USG assisted areas	Previous Period	-	2,509	5,000	10,000	480	1,090	7,592	5,061	-	2,509	-	251	1,394	-	864		
		Current Period	-											-	-	-			
		Total of Two periods	-											251	1,394	-	864		
13	# of people receiving business and vocational skills training	Previous Period	-	1,392	300	1,000	-	200	2,865	1,910	-	907	485	52	1,169	37	134	518	874
		Current Period	-											-	-	-			
		Total of Two periods	-											52	1,169	37	134	518	874
14	# of person days of business and vocational skills training	Previous Period	975	5,795	3,000	240,000	-	2,000	1,433	955	-	4,431	1,364	137	5,246	111	301	2,039	3,756
		Current Period	-											-	-	-			
		Total of Two periods	975											137	5,246	111	301	2,039	3,756
15	# of government line staff trained	Previous Period	-	308	100	500	-	30	457	304	31	277	-	242	21	17	28	291	17
		Current Period	-											-	-	-			
		Total of Two periods	-											242	21	17	28	291	17
16	# of person days of government line staff trained	Previous Period	-	983	1,000	5,000	-	300	228	152	-	983	-	880	24	30	49	908	75
		Current Period	-											-	-	-			
		Total of Two periods	-											880	24	30	49	908	75

Sr. No	PERFORMANCE INDICATORS	Added this period		MC Total to Date	LOP Targets		MC Targets By Fiscal Year				MC Achievements By Fiscal Year			MC Achievements By Province				By Gender	
		Previous Period	Current Period		MC	IDEA-NEW	FY'09	FY'10	FY'11	FY'12	FY'09	FY'10	FY'11	Bdk-shan	Baghlan	Kunduz	Takhar	Male	Female
17	# of families directly benefiting from infrastructure projects including roads, market centers, cold chain and storage facilities projects	Previous Period	9,545	41,965	20,000	75,000	300	23,000	67,598	45,066	-	41,965	-	9,590	19,279	-	7,960		
		Current Period	5,136											-	-	5,136			
		Total of Two periods	14,681													13,096			
18	# of farmers under new, licit contracts	Previous Period	-	-	3,000	10,000	50	800	4,959	3,306	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-													-			
19	Total \$US value of international exports of targeted agricultural commodities as a result of USG assistance	Previous Period	-	-	800,000	5,000,000	-	100,000	74,000	111,000	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-													-			
20	# of off-farm new micro and SMEs receiving IDEA-NEW technical assistance	Previous Period	-	1,020	100	300	10	40	170	113	-	1,020	-	499	241	-	280		
		Current Period	1,020											-	-	-			
		Total of Two periods	1,020													280			
21	# of associations assisted as a result of USG assistance	Previous Period	-	-	80	75	-	30	174	116	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-													-			
22	# of full time equivalent jobs created by USG sponsored alternative development or alternative livelihood activities	Previous Period	325	2,123	7,500	5,000	480	4,020	11,495	7,663	-	2,123	-	233	246	5	66	526	24
		Current Period	1,572											723	358	5	486	1,278	294
		Total of Two periods	1,897													552	1,804	319	
23	\$ value of direct investment leveraged in local business	Previous Period	-	-	150,000	500,000	5,000	30,000	411,384	617,076	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-													-			
24	Increased sales of licit farm and non-farm products in USG-assisted areas over previous year	Previous Period	-	-	0	0	-	25%	0	0	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-													-			
25	Increased production of licit farm products in USG-assisted areas over previous year	Previous Period	-	-	0	0	-	-	0	0	-	-	-	-	-	-	-	-	-
		Current Period	-											-	-	-			
		Total of Two periods	-													-			

ANNEX II: CCI Project Data by Region

No.	PROJECT NAME	PROJECT CODE	DISTRICT	Nov. 01 to 15, 2010	Nov. 16 to 30, 2010	REMARKS	Hectare irrigated (ha)	Canal length (m)	wall length (m)	Road length (km)	Families benefited	Reservoir capacity (m3)
ANGARHAR PROVINCE												
1	Abezangani Pipe Scheme	CCI-080308	Hesarak	100%		Completed		6500	50		430	70cum
2	Khanjar Karez	CCI-080307	Hesarak	100%		Completed	50	1800	900		104	
3	Ragha Canal Improvement	CCI-080310	Hesarak	52%	54%	Active	200	8500	1913		800	
4	Kodikhil Ziarat Kaly Road	CCI-080410	Shirzad	0%		Pending/ Security						
5	Kodikhil 200 KW MHP	CCI-080412	Shirzad	0%		ending /Secur						
6	Baghicha Road	CCI-080511	Khogyani	20%		Cancelled		880		281	9300	850
7	Darwazagai Canal Improvement	CCI-080512	Khogiani	100%		Completed 9-Nov	33.56	2000	255		205	
8	Nemla Manz Road	CCI-080513	Khogiani	15%		Cancelled	400		300	3000	800	
9	Loghdara Canal Intake Improvement	CCI-080514	Khogiani	100%		Completed 9-Nov	61.9	2000	193		100	
10	Derga village Karez	CCI-080515	Khogyani	100%		Completed Jan-10	300	3820	100		200	210cum
11	Toowda Chena Karez	CCI-080516	Khogyani	100%		Completed Jan 2010		1600				210Cum
12	Baghicha Karez Intake	CCI-080517	Khogyani	100%		Completed March	400	3030	50		300	450Cum
13	Seway Zangal Canal	CCI-080518	Khogyani	100%		Completed Jan-10		5000	486			
14	Bibi Mahro Canal	CCI-080611	Chaparhar	100%		Completed	160	4000	258		600	
15	Kandi Bagh & Hafizan Canal Intake	CCI-o8o612	Chaparhar	85%	90%	Active	1200	14000	1020		1500	
16	Landi Pachir Canal Intake Improvement	CCI-080706	Pachir Wa Agam	100%		Completed Dec-09	94.15		325+26 m Weir		700	
17	Landa Khil Canal Intake	CCI-080707	Pachir wa Agam	100%		Completed	120	12000	300		2000	
18	Landay Canal intake	CCI-080708	Pachir wa Agam	100%		Completed	200	6000	300		450	
19	Yaghiband MHP	CCI-080807	Dehballa	100%		Completed Jan-10	8.16	3500	725		250	
20	Shpola canal Intake improvement	CCI-080808	Dehballa	99%	100%	Active	300	3500	515		1200	
21	Shalizar Canal Improvement	CCI-080905	Rodat	100%		Completed Aug-10	360	100			300	

No.	PROJECT NAME	PROJECT CODE	DISTRICT	Nov. 01 to 15, 2010	Nov. 16 to 30, 2010	REMARKS	Hectare irrigated (ha)	Canal length (m)	wall length (m)	Road length (km)	Families benefited	Reservoir capacity (m3)
22	Sarkho Malakana Kariz Improvement	CCI-081106	Nazian	1%		Newly started	140		800		600	
23	Qasi and Gograni Karez Intake	CCI-081309	Shinwar	100%		Completed Dec-09	184.85	5000	410		820	
24	Landi Basswal girls school boundary wall & toilet	CCI-081405	Momandara	88%	98%	Active			300		800	
25	Lalpur Guldag Road Repair	CCI-081504	Lalpur	100%		Completed				12 Km		
26	Qala Shahi School boundary construction	CCI-082005	Dare Nur	100%		Completed	3.056			140	500	
27	Sarachie Ali Khan School boundary wall implementation	CCI-082105	Behsud	80%	90%	Active	5.643		140		1500	
28	Trili Girls & Boys School Boundary Wall	CCI-082307	Achin	100%		Completed			300 m			
29	Makrana Canal Intake	CCI-082308	Achin	100%		Completed April 2	120	3000	295		200	
30	Mamand Olas Canal	CCI-082309	Achin	94%	98%	Active	360		369		1000	
31	Mamand Tangi Village Bridge	CCI-082310	Achin	84%	86%	Active		2400		120	600 RCC	
32	Marko School Boundary Wall	CCI-081310	Shinwari	98%	99%	Completed		900			800	
33	Baghcha Karez	CCI-081312	Shinwari	100%		Completed	80	330				
34	Daga canal intake improvement project	CCI-081313	Shinwar	20%	25%	Active	240	4000	365		345	
34	Koshtal MHP	CCI-082311	Achin	85%	90%	Active					350	
KUNAR PROVINCE												
35	Salar canal improvemet	CCI-100101	Asadabad	100%		Completed	3500	24000	3400		8500	
36	Marawara Kariz improvement	CCI-100201	Marawara	45%		Stopped due to Sep 26 incident	400	2000	400		3600	
37	KCC Coble Stone Road Improvement	CCI-100701	Shegal	100%		Completed	50		250	0.75	200	
38	Warsak Dag Canal Intake Improvement	CCI-101207	Narang	100%		Completed Dec-09	14.3		140+48 m Weir		1660	
39	Qazi Banda Canal Improvement	CCI-101310	Chowkay	100%		Completed Oct-09	16.07		75		427	
40	Chawki Loi Canal	CCI-101311	Chowkay	100%		Completed	3000	11000	824		700	

No.	PROJECT NAME	PROJECT CODE	DISTRICT	Nov. 01 to 15, 2010	Nov. 16 to 30, 2010	REMARKS	Hectare irrigated (ha)	Canal length (m)	wall length (m)	Road length (km)	Families benefited	Reservoir capacity (m3)
41	Garigal Canal Intake Improvement	CCI-101312	Chowkay	75%		Recently started						
LAGHMAN PROVINCE												
42	Sawati Road imp	CCI-090225	Qarghai	100%		Completed	500		638	10,000	800	
43	Shamangal Nelawat canal improvement	CCI-090127	Mehterlam	48%		Stopped due to increased water	600	8000	414		1500	
44	Nahri Karim Canal Improvement	CCI-090226	Qarghai	70%	73%	Active	2400	14000	200		4250	
45	Farman Khail School Boundary Wall	CCI-090227	Qarghai	1%		Newly Started		780				
46	Ali Khail School Boundary Wall	CCI-090710	Qarghai	1%		Newly Started		550				
47	Ali Khail School Boundary Wall	CCI-090128	Qarghai	1%		Newly Started		227				
NOORISTAN PROVINCE												
48	Malil Mashfa Road	CCI-300805	Nurgram	100%		Completed	400		341	3350	1400	

#	PROJECT NAME	PROJECT CODE	DISTRICT	Cum. Progress Nov 1-15	Cum. Progress Nov 16-30	REMARKS	Target	Target	Target	Target	Target	Target
							Irrigated (ha)	Canal Length (M)	Wall Length (M)	Road Length (Km)	Fam. Benefited	(m3)
25		MC-IDEA-NE-BG-E-025-10	Burka	N/A	N/A	Completed	20	100	100	N/A	60	N/A
26	Aabqul Gabion Protection Wall	MC-IDEA-NE-BG-E-032-10	Baghlan-e-Markazi	100%	100%	Completed	15000	160	160	N/A	4666	N/A
27	Tangi Murch Aqueduct	MC-IDEA-NE-BG-E-027-10	Burka	100%	100%	Completed	300	18	18	N/A	1920	N/A
28	Markaz i Burka Protection Wall	MC-IDEA-NE-BG-E-028-10	Burka	100%	100%	Completed	24	10	N/A	40	240	N/A
29	Markaz i Burka Secondary Road Rehabilitation	MC-IDEA-NE-BG-E-029-10	Burka	85%	100%	Ongoing	N/A	N/A	N/A	3.5	400	N/A
30	Arbab Noor Mohammad Intake construction	MC-IDEA-NE-BG-E-012-10	Burka	75%	83%	Ongoing	180	18	N/A	N/A	366	N/A
31	Tangi Murch Protection Wall Construction Project	MC-IDEA-NE-BG-E-028-10	Burka	100%	100%	Completed	24	10	N/A	40	240	N/A
32	Eraghak Aqueduct Construction Project	MC-IDEA-NE-BG-E-031-10	Khost	10%	35%	Ongoing	N/A	6	N/A	N/A	190	N/A
TAKHAR PROVINCE												
1	Khoja Aroq Canals Wash-Culvert Rehabilitation	MC-IDEA-NE-TK-E-001-09	Taloqan	N/A	N/A	Completed	350	132	150	N/A	4200	N/A
2	Taloqan River Bank Gabion Dykes Construction	MC-IDEA-NE-TK-E-002-09	Taloqan	N/A	N/A	Completed	200	N/A	195	N/A	1400	N/A
3	Yakatal Canal Wash-Culvert	MC-IDEA-NE-TK-E-003-	Taloqan	N/A	N/A	Completed	210	43	120	N/A	2700	N/A
4	Khaja Hafiz Protection Dyke	MC-IDEA-NE-TK-E-005-10	Yangi Qala	99%	100%	Completed	1500	N/A	440	N/A	2500	N/A
5	Nuqra Chashma Canal Intake	MC-IDEA-NE-TK-E-004-10	Kalafgan	100%	100%	Ongoing	210	N/A	260	N/A	300	N/A
6	Khaja Mukhtar Canal Intake	MC-IDEA-NE-TK-E-006-10	Taloqan	100%	100%	Complete	2000	305	260	N/A	2000	N/A
7	Ganjaliabgh Gabion Protection Wall	MC-IDEA-NE-TK-E-007/10	Taloqan	24%	30%	On going	300	N/A	300	N/A	150	N/A
8	Gazan Road and Bridge Construction	MC-IDEA-NE-TK-E-008/10	Chah Aab	22%	28%	On going	3000	N/A	9.2	N/A	2200	N/A
9	Qazaq and Baghak Road and Bridge Construction	MC-IDEA-NE-TK-E-009/10	Taloqan	23%	25%	On going	126	N/A	30	1.7	1250	N/A
10	Shori Super Passage	MC-IDEA-NE-TK-E-010/10	Farkhar	5%	10%	On going	200	N/A	N/A	N/A	1200	N/A
11	Saqawa Canal Intake	MC-IDEA-NE-TK-E-011/10	Bangi	5%	12%	On going	1600	420	1.7	N/A	1000	N/A

25%

	PROJECT NAME	PROJECT CODE	DISTRICT	Nov 01-15, 2010	Nov 16-30, 2010	REMARKS	Hectares irrigated (ha)	Protection wall length (m)	Road length (km)	Families benefited
SARI PUL										
1	Micro-hydropower (MHP),Chaila village, Balkhab, Sari Pul	MHP8200.5/1	Balkhab	88%	88%	13KW				150
2	Micro-hydropower (MHP),Hoosh village, Balkhab, Sari Pul	MHP8200.5/2	Balkhab	88%	88%	40KW				180
3	Micro-hydropower (MHP),Khamshorak village, Balkhab, Sari Pul	MHP8200.5/3	Balkhab	68%	68%	10.4KW				70
4	Micro-hydropower (MHP),Parawshan village, Balkhab, Sari Pul	MHP8200.5/4	Balkhab	95%	95%	24KW				130
5	Micro-hydropower (MHP), Dahna Wa Takhsar village, Balkhab, Sari Pul	MHP8200.5/5	Balkhab	70%	70%	21KW				380
FARYAB										
6	Micro-hydropower (MHP),Badi village, Qaysar, Faryab	MHP8200.5/11	Qaysar	100%	100%	3.5KW				60
7	Micro-hydropower (MHP),Gerd-e-Qala village, Kohistan	MHP8200.5/12	Kohistan	100%	100%	5KW				80
8	Micro-hydropower (MHP),Keen Qul village, Bilchiragh	MHP8200.5/6	Bilchiragh	100%	100%	11KW				200
9	Micro-hydropower (MHP), Anjeerak village, Bilchiragh	MHP8200.5/7	Bilchiragh	100%	100%	12.5KW				180
10	Micro-hydropower (MHP), Khush Gozar village, Bilchiragh	MHP8200.5/8	Bilchiragh	100%	100%	14.1KW				180
11	Micro-hydropower (MHP), Mirzayee #1 village, Bilchiragh	MHP8200.5/9	Bilchiragh	100%	100%	10.2KW				180
12	Micro-hydropower (MHP), Mirzayee #2 village, Bilchiragh	MHP8200.5/10	Bilchiragh	100%	100%	11.6KW				180
13	CCI Road Rehab, Maymana/Bilchiragh	CCI-18-06-FA04	Pashtun Kot and Bilchiragh	100%	100%			76m	52 km	50000
14	Ibrahimabad Micro Hydro Power	8200.5/20	Pashtun Kot	20%	20%	4.4KW				
15	Qalai Niasbeq-Payan MHP	8200.5/19	Pashtun Kot	25%	25%	4.6KW				
16	Qalai Niasbeq-Bala MHP	8200.5/18	Pashtun Kot	26%	26%	10.8KW				
17	Hazara Qala MHP	8200.5/17	Pashtun Kot	31%	31%	11.9KW				
18	Nawabad Beqlarsai MHP	8200.5/16	Pashtun Kot	24%	24%	6.2KW				

	PROJECT NAME	PROJECT CODE	DISTRICT	Nov 01-15, 2010	Nov 16-30, 2010	REMARKS	Hectares irrigated (ha)	Protection wall length (m)	Road length (km)	Families benefited
19	Kata Qala Shora-e-Bazar MHP	8200.5/15	Pashtun Kot	40%	40%	14KW				
20	Kata Qala Shora-e-Madrassa MHP	8200.5/14	Pashtun Kot	17%	17%	16KW				
21	Kata Qala Haji Basir Micro Hydro Power	8200.5/13	Pashtun Kot	21%	21%	7.5KW				
BALKH										
22	CFW Khulm/Tela Gabion Protection Wall	CFW16 14 BL01	Khulm	100%	100%		9600	975m		12000
23	CFW Khulm/Do Darak Retaining Wall	CFW 200102	Khulm	100%	100%		9600	100m		12000
24	Warehouse Road Improvement		Mazar-e-Sharif	100%	100%				0.7km	450
25	Mazar Almond Market PCC Platform	BL007	D1 Mazar	100%	100%	158 Shops				
26	CFW Khulm River Gabion protection Extension	BL003	Khulm	70%	70%		500	550m		500
Jawzjan										
27	Construction of Mardian Water Reservoir	JW001	Mardian	31%	51%	3000000 liter				300 Families

No.	PROJECT NAME	PROJECT CODE	DISTRICT	Progress %	Progress %	Hectares		Protection	Road	Families benefited	Reservoir capacity (m3)
				cumulative Nov. 1-15 , 2010	cumulative Nov. 16-30, 2010	irrigated (ha)	Canal length (m)	wall length (m)	length (km)		
1	DehZangy Payan	CCI 190201	Abkamary	100	100	90	2500	235		300	
2	Dehzangy Bala	CCI 190202	Abkamarty	100	100	240	6000	160		600	
3	Dehzenger	CCI 190203	Abkamary	100	100	50	3500	155		200	
4	Zaemat Canal Improvement			83	85	120	7000	380/65		200	
5	Gudol Canal Protection	CCI 190205	Abkamary	98	98	180	3700	250	Stopped, irrigation purpose	700	
6	Pahlawan Canal Protection	CCI 190206	Abkamary	98	98	160	3500	300	Stopped, irrigation purpose	500	
7	Kham e Abbasi Canal Improvement	CCI 190709	Muqur	95	95	100	3200	150	Stopped, irrigation purpose	300	
8	Tagab e Ismail Canal improvement	CCI 190108	Qala e Now	92	95	120	4200	320	Ongoing	800	
9	Echka Canal improvement	CCI 190716	Muqur	85	85	40	5500	235	Stopped, irrigation purpose	470	
10	Karkeyha MHP (7KW)	CCI 190311	Qades	87	89				Ongoing	80	
11	Sarasyab MHP (4KW)	CCI 190310	Qades	80	83				Ongoing	60	
12	Haje Abdulla MHP (3KW)	CCI 190312	Qades	80	83				Ongoing	80	
13	Deh Breenge (MHP (10KW)	CCI 190321	Qades	80	83				Ongoing	180	
14	Agha MHP (3KW)	CCI 190120	Qala E ow	75	80				Ongoing	110	
15	Talabe Beland MHP (4KW)	CCI 190118	Qala E Now	75	80				Ongoing	130	
16	Kondalam MHP (4KW)	CCI 190114	Qala E Now	80	83				Ongoing	50	
17	Amala MHP (4KW)	CCI 190113	Tagab e Esmail	80	83				Ongoing	80	
18	Arbab Mohammed Canal	CCI 190119	Qala E Now	15	30	250	3500	150	Ongoing	80	
19	Tangy canal Intake improvement	CCI 190717	Muqur	10	10	700	12000	400	Stopped, Security	2500	
20	Badghis W/S Market	CCI 190104	Qala E Now	23	25				Ongoing		
21	Construction skill Training	CCI 190127	Qal E Now	43	45				Ongoing		
22	Qulmali Canal improvement	CCI 190224	Abkamary	35	65	400	5500	372	Ongoing	380	
23	Zergunbad MHP	CCI 190122	Loman	60	75				Ongoing		

No.	PROJECT NAME	PROJECT CODE	DISTRICT	Progress %	Progress %	Hectares		Protection	Road	Families benefited	Reservoir capacity (m3)
				cumulative Nov. 1-15, 2010	cumulative Nov. 16-30, 2010	irrigated (ha)	Canal length (m)	wall length (m)	length (km)		
24	Kondalam Canal	CCI 1902	Tagab e esmail	60	70	450	4500	148		300	
25	Fersetan Canal	CCI 190126	Abkamary	50	62	320	4300	300		300	
26	Zer Gunbad Canal Improvement	CCI 190115	Qala-e-Naw	15	30						

ANNEX III: Farmer Training Summary

Eastern Region: November 16-30, 2010

Nº	Province	Districts	Onion 2/	CPF	TIMER	REVAMP	Orchard Dev Prog. 9/	FIELD Program 10/	Nursery Dev Prog 11/		Nº Farmers		
				Vegetables 6/	Vegetables 7/	Vegetables 8/			Male	Females	Male	Female	Total
1	Nangarhar	Achin											0
2	Nangarhar	Batikot		44		42	15						101
3	Nangarhar	Bedsood				15	12			3			30
4	Nangarhar	Chaparhar		36	20		25	10					91
5	Nangarhar	Dari noor		20	17								37
6	Nangarhar	Dihbala		22	42								64
8	Nangarhar	Ghanikhil	35	19		18	5						77
9	Nangarhar	Goshta		21			10						31
10	Nangarhar	Hissarak		16			9						25
11	Nangarhar	Kama		38		59	8						105
12	Nangarhar	Khogyani		17		32	10						59
13	Nangarhar	Kot					20						20
14	Nangarhar	Kuz Kunar		39	31		18						88
16	Nangarhar	Momandara	21				15	3					39
18	Nangarhar	Pachir Wa Agam		45				4					49
19	Nangarhar	Rodat		46	22		12						80
20	Nangarhar	Sherzad		20			9						29
22	Nangarhar	Surkhrod		24									24
		Sub-total	56	407	132	166	168	17	0	3	0	0	949
23	Kunar	Asad Abad		46		75							121
25	Kunar	Chawky			18		5						23
26	Kunar	Dangan					10						10
27	Kunar	Khas Kunar				19	39						58
28	Kunar	Manogai					6	11					17
29	Kunar	Marawara		41									41
30	Kunar	Narang			20		24						44
32	Kunar	Noorgal		66									66
33	Kunar	Serkaney				18	9						27
34	Kunar	Shegal		48			15						63

		Sub-total	0	201	38	112	108	11	0	0	0	0	470
36	Laghman	Alingar		45	20		4						69
37	Laghman	Alishang		38									38
39	Laghman	Mehtarlam		28	21		4			12			65
40	Laghman	Qarghaee			94	36	6	4					140
		Sub-total	0	111	135	36	14	4	0	12	0	0	312
	Total		56	719	305	314	290	32	0	15	0	0	1,731

ANNEX IV: Biweekly Sales Data

Eastern Region: November 16-30, 2010

Products	Local Market		High Value Market		Export Market		Total weight & Value	
	Kg	\$	Kg	\$	Kg	\$	Kg	\$
Vegetables	70,000	16,320	236	274	0	0	70,236	16,594
Fruits	0	0	0	0	0	0	0	0
Herbs	0	0	0	0	0	0	0	0
Cheese	232.7	767.9	0	0	0	0	232.7	767.9
Masroor Foods	0	1,760	0	0	0	0	0	1,760
Textile	0	1,315	0	0	0	0	0	1,315
Snacks/chips	0	0	0	0	0	0	0	0
Chicks Hatched	0	2,117	0	0	0	0	0	2,117
Packaging Cartoons	0	721	0	0	0	0	0	721
Table Eggs	0	10,659	0	0	0	0	0	10,659
TOTAL	70,232.70	33,659.90	236	274	0	0	70,469	33,933.90
<i>Sales directly facilitated by the project since 15th Nov till 30th Nov 2010</i>							33,933.90	

July 1, 2009 – November 30, 2010

Products	Local Market		High Value Market		Export Market		Total Weight & Value	
	Kg	\$	Kg	\$	Kg	\$	Kg	\$
Vegetables	2,924,600	613,797	30,769	40,715	13,495,000	3,613,759.53	16,450,369.00	4,268,271.53
Fruits	187,386	55,108	6,530	16,461	22,500	22,583	216,416	94,152
Herbs	709	200	0	0	0	0	709	200
Cheese	9,355.60	28,599.80	0	0	0	0	9,355.60	28,599.80
Masroor Foods	0	57,016	0	56,352	0	0	0	113,368
Textile	0	30,659.50	0	0	0	0	0	30,659.50
Snacks	0	20,620	0	4391.9	0	0	0	25,012
Chicks Hatched	0	101,730.80	0	0	0	0	0	101,730.80
Cartoons Riaz	0	18,668	0	0	0	0	0	18,668.00
Table Eggs	0	30,807	0	0	0	0	0	30,807
TOTAL	3,122,051	957,206.10	37,299	117,920	13,517,500	3,636,342.58	16676849.6	4,711,469

Annex V: Non-CCI Project List

IDEA-NEW Non-CCI Project List

Province	District	Village	Section	Activity_Code	Activity_Name	Activity_Type	Implementer_Partner	Start_Date	End_Date	Status	Project_Percentage
Kunar	Chawkay	Kulmanai	Gender and Micro Enterprise (GME)	FP1312001	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	7-Jan-09	30-Jun-11	Stoped	0
Kunar	Asadabad	Dandona	Gender and Micro Enterprise (GME)	FFNP1301005	Fruit Forestry Nursery	Fruit Forestry	IDEA-NEW (DAI)	1-Dec-09	12-Dec-11	Active	70
Kunar	Nurgal	Mia Qala	Gender and Micro Enterprise (GME)	FP1312004	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Kunar	Asadabad	Shahedano Kalala	Gender and Micro Enterprise (GME)	VNP1301020	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	13-Sep-09	13-Sep-11	Active	80
Kunar	Nurgal	Mia Qala	Gender and Micro Enterprise (GME)	FP1312003	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Kunar	Nurgal	Kuz Nurgal	Gender and Micro Enterprise (GME)	CHP1313007	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Kunar	Nurgal	Darai Mazar	Gender and Micro Enterprise (GME)	VNP1313016	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Kunar	Chawkay	Shalotai	Gender and Micro Enterprise (GME)	VNP1312017	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Kunar	Chawkay	Kulmanai	Gender and Micro Enterprise (GME)	FP1312002	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Stoped	0
Kunar	Chawkay	Babor	Gender and Micro Enterprise (GME)	VNP1312018	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Dara-Ghar	Gender and Micro Enterprise (GME)	FP702008	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Daralam	Gender and Micro Enterprise (GME)	CHP0702005	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Qalatak	Gender and Micro Enterprise (GME)	FFNP0702003	Fruit Forestry Nursery	Fruit Forestry	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Sawati	Gender and Micro Enterprise (GME)	CHP0702006	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Dara-Ghar	Gender and Micro Enterprise (GME)	FP702009	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Dara-Ghar	Gender and Micro Enterprise (GME)	FP702007	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Alingar	Aba khel	Gender and Micro Enterprise (GME)	FP703006	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Stoped	0

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Laghman	Alingar	Aba Khil	Gender and Micro Enterprise (GME)	FP703005	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Stoped	0
Laghman	Qarghayi	Sawati	Gender and Micro Enterprise (GME)	FFNP0702004	Fruit Forestry Nursery	Fruit Forestry	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Active	80
Laghman	Mihtarlam	Akhond Kaly	Gender and Micro Enterprise (GME)	VNP0701012	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Mihtarlam	Kanda	Gender and Micro Enterprise (GME)	VNP0701011	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Farmankhil	Gender and Micro Enterprise (GME)	VNP0702014	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Laghman	Mihtarlam	Maidani	Gender and Micro Enterprise (GME)	VNP0701013	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	7-Jan-09	30-Jun-11	Completed	100
Laghman	Qarghayi	Kamalpor	Gender and Micro Enterprise (GME)	VNP0702015	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Bati Kot	Ambar khana	Gender and Micro Enterprise (GME)	FP617013	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Nagharak	Gender and Micro Enterprise (GME)	FP602019	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Khogyani	Kaga	Gender and Micro Enterprise (GME)	FFNP605006	Fruit Forestry Nursery	Fruit Forestry	IDEA-NEW (DAI)	1-Dec-09	30-Dec-11	Active	60
Nangarhar	Surkh Rod	Zulm Abad	Gender and Micro Enterprise (GME)	FP602018	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Kama	Landabuch	Gender and Micro Enterprise (GME)	FP618017	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Kama	Landabuch	Gender and Micro Enterprise (GME)	FP618016	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Kuz Kunar	Now Joy	Gender and Micro Enterprise (GME)	FP619015	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Bati Kot	Shash khel	Gender and Micro Enterprise (GME)	FP617012	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Stoped	0
Nangarhar	Bati Kot	Lachapur	Gender and Micro Enterprise (GME)	CHP617008	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Oct-09	1-Oct-10	Completed	100
Nangarhar	Surkh Rod	Sabz Abad	Gender and Micro Enterprise (GME)	MSP602004	Mintorship Program	Mintorship (Perfume Making)	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Shikhmesry	Gender and Micro Enterprise (GME)	MSP602001	Mintorship program	Mintorship (Wool Weaving)	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Bati Kot	Lachapur	Gender and Micro Enterprise (GME)	VNP617019	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	8-Nov-09	8-Nov-10	Completed	100

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Behsud	Lasma Wiala	Gender and Micro Enterprise (GME)	MSP621005	Mintorship Program	Mintorship (Jam & pickle)	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Bati Kot	Hajyano Kalai	Gender and Micro Enterprise (GME)	FP617011	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Stoped	0
Nangarhar	Bati Kot	Daman	Gender and Micro Enterprise (GME)	FP617010	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Daronta	Gender and Micro Enterprise (GME)	MSP602002	Mintorship program	Mintorship (Sisters Bakery)	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Miran	Gender and Micro Enterprise (GME)	MSP602003	Mintorship Program	Mintorship (Shampoo Making)	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Bati Kot	Ambar khana	Gender and Micro Enterprise (GME)	FP617014	Fish Pond Project	Fish Pond	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Bati Kot	Barikab	Gender and Micro Enterprise (GME)	VNP 617021	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	12-Feb-10	12-Feb-11	Completed	100
Nangarhar	Kuz Kunar	Bazarak	Gender and Micro Enterprise (GME)	VNP0619010	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Kuz Kunar	Khiwa	Gender and Micro Enterprise (GME)	VNP0619009	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Active	85
Nangarhar	Kama	Shergal	Gender and Micro Enterprise (GME)	VNP0618008	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Behsud	Tamirat	Gender and Micro Enterprise (GME)	VNP0621007	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Behsud	Joe 10	Gender and Micro Enterprise (GME)	VNP0621006	Vegetable Nursery program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Behsud	Samarkhil Farm	Gender and Micro Enterprise (GME)	VNP0621005	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Shinwar	Ghanikhil /27 wiala	Gender and Micro Enterprise (GME)	VNP0613004	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Naghrak	Gender and Micro Enterprise (GME)	FFNP0602002	Furit Forestry Nursery	Fruit Forestry	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Behsud	Binega	Gender and Micro Enterprise (GME)	VNP0621002	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Behsud	Khushgunbad	Gender and Micro Enterprise (GME)	VNP0621001	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Behsud	Banda	Gender and Micro Enterprise (GME)	FFNP0621001	Fruit Forestry Nursery	Fruit Forestry	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Fateh Abad	Gender and Micro Enterprise (GME)	CHP0602004	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Kama	Akhund Kalay	Gender and Micro Enterprise (GME)	CHP0618003	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Kuz Kunar	Pachai Qala	Gender and Micro Enterprise (GME)	CHP0619002	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Kuz Kunar	Sheege	Gender and Micro Enterprise (GME)	CHP0619001	Cheese Program	Cheese Program	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Narinj Bagh	Gender and Micro Enterprise (GME)	SPF0602001	Surkhroad Packing Facility	Packing Facility	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Active	90
Nangarhar	Behsud	Samarkhil	Gender and Micro Enterprise (GME)	FSP0621001	Fruit Supplying program	Fruit Supplying	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Active	85
Nangarhar	Behsud	Samarkhil Farm	Gender and Micro Enterprise (GME)	CNP 621001	Citruse Project	Citruse Production	IDEA-NEW (DAI)	1-Mar-10	30-Mar-11	Active	70
Nangarhar	Surkhrod	Naghrak	Gender and Micro Enterprise (GME)	CNP 602002	Citruse Project	Citruse Production	IDEA-NEW (DAI)	1-Mar-10	30-Mar-11	Active	70
Nangarhar	Behsud	Samarkhil	Gender and Micro Enterprise (GME)	CPP 621001	Cotton Project	Cotton production	IDEA-NEW (DAI)	1-Apr-10	1-Oct-10	Active	75
Nangarhar	Bati Kot	Lwoartai	Gender and Micro Enterprise (GME)	VNP0617003	Vegetable Nursery Program	Vegetable Nursery	IDEA-NEW (DAI)	1-Jul-09	30-Jun-11	Completed	100
Nangarhar	Surkh Rod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602001	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602002	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602003	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602004	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602005	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602006	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602007	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602008	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Surkhrod	Hejrat Kalay	Gender and Micro Enterprise (GME)	PLP 602009	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Bati Kot	Janatyano Kalai	Gender and Micro Enterprise (GME)	PLP 617010	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Batikot	Janatyano Kalai	Gender and Micro Enterprise (GME)	PLP 617011	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Batikot	Janatiano Kaly	Gender and Micro Enterprise (GME)	PLP 617012	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Batikot	Farm 4	Gender and Micro Enterprise (GME)	PLP 617013	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Batikot	Farm 4	Gender and Micro Enterprise (GME)	PLP 617014	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Behsud	Qalay Dasht	Gender and Micro Enterprise (GME)	PLP 621015	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Behsud	Khoshgumbat	Gender and Micro Enterprise (GME)	PLP 621016	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Behsud	Qalay Dasht	Gender and Micro Enterprise (GME)	PLP 621017	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Behsud	Qalay Dasht	Gender and Micro Enterprise (GME)	PLP 621018	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Behsud	Qalay Dasht	Gender and Micro Enterprise (GME)	PLP 621019	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Behsud	Qalay Dasht	Gender and Micro Enterprise (GME)	PLP 621020	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Behsud	Qalay Dasht	Gender and Micro Enterprise (GME)	PLP 621021	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Kuz Kunar	Sheege	Gender and Micro Enterprise (GME)	PLP 619022	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Kuz kuner	Sheege	Gender and Micro Enterprise (GME)	PLP 619023	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Kuz kuner	Dagiano Kaly	Gender and Micro Enterprise (GME)	PLP 619024	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Kuz kuner	Dagiano Kaly	Gender and Micro Enterprise (GME)	PLP 619025	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Kuz kuner	Dagiano Kaly	Gender and Micro Enterprise (GME)	PLP 619026	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Mihtarlam	Badybiad	Gender and Micro Enterprise (GME)	PLP 701034	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Mihtarlam	Badybiad	Gender and Micro Enterprise (GME)	PLP 701035	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Mehtarlam	Badybiad	Gender and Micro Enterprise (GME)	PLP 701036	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Laghman	Mehtarlam	Badybiad	Gender and Micro Enterprise (GME)	PLP 701037	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Mehtarlam	Badybiad	Gender and Micro Enterprise (GME)	PLP 701038	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Mehtarlam	Badybiad	Gender and Micro Enterprise (GME)	PLP 701039	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Qarghayi	Kanda	Gender and Micro Enterprise (GME)	PLP 701040	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Qarghayi	kanda	Gender and Micro Enterprise (GME)	PLP 701041	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Laghman	Qarghayi	kanda	Gender and Micro Enterprise (GME)	PLP 701042	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Kunar	Asad Abad	Assad Abad	Gender and Micro Enterprise (GME)	PLP 1301043	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Kunar	Asad Abad	Assad Abad	Gender and Micro Enterprise (GME)	PLP 1301046	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	60
Kunar	Asad Abad	Assad Abad	Gender and Micro Enterprise (GME)	PLP 1301047	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Kunar	Assad Abad	Assad Abad	Gender and Micro Enterprise (GME)	PLP 1301044	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	60
Kunar	Assad Abad	Assad Abad	Gender and Micro Enterprise (GME)	PLP 1301045	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Sawkai	Shalutai	Gender and Micro Enterprise (GME)	PLP 1312048	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Sawkai	Shalutai	Gender and Micro Enterprise (GME)	PLP 1312049	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Khogyani	Kaga	Gender and Micro Enterprise (GME)	PLP 605027	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Stoped	0
Nangarhar	Khogianee	Khankhil	Gender and Micro Enterprise (GME)	PLP 605028	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Khogianee	Smasee	Gender and Micro Enterprise (GME)	PLP 605029	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Khogianee	Smasee	Gender and Micro Enterprise (GME)	PLP 605030	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Khogianee	Smasee	Gender and Micro Enterprise (GME)	PLP 605031	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Stoped	0
Nangarhar	Sawkai	Sawkai	Gender and Micro Enterprise (GME)	PLP 1312050	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Rodat	Farm 4	Gender and Micro Enterprise (GME)	HELT609001	Handicraft, Embroidery and literacy training	Handicraft	IDEA-NEW (DAI)	1-Sep-09	28-Feb-10	Completed	100
Nangarhar	Jalalabad	Jalalabad	Gender and Micro Enterprise (GME)	TOT601001	TARAQI SABA TOT	TOT	IDEA-NEW (DAI)	17-Jul-10	30-Aug-10	Active	80
Nangarhar	Bihsud	Joy 11	Gender and Micro Enterprise (GME)	PLP 621032	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Bihsud	Joy 11	Gender and Micro Enterprise (GME)	PLP 621033	Poultry Project	Layer	IDEA-NEW (DAI)	20-Mar-10	30-Mar-11	Active	90
Nangarhar	Kama	Gooj	Gender and Micro Enterprise (GME)	KGP 618001	Kitchen Garden	kitchen Garden	IDEA-NEW (DAI)	1-Oct-10	30-Oct-11	Active	75
Nangarhar	Bihsud	Zangoyee	Gender and Micro Enterprise (GME)	KGP 621002	Kitchen Garden	kitchen Garden	IDEA-NEW (DAI)	1-Oct-10	30-Oct-11	Active	75
Nangarhar	Batikot	Barikab	Gender and Micro Enterprise (GME)	KGP 617003	Kitchen Garden	kitchen Garden	IDEA-NEW (DAI)	1-Oct-10	30-Oct-11	Active	75
Nangarhar	Pachir wa Agam	Saber	Gender and Micro Enterprise (GME)	KGP 607004	Kitchen Garden	kitchen Garden	IDEA-NEW (DAI)	1-Oct-10	30-Oct-11	Active	75
Nangarhar	Pachir wa Agam	Dara	Gender and Micro Enterprise (GME)	KGP 607006	Kitchen Garden	kitchen Garden	IDEA-NEW (DAI)	1-Oct-10	30-Oct-11	Active	75
Laghman	Mihtarlam	Chardehy/ Abdul Wahb Qala	Gender and Micro Enterprise (GME)	KGP 701005	Kitchen Garden	kitchen Garden	IDEA-NEW (DAI)	1-Oct-10	30-Oct-11	Active	75
Laghman	Mihtarlam	Chardehy/ Qala -e-Sefat	Gender and Micro Enterprise (GME)	KGP 701007	Kitchen Garden	kitchen Garden	IDEA-NEW (DAI)	1-Oct-10	30-Oct-11	Active	75
Nangarhar	Shinwar	Faizulah Khan Village	Gender and Micro Enterprise (GME)	SHWP 613001	Clean/drinking water supply(Shall Well)	Shall Well Project	IDEA-NEW (DAI)	21-Jul-10	30-Dec-10	Completed	100
Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementer Partner	Start Date	End Date	Status	Project Percentage
Nangarhar	Behsud	Khoshkonbat	Private Sector Development (PSD)	ZSP-621-007	Zaman Snack production Factory	Enterprise	IDEA-NEW (DAI)	01-Dec-09	19-Mar-10	Completed	100
Nangarhar	Surkh Rod	Ghawchack	Private Sector Development (PSD)	TPJP-602-008	Khalil Rehan Tomato Paste and Jam Factory	Enterprise	IDEA-NEW (DAI)	01-Jan-10	13-Apr-10	Completed	100
Nangarhar	Jalalabad	City	Private Sector Development (PSD)	TAS-601-010	Talc Association	Association	IDEA-NEW (DAI)	13-Jan-10	13-Jan-11	Active	55
Nangarhar	Jalalabad	City	Private Sector Development (PSD)	NIA-601-011	Nangarhar Industry Association	Association	IDEA-NEW (DAI)	10-Jan-10	09-Jan-11	Active	65
Nangarhar	Jalalabad	City	Private Sector Development (PSD)	CAS-601-009	Craftsman Association	Association	IDEA-NEW (DAI)	13-Oct-09	12-Jan-10	Completed	100
Nangarhar	Surkh Rod	Dosaraka	Private Sector Development (PSD)	RPF-602-012	Riaz Packaging Factory	Enterprise	IDEA-NEW (DAI)	01-Nov-09	29-Mar-10	Completed	100

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Jalalabad	city	Private Sector Development (PSD)	FGA-601-001	Fruit Grower Association	Association	IDEA-NEW (DAI)	15-Jul-09	30-Jun-10	Active	90
Nangarhar	Shinwar	Marko	Private Sector Development (PSD)	PF-613-003	Hahji Shamsulhaq Layer Bereder Farm	Poultry Farm	IDEA-NEW (DAI)	16-Aug-09	16-Feb-10	Completed	100
Nangarhar	Jalalabad	Jalalabad city	Private Sector Development (PSD)	PAS-601-004	Poultry Association	Association	IDEA-NEW (DAI)	08-Aug-09	10-Jul-09	Active	55
Nangarhar	Dih Bala	Yaghiband	Private Sector Development (PSD)	RTX-608-005	Rodat Textile weaving factory	Enterprise	IDEA-NEW (DAI)	27-Sep-09	26-Jan-10	Completed	100
Nangarhar	Behsud	Naghlo Joy 10	Private Sector Development (PSD)	ATXD-621-006	Alkozai Textile dying, washing perss center	Enterprise	IDEA-NEW (DAI)	25-Oct-09	25-Oct-11	Active	62
Nangarhar	Behsud	Naghlo Saracha	Private Sector Development (PSD)	PF-621-002	Zamarak broilr Breeder Farm	Poultry Farm	IDEA-NEW (DAI)	01-Oct-09	16-Jun-11	Active	92
Nangarhar	Surkh Rod	New Kabul Bus Station	Private Sector Development (PSD)	WCh-602-013	Wasim Chair Manufacturing Company	Enterprise	IDEA-NEW (DAI)	20-Feb-10	19-May-10	Completed	100
Nangarhar	Jalalabad	Chaknawry	Private Sector Development (PSD)	VNF-601014	Vermicelli & Noodles Factory	Enterprise	IDEA-NEW (DAI)	20-Mar-10	19-Jun-10	Active	52
Nangarhar	Surkh Rod	Dornta	Private Sector Development (PSD)	MSH 602- 015	Mommand Sehat Hatchery	Hatchery	IDEA-NEW (DAI)	06-Mar-10	05-Aug-10	Completed	100
Nangarhar	Jalalabad	City	Private Sector Development (PSD)	FCF-601-016	Fresh & Packages Cakes Factory	Enterprise	IDEA-NEW (DAI)	01-Apr-10	31-Aug-10	Approve	12
Nangarhar	Surkh Rod	Sabzabad	Private Sector Development (PSD)	BBF 602 017	Baryalai Bicycles Factory	Enterprise	IDEA-NEW (DAI)	01-Apr-10	31-Jul-10	Active	21
Nangarhar	Jalalabad	Bez Ekmalaty	Private Sector Development (PSD)	YCC-601-018	Yashfeen Confectionery Factory	Enterprise	IDEA-NEW (DAI)	20-Apr-10	20-Jun-10	Completed	100
Nangarhar	Jalalabad	Jalalabad	Private Sector Development (PSD)	ZRMC-601-019	ZRM Carpet Weaving Company	Enterprise	IDEA-NEW (DAI)	01-Jul-10	31-Dec-10	Active	55
Nangarhar	Kama	Sher Gar	Private Sector Development (PSD)	PF-618-020	M.Ishaq Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	29-Apr-10	31-Dec-12	Active	79
Nangarhar	Kama	Mirzakhil	Private Sector Development (PSD)	PF-618-021	Bakhtyar poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	29-Apr-10	31-Dec-11	Active	79
Nangarhar	Kama	Zar Shoi	Private Sector Development (PSD)	PF-618-022	Murad khan Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	29-Apr-10	31-Dec-11	Active	79
Nangarhar	Kama	Landa boch	Private Sector Development (PSD)	PF-618-023	Sadat Poultry Farm	Layer poultry Farm	IDEA-NEW (DAI)	29-Apr-10	31-Dec-11	Active	79
Nangarhar	Kama	Zar shoi	Private Sector Development (PSD)	PF-618-024	Naseeb Gul Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	29-Apr-10	31-Dec-10	Active	79
Nangarhar	Muhmand Dara	Khan Abad	Private Sector Development (PSD)	PF-614-025	Ekhtyar Ahmad Poultry Farm	Layer poultry Farm	IDEA-NEW (DAI)	29-Apr-10	31-Dec-11	Active	79

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Muhmand Dara	Alijan guly	Private Sector Development (PSD)	PF-614-026	Feroz Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	15-Apr-10	31-Dec-11	Active	79
Nangarhar	Muhmand Dara	Sultan khil	Private Sector Development (PSD)	PF-614-027	Zabet khan Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	15-Apr-10	31-Dec-11	Active	79
Nangarhar	Muhmand Dara	Khan Abad	Private Sector Development (PSD)	PF-614-028	Abdul Wali Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	15-Apr-10	31-Dec-11	Active	79
Nangarhar	Bati Kot	Nawi Lakhti	Private Sector Development (PSD)	PF-617-029	Haji Nader Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	15-Apr-10	31-Dec-11	Active	79
Nangarhar	Bati Kot	Ambr Khan Ali khan Khil	Private Sector Development (PSD)	PF-617-030	Hayatullah Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	14-Apr-10	31-Dec-11	Active	79
Nangarhar	Bati Kot	Daman	Private Sector Development (PSD)	PF-617-031	M. Arif Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	15-Apr-10	31-Dec-11	Active	79
Nangarhar	Bati Kot	Haji Anu Kaly	Private Sector Development (PSD)	PF-617-032	Samiullah Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	15-Apr-10	31-Dec-11	Active	79
Nangarhar	Bati Kot	Paraw	Private Sector Development (PSD)	PF-617-033	Javid Poultry Farm	Layer poultry Farm	IDEA-NEW (DAI)	15-Apr-10	31-Dec-11	Active	79
Nangarhar	Bati Kot	Qala wal	Private Sector Development (PSD)	PF-617-034	Farhad Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	14-Apr-10	31-Dec-11	Active	79
Kunar	Asadabad	Lahurdag	Private Sector Development (PSD)	PF-1301-035	M. Khalid Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	21-Apr-10	31-Dec-11	Active	79
Kunar	Asadabad	Dam Kaly	Private Sector Development (PSD)	PF-1301-036	muhibullah poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	21-Apr-10	31-Dec-11	Active	79
Kunar	Wata Pur	Omer Abad	Private Sector Development (PSD)	PF-1308-037	Isamuddin Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	21-Apr-10	31-Dec-11	Active	79
Kunar	Shegal	Mora	Private Sector Development (PSD)	PF-1307-038	Abdullah Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	21-Apr-10	31-Dec-10	Active	79
Kunar	Nurgal	Mia Qala	Private Sector Development (PSD)	PF-1313-039	Farid Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	21-Apr-10	31-Dec-11	Active	79
Laghman	Alingar	Sakhra	Private Sector Development (PSD)	PF-705-040	DR MoD-32974habt Poultry Farm	Layer Poultry	IDEA-NEW (DAI)	20-Apr-10	31-Dec-11	Active	79
Laghman	Alingar	Parwai	Private Sector Development (PSD)	PF-705-041	Najeebullah Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	20-Apr-10	31-Dec-11	Active	79
Laghman	Alingar	Lajugar	Private Sector Development (PSD)	PF-705-042	Sayeed Mahmud Poultry Farm	Layer Poultry	IDEA-NEW (DAI)	20-Apr-10	31-Dec-11	Active	79
Laghman	Mihtarlam	Harmal	Private Sector Development (PSD)	PF-01-043	Babrak Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	20-Apr-10	31-Dec-11	Active	79
Laghman	Alingar	Sakhra	Private Sector Development (PSD)	PF-705-044	Ezatullah Poultry Farm	Layer Poultry Farm	IDEA-NEW (DAI)	20-Apr-10	31-Dec-11	Active	79

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Dara-I-Noor	Qali Shahi	Private Sector Development (PSD)	DTX-620-046	Dara-i-Noor Textile	Enterprise	IDEA-NEW (DAI)	20-Mar-10	20-Jul-10	Completed	100
Nangarhar	Dara-I-Noor	Qali Shahi	Private Sector Development (PSD)	DCH-620-047	Dara-i-Noor Chalk Factory	Enterprise	IDEA-NEW (DAI)	04-May-10	04-Jul-10	Completed	100
Nangarhar	Achin	Koshtal	Private Sector Development (PSD)	SJP-610-0048	Watan Dost Joinery Program	Enterprise	IDEA-NEW (DAI)	01-Jul-10	31-Aug-10	Approve	27
Nangarhar	Achin	Koshtal	Private Sector Development (PSD)	SJP-610-049	Toti Gul Joinery Program	Enterprise	IDEA-NEW (DAI)	01-Jul-10	31-Aug-10	Cancelled	100
Nangarhar	Behsud	Dubila	Private Sector Development (PSD)	WSF621-050	Wahid Soap Factory	Soap production	IDEA-NEW (DAI)	01-Jul-10	30-Oct-10	Approve	16
Nangarhar	Jalalabad	Zoon 2	Private Sector Development (PSD)	SHPP601-051	Season Honey processing and packaging Factory	Hoeny processing	IDEA-NEW (DAI)	20-Jun-10	20-Aug-10	Approve	55
Laghman	Surkh Rod	Dosaraka	Private Sector Development (PSD)	AMF602-052	Aryan Marble Factory	Marble processing	IDEA-NEW (DAI)	01-Sep-10	01-Aug-11	Approve	25
Nangarhar	Sherzad	Kodikhil	Private Sector Development (PSD)	LMF605-053	Lajbar Marble Factory	Marble processing	IDEA-NEW (DAI)	01-Sep-10	01-Aug-11	Approve	20
Nangarhar	Jalalabad	City	Private Sector Development (PSD)	HAS601-054	Happy Afghanistan Sports	produce Sports tools	IDEA-NEW (DAI)	20-Mar-10	20-May-10	Approve	20
Nangarhar	Jalalabad	City	Private Sector Development (PSD)	ARDF601-055	Ajmal Rahmani Dry Furit processing Company	Dry Furit processing	IDEA-NEW (DAI)	01-Jun-10	30-Sep-10	Approve	20
Nangarhar	Jalalabad	City	Private Sector Development (PSD)	FDC-601-057	Homayoon Fiber Distrbution	Distrbution of fiber	IDEA-NEW (DAI)	03-Dec-09	02-Dec-10	Active	62
Nangarhar	Jalalabad	Charahi Marston	Private Sector Development (PSD)	FTL 601 058	Food Testing Labratroy	Testing of Foods	IDEA-NEW (DAI)	15-Aug-10	30-Sep-10	Approve	12
Nangarhar	Kama	kandi	Private Sector Development (PSD)	STWF-618-059	Sadam Textile Weaving Company	Textile weaving	IDEA-NEW (DAI)	01-Oct-10	31-Dec-10	Approve	42
Nangarhar	Dara-I-Noor	Qali Shahi	Private Sector Development (PSD)	DPCF-620-060	Dara-I-Noor potatoes chips factory	Enterprise	IDEA-NEW (DAI)	01-Jul-10	30-Sep-10	Completed	100
Nangarhar	Jalalabad	Chknowry	Private Sector Development (PSD)	SCP 601-062	Sahill Chips Factory	Enterprise Chips Production Factory	IDEA-NEW (DAI)	01-May-10	01-Jun-10	Active	100
Nangarhar	Rodat	Mirano Kaly	Private Sector Development (PSD)	ETX 609-063	Ebadullah Textile Factory	Enterpris	IDEA-NEW (DAI)	01-Jul-10	31-Dec-10	Active	50
Nangarhar	Rodat	Mirano Kaly	Private Sector Development (PSD)	TTXF 609-064	Tahsel Textile Factory	Enterprise	IDEA-NEW (DAI)	01-Jul-10	31-Dec-10	Active	50
Nangarhar	Rodat	Mirano Kaly	Private Sector Development (PSD)	ZTXF 609-065	Ziarat Gul Textile Factory	Enterprise	IDEA-NEW (DAI)	01-Jul-10	30-Dec-10	Active	50
Nangarhar	Rodat	Mirano Kaly	Private Sector Development (PSD)	TTXF 609-066	Toor Textile Factory	Enterprise	IDEA-NEW (DAI)	01-Jul-10	30-Dec-10	Active	50

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Rodat	Sharasol Village	Private Sector Development (PSD)	HPF 609-067	Haider broiler Farm	Poultry	IDEA-NEW (DAI)	08-Sep-10	08-Nov-10	Active	55
Nangarhar	Rodat	Baro Soor dag	Private Sector Development (PSD)	ShPF 609-068	Sharifullah Broiler Farm	Poultry Farm	IDEA-NEW (DAI)	08-Sep-10	08-Nov-10	Active	55
Nangarhar	Rodat	Bazar	Private Sector Development (PSD)	SHBF 609-069	Shamsrurahman Broiler Farm	poultry	IDEA-NEW (DAI)	23-Oct-10	23-Dec-10	Active	55
Nangarhar	Behsud	Khalis Family	Private Sector Development (PSD)	RBF 621-070	Rahimullah	Poultry	IDEA-NEW (DAI)	19-Oct-10	19-Dec-10	Active	55
Nangarhar	Surkh Rod	Shamsha Poor	Private Sector Development (PSD)	MBF 602-071	Mohammad Alam	Poultry	IDEA-NEW (DAI)	08-Sep-10	08-Nov-10	Active	55
Nangarhar	Muhmand Dara	27 Weala	Private Sector Development (PSD)	ABF-614-072	AzizuRahman Broiler Farm	Poultry Farm	IDEA-NEW (DAI)	09-Aug-10	11-Aug-10	Active	55
Nangarhar	Bati Kot	Nabora Ghundi	Private Sector Development (PSD)	RBF-617-073	Raees Broiler Farm	Poultry Farm	IDEA-NEW (DAI)	09-Aug-10	11-Aug-10	Active	55
Nangarhar	Bati Kot	Farm-e-3	Private Sector Development (PSD)	ZBF-617-074	Zeenatullah Broiler Farm	Poultry Farm	IDEA-NEW (DAI)	09-Sep-10	11-Aug-10	Active	55
Laghman	Mihtarlam	Chelmati	Private Sector Development (PSD)	ZBF-701-075	Zmary Broiler Farm	Poultry Farm	IDEA-NEW (DAI)	08-Oct-10	08-Dec-10	Active	55
Nangarhar	Chaparhar	Dawlat Zai family	Private Sector Development (PSD)	SBF-606-076	Sarajuddin Broiler Farm	Poultry Farm	IDEA-NEW (DAI)	20-Sep-10	20-Nov-10	Active	55
Nangarhar	Behsud	Kariz Kabir	Private Sector Development (PSD)	EBF-621-077	EmamJan	Poultry Farm	IDEA-NEW (DAI)	08-Oct-10	08-Dec-10	Active	55
PROVINCE	DISTRICT_NAME	Project_Village	Infrastructure	Project_ExternalCode	Project_Title	Activity_Type	Implementor	Est_Start_Date	Est_End_Date	Project_Status	Project_Percentage
Badghis	Abqamare	Dehjangay	Infrastructure	CCI200101	Dezangay Canal Protection Works	Irrigation	IDEA-NEW (DAI)	1-Aug-09	30-Dec-09	Completed	100
Badghis	Abqamare	Dehjangay Bala	Infrastructure	CCI200102	Dezangay bala Canal Protection Works	Irrigation	IDEA-NEW (DAI)	1-Aug-09	30-Dec-09	Completed	100
Badghis	Abqamare	Gadul	Infrastructure	CCI190205	Godul Canal Protection	Irrigation	IDEA-NEW (DAI)	16-Feb-10	20-May-10	Active	53
Badghis	Abqamare	Pahlawan	Infrastructure	CCI190206	Pahlawan Canal Protection	Irrigation	IDEA-NEW (DAI)	16-Feb-10	20-May-10	Active	50
Badghis	Abqamare	Tagab-e-Esmail	Infrastructure	CCI190208	Tagab-e-Esmail Canal Improvement	Irrigation	IDEA-NEW (DAI)	16-Feb-10	20-May-10	Active	25
Badghis	Abqamare	Zaimat	Infrastructure	CCI190207	Zaimat Canal Improvement	Irrigation	IDEA-NEW (DAI)	16-Feb-10	20-May-10	Active	35
Badghis	Abqamare	Zengar	Infrastructure	CCI200103	Zengar flood Protection Works	Irrigation	IDEA-NEW (DAI)	1-Aug-09	30-Dec-09	Completed	100
Badghis	Muqur		Infrastructure	CCI190709	Kham e Abassi Canal Improvement	Irrigation	IDEA-NEW (DAI)	16-Feb-10	20-May-10	Active	17

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Kunar	Asadabad	Villages: Stigal, Doshakhal, Gor Gom, Dam, Yargul, Sarai, Tesha, Nawabad, Dandona, Lachigale, Bar Narang, Lamadak Villages.	Infrastructure	CCI100101	Salar Canal Improvement	Irrigation	IDEA-NEW (DAI)	1-Nov-09	1-Feb-10	Active	80
Kunar	Chawkay		Infrastructure	CCI101312	Garigal Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)			Active	15
Kunar	Chawkay	Chawkai,	Infrastructure	CCI101311	Chawkai Canal Improvement	Irrigation	IDEA-NEW (DAI)	1-Dec-09	15-Feb-09	Active	70
Kunar	Chawkay	Qazi Banda, Shalamyar, Gojrano and Pandano	Infrastructure	CCI101310	Qazi Banda Canal Improvement	Irrigation	IDEA-NEW (DAI)	13-Jul-09	5-Sep-09	Completed	100
Kunar	Narang	Qalawoona, Kotgi, Andargosh, Pas Ghondi, Ghondi	Infrastructure	CCI101207	Warsak Dag Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	14-Jul-09	26-Oct-09	Completed	100
Kunar	Shegal	Shegal kalay	Infrastructure	CCI100701	KCC Cobblestone Road Improvement	Road	IDEA-NEW (DAI)	16-Jan-10	1-Apr-10	Active	75
Laghman	Mihtarlam	Shamangale village	Infrastructure	CCI090127	Shamangal Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	1-Mar-10	1-Jun-10	Active	45
Laghman	Qarghayi	Demazang, Ghulam Sulatan, Hasham kala, Ahmadzai, Qarghayi Villages	Infrastructure	CCI090226	Nahri karim Canal Improvement	Irrigation	IDEA-NEW (DAI)	1-Apr-10	1-Jul-10	Active	8
Laghman	Qarghayi	Sawati, Qalai Sarferaz, Charbagh	Infrastructure	CCI090225	Sawati Road Improvement	Road	IDEA-NEW (DAI)	13-Jul-09	29-Nov-09	Active	99.2
Nangarhar	Achin	Band Toree Gatee, Malik Nabi bagh, Shalgar, Magh lana and Morgha	Infrastructure	CCI082309	Mamand Olace Canal Improvement	Irrigation	IDEA-NEW (DAI)	20-Apr-10	20-Jul-10	Active	10
Nangarhar	Achin	Koshtal	Infrastructure	CCI082311	Koshtal Mulayan MHP	Hydro Power	IDEA-NEW (DAI)	1-Apr-10	1-Jul-10	Active	8
Nangarhar	Achin	Makrana.	Infrastructure	CCI082308	Makrana Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	1-Nov-09	1-Feb-10	Completed	100
Nangarhar	Chaparhar	Bibi Mahro, Cheena, Trilai & Akhondzadgan Villages	Infrastructure	CCI080611	Bibi Mahro Canal Intake	Irrigation	IDEA-NEW (DAI)	1-Jan-10	1-Mar-10	Active	65
Nangarhar	Chaparhar	Kandi Bagh, Hafizano, zoghona, Qalay shekh and Sra qala villages	Infrastructure	CCI080612	Kandi Bagh & Hafizano Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	1-Jan-10	1-Mar-10	Active	50
Nangarhar	Dih Bala	Akakhil villages.	Infrastructure	CCI080808	Shpoola Akakhil Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	1-Apr-10	1-Jul-10	Active	15
Nangarhar	Dih Bala	Salara, Koz Yaghi Band and Bar Yaghi Band	Infrastructure	CCI080807	Yaghiband Micro Hydro Power Plant	Hydro Power	IDEA-NEW (DAI)	10-Jul-09	26-Nov-09	Completed	100
Nangarhar	Hisarak	Khanjar Villages	Infrastructure	CCI080307	Khanger kariz Improvement	Irrigation	IDEA-NEW (DAI)	16-Nov-09	16-Jan-09	Active	100
Nangarhar	Hisarak	Ragha villages	Infrastructure	CCI080310	Ragha Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	16-Apr-10	16-Jul-10	Active	9
Nangarhar	Hisarak	Sharif khil, Kapar khil, Lahor khil, Mohammad Aminkhil,	Infrastructure	CCI080308	Abizangiyani Pipe Scheme Project	Pipe Scheme	IDEA-NEW (DAI)	16-Nov-09	16-Jan-09	Active	70
Nangarhar	Khogyani	Baghicha & Soja dag villages	Infrastructure	CCI080517	Baghicha Intake & Karez Improvement	Irrigation	IDEA-NEW (DAI)	18-Jul-09	27-Oct-09	Completed	100

Province	District	Village	Section	Activity Code	Activity Name	Activity Type	Implementing Partner	Start Date	End Date	Status	Project %
Nangarhar	Khogyani	Derga & Abdi villages	Infrastructure	CCI080515	Derga Village Karez Improvement	Irrigation	IDEA-NEW (DAI)	18-Jul-09	27-Oct-09	Completed	100
Nangarhar	Khogyani	Hadari Qala, Rahim jan, Akbar sayed, Naiem jan	Infrastructure	CCI080518	Seway Zangal Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	10-Jul-09	5-Oct-09	Completed	100
Nangarhar	Khogyani	Kaga Old Bazaar, Mordardan, Akbar Khil	Infrastructure	CCI080511	Baghicha Road Improvement	Road	IDEA-NEW (DAI)	18-Jul-09	8-Jan-10	Stopped	20
Nangarhar	Khogyani	Moh Omar, Juma gul, Dawran, Rozidin, Qaatar	Infrastructure	CCI080514	Loghara Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	10-Jul-09	31-Aug-09	Completed	100
Nangarhar	Khogyani	Mulayan, Zamankhill, Abdulghani, Mulakhill	Infrastructure	CCI080512	Darwazagi Canal Improvement	Irrigation	IDEA-NEW (DAI)	10-Jul-09	31-Aug-09	Completed	100
Nangarhar	Khogyani	Musa ghundi, Koza Qala, Loi Kilay	Infrastructure	CCI080513	Nemla Manz Road Improvement	Road	IDEA-NEW (DAI)	10-Jul-09	5-Oct-09	Stopped	15
Nangarhar	Khogyani	Taowda Cheana & Minkay villages	Infrastructure	CCI080516	Taowda Chena Karez Improvement	Irrigation	IDEA-NEW (DAI)	18-Jul-09	26-Sep-09	Completed	100
Nangarhar	Lal Pur	Sarband, Lalpur, Guldag	Infrastructure	CCI081504	Lalpur Road Improvement	Road	IDEA-NEW (DAI)	1-Jan-10	1-Mar-10	Completed	100
Nangarhar	Pachir Wa Agam	Badan Khil & Aini Khil Villages	Infrastructure	CCI080706	Lande Pachir Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	16-Jul-09	5-Dec-09	Completed	100
Nangarhar	Pachir Wa Agam	Bama Khail, Landa Khail, Kagai Kala, Zar Kala, Bande Kala, Lar Kala,	Infrastructure	CCI080707	Landa Khail Canal Repair	Irrigation	IDEA-NEW (DAI)	1-Dec-09	15-Feb-09	Active	88
Nangarhar	Pachir Wa Agam	Bar and Kuz Sabor, Angorano Ghunday and Kata Khil Villages	Infrastructure	CCI080708	Landay Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	1-Dec-09	15-Feb-09	Active	92
Nangarhar	Rodat	Baro, & Soordag Villages	Infrastructure	CCI080905	Baro Shalzar Canal Intake Improvement	Irrigation	IDEA-NEW (DAI)	16-Jan-10	1-Apr-10	Active	60
Nangarhar	Shinwar	Baghcha Villages	Infrastructure	CCI081312	Baghcha Kariz	Irrigation	IDEA-NEW (DAI)	1-Apr-10	1-Jul-10	Active	20
Nangarhar	Shinwar	Ghanikhil	Infrastructure	CCI081310	Marko Girls and Boys School Boundry Wall	School Construction	IDEA-NEW (DAI)	1-Apr-10	1-Jul-10	Active	18
Nangarhar	Shinwar	Kasi, Shergar, Ghani Khil & Ghondai Kalai	Infrastructure	CCI081309	Kasi Intake & Gograni Kariz Improvement	Irrigation	IDEA-NEW (DAI)	18-Jul-09	5-Dec-09	Completed	100
Nangarhar	Spin Ghar	Malak Naiz Kalay, Band Toory Gati, Malak Nabi Kalay, Magholana Village	Infrastructure	CCI082310	Mamand Tangee Bridge	Bridge	IDEA-NEW (DAI)	1-Dec-09	15-Feb-09	Active	42
Nangarhar	Spin Ghar	Spinghar	Infrastructure	CCI082307	Terili Girls & Boys School Boundary wall & Toilets Implementation	School construction	IDEA-NEW (DAI)	16-May-09	16-Aug-09	Completed	100
Nuristan	Nur Gram	Maeen, Malil, Anar Bagh, Gojar and Mashfa villages	Infrastructure	CCI300805	Malil-Mishfa Road Improvement	Road	IDEA-NEW (DAI)	10-Apr-09	10-Jun-09	Completed	100

Annex VI: IDEA-NEW Biweekly Grants Update

EASTERN GRANTS

IDEA-NEW Grants Biweekly Report 16-30 Nov, 2010

Name of Grantee	District/Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	No. of Awards	Grant Status	Grant Start Date	Grant Type	Est. Grant Amount (USD)	Duration of Grant	Deliverables
Approved Grants										
Riaz Packaging Factory/ Engineer Ghulam Hussain	Dosaraka Kabul Jalalabad main road Surkhroad/ Nangrarhar	No Concept	No Concept	1	Approved	1-Apr-10	In-Kind	\$15,000	2.5 Months	Increased number of printed labels for boxes
Amiri & Brother's Carpentry Workshop/ Mohammad Hasan	Taimani Watt, Kabul Province	No Concept	No Concept	1	Approved	14-Dec-09	In-Kind	\$11,200	2 Months	Registration with AISA and renovation of workshop
Rohafza Jam and Pickle company/ Rohafza	Zone 10 Jalalabad City/Nangrarhar province	Approved	Approved	1	Approved	1-Jun-10	In-Kind	\$8,829	2 months	Increased production and sales of Jam and Pickles
Shams Afzali Poultry Production and rearing limited/ Haji Shams ul Haq	Daronta, Surkhroad district, Nangrarhar Province	Approved	Approved	1	Approved	6-Mar-10	In-Kind	\$10,000	5 months	Hiring of ten employees each and ensure good bio-security measures
Shamshad Vermicelli & Noodles Factory/ Ghulam Dastageer	Chinknorey Jalalabad City Nangrarhar province	Approved	Approved	1	Approved	1-Jul-10	In-Kind	\$23,308	4 months	1) Aisa Registration 2) Hiring of Additional 15 Staff members 3) Increased production and sales of Vermicelli and Noodles
Wasim Chair Manufacturing Factory/ Hasan Gul	Kabul Bus Stand, Jalalabad City, Nangrarhar Province	Approved	Approved	1	Approved	20-Feb-10	In-Kind	\$5,000	3 months	Registration with AISA. Hiring of 7 employees and increase the production and sale of plastic furniture.
Omer Farooq Food Company / Haider Baig	Jalalabad City, Nangrarhar Province	Approved	Approved	1	Approved	1-Jul-10	In-Kind	\$45,000	5 months	Hiring of 60 employees and local purchase of raw materials, to increase local cake and pastry manufacturing
Baryalaic bicycle Factory/ Baryalai	Dosaraka Kabul Jalalabad main road, Surkhroad District, Nangrarhar Province	Approved	Approved	1	Approved	1-Jul-10	In-Kind	\$23,000	4 months	1)Hiring of 20 Employee 2) Increase the production and sale of Bicycles 3) local procurements
Lajbar Marble Processing Factory/ Ajab Khan	Shirzad District, Nangrarhar	Approved	Approved	1	Approved	1-Jul-10	In-Kind	\$60,000	6 months	1) Aisa Registration 2) Hiring of Additional 28 Staff members 3) Grantee Should purchase new 250 KW generator 4) Increased production of marble and granite
Arian Marble Industries Limited/ Haji Fazel e Mula	Dosaraka Kabul Jalalabad main road, Surkhroad District, Nangrarhar Province	Approved	Approved	1	Approved	1-Jul-10	In-Kind	\$60,000	6 months	1) Aisa Registration 2) Hiring of Additional 15 Staff members 3) Increased production of marble and granite

Hedayat Barakat Broiler Breeder Farm/ Qari Ihsanullah	Behsud District Nangarhar Province	Approved	Approved	1	Approved	01 July, 2010	In-Kind	\$52,174	6 months	1) Construction of building for 6150 day old Broiler Breeder , Purchasing of automatic Drinker and Feeder. 2) Grantee should order the Broiler Breeder chicks as soon the grants is approved, 3) 50 % of Grant value will be given back to IDEA-NEW in form of Days old Chicks
Happy Afghanistan Sports/Muhammad Katoor	Zone no 4, Jalalabad City , Nangarhar Province	Approved	Approved	1	Approved	01 Aug, 2010	In-Kind	\$7,000	4 months	1)Aisa Registration 2) Increase production. 3) Construction of building and Hiring 8 new staff member.
Clean Drinking Water Supply Project/ Faizullah Khan Head of CDC	Shinwar District, Nangarhar Province	Approved	Approved	1	Approved	20-May-10	In-Kind	\$11,550	2 months	Unskilled Labor will be the Community Contribution
Gulayee Village Aqueduct project/ Abdul Rahman Head of CDC	Ghanikhil District, Nangarhar Province	Approved	Approved	1	Approved	20-May-10	In-Kind	\$12,558	2 months	Unskilled Labor will be the Community Contribution
Watan Dost Carpentry Workshop/ Dost Mohammad	Achin district, Nangarhar Province	Approved	Approved	1	Approved	01 July, 2010	In-Kind	\$9,800	2 months	1) Aisa Registration. 2) Hiring of 6 Employees and provide training 3) Increase production of Door, Window and cupboard
Waheed Soap Factory/ Bismillah	Behsud district, Nangarhar Province	Approved	Approved	1	Approved	01 Aug, 2010	In-Kind	\$30,000	3 Months	1)Construction of building to accommodate new machinery. 2) Hiring of 13 New staff members. 3) Purchased Raw Materials and increase the production and improve quality. 4)Purchased Cartons form Riaz Packages Factory
Ali Zada Green House	Qala -e- Maroof Surkhroad district, Nangarhar Province	Approved	Approved	1	Approved	01 Aug, 2010	In-Kind	\$44,412	2 Months	1) Aisa registration 2)Purchased inputs and other material such as Cucumber Seed, Tomato Seed, Pepper Seed, Farming Tools, Fuel, DAP, UREA, Animal Manure, Safety Tank and Main Pipe. 3)Hiring of 3 new staff member. 4)Increase and produce quantity Cucumber for local and Int'l markets
Ajmal Rahmani Dry Fruit Processing and Packing Company/ Naqibullah	Jalalabad City, Nangarhar Province	Approved	Approved	1	Approved	1-Sep-10	In-Kind	\$48,350	4 months	1) Construction of building. 2) Hiring of 12 people. 3) Purchased Raw Material (Walnuts) Improved quality and improved packaging and Produce products for export market
Pure Afghan Dry Fruit Processing Company/ Samiullah and Abdul Basit	Asadabad District, Kunar Province	Approved	Approved	1	Approved	1-Sep-10	In-Kind	\$47,500	4 Months	1) AISA Registration. 2) Construction of Building. 3)Hiring of 19 staff members. 4)Purchased Raw Material (Walnuts) Improved quality and improved packaging and Produce products for export market

Afghanistan Institute of Business Management	1) Nangarhar, Laghman and Kunar Province	Approved	Approved	1	Approved	01 Oct, 2010	FOG	\$33,600	4 months	<p>Milestone 1) Pre test should be prepare by AIBM and a soft draft should be submitted to IDEA-NEW grants unit. A copy of the trainers' CVs, job descriptions, and contracts will be submitted to IDEA-NEW grants Department. Provide timesheets to IDEA-NEW grants department for payment staff hired under this grant on monthly basis. Provide brief monthly progress reports on the activities to the IDEA-NEW Grants Department. A copy of the training curriculum/ schedule will be submitted to IDEA-NEW grants Department.</p> <p>Milestone # 2) Signed attendance sheets of trainers should be submitted to IDEA-NEW Grants office. All documents and reports must be signed and acknowledged by the project manager. Two page progress report on the status of training. . The report should also include photographs of activities and any other documentation illustrating activities performed under the grant period as well as address problems faced and solutions sought.</p> <p>Milestone # 3) • Final activity report that highlights progress made, challenges, the economic impact the training has had on participants, and lessons learned.</p> <p>• Provide copy of all attendance sheets of the trainers that should be certified by AIBM Manager to IDEA NEW Grants department.</p>
Sadam Textile weaving Company/ Haji Zazai	Kama district. Nangarhar Province	Approved	Approved	1	Approved	01 Oct, 2010	In-Kind	\$17,200	2 Months	1)AISA Registration. 2)Construction of building to accommodate new machinery. 3)Hiring of 7 permanent staff members. 4)Purchased Generator and raw materials
Dago Village Canal Protection wall project/Malak Noor Rahman	Dago Village Chaparhar District, Nangarhar Province	Approved	Approved	1	Approved	01 Nov, 2010	In-Kind	\$15,529	2 Months	Unskilled Labor from starting of Project till end of Project
Rahmatullah Vegetable Production Greenhouse/Rahmatullah	Jamai Mohammad Sideeq Village of Kama District of Nangarhar Province	Approved	Approved	1	Approved	01 Nov, 2010	In-kind	\$10,000	3 Months	1) AISA Registration 2) Land Preparation and purchase all input and required tools for greenhouse 3) As soon the Greenhouse is operational and start it production, monthly and quarterly sale report should be submitted to grants section as well as the technical section
Ihsanullah Off Season Vegetable Production Greenhouse/Ihsanullah	Saqawa Village of Khogyani District of Nangarhar Province	Approved	Approved	1	Approved	01 Nov, 2010	In-Kind	\$6,095	3 Months	1) AISA Registration 2) Land Preparation and purchase all input and required tools for greenhouse 3) As soon the Greenhouse is operational and start it production, monthly and quarterly sale report should be submitted to grants section as well as the technical section

Kunar Pashad Marble Processing Factory	Sarkano District, Kunar Province	Approved	Approved	1	Approved	01 Dec, 2010	In-Kind	\$60,000	6 Months	1) Construction of new building to accommodate the new machinery 2) Hiring of 15 new employeee 3)Purchasing of 350 KW generator and sizer machine 4)Increases the Production of Marble and Granite and sales report on monthly basis
Kaayenat Marhaba Henna Processing and Talcum Powder Manufacturing Factory	Aziz Khan Kas of Qarghayi district of Laghman Province	Approved	Approved	1	Approved	01 Dec, 2010	In-kind	\$22,800	4 Months	1) Construction of New building to accommodate new machinery 2) Purchasing of raw material as mention in grants application 3) Providing and submission of monthly sale report to the grants section.
Approved Concepts										
Textile Weaving Businesses	Shirzad District Nangrarhar Province	Approved	Approved	25	On Hold By PSD	TBD	In-Kind	\$0.00	3 months	TBD
Nangrarhar Juice Production Factory	Surkhroad district, Nangrarhar Province	Approved	Approved	1	On Hold By PSD	TBD	In-Kind	\$0.00	5 months	TBD
Fruits Pulp Centers for Fruit Growers Assn.	Nangrarhar & Kunar, Exact location TBD	Approved	Approved	2	On Hold By PSD	TBD	In-Kind	\$0.00	5 months	TBD
Sisters' bakery	Surkhroad District, Nangrarhar Province	Approved	Pending	1	Pending Approval	TBD	In-Kind	\$0.00	5 months	TBD
Barkakokhiel Pipe scheme & Sanitation Project	Surkhroad district, Nangrarhar Province	Approved	Pending	1	Pending Approval	TBD	In-Kind	\$0.00	2months	TBD
Tatang Gravelling Road	Surkhroad district, Nangrarhar Province	Approved	Pending	1	Pending	TBD	In-Kind	\$0.00	5months	TBD
Fruit Dehydration	Batikot Nangrarhar, Qarghai, Laghman	Pending More Info	Pending	2	Send back to PSD for more info	TBD	In-Kind	\$0.00	5months	TBD
Peanuts & Pine nuts Processing	1) Nangrarhar Province Jalalabad district	Approved	Approved	1	RFA Renounced with the closing date of 15 Sep 2010. No Potential Candidates found to bid	TBD	In-Kind	\$0.00	4 months	TBD
Cotton Processing	Nangrarhar Province Achin district	Approved	Approved	1	Application Pending with grantee	TBD	In-Kind	\$0	3 Months	TBD
Bibi Aisha Carpet Producer Association	Nangrarhar Province Surkhroad district, Faizabad Village	Approved	Approved	1	On Hold By GME	TBD	In-Kind	\$0	6 Months	TBD
Akhund Village Canal protection wall project	Akhund Village, Kama District, Nangrarhar Province	Approved	Approved	1	Application Pending with Applicant	TBD	In-Kind	\$0	40 Days	TBD

Textile Weaving in Rodat District	Hisarshahi Village of Rodat district, Nangarhar Province,	Approved	Approved	5	Out of nine potential candidates 5 became final winners by evaluation committee members which includes: Khaiber Gul, Azizurrahman, Ismaeel Torkhan and Tahsildar.	TBD	In-kind	\$0	3 Months	TBD
Support to Spin Ghar Poultry Farm Association	Jalalabad City of Nangarhar Province	Approved	Approved	1	Technical and cost evaluation been completed and recommended by evaluation committee	TBD	In-Kind	\$0	12 Months	TBD
Carpet Weaving Program	Nangarhar and Kunar Provinces	Approved	Approved	2	RFA date is closed, Only two Potential candidate applied for our RFA, Application will be presented to Evaluation committee members	TBD	In-Kind	\$0	6 Months	TBD
Mazina Girls High School Boundary Wall Project	Mazina Village Rodat District, Nangarhar Province	Approved	Approved	1	Application Pending with grantee	TBD	In-Kind	\$0	3 Months	TBD
Garment Finishing	Majboorabad Area of Jalalabad City	Approved	Approved	1	Under Review	TBD	In-Kind	\$0	2 Months	TBD
Maidanak Village Canal Protection Wall Project	Maidanak Village of Spinghar District of Nangarhar Province	Approved	Approved	1	Application is Under review	TBD	In-Kind	\$0	3 Months	TBD
Gawe Village Canal Rehabilitation Project	Gawe Village of Achin District of Nangarhar Province	Approved	Approved	1	Application is Under review	TBD	In-Kind	\$0	2 Months	TBD
Broiler Breeder Farm	Mihterlam/Qarghay District of Laghman Province	Approved	Approved	1	RFA has been distributed and pre award conference held on 10 Nov 2010 in IDEA NEW Office	TBD	In-Kind	\$0	7 Months	TBD
Javed Afghan Agro Machinery Manufacturing Factory	Jalalabad City of Nangarhar Province	Approved	Approved	1	Application and business plan is pending with technical section	TBD	In-Kind	\$0	6 Months	TBD
Disapproved Grants										
Mohammad Haroon Ibrahimi Walnuts Processing company	Kunar Province. Asadabad district	Approved	Approved	1	Not Approved	TBD	In-Kind	\$0	4 Months	Note: Applicant applied for the walnuts grants through RFA and was not approved by Regional Director

Maiwand Taqab Walnuts Processing and Packing Company	Nangarhar District, Jalalabad city	Approved	Approved	1	Not Approved	TBD	In-Kind	\$0	4 Months	Note: Applicant applied for the walnuts grants through RFA and was not approved by Regional Director
(AWARD)	Mehterlam/Laghaman	No Concept	No Concept	1	Not approved	TBD	FOG	\$0	10 months	Increase the capacity of Afghan women.
Layer Poultry Farms	Eastern Region	Approved	Approved	25	Not Approved	TBD	In-Kind	\$0	6 Months	TBD
Marble and Granite Processing/ National Marble	Surkhroad District, Nangarhar	Approved	Approved	1	Not approved	TBD	In-Kind	\$0		TBD
Omaid Khalid Poultry Services	Behsud District, Nangarhar	Approved	Approved	1	Not approved	TBD	In-Kind	\$0		TBD
Small Joinery Businesses/ Toti Gul	Nangarhar Province Achin district	Approved	Approved	1	Cancelled	01 July, 2010	In-Kind	\$9,800	2 months	1) Aisa Registration. 2) Hiring of 5 Employees and provide training 3) Increase production of Door, Window and cupboard
Omaid Khalid Poultry Services	Close to Poultry market, Omaid Khalid Poultry Services, Shop No. 3,	Approved	Approved	1	Not approved	01 July, 2010	In-Kind	\$52,300	6 Months	
Afghanistan Strategic Research and Services	10th street Dehbori Kabul	Approved	Approved	1	Not approved	01 Sep, 2010	FOG	\$344,700	6 Months	
Khurasan Institute of Higher Education	Opposite Dar Ul Malemmen, Jalalabad Nangarhar	Approved	Approved	1	Not approved	01 Sep, 2010	FOG	\$35,350	6 Months	
Mohammad Haroon Ibrahimi Walnuts Processing Company	Karmool village Asadabad City of Kunar Province	Approved	Approved	1	Not approved	01 Sep, 2010	In-Kind	\$58,000	6 Months	
Army Uniform Sewing Project/ Rahmatullah	Jalalabad City, Nangrarhar Province	Approved	Approved	1	Cancelled	01 July, 2010	FOG	\$52,200	6 months	1)Work Plan 2)CVs of key project staff 3) Monthly reports. 4) Signed daily attendance sheets for training activities.5)Photos.6) Testing for training activities. 7) Signed acknowledgement letter for completion of the project by the relevant government dept and 8)Final completion report

NORTHERN GRANTS

IDEA-NEW Biweekly Grants Update

15-30 November 2010

Name of Grantee	District/ Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	# of Awards	Grant Status	Start Date	Type	Estimated Grant Amount (USD)	Duration	Deliverables
Joint Development Associates (JDA)	Balkh Jawzjan Samangan Sari Pul All districts in the above 4 provinces	Apr 15/09	Apr 15/09	1	Awarded Complete	May 21/09	Fixed Obligation Grant	\$99,735	4 months	<ul style="list-style-type: none"> • Training of 64 farmer trainers • Conducting 2,500 training sessions • Training 75,000 farmers • 10,000 Nos farmer info leaflets • 5,000 Nos awareness posters • 5 Nos one-minute radio messages
International Assistance Mission (IAM)	Faryab All districts of Faryab	Jun 1/09	Jun 1/09	2	Awarded Complete	Jun 10/09	PO	\$6,600	3 months	30,000 melon bags stitched by widows
Agriculture Associations & Agriculture Depots	Balkh Jawzjan Samangan Sari Pul Faryab All districts in the above 5 provinces	Jul 1/09	Jul 1/09	24	Awarded Complete	Sep 5/09 Sep 1/09 Sep 1/09 Sep 15/09 Sep 15/09 Oct 28/09 Nov 8/09 Nov 1/09 Nov 9/09 Dec 12/09 Nov 30/10 Nov 30/10	In-kind grant agreements	\$269,119 \$138,800 \$4,650 \$69,900 \$54,862 \$2,500 \$22,500 \$83,750 \$4,090 \$56,335 \$103,290 \$64,500	9 months	97 Nos tractors & implements 20,000 harvest baskets 25 Nos harvest basket carts 2,000 Felco 610 saws 2,070 Nos Felco 5 shears 5,000 eye goggles 5,000 kg wettable sulphur 25,000 liters horticulture oil 10,000 Nos safety gloves 8,500 liters 1.5EC Deltamethrin 2,200 Felco 611 saws 2,500 Felco 5 shears
Khulm farmer Community	Balkh Khulm	Jan 15/10	Jan 15/10	1	Complete	Mar 29/10		\$86,550	3 months	Used 62 kgs SPLT EC for pomegranate carob moth control imported from ICSA Technologies USA
Dutch Committee for Afghanistan (DCA)	Balkh Jawzjan	Jan 15/10	Jan 20/10	1	Awarded On-going	Apr 1/10	Cost reimburse- ment grant	\$1,917,757	2 years	<ul style="list-style-type: none"> • Animal health & husbandry to 270,000 households • Generate sales >\$900,000 in year 1 of vet goods, vaccines, medicines, vet service) thru VFUs to livestock owners & \$1,120,000 sales in Year 2

Name of Grantee	District/ Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	# of Awards	Grant Status	Start Date	Type	Estimated Grant Amount (USD)	Duration	Deliverables
	Samangan Sari Pul Faryab All districts in the above 5 provinces									<ul style="list-style-type: none"> • Training of 94 VFU staff in Year 1 and 109 persons in Year 2 • Establish 15 Nos new VFUs • Cashmere target of 10MT in Yr 1 and 15MT in Yr 2; Sales in two years >\$300,000 • Establish 25 Nos winter feed banks
Dept of Agriculture	Faryab All districts	Feb 1/10	Feb 1/10	1	Complete	Feb 21/10		\$4,600	1 month	2,300 pine trees for re-forestation
Dept of Agriculture	Sari Pul All districts	Mar 1/10	Mar 1/10	1	Complete	Mar 10/10		\$3,800	1 month	2,000 pine trees for re-forestation
Rabia Maryam Handicrafts Co	Balkh Jawzjan Samangan Sari Pul All districts in the above 4 provinces	Jan 10/10	Jan 10/10	1	Awarded Complete	Feb 2/10	Fixed Obligation grant	\$14,414 \$4,535	3 months	<ul style="list-style-type: none"> • Commercial breeding of silkworms by 400 women • Silkworm eggs purchased from MAIL • 4,000 kgs of fresh silk production
Tela village, Khulm Community	Balkh Khulm	Oct 1/09	Oct 1/09	1	Complete	Nov 1/09	In-kind grant Cash-for-work	\$181,475	5 months	Gabion wall protecting the river bank & preventing flooding Cash-for-work labor
Khulm/Dodarak community	Balkh Khulm	Oct 1/09	Oct 1/09	1	Complete	Nov 1/09	In-kind Grant Cash-for-work	\$28,500	2 months	Retaining wall protecting the river bank & preventing flooding Cash-for-work labor
Faryab Community	Faryab Maymana Pashtun Kot Bilchiragh	Oct 1/09	Oct 1/09	1	Complete	Nov 1/09	In-kind Grant Cash-for-work	\$237,253	9 months	Constructing 39 Nos new culverts along the Maimana/Bulcheragh road Cash-for-work labor
Mazar Community	Balkh Mazar	Feb 1/10	Feb 1/10	1	Complete	Mar 5/10	Cash-for-work	\$17,791	9 months	Rehab of a Mazar Industrial Park neighborhood road Cash-for-work labor
Almond market vendors	Balkh Mazar-e-Sharif	Jun 1/10	Jun 1/10	1	Complete	Jul 1/10	MOU	\$26,361	3 months	Almond market platform for vendors to dry almonds and easy loading of almond bags for trucking Labor as community contribution Internet System IDEA NEW will provide 6 Nos desktop computers and install the internet hardware for 10 computers so that the beneficiaries could access almond market prices
					On-going	Nov 16/Dec 15	MOU	\$2,000	1 month	

Name of Grantee	District/ Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	# of Awards	Grant Status	Start Date	Type	Estimated Grant Amount (USD)	Duration	Deliverables
Chila Village community	Sari Pul Balkhab	Aug 1/09	Aug 1/09	1	Complete.	Aug 17/09	In-kind Grant MOU	\$26,705	14 months	Micro-hydro-power 13kW to 150 households
Hoosh Village community	Sari Pul Balkhab	Aug 1/09	Aug 1/09	1	Complete	Sep 5/09	In-kind Grant MOU	\$41,442	14 months	Micro-hydro-power 40kW to 180 households
Kham Shorack Village community	Sari Pul Balkhab	Aug 1/09	Aug 1/09	1	Additional work need to be done by the community	Sep 5/09	In-kind Grant MOU	\$20,866	14 months	Micro-hydro-power 10.4kW to 70 households
Paraw Shan Village community	Sari Pul Balkhab	Aug 1/09	Aug 1/09	1	Complete	Sep 5/09	In-kind Grant MOU	\$35,550	14 months	Micro-hydro-power 24kW to 130 households
Dhana Kashkak Village community	Sari Pul Balkhab	Aug 1/09	Aug 1/09	1	Additional work need to be done by the community	Sep 5/09	In-kind Grant MOU	\$35,550	14 months	Micro-hydro-power 21.7kW to 380 households
Keen Qala Village community	Faryab Bilchiragh	Aug 1/09	Aug 1/09	1	Complete	Sep 5/09	In-kind Grant MOU	\$31,166	6 months	Micro-hydro-power 11kW to 200 households
Angerack Village community	Faryab Bilchiragh	Aug 1/09	Aug 1/09	1	Complete	Sep 5/09	In-kind Grant MOU	\$29,806	6 months	Micro-hydro-power 12.5kW to 180 households
Khush Gozar Village community	Faryab Bilchiragh	Aug 1/09	Aug 1/09	1	Complete	Sep 5/09	In-kind Grant MOU	\$27,173	6 months	Micro-hydro-power 14.1kW to 180 households
Mirzaee #1 Village community	Faryab Bilchiragh	Aug 1/09	Aug 1/09	1	Complete	Sep 5/09	In-kind Grant MOU	\$27,235	6 months	Micro-hydro-power 10.2kW to 180 households
Mirzaee #2 Village community	Faryab Bilchiragh	Aug 1/09	Aug 1/09	1	Complete	Sep 5/09	In-kind Grant MOU	\$27,400	6 months	Micro-hydro-power 11.6kW to 180 households
International Assistance Mission (IAM)	Faryab Qaysar	Aug 1/09	Aug 1/09	1	Awarded Complete	Aug 18/09	Fixed Obligation Grant	\$5,272	5 months	Micro-hydro-power 3.5kW to 60 households Cost of materials only
International Assistance Mission (IAM)	Faryab Kohistan	Aug 1/09	Aug 1/09	1	Awarded Complete	Sep 2/09	Fixed Obligation Grant	\$7,265	5 months	Micro-hydro-power 5kW to 80 households Cost of materials only
International Assistance Mission (IAM)	Faryab Pashtun Kot	Jul 1/10	Jul 1/10	1	Awarded On-going	Sep 1/10	Fixed Obligation Grant	\$10,096	4 months	Micro-hydro-power 7.5kW to 180 households Cost of materials only

Name of Grantee	District/ Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	# of Awards	Grant Status	Start Date	Type	Estimated Grant Amount (USD)	Duration	Deliverables
	(Haji Basir Village)									
International Assistance Mission (IAM)	Faryab Pashtun Kot (Shura-e-Madrassa Village)	Jul 1/10	Jul 1/10	1	Awarded On-going	Sep 1/10	Fixed Obligation Grant	\$2,307	4 months	Repairs to the existing Micro-hydro-power plant Cost of materials only
International Assistance Mission (IAM)	Faryab Pashtun Kot (Kata Qala Shura-e-Bazar Village)	Jul 1/10	Jul 1/10	1	Awarded On-going	Sep 1/10	Fixed Obligation Grant	\$10,871	4 months	Micro-hydro-power 14kW to 150 households Cost of materials only
International Assistance Mission (IAM)	Faryab Pashtun Kot (Kata Qala Shura-e-Bazar Village)	Jul 1/10	Jul 1/10	1	Awarded On-going	Sep 1/10	Fixed Obligation Grant	\$7,100	4 months	Micro-hydro-power 6.2kW to 140 households Cost of materials only
International Assistance Mission (IAM)	Faryab Pashtun Kot (Azara Qala Village)	Jul 1/10	Jul 1/10	1	Awarded On-going	Sep 1/10	Fixed Obligation Grant	\$12,827	4 months	Micro-hydro-power 11.9kW to 160 households Cost of materials only
International Assistance Mission (IAM)	Faryab Pashtun Kot (Qalai Niasbeq Bala Village)	Jul 1/10	Jul 1/10	1	Awarded n-going	Sep 1/10	Fixed Obligation Grant	\$10,840	4 months	Micro-hydro-power 10.8kW to 160 households Cost of materials only
International Assistance Mission (IAM)	Faryab Pashtun Kot (Qalai Niasbeq Payan Village)	Jul 1/10	Jul 1/10	1	Awarded On-going	Sep 1/10	Fixed Obligation Grant	\$7,163	4 months	Micro-hydro-power 4.6kW to 160 households Cost of materials only
International Assistance Mission (IAM)	Faryab Pashtun Kot (Ibrahimabad Village)	Jul 1/10	Jul 1/10	1	Awarded On-going	Sep 1/10	Fixed Obligation Grant	\$8,912	4 months	Micro-hydro-power 4.4kW to 150 households Cost of materials only

Name of Grantee	District/ Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	# of Awards	Grant Status	Start Date	Type	Estimated Grant Amount (USD)	Duration	Deliverables
Balkh Livestock Development Union (BLDU)	1Koshkag/Balkh 2Sholgara/Balkh 3Hazrati Sultan/Samangan 4Aybak/Samangan 5Qush Tapa/ Sari Pul 6Sayadabad/Sari Pul 7Aqcha/Jawzjan +B288Faizabad/Jawzjan 9Khoja Sabz Posh Pashtun Kot/Faryab	March 22/10	June 10/10	1	Awarded	June 10/10	Cost reimburse- ment Grant	\$199,920	2 Years	Training of staff Installation/commission equipment Training of members in improved housing, nutrition, and care of cows Average daily milk yields exceed 4 liters 100 Nos improved cross-breed female calves Sale of produce to BLDU in Year 1 >\$28,500 Sale of produce to BLDU in Year 2 >\$42,700
Khulm Community	Khulm/Balkh	May 4/10	May 10/10	1	On-going On-going	July 15/10	In-kind Grant	\$99,000	3 Months	Construction of a gabion wall having a length of 550 meters in the Khulm River basis under the Project
Balkh Livestock Development Union (BLDU)	Mazar/Balkh	June 10/10	Jul 15/10	1	Approved. (PO not signed) Transport options under consideration	August 20/10	In-kind grant	\$33,700	1 month	Supply of Ice Cream producing equipment to BLDU for use/return Product diversification by adding ice cream to BLDU's current production line

Name of Grantee	District/ Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	# of Awards	Grant Status	Start Date	Type	Estimated Grant Amount (USD)	Duration	Deliverables
Joint Development Associates (JDA)	<p>Balkh/ Balkh Chimtal Chahar Kent Dawlatabad Dihdadi Kaldar Khulm Kishindh Nahri Shahi Sholgara Shortepa</p> <p>Faryab Andkhoy Dawlatabad Khani Charbagh Khwaja Sabz Posh Pashtun Kot Maymana Qaysar Qaramqul Qorghhan Shirin Tagab</p> <p>Samangan Dara-I Sufi Bala Feroz Nakhchir Hazrati Sultan Khuram Wa Sarbagh Aybak</p> <p>Sari Pul</p>	May 1/10	Jun 5/10	1	Awaiting approval from USAID/	Oct 1/10	Cost reimburse- ment grant	\$1,541,455	2 years	<p>Over the two-year period, set up 65 crop demonstrations attended by a total of 6,500 farmers, who will each attend three field days. Each demonstration will include wheat, a pulse (either lentil or chickpea), and an oil seed (either safflower, canola, flax, or sesame) each with improved agronomy. Farmers will be trained in seed bed preparation, seed production, an IPM approach to weed control, mechanical harvesting, and will be involved in a workshop considering the combined benefits of the technologies presented and the business opportunities afforded by appropriate mechanization and crop diversification.</p> <p>Identify 875 farmers willing, able and qualified by attendance at field days to buy 2WTS subsidized by IDEA-NEW. Provide technical and marketing services training for owner/operators of 2WTS and organize them into groups of ten for follow up support.</p> <p>Identify and demonstrate trailers, reapers, seeders, threshers, combines, water pumps and other equipment that can be powered by 2WTS and other appropriate equipment such as seed-cleaners.</p> <p>Set up 7 demonstrations of improved cultivation powered by four-wheel tractors (4WT) such as mechanical seeding with controlled fertilizer application, zero till and bed-planting on semi-irrigated or rain-fed land.</p> <p>Establish 5 contractor businesses providing these services to farmers on a sustainable commercial basis.</p>
					AO. A Letter of Authorization was signed for 2-month's work.					

Name of Grantee	District/ Province	Concept Approved by Evaluation Committee	Concept Approved by Project Director	# of Awards	Grant Status	Start Date	Type	Estimated Grant Amount (USD)	Duration	Deliverables
										Deliverables <ul style="list-style-type: none"> • 65 crop demos • 6,500 farmers who have attended three field days at crop demonstrations. • 875 owner/operators of 2WTs providing services to farmers in their area. • 13,000 hectares of annual crops cultivated with improved agronomic methods including the use of 2WTs • 7 demos of improved tillage & seeding with 4WTs • 5 contractor businesses providing improved tillage & seeding
Community of Mardian Village, Jawzjan	Mardian/Jawzjan	May15/10	Jun 10/10	1	Complete	Jul 15/10	In-kind Grant	\$65,000	3 months	Imported 2 Nos pond liners from USA
				1	Awarded On-going	Sept 16/10	In-kind Grant	\$49,034	1.5 months	Construct water pond and Install the 2 Nos pondliners
Rabia Maryam Handicrafts Co	Balkh Jawzjan Samangan Sari Pul Faryab All districts in the above 4 provinces	Sep 1/10	Oct 1/10	1	Awarded On-going	Dec 1/10	Reimbursement	\$198,975	8 months	Train 500 women in wool spinning. Giving a wool spinning wheel to each beneficiary (Total = 500 women)

Annex VII: Cooperative Agreement Information

PROJECT Incentives Driving Economic Alternatives for the North, East and West (IDEA-NEW)
START DATE March 2, 2009
END DATE March 1, 2014
COOPERATIVE AGREEMENT NUMBER 306-A-00-09-00508
AOTR/USAID PROGRAM MANAGER [REDACTED]
AGREEMENT OFFICER [REDACTED]
GEOGRAPHIC COVERAGE Northern, Eastern and Western Afghanistan

Project Contact Information

[REDACTED]
Program Director
IDEA-NEW

[REDACTED]
