



USAID
FROM THE AMERICAN PEOPLE

TB CARE I

TB CARE I - Afghanistan

**Year 2
Quarterly Report
July - September 2012**

October 30, 2012

Quarterly Overview

Reporting Country	Afghanistan
Lead Partner	MSH
Collaborating Partners	KNCV, WHO
Date Report Sent	3-nov-12
From	Dr. Khakerah Rashidi
To	Dr. Mohammad Shapor Ikram
Reporting Period	July - September 2012

Technical Areas	% Completion
1. Universal and Early Access	95%
3. Infection Control	85%
6. Health Systems Strengthening	91%
7. M&E, OR and Surveillance	89%
Overall work plan completion	90%

Most Significant Achievements

Access to TB services: From Jul-Sep 2012, a total of 26,843 suspected TB cases were identified in 13 USAID-supported provinces, of them, 1,867 cases turned out to be sputum smear positive and a total of 4,415 cases were notified as tuberculosis. In addition, the case notification and quality of care such as sputum conversion rate and treatment success rate improved significantly. For instance, for urban DOTS case notification increased from 797 in 2008 to an expected level of 1200 in 2012. Also, sputum conversion rate rose from 43% in 2008 to 75% in 2012 and treatment success rate from 43% to 70% in 2011 and for CB-DOTS the treatment success rate ascended to 98% while in rest of country the value for this indicator is 90%.

SOPs training for female staff: From Jul-Sep 2012, a total of 156 female staff from six quick impact provinces were trained on SOPs for case detection and treatment. This training was conducted in five provinces of Wardak, Zabul, Nimroz, Helmand and Farah provinces. The quick impact provinces are located in insecure provinces in the south of country and MSH was asked by USAID to extend its support to these provinces.

TBIS implementation monitoring visits: The TBIS system electronic reporting system was developed and rapidly expanded during APA2. However, for monitoring of this system TB CARE I asked additional funds from the home office to implement its Mini M&E plan. We received the amount USD 10,400 to monitor the implementation all over the country. So far, 29/34 provinces were either visited or the staff was called to national or regional capitals to ensure the proper implementation.

Health facility renovation: TB CARE I was committed to enhance the working climate for front line staff. Thus, from Jul-Sep 2012, seven health facilities were renovated for TBIC in four provinces. Also, seven health facilities in Urban city of Kabul were extensively renovated for TBIC and regular management of day-to-day activities in health facilities.

Overall work plan implementation status

The overall implementation for APA2 is on the right track and that we could managed to achieve the 75% implementation status.

Technical and administrative challenges

Delay in STTA conduction for TBIC that resulted in cancellation of two activities
 Security
 Ramadan , the fasting month, delayed some activities
 Delay in GF round 8 phase II approvals delayed TB CARE I implementation
 High staff turn-over at health facility level
 Demotivation of NTP staff owing to delayed payment

In-country Global Fund status and update

The GF phase of round 8 was finally approved by the GF after a delay of one complete year. However, NTP has not started the implementation of activities so far. in addition, the GF round 10 started implementation in the country.

Quarterly Technical Outcome Report

	Technical Area 1. Universal and Early Access							
Expected Outcomes	Outcome Indicators	Baseline		Target		Result	Highlights of the Quarter	Challenges and Next Steps to Reach the Target
		Data	Year	Data	Year	Y2		
1.2 Increased quality of TB services delivered among all care providers (Supply)	1.2.4 CB-DOTS program is implemented Indicator Value: Score (0-3) based on definition.	2	2011	3	2012	2	The level of CB-DOTS down graded as GF round eight phase II however approved but has not started till end of Sep 2013.	The CB-DOTS in additional two provinces will be started during APA3. in addition, the USAID has promised to allocate additional funds and TB CARE I will be able to implement the full package of CB-DOTS in all 13-USAID supported provinces. Currently, CB-DOTS is implemented in four provinces in subcontract with NGOs and in nine provinces with BRAC.

	<p>1.2.5 Number of sputum smear positive TB cases detected under Urban DOTS in Kabul city</p> <p>Description: This indicator measures the outcome of Urban DOTS implementation in Kabul city</p> <p>Indicator Value: Number</p> <p>Level: National and TB CARE I intervention area</p> <p>Source: NTP surveillance and TB CARE I project</p> <p>Means of Verification: health facilities registers and reports of sputum smear positive TB cases</p> <p>Numerator: Number of sputum smear positive TB cases detected in Urban health facilities</p> <p>Denominator: NA</p> <p>Indicator Value:</p> <p>Level:</p> <p>Source:</p> <p>Means of Verification:</p>	1022	1	1200	2	1180	<p>The Urban DOTS extended to additional public and private facilities during this quarter. Thus, we were able to enhance the case notification. Therefore, cumulatively, 1,180 sputum smear positive TB cases notified till end of Jul 2012.</p>	<p>TB CARE I will enhance the expansion of DOTS to additional 20 health facilities during APA3.</p>
	<p>1.2.6 Proportion of TB suspects identified by Urban DOTS facilities in Kabul city</p> <p>Description: This indicator measures the output of the Urban DOTS facilities</p> <p>Indicator Value: Proportion</p> <p>Level: Provincial and TB CARE I intervention area</p> <p>Source: NTP surveillance data</p> <p>Means of Verification: Urban health facilities TB suspect register and quarterly TB suspect report</p> <p>Numerator: Number of TB suspects identified by urban health facilities</p> <p>Denominator: Number of total</p>	3%	1	5%	2	3%	<p>TB CARE I was able to identify the additional TB case and number of suspected TB cases, but the percentage still remained same as previous year. Collectively, it is expected to identify 13,000 suspected TB cases out of approximately 434,000 outpatients attendees till end of 2012.</p>	<p>TB CARE I will enhance the expansion of DOTS to additional 20 health facilities during APA3.</p>

	<p>1.2.7: Proportion of new sputum smear positive TB cases out of suspected TB cases referred by CHWs.</p> <p>Description: This indicator measures the outcome of CB-DOTS</p> <p>Indicator Value: proportion</p> <p>Level: Provincial and TB CARE I intervention area</p> <p>Source: NTP surveillance data</p> <p>Means of Verification: health facilities TB suspect registration and quarterly suspect management report</p> <p>Numerator: Number of new sputum smear positive TB cases identified by CHWs.</p> <p>Denominator: Total number of TB suspected cases referred by CHWs in 13 USAID supported provinces.</p>	10%	1	10%	2	9%	During Jul-Sep 2012, out of all 1,598 suspected TB cases identified by CHWS in four provinces, 141 turned to be sputum smear positive TB. This makes almost 9%. Thus, we reached to annual project target.	TB CARE I will continue with CB-DOTS implementation in all 13 USAID supported provinces during year three of the project. As per NTP and USAID request we may extend CB-DOTS contract with NGOs in all 13 provinces.
--	--	-----	---	-----	---	----	--	--

Technical Area TB infection control

Expected Outcomes	Outcome Indicators	Baseline		Target		Result	Highlights of the Quarter	Challenges and Next Steps to Reach the Target
		Data	Year	Data	Year	Y2		
3.2 Scaled-up implementation of TB-IC strategies	<p>3.2.2 Key facilities with IC focal person, implementation plan, budget, and monitoring system</p> <p>Indicator Value: Percent</p> <p>Numerator: The number of selected categories of health facilities with all three (a+b+c) interventions in place.</p> <p>Denominator: Total number of health facilities in 19 provinces of the selected categories</p>	3,3	1	10	2	9	During APA2 in total 60 health facilities converted by TBIC measure application. This makes 8.6% (60/700).	This activity will be continued in APA3.

Technical Area 6, Health system strengthening












Expected Outcomes	Outcome Indicators	Baseline		Target		Result	Highlights of the Quarter	Challenges and Next Steps to Reach the Target
		Data	Year	Data	Year	Y2		







6.1 Ensured that TB control is embedded as a priority within the national health strategies and plans, with commensurate domestic financing and supported by the engagement of partners	6.1.1 TB care and control strategic plan embedded within national health strategies, including quantifiable indicators and budget allocations Indicator Value: Yes/No	Yes	1	Yes	2	Yes	The TBIC plan is integrated into general IP plan at national level. At facility level it is integrated only at facilities that covered by TBIC application. Totally, there are 60 health facilities that integrated TBIC plan at general IP plan 60/700).	This activity is planned for APA3 as well.
---	--	-----	---	-----	---	-----	---	--






6.2 TB control components (drug supply and management, laboratories, community care, HRD and M&E) formed integral part of national plans, strategies and service delivery of these components	6.2.1 Supervisory visits conducted according to country supervisory standards Indicator Value: Percent Numerator: Number of annual supervisory visits conducted disaggregated by three levels. Denominator: Number of annual supervisory visits planned disaggregated by three levels in 13 USAID supported provinces.	80%	1	85%	2	100%	In total, all planned 34 visits conducted jointly with NTP and TB CARE I to all 13 provinces. In addition, 102 visits conducted to urban DOTS to Kabul city. Thus we realized 100% of planned visits	TB CARE I will continue its support for supervisory visits to health facilities at 13 USAID supported provinces.
	6.2.2 Status of HRD strategic plans implemented Indicator Value: Score (1-3) based on definition.	2	1	3	2	3	NTP developed HRD strategic plan with assistance from TB CAP and they developed the implementation plan and embeded it into partners work plan such as GF, TB CARE I, WHO, JICA and MOPH.	TB CARE I will continue its support to NTP to implement the HRD strategic plan during APA3 as well.
	6.2.3 People trained using TB CARE funds Indicator Value: Number of people Numerator: Number of people trained disaggregated by	1072	1	1172	2	1392	This quarter, 156 female staff from six quick impact provinces trained in SOPs for case detection and treatment.	TB CARE I will continue its support in form of on-the-job training during APA3. The initial and refresher trainings will be conducted by NTP from GF fund.






Technical Area 7, M&E, Surveillance and OR								
Expected Outcomes	Outcome Indicators	Baseline		Target		Result	Highlights of the Quarter	Challenges and Next Steps to Reach the Target
		Data	Year	Data	Year	Y2		
7.1 Strengthened TB surveillance	7.1.1 An electronic recording and reporting system for routine surveillance exists at national and/or sub-national levels Indicator Value: Yes/No	No	1	Yes	2	Yes	During Jul-Sep 2012, in total provincial TB coordinators from 13 provinces attended two days workshop on TBIS database and feedback provided to them. In addition, the last province was covered and TBIS database was extended to Uruzgan province. Currently, 34/34 provinces covered by electronic TB data reporting.	Follow up of TBIS databae implementation in all 34 provinces.
7.2 Improved capacity of NTPs to analyze and use quality data for management of the TB program	7.2.1 National M&E plan is up-to-date Indicator Value: Yes/No	No	1	Yes	2	Yes	Completed	NA
	7.2.2 NTP provides regular feedback from central to lower levels Indicator Value: Percent per quarter Numerator: Number of quarterly feedback reports prepared and disseminated disaggregated by three levels.	40%	1	60%	2	60%	All 34 planned visites conducted jointly with NTP and TB CARE I staff.	This activity will be followed on during APA3.
	7.2.3 A data quality audit at central level has been conducted within the last 6 months Indicator Value: Yes/No	No	1	Yes	2	NO	The protocol developed and we will be conducting field work in Oct-Nov 2012	TB CARE I assisted NTP on protocol development and field work is planned for data collection in Oct-Nov 2012.
7.3 Improved capacity of NTPs to perform operational research	7.3.1 OR studies completed and results incorporated into national policy/guidelines Indicator Value: Number (of OR studies and instances reported separately)	2	1	2	2	0	Following the research the report will be completed. This is planned for Dec 2012	The report will be completed after data collection in Dec 2012


Quarterly Activity Plan Report





1. Universal and Early Access			Activity Leader	Approved Budget	Cumulative Completion	Planned Completion		Cumulative Progress and Deliverables up-to-date
Outcome	Activity #	Activity				Month	Year	
1.2 Increased quality of TB services delivered by all care providers (supply)	1.2.1	Provide technical assistance to NTP to implement DOTS in 30 additional public and private health facilities in Kabul city.	MSH	40.824	 100%	Aug	2012	Currently, there are 68 facilities that provide DOTS in Kabul city under Urban DOTS.
	1.2.2	Two task force meetings in a quarter will be coordinated. NTP will conduct the meeting and ensure proper documentation and implementation of decisions taken during those meetings.	MSH	121.024	 100%	Aug	2012	All planned task force meetings for this quarter were conducted
	1.2.3	Four training sessions each of 20 individuals (health care staff from urban health facilities, doctors, nurses and lab technicians) will be conducted in Kabul city.	MSH	5.040	 100%	June	2012	21 (4 female and 17 male) staff trained on initial DOTS for five days
	1.2.4	15 sputum collection points in newly covered urban health facilities will be established with technical and financial assistance from TB CARE I.	MSH	6.750	 100%	Sept.	2012	The sputum collection points established in 15 health facilities
	1.2.5	84 visits (21 visits/qtr) will be conducted to supervise and monitor the DOTS implementation in urban health facilities. In each visit one individual from TB CARE I and one from NTP will attend.	MSH	4530	 100%	Sept.	2012	Totally, 102 joint visits with PTC, and NTP were conducted this year.
	1.2.6	Provide assistance to NTP to renovate five urban health facilities in Kabul city.	MSH	12500	 100%	Sept.	2012	All planned renovations conducted this quarter, in total 7 facilities were renovated.
	1.2.7	Provide technical and financial support to NTP to train 36 health care staff of urban health facilities in Kabul city.	MSH	4000	 100%	Sept.	2012	in total 60 individuals from Urban health facilities were trained on SOPs for case detection, treatment and TBIC during this quarter.
	1.2.8	Provide assistance to NTP to conduct one day coordination workshop for 150 individuals (private and public hospital managers, representatives from various ministries, community elites and members from civil society association) will attend this workshop.	MSH	6056	 100%	Sept.	2012	The workshop conducted to members from MOPH and public and private health sector in Sep 2012.
	1.2.9	Assist NTP to conduct awareness raising events in Kabul schools. One event in each quarter, total of 4 school events and four district events will be conducted in one year period.	MSH	2616	 100%	Sept.	2012	All four planned awareness raising activities conducted in four schools during this quarter, in total, 2,400 individuals attended these events.
	1.2.10	CB-DOTS implemented in 13 provinces (9 province will be sub-contracted by BRAC and four provinces by BPHS implementers).	MSH	271929	 50%	Sept.	2012	community based DOTS was expanded and implemented in 6 provinces. And in the rest of provinces as it was complementary to GF round 8, therefore, it was not implemented fully.
					 95%			





3. Infection control			Activity Leader	Approved Budget	Cumulative Completion	Planned Completion		Cumulative Progress and Deliverables up-to-date
Outcome	Activity #	Activity				Month	Year	
3.2 Scale-up implementation of TB-IC strategies	3.2.1	The national TBIC committee will conduct one meeting per month at national level. In total, 12 meetings will be conducted during APA2.	MSH	144	 100%	Sept	2012	This quarter three meetings conducted at national levels
	3.2.2	100 health care workers will be trained on SOPs for community level TBIC SOPs in 19 provinces.	MSH	9.456	 25%	Jun	2012	This activity was cancelled and the money was shifted to training of health facility staff at quick impact provinces
	3.2.3	Provide assistance to NTP to orient PTCS, RTCS, RLSs, PLSs and NGO focal person on TBIC assessment tool implementation. In total, 100 individuals in 19 provinces will be trained on assessment tool implementation in 62 health facilities in 19 provinces.	MSH	4.320	 100%	Feb	2012	in total, 90 health care staff (5 female and 85 male) were trained on assessment tool.
	3.2.4	Financial and technical assistance to NTP to conduct minor renovation for TBIC measures application in 27 health facilities in 19 provinces.	MSH	5.317	 100%	Sept	2012	in total, 27 facilities were renovated in 13 USAID supported provinces in quarter three 2012.
	3.2.5	62 health facility covered by TBIC will have one meeting in a month to monitor the progress and set new targets for next month/qtr. In total, there will be 2508 participants (11 participants per meeting / 1 meeting per month / in 19 provinces).	MSH	2.508	 100%	Sept	2012	Totally, 1440 individuals attended in 180 meetings conducted in 60 health facilities that conducted one meeting per month.
	3.2.6	Assist NTP to develop community level TBIC SOPs, print and disseminate 1000 copies and distribute to most of the 1900 health facilities.	MSH	60.627	Cancelled	Jul	2012	This activity was cancelled
	3.2.7	The TBIC IEC materials for community level developed and 4833 packages will be disseminated to all health facilities and health posts country wide.	MSH	14.498	Cancelled	Jul	2012	Cancelled
					 85%			

6. Health System Strengthening								
Outcome	Activity #	Activity	Activity Leader	Approved Budget	Cumulative Completion	Month	Year	Cumulative Progress and Deliverables up-to-date
6.1 Ensure that TB control is embedded as a priority within health systems and plans, with commemorate domestic financing and support by the engagement of partners	6.1.1	Assist NTP to conduct the task force meeting regularly. There will be 3 meetings/month and in total 27 TB task force meetings in a year.	MSH	675	 100%	June	2012	There were seven task force meetings conducted this quarter by NTP that brings the total meetings conducted to 25 this year.
	6.1.2	Assist NTP to conduct world TB day celebration at 320 health facilities in 13 USAID supported provinces.	MSH	20,800	 100%	Mar	2012	TB CARE I provided assistance to NTP to conduct World TB day in four provinces and 320 health facilities in USAID supported provinces across the country
	6.1.3	Provide assistance to NTP to develop, print and disseminate the advocacy kit to address MPs, policy makers and donors. 500 copies of this document will be printed and disseminated.	MSH	45,597	 100%	Mar	2012	14,000 IEC materials (billboard, Banners and brochures) developed and disseminated to all health facilities in the country on the occasion of World TB day celebration.
	6.1.4	Assist NTP to improve coordination with other stakeholders through attendance and presentation at central and provincial levels coordination meetings such as GCMU, CGHN, CCM, PHCC and CDC and BPHS coordination meetings. In total, there are 12 PHCC and CDC meetings at each province and four BPHS coordination meetings at national levels.	MSH		 75%	Sep	2012	There were regular meetings conducted with various stakeholders especially the MOPH to put the TB in the higher agenda of policy makers. Thus, NTP regularly conducted meetings with different departments such as CDC, HMIS, M&E and etc.
					 94%			

Outcome	Activity #	Activity	Activity Leader	Approved Budget	Cumulative Completion	Month	Year	Cumulative Progress and Deliverables up-to-date
6.2 TB control components (drug supply and management, laboratories, community care, HRD and M&E) formed integral part of national plans, strategies and service delivery of these components.	6.2.1	To provide assistance to NTP to conduct two days on the job training for 400 health care staff at DOTS learning centers.	MSH	48.056	 75%	Aug	2012	In total, 270 individuals attended the on-the-job training in all TB CARE I supported provinces during APA2 (Mar-Jun).
	6.2.2	Provide support to NTP to develop on the job training model guide for utilizing the DOTS learning center and print and disseminate 300 copies to 13 provinces.	MSH	4.256	 100%	Feb	2012	Completed
	6.2.3	Provide technical and financial support to NTP to conduct two day training for 100 female health workers in five selected provinces.	MSH	18.600	 100%	Jul	2012	Totally, 156 female staff trained in six quick impact provinces this quarter.
	6.2.4	Assist NTP HRD central team to assess the staff capacity and identify the capacity building needs. This workshops will be conducted in seven regions and totally, 80 NTP staff will be attending this workshop.	MSH	10.296	Cancelled	May	2012	NTP cancelled this activity and budget shifted to activity above (6.2.3). TB CARE I submitted budget reallocation for approvals to USAID and PMU.
	6.2.5	Provide assistance to NTP to conduct three days workshop on MOST for TB tool for 90 individuals in seven regions.	MSH	18.176	 75%	Aug	2012	Collectively, 54 individuals from all 13 USAID supported provines trained on MOST for TB follow up.
	6.2.6	Preparation and development of proposal for Global Fund round 12.	MSH	35.941	Cancelled	Sep	2012	This activity was cancelled as RFA for GF R-12 has not announced yet. TB CARE I will reprogram this amount to other activities in this TA which does not need approvals from USAID or PMU.
					 88%			

 **91%**

7. M&E, Surveillance and OR			Activity Leader	Approved Budget	Cumulative Completion	Planned Completion		Cumulative Progress and Deliverables up-to-date
Outcome	Activity #	Activity				Month	Year	
7.1 Strengthening M&E surveillance	7.1.1	Train 100 individuals (84 from provinces and 16 from central NTP) on TBIS database utilization from 34 provinces	MSH	15.200	 100%	Feb	2012	111(3 female and 108 male) staff from 32 provinces trained on the TBIS database. NTP received the first ever electronic copy of reports.
	7.1.2	34 province will be visited once in six month by NTP surveillance and M&E unit and TB CARE I team to supervise and monitor the TBIS database implementation process.	MSH	5.796	 100%	Jul	2012	29/34 provinces was visited this quarter with assistance from TB CARE I. TB CARE I asked the home office for additional fund for Mini M&E plan implementation.
	7.1.3	33 computers will be distributed to PTCs from 33 provinces i.e. one desk top computer per province. This is a dedicated computer for TBIS database utilization.	MSH	3.300	 100%	Feb	2012	32 computers disseminated to all the provinces for database utilization. TB CARE I was granted USD 10,400 for implementation of Mini M&E plan and all the allocated fund was utilized.
	7.1.4	Provide assistance to NTP to finalize the drafted TBIS procedure manual and print, disseminate 1000 copies to all health facilities in the country.	MSH	5.136	 75%	May	2012	The manual is completed and quotation was collected from various vendors for translation and printing.

Outcome	Activity #	Activity	Activity Leader	Approved Budget	Cumulative Completion	Month	Year	Cumulative Progress and Deliverables up-to-date
7.2 Improve capacity of NTPs to analyze and use quality data for management of Tb program	7.2.1	Quarterly review workshops will be conducted in six provinces with approximately 34 individual per province.	MSH	85.348	 100%	Sep	2012	In Jul 2012, the quarterly review workshops were conducted in 12/13 USAID supported provinces.
	7.2.2	Assist NTP to conduct three-day annual national evaluation workshop. 218 individuals such as PTCs, RTCs, PLSs, RLSs, senior NTP staff, high delegation of MOPH	MSH	96.882	Cancelled	May	2012	This activity was cancelled and the reallocation budget sent to USAID and PMU for their approvals
	7.2.3	Assist NTP to print, disseminate the national evaluation workshop results. 1000 copies of the evaluation reports will be printed and disseminated to all stakeholders in the country.	MSH	14.256	Cancelled	May	2012	This activity was cancelled and the reallocation budget sent to USAID and PMU for their approvals
	7.2.4	Assist NTP to train 15 individuals from MOPH/GCMU on TB program monitoring. The GCMU M&E consultants will be trained on TB supervision and monitoring aiming at unify the TB definitions.	MSH	375	 100%	Mar	2012	This was already conducted during first quarter.
						Planned Completion		
Outcome	Activity #	Activity	Activity Leader	Approved Budget		Month	Year	Cumulative Progress and Deliverables up-to-date
7.3 Improved capacity of NTPs to performed operational research	4.1.1	Provide technical and financial support to NTP to conduct two operational research studies during APA 2	MSH	10.000	 50%	Sept.	2012	The protocol was developed and submitted to NTP for their implementation of field work.
					 89%			

Quarterly MDR-TB Report

Country	Afghanistan
---------	-------------

Period	JULY-SEPTEMBER 2012
--------	---------------------

MDR TB cases diagnosed and put on treatment in country

Quarter	Number of MDR cases diagnosed	Number of MDR cases put on treatment
Jan-Dec 2010	19	0
Jan-Sep 2011	14	14
Oct-Dec 2011	8	8
Total 2011	22	22
Jan-Mar 2012	17	17
Apr-Jun 2012	3	3
July - Sept 2012	9	9
Total 2012	46	46

Quarterly GeneXpert Report

Country	Afghanistan
---------	-------------

Period	JULY-SEPTEMBER 2012
--------	---------------------

Table 1: GeneXpert instruments and cartridges procured or planned by quarter

	Procured			# still planned for procurement in APA 2	Month, Year procurement planned (i.e. April 2012)
	Jan-Dec 2011	Jan-Sept 2012	Cumulative total		
# GeneXpert Instruments	0	0		0	
# Cartridges	0	0		0	

Table 2: Cumulative List of GeneXpert Instruments Procured to Date or Planned in the Next Quarter

Already procured or still planned? (i.e. Write "Procured" or "Planned")	Instrument	# of Modules (1, 2, 4, or 16)	Location(s) (facility name & city/ province or TBD)	USG Funding Source (e.g., PEPFAR COP FYxx, USAID) ¹	Partner/ Implementing Organization; Additional Comments

¹ Differentiating between PEPFAR and USAID-funded is important. If it is PEPFAR funded, specify the fiscal year (i.e. FY2011). Add rows if there are more than 8 instruments in total.

Table 3: Cumulative Xpert MTB/RIF Cartridges Procured to Date or Planned for Next Quarter

Already procured or still planned? (i.e. Write "Procured" or "Planned")	Order #	# of Cartridges*	Location(s) (facility name and city/ province or TBD)	USG Funding Source (e.g., PEPFAR COP FYxx, USAID) ¹	Comments

*There are 10 cartridges per kit, but we need the total # of **cartridges** (not kits)
Add an additional row for every procurement order of cartridges


Any additional information/clarifications to the above (optional)

Please provide a brief description of any significant problems encountered in use of the GeneXpert machine(s) and Xpert MTB/RIF cartridges

Please describe technical assistance or evaluation of implementation activities performed and planned.

Quarterly Photos (as well as tables, charts and other relevant materials)

Trend of suspect management in Kabul 2008-2012

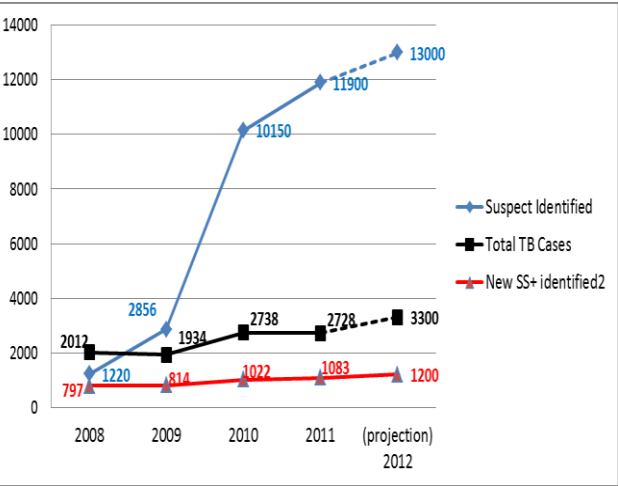


Student awareness event in Kabul city 2012



Waiting area build out side of OPD in NTI, Aug, 2012



Sputum collection points established in Ahmad Shah Baba Mina clinic

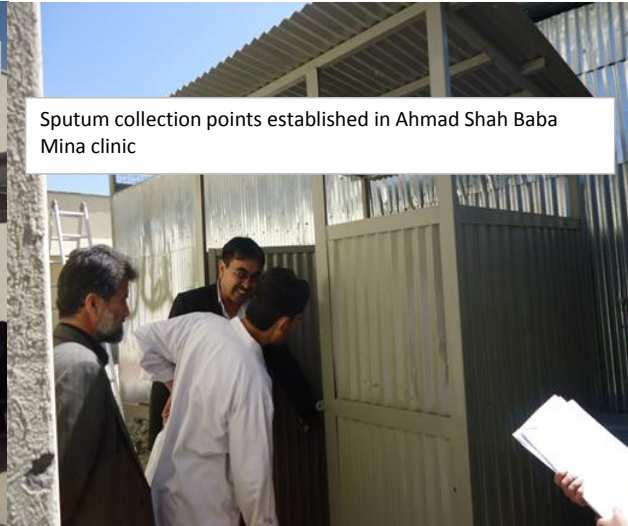

Inventory List of Equipment - TB CARE I

Organization:	TB CARE I
Country:	Afghanistan
Reporting period:	July - September 2012
Year:	APA 2



USAID
FROM THE AMERICAN PEOPLE

TB CARE I

Description (1)	ID numbers (2)	Acquisition date (3)	Acquisition cost (4)	V.A.T (5)	Location (6)	Condition (7)	Disposition date (8)	Title held by (9)	Serial
Microscope	9070	4-mei-10	\$0,00		AADA	A			9G81235
Microscope	9082	4-mei-10	\$0,00		AADA	A			9G81239
Microscope	9085	4-mei-10	\$0,00		AADA	A			9G81255
Microscope	9086	4-mei-10	\$0,00		AADA	A			9G81000
Microscope	9087	4-mei-10	\$0,00		AADA	A			9G81258
Microscope	9088	4-mei-10	\$0,00		AADA	A			9G81211
Microscope	9089	4-mei-10	\$0,00		AADA	A			9G81242
Microscope	9090	4-mei-10	\$0,00		AADA	A			9G81250
Microscope	9091	4-mei-10	\$0,00		AADA	A			9G81003
Microscope	9092	4-mei-10	\$0,00		AADA	A			9G81251
Microscope	9100	4-mei-10	\$0,00		AADA	A			9G81215
Microscope	9101	4-mei-10	\$0,00		AADA	A			9G81207
Microscope	9084	22-feb-11	\$0,00		AHDS	A			9G81237
Microscope	9094	22-feb-11	\$0,00		AHDS	A			9G81301
Microscope	9106	4-mei-10	\$0,00		AHDS	A			9G81253
Microscope	9104	4-mei-10	\$0,00		AKHS	A			9G81304
Microscope	9105	4-mei-10	\$0,00		AKHS	A			9G81247
Microscope	9107	4-mei-10	\$0,00		AKHS	A			9G81256
Microscope	9108	4-mei-10	\$0,00		AKHS	A			9G81022

Microscope	9109	4-mei-10	\$0,00		AKHS	A			9G81024
------------	------	----------	--------	--	------	---	--	--	---------

Microscope	9110	4-mei-10	\$0,00		AKHS	A		9G81206
Computer, laptop	7587	16-apr-09	\$0,00		Badakhshan	A		CN-OHN338-48643-8BS-0350
Printer	7632	16-apr-09	\$0,00		Badakhshan	A		CNCIJ01907
Scanner	7649	16-apr-09	\$0,00		Badakhshan	A		CN87HTO3N
Stabilizer	7701	16-apr-09	\$0,00		Badakhshan	A		SVC-2000 VA
Computer, desktop	0333	30-jan-12	\$0,00		badghis	A		8Y2Z42S
Computer, desktop	0339	30-jan-12	\$0,00		badghis	A		63D452S
Stabilizer	9765	6-mrt-12	\$0,00		badghis	A		
Stabilizer	9764	6-mrt-12	\$0,00		badghis	A		
Computer, desktop	0344	30-jan-12	\$0,00		Baghlan	A		G2D452S
Computer, laptop	7594	9-apr-23	\$0,00		Baghlan	A		CN-OHN338-48643-8BS-0446
Printer	7629	23-apr-09	\$0,00		Baghlan	A		CNC1J00793
Scanner	7646	23-apr-09	\$0,00		Baghlan	A		CN869THO82
Stabilizer	9782	6-mrt-12	\$0,00		Baghlan	A		
Stabilizer	7702	23-apr-09	\$0,00		Baghlan	A		
Stabilizer	9780	6-mrt-12	\$0,00		Balkh	A		
Computer, desktop	0347		\$0,00		Bamyan	A		B2D452S
Computer, laptop	7586	16-apr-09	\$0,00		Bamyan	A		CN-OHN338-48643-8BS-0029
Printer	7633	16-apr-09	\$0,00		Bamyan	A		CNCIJ00723
Scanner	7648	16-apr-09	\$0,00		Bamyan	A		CN85DTHOCN
Stabilizer	7698	16-apr-09	\$0,00		Bamyan	A		SVC-2000 VA
Stabilizer	9780	6-mrt-12	\$0,00		Bamyan	A		
Microscope	9072	4-mei-10	\$0,00		BDN	A		9G81248
Microscope	9073	14-feb-11	\$0,00		BDN	A		9G81244
Microscope	9074	4-mei-10	\$0,00		BDN	A		9G80999
Microscope	9075	4-mei-10	\$0,00		BDN	A		9G81012
Microscope	9076	4-mei-10	\$0,00		BDN	A		9G81302
Microscope	9077	4-mei-10	\$0,00		BDN	A		9G81245
Microscope	9080	4-mei-10	\$0,00		BDN	A		9G81216
Microscope	9096	4-mei-10	\$0,00		BRAC	A		9G81039
Microscope	9097	4-mei-10	\$0,00		BRAC	A		9G81006
Other	8318	14-okt-09	\$0,00		BRAC	A		20083069
Other	8319	14-okt-09	\$0,00		BRAC	A		20082925
Other	8320	14-okt-09	\$0,00		BRAC	A		20083109
Other	8321	14-okt-09	\$0,00		BRAC	A		20082936
Microscope	9079	9-nov-10	\$0,00		CAF	A		9G81026
Microscope	9093	9-nov-10	\$0,00		CAF	A		9G81005
Microscope	9102	28-feb-11	\$0,00		CAF	A		9G812110
Computer, desktop	0345		\$0,00		Daikondy	A		BZ2Z42S
Stabilizer	9758	6-mrt-12	\$0,00		Daikondy	A		
Computer, desktop	0335		\$0,00		Faryab	A		H13Z42S
Computer, laptop	7590	23-apr-09	\$0,00		Faryab	A		CN-OHN338-48643-8BS-0473
Printer	7625	23-apr-09	\$0,00		Faryab	A		CNC1J00796
Scanner	7652	23-apr-09	\$0,00		Faryab	A		CN86KTHIVT
Stabilizer	7703	23-apr-09	\$0,00		Faryab	A		
Stabilizer	11020		\$0,00		Faryab	A		

Computer, desktop	0375	30-jan-12	\$0,00		Ghazni	A		B13Z42S
Computer, laptop	7837	5-okt-09	\$0,00		Ghazni	A		13203320176
Printer	7623	23-apr-09	\$0,00		Ghazni	A		CNC1JO1884
Scanner	7644	23-apr-09	\$0,00		Ghazni	A		CN86BTHO7J
Stabilizer	9773	6-mrt-12	\$0,00		Ghazni	A		
Stabilizer	7683	1-jan-10	\$0,00		Ghazni	A		
Computer, desktop	0332	30-jan-12	\$0,00		Ghoor	A		3Y2Z42S
Stabilizer	9750	6-mrt-12	\$0,00		Ghoor	A		
Microscope	9078	4-mei-10	\$0,00		Health net	A		9G81212
Microscope	9095	4-mei-10	\$0,00		Health net	A		9G81246
Computer, desktop	0353	30-jan-12	\$0,00		Heart	A		HZZ42S
Computer, laptop	7592	16-apr-09	\$0,00		Heart	A		CN-OHN338-48643-8BS-0281
Printer	7631	16-apr-09	\$0,00		Heart	A		CNCI300747
Scanner	7653	16-apr-09	\$0,00		Heart	A		CN87RT1103
Stabilizer	7700	16-apr-09	\$0,00		Heart	A		SVC-2000 VA
Stabilizer	9752	6-mrt-12	\$0,00		Heart	A		
Computer, desktop	0363	26-jan-12	\$0,00		Helmand	A		JZZ42S
Stabilizer	9780	6-mrt-12	\$0,00		Helmand	A		
Microscope	9098	4-mei-10	\$0,00		IMC	A		9G81303
Microscope	9099	4-mei-10	\$0,00		IMC	A		9G81210
Computer, laptop	7835	5-okt-09	\$0,00		Jawzjan	A		17288146288
Printer	7619	23-apr-09	\$0,00		Jawzjan	A		CNC1JO2218
Scanner	7637	16-apr-09	\$0,00		Jawzjan	A		CN856THIFH
Stabilizer	7664	6-aug-09	\$0,00		Jawzjan	A		
Stabilizer	9859	30-jan-12	\$0,00		Jawzjan	A		
Computer, laptop	0555	7-mei-12	\$0,00		Kabul	A		9G973R1
Computer, desktop	0343		\$0,00		Kandahar	A		JY2Z42S
Computer, laptop	7588	23-apr-09	\$0,00		Kandahar	A		CN-OHN338-48643-8BS-0299
Computer, laptop	7593	23-apr-09	\$0,00		Kandahar	A		CN-OHN338-48643-8BS-0243
Printer	7621	23-apr-09	\$0,00		Kandahar	A		CNC1JO0815
Scanner	7651	23-apr-09	\$0,00		Kandahar	A		CN86BTH12P
Stabilizer	7704	23-apr-09	\$0,00		Kandahar	A		
Stabilizer	9763	6-mrt-12	\$0,00		Kandahar	A		
Computer, desktop	0355		\$0,00		Kapisa	A		243Z42S
Stabilizer	9778	8-jan-12	\$0,00		Kapisa	A		
Computer, desktop	0358	30-jan-12	\$0,00		Khost	A		4X2Z42S
Stabilizer	9751	6-mrt-12	\$0,00		Khost	A		
Computer, desktop	0336	30-jan-12	\$0,00		Kunduz	A		443Z42S
Stabilizer	9780	6-mrt-12	\$0,00		Kunduz	A		
Computer, desktop	0360	11-jan-12	\$0,00		Kunnar	A		143Z42S
Stabilizer	9770	11-jan-12	\$0,00		Kunnar	A		
Computer, desktop	0352	11-jan-12	\$0,00		Laghman	A		9ZZ42S
Stabilizer	9749	6-mrt-12	\$0,00		Laghman	A		
Computer, desktop	0340		\$0,00		Logar	A		73D452S
Stabilizer	9760	8-jan-12	\$0,00		Logar	A		
Computer, desktop	0362	11-jan-12	\$0,00		Nangarhar	A		g13z42s

Stabilizer	9779	11-jan-12	\$0,00		Nangarhar	A			
Computer, desktop	0334	30-jan-12	\$0,00		Nimroz	A			4Y2Z42S
Stabilizer	9756	6-mrt-12	\$0,00		Nimroz	A			
Computer, desktop	0357	11-jan-12	\$0,00		Nooristan	A			4Y2Z42S
Stabilizer	9757	11-jan-12	\$0,00		Nooristan	A			
Air conditioner	10284	9-feb-11	\$600,00		NTP	A			Y2KEPAKZB00073
Air conditioner	10285	9-feb-11	\$600,00		NTP	A			Y2KEPACZB00117
Amplifier	7916	20-mei-09	\$0,00		NTP	A			1150916
Cabinet	7555	4-mrt-09	\$0,00		NTP	A			
Cabinet	8055	27-mei-09	\$110,00		NTP	A			
Cabinet	8056	27-mei-09	\$110,00		NTP	A			
Cabinet	8057	27-mei-09	\$110,00		NTP	A			
Chair	10297	17-feb-11	\$40,00		NTP	A			
Chair	10298	17-feb-11	\$40,00		NTP	A			
Chair	10299	17-feb-11	\$40,00		NTP	A			
Chair	10300	17-feb-11	\$40,00		NTP	A			
Chair	10301	17-feb-11	\$40,00		NTP	A			
Chair	10302	17-feb-11	\$40,00		NTP	A			
Chair	10303	17-feb-11	\$40,00		NTP	A			
Chair	10304	17-feb-11	\$40,00		NTP	A			
Chair	10305	17-feb-11	\$40,00		NTP	A			
Chair	10306	17-feb-11	\$40,00		NTP	A			
Chair	10307	17-feb-11	\$40,00		NTP	A			
Chair	10308	17-feb-11	\$40,00		NTP	A			
Chair	10309	17-feb-11	\$40,00		NTP	A			
Chair	10310	17-feb-11	\$40,00		NTP	A			
Chair	10311	17-feb-11	\$40,00		NTP	A			
Chair	10312	17-feb-11	\$40,00		NTP	A			
Chair	10313	17-feb-11	\$40,00		NTP	A			
Chair	10314	17-feb-11	\$40,00		NTP	A			
Chair	10315	17-feb-11	\$40,00		NTP	A			
Chair	10316	17-feb-11	\$40,00		NTP	A			
Chair	10317	17-feb-11	\$40,00		NTP	A			
Chair	10318	17-feb-11	\$40,00		NTP	A			
Chair	10319	17-feb-11	\$40,00		NTP	A			
Chair	10320	17-feb-11	\$40,00		NTP	A			
Chair	10321	17-feb-11	\$40,00		NTP	A			
Chair	10322	17-feb-11	\$40,00		NTP	A			
Chair	10323	17-feb-11	\$40,00		NTP	A			
Chair	10324	17-feb-11	\$40,00		NTP	A			
Chair	10325	17-feb-11	\$40,00		NTP	A			
Chair	10326	17-feb-11	\$40,00		NTP	A			
Chair	10327	17-feb-11	\$40,00		NTP	A			
Chair	10828	11-okt-11	\$135,00		NTP	A			
Chair	10829	11-okt-11	\$135,00		NTP	A			
Chair	10830	11-okt-11	\$135,00		NTP	A			

Chair	10831	11-okt-11	\$135,00		NTP	A			
Chair	10832	11-okt-11	\$135,00		NTP	A			
Chair	10833	11-okt-11	\$135,00		NTP	A			
Chair	10834	11-okt-11	\$135,00		NTP	A			
Chair	10835	11-okt-11	\$135,00		NTP	A			
Chair	7556	4-mrt-09	\$0,00		NTP	A			
Chair	7557	17-feb-09	\$0,00		NTP	A			
Chair	8011	27-mei-09	\$46,00		NTP	A			
Chair	8012	27-mei-09	\$46,00		NTP	A			
Chair	8013	27-mei-09	\$46,00		NTP	A			
Chair	8014	27-mei-09	\$46,00		NTP	A			
Chair	8015	27-mei-09	\$46,00		NTP	A			
Chair	8016	27-mei-09	\$46,00		NTP	A			
Chair	8017	27-mei-09	\$46,00		NTP	A			
Chair	8018	27-mei-09	\$46,00		NTP	A			
Chair	8019	27-mei-09	\$46,00		NTP	A			
Chair	8020	27-mei-09	\$46,00		NTP	A			
Chair	8022	27-mei-09	\$0,00		NTP	A			
Chair	8023	27-mei-09	\$0,00		NTP	A			
Chair	8024	27-mei-09	\$0,00		NTP	A			
Chair	8025	27-mei-09	\$0,00		NTP	A			
Chair	8026	27-mei-09	\$0,00		NTP	A			
Chair	8027	27-mei-09	\$0,00		NTP	A			
Chair	8028	27-mei-09	\$0,00		NTP	A			
Chair	8029	27-mei-09	\$0,00		NTP	A			
Chair	8030	27-mei-09	\$0,00		NTP	A			
Chair	8031	27-mei-09	\$0,00		NTP	A			
Chair	8032	27-mei-09	\$0,00		NTP	A			
Chair	8033	27-mei-09	\$0,00		NTP	A			
Chair	8035	27-mei-09	\$0,00		NTP	A			
Chair	8036	27-mei-09	\$0,00		NTP	A			
Chair	8037	27-mei-09	\$0,00		NTP	A			
Chair	8038	27-mei-09	\$0,00		NTP	A			
Chair	8039	27-mei-09	\$0,00		NTP	A			
Chair	8040	27-mei-09	\$0,00		NTP	A			
Chair	8042	27-mei-09	\$0,00		NTP	A			
Chair	8043	27-mei-09	\$0,00		NTP	A			
Chair	8044	27-mei-09	\$0,00		NTP	A			
Chair	8045	27-mei-09	\$0,00		NTP	A			
Chair	8046	27-mei-09	\$0,00		NTP	A			
Chair	8047	27-mei-09	\$0,00		NTP	A			
Chair	8049	27-mei-09	\$0,00		NTP	A			
Chair	8050	27-mei-09	\$0,00		NTP	A			
Chair	8051	27-mei-09	\$0,00		NTP	A			
Chair	8052	27-mei-09	\$0,00		NTP	A			
Chair	8053	27-mei-09	\$0,00		NTP	A			

Chair	8054	27-mei-09	\$0,00		NTP	A		
Chair	8088	16-jun-09	\$0,00		NTP	A		
Chair	8089	16-jun-09	\$0,00		NTP	A		
Chair	8090	16-jun-09	\$0,00		NTP	A		
Chair	8091	16-jun-09	\$0,00		NTP	A		
Chair	8092	16-jun-09	\$0,00		NTP	A		
Chair	8093	16-jun-09	\$0,00		NTP	A		
Computer, desktop	7723	12-apr-09	\$0,00		NTP	A		GYKDY1S
Computer, desktop	7735	12-apr-09	\$0,00		NTP	A		BP8DY1S
Computer, desktop	1114	21-feb-11	\$1.130,00		NTP	B		SGH3390BGZ
Computer, desktop	1187	21-feb-11	\$1.130,00		NTP	B		SGH3390BH6
Computer, desktop	151	21-feb-11	\$1.130,00		NTP	B		SGH3390BHH
Computer, desktop	167	21-feb-11	\$1.130,00		NTP	B		SGH390BGP
Computer, desktop	641	21-feb-11	\$1.130,00		NTP	B		SGH3390BH9
Computer, desktop	838	21-feb-11	\$1.130,00		NTP	B		SGH3390BJ5
Computer, desktop	878	21-feb-11	\$1.130,00		NTP	B		SGH3390BJB
Computer, desktop	892	21-feb-11	\$0,00		NTP	B		
Computer, desktop	893	21-feb-11	\$1.130,00		NTP	B		SGH3390BGL
Computer, desktop	0365	12-mei-11	\$0,00		NTP	A		6X2Z42S
Computer, desktop	0348	30-jan-12	\$0,00		NTP	A		113Z42S
Computer, laptop	7828	5-okt-09	\$0,00		NTP	A		6432741424
Computer, laptop	7822	5-okt-09	\$0,00		NTP	A		28172057968
Computer, laptop	0554		\$0,00		NTP	A		3V973R1
Computer, laptop	0553	25-jul-12	\$0,00		NTP	A		DK873R1
Computer, laptop	0556		\$0,00		NTP	A		7N973R1
Copier	7707	12-apr-09	\$0,00		NTP	A		MWM58971
Desk	10805	11-okt-11	\$151,00		NTP	A		
Desk	10821	11-okt-11	\$151,00		NTP	A		
Desk	10822	11-okt-11	\$151,00		NTP	A		
Desk	10823	11-okt-11	\$151,00		NTP	A		
Desk	10824	11-okt-11	\$151,00		NTP	A		
Desk	10825	11-okt-11	\$151,00		NTP	A		
Desk	10826	11-okt-11	\$151,00		NTP	A		
Desk	10827	11-okt-11	\$151,00		NTP	A		
Desk	7580	24-mrt-09	\$0,00		NTP	A		
Desk	8001	27-mei-09	\$96,00		NTP	A		
Desk	8002	27-mei-09	\$96,00		NTP	A		
Desk	8003	27-mei-09	\$96,00		NTP	A		
Desk	8004	27-mei-09	\$96,00		NTP	A		
Desk	8005	27-mei-09	\$96,00		NTP	A		
Desk	8006	27-mei-09	\$96,00		NTP	A		
Desk	8007	27-mei-09	\$96,00		NTP	A		
Desk	8008	27-mei-09	\$96,00		NTP	A		
Desk	8009	27-mei-09	\$96,00		NTP	A		
Desk	8010	27-mei-09	\$96,00		NTP	A		
Fan	2728	2-jun-10	\$0,00		NTP	B		

Heater, gas	8094	16-jun-09	\$0,00		NTP	A		
LCD projector	10054	9-feb-11	\$0,00		NTP	A		7078356-M
LCD projector	7914	20-mei-09	\$0,00		NTP	A		S01-7079009-1
Monitor	7747	12-apr-09	\$0,00		NTP	A		CN-OG349H-64180-894-1HLL
Monitor	7749	12-apr-09	\$0,00		NTP	A		CN-OG349H-64180-88T3GAL
Monitor	1465	21-feb-11	\$1,00		NTP	B		CN330XY554
Monitor	1490	21-feb-11	\$1,00		NTP	B		CN330XY638
Monitor	4141	21-feb-11	\$1,00		NTP	C		CX000505842266
Monitor	5141	21-feb-11	\$1,00		NTP	B		CX000504793740
Monitor	6146	21-feb-11	\$1,00		NTP	C		CX000447243410
Monitor	6282	21-feb-11	\$0,00		NTP	A		
Monitor	6364	21-feb-11	\$1,00		NTP	B		AQ15HDBT71235713
Monitor	6366	21-feb-11	\$1,00		NTP	C		CX000504782555
Monitor	899	21-feb-11	\$1,00		NTP	B		CN330XY468
Monitor	927	21-feb-11	\$1,00		NTP	C		AQ15HDBT914050E
Other	10296	17-feb-11	\$330,00		NTP	A		
Printer	7618	16-jun-09	\$0,00		NTP	A		CNC1JO2222
Printer	7606	16-jun-09	\$0,00		NTP	A		CNFY136195
Scanner	7643	23-apr-09	\$0,00		NTP	A		CN84JTRO2P
Screen, projection	10608	22-mei-11	\$120,00		NTP	A		
Screen, projection	7915	20-mei-09	\$0,00		NTP	A		
Stabilizer	10287	9-feb-11	\$0,00		NTP	A		
Stabilizer	9835	30-sep-10	\$70,00		NTP	A		NIL
Stabilizer	7676	8-sep-09	\$0,00		NTP	A		
Stabilizer	7686	8-sep-09	\$0,00		NTP	A		
Stabilizer	7687	8-sep-09	\$0,00		NTP	A		
Switch	10806	8-okt-11	\$0,00		NTP	A		CVR01255662
Switch	10807	8-okt-11	\$0,00		NTP	A		
Switch	10808	8-okt-11	\$0,00		NTP	A		
Table	10494	7-mei-11	\$105,00		NTP	A		
Table	10495	7-mei-11	\$105,00		NTP	A		
Table	10496	7-mei-11	\$105,00		NTP	A		
Table	10497	7-mei-11	\$105,00		NTP	A		
Table	10498	7-mei-11	\$105,00		NTP	A		
Table	10499	7-mei-11	\$105,00		NTP	A		
Table	10500	7-mei-11	\$105,00		NTP	A		
Table	10501	7-mei-11	\$105,00		NTP	A		
Table	10502	7-mei-11	\$105,00		NTP	A		
Table	10503	7-mei-11	\$105,00		NTP	A		
Table	10504	7-mei-11	\$105,00		NTP	A		
Table	10505	7-mei-11	\$105,00		NTP	A		
Table	10506	7-mei-11	\$105,00		NTP	A		
Table	10507	7-mei-11	\$105,00		NTP	A		
Table	10508	7-mei-11	\$105,00		NTP	A		
Table	10509	7-mei-11	\$105,00		NTP	A		
Table	7554	4-mrt-09	\$0,00		NTP	A		

Table	7579	17-feb-09	\$0,00		NTP	A		
Table	8021	27-mei-09	\$662,00		NTP	A		
Table	8034	27-mei-09	\$600,00		NTP	A		
Table	8041	27-mei-09	\$600,00		NTP	A		
Table	8048	27-mei-09	\$600,00		NTP	A		
Table	8087	16-jun-09	\$0,00		NTP	A		
VSAT Equipment	0529	9-okt-11	\$0,00		NTP	A		
Computer, desktop	0338	30-jan-12	\$0,00		Paktika	A		83D452S
Computer, laptop	7829	5-okt-09	\$0,00		Paktika	A		12963088432
Printer	7627	23-apr-09	\$0,00		Paktika	A		CNC1JO1897
Scanner	7647	23-apr-09	\$0,00		Paktika	A		CN86KTHWQ
Stabilizer	7662	9-jun-10	\$0,00		Paktika	A		
Stabilizer	9762	6-mrt-12	\$0,00		Paktika	A		
Computer, desktop	0341	30-jan-12	\$0,00		Paktiya	A		F3D452S
Computer, laptop	7831	5-okt-09	\$0,00		Paktiya	A		43317108784
Computer, laptop	7839	5-okt-09	\$0,00		Paktiya	A		32854827376
Printer	7620	23-apr-09	\$0,00		Paktiya	A		CNC1JO0824
Printer	7617	16-jun-09	\$0,00		Paktiya	A		CNC1JO0812
Scanner	7640	23-apr-09	\$0,00		Paktiya	A		CN87HTHIHY
Scanner	7641	23-apr-09	\$0,00		Paktiya	A		CN86KTHIS3
Stabilizer	7682	1-jan-10	\$0,00		Paktiya	A		
Stabilizer	7699	12-mei-09	\$0,00		Paktiya	A		SVC 2000VA
Stabilizer	9767	6-mrt-12	\$0,00		Paktiya	A		
Computer, desktop	0354		\$0,00		Panjshir	A		HX2Z42S
Stabilizer	9774	8-jan-12	\$0,00		Panjshir	A		
Computer, desktop	0356		\$0,00		Parwan	A		DX2Z42S
Computer, desktop	0359	30-jan-12	\$0,00		Parwan	A		J13Z42S
Stabilizer	9771	8-jan-12	\$0,00		Parwan	A		
Stabilizer	9772	6-mrt-12	\$0,00		Parwan	A		
Stabilizer	9775	6-mrt-12	\$0,00		Samangan	A		
Computer, desktop	0351	30-jan-12	\$0,00		Saripul	A		5Z2Z42S
Stabilizer	9753	6-mrt-12	\$0,00		Saripul	A		
Microscope	9081	21-apr-11	\$0,00		SDO	A		9G81241
Microscope	9103	9-jan-12	\$0,00		SDU	A		9G81249
Computer, desktop	0361	30-jan-12	\$0,00		Takhar	A		3X2Z42S
Computer, laptop	7589	23-apr-09	\$0,00		Takhar	A		CN-OHN338-48643-8BS-0279
Printer	7628	23-apr-09	\$0,00		Takhar	A		CNC1JO0743
Scanner	7642	23-apr-09	\$0,00		Takhar	A		CN86BTHOOT
Stabilizer	7705	23-apr-09	\$0,00		Takhar	A		
Stabilizer	9768	6-mrt-12	\$0,00		Takhar	A		
Air conditioner	0453		\$0,00		TB Care 1	A		
Air conditioner	0187	1-apr-08	\$600,00		TB Care 1	B		PAJY800017N
Cabinet	7397	14-jan-09	\$0,00		TB CARE 1	A		
Cabinet	7403	14-jan-09	\$0,00		TB CARE 1	A		
Cabinet	46	1-apr-08	\$123,00		TB CARE 1	B		
Cabinet	6722	6-jan-08	\$70,00		TB CARE 1	A		

Cabinet	6727	6-jan-08	\$36,00		TB CARE 1	A		
Cabinet	6731	6-jan-08	\$36,00		TB CARE 1	A		
Cabinet	995	1-apr-08	\$35,00		TB CARE 1	B		
Camera	10811	18-okt-11	\$0,00		TB CARE 1	A		
Camera	10844	29-okt-11	\$0,00		TB CARE 1	A		
Camera	10845	29-okt-11	\$0,00		TB CARE 1	A		
Camera	5486	1-apr-08	\$395,00		TB CARE 1	A		682395
Camera	8162	9-aug-09	\$0,00		TB CARE 1	A		
Camera	8165	9-aug-09	\$0,00		TB CARE 1	A		
Camera	8836	26-jan-10	\$460,00		TB CARE 1	A		1735831
Camera	9989	27-jan-11	\$0,00		TB CARE 1	A		
CDMA/for net	8429		\$0,00		TB CARE 1	A		KTZAB10961900377
CDMA/for net	9915	10-nov-10	\$0,00		TB CARE 1	A		2009CP1510
CDMA/for net	8243	13-aug-09	\$0,00		TB CARE 1	A		KTAB10961900183
Chair	10444	31-jan-12	\$0,00		TB CARE 1	A		
Chair	12057	11-jul-12	\$0,00		TB CARE 1	A		
Chair	3850	1-apr-08	\$70,00		TB CARE 1	B		
Chair	3511	1-apr-08	\$70,00		TB CARE 1	B		
Chair	7099	14-jan-09	\$43,00		TB CARE 1	A		
Chair	7398	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7399	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7400	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7401	14-jan-09	\$0,00		TB CARE 1	A		
Chair	8750	14-jan-10	\$0,00		TB CARE 1	A		
Chair	8751	14-jan-10	\$0,00		TB CARE 1	A		
Chair	2755		\$0,00		TB CARE 1	B		
Chair	2756		\$0,00		TB CARE 1	B		
Chair	2757		\$0,00		TB CARE 1	B		
Chair	2758		\$0,00		TB CARE 1	B		
Chair	2759		\$0,00		TB CARE 1	B		
Chair	2760		\$0,00		TB CARE 1	B		
Chair	7101	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7384	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7385	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7386	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7387	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7388	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7389	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7390	14-jan-09	\$0,00		TB CARE 1	A		
Chair	7391	14-jan-09	\$0,00		TB CARE 1	A		
Chair	742	17-nov-08	\$0,00		TB CARE 1	A		
Chair	9246	8-jun-10	\$0,00		TB CARE 1	A		
Chair	9295	8-jun-10	\$0,00		TB CARE 1	A		
Chair	9296	8-jun-10	\$0,00		TB CARE 1	A		
Computer, desktop	0194	10-jan-10	\$770,00		TB Care 1	A		DZFP22s
Computer, desktop	0179		\$0,00		TB Care 1	A		B-R4X1S

Flash memory	9507	2-aug-10	\$12,00
Flash memory	6900	20-okt-08	\$0,00
Flash memory	6947	17-nov-08	\$0,00
GPS	5150	1-apr-08	\$40,00
GPS	5155	1-apr-08	\$40,00
GPS	5216	1-apr-08	\$40,00
LCD projector	0193	1-jan-10	\$0,00
LCD projector	0331	7-jun-11	\$0,00
Mobile phone	8175	8-jun-09	\$0,00
Mobile phone	9356	6-jul-10	\$0,00
Mobile phone	10877	3-jan-12	\$0,00
Mobile phone	9342	21-jun-10	\$0,00
Mobile phone	8187	8-jun-09	\$0,00
Mobile phone	10518	7-apr-11	\$240,00
Mobile phone	9925	23-nov-10	\$0,00
Mobile phone	8154	3-aug-09	\$0,00
Mobile phone	10657	17-nov-08	\$0,00
Mobile phone	6948	17-nov-08	\$0,00
Printer	7396	14-jan-09	\$0,00
Printer	0181		\$0,00
Radio	0195	1-apr-08	\$420,00
Rug	6974	25-nov-08	\$0,00
Rug	7382	14-jan-09	\$0,00
Rug	7393	14-jan-09	\$0,00
Rug	7394	14-jan-09	\$0,00
Rug	7395	14-jan-09	\$0,00
Scanner	6903	20-okt-08	\$0,00
Screen, projection	10520	11-apr-11	\$0,00
Screen, projection	8161	8-jun-09	\$0,00
Stabilizer	7661	9-jun-10	\$0,00
Stabilizer	7691	9-jun-10	\$0,00
Switch	7787	4-jun-09	\$0,00
Switch	7789	4-jun-09	\$0,00
Switch cage	5722	1-apr-08	\$0,00
Table	6060	1-apr-08	\$58,00
Table	7379	14-jan-09	\$0,00
Table	7402	14-jan-09	\$0,00
Table	8752	14-jan-10	\$0,00
Table	490	1-apr-08	\$44,00
Table	7366	11-jan-09	\$0,00
Table	7380	14-jan-09	\$0,00
Table	7392	14-jan-09	\$0,00
Thuraya	0196	8-feb-09	\$385,00
UPS	9796	30-sep-10	\$119,00
UPS	13137	2-aug-12	\$0,00
UPS	10083	4-jan-11	\$144,00

[illegible]

790 368 28
790 395 22
790 444 72
7027200938s
7056231-A
355218-03-530777-5
358234-03-822657-0
356274-04-8692355
358234-03-823553-0
355218035345940
352551-04-314834-1
354344-04-633544-8
355218-03-534666-6
355393-04-187995-8
IMEI:352912/02/445364/9
749TJAU847
CN81VTR10s
07804901598
CSV01HB34964
35601300-367822-7
NIL

UPS	7607	16-jun-09	\$0,00
UPS	9801	30-sep-10	\$119,00
Computer, desktop	0342		\$0,00
Stabilizer	9776	8-jan-12	\$0,00
Computer, desktop	0350		\$0,00
Stabilizer	9755	6-mrt-12	\$0,00

TB CARE 1	A
TB CARE 1	A
Wardak	A
Wardak	A
Zabul	A
Zabul	A

080314-87730034
NIL
J33Z42S
213Z42S
