



Healthy Mother/Healthy Child Results Package

Quarterly Performance Monitoring Report Option Period Quarter Six January 1 – March 31, 2003



John Snow, Inc.
Arabic Software Engineering (ArabSoft)
Clark Atlanta University
The Manoff Group, Inc.
TransCentury Associates

In collaboration with
The Ministry of Health and Population
Cairo, Egypt
and
USAID/Egypt
(Contract No. 263-C-00-98-00041-00)

April 15, 2003

TABLE OF CONTENTS

Introduction ----- 01

HM/HC Coverage Profile (March 2003) ----- 02

Task One: Basic Package of Essential Services Established and Standards Defined ----- 03

Task Two: Pre/In-Service Training System Designed to Disseminate Standards to Public and Private Providers ----- 11

Task Three: Public and Private Provider Partnerships with Communities to Develop and Manage District Plans ----- 21

Task Four: Monitoring System in place to Track Utilization and Impact and Provide Feedback ----- 25

Task Five: Research Activities ----- 27

Task Seven: Better Social Community Services ----- 31

Task Ten: Small Grant Program ----- 39

Task Eleven: Commodity Procurement Program ----- 41

Task Twelve: Coordination Activities ----- 45

Contract Administration ----- 55

LIIST OF ANNEXES

Annex A - Performance Milestones Charts -----	057
Annex B - Maps of Target Governorates -----	061
Annex C - JSI Contract Staff List -----	071
Annex D - Summary of Upgraded Status of Facilities in Target Districts -----	079
Annex E - Summary of Training of Personnel in Target Districts -----	093
Annex F - Summary of Management Improvement Activities at District Level -----	103
Annex G - Summary of Management Improvement Activities at Governorate Level -----	113
Annex H - Status of Community Level Activities -----	117
Annex I - A List of Trainings and Workshops by Date, Title, Site and Number of Trainees Conducted During the Period from January to March 2002 -----	131
Annex J - MOHP/ USAID/ JSI Monthly Coordination Meetings -----	139

LIST OF TABLES

Table 1 – Phase II BEOC Facilities -----	03
Table 2 – Renovation Status for Phase I BEOC Facilities -----	06

ACRONYMS

ANC	Antenatal Care
Aswan THO	Aswan Teaching Hospital
AWP	Annual Work Plan
BBC	Basic Benefit Package
BEOC	Basic Essential Obstetrical Care
CAP	Community Action Plan
CBT	Competency Based Training
CCO HQ	Curative Care Organization Headquarters
CDA	Community Development Association
CDS	Community Development Specilaist
CEOC	Comprehensive Essential Obstetrical Care
CHC	Community Health Committee
CNI-DMT	Community Needs Identification and Decision Making Tool Process
CNI-RHS	Community Needs Identification Rapid Household Survey
CPAP	Continuous Positive Airway Pressure
CQI	Continuous Quality Improvement
CTO	Cognizant Technical Officer
DCOP	Deputy Chief of Party
DH	District Hospital
DNF	Death Notification Forms
DOC	Deputy Chief of Party
DSMC	District Safe Motherhood Committee
DT2	Development Training Two
ED	Emergency Department
EMRO	Eastern Mediterranean Regional Office
EMS	Emergency Medical Services
EOC	Essential Obstetrical Care
EPI/ POLIO	Expanded Program for Immunization/ Poliomyelitis
ER	Emergency Room
FGC	Female Genital Cutting
FGD	Focus Group Discussions
FP/ RH	Family Planning/ Reproductive Health

GALAE	General Authority For Literacy And Adult Education
GH	General Hospital
GIS	Geographic Information System
GOE	Government of Egypt
GSMC	Governorate Safe Motherhood Committee
GWU	George Washington University
HIO	Health Insurance Organization
HIS	Health Information System
HM/HC	Healthy Mother/Healthy Child
HSMC	Hospital Safe Motherhood Committee
HSRP	Health Sector Reform Project
HU	Health Unit
I. V.	Intra Venus
IC	Infection Control
IDSC	Information and Decision support Center (of the Cabinet)
IEC	Information, Education and Communication
IFA	Invitation for Application
IFB	Invitation for Bids
IIE/DT2	Institute of International Education/Development Training Two
IIT	Integrated Implementation Teams
IMCI	Integrated Management of Childhood Illnesses
IPC	Interpersonal Communication
ITI	International Trachoma Initiative
JSI	John Snow, Inc.
MCH	Maternal Child Health
MCH FP	Maternal and Child Health part of the Family Planning
MHIS	Management Health Information System
MMSS	Maternal Mortality Surveillance System
MOE	Ministry Of Education
MOHP	Ministry of Health and Population
MOISA	Ministry of Insurance and Social Affairs
MS	Microsoft
MVA	Manual Vacuum Aspiration
NAMRU3	Naval American Medical Research Unit 3
NC	Neonatal Care

NCPAP	Nasal Continuous Positive Airway Pressure
NCU	Neonatal Care Unit
NGO	Non Governmental Organization
NICHP	National Information Center for Health and Population
NICU	Neonatal Intensive Care Unit
NMMS	National Maternal Mortality Study
Ob/Gyn	Obstetric and Gynecology
OJT	On Job Training
OR	Operation Research
PHC	Primary Health Care
PHTAC	Population and Health Technical Advisory Committee
QA	Quality Assurance
QPMR	Quarterly Performance Monitoring Report
RFP	Request for Proposal
RFQ	Request for Quotation
RHS	Rapid Household Survey
SHIP	Students Health Insurance Program
SIF	Service Improvement Fund
SMC	Safe Motherhood Committee
SQL	Structure Query Language
TCA	Transcentury Associates
TOT	Training of Trainers
UHC	Urban Health Center
UNICEF	United Nations Children's Fund
US	United States
USAID	United States Agency for International Development
WHO	World Health Organization

INTRODUCTION

Pursuant to Section F.4.1 of the John Snow, Inc/U.S. Agency for International Development (JSI/USAID) Contract No. 263-C-00-98-00041-00, JSI is required to submit Performance Monitoring Reports summarizing the progress of major activities in process, indicating any problems encountered and proposing remedial actions as appropriate. These reports are to be submitted quarterly for calendar quarters ending the last day of March, June, September and December for each year of the Contract.

This current Quarterly Performance Monitoring Report (QPMR VI) represents the Sixth quarter of the Option Period contract and covers the period from January 1 through March 31, 2003.

This document is organized according to the twelve tasks of the contract along with a section on contract administration. Each task contains a narrative with the following sections:

- Accomplishments
- Constraints
- Proposed Actions to Overcome Constraints

The attached annexes document progress in the following aspects of the Project:

Annex A: Status of the Option Period Performance Milestones

Annex B: Maps of Target Governorates

Annex C: Contract Staff List

Annex D: Summary of Upgraded Status of Facilities in Target Districts

Annex E: Summary of Training of Personnel in Target Districts

Annex F: Summary of Management Improvement Activities at District Level

Annex G: Summary of Management Improvement Activities at Governorate Level

Annex H: Status of Community Level Activities

HM/HC Coverage Profile (March 2003)

District	Population	Estimated Female Population	Estimated Females in Reproductive Age	Live Births	Estimated Pregnant Females
ASWAN					
Aswan	297576	147315	44636	7959	12766
Daraw	89145	44131	13372	2401	3824
Kom Ombo	259539	128485	38931	8139	11134
Nasr Nouba	72173	35729	10826	2161	3096
Edfu	324270	160530	48641	8685	13911
Total	1042703	516190	156405	29345	44732
LUXOR					
Luxor Bandar	1920690	950837	288104	4742	82398
Bayadaya	2460974	1218304	369146	6279	105576
Total	4381664	2169141	657250	11021	187973
QENA					
Qous	325368	161073	48805	10511	13958
Esna	300500	148762	45075	9940	12891
Armant	157355	77899	23603	4462	6751
Qena	488733	241947	73310	15380	20967
Deshna	293400	145248	44010	11367	12587
El-Wakf	61828	30608	9274	1880	2652
Neqada	129766	64241	19465	3757	5567
Qift	117219	58029	17583	3727	5029
Naga Hamadi	418156	207008	62723	13052	17939
Abu Tesht	325857	161315	48879	12164	13979
Farshout	127615	63176	19142	26016	5475
Total	2745797	1359305	411870	112256	117795
SOHAG					
Sohag	548388	271479	82258	17033	23526
Tahta	3377779	1672168	506667	9889	144907
Gerga	384313	190254	57647	11557	16487
Total	4310480	2133901	646572	38479	184920
ASSIUT					
Gharb Assiut	207442	102694	31116	3693	8899
Shark Assuit	17222	8526	2583	3535	739
Markaz Assiut	363896	180147	54584	9983	15611
Total	588560	291366	88284	17211	25249
MINYA					
Menya	664547	328984	99682	19673	28509
Samalout	526389	260589	78958	17231	22582
El-Fekreya	431326	213528	64699	13660	18504
Total	1622262	803100	243339	50564	69595
BEHENS					
Beni suef	463251	229332	69488	12449	19873
Ehnesia	254540	126010	38181	8612	10920
El Wasta	329130	162936	49370	10673	14120
El Fashn	304372	150679	45656	10262	13058
Beba	302392	149699	45359	9484	12973
Nasser	261499	129455	39225	7512	11218
Somosta	179752	88986	26963	5726	7711
Total	2094936	1037097	314240	64718	89873
FAYOUM					
Sennoures	386970	191569	58046	11608	16601
Etsa	464444	229923	69667	14567	19925
Bandar Fayoum	286751	141956	43013	7585	12302
Tamia	286845	142002	43027	8959	12306
Markaz El Fayoum	347599	172079	52140	10325	14912
Ibshway	531660	263198	79749	16234	22808
Total	2304269	1140727	345640	69278	98853
Grand Total	14780191	7316926	2217029	392872	634070

C.10.1 TASK ONE: Basic Package of Essential Services Established and Standards Defined

Accomplishments

Activity No. 1.1 Develop and Sign Memoranda of Cooperation

- The JSI Chief of Party and Deputy Chief of Party met with the newly appointed Undersecretary/MCH Director, Giza MOHP. The objectives of the meeting were to present the HM/HC project, to submit a draft of the Memorandum of Cooperation for review, and to set up a ceremonial meeting for the signing of the MOC by the Governor and concerned parties. The signing of the MOC will set the stage for beginning the implementation of HM/HC interventions in Giza Governorate.

Activity No. 1.2 Prepare a District Profile and Select BEOCs

- In cooperation with Task Three, BEOC facilities were selected in 16 districts of Phase II.
- The outcome of the selection process resulted in identifying 36 BEOC facilities that were selected according to the set criteria agreed upon (district population, population of local administrative units, distribution of health facilities utilization, distance, etc...). Table 1 lists Phase II selected BEOCs.

Table 1. Phase II BEOC Facilities

Governorate	District	BEOCs	No.
Sohag			
	Akhmeim	Nida Integrated Hospital El Koola Integrated Hospital	2
	El Balyana	El Sheikh Baraka Woman H. U. El Sheikh Marzouk Integrated H. U.	2
	Geheina	Eneibis Integrated Hospital	1
	Tahta	Tahta Maternity Shatturaa Integrated H.U. El Sawamaa Integrated Hospital	3
	El Mounshaa	Maternity Center El Zok El Sharkia Integrated H. Awlad El Sheikh Woman H.U. Awlad Hamza Integrated Hospital.	4
	El Maragha	Shandaweel Integrated Hospital. El Gherazat Integrated Health Unit	2
	Gerga	El Berba Integrated Health Unit	1
	Tema	Tema Urban Health Center Om Dooma Integrated Hospital El Rayayna Integrated Hospital	3
	Saqolta	Saqolta Maternity Al Galaweya Integrated Hospital	2

Governorate	District	BEOCs	No.
	Dar EL Salam	Al Naghameesh Rural H. U.	1
Assiut			
	El Fath	El Fath Urban Health Center El Atawla Integrated Hospital El Wasta Integrated Hospital	3
	El Kouseyah	El Kouseyah Maternity Beni Korra Woman Health Unit Fazara Integrated Hospital	3
	El Ghanayem	Urban Health Center, Maternity	1
Menya			
	Deir Mowas	Deir Mowas Maternity Beni Haraam H. U. Nazlet Badarman Integrated Hospital	3
	Fakreya	Asmant Integrated Hospital	1
	Beni-Mazar	Sandafa Integrated Hospital Beni-Ali Integrated Hospital Abu Garg Woman H. U. El Sheik Fadl Integrated Hospital	4
Total	16	36	

- The selection was immediately followed by an assessment for all these BEOC facilities to determine their requirements including staffing, and physical requirements (renovation, furniture, and commodities) among others; and to develop an improvement plan for each facility.

Activity No. 1.3 Assist in the Self Assessment of CEOC and development of Improvement Plans and Monitor Implementation

- General and District hospital profiles were prepared for Phase II of the Option Period and used to develop, implement and monitor improvement plans. The profiles and self improvement plans include:
 - Facility baseline assessment
 - Facility plan for renovation with schedule of implementation
 - List of commodities needed for each hospital and schedule of procurement, delivery and installation
 - Human resources development plan for the hospital, including training plan and status of implementation
 - Reports of management and clinical performance indicators (retrospective and summary of concurrent indicators) produced by monitoring.
- The Integrated Implementation visits by JSI clinical supervisors proved to be effective in helping the facility teams achieve the following:
 - Discuss the status of the implementation of activities at the facility level.
 - Assure flow of information among different members/ departments.
 - Identify problems at facility level and develop solutions.
 - Identify problems needing involvement of higher management at MOHP/JSI.

- Integrate and coordinate activities at the facility level.
- The following facilities were covered by the visits of the Integrated Teams during this quarter:
 - Sohag Governorate: Sohag General Hospital, Tahta District Hospital, Gerga District Hospital, Maragha District Hospital, Tema District Hospital, Geheina District Hospital
 - Assiut Governorate: Assiut General Hospital, New Eman General Hospital, Specialized Hospital, Ghanayem District Hospital, Kouseyah District Hospital
 - Menya Governorate: Menya General Hospital, Samalout District Hospital, Abu Qurkas District hospital, Beni Mazar District Hospital and Deir Mowas District Hospital

Activity No. 1.4 Initiate and Monitor the Implementation of the Renovation Plans

- Renovation activities were completed in all hospitals of Phase I of the Option Period, except for Somosta District Hospital (Beni Suef), where they are not completed yet (by the MOHP).
- Renovation activities supported by JSI were completed in the following facilities of Phase II of the Option Period:
 - Fakreya District Hospital and Beni Mazar District Hospital (Menya)
 - EL Ghanayem District Hospital (Assiut)
 - Gerga District Hospital, Tema District Hospital and Tahta District Hospital (Sohag)
- Blue prints, estimated costs, and bills of quantity for the facilities where renovation is planned by HM/HC were completed. The following is a list of these facilities:
 - Deir Mowas and Malawi District Hospitals (Menya)
 - El Kouseyah, Sahel Selem, Badary and Dayrout District Hospitals (Assiut)
 - Gerga, Tema, Saqolta, Akhmeim and El Balyana District Hospitals (Sohag)
- Blue prints and bills of quantity for the renovations planned to be supported by JSI were completed for the following facilities:
 - Maragha, Geheina, El Mounshaa and Dar El Salam District Hospitals (Sohag)
- The Interim Spaces for obstetrics, NICU and OR were selected in the facilities to be renovated, to secure the provision of services without interruption. These include:
 - Mallawi District Hospital (interim for Obstetric) (Menya)
 - Badary District Hospital (Obstetric, NICU and OR), Sahel Selem District Hospital (Obstetric), El Kouseyah District Hospital (Obstetric, NICU and OR) (Assiut)
 - Gerga DH (Obstetric and OR) (Sohag)
- Renovation was completed in all BEOC facilities of Phase I of the Option Period.

Table 2. Renovated BEOC Facilities (Phase I)

Governorate	District	Facility name
Beni Suef	Nasser	1. Nasser Maternity Center
		2. Ashmant I.H.U.
	Somosta	1. Shantur I.H.U.
		2. Dshtut I.H.U.
El Fayoum	Tamia	1. Tamia Maternity center
		2. Sersena I.H.U.
	Sennoures	1. Sennoures Maternity Center
		2. Fedemeen District Hospital
El Menya	Markaz	1. Suzan Mubarak Health Center
		2. Damsheer I.H.U.
		3. Tahna El Gabal I.H.
		4. Talla I.H.
		5. Tahnasha I.H.
	Samalout	1. El Saleba R.H.U.
		2. Qulosna I.H.
		3. Daqoof I.H.
		4. Manshiat El Sheraie I.H.
		5. El Bayaho I.H.
Assiut	Markaz	1. Naga Sabaa I.H.
		2. El Moteaa I.H.
	Shark	1. El Walideia Maternity Center
	Gharb	1. El Arbaeen Urban Health Center
Sohag	Markaz	1. Gazeret Shandaweel I.H.
		2. Balasfoura I.H.

- The blueprints for the BEOC facilities of Phase II of the Option Period were finalized.

Activity No. 1.5 Monitor the Delivery, Installation, Staff Training, Maintenance and Repairing of Equipment

- Commodities were delivered to all facilities of Phase I of the Option period, except for Somosta. However, there are few missing items that we are in the process of delivering them.

- Commodities for the Somosta facility are available, and will be delivered upon completion of renovation activities (by the MOHP).
- Commodities were delivered for 24 of the BEOC facilities of Phase I of the Option Period.
- In coordination with Task Eleven, procurement plans for 36 BEOC facilities of Phase II of the Option Period were completed. Delivery is on-going.
- The biomedical engineers conducted 70 person/day visits to the OB/GYN, NC, CSSD and OR departments in the facilities of both the Base and Option Periods. Review and screening of available equipment, maintenance and repair of *out of order* commodities, and provision of technical assistance and on-the-job-training (OJT) to the hospital maintenance staff were conducted during these visits.

Activity No. 1.6 Upgrade the Managerial Capacity of Hospital Management and Hospital Safe Motherhood Committees

- A new training curriculum for Safe Motherhood Committees (SMCs) of general and district hospitals was developed. The curriculum aims to promote planning, management and quality improvement skills of the hospital staff. The planned duration of training is four days.

Activity No. 1.7 Coordinate the Phasing-out and Sustainability Plans from Target Governorates

- A Beni Suef Phase Out workshop was conducted on February 23, 2003. Eighty participants from SMCs at governorate, district and hospital levels participated in the workshop, which was inaugurated by the Undersecretary and HM/HC Executive Director, MOHP, and the Chief of Health and Population Division, USAID.

From	To	No. of Participants
Feb. 23, 03	Feb. 23, 03	80

- The workshop reviewed the achievements of HM/HC and discussed strategies and plans of MCH and Curative Care, followed by the Beni Suef MOHP Directorate to sustain HM/HC project achievements. In addition service standards, protocols, competency-based training (CBT) curricula, the quality assurance (QA) system and management tools were reviewed, and plans to sustain them were developed.
- Preparation activities are under way to develop a completion report and organize Phase-out workshops for Fayoum and Qena by mid-April and the beginning of May, 2003 respectively.

Activity No. 1.8 Assist the MOHP / Urban Health Development to Pilot Test Adapted HM/HC Interventions in 1-2 Urban Slum Areas

Carry Out the Situation Analysis for Each of the Selected Slum Areas:

- On March 9, 2003, a meeting was conducted with Mr. Sayed Keshta to establish the requirements for implementation of NGO activities in the target slum areas. A follow-up meeting with Mr. Kamal Sherif, MOHP contact person for NGO was planned. The MOHP NGOs Regional Directory was collected.
- The two CEOC, El Khalifa and Embaba general hospitals, were assessed for adequacy of physical structure by JSI engineering staff. A final report is under preparation.
- HIS information available on the two slum medical centers has been compiled and collected from Task Four. Information on commodities and supplies at the two slum medical centers has been entered into the Quality Assurance Database.
- Family Planning Center data has been compiled and collected from the Gharb El Mattar Urban medical center to complete the health center profile. The same data is pending compilation at the Basateen Sharq Urban medical center.

Adapt HM/HC Interventions in 1-2 Slum Areas

- On February 3, 2003, a meeting was attended by Dr. Salwa Farag, HM/HC training staff, MOHP, Dr. Nevine Hassanein and Ms. Mona Selim to discuss the various training activities that would be implemented in the slum areas. Dr. Salwa showed great enthusiasm with regards to cooperation with the slums HM/HC pilot training activities, and suggested further meetings to plan collaboration, and determine resource allocations. Other issues discussed included referral system policies, training and forms used between basic facilities (PHC units) and the second level.
- A meeting was held on March 10 attended by Dr. Osama Abd El Gawad, General Manager, El Mattar Gharb Urban Health Center, 18 members of the center health staff (mostly nurses), Dr. Salwa Farag, Ms. Ahlam, Nurse Supervisor North Giza District, and three dayas from the North Giza district. From JSI the meeting was attended by Dr. Reginald Gipson, Ms. Pamela Putney (external consultant), Dr. Nevine Hassanein, Dr. Mohamed Ismail, Dr. Tarek Elshimi. The objectives of the meeting were:
 - To present challenges of home-births situation to unit health staff.
 - To discuss approaches and suggest solutions towards safer home-delivery.
 - To assess existing attitudes between official health staff and community dayas.
 - To initiate rapport, establish key contacts and open channels of communication with dayas and health staff for planned future initiatives
- Several presentations by JSI/MOHP staff introduced the audience to the topic of home-births, and explained the opportunities for reduction of maternal mortality. Improved quality of provider care, and the establishment of an effective referral system were suggested as the main interventions required.

The need for cooperation with dayas to achieve these goals was emphasized, and the health staff was invited to consider the positions of dayas and their patron families with greater respect and appreciation. The three dayas were interviewed in the second half of the meeting. The outcome of the meeting was as follows:

- The health staff showed great receptivity to the problem and enthusiasm for working with HM/HC initiatives to improve quality of care in home-births and establish contact and positive relationships with dayas
- Health staff agreed that friendly relationships with dayas was necessary to encourage them to refer complicated home-birth cases from home.
- Participants emphasized the need for (two-year) renewable licensing of dayas, to ensure their attendance of MOHP refresher training courses
- Nurses expressed the need for continued training in midwifery after graduation, and showed great interest in the four month course offered by the MOHP.
- Health staff identified the absence of transportation as a significant obstacle to institutional delivery in their catchment area.
- The perceived attitudes towards dayas were very positive. Dr. Osama and the nursing supervisor were both identified as key personnel for their network of contacts within the daya community, and for their supportive attitudes and behavior.
- Daily seminars held at the health center to raise community awareness of MCH issues were also identified as suitable opportunities for future visits.
- A future meeting to discuss the referral system between the health units and district hospitals was tentatively arranged with Dr. Osama to precede the MOHP planned implementation of a revised referral system (linking the unit with the district hospital) scheduled for May.
- Other issues discussed included the adequacy of the birth-kit particularly as relates to infection control.
- On March 16, a meeting was conducted at JSI attended by Mr. Said El Deeb, Dr. George Sanad, Mr. Khaled El Sayed, Drs. Nevine Hassanein and Tarek Elshimi, to establish the detailed process for implementation of each of the Management and Community activities in the two slum areas. Follow up meetings with Cairo and North Giza Directorate managers; and with managers of the relevant district health administrations were also planned. The necessary materials for these meetings were compiled.
- On March 18, a meeting was conducted with Dr. Said Madkour, Director General of IMCI. By the end of the meeting, Dr. Madkour agreed to implement IMCI activities in two HM/HC slum areas in collaboration with FM program, on condition that a minimum of 24 physicians per IMCI training course could be provided, that data collection forms as well as the community component of IMCI be coordinated with the JSI team.
- On March 18, a meeting was attended by Dr. Laila Solaiman, Director of Primary Health Care, to obtain approval for implementation of Family Medicine (FM) activities in the two HM/HC pilot slum areas in coordination with Integrated Management of Childhood Illness (IMCI). Dr. Solaiman

expressed an open attitude towards implementing FM programs in the slum areas in a coordinated manner with PHC and IMCI programs.

- On March 24, a second meeting was conducted with Dr. Laila Solaiman, to obtain information about the family medicine program and curriculum, and to reinforce the working relationship established after March 18 introduction.
- On March 26, A meeting was attended by Dr. Salwa Farag, Dr. Mahmoud El Bahrawi, Dr Khaled Otafi (HM/HC training staff), and Dr. Nevine Hassanein to discuss possibilities for the implementation of MCH training in the health centers of pilot HM/HC. The possible content of this training was also discussed.

Assist in the Plan Development to improve Perinatal Health Care Services and their Utilization

- Activities to improve perinatal health services are contingent on the completion of the situation analysis and coordination activities with various MOHP bodies. Progress in this area is expected to begin with slum pilot project implementation scheduled to start in the final quarter of 2003.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.2 TASK TWO: Pre/In-Service Training System Designed to Disseminate Standards to Public and Private Providers

Accomplishments

Activity No. 2.1 Disseminate Standards and Build MOHP Training Capacity

- Clinical performance monitoring system was used in Sohag, Assiut and Menya governorates to achieve continuous involvement of lead trainers in all EOC workshops and on-the-job-training.
- Lead trainers were given training tasks to carry out in their facilities during the periods between clinical supervisory visits. These tasks were monitored and checked by the JSI clinical supervisors.
- Nurse lead trainers from Aswan, Luxor, Qena and Sohag were trained in a TOT course. The training was scheduled as follows:

Governorate	From	To	No. of Participants
Aswan	Jan. 11, 03	Jan. 16, 03	25
Qena			
Sohag			
Luxor			

Activity No. 2.2 Sustain, Organize and Implement EOC Training and Clinical Supervision

- Based on information from the MMSS in the districts of Qena, Beni Suef and Fayoum governorates, technical assistance was provided at base period facilities, to help health providers develop improvement plans that address factors contributing to maternal deaths.
- Three CEOC workshops were conducted in Assiut, Menya and Sohag governorates. Trainees were facility obstetricians, and were trained to identify direct causes of maternal deaths and avoidable factors, particularly substandard care. The workshops were held on the following dates:

Governorate	From	To	No. of Participants
Assiut	Jan. 11, 03	Jan. 20, 03	24
Menya	Jan. 21, 03	Jan. 30, 03	24
Sohag	Mar. 11, 03	Mar. 20, 03	21
Total			69

- Continuous OJT/clinical supervisory visits were conducted to 25 districts in Fayoum, Beni Suef, Qena, Sohag, Assiut and Menya Governorates. Each of these districts was visited from six to nine days/month by clinical supervisors to ensure implementation of the EOC protocols. In addition, one day visits were conducted to all Phases III district hospitals of the Option Period, to provide them with all CEOC training documents and to work specifically on the clinical problems that came up from the initial assessment.

- The *Concurrent Assessment* Clinical Performance Monitoring Indicators are being used in Sohag, Assiut and Menya governorates to monitor progress of the obstetricians towards competency and mastery of the Essential Obstetric Care skills. *Concurrent Assessment* as a tool is very helpful to the obstetricians to figure out their areas of weakness and to outline their Clinical Self Improvement Plans.

Activity No. 2.3 Sustain, Organize and Implement NC Training and Clinical Supervision

- The following Basic and Advanced Neonatal Care Workshops for Physicians were conducted during the period from January to March 2003.

Governorate	Workshop	From	To	No. of Participants
Sohag	Basic NC	Jan. 12, 03	Jan. 15, 03	17
	Advanced NC	Feb. 16, 03	Feb. 20, 03	17
Menya	Basic NC	Jan. 13, 03	Jan. 16, 03	15
	Advanced NC	Feb. 23, 03	Feb. 27, 03	15
Sohag	Basic NC	Mar. 9, 03	Mar. 12, 03	21
Assiut	Basic NC	Mar. 10, 03	Mar. 13, 03	17
Total				102

- The following Resuscitation Sessions were conducted during the period from January to March 2003

Governorate	Workshop	From	To	No. of Participants
Assiut	Resuscitation session	Jan. 16, 03	Jan. 16, 03	24
Menya	Resuscitation session	Jan. 27, 03	Jan. 27, 03	24
Sohag	Resuscitation session	Mar. 16, 03	Mar. 16, 03	21
Total				69

- Technical assistance was provided to Option Period facilities in continuous visits to Phases I and II facilities in Menya, Assiut, Sohag, Beni Suef and Fayoum governorates. Each of these facilities was visited monthly by the clinical supervisor for three days to ensure implementation of neonatal protocols.
- Technical assistance continued to be provided at 19 Base Period facilities concentrating on continuous positive airway pressure (CPAP) therapy in units which provide this service. Infection control and resuscitation training for Neonatal and Obstetric staff was also performed. The clinical supervisory practice concentrated on emphasizing the use and sustainability of the QA checklists for assessment of the training (Concurrent Checklist) and Clinical Performance (Retrospective Checklist). A total of 344 supervisory days were carried out from January – March 2003.

- The training program for I.V. fluid preparation and mixing was done in an additional three units. These units are:
 - Akmeim D.H. in Sohag
 - Gehina D.H. in Sohag
 - Deir Mowas D.H., in Menya
 - A pilot for the use of a closed system for infusion of a closed system for infusion of I.V. fluids in the neonatal units to reduce the incidence of infection was conducted in Embaba General Hospital. The pilot was coordinated by Dr. Hany Ali.

Governorate	Workshop	From	To	No. of Participants
Sohag	NICU I.C.	Feb. 18, 03	Feb. 20, 03	8 physicians 5 nurses
Sohag	NICU I.C.	Mar. 15, 03	Mar. 17, 03	5 physicians 11 nurses
Menya	NICU I.C.	Mar. 22, 03	Mar. 24, 03	7 physicians 13 nurses
Total				20 physicians 29 nurses

- One CPAP workshop was done, and was coordinated by Dr. Hany Ali, Director of The Neonatal Unit, George Washington University, Washington D.C. USA.

Governorate	Workshop	From	To	No. of Participants
Qena	CPAP	Jan. 4, 03	Jan. 5, 03	22 physicians 10 nurses

- Another follow up training course on CPAP was done in Beni Suef General Hospital for one day by Dr. Hany Ali as well

Activity No. 2.4 Sustain, Organize and Implement Nursing Training and Clinical Supervision

- Two EOC workshops for nurses were conducted in Sohag and Assiut governorates. Trainees were instructed on nursing procedures in the obstetric department and delivery room. The workshops were held on the following dates:

Governorate	From	To	No. of Participants
Sohag	Jan. 11, 03	Jan. 16, 03	22
Assiut	Mar. 15, 03	Mar. 20, 03	16
Total			83

- Technical assistance and continuous OJT/Clinical Supervisory visits were continued to districts in Fayoum, Beni Suef, Qena, Sohag, Assiut and Menya governorates. Each of these districts was visited from six to nine days by the nurse supervisors to ensure implementation of the protocols.

- Two Neonatal Care Workshops for Nurses were conducted in Sohag and Menya, as follows:

Governorate	From	To	No. of Participants
Sohag	Jan. 18, 03	Jan. 23, 03	23
Menya	Mar. 15, 03	Mar. 20, 03	21
Total			44

Activity No. 2.5 Sustain, Organize and Implement Nurse Midwifery Training and Clinical Supervision

- A four months Midwifery Training Course (November 2002 – March 2003), was completed in Sohag Governorate, and was attended by 24 nurses. The graduation ceremony, will take place during the month of May 2003.

Activity No. 2.6 Strengthen Other Clinical Support Services

2.6.1 Anesthesia Services

- OJT for safe obstetric anesthesia (preoperative visits, monitoring during operation time and at recovery time, general and regional anesthesia, infection control) was conducted in the following facilities:
 - Sohag GH, Gerga DH, Tahta DH, Tema DH, Maragha DH (Sohag)
 - Menya GH, Samalout DH, Abu Qurkas DH, Beni Mazar DH, Deir Mowas DH (Menya)
 - Assiut GH, Specialized H, New Eman DH, El Ghanayem DH, El Kouseyah DH(Assiut)
 - Nasser DH, Somosta DH (Beni Suef)
 - Senores DH and Tamia DH (Fayoum)
- Assessment of the present status of anesthesia equipment was performed and a procurement plan was completed.
- In cooperation with the EOC coordinator, cases of maternal mortality were investigated and avoidable cases were discussed with staff and administration of the concerned hospitals. A self-improvement plan was developed at each facility.
- Three CEOC workshops were conducted, in each of Menya, Assiut, and Sohag governorates. The workshops emphasized hypovolemia as a major contributing factor in maternal death. Obstetricians were instructed on the proper management of hypovolemia, including adequate resuscitation, first aid management, intravenous fluid therapy, and blood products transfusion. The workshops were held on the following dates:

Governorate	From	To	No. of Participants
Assiut	Jan. 11, 03	Jan. 20, 03	24
Menya	Jan. 21, 03	Jan. 30, 03	24
Sohag	Mar. 11, 03	Mar. 20, 03	21
Total			69

- The anesthesia module was developed.
- Preparation of the manual for anesthesia technician training program (final editing) was completed.
- The clinical performance monitoring indicators (concurrent assessment) for anesthesia were developed and are ready for implementation.

2.6.2 Emergency Medical Services (EMS)

- Service standards for EMS were completed and sent for publishing.
- A draft of Maternal and Neonatal Emergency Medical Service, Manual for Physicians was produced and is currently being revised.
- A binder on *Emergency Service for Obstetric and Neonatal Care in Upper Egypt Pilot Hospitals* was developed to summarize the processes and progress of this task activity. The binder will be used for coordinated actions with relevant sectors in the MOHP.
- A draft of *Emergency Room Manual for Nurses (Arabic)* was developed and is being revised.
- An organizational structure for Emergency Departments (ED), compatible with the local context, was developed and set up in the following facilities: El Menya General Hospital, Samalout District Hospital (Menya Governorate), Sohag General Hospital, Tahta District Hospital (Sohag Governorate), Assiut General Hospital and El Eman Specialized Hospital (Assiut Governorate), Maghagha District Hospital ((Menya Governorate), Tema District Hospital (Sohag Governorate), and Kouseyah District Hospital (Assiut Governorate).
- OJT supervisory visits were conducted at four general hospitals (Menya, Sohag, Assiut and New Eman) and five district hospitals (Samalout, Tahta, Kouseyah, Tema and Maghagha District Hospitals). Visits were conducted once per month for each of the nine facilities. A total of 24 visits were conducted for the 9 facilities during the period from January 2003 to March 2003:

Workshop	Governorate	From	To	No. of Participants
EMS (Physicians)	Sohag	Jan. 5, 03	Jan. 6, 03	19
EMS (Nurses)	Menya	Feb 4, 03	Feb. 5, 03	21
EMS (Nurses)	Sohag	Mar. 5, 03	Mar. 6, 03	17
Total				57

- A combined visit by an Emergency Medical Systems consultant from the USA, a USAID representative, the JSI Team and EMS/MOHP, was conducted to Menya Governorate to evaluate the impact of project interventions on the performance of Emergency Departments. Feedback was positive.

2.6.3 Blood Bank Services

- The Blood Bank Manual was developed
- Blood Transfusion Service Standards and Blood Bank Monitoring Checklists were developed
- Infection Control at Blood Banks Protocol was developed.

2.6.4 Laboratory Services

- The laboratory activities are done in cooperation with the Central Department of Laboratories, MOHP. The Laboratory Services aim to develop physician skills in requesting appropriate tests and interpreting test results, particularly in critical cases. The above mentioned activities also help in bridging the communication gap between clinicians (laboratory users) and Laboratory Service providers. Activities also aim to better coordinate the link between hospitals, the Governorate Health Department and the MOHP Central Laboratory Department. Training of Technicians on the technical use of equipment will be the responsibility of the Central Laboratory Department at the MOHP as agreed.
- A Guide to Clinical Aspects of Laboratory Services was drafted and is currently being revised
- A list of essential laboratory investigations for General and District Hospitals was developed in conjunction with the Central Laboratory Department, MOHP.
- A list of available laboratory investigations during and after regular working hours was developed by the Laboratory Department in each of the pilot hospitals.
- A policy on the use of the Integrated Laboratory was developed in each governorate to provide bacteriological laboratory services for hospitals where this was lacking. Implementation of the policy started in Assiut GH. Strengthening of this integrated microbiology service needs combined effort from HM/HC, Central Department of Laboratory and Local Governorates.
- Laboratory Committees have been established in pilot hospitals in the three governorates of the Option Period. The duties of these committees are as follows:
 - Establish and monitor laboratory services at the hospital
 - Issue local guidelines
 - Solve local problems, and
 - Follow-up on the use of the laboratory manual
- A national revised *Laboratory Request Form* is being developed in the Central Laboratory Department and is in the process of finalization and approval.
- A *Laboratory Service Standards Guide* is under development and will target the laboratory committee members
- A *Laboratory Checklist* was developed to be used by JSI Clinical Supervisors during their field visits to collect information, monitor performance and record incidence reports related to laboratory services in their visited facilities.
- Two laboratory services workshops were conducted during the last quarter. The workshops focused on the clinical aspects of laboratory services and

clinician contribution to good laboratory performance. The workshops were scheduled as follows:

Governorate	From	To	No. of Participants
Sohag	Feb. 25, 03	Feb. 25, 03	21
Menya	Mar. 26, 03	Mar. 26, 03	17
Total			38

Activity No. 2.7 Infection Control Activities

- A meeting was conducted on January 21, 2003 with the central Infection control unit director /MOHP to discuss coordination of activities between JSI and the infection control unit.
- A two day visit was conducted on February 25-26, 2003, with the Central Infection Control Unit/MOHP Director and his assistant traveled to Sohag where the JSI Infection Control Team and Field Office staff provided assistance to select infection control teams at all Sohag hospitals. The infection control team selection included a doctor and nurse/s (one or two nurses according to hospital number of beds) whom will be dedicated according to Ministerial decree number 100/2002. These teams will be trained during April-May 2003.
- Supervisory visits were conducted to all Phase I and phase II/Option period hospitals during which, efforts were made to emphasize the importance of a comprehensive approach to infection control.
- The quarterly integrated infection control OJT/Supervisory follow-up visits were conducted at the following hospitals: Sohag General Hospital, Tahta District Hospital, Gerga District Hospital, Maragha district Hospital, Tema District Hospital, Geheina District Hospital/Sohag, Assiut General Hospital, New Eman General Hospital, Specialized Hospital, Ghanayem District Hospital, Kouseyah District Hospital/Assiut and Menya General Hospital, Samalout District hospital, Abu Qurkas District hospital, Beni Mazar District Hospital, Deer and Mowas District Hospital/ Menya.
- Implementation of behavior change infection control activities were planned. The plan based on research shown that sepsis is the third leading cause of both maternal and neonatal deaths. However, there are different issues related to IC in each hospital that affect sepsis rates. IC Committees and IC Teams have been created for each hospital but are not fully active. Six major infection control issues have been highlighted due to their importance and will be addressed, the IC Procedures are as follows:
 - Proper hand washing & scrubbing
 - Proper IV Preparation and medicine preparation
 - Proper use of protective devices
 - Proper processing of instruments
 - Proper patient preparation, and
 - Proper waste disposals
- Each of the six different IC procedures will be investigated by conducting a behavioral analysis to understand why providers are not practicing/following the right infection control procedures, barriers and resistances to practicing proper infection control will also be identified. Based on the assessment

appropriate interventions to address the major IC issues will be designed to improve provider behavior related to infection control issues.

- Two OR and Two CSSD workshops were conducted during the last quarter. The workshops were held on the following dates:

Workshop	Governorate	From	To	No. of Participants
CSSD	Sohag (For Sohag & Assiut Nurses)	Mar. 8, 03	Mar. 9, 03	28
OR	Sohag (For Sohag & Assiut Nurses)	Mar. 11, 03	Mar. 13, 03	29
CSSD	Menya	Mar. 11, 03	Mar. 12, 03	16
OR	Menya	Mar. 29, 03	Mar. 31, 03	20
Total				93

- Three one-day Infection Control training sessions were conducted at the three CBT EOC workshops. The training was scheduled as follows:

Governorate	From	To	No. of Participants
Sohag	Mar. 18, 03	Mar. 18, 03	20
Assiut	Jan. 17, 03	Jan. 17, 03	20
Menya	Jan. 28, 03	Jan. 28, 03	20
Total			60

Activity No. 2.8 Involve Private Sector Services Provided by Physicians and Pharmacists in HM/HC

- Information was updated on private sector providers with the assistance of local syndicates, the Private Sector MOHP Departments and the Pharmacy Inspection Departments. The updates included the number of private clinics, polyclinics, private hospitals and pharmacies in the target governorates.
- Three CBT EOC training courses were conducted for private physicians on the following dates:

Governorate	From	To	No. of Participants
Assiut	Jan. 17, 03	Jan. 17, 03	20
Menya	Jan. 28, 03	Jan. 28, 03	20
Sohag	Mar. 18, 03	Mar. 18, 03	20
Total			60

Activity No. 2.9 Implement IMCI Program in New Governorates

- No activities were done this quarter.

Activity No. 2.10 Conduct Refresher Courses for Dayas

- No activities were done this quarter.

Activity No. 2.11 Teleconferencing and Off-Shore Training

- During March 2003, the Ninth Teleconference session *Harmful Practices and Substandard Care* was conducted with George Washington University.
- Dissemination for the nine teleconferences modules, supporting materials and videotapes was planned.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.3 TASK THREE: Public and Private Provider Partnerships with Communities to Develop and Manage District Plans

Accomplishments

Activity No. 3.1 Community Level Involvement

- During this quarter, 12 community action plans (CAPs) were developed in ten districts in Assiut, Sohag and Menya. These CAPs were submitted to District Health and Safe Motherhood Committees for incorporation into the district health plans.
- During the base period, a *second round* of community needs assessments (CNA) were conducted in 24 districts in Qena, Fayoum, and Beni Suef. The purpose was to assess the impact of HM/HC interventions on community knowledge and health practices. Based on the results of the second round of CNA, the CAPs have been updated, and will be incorporated into the district health plans.

Activity No. 3.2 District Level Interventions

- Three four-day workshops on quality management were conducted in Sohag for hospital SMCs. The workshops were attended by a total of 60 participants representing hospital SMCs from Geheina, Akmeim, Tema, El-Balyana, Dar El-Salam, El-Mounshaa, Maragha, and Saqolta. The objective of the workshops was to enhance capabilities in the areas of planning, facility management, monitoring, quality care and service standards compliance. The 3 workshops were scheduled as follows:

From	To	No. of Participants
Jan. 27, 03	Jan. 30, 03	21
Mar. 10, 03	Mar. 13, 03	22
Mar. 24, 03	Mar. 27, 03	17
Total		60

- Two three-day workshops on management and planning for district SMCs were conducted in Sohag. The workshops were attended by a total of 39 participants representing SMCs from El-Balyana, Tema, Dar El-Salam, and El-Mounshaa districts. For the practical training sessions of these two workshops, participants were asked to present a situation analysis based on district data for MCH services. The analysis was used to develop district HM/HC plans based on the *Revised Guidelines for District Planning and Monitoring*. Task 7 training staff conducted a new workshop session on service provider sensitization, which is an important addition to the workshop agenda. A training report was developed which includes the results of pre/post-training tests, participation and course evaluation. The 2 workshops were scheduled as follows:

From	To	No. of Participants
Jan 13 2003	Jan 15, 2003	21
Jan. 21, 2003	Jan 23, 2003	18
Total		39

- Meetings were conducted for district SMC members and the drafts of district HM/HC plans were reviewed.
- Quarterly progress reports were developed by district SMCs detailing achievements during the fourth quarter of 2002. These achievements were compared to the respective 2002 Annual Work Plans (AWPs), and HM/HC indicators.

Activity No. 3.3 Governorate Level Participation

- Three two-day workshops on Better Utilization of Service Improvement Funds were conducted in each of Sohag, Assiut and Menya. The workshops were attended by a total of 129 participants representing facility, district, and governorate level SMCs. Ministry of Finance representatives were also in attendance. The workshops were scheduled as follows:

Governorate	From	To	No. of Participants
Sohag	Feb. 5, 03	Feb. 6, 03	54
Assiut	Feb. 19, 03	Feb. 20, 03	50
Menya	Feb. 26, 03	Feb. 27, 03	25
Total			129

- Governorate SMC meetings were conducted in which district quarterly progress reports were discussed.
- A joint meeting attended by 124 participants representing members of governorate and district safe motherhood and health committees was conducted in Menya on February 25, 2003 to review achievements and district quarterly reports.

Activity No. 3.4 National Level Oversight

- In collaboration with TAHSEEN Project, a presentation on HM/HC Management, Planning and Continuous Quality Improvement activities was conducted on February 4, 2003. A briefing about this meeting is included in Task 12 of this report.

Activity No. 3.5 Quality Assurance

- New training materials in *Continuous Quality Improvement (CQI)* have been finalized and used in workshops during this quarter. These materials replace the former course entitled *Service Standards & Quality Assurance (QA)* in order to reflect the latest concepts on the implementation of quality management in healthcare. They have been merged with planning and monitoring guidelines to form the training materials used during the quality management workshops directed to SMC members of general/district hospitals.

- Quality reports covering both managerial and clinical aspects of performance for obstetrics departments in the fourth quarter (Q4), 2002 have been produced and submitted to SMCs. Two reports have been produced so far (Q3 & Q4) for phase two district hospitals of Menya, Assiut and Sohag governorates, while three reports have been accumulated for phase one general/district hospitals. According to the reports, significant improvement in both managerial and clinical care processes has been achieved. The reports were effectively used during SMC meetings to identify problem areas and opportunities for improvement. They were also used as critical inputs for developing self-improvement plans. Many identified problems could be solved at the facility level.
- A new manual has been drafted to be used at the obstetrics department level. It describes department managerial processes and standards, and monitoring tools for both managerial and clinical processes. It is intended to support the implementation of the CQI approach at the department level.
- Coordination with other tasks (especially task 2) is on-going to upgrade relevant standards and monitoring tools towards more effective definition and measurement of quality for CQI purposes.
- In close coordination with the HM/HC QA unit, three 3-day workshops were conducted in Sohag governorate to support institutionalization of the MCH QA system. The workshops addressed service standards and monitoring checklists for the different MCH activities, and the use of these tools by SMC members for continuous monitoring and improvement of services. The workshops were attended by a total of 58 participants representing district SMC members of Dar El-Salam, Tema, El-Mounshaa, El-Balyana, El-Maragha, and Saqolta. The workshops were scheduled as follows:

From	To	No. of Participants
Jan. 13, 03	Jan. 15, 03	20
Jan. 21, 03	Jan. 23, 03	18
Mar. 10, 03	Mar. 12, 03	20
Total		58

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.4 TASK FOUR: Monitoring System in place to Track Utilization and Impact and Provide Feedback

Accomplishments

Activity No. 4.1 Assist the MOHP to Set Up MHIS Centers at District Level in Coordination with Family Planning

- Currently nine district Management Health Information Systems (MHIS) Centers in Giza are operating: North Giza, El Omrania, South Giza, El Haram, Giza Markaz, El Warrak, El Badrashein, El Ayat, and Boulaq El Dakroul.
- The installation of dial-up terminals for data transfer at the district level is currently in process. The computers were provided by Family Planning (MOHP) to all districts in Giza except Dokki and El Wahat al Bahareya. The computers lacked the Fax/Modem cards necessary for dial-up connections to the governorate MHIS Center. JSI procured the Fax/Modem Cards which are now ready for installation. In March, the Giza governorate MHIS Center installed a working telephone line. Dial-up connections are therefore expected to be ready for operation in April.
- Assessment for MHIS center renovations requirements is currently in process for four districts: Dokki, South Giza, Menshaat El Qanater, and Etfeih.

Activity No. 4.2 Design and Upgrade User Friendly Software for MHIS

- The new HIS software application is developed and the Planning and Monitoring System is completed.
- During January, the new system was presented at NICHHP premises. The presentation was attended by Dr. Esmat Mansour, Dr. Hanem Abdel Aziem, Dr. Hassan El Kalla, Dr. Sanaa Ibrahim, representatives from other MOHP departments, as well as key USAID persons. A similar presentation was delivered in Dr. Hanem Abdel Aziem's office to her key staff.
- HM/HC project in coordination with NICHHP organized a meeting in Dar-el-Defaa El Gawy where NICHHP announced the release of the new system and its pilot implementation in Alexandria and Menya beginning in March 2003.
- HM/HC and NICHHP established an implementation team to run the pilot implementation in the aforementioned governorates.
- Training for MHIS technical specialists took place during this quarter in four events:

Governorate	From	To	No. of Participants
Cairo	Feb. 16, 03	Feb. 20, 03	10
Cairo	Feb. 23, 03	Feb. 27, 03	12
Alexandria	Mar. 15, 03	Mar. 19, 03	10
Menya	Mar. 22, 03	Mar. 26, 03	12
Total			44

- The new MHIS Application has been installed in governorate MHIS centers in Menya and Alexandria.

Activity No. 4.3 Develop and Implement a Quality Assurance Monitoring Checklist for the District MHIS Centers

- NICHIP in coordination with HM/HC Project, will start establishing a National Health Informatics Resources Database. It is suggested that the MHIS quality assurance monitoring checklist will serve as a basic tool for data collection for the Health Informatics Resource Database.

Activity No. 4.4 Establish Monitoring Mechanisms at Facility and Community Levels

- Curricula for two workshops were developed. One for health officers for data use, and the other for MHIS Center staff members to provide technical support for health officers in using the system. The data use workshops will be based on the new MHIS application and the Planning and Monitoring system.
- April-June 2003 Workshops on data use for target districts in Sohag, Menya and Assiut, are currently being planned by Tasks Three and Four.

Constraints

- None.

Proposed Actions to Overcome Constraints

- None.

C.10.5 TASK FIVE: Research Activities

Accomplishments

Activity No. 5.1 Assist in the Development of Policy/Procedure Guidelines for the Maternal Mortality Surveillance System (MMSS)

- Completed.

Activity No. 5.2 Training on the Maternal Mortality Surveillance System

- MMSS was introduced to Ob/Gyn and Anesthesiologists working in district/general hospitals and at the private sector in the following governorates:

Governorate	From	To	Number of participants
Luxor	Jan. 25, 03	Jan. 26, 03	30
Qena	Jan. 27, 03	Jan. 28, 03	40
	Jan. 29, 03	Jan. 30, 03	40
Sohag	Feb. 24, 03	Feb. 25, 03	28
	Feb. 26, 03	Feb. 27, 03	24
Total			162

Activity No. 5.3 Implement the Maternal Mortality Surveillance System in Nine Upper Egypt Governorates

- The MMSS Performance Monitoring Checklists were developed and tested to assess the performance of health offices, health districts, and health directorates.
- Based on the results of the pilot-test, the monitoring checklists were revised and refined. The tool was then used by a team from MOHP/HM/HC and JSI/FETP physicians. The following table shows governorates where field visits were conducted to monitor the performance and dates of visits.

Governorates	From	To	Number of District visited	Number of health office visited
Assiut	Jan. 11, 03	Jan. 16, 03	6	79
Beni Suef	Jan. 21, 03	Jan. 23, 03	4	52
Menya	Feb. 01, 03	Feb. 06, 03	6	69
Fayoum	Mar. 01, 03	Mar. 03, 03	5	41
Luxor	Mar. 15, 03	Mar. 16, 03	2	16
Qena	Mar. 17, 03	Mar. 20, 03	7	65
Total			30	322

- The results of the above field visits that revealed specific areas of weakness were discussed in the Safe Motherhood Committees at the governorate level and corrective actions were taken.

Activity No. 5.4 Identify and Conduct Operation Research Studies

- Preparatory actions to conduct five operation research studies were completed and implementation was started:

OR1 A: Premixed intravenous fluid formulae for neonates for the prevention of nosocomial infection.

- Implementation of this study is currently under way at the Neonatal Unit at Kasr El Aini Hospital, Cairo University.

OR1 B: Cost-effectiveness study of premixed IV fluid formulae for neonates versus regular formulae for prevention of systemic nosocomial infections.

- Due to the importance of the topic and its relation to OR1, it was decided to include this as part of OR1 despite the difference in objectives and methodology. Data collection did not start yet.

OR 2: Cost analysis and efficiency indicators of three neonatal intensive care units in Upper Egypt.

- Implementation did not start yet.

OR 3: Defining indicators and developing tools for monitoring client satisfaction for maternal and child health services from community women's perspective.

- An extensive search was done to ensure that this topic has not been studied before. The research will consist of two rounds of data collection. The first round, aims at identifying client satisfaction indicators developed from the clients' perspective. These indicators will be used to develop tools for the routine collection of client satisfaction data. The second component of the study will test these tools to select the most suitable ones for routine data collection. Preparations for the first round of data collection are currently taking place.

OR 4: Taxonomy of maternal and child health terms.

- A comprehensive list of terms used in maternal and child health were compiled by the relevant clinical staff, tested in the field and modified accordingly. Guides for the focus group discussions and in-depth interviews were developed and pilot tested. Data collection and analysis are currently taking place.

OR 5: Reasons for the poor availability of blood for emergency obstetric care in Upper Egypt.

- Data collection tools were completed, pilot tested and revised. Training of data collectors was completed. Currently data collection, entry and verification are taking place.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.7 TASK SEVEN: Better Social Community Services

Accomplishments

Activity No. 7.1 Community Needs Identification and Decision-Making

- Fourteen one-day workshops were held in Menya, Sohag and Assiut to train Community Health Committees (CHCs) on the Community Needs Identification and Decision-Making Tool (CNI-DMT) that will be used in their respective communities.
- The workshops were attended by a total of 112 participants representing CHC members, heads of local administration units, and managers of the health facilities in these communities. The main results of the workshops were the scheduling agreements for the Rapid Household Surveys Workshops that will be conducted in their communities; and the nomination of the Outreach workers who will be trained to conduct the surveys.

Governorate	District	Community	Date
Assiut	El Fath	El Fath	February 2003
		El Atawla	January 2003
	El Kouseyah	Fazara Beni Koura El Kouseyah	March 2003 March 2003 March 2003
Sohag	Geheina	Eneibis	February 2003
	Tema	Om Dooma	January 2003
		El Rayayna Tema	January 2003 January 2003
El Mounshaa	Awlad Hamza Awlad El Sheikh	March 2003 March 2003	
Menya	Deir Mowas	Deir Mowas	February 2003
	Beni Mazar	Sandafa Beni Aly	January 2003 March 2003

- In Assiut, Sohag and Menya, five-day workshops were held in 12 out of the 14 communities where CHC members were trained. The workshops trained Community Outreach Workers on conducting Community Needs Identification-Rapid Household Surveys (CNI-RHS). 15 Outreach Workers from each community (a total of 180) were selected and trained on the CNI-RHS process, and they subsequently conducted the process in each of the following communities.

Governorate	District	Community	Date
Assiut	El Fath	EL Fath	February 2003
		El Atawla	January 2003
	El Kouseyah	El Kouseyah	January 2003
Sohag	Geheina	Eneibis	February 2003
	Tema	Om Dooma	January 2003
		El-Rayayna	January 2003
		Tema	January 2003
El Menshah	Awlad Hamza Awlad El Sheikh	March 2003-03- 30 March 2003	
Menya	Deir Mowas	Deir Mowas	February 2003
	Beni Mazar	Sandafa Beni Aly	January 2003 March 2003

- The workshops were preceded by the development of community profiles for each of the ten communities. These profiles include demographic data collected from the local administration units and health units of the communities. The main purpose of these profiles is to portray communities with their unique characteristics, services and resources.
- The main objectives of the workshops were to learn to use the RHS to identify:
 - key behaviors related to MCH issues – whether they are followed by women or not,
 - whether danger signs during pregnancy, delivery, postpartum and care for the newborn are known by women or not,
 - main obstacles that could hinder accessing the MCH services in the communities.
- To conduct the RHS, a random sample of 50 mothers with a baby less than one year old was selected from the Birth Register of the health units for interview during the RHS.
- Over a five-day period, the RHS interview process was conducted in each community and the results were manually tabulated and finalized for action.
- The workshops were preceded by the development of community profiles for each of the ten communities. These profiles include demographic data collected from the local administration units and health units of the communities. The main purpose of these profiles is to portray communities with their unique characteristics, services and resources.
- Following the RHS, twelve CHCs workshops were conducted to:
 - share the results of the RHS,
 - identify the community needs/problems related to MCH issues,
 - Prioritize and analyze these problems,
 - suggest alternatives for solutions to address these problems and meet the community needs,

- develop Community Actions Plans (CAPs) to guide the community actions in this respect.
- The action plan workshops were attended by 360 participants who represent CHCs members, Community Outreach Workers who conducted the CNI-RHS process and Heads of the Village Executive Councils in these communities.
- The CAPs describe the problems/needs of the community, their priority order, their causes, suggested interventions, and the responsible persons and time frame for each intervention. Some of the CAPs problems/needs are addressed at the community level. Others that are beyond the capability of the community are submitted to the district to be incorporated in the district health plans.
- Twenty-Four three-day workshops were conducted for the second round of CNA in Qena, Fayoum and Beni Suef to assess impact of the HM/HC interventions on the community health knowledge and behaviors. The workshops followed the same pattern of the first Community Needs Assessment (CNA). During these workshops, a total of 360 Community Outreach Workers (15 from each community) were trained and accordingly implemented the surveys in the following communities.

Governorate	District	Community	Date
Qena	Qena	Karm Omran	February 2003
		Awlad Amr	February 2003
		Dandara	March 2003
	Deshna	Abu Manaa	January 2003
		Fao	January 2003
	Naga Hamadi	El Rahmaneya	March 2003
		Gharby Bahgora	March 2003
		Hew	March 2003
		El Halfaia Bahary	March 2003
	Naqada	Bahary Gamoula	January 2003
	Abu Tesht	Abu Shousha	January 2003
		Bakhaness	January 2003
Farshout	El Araky	March 2003	

Governorate	District	Community	Date
Fayoum	Fayoum Urban	Sheikh Hassan	January 2003
		El Hadka	February 2003
	Etsa	Defno	March 2003
		Kalmshaa	February 2003
Ebshway	El Shawashna	El Agameen	January 2003
		Kouta	January 2003
			March 2003
Fayoum Rural	El Lahon	Desia	March 2003
			March 2003
Beni Suef	El-Fashn	El Fant	January 2003
		Delhanes	January 2003

- Results of the surveys were shared with the Community Health Committees (CHC) so as to adapt the community action plans accordingly. This was achieved in 24 CHC workshops attended by 720 participants representing CHC members, the Outreach Workers who conducted the RHS and Heads of the Village Executive Councils in the targeted communities.

Activity No. 7.2 Community Health Education

7.2.1 Health Providers Sensitization

- Two workshops were conducted for 39 health providers and decision-makers from the districts of El-Balyana, Tema, Dar El-Salam, and El-Mounshaa in Sohag. Participants were alerted to the community perceptions and beliefs related to MCH issues. The main objective was for health providers to keep these perceptions and beliefs into consideration during patient interactions:

From	To	No. of Participants
Jan. 13, 03	Jan. 15, 03	20
Jan. 21, 03	Jan. 23, 03	19
Total		39

7.2.2. Integrating HM/HC Messages in the Literacy Curricula of General Authority for Literacy and Adult Education (GALAE)

- As a result of signing the Memorandum of Cooperation with GALAE for the replication of the literacy pilot – *Integrating Health Messages in the Literacy Curricula of GALAE* – in Luxor, Cairo and Giza; and for working with the GALAE central level trainers, two workshops were conducted as detailed below.
- The first workshop was conducted over a five-day period from February 16 through 20, 2003 for 42 GALAE literacy facilitators and supervisors from Luxor. The objective of the workshop was to discuss the replication of the previous experience of – *Integrating Health Messages in the Literacy Curricula*

of GALAE – in Luxor (about 300 literacy classes). The workshop was attended by Mr. Ahmed Abul Wafa, Head of GALAE Luxor, Dr. Ahmed Abdel Moneim, Luxor Health Director and General Samir Rizk on Behalf of The Chief of Luxor Supreme Council. Workshop participants were trained to instruct teachers on the delivery of HM/HC health messages within the GALAE literacy curricula.

- The second workshop was conducted for 40 literacy facilitators and supervisors from Cairo, Giza and from the central level . The workshop was conducted on March 10-12, 2003. It was designed to prepare trained literacy teachers to become trainers of other literacy teachers in Cairo and Giza. Pairs of trained teachers, with the support of their supervisors, would subsequently train between 10 and 15 new teachers through a decentralized plan in Cairo and Giza.

Activity No. 7.3 Training of Health Educators

- No activities were done this quarter.

Activity No. 7.4 Female Genital Cutting

- A TOT refresher workshop was conducted in Assiut Governorate. The participants were nominated from amongst Health Social Workers, Health Educators and Community Outreach Workers of non-government organizations (NGOs) in Menya, Sohag and Assiut Governorates. The workshop was scheduled as follows.

From	To	No. of Participants
Feb. 18, 03	Feb. 20, 03	9

- TOT and female genital cutting (FGC) curricula were finalized and ready for printing in the next quarter.

Activity No. 7.5 Engaging the Private Sector

- Work is pending for Minister of Health and Population approval on the Public/Private Strategy that was submitted on September 2002.
- A letter was sent to Procter & Gamble Co. to request donation of 6 months' supply of detergents for the laundry rooms that were established in Menya, Sohag and Assiut hospitals.

Activity No. 7.6 Continuing Community Activities

- The Woman Health Card was approved by HM/HC Executive Director and was sent to TAHSEEN/Catalyst Project to review the Family Planning section in this card.
- The changes recommended from the pretesting research, were inserted in the Counseling Cards. A RFP, for printing these cards, was developed and is ready for sending out in the next quarter.
- The Technical content and flow chart of the CD development were finalized. An RFP was sent out to four Media Companies to submit their proposals on the development of nine Interactive CDs.

- The success stories and lessons learned have been collected, revised and finalized by the relevant task managers.
- The shooting of an extra teleconference session on Harmful Practices and Substandard Care was shot on March 20, 2003. Also, the offline presentation of the second teleconference on *Hypertensive Disorders in Pregnancy and Intra-Uterine Growth Retardation* was re-shot in the same day of this extra teleconference. The editing and revision of the eighth teleconference video tapes, have been finalized and are currently being duplicated (Betacam and VHS) by the production house. A distribution plan for the eight video tapes will be developed in the next quarter to the different target audiences.
- Three stories were developed about three technical people working in JSI in order to document HM/HC activities implemented in the neonatal, EOC and community components. The stories were developed for the 25th Anniversary Book that would be published by JSI Boston. A photo-shooting day was organized for neonatal, EOC and Community JSI staff in Fayoum Governorate on March 23, 2003. The three stories were finalized and sent out to JSI Boston for publishing.
- Nine abstracts were approved for the Global Health Conference that would take place in Washington in May, 2003. Drafting and developing the nine presentations is now in process.
- The USAID Washington Brown Bag Meeting was scheduled on May 17, 2003. An event Description Form for this event was developed and finalized.
- The HM/HC Publications booth and 23 Posters were prepared and displayed in the entrance of the USAID building in Maadi, Cairo to document the different HM/HC activities and achievements.

Activity No. 7.7 Strengthen IPC Training for Physicians and Nurses

- Translation of the IPC one day module from English to Arabic was finalized. Initiation of the IPC plan and printing of IPC Module will be done next quarter.

Activity No. 7.8 Taxonomy of MCH Terms

- AMER Research Co. was selected to conduct the Taxonomy of MCH Terms. The contract was developed and signed by both parties.
- The pretesting results of the discussion guide were integrated into the taxonomy research questionnaires. Modifications of the three taxonomy lists on Anesthesia, Ob/Gyn and neonatology have been inserted and finalized.
- Field research was carried out in Menya Governorate from February 13-28, 2003. Six Focus Group Discussion and 12 in-depth interviews were conducted in the Menya Governorate. The first report on the Menya Governorate was submitted for JSI review and approval.

Activity No. 7.9 Behavior Change

- During this quarter, a literature review of the tools to be used in developing the behavior change module has been completed. The behavior change module will be developed next quarter.
- Work is on-going to implement the Behavior Change Plan.

Activity No. 7.10 Gold Star

- A final design for the MCH Gold Star Sign for PHC health facilities and hospitals was produced and made available.

Activity No. 7.11 Health Education Activities to Support SHIP in Schools

- Health education activities have been launched in all districts of Sohag, eight districts in Assiut (Shark Assiut, Gharb Assiut, Markaz Assiut, El Ghanayem, El Badary, El Kouseyah, Dayrout and Sahel Selim) and six districts in El Menya (Menya, Samalout, Abu Qurkas, Maghagha, Beni Mazar and Deir Mowas).
- Trained supervisors conducted one-day training courses for the science teachers who were assigned to implement health education activities in their schools. 643, 435 and 490 science teachers were trained in Sohag, Assiut and El Menya respectively. Health education started in target schools immediately after training of the science teachers.

Workshop	Governorate	From	To	No. of Participants
Science Technical Supervisors	Sohag	Jan. 22, 03	Jan. 23, 03	27
	Assiut	Feb. 17, 03	Feb. 18, 03	29
	Menya	Feb. 19, 03	Feb. 20, 03	23
Total				79

- Health Education program posters, booklets and video tapes were distributed to target schools in all governorates except for Beni Suef. Anemia prevention booklets for secondary school students were only distributed in El Menya governorate.
- The two Health Education Guides were distributed to be used by the health education providers in target schools:
 - Health Education Guide Part 2 was distributed to the HIO Health Educators in all Base Period governorates except for Beni Suef. It includes smoking prevention activities. It is a complementary part to the original guide that addresses anemia.
 - The Health Education Guide for science teachers was distributed to science teachers in the target schools in Sohag, Assiut and El Menya governorates. It addresses both anemia and smoking.

Activity No. 7.12 Iron Supplementation Program

- Target schools in all governorates were provided with the iron tablets and registers needed for implementing the program. Implementation started on February 1st (the beginning of the second semester of the school year 2002-2003). The delay in implementing the program was due to unavailability of cups. To overcome this problem, one disposable cup was given to each student in most schools to be used during the whole weeks of the second semester.

Activity No. 7.13 Pilot Testing of IEC for Smoking Prevention

- The smoking brochure was distributed to all target schools in the eight governorates. The brochure is used during the health education sessions by both health educators in the base period governorates, and science teachers in the option period governorates.

Constraints

- Unavailability of cups resulted in delay of iron supplementation for a whole semester; it started in February 2003 although it was planned to start as scheduled by September 2002.
- Health education program stopped in Beni Suef governorate as a result of the HIO refusal to renew the contracts of the Health Educators.

Proposed Actions to Overcome Constraints

- Start purchasing process for permanent plastic cups immediately to ensure their availability before the beginning of the coming school year; September 2003.
- Renewing contracts of the Health Educators in Beni Suef to ensure continuity of the health education program in the target schools.

C.10.10 TASK TEN: Small Grants Program**Accomplishments****Activity No. 10.1 Management and Monitoring of the Base Period Awarded 102 Grants**

- Technical and Financial Close out of (102) granted NGOs are completed.

Governorate/ District	No. of Grants or No. of NGOs	Fund Amount
Beni-Suef	8	358810
Fayoum	15	604155
Qena	50	1428500
Luxor	8	174040
Aswan	21	540868
Total	102	3,106,373

Governorate/ District	Seminars				Home visits	
	No. of seminars	Attendees			No.	Attendees
		Male	Female	Total		
Beni-Suef	510	1897	24030	25927	231201	144782
Fayoum	904	1456	27489	28945	124369	73289
Qena	2116	7909	81848	89757	407975	490775
Luxor	254	746	9668	10414	33209	39101
Aswan	608	2749	26746	29495	125519	102159
Total	4392	14757	169781	184538	922273	850106

- Partial payments were advanced to eighteen (18) NGOs with a total of LE 192,603 for ongoing grant activities.
- Tools to check on the quality of seminars and support groups of NGOs outreach workers, were developed and to be used next quarter.
- Reviewed and re-designed the trainer manual, trainee manual and training materials of proposal writing used in training of qualified NGOs.
- Developed tools and techniques (Questionnaire, problem tree and logic framework) to assess community HM/HS problems, causes and consequences.
- This will help qualified NGOs to write accurate, comprehensive and logical proposals.

Activity No. 10.2 Modify the Existing IFA and the Structure of the Review Panel

- No activities

Activity No. 10.3 Provide Grants to Capable Local NGOs through Standardized Mechanism

- Thirty-One assessed NGOs in Menya, 20 in Assiut and 54 in Sohag were oriented on HM/ HC project and its small grant program. The orientation included the following:
 - The mother and child program
 - Causes of the program
 - The project goal
 - The project components and activities
 - Criteria for selecting NGOs
 - Process and steps for working with the small grant program

Governorate	No. of Assessed NGOs	Qualified NGOs after assessment
Sohag	54	31
Menya	31	27
Assiut	20	14
Total	105	72

- Training was conducted on proposal writing for 21 Qualified NGOs out of 31 assessed in Sohag.

From	To	No. of NGOs	No. of Participants		Trainers
			From NGOs	From MOISA	
Mar. 24, 03	Mar. 27, 03	11	22	5	Worker Specialist and CDSs' of Sohag, Assiut and Menya
Mar. 30, 03	Apr. 2, 03	10	20	5	
Total		21	42	10	

Activity No. 10.4 Training Awarded NGOs (Technically and Financially)

- No activities were done this quarter.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.11 TASK ELEVEN: Commodity Procurement Program

Accomplishments

Activity No. 11.1 Commodities

- JSI/TCA completed the procurement process and issued Purchase Orders for a total of US\$ 4,391,677.66. The total amount committed to date is 49% of the total procurement budget.
- TCA has procured the following items this quarter per the Life of Contract Procurement Plan:
 - Local medical furniture, equipment, and supplies
 - Local washing machines and dryers
 - Local computing and audio-visual equipment
 - Local air conditioners
 - CPAP supplies
- Technical specifications for the remaining offshore medical equipment requirements have been drafted and the IFB is being prepared for release.
- A spreadsheet has been developed to define the remaining local medical requirements and the RFQs will be released soon.
- Offshore medical equipment awarded under IFB #12 was received in Cairo and is being prepared for distribution to MOHP facilities. Additional containers are being shipped now to Cairo.
- The vehicles have been received in Cairo and pre-delivery inspection (PDI) of the vehicles is underway. After the completion of the PDI, the vehicles will be turned over to the MOHP for final distribution.
- JSI and TCA have accepted delivery and installed the following items for Option Period recipient locations this quarter:
 - Medical equipment, furniture, and supplies in completed Phase One and Phase Two facilities
 - Interim requirements for medical equipment, furniture, and supplies for select Phase Two facilities
 - Air conditioners for Phase One facilities (General/District Hospitals and BEOCs) and for District Health Offices
 - Office furniture for select District Health Offices
 - Training room furniture and audio-visual equipment for General Hospital Resource Rooms
 - Medical supplies for Cairo University and Imbaba Hospital infection control activities
- Discussions have continued with ICS, Preemicare, and Hi-Med regarding the Preemicare incubators. All correspondence has been shared with USAID.
- Inventory in the warehouse was maintained and a physical inventory was completed.
- The computerized Commodity Procurement Database was maintained and produced required reports.
- The Procurement Milestone documenting the procurement of \$3 Million in commodities was completed and submitted to USAID for approval.

- Distribution reports were provided to the GOE Customs Representative and Sales Tax Authority as required.

Activity No. 11.2 Renovations

- All the bidding, contracting and financial procedures related to the renovation process were implemented according to the renovation plan.
- Meetings have been held with the MOHP and USAID regarding Phase II renovations to be funded by the MOHP.
- An RFQ for Phase II facilities requiring renovations to be funded by JSI is being finalized.

Activity No. 11.3 Publications

- A draft RFP for printing of IEC materials and counseling cards have been developed and will be sent out early next quarter.
- Two Health Education Manuals for the SHIP program were printed and delivered to the new target governorates such as Menya, Sohag and Assiut.

Governorate	Distribution Plan of the Health Education Manuals	
	Manual 1	Manual 2
Aswan		22
Luxor		32
Beni Suef		
Fayoum		22
Qena		32
Menya	600	
Assiut	485	
Sohag	755	
Total	1840	108

- Three Hundred Thousand (300.000) copies of the Anti-Smoking Flyer were printed and delivered to JSI, Maadi warehouse. A distribution plan to disseminate these flyers through the SHIP program has been developed and distributed as follows:

Governorate	Distribution Plan of the Anti-Smoking Flyer
Aswan	22.346
Luxor	24.176
Beni Suef	27.157
Fayoum	33.591
Qena	
Menya	50.030
Assiut	48.732
Sohag	54.812
Total	260.844

- An RFP was sent out to four Media Companies to submit their proposals on the development of a nine Interactive CDs. Selection of the successful bidder and the initiation of the CD development process will start early next quarter.
- On-going activities include the Design of the Commodities Forms and the Admission Sheet.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.12 TASK TWELVE: Coordination Activities

Accomplishments

MOHP/ USAID/ JSI Monthly Coordination Meeting

- During this quarter, Monthly Coordination Meetings were held on regular basis and involved the Undersecretary for Integrated Health Care, HM/HC Executive Director, USAID/ HM/HC Team Leader and JSI Chief of Party.
- The primary purpose of the meeting is to review the Monthly Work plan, coordinate activities and secure the involvement of HM/HC Project Staff in joint missions with JSI staff.
- The meeting also discusses areas of intra-ministerial coordination and integration, as well as coordination with other ministries and government and non-government organizations.
- Annex I contains the minutes of the meetings for each of January, February and March, 2003.

MOHP-Intra-Ministerial Coordination

A- MCH, HR Development and Nursing Departments

- A meeting was held with Dr. Bahya Fouad, MOHP Undersecretary for nursing services, on January 4, 2003 to discuss ways and means to strengthen nursing services capacity in target governorates. The meeting concluded with the following:
 - Conduct situation analysis of nursing services (availability, development, qualifications and experience, training, supervisory system, etc..) to identify problems and areas of weakness. Sohag is selected to be the first governorate on the list for situation analysis.
 - A one-day workshop was held on January 8, 2003 to review the revised secondary technical nursing school curriculum (covering Maternity, Pediatric, Neonatal and Community Health Nursing) and to reach a consensus on the final draft. The workshop was attended by the central Committee for Secondary Technical Nursing School Curriculum Development, headed by Dr. Azza El Hussein, Undersecretary of Research and Studies; Dr. Bahaya Fouad, Undersecretary of Nursing Services; the authors of the curriculum; representatives of HM/HC Project; Human Resources Central Department; Nursing Services Central Department and selected teachers from six secondary technical nursing schools.
 - The review process resulted in the introduction of minor modifications to the developed curriculum that could easily be incorporated.

B - IMCI

- A meeting was held with Dr. Said Madkour, National Coordinator for IMCI to obtain approval for implementation of Integrated Management of Childhood Illness (IMCI) activities in the 2 HM/HC pilot slum areas in coordination with the Family Medicine (FM) Program.

- JSI COP referred to the previous success of IMCI programs implemented in 17 target districts in Upper Egypt, and expressed the intention of HM/HC to implement the IMCI program in the pilot HM/HC slum facilities, integrating IMCI programs with FM. Drs. Madkour/ Nagati welcomed the cooperation with the following qualifications:
 - Customization of IMCI program must not compromise quality.
 - IMCI is always implemented at the district scale to save costs, especially in training.
- JSI team stressed the current political support and window of opportunity for funding of IMCI activities in slum areas by the Urban Health General Department, conditional on the success of the pilot project in the two HM/HC selected slum areas. Funding is not currently offered for district level implementation.
- By the end of the meeting the following conclusions and recommendations were set:
 - Drs. Madkour/ Nagati agreed to implement IMCI activities in 2 HM/HC slum areas in collaboration with FM program, with the following conditions:
 - Minimum of 24 physicians per IMCI training course
 - Data forms to be coordinated with JSI team for community component of IMCI.
 - Slum IMCI activities if expanded beyond two units would be scaled up to district level.
 - With regards to IMCI training duration and geographical coverage:
 - IMCI training already compressed into seven days, which is the shortest in the world.
 - Existing and planned districts for IMCI intervention, which overlap with HM/HC target districts will be communicated to JSI for coordination and integration.

C – Primary Health Care General Department

- A meeting was held with Dr. Laila Solaiman, Director General of PHC Department on March 18, 2003 to:
 - obtain approval for implementation of Family Medicine (FM) activities in the two HM/HC pilot slum areas in coordination with Integrated Management of Childhood Illness (IMCI).
 - discuss implementation of FM activities in collaboration with HM/HC in target Upper Egypt districts/ governorates.
- Dr. Solaiman expressed an open attitude towards implementing FM programs in the slum areas in a coordinated manner with IMCI programs. She is also willing to plan for collaborative activities with HM/HC in Upper Egypt and promised to provide a copy of FM Curriculum.
- By the end of the meeting the following conclusions and recommendations were set:
 - With regards to pilot HM/HC in slum areas, Dr. Solaiman agreed to the following:
 - to implement FM activities in the two HM/HC slum units.

- to collaborate with IMCI implementation in slum pilot areas, and support the 7-day IMCI training program as one of the modules of FM.
 - To meet with JSI team on March 30 2003 to present FM activities
 - With regards to cooperation between FM program and HM/HC in Upper Egypt, the following was agreed:
 - Cooperation to be established in Assiut where district coverage coincides between HM/HC and FM program.
 - Such cooperation can be expanded to El Menya and Sohag once FM program is implemented there.
- On March 30, Dr. Laila Solaiman , visited JSI office and presented to JSI staff an overview of the FM program that included the conceptual outline, strategies, phases and planned modules of the training curriculum. Agreement was reached to select one district in Menya to integrate FM, HM/HC, Family Planning and other health care activities, as a model for future replication in other districts.

D – Health Sector Reform (HSR)

- Coordination between HM/HC and HSR is on going at the central level through information sharing and at the local level through coordinating activities in Sohag governorate as it is a target governorate for both HM/HC and HSR Project.
- In Sohag, JSI Field Office Manger met with the local head of EU Technical Support Office Dr. Ibrahim El Zik, to discuss areas of coordination and cooperation thereby avoiding duplication and overlap.
- As HSR is in the process of introducing adjustments and procuring (some) equipment in the newly established hospitals in Maragha and Geheina, JSI provided HSR with the blue prints of Maragha and Geheina District Hospitals developed by HM/HC and JSI, and the list of standard equipment to be procured for the obstetric and NICU departments of the two hospitals. JSI will develop the two newly renovated departments while HSR will equip the remaining departments of the hospitals.
- A meeting was held with Drs. Hosni Tamam, Mushira El Shafei and Samir El Namiki, HSR consultants, to obtain information about the FM curriculum developed by HSR. They advised that the curriculum will be ready towards the end of March, at which time a contract would be presented to bidders for implementation in Alexandria, Menoufia and Sohag.

E – Infection Control Directorate

- A meeting was held with Dr. Amr Kandil, Director of Infection Control Unit/ MOHP on January 21, 2003 to discuss coordination areas and steps to integrate activities. JSI committed itself to provide a training component on infection control as an integral part of its competency based training in the areas of EOC, NC, CSD and ER and encouraged the Infection Control Unit to participate and follow up on this training.
- With regards to plans to institutionalize the system of infection control at different levels in accordance with the Ministerial Decree regulating this

activity, it was agreed that the Infection Control Unit will work closely with JSI to plan the establishment of the governorate Infection Control Unit, and the Hospital Infection Control Committee and Team at the same time that JSI is phasing in with its interventions.

- JSI promised to provide two day training sessions on Infection Control at newly established units/committees and teams in accordance with the JSI phase-in plan.

F – NICHP

- Dr Esmat Mansour, Undersecretary for Integrated Health Care (IHC) and Executive Director of HM/HC Project and Dr. Sanaa Ibrahim, Director General of the National Information Center for Health and Population (NICHP) called for a meeting in the National Center on January 14, 2003, to introduce the HIS after its assessment, revision and redevelopment. Other sectors of MOHP, particularly those involved in the development or operation of health information systems were invited to this meeting to discuss means and ways to coordinate health information activities.
- The meeting was attended by Dr. Hassan El Kalla, Under Secretary, Curative Care, Dr. Hanem Abdel Azeem Zaher, Under Secretary, Technical support and Project Development, Dr. Samir Fouad, Undersecretary, Planning and Monitoring, Dr. Zeinab Youssef, Undersecretary, Occupational Health and Dr. Nasr El Sayed, National AIDS Control Program Director. USAID/ Health and Population Section and JSI were represented by key staff. The undersecretaries also asked a number of their key staff to attend the presentation.
- Task Four manager presented the results of the HIS assessment, analysis and design of the new application as well as the implementation methods.
- At the end of the meeting, Dr. Hanem Abdel Azeem, Undersecretary for Technical Support and Project Development asked JSI to present and demonstrate the whole set of applications to the Health Reform Project staff, which was done on January 18, 2003.
- A separate meeting was held with Dr. Sanaa Ibrahim, Director General of NICHP, on January 18, 2003 to discuss the schedule of pilot testing for the implementation of the upgraded system in Menya, Alexandria and South Sinai governorates.
- JSI supported NICHP in pilot testing the upgraded system in Menya and Alexandria.

G – EPI/ Maternal and Neonatal Tetanus

- In response to the concerns expressed in the MOHP/ USAID/ JSI Monthly Coordination Meeting (March 2003) related to the incidence rates of cases of Neonatal Tetanus at the national level and the proposition presented by JSI to mobilize HM/HC resources to address this problem in high risk districts within its target governorates in Upper Egypt, Dr. Nahed Matta, USAID called for a meeting on March 25, attended by Dr. Esmat Mansour, Undersecretary for Integrated Health Care and HM/HC Executive Director, Director General of Communicable Diseases, EFP Managers, EPI Consultants, JSI Chief of Party and UNICEF Assistant Project Officer.

- By the end of the meeting, the participants agreed on the following priority ranking of the interventions aiming at eliminating Neonatal Tetanus:
 - TT vaccination coverage with two doses to expand nationally and with three doses in high-risk districts, this activity is to be supported by IEC and Community Mobilization.
 - Strengthen the national MNT Surveillance system by helping MOHP to collect relevant information/ data from various sources.
 - Clean delivery services.
- As for cooperation between HM/HC and EPI, it was agreed that EPI Department would provide JSI with a list of high-risk districts in Upper Egypt. HM/HC - supported by USAID/ JSI- will help in implementing the high-risk campaign approach in these districts, particularly through mobilizing communities, increasing knowledge and creating demand for vaccination to increase coverage rates.

TAHSEEN Project

A - Orientation/ Coordination Meeting

- The First Orientation/Coordination Meeting was held on February 4, 2002 at JSI and was attended by TAHSEEN Project-CATALYST and JSI key staff. The Purpose of the Meeting was to give a brief orientation presentation on the TAHSEEN project and the HM/HC project, introduce key personnel and initiate discussions on areas of coordination and a mechanism for collaboration. TAHSEEN Chief of Party presented a brief overview of the project, then JSI staff presented the HM/HC objectives, tasks, activities and accomplishments as well as the salient features of the Annual Work Plan (2002/2003). HM/HC provided TAHSEEN project with all the publications and information and expressed readiness to share field experiences.
- By the end of the meeting an agreement was reached to meet in small groups to:
 - Further understand the scope of work of each project.
 - Identify activities that require coordination.
 - Agree on a mechanism, i.e. "Coordination Teams/Counterparts" for collaboration and coordination of activities.

B - Interaction with the Monthly MOHP/ USAID/ JSI Coordination Meeting

- In the MOHP/ USAID/ JSI Monthly Coordination Meeting of February 2, 2003, Dr. Esmat Mansour, Undersecretary for Integrated Health Care and HM/HC Executive Director identified two critical areas that require coordination and collaboration between HM/HC and TAHSEEN, and requested JSI to explore the possibility of initiating a dialogue with TAHSEEN to implement them. The two areas are:
 - Women Health Card:
 - MOHP, with support from USAID/ JSI has revised and refined the Women Health Card, which is now subject to final review by the National Women Council. Dr. Esmat encouraged JSI to propose to TAHSEEN to review the FP section of the card.

- Once the card is finalized, TAHSEEN will promote use of the Card for recording family planning services provided to the women. The aim is to encourage women to maintain and use the card for more than one pregnancy as women are accustomed to disposing of the card after delivery.
- Institutionalization and Mainstreaming FP Curriculum of the Secondary Technical Nursing School:
 - Changes/ modifications of MCH curriculum were proposed based on a thorough review of the current curriculum. The newly revised curriculum will be implemented in all nursing schools (228 schools), starting on the school year (2003/2004).
 - HM/HC Executive Director, also, suggested a similar process to be adopted and followed by TAHSEEN in collaboration with MOHP- FP and Research and Development Central Departments to revise the FP component of the Secondary Technical Nursing School curriculum.
- TAHSEEN has reacted very positively to these two suggestions and promised that they should be on the list of their priorities.

C - Follow up, Meetings and Actions

- To follow up on the orientation and coordination meeting, two meetings were held between key staff of the two parties (JSI/TAHSEEN) on February 25 and March 2, 2003. The two parties work from the same base of knowledge.
- Areas identified for collaboration and coordination include, but are not necessarily limited to the following areas:
 - Coordination of the development of cross-referral mechanisms between MCH and FP services to avoid missed family planning opportunities; as well as coordination of the development of post-partum IUD services in facilities where EOC services are being established.
 - CBT methodology and curriculum particularly modules on counseling.
 - Add STP/ RTI to the standards of services and protocols of the Package of Essential Services.
 - Coordinate the CQI activities to certify and accredit FP/ MCH services and link the CQI with supervisory and incentive systems.
 - Coordinate the communication messages and materials.
 - Continue the collaboration and coordination in establishing district level Management Health Information Centers with the purpose of maximizing the sharing of resources to avoid duplication.
 - The two parties agreed to collaborate and work closely together to jointly develop and implement FP/ MCH activities in one governorate, i.e. Menya. In this respect district level plans that integrate all HM/HC activities will be developed, implemented and monitored.

D – An Outline of a Plan of Action for Coordination and Cooperation

- After the series of meetings mentioned above, the two parties met on March 23, 2003 to list all conclusions reached in these meetings and outline a plan of action, with mechanisms for detailing activities, assigning responsibilities and developing a timetable. The following is a summary of the main conclusions:

- Seven recommendations (with supporting documents) proposed by HM/HC and three recommendations proposed by TAHSEEN were the basis of discussion.
- The recommendations were reviewed and discussed. As a result, it was agreed that Task/ Activity working groups would be established to deal with specific areas of coordination and collaboration.
- Mr. Sobhi Moharram, DCOP, JSI and Dr. Ton van der Velden, QI Specialist, TAHSEEN, are assigned as focal persons to facilitate the day-to-day and overall coordination of the working groups.
- The Coordinating Team (Ton & Sobhi) were assigned the following two priority responsibilities:
 - To review and revise the Draft MOC between FP and MCH Sections. As JSI developed this draft, TAHSEEN was requested to review and revise the FP component and e-mail it to JSI.
 - To prepare a draft plan of action for phasing into Menya with integrated FP/ MCH services.
- Regarding TAHSEEN's recommendations that HM/HC and TAHSEEN are to jointly address increased availability and quality of non-elective tubal ligation. It was agreed that the implementation of such recommendations needed a clear guiding policy from MOHP counterparts.
- JSI responded positively to TAHSEEN's recommendation to explore the possibility of expanding Evidence Based Medicine to MCH topics.
- The following working groups were defined:

#	Task/ Activity	Purpose	Members
1	Nursing Secondary Technical School - FP Curriculum	-Review the process to revise, refine, modify and acquire consensus and approval on an updated revised curriculum and Teacher's guide. -Develop a plan of action to initiate and accomplish this activity. -Develop a support plan to provide technical assistance to institutionalize the curriculum at the national level.	-Dr. Nasr El Kholy, TAHSEEN -Dr. Maaly Guemaie, JSI -Dr. Mohamed Mustafa, JSI
2	Women Health Card	- FP services section of the Card, are to be reviewed by TAHSEEN urgently. -HM/HC supported by JSI will design and finalize the Card. -Discuss and agree on ways and means to promote the use of the card by women as a record of the provision of FP	-Dr. Nahla A. Tawab, TAHSEEN -Dr. Ingy Khorshid, TAHSEEN -Ms. Marwa Kamel, JSI

#	Task/ Activity	Purpose	Members
		services and a guide for child spacing between pregnancies	
3	MHIS	- Determine if the "System of Codes" for MCH and POP HIS can be integrated within the new MHIS application. - Explore the situation of the implementation of the plan developed by POP IV for a new decentralized MIS design with a revised software program.	-Eng. El Sayed Mohamed, TAHSEEN -Eng. Khaled A. Fattah, JSI
4	Post-Partum Care Guidelines	- To review and give final input to the guidelines - To take the necessary actions to publish the document as MOHP's publication - Based on the guidelines, develop a protocol of service standards, modules for training and QA Checklists.	-Dr. Ton van Velden, TAHSEEN -Dr. Nasser El Koly, TAHSEEN -Mr. Tom Coles, JSI -Dr. Sabry Hamza, JSI -Dr. Waffaie El Sakkary, JSI
5	Private Sector	- Examine the possibility of working with the Ask/ Consult network to expand the availability of commodities needed fro MCH services	-Mr. Fawzy A. Ghani, TAHSEEN -Dr. Nahla A. Tawab, TAHSEEN -Dr. Hassan El Sheikh, JSI -Ms. Marwa Kamel, JSI

USAID/ Communication for Healthy living (CHL) Project

- The purpose of the meetings that were held at the JSI office on January 15 and 20, 2003 were to present the HM/HC communication activities and lessons learned to the CHL project.
- The JSI team presented the IEC activities that included mass media campaigns, training of health educators and social workers, print and audiovisual materials for providers and their clients, and public/private partnership. The JSI team also presented the community activities that included the formation of community health committees, the community needs identification/ decision making process, and the NGO small grants program.
- After presentations, discussions followed about lessons learned in the three HM/HC components presented.
- JSI staff was requested by the CHL team to write up the MCH communication needs so that CHL could design programs meeting those needs. JSI subsequently submitted a proposed list of MCH Communication Materials needed, and a second list of materials needing revision or reproduction.

- CHL explained that work on their project document was on-going and would be shared with JSI.

GALAE

- In coordination with the Ford Foundation, World Education and GALAE, a five-day TOT workshop was held in Luxor from February 16 to 20, 2003. The TOT workshop was meant to replicate the literacy experience – *Integrating HM/HC Messages into the Literacy Curricula of GALAE* – in the rest of the literacy classes in Luxor (approximately 300 classes) after the overwhelming success of the pilot phase in 30 Luxor classes.
- At the end of the workshop, participants set dates and logistical arrangements for conducting decentralized training workshops for the remaining literacy facilitators and supervisors in Luxor using the workshop-trained facilitators as trainers.
- Mr. Ahmed Abul Wafa, Head of GALAE Luxor, Dr. Ahmed Abdel Moneim, Luxor Health Director and General Samir Rizk on behalf of The Chief of Luxor Supreme Council attended the Workshop. The Workshop was attended by 42 GALAE literacy facilitators and Supervisors from Luxor who were trained on how to train teachers, and how to deliver the HM/HC messages within the literacy curricula of GALAE.

Workshop	From	To	No. of Participants
TOT	Feb. 16, 03	Feb. 20, 03	42



Egyptian Society for Population Studies and Reproductive Health

- JSI participated in a workshop on January 9, 2002 to disseminate the results of interventions made to integrate a reproductive health framework for the PHC level. The intervention was based on a study, which was conducted in Giza governorate to determine the prevalence of reproductive morbidity. The study was implemented in 18 health centers in Giza, two health centers in Qaliubiya and one slum area in Cairo.
- The interventions include the following four components:
 - Upgrade the basic level of infrastructure of health care centers at low cost;
 - Expand and integrate reproductive health services at primary health care level, which involves training and re-training of medical and non-medical personnel;
 - Expand Health education to community women;
 - Develop indicators to monitor and evaluate the progress and cost of the intervention.
- A separate evaluation of the intervention was done by Dr. Jack Reynolds, who presented its key achievements, shortcomings, challenges, recommendations and overall conclusions.


ANNEX A - PERFORMANCE MILESTONES CHART

No.	Date Due	Task No.	Milestone	Submitted	Validated	Approved	Comments
						USAID	
1	09/15/2002	11	Development of HM/HC Project Procurement Plan	04/14/2002	✓	06/02/2002	Completed
2	09/15/2002	1	Implementation of basic package in 12 additional districts for a cumulative total of 37	03/15/2003	✓		
3	09/15/2002	2	Assist in the coordinated implementation of IMCI training in at least one additional target governorate.	09/08/2002	✓	09/30/2002	Completed
4	09/15/2002	3	12 Additional District Health Plans and Monitoring Systems developed and implemented for a cumulative total of 37 districts.	09/12/2002	✓	12/19/2002	Completed
5	09/15/2002	4	Assist MOHP to establish 70 district MHS centers.	09/08/2002	✓	12/31/2002	Completed
6	09/15/2002	5	5 operations research studies completed.	09/12/2002	✓	02/04/2003	Completed
7	09/15/2002	7	Community Action Plans developed and implemented in 12 additional districts for a cumulative total of 37 districts.	09/08/2002	✓	09/30/2002	Completed
8	09/15/2002	10	A cumulative total of 120 small grants awarded to NGOs in target districts.	09/08/2002	✓	09/30/2002	Completed
9	09/15/2002	11	Procurement of \$ 1.4 Million of Project commodities.	09/12/2002	✓	10/03/2002	Completed
10	03/15/2003	11	Procurement of \$ 3 Million of Project commodities.	03/15/2003	✓		
11	09/15/2003	1	Implementation of basic package in 16 additional districts for a cumulative total of 53				
12	09/15/2003	2	Monitor QA scores of neonatal centers in target governorates.				
13	09/15/2003	3	16 Additional District Health Plans and Monitoring Systems developed and implemented for a cumulative total of 53 districts.				
14	09/15/2003	4	Assist MOHP to establish 75 district MHS centers.				
15	09/15/2003	5	5 operations research studies completed.				
16	09/15/2003	7	Community Action Plans developed and implemented in 16 additional districts for a cumulative total of 53 districts.				
17	09/15/2003	7	Assist the MOHP and HIO to maintain the Adolescent Anemia Prevention Program in the five original UE governorates and phase into the new target governorates.				
18	09/15/2003	10	A cumulative total of 140 small grants awarded to NGOs in target districts.				
19	09/15/2003	11	Procurement of \$ 5.5 Million of Project commodities.				
20	09/15/2004	1	Implementation of basic package in 17 additional districts for a cumulative total of 70				
21	09/15/2004	2	Complete implementation of MCH-FP integrated package of services in one pilot district including Health Sector Reform.				
22	09/15/2004	3	17 Additional District Health Plans and Monitoring Systems developed and implemented for a cumulative total of 70 districts.				
23	09/15/2004	4	Assist MOHP to establish 80 district MHS centers.				
24	09/15/2004	5	Assist MOHP in the development and pilot test of a national maternal mortality surveillance system.				
25	09/15/2004	7	Community Action Plans developed and implemented in 17 additional districts for a cumulative total of 70 districts.				
26	09/15/2004	10	A cumulative total of 160 small grants awarded to NGOs in target districts.				
27	09/15/2004	11	Procurement of \$ 7.5 Million of Project commodities.				
28	03/15/2005	1	Implementation of basic package in 5 additional districts for a cumulative total of 75				
29	03/15/2005	2	Assist the MOHP/Urban Health Department to pilot test adapted HM/HC interventions in 1-2 urban slum areas.				
30	03/15/2005	3	5 Additional District Health Plans and Monitoring Systems developed and implemented for a cumulative total of 75 districts.				
31	03/15/2005	4	Assist MOHP to establish 85 district MHS centers.				
32	03/15/2005	5	12 operations research studies completed.				
33	03/15/2005	5	Monitor implementation of surveillance system in target governorates of Upper Egypt.				
34	03/15/2005	7	Community Action Plans developed and implemented in 5 additional districts for a cumulative total of 75 districts.				
35	03/15/2005	10	A cumulative total of 170 small grants awarded to NGOs in target districts.				
36	03/15/2005	11	Procurement of \$ 9 Million of Project commodities.				


ANNEX B - MAPS OF TARGET GOVERNORATES

LEGEND	YES	NO
Directorate MHIS Center Upgraded		
District MHIS Center Established		
Neonatal Care Center Upgraded		
CEOC Center Upgraded		
BEOC Center Upgraded		


Beni Suef

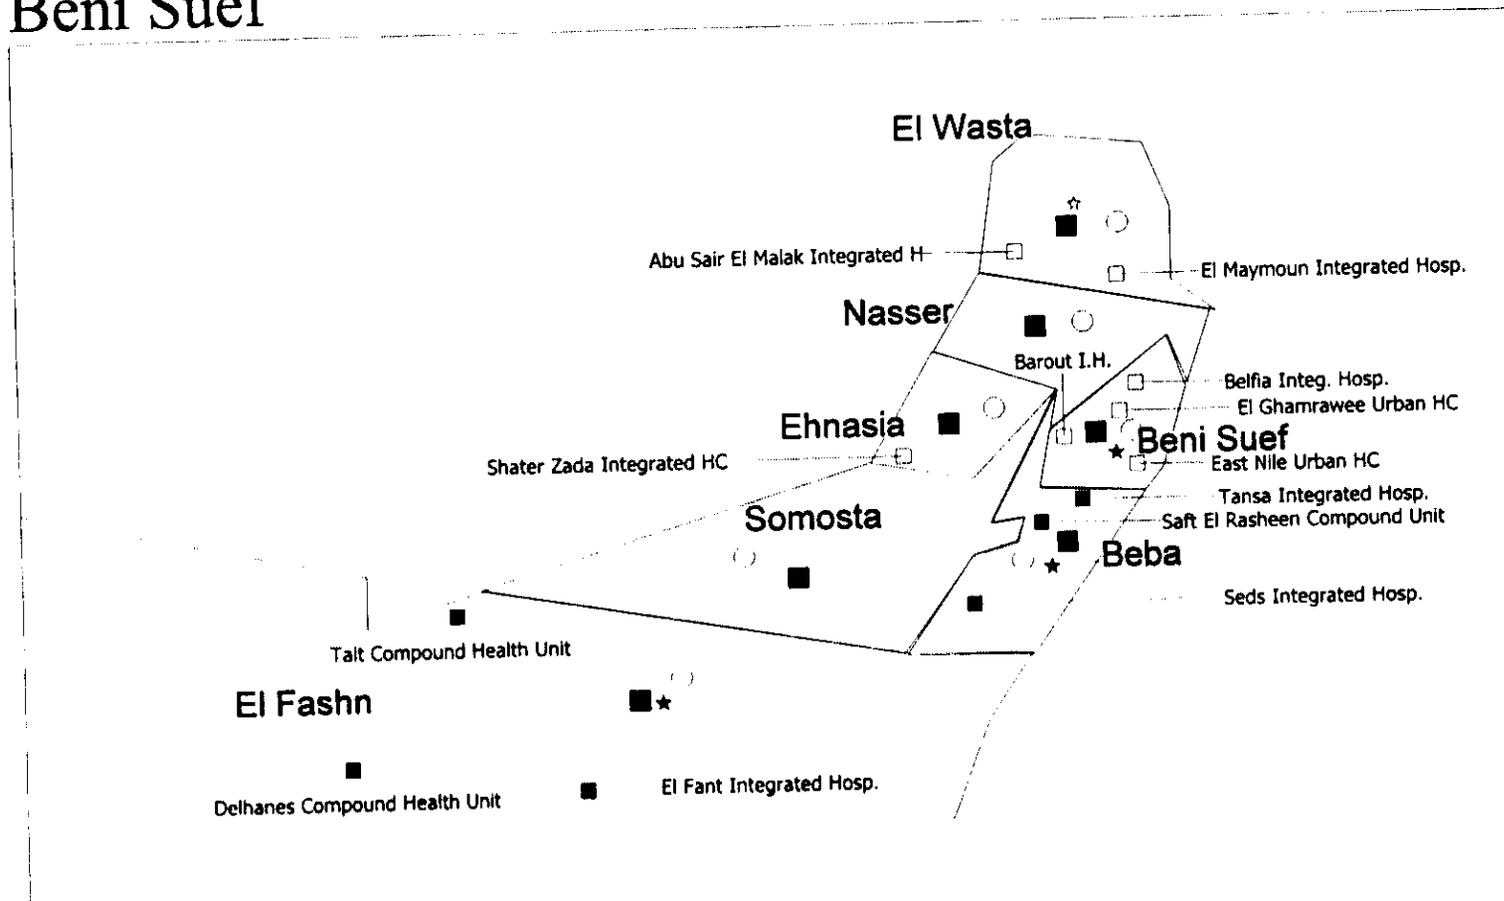


Fayoum

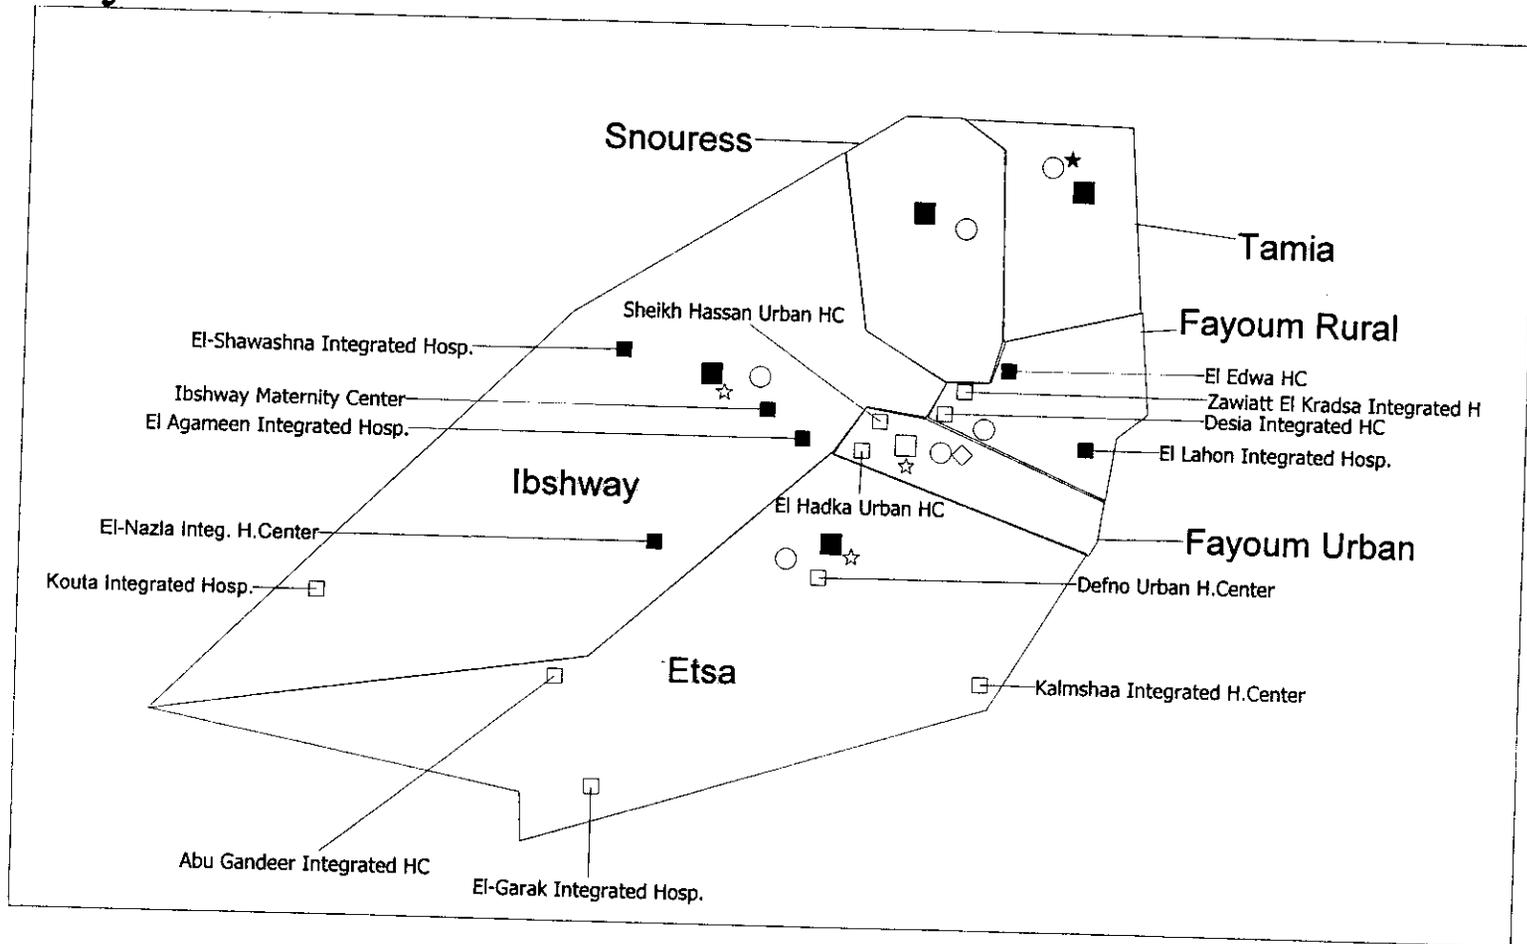


El Menya

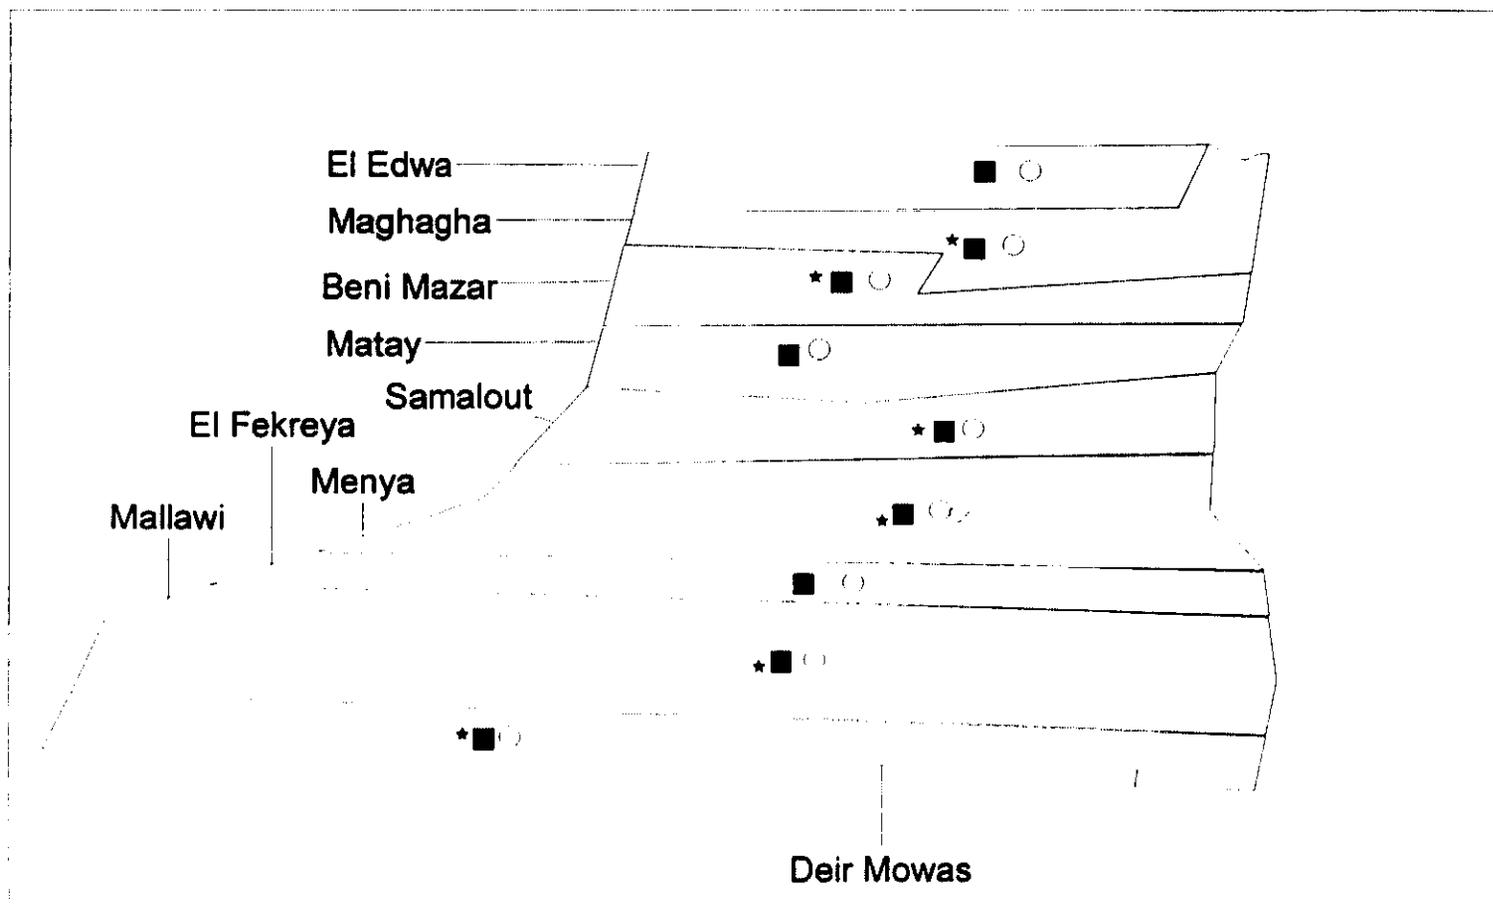


Assiut

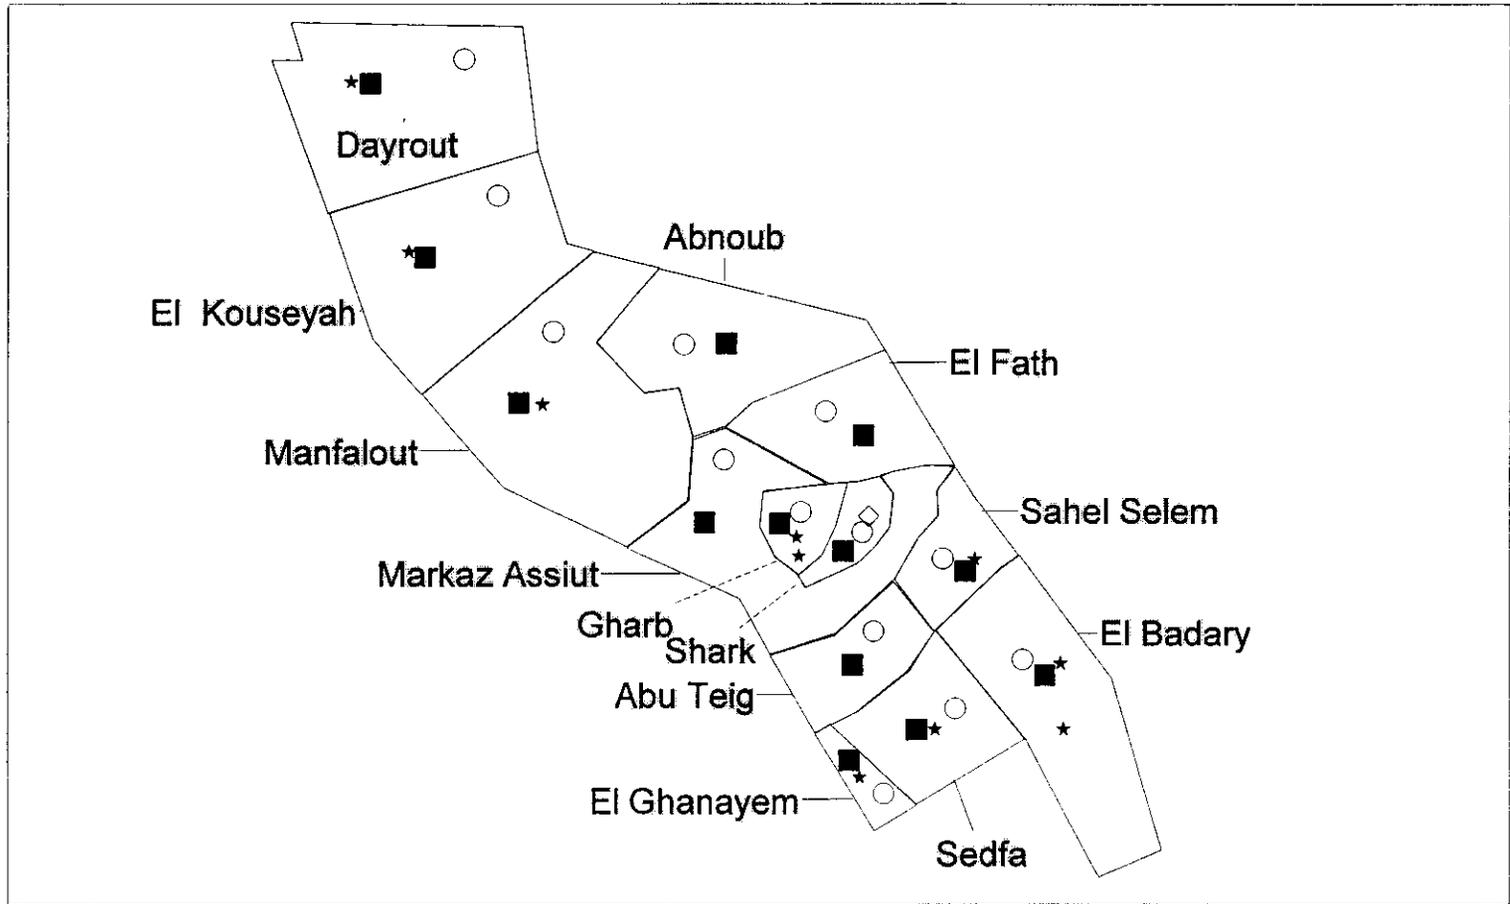


Sohag

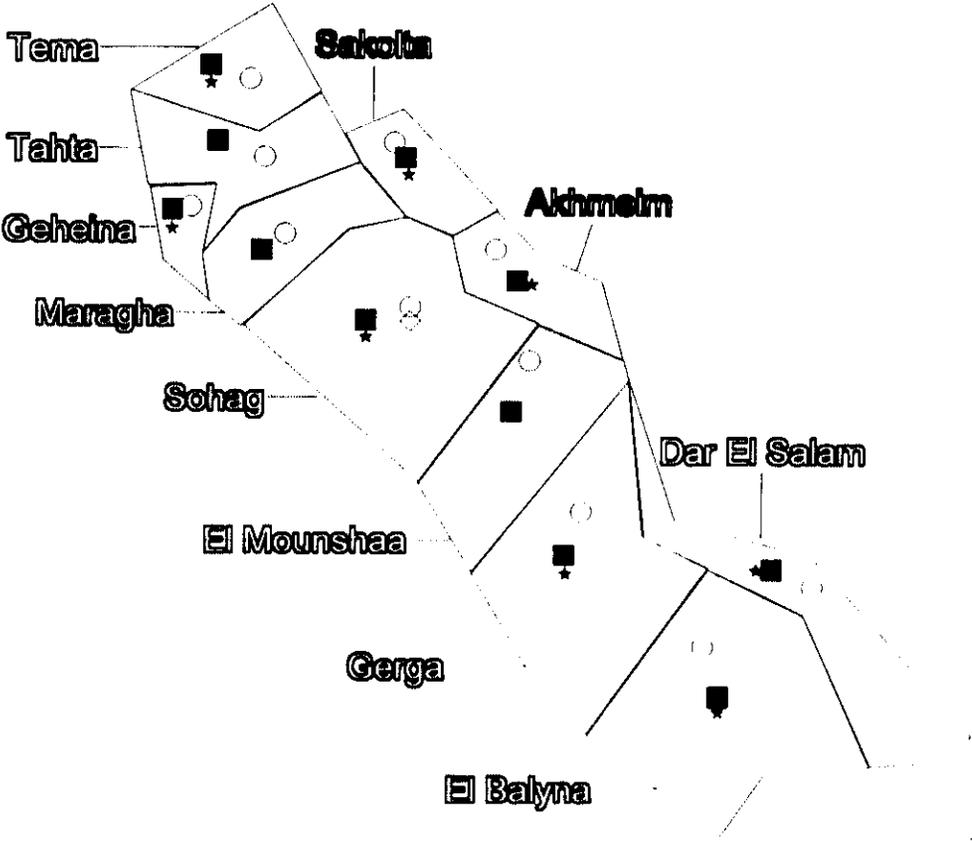

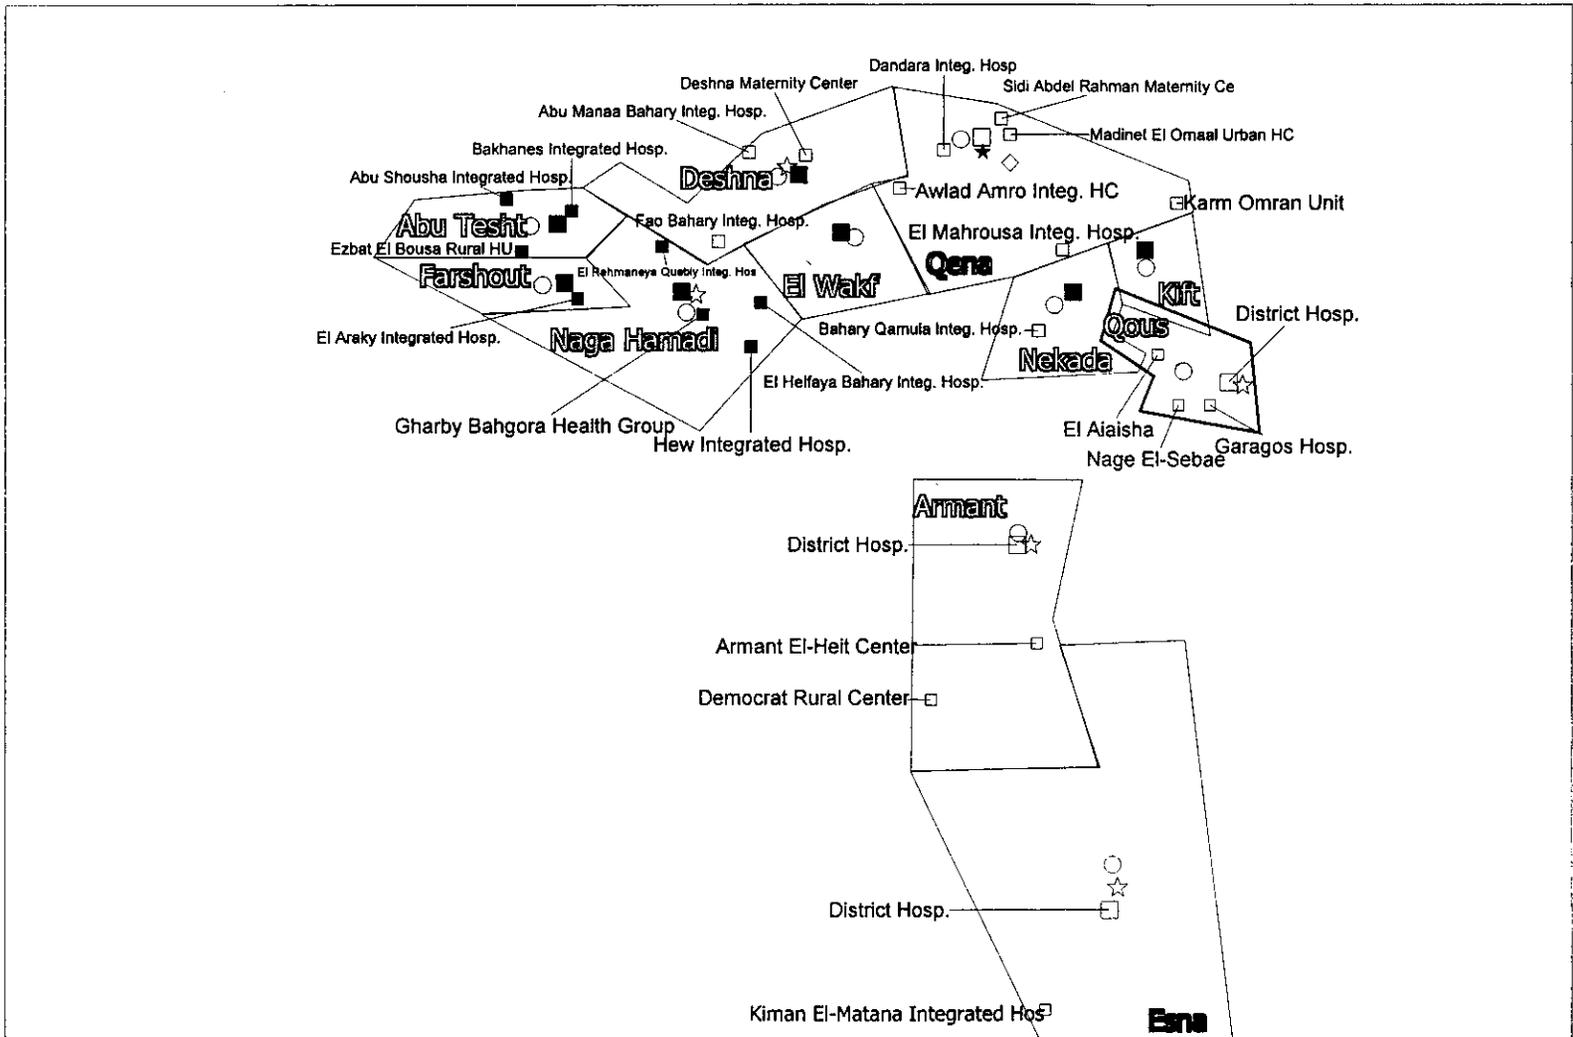

Giza

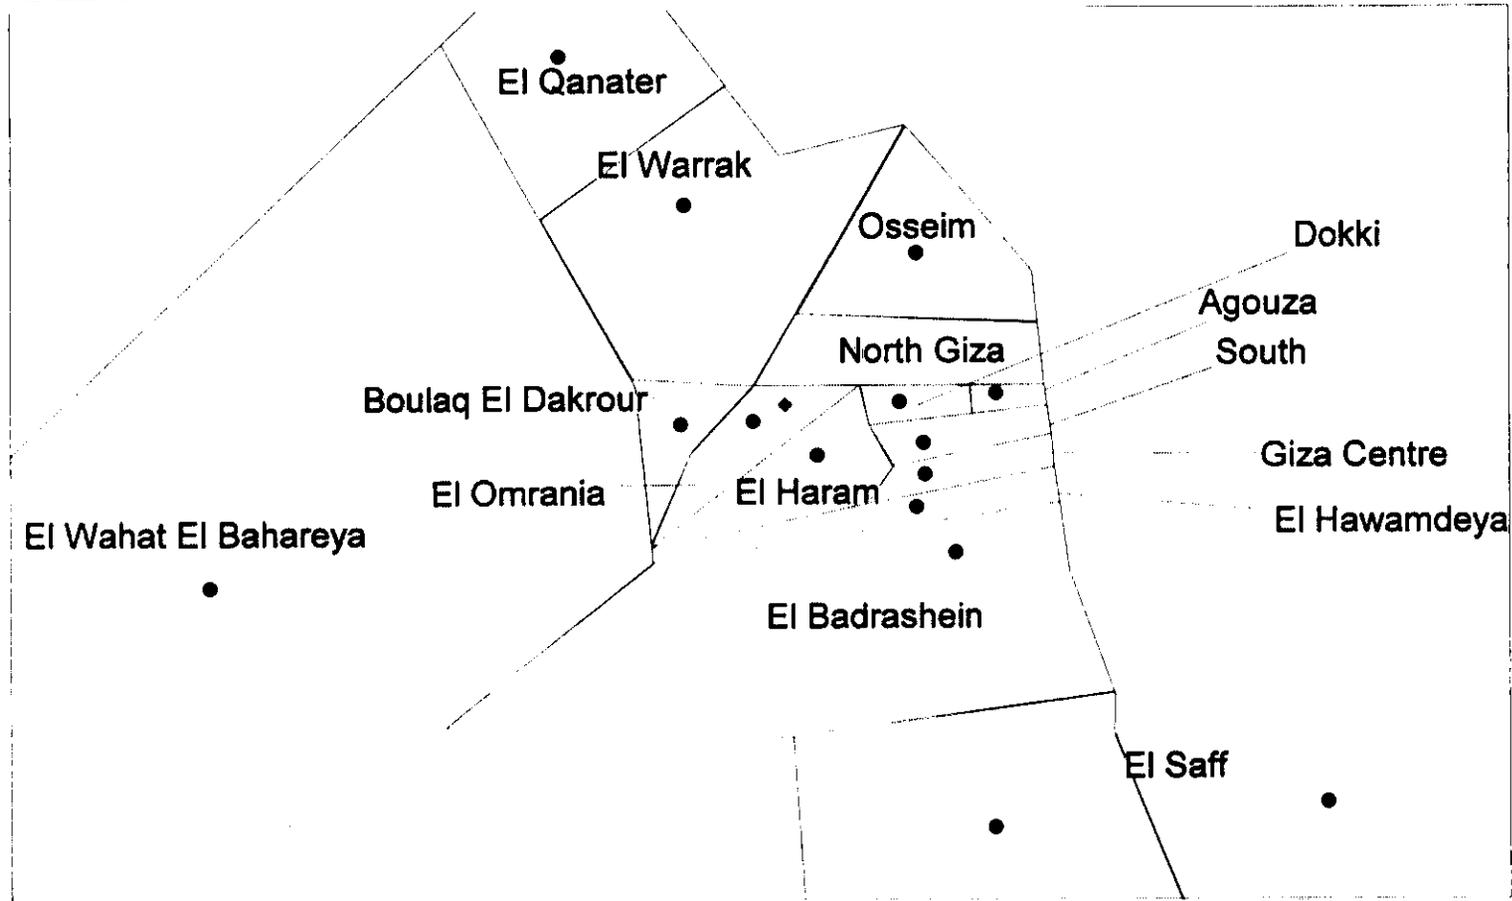

ANNEX C - JSI CONTRACT STAFF LIST

**John Snow, Inc. HM/HC
Staff Names and Titles
Option Period - March 31, 2003**

Names	Titles
JSI / Cairo office Full-Time Employees	
Reginald Gipson	Chief of Party
Sobhi Moharram	Deputy Chief of Party Coordinator for Tasks 1, 3, 4, 5, 7 & 10
Tom Coles	Health Providers Training Supervisor Coordinator for Task 2
Katrina Kruhm	Project Administrator Coordinator for Task 11
Hassan El Sheikh	Implementation Team Coordinator Task Team Member: Task 1 & 2
Mohsen El-Said	Implementation Specialist (Assiut & Menya) Task Team Member: Task 1
Abdel Moneim Hamed	Implementation Specialist (Sohag) Task Team Member: Task 1
Dalia Raafat	Architect & Quantity Surveyor Task Team Member: Task 1
Mostafa Taher	Field Civil Engineer Task Team Member: Task 1
Ghada Sherif	Infection Control Specialist Task Team Member: Task 2
Lamiaa Mohsen	Perinatal Coordinator Task Team Member: Task 2
Mohamed Moustafa	Training Specialist Task Team Member: Task 2
George Sanad	Health Management Specialist Task Team Member: Task 3
Wafaei El-Sakkary	Quality Assurance Specialist Task Team Member: Task 3
Sherif El-Kamhawy	Quality Assurance Assistant Task Team Member: Task 3
Khaled Abdel Fattah	Senior Systems Analyst (Arabsoft) Task Team Member: Task 4
Sameh Gamil	Senior Systems Engineer (Arabsoft) Task Team Member: Task 4
Adel Hakim	Maternal Mortality Surveillance System Specialist Task Team Member: Task 5
Khaled Nada	Operation Research Specialist Task Team Member: Task 5
Marwa Kamel	Communication & Public Relations Specialist Task Team Member: Task 7
Ihab Abdel Ghani	Community Health & Health Educators Specialist Task Team Member: Task 7
Heba Rafik	Communications & Contracting Specialist Task Team Member: Task 7
Dalia Sherif	Communications Assistant Task Team Member: Task 7

Names	Titles
haled El-Sayed	Community Mobilization Specialist Task Team Member: Task 7
laha Anis	Training Specialist Task Team Member: Task 7
ana Abdel Megeid	SHIP Assistant Task Team Member: Task 7
l-Sayed Kishta	Community Outreach Worker Specialist Task Team Member: Task 10
lohamed Mansour	Procurement & Commodity Logistics Specialist Task Team Member: Task 10 & 11
farion Charobim	Procurement Specialist Task Team Member: Task 11
la Zakaria	Administrative / Contracting Specialist Task Team Member: Task 11
azem Mansour	Financial Manager & Deputy Administrator
mr Obeid	Senior Accountant
assem Reda	Senior Accountant
aglaa El-Bakri	Office Manager
lanar Adel	Administrative / Personnel Specialist
ami Ezzy	Senior Network Administrator
mr Hassan	Assistant Network Administrator
ihan Iskandar	Senior Program Assistant (COP)
alia Hassan	Program Assistant (Management)
ariam Samir	Program Assistant(MMSS)
assant Al-Ashkar	Program Assistant (Service Development & Delivery)
eveen Sami	Program Assistant (Health Providers Training Supervisor)
esrine Sobhi	Executive Secretary
gy Kotb	Executive Secretary
mira Diaa	Executive Secretary
ina Khairy	Executive Secretary / Travel Assistant
la Hussein	Secretary
oha Hassan	Secretary
ashwa Bahgat	Secretary
oaa Ibrahim	Secretary
ina Bahader	Receptionist/Secretary
is Guirguis	Data Entry Assistant
alid Salah	Data Management Assistant (SHIP & Cocurrent EOC Assessment)
arek El-Nadi	Senior Driver
li Yassin	Driver
assaballah Mostafa	Driver
yman Mohamed	Messenger/ Expeditor
hmed Moawad	Messenger/ Expeditor
lohamed Harbi	Messenger / Store-Keeper
yman Mirghani	Photocopy Clerk
assan Fawzi	Office Boy
haled El-Ghoneimy	Office Boy
Part-Time Employees	

Names	Titles
Nevine Hassanein	Slum Areas Development Coordinator
Tarek El-Shimi	Management Specialist (Urban Slums & Monitoring)
Mohamed Rashad	Architectural & Engineering Specialist
Mohamed Magdy Al-Aasar	Field Civil Engineer
Mohamed Helmy	Electrical Engineer
Khaled Saber	Bio-Medical Engineer
Iman Radwan	Bio-Medical Engineer
Hussein Khamis	Support Services Coordinator
Sabry Hamza	EOC Coordinator
Ashraf Shawat	Anesthesiology Specialist
Ahmed Abou Zeid	Anesthesiology Specialist
Amr Abul Padl	Emergency Room Team Trainer Specialist
Salwa Teama	Hematology Specialist
Ahmed Ashraf Wegdan	Infection Control Specialist
Alaa Abou Zeid	Infection Control Specialist
Amr Fathi	Clinical Supervisor
Abdel-Ghaffar Mohamed	Clinical Supervisor
Ahmed Samy	Clinical Supervisor
Ahmed Mohamed	Clinical Supervisor
Assem Anwar	Clinical Supervisor
Hossam Ahmed	Clinical Supervisor
Ihab El-Nashar	Clinical Supervisor
Magdy Sweed	Clinical Supervisor
Magdy Tawfik	Clinical Supervisor
Mahmoud Rizk	Clinical Supervisor
Mahmoud Shokry	Clinical Supervisor
Mohamed Sabry	Clinical Supervisor
Mohamed Mahmoud	Clinical Supervisor
Sayed Mostafa	Clinical Supervisor
Tarek El-Dessouky	Clinical Supervisor
Yasser Abou-taleb	Clinical Supervisor
Ahmed Reda	Neonatal Clinical Supervisor
Aly Bayoumi	Neonatal Clinical Supervisor
Dahlia El-Sebaei	Neonatal Clinical Supervisor
Hanan Abdel Moneim	Neonatal Clinical Supervisor
Hisham Ali	Neonatal Clinical Supervisor
Mostafa Abdel Azeem	Neonatal Clinical Supervisor
Mounir Mostafa	Neonatal Clinical Supervisor
Salah El-Din Ahmed	Neonatal Clinical Supervisor
Sherif Mohamed	Neonatal Clinical Supervisor
Ismail El-Hawary	Neonatal Specialist
Maaly Guimeci	Senior Nurse Advisor
Rosario Raz	Nursing Master Trainer
Abeer El-Kotb	Nursing Trainer / Supervisor
Enayat El-Sayed	Nursing Trainer / Supervisor
Hamida Alam El-Din	Nursing Trainer / Supervisor

Names	Titles
nan Said	Nursing Trainer / Supervisor
ba Ezzat	Nursing Trainer / Supervisor
an Abdel Samea	Nursing Trainer / Supervisor
adiha Mohamed	Nursing Trainer / Supervisor
adia Abd-Allah	Nursing Trainer / Supervisor
bab El-Sayed	Nursing Trainer / Supervisor
anda El-Sayed	Nursing Trainer / Supervisor
asha Adel	Nursing Trainer / Supervisor
har Nagieb	Nursing Trainer / Supervisor
har younes	Nursing Trainer / Supervisor
aid El-Dib	Health Management & Community Health Coordinator
livia Riad	Management Specialist
la Hamdy	Community Development Trainer / Qena
onald Benson	Publications Coordinator
dam Taylor	Editor
eidi Thurmon	Editor
martha Abou El-Ella	Editor
michelle Auld	Editor
samantha Bramely	Editor
lison Bichard	Technical Writer / Editor
erin Benson	Technical Writer / Editor
Fayoum Field Office	
Marwan Abdel Fattah	Maternal & Child Health / Management Specialist / Field Office Manager
Amal Abdel Gawad	Community Development Specialist
Sameh Sabry	Field Program Assistant (SHIP) / Fayoum & Beni Suf
Ashraf Saad	Administrative Assistant
Gamal Abdel-Azeem	Driver
Rabie Khamis	Office Boy
Qena Field Office	
Mamdouh Aboul-Kassem	Maternal & Child Health Specialist / Field Office Manager
Israa Ibrahim Raslaan	Community Development Specialist
Hussein Kamel	Field Program Assistant (SHIP), Qena & Sohag
Essam El-Sayed	Administrative Assistant
Khaled Hamdan	Driver
Mohamed Fawzi	Office Boy
Assiut Field Office	
Abdel Aziz Mohamed	Maternal & Child Health Specialist
Tarek Abdel-Wahed	Health Planning & Management Specialist/ Field Office Manager
Mohamed Youssef	Community Development Specialist
Akram Yehia	Field Program Assistant (SHIP)
Mahmoud Ahmed	Administrative Assistant
Mohamed Ali	Driver
Nasser Sayed	Office Boy

Names	Titles
Minia Field Office	
Gihan Shafik	Maternal & Child Health Specialist
Amgad George	Health Planning & Management Specialist/ Field Office Manager
Mostafa Sayed	Community Development Specialist
Ahmed Hosni	Field Program Assistant (SHIP)
Samah Khalifa	Administrative Assistant
Gamal Ahmed	Office Boy
Sohag Field Office	
Gamal El-Korashy	Maternal & Child Health Specialist / Field Office Manager
Ossama Ibrahim Mohamed	Health Planning & Management Specialist / Sohag & Qena
Ahmed Ramadan	Community Development Specialist
Ashraf Mostafa	Administrative Assistant
Mohamed Sayed	Administrative Assistant
Hassan Abbas	Driver
Seoudi Fayez	Office Boy

**ANNEX D - SUMMARY OF UPGRADED STATUS OF FACILITIES
IN TARGET DISTRICTS**

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SAC	
Target Governorates Total			67%	43%	29%	12%	65%	2
Qena Governorate			100%	100%	75%	0%	100%	0
Qift District			100%	100%	75%	0%	100%	0
Qift District Hospital	CEOC	I				In Process		Interim
Qift District Hospital	CSSD	I				In Process		Interim
Qift District Hospital	LR	I						0
Qift District Hospital	OR	I			Partial	In Process		Interim
El Wafd District			100%	100%	75%	0%	100%	0
El Wafd District Hospital	CEOC	I				In Process		Interim
El Wafd District Hospital	CSSD	I				In Process		Interim
El Wafd District Hospital	LR	I						0
El Wafd District Hospital	OR	I			Partial	In Process		Interim

Summary of Upgrade Status of Facilities in Target Districts

04/07/2003

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SMC	
Fayoum Governorate			100%	100%	79%	50%	100%	0
Sennoures District			100%	100%	71%	43%	100%	0
Sennoures District Hospital	CEOC	I						Interim
Sennoures District Hospital	NCU2	I				In Process		Interim
Sennoures District Hospital	CSSD	I						Interim
Sennoures District Hospital	LR	I						0
Sennoures District Hospital	OR	I			Partial			Interim
Maternity Center	BEOC	I				In Process		Interim
Fedimeen District Hospital	BEOC	I			Available	In Process		Interim
Tamia District			100%	100%	86%	57%	100%	0
Tamia District Hospital	CEOC	I						Interim
Tamia District Hospital	NCU2	I						Interim
Tamia District Hospital	CSSD	I						Interim
Tamia District Hospital	LR	I						0
Tamia District Hospital	OR	I			Partial			Interim
Maternity Center	BEOC	I				In Process		Interim
Sorsena L.H.U	BEOC	I				In Process		Interim

QPMR VI		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Assessment	Renovation	Commodities	Training	SAC	
Beni Suef Governorate				100%	67%	67%	45%	100%	2
Nasser District				100%	100%	100%	43%	100%	2
Nasser District Hospital		CEOC	I						
Nasser District Hospital		NCU2	I				In Process		
Nasser District Hospital		CSSD	I						0
Nasser District Hospital		LR	I						0
Nasser District Hospital		OR	I						0
Maternity Center		BEOC	I				In Process		0
Ashmant LH.U		BEOC	I				In Process		0
Somosta District				100	33	33	50	100	6
Somosta District Hospital		CEOC	I		Construction	Available			Interim
Somosta District Hospital		CSSD	I		Construction	Available			0
Somosta District Hospital		LR	I		Construction	Partial			0
Somosta District Hospital		OR	I		Construction	Available			0
El Shankar LH.U		BEOC	I				In Process		0
Dashout LH.U		BEOC	I						0

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SMC	
Assiut Governorate			100%	33%	19%	9%	96%	0
Gharb Assiut District		I	100%	100%	29%	29%	100%	0
El-Eman El-Gadida	CEOC	I			Partial	In Process		0
El-Eman El-Gadida	NCU2	I						0
El-Eman El-Gadida	CSSD	I			On Order			0
El-Eman El-Gadida	LR	I						0
El-Eman El-Gadida	OR	I			On Order	In Process		0
El-Eman El-Gadida	ER	I			On Order	In Process		0
El Arabaen Urban Health Center	BEOC	I			Available	In Process		0
Shark Assiut District		I	100%	88%	13%	13%	100%	0
Assiut General Hospital	CEOC	I			Partial	In Process		0
Assiut General Hospital	NCU2	I			Partial	In Process		0
Assiut General Hospital	CSSD	I			Partial			0
Assiut General Hospital	LR	I			Partial			0
Assiut General Hospital	OR	I			Partial	In Process		0
Assiut General Hospital	ER	I		0	Partial	In Process		0
Assiut General Hospital	Lab	I			0			0
El Walideia Maternity Center	BEOC	I				In Process		0
Markaz Assiut District		I	100%	100%	29%	29%	100%	0
Ob/Gyn Hospital	CEOC	I			Partial	In Process		0
Ob/Gyn Hospital	NCU2	I			Partial	In Process		0
Ob/Gyn Hospital	CSSD	I			Partial			0
Ob/Gyn Hospital	LR	I			Partial			0
Ob/Gyn Hospital	OR	I			Partial			0
Naga Sabaa Integrated Hospital	BEOC	I				In Process		0
El Moleaa Integrated Hospital	BEOC	I				In Process		0
El Ghanayem District	0	II	100%	100%	33%	17%	100%	0
El Ghanayem District Hospital	CEOC	II			Available			0
El Ghanayem District Hospital	NCU2	II				In Process		0
El Ghanayem District Hospital	CSSD	II			Available	In Process		0
El Ghanayem District Hospital	LR	II						0
El Ghanayem District Hospital	OR	II			Available			0
UHC, Maternity	BEOC	II			On Order			0
El Kouseyah District		II	100%	0%	22%	0%	100%	0
El Kouseyah District Hospital	CEOC	II		Contract	Available			0
El Kouseyah District Hospital	NCU2	II		Contract		In Process		0
El Kouseyah District Hospital	CSSD	II		Contract	Available	In Process		0
El Kouseyah District Hospital	LR	II		Contract				0
El Kouseyah District Hospital	OR	II		Contract	Available	In Process		0
El Kouseyah District Hospital	ER	II		Plans	Available			0
El Kouseyah Maternity	BEOC	II		Plans	Available			0
Beni Korra W.H.U	BEOC	II		Plans	Available			0
Fazara Integrated Hospital	BEOC	II		Plans	Available			0
El Fath District		II	100%	0%	0%	33%	100%	0
El Fath U.H.C	BEOC	II		0	Available			0
El Atawla I.H.	BEOC	II		0	Partial			0
El Wasta I.H.	BEOC	II		0	Available			0
Sahel Seleem District		III	100%	0%	40%	0%	100%	0
Sahel Seleem District Hospital	CEOC	III			Bid Process	On Order		0
Sahel Seleem District Hospital	NCU2	III			Bid Process	In Process		0
Sahel Seleem District Hospital	CSSD	III			Bid Process	On Order		0
Sahel Seleem District Hospital	LR	III			Plans			0
Sahel Seleem District Hospital	OR	III			Bid Process	On Order		0
El Badary District		III	100%	0%	20%	0%	50%	0
El Badary District Hospital	CEOC	III			Contract	On Order		0
El Badary District Hospital	NCU2	III			Contract	In Process		0
El Badary District Hospital	CSSD	III			Contract	On Order		0
El Badary District Hospital	LR	III		0	0	0	0	0
El Badary District Hospital	OR	III			Contract	On Order		0
Dayrout District		III	100%	0%	20%	0%	100%	0
Dayrout District Hospital	CEOC	III			Bid Process	On Order		0

Summary of Upgrade Status of Facilities in Target Districts

QPMR VI		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Assessment	Renovation	Commodities	Training	SAC	
								0	
Dayrout District	Hospital	NCU2	III		Bid Process		0	0	
Dayrout District	Hospital	CSSD	III		Bid Process	On Order	In Process	0	
Dayrout District	Hospital	LR	III		Plans	Partial		0	
Dayrout District	Hospital	OR	III		Bid Process	On Order	In Process	0	
Abu Teig District			III	100	0	0	0	0	
Abu Teig District	Hospital	CEOC	III		Plans	On Order		0	
Abu Teig District	Hospital	CSSD	III		Plans	On Order		0	
Abu Teig District	Hospital	LR	III		Plans	On Order	0	0	
Abu Teig District	Hospital	OR	III		Plans	On Order		0	
Sedfa District			III	100	0	20	0	0	
Sedfa District	Hospital	CEOC	III			On Order		0	
Sedfa District	Hospital	NCU2	III				In Process	0	
Sedfa District	Hospital	CSSD	III		0	On Order		0	
Sedfa District	Hospital	LR	III		Plans	On Order		0	
Sedfa District	Hospital	OR	III		0	On Order		0	
Mansafout District			III	100	0	20	0	0	
Mansafout District	Hospital	CEOC	III		Plans	On Order		0	
Mansafout District	Hospital	NCU2	III		Plans		In Process	0	
Mansafout District	Hospital	CSSD	III		Plans	On Order		0	
Mansafout District	Hospital	LR	III		Plans	On Order		0	
Mansafout District	Hospital	OR	III		Plans	0		0	
Abnoub District			III	100	0	0	0	0	
Abnoub District	Hospital	CEOC	III		Plans	On Order		0	
Abnoub District	Hospital	CSSD	III		Plans	On Order		0	
Abnoub District	Hospital	LR	III		Plans	On Order		0	
Abnoub District	Hospital	OR	III		Plans	On Order		0	

Summary of Upgrade Status of Facilities in Target Districts

04/07/2003

QPMR VI		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Facility	Assessment	Renovation	Commodities	Training	
Sohag Governorate				100%	44%	15%	0%	100%	0
Sohag District			I	100%	78%	67%	0%	100%	0
Sohag General Hospital		CEOC	I	100%	78%	67%	0%	100%	0
Sohag General Hospital		NCU2	I				In Process		0
Sohag General Hospital		CSSD	I				In Process		0
Sohag General Hospital		LR	I				In Process		0
Sohag General Hospital		OR	I		Plans	Partial			0
Sohag General Hospital		ER	I			On Order	In Process		0
Sohag General Hospital		Lab	I		0		In Process		0
Gazeret Shandaweel I. H.		BEOC	I			0			0
Balastoura I.H.		BEOC	I						0
Tahta District			II	100%	67%	0%	0%	100%	0
Tahta District Hospital		CEOC	II	100%	67%	0%	0%	100%	0
Tahta District Hospital		NCU2	II			Available	In Process		0
Tahta District Hospital		CSSD	II			Available			0
Tahta District Hospital		LR	II			Available	In Process		0
Tahta District Hospital		OR	II		Plans	Available			0
Tahta District Hospital		ER	II			Available	In Process		0
Tahta Maternity Center		BEOC	II			Available	In Process		0
Shatoura I.H.U.		BEOC	II			Available			0
El Sawamaa I.H.		BEOC	II		Plans	Available			0
Gerga District			II	100%	50%	17%	0%	100%	0
Gerga District Hospital		CEOC	II	100%	50%	17%	0%	100%	0
Gerga District Hospital		NCU2	II			Available	In Process		0
Gerga District Hospital		CSSD	II						0
Gerga District Hospital		LR	II		Plans	Available	In Process		0
Gerga District Hospital		OR	II		Plans	Available			0
El-Magabra I.H.		BEOC	II		Plans	Available	In Process		0
Tema District			II	100%	22%	0%	0%	100%	0
Tema District Hospital		CEOC	II	100%	22%	0%	0%	100%	0
Tema District Hospital		NCU2	II			Partial			0
Tema District Hospital		CSSD	II			Partial			0
Tema District Hospital		LR	II		Plans	On Order			0
Tema District Hospital		OR	II		Plans	On Order			0
Tema District Hospital		ER	II		Plans	On Order			0
Tema U.H.C.		BEOC	II		Plans	0			0
Om Dooma I.H.		BEOC	II		Plans	On Order			0
El Rayayna I.H.		BEOC	II		Plans	On Order			0
El Balyana District			II	100%	33%	0%	0%	100%	0
El Balyana District Hospital		CEOC	II	100%	33%	0%	0%	100%	0
El Balyana District Hospital		CSSD	II			On Order			0
El Balyana District Hospital		LR	II			On Order			0
El Balyana District Hospital		OR	II		Plans	On Order			0
Al Sheikh Baraka W.H.U		BEOC	II		Plans	On Order			0
Al Sheikh Marzouk I.H.U		BEOC	II		Plans	On Order			0
Dar El-Salam District			II	100%	33%	17%	0%	100%	0
Dar El-Salam District Hospital		CEOC	II	100%	33%	17%	0%	100%	0
Dar El-Salam District Hospital		NCU2	II		Construction	On Order			0
Dar El-Salam District Hospital		CSSD	II		Construction				0
Dar El-Salam District Hospital		LR	II			On Order			0
Dar El-Salam District Hospital		OR	II		Construction	On Order			0
El Naghameesh RHJ		BEOC	II			On Order			0
Saqolta District			II	100%	14%	14%	0%	100%	0
Saqolta District Hospital		CEOC	II	100%	14%	14%	0%	100%	0
Saqolta District Hospital		NCU2	II			On Order			0
Saqolta District Hospital		CSSD	II						0
Saqolta District Hospital		LR	II		Plans	On Order			0
Saqolta District Hospital		OR	II		Plans	On Order			0
Saqolta Maternity		BEOC	II		Plans	On Order			0
El Galaweya I.H		BEOC	II		Plans	On Order			0
Geheina District			II	100%	83%	17%	0%	100%	0

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SAC	
Geheina District Hospital	CEOC	II			On Order			0
Geheina District Hospital	NCUZ	II						0
Geheina District Hospital	CSSD	II			On Order			0
Geheina District Hospital	LR	II		Plans	On Order			0
Geheina District Hospital	OR	II			On Order			0
Enebis LH	BEOC	II			On Order			0
Maragha District		II	100	57	14	0	100	0
Maragha District Hospital	CEOC	II			On Order	In Process		0
Maragha District Hospital	NCUZ	II						0
Maragha District Hospital	CSSD	II			On Order	In Process		0
Maragha District Hospital	LR	II		Plans	On Order			0
Maragha District Hospital	OR	II			On Order	In Process		0
Shandawel LH	BEOC	II		Plans	On Order			0
El Ghazal LHU	BEOC	II		Plans	On Order			0
Akhmeim District		II	100	0	14	0	100	0
Akhmeim District Hospital	CEOC	II			Plans	On Order		0
Akhmeim District Hospital	NCUZ	II			Plans			0
Akhmeim District Hospital	CSSD	II			Plans	On Order		0
Akhmeim District Hospital	LR	II			Plans	On Order		0
Akhmeim District Hospital	OR	II			Plans	On Order		0
Neida LH	BEOC	II			Plans	On Order		0
El Koola LH	BEOC	II			Plans	On Order		0
El-Mounshaa District		II	100	44	0	0	100	0
El-Mounshaa District Hospital	CEOC	II			On Order			0
El-Mounshaa District Hospital	NCUZ	II			On Order			0
El-Mounshaa District Hospital	CSSD	II			On Order			0
El-Mounshaa District Hospital	LR	II		Plans	On Order			0
El-Mounshaa District Hospital	OR	II			On Order			0
Maternity Center	BEOC	II		Plans	On Order			0
El Zok El Sharbia LH	BEOC	II		Plans	On Order			0
Awad El Sheikh W.H.U	BEOC	II		Plans	On Order			0
Awad Hamza LH	BEOC	II		Plans	On Order			0

Summary of Upgrade Status of Facilities in Target Districts

04/07/2003

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SMC	
Menya Governorate			100%	38%	10%	0%	100%	0
Menya District			100%	100%	17%	0%	100%	0
Menya General Hospital	CEOC	I			Partial	In Process		0
Menya General Hospital	NCU2	I			Partial	In Process		0
Menya General Hospital	CSSD	I			Partial	In Process		0
Menya General Hospital	LR	I			On Order			0
Menya General Hospital	OR	I			Partial	In Process		0
Menya General Hospital	ER	I			Partial	In Process		0
Menya General Hospital	Lab	I						0
Suzan Mubarak Medical Center	BEOC	I			On Order	In Process		0
Damsheer I.H.U.	BEOC	I				In Process		0
Talla I.H.	BEOC	I			On Order	In Process		0
Tahnasha I.H.	BEOC	I			On Order			0
Tahna El Gabal I.H.	BEOC	I			On Order	In Process		0
Samalout District			100%	92%	8%	0%	100%	0
Samalout District Hospital	CEOC	I			Partial	In Process		0
Samalout District Hospital	NCU2	I			Partial	In Process		0
Samalout District Hospital	CSSD	I			Partial	In Process		0
Samalout District Hospital	LR	I			On Order			0
Samalout District Hospital	OR	I		0	Partial	In Process		0
Samalout District Hospital	ER	I			Partial	In Process		0
Samalout District Hospital	Lab	I						0
Qulosna I.H.	BEOC	I			On Order	In Process		0
Daqoof I.H.	BEOC	I			On Order	In Process		0
El Saleba I.H.U.	BEOC	I			On Order	In Process		0
Manshiat El Sheraie I.H.	BEOC	I			On Order	In Process		0
El Bayaho I.H.	BEOC	I			On Order			0
Fekrya District			100%	67%	0%	0%	100%	0
Fekrya District Hospital	CEOC	II			Available	In Process		0
Fekrya District Hospital	NCU2	II			Plans	Available	In Process	0
Fekrya District Hospital	CSSD	II			Available	Available	In Process	0
Fekrya District Hospital	LR	II			Plans	Available		0
Fekrya District Hospital	OR	II			Available	In Process		0
Asmant I.H.U.	BEOC	II			On Order			0
Deir Mowas District			100%	44%	11%	0%	100%	0
Deir Mowas District Hospital	CEOC	II			Available			0
Deir Mowas District Hospital	NCU	II			Contract	In Process		0
Deir Mowas District Hospital	CSSD	II			Available			0
Deir Mowas District Hospital	LR	II			Contract	Available		0
Deir Mowas District Hospital	OR	II			Available			0
Suzan Mubarak Urban Health Center	NCU2	II			Available			0
Deir Mowas Maternity	BEOC	II			Plans	Available		0
Nazlet Badraman I.H.	BEOC	II			Plans	Available		0
Beni Haraam H,U	BEOC	II			Plans	Available		0
Beni Mazar District			100%	40%	10%	0%	100%	0
Beni Mazar District Hospital	CEOC	II			Available			0
Beni Mazar District Hospital	NCU2	II				In Process		0
Beni Mazar District Hospital	CSSD	II			Available			0
Beni Mazar District Hospital	LR	II			Available			0
Beni Mazar District Hospital	OR	II		0	Available			0
Beni Mazar District Hospital	ER	II		0	Available			0
Sandafa I.H.	BEOC	II			Plans	Available		0
Beni Ali I.H.	BEOC	II			Plans	Available		0
Abu Garg W.H.C	BEOC	II			Plans	Available		0
El Sheikh Fadl I.H.	BEOC	II			Plans	Available		0
Maghagha District			100%	0%	20%	0%	100%	0
Maghagha District Hospital	CEOC	III			Plans	On Order		0
Maghagha District Hospital	NCU2	III			Plans		In Process	0
Maghagha District Hospital	CSSD	III			Plans	On Order	In Process	0
Maghagha District Hospital	LR	III			Plans	On Order		0
Maghagha District Hospital	OR	III			Plans	On Order	In Process	0

Summary of Upgrade Status of Facilities in Target Districts

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SAC	
Maghagha District Hospital	ER	III			On Order			0
Mattay District		III	100%	0%	0%	0%	100%	0
Mattay District Hospital	CEOC	III		Plans	On Order			0
Mattay District Hospital	NCU2	III		Plans	Partial			0
Mattay District Hospital	CSSD	III		Plans	On Order			0
Mattay District Hospital	LR	III		Plans	On Order			0
Mattay District Hospital	OR	III		Plans	On Order			0
EI Edwa District		III	100%	0%	0%	0%	100%	0
EI Edwa District Hospital	CEOC	III		Plans	On Order			0
EI Edwa District Hospital	NCU2	III		Plans	Partial			0
EI Edwa District Hospital	CSSD	III		Plans	On Order			0
EI Edwa District Hospital	LR	III		Plans	On Order			0
EI Edwa District Hospital	OR	III		Plans	On Order			0
Mallawi District		III	100%	0%	20%	0%	100%	0
Mallawi District Hospital	CEOC	III		Contract	On Order			0
Mallawi District Hospital	NCU2	III		Contract		In Process		0
Mallawi District Hospital	CSSD	III		Contract	On Order			0
Mallawi District Hospital	LR	III		Contract	On Order			0
Mallawi District Hospital	OR	III		Contract	On Order			0

Summary of Upgrade Status of Facilities in Target Districts

04/07/2003

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SMC	
Giza Governorate			0%	1%	0%	0%	0%	0
North Giza District			0%	0%	0%	0%	0%	0
El-Tahrir District Hospital	CEOC		0	0	On Order			0
El-Tahrir District Hospital	NCU2		0	0	On Order			0
El-Tahrir District Hospital	CSSD		0	0	0			0
El-Tahrir District Hospital	LR		0	0	0			0
El-Tahrir District Hospital	OR		0	0	0			0
El Agouza District			0%	0%	0%	0%	0%	0
Embaba General Hospital	CEOC		0	0	On Order			0
Embaba General Hospital	NCU3		0	0	On Order			0
Embaba General Hospital	CSSD		0	0	0			0
Embaba General Hospital	LR		0	0	0			0
Embaba General Hospital	OR		0	0	0			0
El Omrania District			0%	0%	0%	0%	0%	0
El Omrania District Hospital	CEOC		0	0	On Order			0
El Omrania District Hospital	CSSD		0	0	0			0
El Omrania District Hospital	LR		0	0	0			0
El Omrania District Hospital	OR		0	0	0			0
South Giza District			0%	20%	0%	0%	0%	0
Om El-Masryeen Hospital	CEOC	IV	0	0	On Order			0
Om El-Masryeen Hospital	NCU2	IV	0	0	On Order			0
Om El-Masryeen Hospital	CSSD	IV	0	0	0			0
Om El-Masryeen Hospital	LR	IV	0	0	0			0
Om El-Masryeen Hospital	OR	IV	0	0	0			0
El-Haram District			0%	0%	0%	0%	0%	0
El-Haram District Hospital	CEOC		0	0	On Order			0
El-Haram District Hospital	NCU2		0	0	On Order			0
El-Haram District Hospital	CSSD		0	0	0			0
El-Haram District Hospital	LR		0	0	0			0
El-Haram District Hospital	OR		0	0	0			0
Markaz Giza District			0%	0%	0%	0%	0%	0
Markaz Giza District Hospital	CEOC	IV	0	0	On Order			0
Abu El-Nomros Hospital	NCU2	IV	0	0	On Order			0
Markaz Giza District Hospital	CSSD	IV	0	0	0			0
Markaz Giza District Hospital	LR	IV	0	0	0			0
Markaz Giza District Hospital	OR	IV	0	0	0			0
Warak District			0%	0%	0%	0%	0%	0
Warak District Hospital	CEOC	IV	0	0	On Order			0
Warak District Hospital	CSSD	IV	0	0	0			0
Warak District Hospital	LR	IV	0	0	0			0
Warak District Hospital	OR	IV	0	0	0			0
Oseim District			0%	0%	0%	0%	0%	0
Oseim District Hospital	CEOC	IV	0	0	On Order			0
Oseim District Hospital	CSSD	IV	0	0	0			0
Oseim District Hospital	LR	IV	0	0	0			0
Oseim District Hospital	OR	IV	0	0	0			0
Hawamdeya District			0%	0%	0%	0%	0%	0
Hawamdeya District Hospital	CEOC	III	0	0	On Order			0
Hawamdeya District Hospital	NCU2	III	0	0	On Order			0
Hawamdeya District Hospital	CSSD	III	0	0	0			0
Hawamdeya District Hospital	LR	III	0	0	0			0
Hawamdeya District Hospital	OR	III	0	0	0			0
El Badrashein District			0%	0%	0%	0%	0%	0
El Badrashein District Hospital	CEOC	III	0	0	On Order			0
El Badrashein District Hospital	NCU2	III	0	0	On Order			0
El Badrashein District Hospital	CSSD	III	0	0	0			0
El Badrashein District Hospital	LR	III	0	0	0			0
El Badrashein District Hospital	OR	III	0	0	0			0
El Ayat District			0%	0%	0%	0%	0%	0
El Ayat District Hospital	CEOC	III	0	0	On Order			0
El Ayat District Hospital	CSSD	III	0	0	0			0

QPMR VI			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SMC	
El Ayat District Hospital	LR	III	0	0	0			0
El Ayat District Hospital	OR	III	0	0	0			0
El Saff District			0	0	0	0	0	0
El Saff District Hospital	CEOC	III	0	0	On Order		0	0
El Saff District Hospital	CSSD	III	0	0	0			0
El Saff District Hospital	LR	III	0	0	0			0
El Saff District Hospital	OR	III	0	0	0			0
Elfeih District			0	0	0	0	0	0
Elfeih District Hospital	CEOC	III	0	0	On Order		0	0
Elfeih District Hospital	CSSD	III	0	0	0			0
Elfeih District Hospital	LR	III	0	0	0			0
Elfeih District Hospital	OR	III	0	0	0			0
El Wahat Baharia District			0	0	0	0	0	0
El Wahat Baharia District Hospital	CEOC	III	0	0	On Order		0	0
El Wahat Baharia District Hospital	NCUJ	III	0	0	On Order			0
El Wahat Baharia District Hospital	CSSD	III	0	0	0			0
El Wahat Baharia District Hospital	LR	III	0	0	0			0
El Wahat Baharia District Hospital	OR	III	0	0	0			0
Menshaat El Qanater District			0	0	0	0	0	0
Menshaat El Qanater District Hospital	CEOC	IV	0	0	On Order		0	0
Menshaat El Qanater District Hospital	CSSD	IV	0	0	0			0
Menshaat El Qanater District Hospital	LR	IV	0	0	0			0
Menshaat El Qanater District Hospital	OR	IV	0	0	0			0
El Dokki District			0	0	0	0	0	0
El Dokki District Hospital	CEOC		0	0	On Order		0	0
Om El-Abtal Hospital	NCUJ		0	0	On Order			0
El Dokki District Hospital	CSSD		0	0	0			0
El Dokki District Hospital	LR		0	0	0			0
El Dokki District Hospital	OR		0	0	0			0
Boulaq El Dakroul District			0	0	0	0	0	0
Boulaq El Dakroul Hospital	CEOC		0	0	On Order		0	0
Boulaq El Dakroul Hospital	NCUJ		0	0	0			0
Boulaq El Dakroul Hospital	CSSD		0	0	0			0
Boulaq El Dakroul Hospital	LR		0	0	0			0
Boulaq El Dakroul Hospital	OR		0	0	0	0	0	0
Giza Governorate			0	0	0	0	0	0
Ezbat El Mattar Slum Area			0	0	0	0	0	0
Imbabba General Hospital	CEOC		0	0	0		0	0
Ezbat EL Mattar Slum Area	BEOC		0	0	0		0	0
Cairo Governorate			0	0	0	0	0	0
El Basateen Slum Area			0	0	0	0	0	0
El Khalifa General Hospital	CEOC		0	0	0		0	0
El Basateen Slum Area	BEOC		0	0	0		0	0

**ANNEX E - SUMMARY OF TRAINING OF PERSONNEL IN
TARGET DISTRICTS**

QPMR VI		Type	Phase	Physicians			Nurses			Lead Trainers		
Governorate	District			EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
Target Governorates Total				12	51	63	121	65	186	2	1	3
Gena Governorate					0		6	6	12			
Qift District							4	4	8			
	Qift District Hospital	CEOC	I				3	3	6			
	Qift District Hospital	CSSD	I				1	1	2			
	Qift District Hospital	LR	I									
	Qift District Hospital	OR	I									
El Wafd District							4	4	8			
	El Wafd District Hospital	CEOC	I				3	3	6			
	El Wafd District Hospital	CSSD	I				1	1	2			
	El Wafd District Hospital	LR	I									
	El Wafd District Hospital	OR	I									
Fayoum Governorate				4	4	8	26	4	32	2	1	3
Sennoures District							18	18	36			
	Sennoures District Hospital	CEOC	I				10	10	20			
	Sennoures District Hospital	NCU2	I									
	Sennoures District Hospital	CSSD	I				8	8	16			
	Sennoures District Hospital	LR	I									
	Sennoures District Hospital	OR	I									
	Maternity Center	BEOC	I									
	Fedimeen District Hospital	BEOC	I									
Tamia District				4	4	8	10	4	14	2	1	3
	Tamia District Hospital	CEOC	I	4		4	5		5	2		2
	Tamia District Hospital	NCU2	I		4	4		4	4		1	1
	Tamia District Hospital	CSSD	I				5		5			
	Tamia District Hospital	LR	I									
	Tamia District Hospital	OR	I									
	Maternity Center	BEOC	I									
	Sersona L.H.U	BEOC	I									
Beni Suef Governorate							25	25	50			
Nasser District							14	14	28			
	Nasser District Hospital	CEOC	I				10	10	20			
	Nasser District Hospital	NCU2	I									
	Nasser District Hospital	CSSD	I				4	4	8			
	Nasser District Hospital	LR	I									
	Nasser District Hospital	OR	I									
	Maternity Center	BEOC	I									
	Ashmant L.H.U	BEOC	I									
Somosta District							11	11	22			
	Somosta District Hospital	CEOC	I				6	6	12			
	Somosta District Hospital	CSSD	I				5	5	10			
	Somosta District Hospital	LR	I									
	Somosta District Hospital	OR	I									
	El Shantour L.H.U	BEOC	I									
	Dashout L.H.U	BEOC	I									
Assiut Governorate				8	7	15	22	22	44			
Gharb Assiut District				5	5	10	5	5	10			
	El-Eman El-Gadida	CEOC	I	5		5						
	El-Eman El-Gadida	NCU2	I		5	5						
	El-Eman El-Gadida	CSSD	I				5	5	10			
	El-Eman El-Gadida	LR	I									
	El-Eman El-Gadida	OR	I									
	El-Eman El-Gadida	ER	I									
	El Arabaen Urban Health Center	BEOC	I									
Shark Assiut District							9	9	18			
	Assiut General Hospital	CEOC	I									
	Assiut General Hospital	NCU2	I									
	Assiut General Hospital	CSSD	I				9	9	18			

Summary of Training of Personnel in Target Districts

04/07/2003

QPMR VI			Physicians			Nurses			Lead Trainers		
Governorate District	Type	Phase	EOC	Neonatal	Total	EOC	Neonatal	Total	EOC	Neonatal	Total
			Training	Training		Training	Training		Training	Training	
Assiut General Hospital	LR	I									
Assiut General Hospital	OR	I									
Assiut General Hospital	ER	I									
Assiut General Hospital	Lab	I									
El Walidela Maternity Center	BEOC	I									
Markaz Assiut District		I				6		6			
Ob/Gyn Hospital	CEOC	I									
Ob/Gyn Hospital	NICU	I									
Ob/Gyn Hospital	CSSD	I				6		6			
Ob/Gyn Hospital	LR	I									
Ob/Gyn Hospital	OR	I									
Naga Sabaa Integrated Hospital	BEOC	I									
El Moteaa Integrated Hospital	BEOC	I									
El Ghanayem District		II				2		2			
El Ghanayem District Hospital	CEOC	II									
El Ghanayem District Hospital	NCU2	II									
El Ghanayem District Hospital	CSSD	II				2		2			
El Ghanayem District Hospital	LR	II									
El Ghanayem District Hospital	OR	II									
UHC, Maternity	BEOC	II									
El Kouseyah District		II									
El Kouseyah District Hospital	CEOC	II									
El Kouseyah District Hospital	NCU2	II									
El Kouseyah District Hospital	CSSD	II									
El Kouseyah District Hospital	LR	II									
El Kouseyah District Hospital	OR	II									
El Kouseyah District Hospital	ER	II									
El Kouseyah Maternity	BEOC	II									
Beni Korra W.H.U	BEOC	II									
Fazara Integrated Hospital	BEOC	II									
El Fath District		II	3		3						
El Fath U.H.C	BEOC	II									
El Atawla I.H.	BEOC	II	3		3						
El Wasta I.H.	BEOC	II									
Sahel Seleem District		III									
Sahel Seleem District Hospital	CEOC	III									
Sahel Seleem District Hospital	NCU2	III									
Sahel Seleem District Hospital	CSSD	III									
Sahel Seleem District Hospital	LR	III									
Sahel Seleem District Hospital	OR	III									
El Badary District		III									
El Badary District Hospital	CEOC	III									
El Badary District Hospital	NCU2	III									
El Badary District Hospital	CSSD	III									
El Badary District Hospital	LR	III									
El Badary District Hospital	OR	III									
Dayrout District		III									
Dayrout District Hospital	CEOC	III									
Dayrout District Hospital	NCU2	III									
Dayrout District Hospital	CSSD	III									
Dayrout District Hospital	LR	III									
Dayrout District Hospital	OR	III									
Abu Teig District		III									
Abu Teig District Hospital	CEOC	III									
Abu Teig District Hospital	CSSD	III									
Abu Teig District Hospital	LR	III									
Abu Teig District Hospital	OR	III									
Sedfa District		III									
Sedfa District Hospital	CEOC	III									
Sedfa District Hospital	NCU2	III									
Sedfa District Hospital	CSSD	III									

QPMR VI Governorate District	Type	Phase	Physicians				Nurses				Lead Trainers						
			EOC Training	Neonatal Training	Total		EOC Training	Neonatal Training	Total		EOC Training	Neonatal Training	Total				
Sedfa District Hospital	LR	III															
Sedfa District Hospital	OR	III															
Manfalout District				2	2												
Manfalout District Hospital	CEOC	III															
Manfalout District Hospital	NCU2	III		2	2												
Manfalout District Hospital	CSSD	III															
Manfalout District Hospital	LR	III															
Manfalout District Hospital	OR	III															
Abnoub District																	
Abnoub District Hospital	CEOC	III															
Abnoub District Hospital	CSSD	III															
Abnoub District Hospital	LR	III															
Abnoub District Hospital	OR	III															
Sohag Governorate							12		12								
Sohag District							4		4								
Sohag General Hospital	CEOC	I															
Sohag General Hospital	NCU2	I															
Sohag General Hospital	CSSD	I					4		4								
Sohag General Hospital	LR	I															
Sohag General Hospital	OR	I															
Sohag General Hospital	ER	I															
Sohag General Hospital	Lab	I															
Gazeret Shandaweel I. H.	BEOC	I															
Balassfoura LH.	BEOC	I															
Tahta District							3		3								
Tahta District Hospital	CEOC	II															
Tahta District Hospital	NCU2	II															
Tahta District Hospital	CSSD	II					3		3								
Tahta District Hospital	LR	II															
Tahta District Hospital	OR	II															
Tahta District Hospital	ER	II															
Tahta Maternity Center	BEOC	II															
Shattoura L.H.U.	BEOC	II															
El Sawamaa LH.	BEOC	II															
Gerga District							3		3								
Gerga District Hospital	CEOC	II															
Gerga District Hospital	NCU2	II															
Gerga District Hospital	CSSD	II					3		3								
Gerga District Hospital	LR	II															
Gerga District Hospital	OR	II															
El-Magabra LH.	BEOC	II															
Tema District																	
Tema District Hospital	CEOC	II															
Tema District Hospital	NCU2	II															
Tema District Hospital	CSSD	II															
Tema District Hospital	LR	II															
Tema District Hospital	OR	II															
Tema District Hospital	ER	II															
Tema U.H.C.	BEOC	II															
Om Dooma LH.	BEOC	II															
El Rayayma LH.	BEOC	II															
El Bahyana District																	
El Bahyana District Hospital	CEOC	II															
El Bahyana District Hospital	CSSD	II															
El Bahyana District Hospital	LR	II															
El Bahyana District Hospital	OR	II															
Al Sheikh Baraka W.H.U	BEOC	II															
Al Sheikh Marzouk L.H.U	BEOC	II															
Dar El-Salam District																	
Dar El-Salam District Hospital	CEOC	II															
Dar El-Salam District Hospital	NCU2	II															

Summary of Training of Personnel in Target Districts

04/07/2003

QPMR VI		Type	Phase	Physicians			Nurses			Lead Trainers		
Governorate	District			EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
	Dar El-Salam District Hospital	CSSD	II									
	Dar El-Salam District Hospital	LR	II									
	Dar El-Salam District Hospital	OR	II									
	El Naghameesh RHU	BEOC	II									
	Saqolta District		II									
	Saqolta District Hospital	CEOC	II									
	Saqolta District Hospital	NCU2	II									
	Saqolta District Hospital	CSSD	II									
	Saqolta District Hospital	LR	II									
	Saqolta District Hospital	OR	II									
	Saqolta Maternity	BEOC	II									
	El Galaweya I.H	BEOC	II									
	Geheina District		II									
	Geheina District Hospital	CEOC	II									
	Geheina District Hospital	NCU2	II									
	Geheina District Hospital	CSSD	II									
	Geheina District Hospital	LR	II									
	Geheina District Hospital	OR	II									
	Eneibls I.H	BEOC	II									
	Maragha District		II				2		2			
	Maragha District Hospital	CEOC	II									
	Maragha District Hospital	NCU	II									
	Maragha District Hospital	CSSD	II				2		2			
	Maragha District Hospital	LR	II									
	Maragha District Hospital	OR	II									
	Shandaweel I.H.	BEOC	II									
	El Gherazat I.H.U.	BEOC	II									
	Akhmeim District		II									
	Akhmeim District Hospital	CEOC	II									
	Akhmeim District Hospital	NCU2	II									
	Akhmeim District Hospital	CSSD	II									
	Akhmeim District Hospital	LR	II									
	Akhmeim District Hospital	OR	II									
	Neida I.H.	BEOC	II									
	El Koola I.H.	BEOC	II									
	El-Mounshaa District		II									
	El-Mounshaa District Hospital	CEOC	II									
	El-Mounshaa District Hospital	NCU2	II									
	El-Mounshaa District Hospital	CSSD	II									
	El-Mounshaa District Hospital	LR	II									
	El-Mounshaa District Hospital	OR	II									
	Maternity Center	BEOC	II									
	El Zok El Sharkia I.H.	BEOC	II									
	Awlad El Sheikh W.H.U	BEOC	II									
	Awlad Hamza I.H.	BEOC	II									
	Menya Governorate				7	7	26	3	29			
	Menya District		I				18		18			
	Menya General Hospital	CEOC	I									
	Menya General Hospital	NCU2	I									
	Menya General Hospital	CSSD	I				18		18			
	Menya General Hospital	LR	I									
	Menya General Hospital	OR	I									
	Menya General Hospital	ER	I									
	Menya General Hospital	Lab	I									
	Suzan Mubarak Medical Center	BEOC	I									
	Damsheer I.H.U.	BEOC	I									
	Talla I.H.	BEOC	I									
	Tahnasha I.H.	BEOC	I									
	Tahna El Gabal I.H.	BEOC	I									
	Samalout District		I				4		4			
	Samalout District Hospital	CEOC	I									

QPMR VI Governorate District	Type	Phase	Physicians			Nurses			Lead Trainers		
			EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
Samalout District Hospital	NCU2	I									
Samalout District Hospital	CSSD	I				4		4			
Samalout District Hospital	LR	I									
Samalout District Hospital	OR	I									
Samalout District Hospital	ER	I									
Samalout District Hospital	Lab	I									
Qulosna I.H.	BEOC	I									
Daqoof I.H.	BEOC	I									
EI Saleba L.H.U.	BEOC	I									
Marshiat EI Sheraie L.H.	BEOC	I									
EI Bayaho LH	BEOC	I									
Fekrya District		II				4		4			
Fekrya District Hospital	CEOC	II									
Fekrya District Hospital	NCU2	II									
Fekrya District Hospital	CSSD	II				4		4			
Fekrya District Hospital	LR	II									
Fekrya District Hospital	OR	II									
Asmant L.H.U.	BEOC	II									
Deir Mowas District		II		7	7		3	3			
Deir Mowas District Hospital	CEOC	II									
Deir Mowas District Hospital	NCU2	II									
Deir Mowas District Hospital	CSSD	II									
Deir Mowas District Hospital	LR	II									
Deir Mowas District Hospital	OR	II									
Suzan Mubarak Urban Health Center	NCU2	II		7	7		3	3			
Deir Mowas Maternity	BEOC	II									
Nazlet Badraman L.H.	BEOC	II									
Beni Haraam H.U	BEOC	II									
Beni Mazar District		II									
Beni Mazar District Hospital	CEOC	II									
Beni Mazar District Hospital	NCU2	II									
Beni Mazar District Hospital	CSSD	II									
Beni Mazar District Hospital	LR	II									
Beni Mazar District Hospital	OR	II									
Beni Mazar District Hospital	ER	II									
Sandafa LH	BEOC	II									
Beni Ali LH	BEOC	II									
Abu Garg W.H.C	BEOC	II									
EI Sheikh Fadl LH	BEOC	II									
Maghagha District		III									
Maghagha District Hospital	CEOC	III									
Maghagha District Hospital	NCU2	III									
Maghagha District Hospital	CSSD	III									
Maghagha District Hospital	LR	III									
Maghagha District Hospital	OR	III									
Maghagha District Hospital	ER	III									
Mattay District		III									
Mattay District Hospital	CEOC	III									
Mattay District Hospital	NCU	III									
Mattay District Hospital	CSSD	III									
Mattay District Hospital	LR	III									
Mattay District Hospital	OR	III									
EI Edwa District		III									
EI Edwa District Hospital	CEOC	III									
EI Edwa District Hospital	NCU	III									
EI Edwa District Hospital	CSSD	III									
EI Edwa District Hospital	LR	III									
EI Edwa District Hospital	OR	III									
Mallawi District		III									
Mallawi District Hospital	CEOC	III									
Mallawi District Hospital	NCU2	III									

Summary of Training of Personnel in Target Districts

04/07/2003

QPMR VI			Physicians				Nurses				Lead Trainers			
Governorate District	Type	Phase	EOC	Neonatal	Total	EOC	Neonatal	Total	EOC	Neonatal	Total			
			Training	Training		Training	Training							
Mallawi District Hospital	CSSD	III												
Mallawi District Hospital	LR	III												
Mallawi District Hospital	OR	III												
Giza Governorate														
North Giza District														
El-Tahrir District Hospital	CEOC			5	5		10	10						
El-Tahrir District Hospital	NCU2			5	5		10	10						
El-Tahrir District Hospital	CSSD													
El-Tahrir District Hospital	LR													
El-Tahrir District Hospital	OR													
El Agouza District														
Embaba General Hospital	CEOC			8	8		15	15						
Embaba General Hospital	NCU3			8	8		15	15						
Embaba General Hospital	CSSD													
Embaba General Hospital	LR													
Embaba General Hospital	OR													
El Omrانيا District														
El Omrانيا District Hospital	CEOC													
El Omrانيا District Hospital	CSSD													
El Omrانيا District Hospital	LR													
El Omrانيا District Hospital	OR													
South Giza District			IV											
Om El-Masryeen Hospital	CEOC	IV		8	8		11	11						
Om El-Masryeen Hospital	NCU2	IV		8	8		11	11						
Om El-Masryeen Hospital	CSSD	IV												
Om El-Masryeen Hospital	LR	IV												
Om El-Masryeen Hospital	OR	IV												
El-Haram District														
El-Haram District Hospital	CEOC													
El-Haram District Hospital	NCU2						2	2						
El-Haram District Hospital	CSSD													
El-Haram District Hospital	LR													
El-Haram District Hospital	OR													
Markaz Giza District			IV											
Markaz Giza District Hospital	CEOC	IV		7	7		8	8						
Abu El-Nomros Hospital	NCU2	IV		7	7		8	8						
Markaz Giza District Hospital	CSSD	IV												
Markaz Giza District Hospital	LR	IV												
Markaz Giza District Hospital	OR	IV												
Warak District			IV											
Warak District Hospital	CEOC	IV												
Warak District Hospital	CSSD	IV												
Warak District Hospital	LR	IV												
Warak District Hospital	OR	IV												
Oseim District			IV											
Oseim District Hospital	CEOC	IV												
Oseim District Hospital	CSSD	IV												
Oseim District Hospital	LR	IV												
Oseim District Hospital	OR	IV												
Hawamdeya District			III											
Hawamdeya District Hospital	CEOC	III		5	5		12	12						
Hawamdeya District Hospital	NCU2	III		5	5		12	12						
Hawamdeya District Hospital	CSSD	III												
Hawamdeya District Hospital	LR	III												
Hawamdeya District Hospital	OR	III												
El Badrashein District			III											
El Badrashein District Hospital	CEOC	III												
El Badrashein District Hospital	NCU2	III												
El Badrashein District Hospital	CSSD	III												
El Badrashein District Hospital	LR	III												
El Badrashein District Hospital	OR	III												

QPMR VI		Type	Phase	Physicians			Nurses			Lead Trainers		
Governorate	District			EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
El Ayat District			III									
	El Ayat District Hospital	CEOC	III									
	El Ayat District Hospital	CSSD	III									
	El Ayat District Hospital	LR	III									
	El Ayat District Hospital	OR	III									
El Saff District			III									
	El Saff District Hospital	CEOC	III									
	El Saff District Hospital	CSSD	III									
	El Saff District Hospital	LR	III									
	El Saff District Hospital	OR	III									
Elfeih District			III									
	Elfeih District Hospital	CEOC	III									
	Elfeih District Hospital	CSSD	III									
	Elfeih District Hospital	LR	III									
	Elfeih District Hospital	OR	III									
El Wahat Baharia District			III									
	El Wahat Baharia District Hospital	CEOC	III									
	El Wahat Baharia District Hospital	NCU2	III									
	El Wahat Baharia District Hospital	CSSD	III									
	El Wahat Baharia District Hospital	LR	III									
	El Wahat Baharia District Hospital	OR	III									
Menshaat El Qanater District			IV									
	Menshaat El Qanater District Hospital	CEOC	IV									
	Menshaat El Qanater District Hospital	CSSD	IV									
	Menshaat El Qanater District Hospital	LR	IV									
	Menshaat El Qanater District Hospital	OR	IV									
El Dokki District			III									
	El Dokki District Hospital	CEOC	III									
	Om El-Abtal Hospital	NCU2	III									
	El Dokki District Hospital	CSSD	III									
	El Dokki District Hospital	LR	III									
	El Dokki District Hospital	OR	III									
Boulaq El Dakroun District			III									
	Boulaq El Dakroun Hospital	CEOC	III									
	Boulaq El Dakroun Hospital	NCU2	III									
	Boulaq El Dakroun Hospital	CSSD	III									
	Boulaq El Dakroun Hospital	LR	III									
	Boulaq El Dakroun Hospital	OR	III									
Giza Governorate			III									
Ezbat El Mattar Slum Area			III									
	Imbaba General Hospital	CEOC	III									
	Ezbat EL Mattar Slum Area	BEOC	III									
Cairo Governorate			III									
El Basateen Slum Area			III									
	El Khalifa General Hospital	CEOC	III									
	El Basateen Slum Area	BEOC	III									

**ANNEX F - SUMMARY OF MANAGEMENT IMPROVEMENT
ACTIVITIES AT DISTRICT LEVEL**

QPMR VI Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Target Governorates Total		38	39	15	270	291	155	24		15				45	220
Qena Governorate		2	2	2	30	32	22	2		2				2	6
Qift District		1	Yes	Yes	15	15	11	1		Yes				Yes	4
Qift District Hospital		Yes													
Qift District Hospital		NA													
Qift District Hospital		NA													
Qift District Hospital		NA													
El Wakf District		1	Yes	Yes	15	17	11	1		Yes				Yes	4
El Wakf District Hospital		Yes													
El Wakf District Hospital		NA													
El Wakf District Hospital		NA													
El Wakf District Hospital		NA													
Fayoum Governorate		2	2	2	30	34	20	2		2				2	6
Sennoures District		1	Yes	Yes	14	16	10	1		Yes				Yes	4
Sennoures District Hospital		Yes													
Sennoures District Hospital		NA													
Sennoures District Hospital		NA													
Sennoures District Hospital		NA													
Sennoures District Hospital		NA													
Maternity Center		NA													
Fedimeen District Hospital		NA													
Tamia District		1	Yes	Yes	15	15	10	1		Yes				Yes	5
Tamia District Hospital		Yes													
Tamia District Hospital		NA													
Tamia District Hospital		NA													
Tamia District Hospital		NA													
Tamia District Hospital		NA													
Maternity Center		NA													
Sersena L.H.U		NA													
Beni Suef Governorate		2	2	2	30	40	16	2		2				2	6
Nasser District		1	Yes	Yes	12	20	6	1		Yes				Yes	4
Nasser District Hospital		Yes													
Nasser District Hospital		NA													
Nasser District Hospital		NA													
Nasser District Hospital		NA													
Nasser District Hospital		NA													
Maternity Center		NA													
Ashmant L.H.U		NA													
Somosta District		1	Yes	Yes	16	20	6	1		Yes				Yes	4
Somosta District Hospital		Yes													
Somosta District Hospital		NA													
Somosta District Hospital		NA													
Somosta District Hospital		NA													
El Shantour L.H.U		NA													
Dashtout L.H.U		NA													
Assiut Governorate		12	13	3	38	56	35	3		3				11	45
Gharb Assiut District		1	Yes	Yes	11	25	12	1		Yes				Yes	4
El-Eman El-Gadida		Yes													
El-Eman El-Gadida		NA													
El-Eman El-Gadida		NA													
El-Eman El-Gadida		NA													
El-Eman El-Gadida		NA													
El Arabaen Urban Health Center		NA													
Shark Assiut District		1	Yes	Yes	12	15	12	1		Yes				Yes	4

QPMR VI Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Assiut General Hospital	I	Yes													
Assiut General Hospital	I	NA													
Assiut General Hospital	I	NA													
Assiut General Hospital	I	NA													
Assiut General Hospital	I	NA													
Assiut General Hospital	I	NA													
Assiut General Hospital	I	NA													
El Walideia Maternity Center	I	NA													
Markaz Assiut District	I	1	Yes	Yes	15	16	12	1		Yes			Yes	6	
Ob/Gyn Hospital	I	Yes													
Ob/Gyn Hospital	I	NA													
Ob/Gyn Hospital	I	NA													
Ob/Gyn Hospital	I	NA													
Ob/Gyn Hospital	I	NA													
Naga Sabaa Integrated Hospital	I	NA													
El Moteaa Integrated Hospital	I	NA													
El Ghanayem District	II	1	Yes										Yes	4	
El Ghanayem District Hospital	II	Yes													
El Ghanayem District Hospital	II	NA													
El Ghanayem District Hospital	II	NA													
El Ghanayem District Hospital	II	NA													
El Ghanayem District Hospital	II	NA													
UHC, Maternity	II	NA													
El Kouseyah District	II	1	Yes										Yes	4	
El Kouseyah District Hospital	II	Yes													
El Kouseyah District Hospital	II	NA													
El Kouseyah District Hospital	II	NA													
El Kouseyah District Hospital	II	NA													
El Kouseyah District Hospital	II	NA													
El Kouseyah District Hospital	II	NA													
El Kouseyah Maternity	II	NA													
Beni Korra W.H.U	II	NA													
Fazara Integrated Hospital	II	NA													
El Fath District	II		Yes												
El Fath U.H.C	II	NA													
El Atawlia I.H.	II	NA													
El Wasta I.H.	II	NA													
Sahel Seleem District	III	1	Yes										Yes	4	
Sahel Seleem District Hospital	III	Yes													
Sahel Seleem District Hospital	III	NA													
Sahel Seleem District Hospital	III	NA													
Sahel Seleem District Hospital	III	NA													
Sahel Seleem District Hospital	III	NA													
El Badary District	III	1	Yes										Yes	4	
El Badary District Hospital	III	Yes													
El Badary District Hospital	III	NA													
El Badary District Hospital	III	NA													
El Badary District Hospital	III	NA													
El Badary District Hospital	III	NA													
Dayrout District	III	1	Yes												
Dayrout District Hospital	III	Yes													
Dayrout District Hospital	III	NA													
Dayrout District Hospital	III	NA													
Dayrout District Hospital	III	NA													
Dayrout District Hospital	III	NA													
Abu Teig District	III	1	Yes										Yes	4	

QPMR VI Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Abu Teig District Hospital	III	Yes													
Abu Teig District Hospital	III	NA													
Abu Teig District Hospital	III	NA													
Abu Teig District Hospital	III	NA													
Sedfa District	III	1	Yes										Yes	4	
Sedfa District Hospital	III	Yes													
Sedfa District Hospital	III	NA													
Sedfa District Hospital	III	NA													
Sedfa District Hospital	III	NA													
Sedfa District Hospital	III	NA													
Manfalout District	II	1	Yes										Yes	4	
Manfalout District Hospital	III	Yes													
Manfalout District Hospital	III	NA													
Manfalout District Hospital	III	NA													
Manfalout District Hospital	III	NA													
Manfalout District Hospital	III	NA													
Abnoub District	II	1	Yes										Yes	4	
Abnoub District Hospital	III	Yes													
Abnoub District Hospital	III	NA													
Abnoub District Hospital	III	NA													
Abnoub District Hospital	III	NA													
Sohag Governorate		11	11	3	103	69	54	6		3			10	43	
Sohag District	I	1	Yes	Yes	20	20	15	2		Yes			Yes	6	
Sohag General Hospital	I	Yes													
Sohag General Hospital	I	NA													
Sohag General Hospital	I	NA													
Sohag General Hospital	I	NA													
Sohag General Hospital	I	NA													
Sohag General Hospital	I	NA													
Sohag General Hospital	I	NA													
Gazaret Shandaweel I. H.	I	NA													
Balassfoura LH.	I	NA													
Tahta District	II	1	Yes	Yes	20	20	15	2		Yes			Yes	4	
Tahta District Hospital	II	Yes													
Tahta District Hospital	II	NA													
Tahta District Hospital	II	NA													
Tahta District Hospital	II	NA													
Tahta District Hospital	II	NA													
Tahta District Hospital	II	NA													
Tahta Maternity Center	II	NA													
Shaitoura LH.U.	II	NA													
El Sawamaa LH.	II	NA													
Gerga District	II	1	Yes	Yes	15	22	15	2		Yes			Yes	4	
Gerga District Hospital	II	Yes													
Gerga District Hospital	II	NA													
Gerga District Hospital	II	NA													
Gerga District Hospital	II	NA													
Gerga District Hospital	II	NA													
El-Magabra LH.	II	NA													
Tema District	II	1	Yes		9										
Tema District Hospital	II	Yes													
Tema District Hospital	II	NA													
Tema District Hospital	II	NA													
Tema District Hospital	II	NA													
Tema District Hospital	II	NA													
Tema District Hospital	II	NA													

Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Tema U.H.C.	II	NA													
Om Dooma I.H.	II	NA													
El Rayayna I.H.	II	NA													
El Balyana District	II	1	Yes		8								Yes	4	
El Balyana District Hospital	II	Yes													
El Balyana District Hospital	II	NA													
El Balyana District Hospital	II	NA													
El Balyana District Hospital	II	NA													
Al Sheikh Baraka W.H.U	II	NA													
Al Sheikh Marzouk I.H.U	II	NA													
Dar El-Salam District	II	1	Yes		9								Yes	4	
Dar El-Salam District Hospital	II	Yes													
Dar El-Salam District Hospital	II	NA													
Dar El-Salam District Hospital	II	NA													
Dar El-Salam District Hospital	II	NA													
Dar El-Salam District Hospital	II	NA													
El Naghameesh RHU	II	NA													
Saqolta District	II	1	Yes										Yes	4	
Saqolta District Hospital	II	Yes													
Saqolta District Hospital	II	NA													
Saqolta District Hospital	II	NA													
Saqolta District Hospital	II	NA													
Saqolta District Hospital	II	NA													
Saqolta Maternity	II	NA													
El Galaweya I.H	II	NA													
Geheina District	II	1	Yes		7	7							Yes	4	
Geheina District Hospital	II	Yes													
Geheina District Hospital	II	NA													
Geheina District Hospital	II	NA													
Geheina District Hospital	II	NA													
Geheina District Hospital	II	NA													
Eneibis I.H	II	NA													
Maragha District	II	1	Yes										Yes	4	
Maragha District Hospital	II	Yes													
Maragha District Hospital	II	NA													
Maragha District Hospital	II	NA													
Maragha District Hospital	II	NA													
Maragha District Hospital	II	NA													
Shandaweel I.H.	II	NA													
El Gherazat I.H.U.	II	NA													
Akhmeim District	II	1	Yes		8								Yes	4	
Akhmeim District Hospital	II	Yes													
Akhmeim District Hospital	II	NA													
Akhmeim District Hospital	II	NA													
Akhmeim District Hospital	II	NA													
Akhmeim District Hospital	II	NA													
Neida I.H.	II	NA													
El Koola I.H.	II	NA													
El-Mounshaa District	II	1	Yes		9								Yes	5	
El-Mounshaa District Hospital	II	Yes													
El-Mounshaa District Hospital	II	NA													
El-Mounshaa District Hospital	II	NA													
El-Mounshaa District Hospital	II	NA													
El-Mounshaa District Hospital	II	NA													
Maternity Center	II	NA													
El Zok El Sharkia I.H.	II	NA													

QPMR VI Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Awlad El Sheikh W.H.U	II	NA													
Awlad Hamza L.H.	II	NA													
Menya Governorate		9	9	3	34	60	37	9		3			9	35	
Menya District	I	1	Yes	Yes	11	20	12	3		Yes			Yes	6	
Menya General Hospital	I	Yes													
Menya General Hospital	I	NA													
Menya General Hospital	I	NA													
Menya General Hospital	I	NA													
Menya General Hospital	I	NA													
Menya General Hospital	I	NA													
Menya General Hospital	I	NA													
Suzan Mubarak Medical Center	I	NA													
Damsheer L.H.U.	I	NA													
Talla L.H.	I	NA													
Tahnasha L.H.	I	NA													
Tahna El Gabal L.H.	I	NA													
Samalout District	I	1	Yes	Yes	11	20	12	3		Yes			Yes	4	
Samalout District Hospital	I	Yes													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Quloona L.H.	I	NA													
Daqoof L.H.	I	NA													
El Saleba L.H.U.	I	NA													
Manshiat El Sheraie L.H.	I	NA													
El Bayaho L.H.	I	NA													
Fekrya District	II	1	Yes	Yes	12	20	13	3		Yes			Yes	4	
Fekrya District Hospital	II	Yes													
Fekrya District Hospital	II	NA													
Fekrya District Hospital	II	NA													
Fekrya District Hospital	II	NA													
Fekrya District Hospital	II	NA													
Asmant L.H.U.	II	NA													
Deir Mowas District	II	1	Yes										Yes	4	
Deir Mowas District Hospital	II	Yes													
Deir Mowas District Hospital	II	NA													
Deir Mowas District Hospital	II	NA													
Deir Mowas District Hospital	II	NA													
Deir Mowas District Hospital	II	NA													
Suzan Mubarak Urban Health Center	II	NA													
Deir Mowas Maternity	II	NA													
Nazlet Badraman L.H.	II	NA													
Beni Haraam H. U.	II	NA													
Beni Mazar District	II	1	Yes										Yes	4	
Beni Mazar District Hospital	II	Yes													
Beni Mazar District Hospital	II	NA													
Beni Mazar District Hospital	II	NA													
Beni Mazar District Hospital	II	NA													
Beni Mazar District Hospital	II	NA													
Beni Mazar District Hospital	II	NA													
Sandafa L.H.	II	NA													
Beni Ali L.H.	II	NA													
Abu Garg W.H.C.	II	NA													

QPMR VI	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Governorate District															
El Sheikh Fadl I.H	II	NA													
Maghagha District	III	1	Yes										Yes	4	
Maghagha District Hospital	III	Yes													
Maghagha District Hospital	III	NA													
Maghagha District Hospital	III	NA													
Maghagha District Hospital	III	NA													
Maghagha District Hospital	III	NA													
Maghagha District Hospital	III	NA													
Mattay District	III	1	Yes										Yes	4	
Mattay District Hospital	III	Yes													
Mattay District Hospital	III	NA													
Mattay District Hospital	III	NA													
Mattay District Hospital	III	NA													
Mattay District Hospital	III	NA													
El Edwa District	III	1	Yes										Yes	4	
El Edwa District Hospital	III	Yes													
El Edwa District Hospital	III	NA													
El Edwa District Hospital	III	NA													
El Edwa District Hospital	III	NA													
El Edwa District Hospital	III	NA													
El Edwa District Hospital	III	NA													
Mallawi District	III	1	Yes										Yes	4	
Mallawi District Hospital	III	Yes													
Mallawi District Hospital	III	NA													
Mallawi District Hospital	III	NA													
Mallawi District Hospital	III	NA													
Mallawi District Hospital	III	NA													
Giza Governorate													9	68	
North Giza District													Yes	4	
El-Tahrir District Hospital															
El-Tahrir District Hospital		NA													
El-Tahrir District Hospital		NA													
El-Tahrir District Hospital		NA													
El-Tahrir District Hospital		NA											No	4	
El Agouza District															
Embaba General Hospital															
Embaba General Hospital		NA													
Embaba General Hospital		NA													
Embaba General Hospital		NA													
Embaba General Hospital		NA													
El Omrania District													Yes	4	
El Omrania District Hospital															
El Omrania District Hospital		NA													
El Omrania District Hospital		NA													
El Omrania District Hospital		NA													
South Giza District	IV												Yes	4	
Om El-Masryeen Hospital	IV														
Om El-Masryeen Hospital	IV	NA													
Om El-Masryeen Hospital	IV	NA													
Om El-Masryeen Hospital	IV	NA													
Om El-Masryeen Hospital	IV	NA													
El-Haram District													Yes	4	
El-Haram District Hospital															
El-Haram District Hospital		NA													
El-Haram District Hospital		NA													
El-Haram District Hospital		NA													
El-Haram District Hospital		NA													

QPMR VI Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Markaz Giza District	IV												Yes	4	
Markaz Giza District Hospital	IV														
Abu El-Nomros Hospital	IV	NA													
Markaz Giza District Hospital	IV	NA													
Markaz Giza District Hospital	IV	NA													
Markaz Giza District Hospital	IV	NA													
Warak District	IV												Yes	4	
Warak District Hospital	IV														
Warak District Hospital	IV	NA													
Warak District Hospital	IV	NA													
Warak District Hospital	IV	NA													
Oseim District	IV												No	4	
Oseim District Hospital	IV														
Oseim District Hospital	IV	NA													
Oseim District Hospital	IV	NA													
Oseim District Hospital	IV	NA													
Hawamdeya District	III												No	4	
Hawamdeya District Hospital	III														
Hawamdeya District Hospital	III	NA													
Hawamdeya District Hospital	III	NA													
Hawamdeya District Hospital	III	NA													
Hawamdeya District Hospital	III	NA													
El Badrashein District	III												Yes	4	
El Badrashein District Hospital	III														
El Badrashein District Hospital	III	NA													
El Badrashein District Hospital	III	NA													
El Badrashein District Hospital	III	NA													
El Badrashein District Hospital	III	NA													
El Ayaat District	III												Yes	4	
El Ayaat District Hospital	III														
El Ayaat District Hospital	III	NA													
El Ayaat District Hospital	III	NA													
El Ayaat District Hospital	III	NA													
El Saff District	III												No	4	
El Saff District Hospital	III														
El Saff District Hospital	III	NA													
El Saff District Hospital	III	NA													
El Saff District Hospital	III	NA													
Elfeih District	III												No	4	
Elfeih District Hospital	III														
Elfeih District Hospital	III	NA													
Elfeih District Hospital	III	NA													
Elfeih District Hospital	III	NA													
El Wahat Baharia District	III												No	4	
El Wahat Baharia District Hospital	III														
El Wahat Baharia District Hospital	III	NA													
El Wahat Baharia District Hospital	III	NA													
El Wahat Baharia District Hospital	III	NA													
El Wahat Baharia District Hospital	III	NA													
Menshaat El Qanater District	IV												No	4	
Menshaat El Qanater District Hospital	IV														
Menshaat El Qanater District Hospital	IV	NA													
Menshaat El Qanater District Hospital	IV	NA													
Menshaat El Qanater District Hospital	IV	NA													
El Dokki District													No	4	
El Dokki District Hospital															

QPMR VI Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Om El-Abtal Hospital		NA													
El Dokki District Hospital		NA													
El Dokki District Hospital		NA													
El Dokki District Hospital		NA													
Boulaq El Dakroul District													Yes	4	
Boulaq El Dakroul Hospital															
Boulaq El Dakroul Hospital		NA													
Boulaq El Dakroul Hospital		NA													
Boulaq El Dakroul Hospital		NA													
Boulak El Dakroul Hospital		NA													
Giza Governorate															
Ezbat El Mattar Slum Area															
Imbaba General Hospital															
Ezbat EL Mattar Slum Area															
Cairo Governorate															
El Basateen Slum Area															
El Khalifa General Hospital															
El Basateen Slum Area															

**ANNEX G - SUMMARY OF MANAGEMENT IMPROVEMENT
ACTIVITIES AT GOVERNORATE LEVEL**

QPMR VI		No. of Districts	GSMC Established & Trained	GHC Established & Oriented	GSMC Meetings	Joint GSMC/GHC Meetings	GSMC Members Trained	GHC Members Oriented	Governorate Information Center Upgraded
Governorate									
Totals		50	6	6	42	8	80	79	6
Qena		2	Yes	Yes	11	2	14	7	Yes
Fayoum		2	Yes	Yes	9	2	16	16	Yes
Beni Suef		2	Yes	Yes	6	1	10	10	Yes
Assiut		13	Yes	Yes	5	1	14	16	Yes
Sohag		11	Yes	Yes	7	1	14	12	Yes
Menya		9	Yes	Yes	4	1	12	18	Yes
Giza		11							

ANNEX H - STATUS OF COMMUNITY LEVEL ACTIVITIES

Status of Community Level Activities

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Target Governorates Total				139	49	47	47
Gena Governorate				6	2	2	2
Qift District				3	1	1	1
Qift District Hospital		CEOC	1	Yes	Yes	Yes	Yes
Qift District Hospital		CSSD	1	Yes	NA	NA	NA
Qift District Hospital		LR	1	NA	NA	NA	NA
Qift District Hospital		OR	1	Yes	NA	NA	NA
El Wafd District				3	1	1	1
El Wafd District Hospital		CEOC	1	Yes	Yes	Yes	Yes
El Wafd District Hospital		CSSD	1	Yes	NA	NA	NA
El Wafd District Hospital		LR	1	NA	NA	NA	NA
El Wafd District Hospital		OR	1	Yes	NA	NA	NA

Status of Community Level Activities

04/07/2003

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Fayoum Governorate				12	4	4	4
Sennoures District			I	6	2	2	2
Sennoures District Hospital		CEOC	I	Yes	NA	NA	NA
Sennoures District Hospital		NCU2	I	Yes	NA	NA	NA
Sennoures District Hospital		CSSD	I	Yes	NA	NA	NA
Sennoures District Hospital		LR	I	NA	NA	NA	NA
Sennoures District Hospital		OR	I	Yes	NA	NA	NA
Maternity Center		BEOC	I	Yes	Yes	Yes	Yes
Fedimeen District Hospital		BEOC	I	Yes	Yes	Yes	Yes
Tamia District			I	6	2	2	2
Tamia District Hospital		CEOC	I	Yes	NA	NA	NA
Tamia District Hospital		NCU2	I	Yes	NA	NA	NA
Tamia District Hospital		CSSD	I	Yes	NA	NA	NA
Tamia District Hospital		LR	I	NA	NA	NA	NA
Tamia District Hospital		OR	I	Yes	NA	NA	NA
Maternity Center		BEOC	I	Yes	Yes	Yes	Yes
Sersena I.H.U		BEOC	I	Yes	Yes	Yes	Yes

Status of Community Level Activities

04/07/2003

QPMR VI	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate District Facility						
Beni Suef Governorate			11	4	4	4
Nasser District		1	6	2	2	2
Nasser District Hospital	CEOC	1	Yes	NA	NA	NA
Nasser District Hospital	NCU2	1	Yes	NA	NA	NA
Nasser District Hospital	CSSD	1	Yes	NA	NA	NA
Nasser District Hospital	LR	1	NA	NA	NA	NA
Nasser District Hospital	OR	1	Yes	NA	NA	NA
Maternity Center	BEOC	1	Yes	Yes	Yes	Yes
Ashmant LHU	BEOC	1	Yes	Yes	Yes	Yes
Somosta District		1	5	2	2	2
Somosta District Hospital	CEOC	1	Yes	NA	NA	NA
Somosta District Hospital	CSSD	1	Yes	NA	NA	NA
Somosta District Hospital	LR	1	NA	NA	NA	NA
Somosta District Hospital	OR	1	Yes	NA	NA	NA
EI Shamber LHU	BEOC	1	Yes	Yes	Yes	Yes
Dashout LHU	BEOC	1	Yes	Yes	Yes	Yes

Status of Community Level Activities

04/07/2003

QPMR VI						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Assiut Governorate			19	10	8	8
Gharb Assiut District			6	1	1	1
El-Eman El-Gadida	CEOC	I	Yes	NA	NA	NA
El-Eman El-Gadida	NCU2	I	Yes	NA	NA	NA
El-Eman El-Gadida	CSSD	I	Yes	NA	NA	NA
El-Eman El-Gadida	LR	I	NA	NA	NA	NA
El-Eman El-Gadida	OR	I	Yes	NA	NA	NA
El-Eman El-Gadida	ER	I	Yes	NA	NA	NA
El Arabaen Urban Health Center	BEOC	I	Yes	Yes	Yes	Yes
Shark Assiut District			7	1	1	1
Assiut General Hospital	CEOC	I	Yes	NA	NA	NA
Assiut General Hospital	NCU2	I	Yes	NA	NA	NA
Assiut General Hospital	CSSD	I	Yes	NA	NA	NA
Assiut General Hospital	LR	I	NA	NA	NA	NA
Assiut General Hospital	OR	I	Yes	NA	NA	NA
Assiut General Hospital	ER	I	Yes	NA	NA	NA
Assiut General Hospital	Lab	I	Yes	NA	NA	NA
El Waldeia Maternity Center	BEOC	I	Yes	Yes	Yes	Yes
Markaz Assiut District			6	2	2	2
Ob/Gyn Hospital	CEOC	I	Yes	NA	NA	NA
Ob/Gyn Hospital	NICU	I	Yes	NA	NA	NA
Ob/Gyn Hospital	CSSD	I	Yes	NA	NA	NA
Ob/Gyn Hospital	LR	I	NA	NA	NA	NA
Ob/Gyn Hospital	OR	I	Yes	NA	NA	NA
Naga Sabaa Integrated Hospital	BEOC	I	Yes	Yes	Yes	Yes
El Moteaa Integrated Hospital	BEOC	I	Yes	Yes	Yes	Yes
El Ghanayem District						
El Ghanayem District Hospital	CEOC	II		NA	NA	NA
El Ghanayem District Hospital	NCU2	II		NA	NA	NA
El Ghanayem District Hospital	CSSD	II		NA	NA	NA
El Ghanayem District Hospital	LR	II		NA	NA	NA
El Ghanayem District Hospital	OR	II		NA	NA	NA
UHC, Maternity	BEOC	II				
El Kouseyah District				3	1	1
El Kouseyah District Hospital	CEOC	II		NA	NA	NA
El Kouseyah District Hospital	NCU2	II		NA	NA	NA
El Kouseyah District Hospital	CSSD	II		NA	NA	NA
El Kouseyah District Hospital	LR	II		NA	NA	NA
El Kouseyah District Hospital	OR	II		NA	NA	NA
El Kouseyah District Hospital	ER	II		NA	NA	NA
El Kouseyah Maternity	BEOC	II		Yes	Yes	Yes
Beni Korra W.H.U	BEOC	II		Yes		
Fazara Integrated Hospital	BEOC	II		Yes		
El Fath District				3	3	3
El Fath U.H.C	BEOC	II		Yes	Yes	Yes
El Abawla I.H.	BEOC	II		Yes	Yes	Yes
El Wasta I.H.	BEOC	II		Yes	Yes	Yes
Sahel Seleem District						
Sahel Seleem District Hospital	CEOC	III		NA	NA	NA
Sahel Seleem District Hospital	NCU2	III		NA	NA	NA
Sahel Seleem District Hospital	CSSD	III		NA	NA	NA
Sahel Seleem District Hospital	LR	III		NA	NA	NA
Sahel Seleem District Hospital	OR	III		NA	NA	NA
El Badary District						
El Badary District Hospital	CEOC	III		NA	NA	NA
El Badary District Hospital	NCU2	III		NA	NA	NA
El Badary District Hospital	CSSD	III		NA	NA	NA
El Badary District Hospital	LR	III		NA	NA	NA
El Badary District Hospital	OR	III		NA	NA	NA
Dayrout District						

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
	Dayrout District Hospital	CEOC	III		NA	NA	NA
	Dayrout District Hospital	NCUZ	III		NA	NA	NA
	Dayrout District Hospital	CSSD	III		NA	NA	NA
	Dayrout District Hospital	LR	III		NA	NA	NA
	Dayrout District Hospital	OR	III		NA	NA	NA
Abu Teig District			III				
	Abu Teig District Hospital	CEOC	III		NA	NA	NA
	Abu Teig District Hospital	CSSD	III		NA	NA	NA
	Abu Teig District Hospital	LR	III		NA	NA	NA
	Abu Teig District Hospital	OR	III		NA	NA	NA
Sedfa District			III				
	Sedfa District Hospital	CEOC	III		NA	NA	NA
	Sedfa District Hospital	NCUZ	III		NA	NA	NA
	Sedfa District Hospital	CSSD	III		NA	NA	NA
	Sedfa District Hospital	LR	III		NA	NA	NA
	Sedfa District Hospital	OR	III		NA	NA	NA
Manfalous District			III				
	Manfalous District Hospital	CEOC	III		NA	NA	NA
	Manfalous District Hospital	NCUZ	III		NA	NA	NA
	Manfalous District Hospital	CSSD	III		NA	NA	NA
	Manfalous District Hospital	LR	III		NA	NA	NA
	Manfalous District Hospital	OR	III		NA	NA	NA
Abnoub District			III				
	Abnoub District Hospital	CEOC	III		NA	NA	NA
	Abnoub District Hospital	CSSD	III		NA	NA	NA
	Abnoub District Hospital	LR	III		NA	NA	NA
	Abnoub District Hospital	OR	III		NA	NA	NA

Status of Community Level Activities

04/07/2003

QPMR VI						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Sohag Governorate			64	14	14	14
Sohag District			8	2	2	2
Sohag General Hospital	CEOC	I	Yes	NA	NA	NA
Sohag General Hospital	NCU2	I	Yes	NA	NA	NA
Sohag General Hospital	CSSD	I	Yes	NA	NA	NA
Sohag General Hospital	LR	I	NA	NA	NA	NA
Sohag General Hospital	OR	I	Yes	NA	NA	NA
Sohag General Hospital	ER	I	Yes	NA	NA	NA
Sohag General Hospital	Lab	I	Yes	NA	NA	NA
Gazeret Shandawel I. H.	BEOC	I	Yes	Yes	Yes	Yes
Balastoura I.H.	BEOC	I	Yes	Yes	Yes	Yes
Tahta District			8	3	3	3
Tahta District Hospital	CEOC	II	Yes	NA	NA	NA
Tahta District Hospital	NCU2	II	Yes	NA	NA	NA
Tahta District Hospital	CSSD	II	Yes	NA	NA	NA
Tahta District Hospital	LR	II	NA	NA	NA	NA
Tahta District Hospital	OR	II	Yes	NA	NA	NA
Tahta District Hospital	ER	II	Yes	NA	NA	NA
Tahta Maternity Center	BEOC	II	Yes	Yes	Yes	Yes
Shattoura I.H.U.	BEOC	II	Yes	Yes	Yes	Yes
El Sawamaa I.H.	BEOC	II	Yes	Yes	Yes	Yes
Gerga District			5	1	1	1
Gerga District Hospital	CEOC	II	Yes	NA	NA	NA
Gerga District Hospital	NCU2	II	Yes	NA	NA	NA
Gerga District Hospital	CSSD	II	Yes	NA	NA	NA
Gerga District Hospital	LR	II	NA	NA	NA	NA
Gerga District Hospital	OR	II	Yes	NA	NA	NA
El-Magabra I.H.	BEOC	II	Yes	Yes	Yes	Yes
Tema District			8	3	3	3
Tema District Hospital	CEOC	II	Yes	NA	NA	NA
Tema District Hospital	NCU2	II	Yes	NA	NA	NA
Tema District Hospital	CSSD	II	Yes	NA	NA	NA
Tema District Hospital	LR	II	No	NA	NA	NA
Tema District Hospital	OR	II	Yes	NA	NA	NA
Tema District Hospital	ER	II	Yes	NA	NA	NA
Tema U.H.C.	BEOC	II	Yes	Yes	Yes	Yes
Om Dooma I.H.	BEOC	II	Yes	Yes	Yes	Yes
El Rayayna I.H.	BEOC	II	Yes	Yes	Yes	Yes
El Balyana District			5			
El Balyana District Hospital	CEOC	II	Yes	NA	NA	NA
El Balyana District Hospital	CSSD	II	Yes	NA	NA	NA
El Balyana District Hospital	LR	II	NA	NA	NA	NA
El Balyana District Hospital	OR	II	Yes	NA	NA	NA
Al Sheikh Baraka W.H.U	BEOC	II	Yes			
Al Sheikh Marzouk I.H.U	BEOC	II	Yes			
Dar El-Salam District			5			
Dar El-Salam District Hospital	CEOC	II	Yes	NA	NA	NA
Dar El-Salam District Hospital	NCU2	II	Yes	NA	NA	NA
Dar El-Salam District Hospital	CSSD	II	Yes	NA	NA	NA
Dar El-Salam District Hospital	LR	II	NA	NA	NA	NA
Dar El-Salam District Hospital	OR	II	Yes	NA	NA	NA
El Naghameesh RHJ	BEOC	II	Yes			
Saqolta District						
Saqolta District Hospital	CEOC	II		NA	NA	NA
Saqolta District Hospital	NCU2	II		NA	NA	NA
Saqolta District Hospital	CSSD	II		NA	NA	NA
Saqolta District Hospital	LR	II		NA	NA	NA
Saqolta District Hospital	OR	II		NA	NA	NA
Saqolta Maternity	BEOC	II				
El Galaweya I.H	BEOC	II				

Status of Community Level Activities

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Geheina District			II	5	1	1	1
	Geheina District Hospital	CEOC	II	Yes	NA	NA	NA
	Geheina District Hospital	NCU2	II	Yes	NA	NA	NA
	Geheina District Hospital	CSSD	II	Yes	NA	NA	NA
	Geheina District Hospital	LR	II	NA	NA	NA	NA
	Geheina District Hospital	OR	II	Yes	NA	NA	NA
	Enabis LH	BEOC	II	Yes	Yes	Yes	Yes
Maragha District			II	6	2	2	2
	Maragha District Hospital	CEOC	II	Yes	NA	NA	NA
	Maragha District Hospital	NCU	II	Yes	NA	NA	NA
	Maragha District Hospital	CSSD	II	Yes	NA	NA	NA
	Maragha District Hospital	LR	II	NA	NA	NA	NA
	Maragha District Hospital	OR	II	Yes	NA	NA	NA
	Shandawol LH.	BEOC	II	Yes	Yes	Yes	Yes
	EI Gherazal LH.U.	BEOC	II	Yes	Yes	Yes	Yes
Akhmeim District			II	6	2	2	2
	Akhmeim District Hospital	CEOC	II	Yes	NA	NA	NA
	Akhmeim District Hospital	NCU2	II	Yes	NA	NA	NA
	Akhmeim District Hospital	CSSD	II	Yes	NA	NA	NA
	Akhmeim District Hospital	LR	II	NA	NA	NA	NA
	Akhmeim District Hospital	OR	II	Yes	NA	NA	NA
	Neida LH.	BEOC	II	Yes	Yes	Yes	Yes
	EI Koola LH.	BEOC	II	Yes	Yes	Yes	Yes
EI-Mounshaa District			II	6			
	EI-Mounshaa District Hospital	CEOC	II	Yes	NA	NA	NA
	EI-Mounshaa District Hospital	NCU2	II	Yes	NA	NA	NA
	EI-Mounshaa District Hospital	CSSD	II	Yes	NA	NA	NA
	EI-Mounshaa District Hospital	LR	II	NA	NA	NA	NA
	EI-Mounshaa District Hospital	OR	II	Yes	NA	NA	NA
	Maternity Center	BEOC	II	Yes			
	EI Zok EI Sharbia LH.	BEOC	II	Yes			
	Awlad EI Sheikh W.H.U.	BEOC	II	Yes			
	Awlad Hamza LH.	BEOC	II	Yes			

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Menya Governorate				27	15	15	15
Menya District			I	11	5	5	5
Menya General Hospital	CEOC	I	Yes	NA	NA	NA	NA
Menya General Hospital	NCU2	I	Yes	NA	NA	NA	NA
Menya General Hospital	CSSD	I	Yes	NA	NA	NA	NA
Menya General Hospital	LR	I	NA	NA	NA	NA	NA
Menya General Hospital	OR	I	Yes	NA	NA	NA	NA
Menya General Hospital	ER	I	Yes	NA	NA	NA	NA
Menya General Hospital	Lab	I	Yes	NA	NA	NA	NA
Suzan Mubarak Medical Center	BEOC	I	Yes	Yes	Yes	Yes	Yes
Damshier I.H.U.	BEOC	I	Yes	Yes	Yes	Yes	Yes
Talla I.H.	BEOC	I	Yes	Yes	Yes	Yes	Yes
Tahnasha I.H.	BEOC	I	Yes	Yes	Yes	Yes	Yes
Tahna El Gabal I.H.	BEOC	I	Yes	Yes	Yes	Yes	Yes
Samalout District			I	11	5	5	5
Samalout District Hospital	CEOC	I	Yes	NA	NA	NA	NA
Samalout District Hospital	NCU2	I	Yes	NA	NA	NA	NA
Samalout District Hospital	CSSD	I	Yes	NA	NA	NA	NA
Samalout District Hospital	LR	I	NA	NA	NA	NA	NA
Samalout District Hospital	OR	I	Yes	NA	NA	NA	NA
Samalout District Hospital	ER	I	Yes	NA	NA	NA	NA
Samalout District Hospital	Lab	I	Yes	NA	NA	NA	NA
Qulosna I.H.	BEOC	I	Yes	Yes	Yes	Yes	Yes
Daqoof I.H.	BEOC	I	Yes	Yes	Yes	Yes	Yes
El Saleba I.H.U.	BEOC	I	Yes	Yes	Yes	Yes	Yes
Manshiat El Sheraiet I.H.	BEOC	I	Yes	Yes	Yes	Yes	Yes
El Bayaho I.H.	BEOC	I	Yes	Yes	Yes	Yes	Yes
Fekrya District			II	5	1	1	1
Fekrya District Hospital	CEOC	II	Yes	NA	NA	NA	NA
Fekrya District Hospital	NCU2	II	Yes	NA	NA	NA	NA
Fekrya District Hospital	CSSD	II	Yes	NA	NA	NA	NA
Fekrya District Hospital	LR	II	NA	NA	NA	NA	NA
Fekrya District Hospital	OR	II	Yes	NA	NA	NA	NA
Asmant I.H.U.	BEOC	II	Yes	Yes	Yes	Yes	Yes
Deir Mowas District			II		3	3	3
Deir Mowas District Hospital	CEOC	II			NA	NA	NA
Deir Mowas District Hospital	NCU2	II			NA	NA	NA
Deir Mowas District Hospital	CSSD	II			NA	NA	NA
Deir Mowas District Hospital	LR	II			NA	NA	NA
Deir Mowas District Hospital	OR	II			NA	NA	NA
Suzan Mubarak Urban Health Center	NCU2	II			NA	NA	NA
Deir Mowas Maternity	BEOC	II			Yes	Yes	Yes
Nazlet Badraman I.H.	BEOC	II			Yes	Yes	Yes
Beni Haraam H.U.	BEOC	II			Yes	Yes	Yes
Beni Mazar District			II		1	1	1
Beni Mazar District Hospital	CEOC	II			NA	NA	NA
Beni Mazar District Hospital	NCU2	II			NA	NA	NA
Beni Mazar District Hospital	CSSD	II			NA	NA	NA
Beni Mazar District Hospital	LR	II			NA	NA	NA
Beni Mazar District Hospital	OR	II			NA	NA	NA
Beni Mazar District Hospital	ER	II			NA	NA	NA
Sandafa I.H.	BEOC	II			Yes	Yes	Yes
Beni Ali I.H.	BEOC	II					
Abu Garg W.H.C	BEOC	II					
El Sheikh Fadl I.H.	BEOC	II					
Maghagha District			III				
Maghagha District Hospital	CEOC	III			NA	NA	NA
Maghagha District Hospital	NCU2	III			NA	NA	NA
Maghagha District Hospital	CSSD	III			NA	NA	NA
Maghagha District Hospital	LR	III			NA	NA	NA

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
	Maghagha District Hospital	OR	III		NA	NA	NA
	Maghagha District Hospital	ER	III		NA	NA	NA
Maltay District			III				
	Maltay District Hospital	CEOC	III		NA	NA	NA
	Maltay District Hospital	NCU	III		NA	NA	NA
	Maltay District Hospital	CSSD	III		NA	NA	NA
	Maltay District Hospital	LR	III		NA	NA	NA
	Maltay District Hospital	OR	III		NA	NA	NA
El Edwa District			III				
	El Edwa District Hospital	CEOC	III		NA	NA	NA
	El Edwa District Hospital	NCU	III		NA	NA	NA
	El Edwa District Hospital	CSSD	III		NA	NA	NA
	El Edwa District Hospital	LR	III		NA	NA	NA
	El Edwa District Hospital	OR	III		NA	NA	NA
Ma Jawi District			III				
	Mallawi District Hospital	CEOC	III		NA	NA	NA
	Mallawi District Hospital	NCL2	III		NA	NA	NA
	Mallawi District Hospital	CSSD	III		NA	NA	NA
	Mallawi District Hospital	LR	III		NA	NA	NA
	Mallawi District Hospital	OR	III		NA	NA	NA

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Giza Governorate							
North Giza District							
	El-Tahrir District Hospital	CEOC			NA	NA	NA
	El-Tahrir District Hospital	NCU2		NA	NA	NA	NA
	El-Tahrir District Hospital	CSSD					
	El-Tahrir District Hospital	LR					
	El-Tahrir District Hospital	OR					
El Agouza District							
	Embaba General Hospital	CEOC			NA	NA	NA
	Embaba General Hospital	NCU3		NA	NA	NA	NA
	Embaba General Hospital	CSSD					
	Embaba General Hospital	LR					
	Embaba General Hospital	OR					
El Omrania District							
	El Omrania District Hospital	CEOC			NA	NA	NA
	El Omrania District Hospital	CSSD					
	El Omrania District Hospital	LR					
	El Omrania District Hospital	OR					
South Giza District							
	Om El-Masryeen Hospital	CEOC	IV		NA	NA	NA
	Om El-Masryeen Hospital	NCU2	IV	NA	NA	NA	NA
	Om El-Masryeen Hospital	CSSD	IV				
	Om El-Masryeen Hospital	LR	IV				
	Om El-Masryeen Hospital	OR	IV				
El-Haram District							
	EH-Haram District Hospital	CEOC			NA	NA	NA
	EH-Haram District Hospital	NCU2		NA	NA	NA	NA
	EH-Haram District Hospital	CSSD					
	EH-Haram District Hospital	LR					
	EH-Haram District Hospital	OR					
Markaz Giza District							
	Markaz Giza District Hospital	CEOC	IV		NA	NA	NA
	Abu El-Nomros Hospital	NCU2	IV	NA	NA	NA	NA
	Markaz Giza District Hospital	CSSD	IV				
	Markaz Giza District Hospital	LR	IV				
	Markaz Giza District Hospital	OR	IV				
Warak District							
	Warak District Hospital	CEOC	IV		NA	NA	NA
	Warak District Hospital	CSSD	IV				
	Warak District Hospital	LR	IV				
	Warak District Hospital	OR	IV				
Oseim District							
	Oseim District Hospital	CEOC	IV		NA	NA	NA
	Oseim District Hospital	CSSD	IV				
	Oseim District Hospital	LR	IV				
	Oseim District Hospital	OR	IV				
Hawamdeya District							
	Hawamdeya District Hospital	CEOC	III		NA	NA	NA
	Hawamdeya District Hospital	NCU2	III	NA	NA	NA	NA
	Hawamdeya District Hospital	CSSD	III				
	Hawamdeya District Hospital	LR	III				
	Hawamdeya District Hospital	OR	III				
El Badrashein District							
	El Badrashein District Hospital	CEOC	III		NA	NA	NA
	El Badrashein District Hospital	NCU2	III	NA	NA	NA	NA
	El Badrashein District Hospital	CSSD	III				
	El Badrashein District Hospital	LR	III				
	El Badrashein District Hospital	OR	III				
El Ayat District							
	El Ayat District Hospital	CEOC	III		NA	NA	NA

QPMR VI		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
	El Ayat District Hospital	CSSD	III				
	El Ayat District Hospital	LR	III				
	El Ayat District Hospital	OR	III				
El Saff District			II				
	El Saff District Hospital	CEOC	III		NA	NA	NA
	El Saff District Hospital	CSSD	III				
	El Saff District Hospital	LR	III				
	El Saff District Hospital	OR	III				
Elfeh District			II				
	Elfeh District Hospital	CEOC	III		NA	NA	NA
	Elfeh District Hospital	CSSD	III				
	Elfeh District Hospital	LR	III				
	Elfeh District Hospital	OR	III				
El Wahat Baharia District			II				
	El Wahat Baharia District Hospital	CEOC	III		NA	NA	NA
	El Wahat Baharia District Hospital	NCU2	III	NA	NA	NA	NA
	El Wahat Baharia District Hospital	CSSD	III				
	El Wahat Baharia District Hospital	LR	III				
	El Wahat Baharia District Hospital	OR	III				
Menshaat El Qanater District			IV				
	Menshaat El Qanater District Hospital	CEOC	IV		NA	NA	NA
	Menshaat El Qanater District Hospital	CSSD	IV				
	Menshaat El Qanater District Hospital	LR	IV				
	Menshaat El Qanater District Hospital	OR	IV				
El Dokki District							
	El Dokki District Hospital	CEOC			NA	NA	NA
	Om El-Abtal Hospital	NCU2		NA	NA	NA	NA
	El Dokki District Hospital	CSSD					
	El Dokki District Hospital	LR					
	El Dokki District Hospital	OR					
Boulaq El Dakroul District							
	Boulaq El Dakroul Hospital	CEOC			NA	NA	NA
	Boulaq El Dakroul Hospital	NCU2					
	Boulaq El Dakroul Hospital	CSSD					
	Boulaq El Dakroul Hospital	LR					
	Boulaq El Dakroul Hospital	OR		NA	NA	NA	NA
Giza Governorate							
Ezbat El Matter Slum Area							
	Imbaba General Hospital	CEOC					
	Ezbat EL Matter Slum Area	BEOC					
Cairo Governorate							
El Basateen Slum Area							
	El Khalfa General Hospital	CEOC					
	El Basateen Slum Area	BEOC					

**ANNEX I - TRAININGS AND WORKSHOPS BY DATE, TITLE,
SITE AND NUMBER OF TRAINEES CONDUCTED DURING THE
PERIOD FROM JANUARY TO MARCH 2002**

SUMMARY OF CLINICAL TRAINING IN UPPER EGYPT (January - March 2003, Quarter VI)

District	No. of Physicians Trained												No. of Nurses Trained							No. of Lead Trainers Trained					
	NC Physician Trained on Basic NC	NC Physician Trained on Advanced NC	EOC Physician Service Providers	(EOC Basic Competency)	(EOC Mastery)	EOC Anesthesia for Physicians	Emergency Services for Physicians	Laboratory Services for Physicians	Blood Bank Services for Physicians	Private sector (physicians)	Private sector (pharmacists)	EOC (Infection control)	Total Physicians Trained	NC Nurses	EOC Nurses	Emergency Services for Nurses	OR Nurses	CSSD Nurses	Midwifery Skills for Nurses	Total Nurses Trained	NC Physicians	EOC Physicians	Emergency Services for Physicians	Anesthesiologists	Nurses
Assiut	6	6										0	12						0					7	7
Assiut												12							12					6	6
Assiut	1	1										0							0					6	6
Bent Sng	5	5	3	4								4	17	2					0						0
Bent Sng												13							0						0
Fayoum	12	13	6	4								4	14	4					0						0
Fayoum												31							18						0
El-Dokki	9	9										0	16						0				6	6	0
El-Dokki												18							16						0
Matruh	15	15	24	13		0		19	20		20	126	21		21	16	18		76						0
Matruh	22	22	75			4	10	6			9	148	26	52		8	8		94						0
Matruh	17		24	15		0			24		20	100		16		20	20		56						0
Matruh	21	20	69			3	12	4			9	138	24	42	18	10	10		84						0
Matruh	38	18	21	17		0	19	21	20		20	174	23	22	18	10	10		83				6	6	0
Matruh	23	23	154			5	8	2			7	222	22	60		9	9		100				6	6	0
Matruh												0							0						0
Matruh												0							0						0
Matruh	70	33	69	53	0	0	19	40	0	64	0	408	44	38	39	46	48	0	215	0	0	0	0	25	25
Matruh	99	99	307	0	0	12	30	12	0	0	0	584	131	160	0	26	26	0	343	0	0	0	0	0	0

- 1) CR = Classroom: Indicate the number to participants who attended classroom/workshop training.
- 2) OJT = On-the-job training: Indicate the number of days spent on post-classroom/workshop OJT.
- 3) NA = Not Applicable: In some cases CR will be NA, i.e., EOC Basic Competency and EOC Mastery.

**SUMMARY OF MANAGEMENT AND COMMUNITY ACTIVITIES IN UPPER EGYPT
(January - March 2003, Quarter VI)**

	G & D SMCs Members Trained				Hospitals SMCs Members Trained		Health Committee members Oriented	GSMCs Meetings	DSMCs Meetings	Hospital SMCs Meetings	SMCs & HC's Joint Meetings	Quarterly Reports	MMSS Training Session (# trained)	MMSS OJT (P/D)	Providers Sensitization (Providers trained)	Community Health Committee members Oriented	Outreach Workers Trained	Community Needs Assessment Conducted	Community Action Plan Developed	Health Educators Training (# trained)	TOT Training (# trained)	IPC Training (# trained)	FGM Training (# trained)	Communication Materials	
	Planning and Management Training (# trained)	Quality Assurance Training (# trained)	TOT (# trained)	Data Use Training (# trained)	Management & Quality Assurance Training (# trained)	TOT (# trained)																		IEC	Publications
Aswan													63	0										22	22
Luxor								2	2				144	16										24	32
									1			1	324	21		60	30	2	2					27	
								2	4	5		1	192	24		270	135	9	9					33	22
								1	18		4	1	605	26		390	195	13	13						32
Matruh								2	7	6	1	1	554	39		90	45	3	3					50	600
Assiut								1	8	2		1	253	48		150	45	3	3				9	48	485
Shubra	39	58			60			1	8	23		1	210	30	39	180	90	6	6					54	755
												1	161	30											
Total	39	58	0	0	60	0	0	9	48	36	5	7	2506	234	39	1140	540	36	36	0	0	0	9	258	1948

**SUMMARY OF MANAGEMENT AND COMMUNITY ACTIVITIES IN UPPER EGYPT
(January - March 2003, Quarter VI)**

	No. of Schools	No. of Students	No. of Trained personnel		Orientation for NGOs (# trained)	NGOs Assessed	Training Proposal Writing (# trained)	Grants Awarded	Training Awarded NGOs		Home Visits by NGO Outreach Workers	Community Seminars	
			Science Technical Supervisors	Science Teachers					Financially & Admin. (# trained)	Outreach Workers (# trained)		Number Conducted	Number of Participants
							21				33209	608	29495
							8				125519	254	10414
							8				231201	510	25927
							15				124369	904	28945
							50				407975	2116	89757
	414	211,312	23	490	54	31							
	405	237,082	29	435	62	20							
Sohag	677	410,776	27	643		54	50						
Giza													
Total	1496	859,170	79	1568	4	105	2	102	0	0	922273	4392	184538

**ANNEX I - MOHP/ USAID/ JSI MONTHLY COORDINATION
MEETINGS**

MOHP/ USAID/JSI Monthly Coordination Meeting

Date: 5 January 2003

Attendees:

Dr. Esmat Mansour,	Undersecretary PHC/ HM/HC Executive Director, MOHP
Dr. Nahed Matta,	HM/HC RP Team Leader, USAID
Eng. Ragi Shoukry,	Engineering Section, HM/HC Project, MOHP
Dr. Reginald Gipson,	Chief of Party, JSI
Mr. Sobhi Moharram,	Deputy Chief of Party, JSI
Ms. Katrina Kruhm,	Project Administrator/ Task11 Manager, JSI
Dr. Hassan el Sheikh,	Implementation Coordinator, JSI
Eng. Mohamed Rashad,	JSI
Eng. Mohamed Aser,	JSI
Eng. Dalia Raafat,	JSI

Venue: JSI Office

I. Phase I Renovations

- All renovations completed except Samosta DH. This is being completed by the MOHP at the governorate level. Renovations expected to be completed in June, 2003. Concern about the completion of the March 15, 2003 Task One milestone was expressed. Dr. Nahed stated that the milestone could still be approved provided all other activities were completed for the facility, including the provision of interim commodities, as the completion of the renovations was outside of the manageable interest for JSI and the HM/HC Project.
- Dr. Nahed also requested a one page summary detailing Phase I renovation expenditures by facility.
- Although minor renovations were completed by JSI in Assuit and Menya GHs in Phase I, it was decided that the MOHP would complete major renovations for these facilities during Phase II.

II. Phase II Renovations

- Sample floor plans were presented by the JSI Engineering Team which was developed in cooperation of Eng. Ragi, HM/HC Project. Floor plans were accepted except for El Badary DH in which Dr. Esmat suggested that the Eclampsia Room be kept separate from the High-Risk Pregnancy Room. The Pre-Labor and High-Risk Pregnancy Room should be combined.
- Discussion was held about the cost of completing renovations from scratch in a separate building. Eng. Ragi was requested to complete the specs for such a

scenario including the drawings, cost estimates, and land requirements. However, Dr. Esmat said that this was against the current policy of the MOHP which was to renovate the facilities present rather than create new facilities.

- The Engineers were requested to get the approval of Undersecretaries of the renovation plans that had not yet been approved.
- JSI will finalize the proposed plans and submit to the MOHP and USAID for final review and comment. Dr. Esmat will then share the plans with H.E. the Minister.
- For Phase II renovations, there is sufficient money to complete all required renovations (LE 2 Million from the PIL and LE 1.5 Million from the GOE contribution).

III. Phase III/IV Renovations

- Floor plans and estimates will be developed for the Phase III/IV facilities (including Giza) will be completed soon and submitted to the MOHP.
- JSI is also drafting the MOC for Giza governorate.

IV. Completion of Renovations

- Preliminary discussions were held related to the completion of renovations. A suggestion was raised that a plaque should be provided at the end of the renovation activity stating that this facility has been renovated by the HM/HC Project. Discussions were also held about QA certification of facilities.
- Dr. Nahed also stated that the H.E. Ambassador would like to be present for the inauguration of some renovated facilities and /or delivery of a major procured commodities, at his convenience, and this should be kept in mind for any major renovation/ commodity delivery in the future.

V. Review of Monthly Calendar

- JSI presented the monthly coordination calendar. A discussion was held about the integrated facility team visits. MOHP participation in the district/ governorate SMC meetings was encouraged. Dr. Esmat and Dr. Nahed expressed interest in attending a governorate-level SMC meeting in January or February.

VI. DT2 Plan for 2003

- Dr. Nahed presented the plan for Dr. Esmat's signature. Discussions were held related to the Hospital Administration course and it was agreed that it would

be better to ask IHP-Santa Cruz if they could add a focus on hospital administration to their current Leadership/TQM course.

- With the cost savings, Dr. Nahed asked for additional course ideas. Suggestions raised were as follows:
 - A course on Research Methodology (Quantitative, Qualitative, and Critical Analysis of Research Studies) for MOHP and University staff was suggested by Dr.Esmat.
 - Increase the number of the participants in the Leadership/TQM course to be held in Santa Cruz from 10 to 15 participants as was suggested by Mr.Sobhi.

Dr. Nahed will discuss both options with DT2 and report back.

- The need to advertise for the first Leadership/TQM course was also discussed. It was stated that the MOHP should advertise for an estimated 25-30 slots assuming that 11-15 participants would be eligible for the visa. Dr. Esmat promised to prepare the criteria for the selection of candidates before the advertisement.

VI. Global Health Conference

- The plan for the GHC was discussed. Dr. Nahed said she would review and sign the concurrence request for JSI staff. She also requested JSI to pay for MOHP staff selected to present at the conference. JSI agreed to send over a concurrence request for signature.
- JSI will look into the pre and post activities that will be held at the conference for participation by the MOHP staff.
- JSI will also send the expenditures to date for MOHP conference/training activities paid under the JSI contract.

VII. USAID Trip Reports

- Dr. Nahed shared her trip reports from recent visits to Assuit and Menya. Some of the issues discussed in detail were as follows:
 - Provision of IMCI training or an abbreviated IMCI training for the anchor facilities. Dr. Said Madkour agreed to review the possibility of including these facilities in the IMCI training program. JSI is to send him the list of the Phase I and II BEOCs.
 - Practical (hands-on) clinical training for the BEOC staff that is being held at the District Hospital need to be emphasized and related directly to JSI clinical supervisors visits to the general and district hospitals in accordance with the MWP. The role of JSI Field Office in coordinating

- these activities, ensuring the participation of the target group of physicians and involving the local lead trainers in this activity is of vital importance.
- There is a need to clarify how the selected Lead Trainers from the DH level could – with close supervision and support from JSI clinical supervisor- provide training to the doctors that are not working in the selected anchors facilities within each district. This –in turn- will necessitate institutionalizing the system of Lead Trainers within MOHP system (Central Department for Human Resources Development) so that Lead Trainers could be compensated from MOHP budget for this additional activity. Dr. Gipson agreed to investigate this issue and submit to the next Monthly Coordination Meeting a proposal.
 - Need to concentrate on the general image of the selected anchors, particularly actions to be taken by MCH General Department and JSI to improve the status of these facilities based on the results of the PHC QA Monitoring Checklists of service standards for the facility.
 - Dr. Gipson said that JSI was looking at appropriate training solutions for home deliveries.

VIII. EOC and NC Modules/Resources and Teleconference Videos

- Dr. Gipson presented completed copies with CDs of the EOC and NC modules/resources. He explained that 250 sets had been produced and that JSI is finalizing the plan for distribution. At least one set will be sent to each of the medical schools and to each of the General/District Hospitals. A proposed list of distribution will be submitted to Dr. Esmat for review and comment.
- Dr. Esmat asked for the estimated cost of duplication to reproduce each set.
- Dr. Gipson also explained that the teleconference videos were being completed and will be distributed with the Module/Resource Sets to be used as a complete package. Each session will be on its own videotape.

VIII. Phase-Out Strategy

- Dr. Nahed expressed her desire to meet again later to discuss the phase-out strategy of HM/HC activities from the Base Period governorates.

IX. Women's Health Card

- Copies of the revised Women's Health Card were presented by JSI. JSI will follow-up to see if there are any additional comments. The cards will be printed by the MOHP.

X. Research Milestone

- Dr. Gipson shared with Dr. Nahed the research dissemination report from the Base Period. Dr. Nahed said she is following up with the Task Five milestone and will respond to JSI soon.

XI. Future Meetings

- A joint meeting was scheduled at 12:30pm on January 14, 2003 at NIHC for a demonstration of the upgraded MHIS system.
- The February monthly coordination meeting was scheduled for Sunday, Feb 2 at 10am in the HM/HC Office. The agenda of the meeting will be as follows:
 - 10-1100 AM Review and discuss MWP.
 - 11-12 A Joint Meeting of the three MOHP Central Departments (Undersecretaries of Human Resource, Nursing Services and PHC/Executive Director HM/HC) to present the results of the Consensus Meeting on the nursing school curriculum and plan to institutionalize it nationally.

**MOHP/USAID/JSI Monthly Coordination Meeting
February 2, 2003**

Attendees:

Dr. Esmat Mansour	Undersecretary Integrated Health Care, HM/HC Executive Director, MOHP
Dr. Azza El Hussein	Undersecretary Research and Studies, MOHP
Dr. Baheya Fouad	Undersecretary Nursing Services, MOHP
Dr. Kahled Nasr	Deputy Executive Director, HM/HC, MOHP
Dr. Nahed Matta	HM/HC RP Team Leader, USAID
Mr. Sobhi Moharram	Deputy Chief of Party, JSI

Venue:

I. Review of Monthly Calendar and Workplan

- JSI presented the MWP with the calendar. The integrated facility team visits were highlighted and discussion was focused on the completion report of the Phasing Out Workshop from Beni Suef which will be held on February 23, 2003. Dr. Esmat confirmed her participation while Dr. Nahed will not be able to attend due to her travel to the States.
- Dr. Nahed reiterated that she would like to have a special meeting on her return to discuss the phase-out strategy.
- Dr. Esmat signed the official letter to the Director General of Health and Population, Beni Suef informing him with the date of the phasing-out, the sustainability planning workshop and the hand over of JSI office to the Governorate Director of MCH on 15 March, 2003.

II. SHIP

- JSI presented to the meeting a memo discussing the current status of implementation of the program by the end of December, 2002 against its three components: Iron supplementation, health education and production of IEC materials and the action plan for the period from January to 15 September, 2003 covering the remaining period of the SHIP two year contract. The meeting also reviewed the memo approved by H.E. the Minister of Health and Population that was submitted by the HM/HC Executive Director and the Chairman of HIO to go national with the program.
- The program was not implemented in the first semester of the scholastic year 2002/2003 due to reasons beyond the control of JSI i.e. non-availability of cups and lag in reproduction of IEC materials and registers.
- JSI confirmed that the program will be implemented in the second semester (February – May 2003) in all the governorates of the Base Period and the three governorates of the Option Period: Sohag, Assiut and Menya.

- It is the decision of the HIO that the iron supplementation component be implemented on the basis of one cup per student for the whole year to save money.
- The SHIP was extended for only two years out of the three years and half, being the duration of the Option Period. The two years contact is completed by a milestone report to be submitted by JSI on September 15, 2003 that reads "*Assist MOHP and HIO to Maintain the Adolescent Anemia Prevention in the Five Original Upper Egypt Governorates and Phase into the New Target Governorates.*"
- By the end of the two years, JSI would have phased into SHIP in the three Upper Egypt Governorates, being Sohag, Assiut and Menya in accordance with the submitted action plan, hence, the milestone report, in JSI's view, Upper Egypt would cover only these governorates. The remaining governorate, i.e. Giza, will be covered on 2006/2007 through the approved going national plan of MOHP/HIO.
- In response to the above, Dr. Nahed Matta made it clear that she would like to return back to her documents before concurring with this.

III. Leadership, TQM and Hospital Administration Course

- It was agreed to ask IHP-Santa Cruz to add a focus on hospital administration to the current Leadership/TQM Course. Dr. Nahed Matta advised that IIE/DT2 informed her that this course will take place on August 2003.
- In a follow up to this agreement, Dr. Nahed Matta informed JSI that a group of IHP-Santa Cruz is in town which represents an opportunity to discuss with them the training design of the course.
- JSI met with Mr. Dale Flowers, Chief Trainers, IHP on February 4, 2003. The following sessions were suggested to be added:
 - ♦ *Financial Management:*
 - Development of hospital business plan.
 - Implementation of hospital business plan.
 - ♦ *Commodity Management:*
 - Estimation of future needs of supplies and pharmaceuticals.
 - Development of medical equipment maintenance system.
- It was agreed that the number of participants in this course will be 15 participants. MOHP will advertise 30 slots (15 original nominees and 15 alternates) to guarantee full participation.
- It was agreed on the following criteria for selecting the nominees:
 1. *Target Groups:*
 - District Health Managers/Assistant District Health Managers.
 - General and District Hospital Managers.
 - Heads of OB/Gyn and Neonatal Care Departments of the General and District Hospitals.
 - Governorate Directors of MCH.
 - HM/HC Project Key Staff, MOHP.

- Hospital Administration Key Staff, Curative Care Department, MOHP.

2. *General Requirements:*

- Expertise background in the topic area of the course and assurance of potential application of the knowledge and skills acquired after return back.
- First priority to nominees from Option Period Governorates: Sohag, Assiut, Menya and Giza.
- Good communication in English and pass satisfactory a personal interview.
- Maximum 55 years old.
- Excellent performance evaluation reports covering the last two years of service.
- Not enrolled in any post graduate education/studies.
- Have not traveled abroad for a short or long term similar event for the last two years.

IV. A Course on Research Methodology

- In response to Dr. Esmat's previous request to organize a course on research methodology within the DT2 Plan 2003, Dr. Nahed Matta indicated that the Summer Institute in Reproductive Health and Development is organizing a course in research in reproductive health from 7 to 18 July, 2003 that could meet MOHP requirements. She promised to explore the possibility of sending participant(s) to this course and other available opportunities and report back. The course will not be funded as part of DT2 Plan 2003.

V. Women Health Card

- Dr. Esmat advised that her team has revised the card. She also presented the card to the National Population Council for review.
- Dr. Khaled Nasr, Deputy Executive Director, HM/HC will call JSI to participate in a meeting during February in the project to review changes/modifications for final approval and printing.
- The issue of the tendency of women to use the Women Health Card for one pregnancy only while it is intended to be used for three pregnancies was raised. Dr. Esmat believes that coordination with TAHSEEN Project could lead to surmount this issue through the use of the card to provide the family planning services between pregnancies.

VI. Global Health Council Conference

- Ms. Marwa Kamel, JSI, will be the focal person for developing and coordinating the presentations of Global Health Council for all the participants on the basis of one to one presentation and small meeting with Panelists. A one day meeting for all the participants will be organized prior to the departure of the participants.
- Related to he above, Dr. Esmat advised that she may be assigned to represent Egypt in the WHO General Assembly that will be held its meeting

on 19-21 May, 2003 in Geneva. This might entail her inability to join Global Health Council from its beginning.

VII. Preemicare Incubators

- The participants were briefed on latest actions taken to suspend the utilization of these incubators temporarily till the manufacturing company take the necessary actions to guarantee safe operation of these incubators.
- Dr. Esmat will set up a committee from MOHP representatives and resources from the university to check the incubators before she officially authorizes the facilities to reuse them.

VIII. White Ribbon Alliance for Safe Motherhood

- HM/HC Executive Director and JSI Deputy Chief of Party participated in the Global Conference of the White Ribbon Alliance (WRA) held in India on October 2002. Feasibility of applying to the WRA Annual Contest was discussed as the winners receive recognition at the Annual Global Health Council Meeting. The following are the conclusion of discussion:
 - As JSI Egypt and the Egyptian Family Health Society have joined WRA as members, HM/HC also could join as a member and be added to the WRA distribution list of publications.
 - It is believed that the time available to meet deadline and conditions for WRA contest participation make it difficult to participate in this year's contest.

IX. Institutionalization and Mainstreaming MCH Curriculum of the Secondary Technical Nursing School

1- Endorsement of Changes/Modifications

- Changes/modifications proposed by the Central Committee for Curriculum Development for Secondary Nursing School have been endorsed.
- A complete set of CDs containing the revised curriculum will be sent by February 16, 2003 to Dr. Azza El Hussein for reproduction.
- The revised curriculum will be used in all the nursing schools (228 schools) starting by the scholastic year 2003/2004.

2- Actions to Support the Institutionalization/Mainstreaming Process

- JSI will design and conduct Three TOT workshops as follows:
 - One workshop for teachers supervisors at the central level, and
 - Trainers trained at central level will conduct, with technical support from JSI, two TOT workshops in Lower and Upper Egypt.
 - The Central Department for Human Resources Development will assume the responsibility of organizing and conducting local training courses using local trainers for school's principals, supervisors and teachers in all the governorates.
 - All the training should take place on June and July 2003 before the start of the scholastic year 2003/2004.

- Regarding the reproduction of Teacher's Guide, Dr. Azza El Hussein will fund the reproduction of 1200 copies required through available budget item line. Dr. Esmat Mansour expressed readiness to support this activity from HM/HC Project fund to supplement any shortage of allocated fund by the Central Department for Human Resources.

3- Models for Training in the Secondary Technical Nursing Schools

- Dr. Azza El Hussein will forward to JSI a list of schools to receive the training models based on needs assessment.

4- Family Planning Curriculum

- The revised component of the Secondary Technical Nursing School focused on the MCH component only, there is a need to conduct a similar revision and updating of the Family Planning component of the curriculum. This is a proposed area of cooperation and coordination between TAHSEEN Project, HM/HC Project and Central Department of Human Resources (MOHP).

X. Strengthening the Nursing Services Capacity in Upper Egypt

- This issue was raised thoroughly in the meeting and serious reasons to it were discussed. It was agreed to conduct a situation analysis at the governorate level to assess the capacity of the nursing services and based on the results, specific plans of action will be developed.

MOHP/ USAID/ JSI Monthly Coordination Meeting

March 11, 2003

Participants:

Dr. Esmat Mansour	Undersecretary Integrated Health Care, HM/HC Executive Director, MOHP
Dr. Nahed Matta	HM/HC RP Team Leader, USAID
Dr. Reginald Gipson	Chief of Party, JSI
Mr. Sobhi Moharram	Deputy Chief of Party, JSI
Dr. Khaled Nasr	Deputy Executive Director, HM/HC, MOHP

I- Review and Follow up the Minutes of the Previous Meeting

(A) Secondary Technical Nursing Schools Curriculum

- In fulfillment of the recommendations of the previous meeting, the participants noted, with appreciation, the actions taken by Dr. Azza EL Hussein, MOHP Undersecretary for Research and Development to effect the use of the revised MCH component of the curriculum in all the said schools (252 schools) starting the school year 2003/2004.
- Monitoring the implementation of agreed upon actions will take place in the forthcoming meetings, to support the mainstreaming of the newly revised curriculum, i.e., TOT Workshops, to ensure quality application of the curriculum.
- TAHSEEN was contacted based on the advice of the HM/HC Executive Director to approach the TAHSEEN Project to conduct the same process to revise and update the FP component of MOHP curricula for Secondary Technical Nursing Schools. TAHSEEN reacted positively to the proposal. Dr. Nahed pointed out the fact that there was an urgent need to follow-up with TAHSEEN since immediate action was required by TAHSEEN to take advantage of this opportunity which was limited by the current time schedule for the printing of the material.
- On the overall coordination between TAHSEEN and HM/HC Projects, JSI is working with TAHSEEN to develop a framework of cooperation and coordination with well-specified mechanisms of collaboration based on the current and previous involvement in POP II, III and IV Projects, as well as the three meetings JSI had with TAHSEEN in February 2003.
- Dr. Matta suggested that JSI send a summary of previous meetings with TAHSEEN which identifies the time limited critical priority areas for coordination such as the revision of the Nursing School Curricula. The suggestion was strongly supported by Ms. Brenda Doe, USAID/Family Planning Team Leader, during discussions held with the JSI Chief of Party when they attended the "Briefing on TAHSEEN's Workplan 2003" on March 16, 2003.
- The JSI Chief of Party sent a letter to the TAHSEEN Country Representative detailing seven areas of cooperation with seven recommendations. A meeting

between the two projects is scheduled to discuss and agree on the coordination and implementation steps.

(B) Women's Health Card

- The Women's Health Card still is being reviewed by the National Women Council. The MOHP will call JSI for a meeting to incorporate changes/modifications as soon as the review process by the National Women Council is completed.
- Based on the advice of Dr. Esmat Mansour, TAHSEEN was approached to review the FP section of the card and to promote the use of the card as a record of contraceptive use which in turn would encourage women to keep the card and use it for more than one pregnancy.

(C) SHIP

- Dr. Nahed Matta agreed that the next milestone report to be submitted on September 15, 2003 will cover activities and accomplishments in the Second Phase three governorates of the Option Period, i.e, Menya, Assiut and Sohag in addition to a Plan of Action to phase into Giza Governorate.
- Dr. Esmat Mansour advised that the HIO Chairman has assigned a new full time HIO staff to support Dr. Omaima, the HIO counterpart, in overseeing the implementation of SHIP in Upper Egypt and to develop a Plan of Action to go national with this program.
- Dr. Esmat Mansour requested JSI support to work with HIO and HM/HC counterparts to develop a Plan of Action to expand the program at the national level, particularly on specifying the financial sources to be allocated in GOE fiscal year 2003/2004.
- Dr. Esmat expressed her wish that JSI would continue its support to phase into Giza as well as assistance for the nation wide expansion of the program. Dr. Matta indicated that this is beyond the contractual obligations of the contractor, however the request would be considered taking into consideration the magnitude of technical assistance required, its cost and availability of funds. Dr. Matta further stated that JSI should assess the amount of savings due to the change in the exchange rate to determine how much additional funds (Egyptian Pounds) were available to increase the amount of local technical assistance. Dr. Gipson stated that the saving might be used for a COLA increase and/or increase in staff salaries if approved by the USAID.

(D) Preemicare Incubators

- JSI Chief of Party advised that the manufacturing company shipped the required spare parts and are scheduled to arrive by March 14 and the company team is expected to arrive on March 25 to start work.
- Dr. Esmat assigned Dr. Nahed Fahmy, Biomedical Engineer Manal from HM/HC in addition to a resource person from Cairo University, Faculty of Engineering to supervise and give back up support to the manufacturing company team. JSI also assigned Dr. Lamiaa Mohsen and Biomedical Engineer Khaled Saber to join the team.

(E) Leadership, TQM and Hospital Administration (Santa Cruz)

- Dr. Nahed Matta distributed the preliminary outline and itinerary of the course received from IHP through IIE/DT2.
- Dr. Esmat Mansour presented the draft final list of criteria for nominations before submission to Dr. Azza El Husseini for announcement. It was agreed on the following:
 - The personal interview would reveal whether the nominee could communicate fairly in English.
 - Secure well-balanced representation of governorates as well as giving preference to nominees from Upper Egypt between eligible nominees.
 - Ensure the wide circulation of the announcement to outreach the target group and secure enough number of nominees. JSI promised to filter down the announcement to all potential nominees in Upper Egypt target governorate.
 - Ranking the list of the alternate nominees according to priority order.
 - Dr. Esmat agreed to a proposal forwarded by Dr. Nahed Matta, to allow representatives from USAID and JSI to attend the selection panel as observers.

(F) Global Health Council Conference

- Participants will leave for Washington DC on May 25, 2003.
- The presentation at USAID will take place from 12:00 – 02:30 PM on May 27, 2003.
- The congressional briefing will take place in the morning (08:30 AM to 10:30 AM) and is pending the clearance from USAID/ Legal office. JSI Boston was requested to use their good offices to facilitate the process.
- Ms. Marwa Kamel, JSI will draft a plan to meet with presenters and call for a one day meeting for rehearsal before departure.
- Questions and answers (Q/A) to respond to audience after each presentation to be developed as background papers for presenters.

II- New Topics Presented and Discussed

(A) Maternal and Neonatal Emergency Services

- JSI Chief of Party handed over a copy of the comprehensive set of material produced related to emergency and neonatal care (service standards, protocols, training curriculum and modules and proposed organizational structure of the Emergency Department at General as well as District Hospitals). JSI Chief of Party emphasized that these materials are produced with close collaboration between JSI, HM/HC, Emergency Department and Curative Care Department.
- The Chief of Party advised that -upon USAID's request- he provided a similar copy to USAID, as there is a mission to visit Egypt, sponsored by the Health Sector Reform Project, to explore ways and means to support emergency care. JSI was asked to facilitate and prepare a field visit for the said mission to Menya General Hospital and Samalout District Hospital on March 12 and 13, 2003.
- HM/HC Project is requested to review the materials produced technically as first steps, then set up a meeting to review them with the Emergency Central

Department, MOHP so that JSI would publish them within HM/HC publications.

(B) Neonatal Tetanus/ Tetanus Toxioid

- JSI Chief of Party expressed his concerns as information available by HIS system, coverage and reported neonatal tetanus cases, indicates clearly that there is room to do more in this area, which affects maternal and neonatal mortality. Dr. Gipson raised the question about the role of HM/HC/ JSI in addressing this issue, if any.
- Dr. Esmat Mansour and Dr. Nahed Matta confirmed that this is a worthy endeavor of vital importance and an area that needs mobilization of all resources in a collective effort to increase coverage and number of women that are fully immunized. As UNICEF is one of the key players in these areas, it was agreed to set up a separate meeting that involves all the partners and develop a plan of action with clear responsibilities and timetable.
- In this respect Dr. Nahed Matta would like to explore the possibility of using the surplus funds under IL No. 4 resulting from the change in the dollar/LE exchange rate, to consider activities in this area. She mentioned that USAID was able, through this way, to add L.E. 3.1 million more to the forthcoming March polio campaign, however all surplus funds were used in the recent IL amendment approved in February 2003.

(C) Exchange Rate and its impact on IL Fund

- Related to the exchange rate, Dr Mansour questioned whether it is possible to affect an increase of the salaries of the contracted staff of HM/HC Project due to the devaluation of the Egyptian Pound. Dr. Nahed pointed out that such decision should take in consideration, GOE plans and actions related to the salaries of MOHP employees lest, the gap should be widened between the Project contracted staff and GOE/ MOHP staff. USAID policy and decision in that respect will not be taken on individual cases/ Projects, but will be based on thorough situation analysis to be applied for all projects.

(D) Maternal Mortality Surveillance System

- JSI Chief of Party presented the results of monitoring the performance of the MMSS in the governorates of Beni Suef, Menya, Assiut, Sohag and which revealed specific areas of weakness, and the corrective actions that were taken.
- As this monitoring tool was pilot tested by a team of JSI/ HM/HC, JSI/ FETP physicians and proved to be useful, it is time to institutionalize this tool and build the capacity of Assistant District Manager and the MCH Director at the governorate level to conduct this monitoring, act on findings and report to higher authorities.
- The following are main findings revealed by reports:
 - The old maternal death questionnaire is still in use.
 - The questionnaires and analysis of avoidable factors are not submitted to the Safe Motherhood Committee for corrective actions, as it is claimed that it is requested to be sent directly to the central level.
- Dr. Esmat Mansour, in response to the above, reiterated that the MMSS is catching up and needs to be strengthened. Governorates' SMC should play an active and decisive role in identifying the causes of death, avoidable or not, as well as the corrective actions to be taken within a plan for improvement.

- To enforce this, Dr. Esmat decided to issue a directive to hold allocated incentives for cases if they not using the final revised questionnaire, which contains the identified cause of death and the corrective action plan, signed off by the Chairman of the SMC at the governorate level.
- The Undersecretary, HM/HC Executive Director, directed to call for a one day meeting to be attended by all the governorates Directors of MCH to discuss the issues and orient them on the new procedures and directives for immediate actions.

(E) Use of HM/HC Cars Survey

- JSI Chief of Party informed the meeting on the arrival of 44 cars for the project and Dr. Mansour distributed a list of allocation of these cars as approved by H.E. Minister of Health and Population. Dr. Nahed Matta requested to see the distribution list which has to match the original plan and request submitted to USAID for the vehicle approval memo.
- Dr. Matta requested a survey to be conducted to ensure that the cars provided previously by the USAID to HM/HC are used for the purposes they are assigned to, in accordance with the bilateral agreement and the relevant Ministerial Decrees. Dr. Mansour responded positively to this request and promised to take action to conduct this survey and submit the results.

(F) Interim DHS Analysis

- Dr. Nahed Matta handed over to Dr. Esmat Mansour a hard copy of the Interim DHS Analysis Report for her review and comments. She e-mailed it to JSI for the same purpose.

(G) Giza Memo of Cooperation

- JSI Chief of Party briefed the participants on the meeting he and his deputy had with the newly appointed Undersecretary of Health and Population, Giza Governorate on March 6, 2003 to orient him on the HM/HC and share with him the draft MOC for his review, final approval and set up a signing ceremonial meeting with the governor.
- As related to JSI Field Office in Giza Governorate, Dr. Esmat Mansour suggested that El Moneib Medical Center has an office space that would be appropriate premises for JSI Field Office.
