



**Palestinian Environmental
Improvement / Vocational Training Program (PEIP/VTP)**

Award No. 294-A-00-02-00218-00

**Seventh Quarterly Report
January – March 2004**



April, 2004
Country Representative Office
CHF International / West Bank and Gaza

1	EXECUTIVE SUMMARY	3
1.1	OVERVIEW	3
1.2	EXPECTED RESULTS	4
1.3	PRELIMINARY PROGRAM END ACHIEVEMENTS	6
1.3.1	Employment Generation	6
1.3.2	Environmental Improvements	7
1.3.3	Public Awareness and Neighborhood Environmental Stewardship.....	7
1.3.4	Municipal Capacity Building.....	7
1.3.5	Municipal Matching Contribution	8
1.3.6	Vocational Training.....	8
2	STAFFING	8
3	CURRENT ACTIVITIES	9
3.1	CURRENT STATUS	9
3.1.1	Employment Generated.....	10
3.1.2	Waste Collected	12
3.1.3	Survey of Waste Accumulation.....	16
3.1.4	Public Awareness Program	19
3.1.5	Vocational Training.....	20
3.1.6	Municipal Partnership.....	22
3.1.7	Coordination with Community Organizations.....	24
3.1.8	Beneficiaries and Impact Indicators.....	24
3.2	USAID PERFORMANCE MONITORING PLAN.....	25
3.3	SUMMARY OF OUTPUT INDICATORS	26
3.4	AUDITED PROGRESS TO DATE	26
4	FINANCIAL MANAGEMENT/REPORTING	27
5	OTHER ISSUES	27
6	ANNEXES	28
6.1	DETAILED WASTE COLLECTION REPORTS (GAZA NORTH) FOR CURRENT QUARTER	28

The photograph on the front cover shows USAID's CTO – Mr. Fadi Khoury visiting the PEIP/VTP program in Ramallah and Al Bireh, accompanied by CHF's Country Director – Ms. Lana Abu Hijleh, CHF's Program Director - Ms. Liesbeth Zonneveld, CHF's Local Consultant Mr. Mohammed ElHamidi, CHF's Deputy Program Director for the West Bank, .Mr. Musa Awad.

1 Executive Summary

1.1 Overview

This document constitutes the seventh quarterly report submitted by CHF to USAID for the Palestinian Environmental Improvement Program/Vocational Training Program (PEIP/VTP) in Gaza North and the cities of Ramallah/AI Bireh and Nablus. This report details the achievements and impacts made over the period from January through March 2004.

On May 10, 2004, the PEIP/VTP field program activities will have ceased and all close-out procedures, final financial and program reports will have come to completion on July 18, 2004, as specified in the cooperative agreement.



Building job security one stone at a time, through the building of retaining walls in Ramallah, West Bank.

On July 19, 2002, USAID awarded a grant¹ to CHF to implement its PEIP/VTP program in support of USAID's JOBS program. Total funding for the program is estimated at \$6,891,339 of which USAID will provide \$5,366,991. CHF and its municipal partners will make contributions to the program of approximately \$1,524,348. The program will be managed and implemented by CHF in partnership with the municipalities.

The principal goal of the CHF PEIP/VTP is to create both immediate short-term employment and long-term sustainable employment in Northern Gaza Strip towns of Jabaliya, Beit Lahia, and Beit Hanoun, and in the West Bank towns of Ramallah, Al Bireh, and Nablus. The program consists of intensive cleaning of open sites in these municipalities where dirt, litter and debris have accumulated. Therefore, not only does the PEIP/VTP create employment but also contributes to improvements in the quality of

¹ Award No. 294-A-00-02-00218-00.

life for up to 320,000 Palestinians in the target municipalities. Trained public awareness teams work directly with the public, both individuals and businesses, to ensure that once an area has been cleaned, the public will work to maintain the cleanliness in the open spaces. Finally, in addition to employment generated and quality-of-life improvements, at least 361 persons will be vocationally trained over the life of the program. Those trained will be better able to enter the permanent job market at the end of the program.

The program is being implemented in partnership with the Northern Gaza Strip and the West Bank municipalities. Waste is collected by CHF program personnel at strategic points throughout the city. CHF then coordinates with the municipalities to transport the collected solid waste to the environmentally safe landfill. This unique partnership allows for a significant local contribution to the program.



1.2 Expected Results

At the end of the project, CHF will have:

- created 370 new jobs with 2,590 direct beneficiaries;
- created 7,400 person months of direct employment (225,078 person days);
- generated 829 person months of “spin-off” employment (25,209 person days);
- reduced poverty and social exclusion for the 2,590 family members of the persons employed under the program;
- improved the quality-of-life for approximately 320,000 Palestinians;
- supported municipal waste collection efforts in both the short and long term;
- cleaned up vacant lots and public lands with accumulated wastes, including the Jabalia and Beit Lahia municipal beach;

- carried out public awareness activities targeted at Northern Gaza Strip and West Bank municipalities' neighborhood citizens and establishments;
- developed partnerships with municipal leaders, citizens groups, local women's organizations, and local private organizations and NGOs;
- carried out a rapid assessment of training needs;
- implemented vocational training of at least 361 persons, who will be better able to enter the permanent job market at program end; and
- Conducted an end-term assessment of training effectiveness and potential employability.

The following table shows the achieved outputs for year 1, the planned outputs for year 2, and the proposed outputs for the entire program duration:

Output	Achieved for Year 1	Planned for Year 2	Proposed for Program Duration
Direct employment generation	106,702 person days of employment (3,508 person months)	118,376 person days of employment (3,892 person months)	225,078 person days of employment (7,400 person months)
Income generated by employment hires	\$1,270,396.31	\$1,693,133	\$2,963,529
Direct Beneficiaries per month	319 persons x 7 average family size = 2,233 persons	370 persons x 7 average family size = 2,590 persons	370 persons x 7 average family size = 2,590 persons
Tons solid waste collected	81,477 tons	51,434 tons	132,911 tons
M ² cleaned	4,056,320 m ²	4,000,000 m ²	7,721,519 m ²
Training hours	61,001 hours	35,299 hours	96,300 hours

The following table shows the achieved outputs as of March 31, 2004:

Output	Achieved as of March 31, 2004 (93.03%)	Proposed for Program Duration (100%)
Direct employment generation	225,896 person days of employment (7,427 person months) (100.37%)	225,078 person days of employment (7,400 person months)
Income generated by employment hires	\$2,758,021 (93.07%)	\$2,963,529
Direct beneficiaries per month	371 persons X 7 average family size = 2,597 persons	370 persons x 7 average family size = 2,590 persons
Tons solid waste transferred	160,326 tons (120.6%)	132,911 tons
m ² cleaned	8,054,000 m ² (216.4%)	7,721,519 m ²
Training hours provided	105,419 hours (109.5%)	96,300 hours
Matching Contributions	\$ 1,694,280 (111.2%)	\$1,524,348

1.3 Preliminary Program End Achievements

Over the 20-month program period, PEIP/VTP made a number of impressive achievements.

1.3.1 Employment Generation

- The PEIP/VTP program created to date 225,896 person days of direct employment: 818 more days of employment than – or 100.37% of – its agreed upon target (225,078) to be achieved at program end.
- The PEIP/VTP program generated exactly \$2,758,021 in income for Palestinian laborers.
- On average, the PEIP/VTP program generated 371 person months of employment per calendar month, meaning that on average 371 laborers were employed each month for the 20-month period.

1.3.2 Environmental Improvements

- Over the 20-month program period, PEIP/VTP removed exactly 160,326 tons of solid waste from open areas, clearing approximately 8 square kilometers of land, or 8,054,000 square meters.
- In Gaza North, over the 20-month program period, the re-dirtying rate of vacant lots cleaned by PEIP/VTP was a mere 3.4%. The 1,601 tons of newly accumulated waste found in the re-dirtying survey, approximately equal to 44% of one month's production of household waste for the Gaza North population of more than 180,000 citizens, was re-collected.

1.3.3 Public Awareness and Neighborhood Environmental Stewardship

- In Gaza North, PEIP/VTP's community outreach team has organized over the 20-month program period 10,197 sessions for approximately 34,862 citizens on solid waste management issues, environmental improvements, and the roles and responsibilities of the public in maintaining clean vacant lots and open areas.
- In Gaza North, over the 20-month program period, 42 neighborhood-level cleaning campaigns were organized in which more than 1,270 men, women, and children participated.

1.3.4 Municipal Capacity Building

- Together with municipal leaders and formal and informal citizen groups, PEIP/VTP developed clear procedures on how to develop a cleaning plan, including: ongoing surveying, data collection, technical and environmental reviews; feedback gained from specially formed neighborhood committees on environmental cleanup implementation; the establishment of collaborative efforts between citizens and local governing bodies; the development of sustainable Site Maintenance Plans and Waste Removal Action Plans per neighborhood.
- PEIP/VTP's public awareness and surveying teams worked closely with the participating municipalities to develop and implement a re-dirtying survey and a follow-up cleaning plan in anticipation of the PEIP/VTP program end. The re-dirtying survey and follow-up plan will be published separately by CHF. Municipality.



CHF public awareness staff during an environmental campaign was painting in participation with the Zayed Bent Harehta Elementary School in Beit Lahia, in which 270 students participated.

1.3.5 Municipal Matching Contribution

- The PEIP/VTP cooperative agreement specified that the partner municipalities would contribute a match of \$1,524,348 to the USAID award of \$5,366,991. Despite the ongoing conflict, the mayors of partner municipalities have informed CHF that the total contribution to the PEIP/VTP program equaled \$1,694,280, this amounts to 111.2 % of the agreed upon match.

1.3.6 Vocational Training

- PEIP/VTP provided 105,419 hours of vocational training to laborers hired under the program, 9,119 more than its target of 96,300 training hours.
- The PEIP/VTP program provided vocational training courses that responded to the particular skill sets, skill needs and future job choices of each employment generation hire.
- To date, 693 CHF employment generation hires participated in 117 different training courses.

2 Staffing

The following thirteen persons make up the management team:

Name	Title
L. Zonneveld	Program Director
T. Zourob	Deputy Program Director – Gaza
M. Awad	Deputy Program Director – West Bank
A. Skaik	Financial Controller Gaza and West Bank
H. Saba	Assistant Administrator – Gaza and West Bank
H. Ghayada	MIS Manager and Executive Assistant – Gaza
Z. Lababidi	Training Coordinator – Gaza
A. Bayya	Financial Administrator – West Bank
N. Zakout	Senior Community Services Specialist – Gaza
S. Yahia	Community Services Specialist – West Bank
S. Shaaban	Training Specialist – West Bank
E. Allan	Office Manager – West Bank
M. ElHmaidi	Consultant

3 Current Activities

3.1 Current Status

The first 20 months of the 24-month PEIP/VTP program award period ended on March 24, 2004. All program components are on schedule or ahead of schedule.

During this 3 months period, Ramallah, Al Bireh, and Nablus cities experienced repeated incursions by the Israeli Defense Forces, causing restrictions in movement and work at all three sites. During the month of January, the IDF imposed complete closure/curfew for nine days in Nablus so none of CHF's laborers could reach their work sites, and imposed partial closure for six days.

In the month of February, the IDF imposed partial closure for three days in Ramallah and Nablus causing work interruptions. Subsequently during the month of March, the IDF imposed partial closures/curfew for five days in Ramallah. In Ramallah and Nablus, the Palestinian Authority announced a full three day mourning period following the assassination of Sheikh Ahmad Yassin and CHF's offices were closed as advised by the USAID mission.



CHF laborers, during a cleaning campaign in Jabaliya town.

CHF's Security and Emergency Plans were updated for all three areas in view of a deteriorating security and political situation in Gaza and the West Bank.

On March 4, USAID CTO Fadi Khoury visited the PEIP/VTP program in Ramallah and Al Bireh, accompanied by CHF's Country Director, Lana Abu-Hijleh, PEIP/VTP Program Director, Liesbeth Zonneveld, PEIP/VTP Program Director and CHF Consultant Sawsan Huleilah. CHF gave a brief presentation about the goals, activities, and achievements to date, after which program sites were visited including stonewall building and cleaning in Ramallah, a solid waste re-use training activity, and CHF's PEIP/VTP public outreach team cleaning campaign in participation with Khalil Rahman School at Al Irsal zone.

From 14th to the 17th March 2004, CHF-International Chairman of the Board, Mr. Don McCreary and Senior Program Officer, Ms. Delila Khaled visited the Palestinian Territories to review the CHF-West Bank/Gaza Program. During the visit Mr. McCreary visited CHF offices in Jerusalem, Gaza and the West bank and met with all the staff and conducted site visits to several programs around the country. Further, he met with partner organizations including Gaza and Nablus municipalities and informally with USAID mission director and deputy director of the project development office. The Chairman was highly impressed with CHF's programs in the Territories and with the level of achievements despite the prevailing political and security situation.

Following the assassination of Sheikh Ahmad Yassin on Monday 22 March 2004, all CHF offices in Dahiet Al-Barid, West Bank and Gaza were closed for a four day period in

compliance with the security advice of the USAID mission. The Country Director along with the VSP and PEIP/VTP Directors continued to work and monitor the program implementation out of the Country Director's residence in Jerusalem.

3.1.1 Employment Generated


The PEIP/VTP program created, as of the end of March 2004, 225,896 person days (or 7,427 person months) of employment, generating exactly \$2,758,020 in income for Palestinian laborers. On average, 371 person months of employment have been generated per calendar month.

The following graphs represent the number of person days of employment created and the amount of employment income generated during the current reporting period and to date.




A section of PEIP/VTP program labor force ensuring cleanliness at neighborhood level.


Person Days of Employment Generated in Year 2

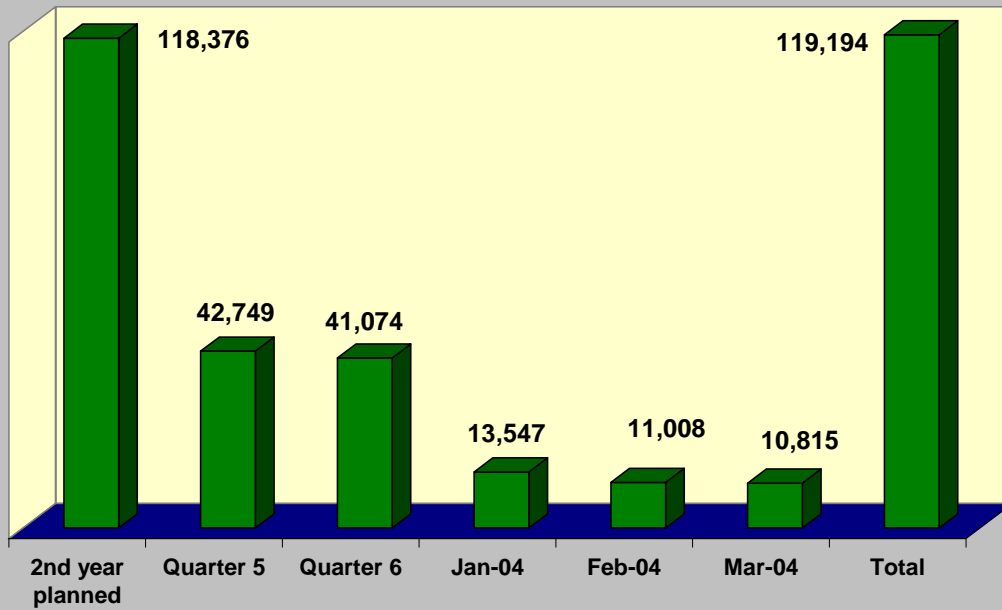


Person Days of Employment Generated to Date

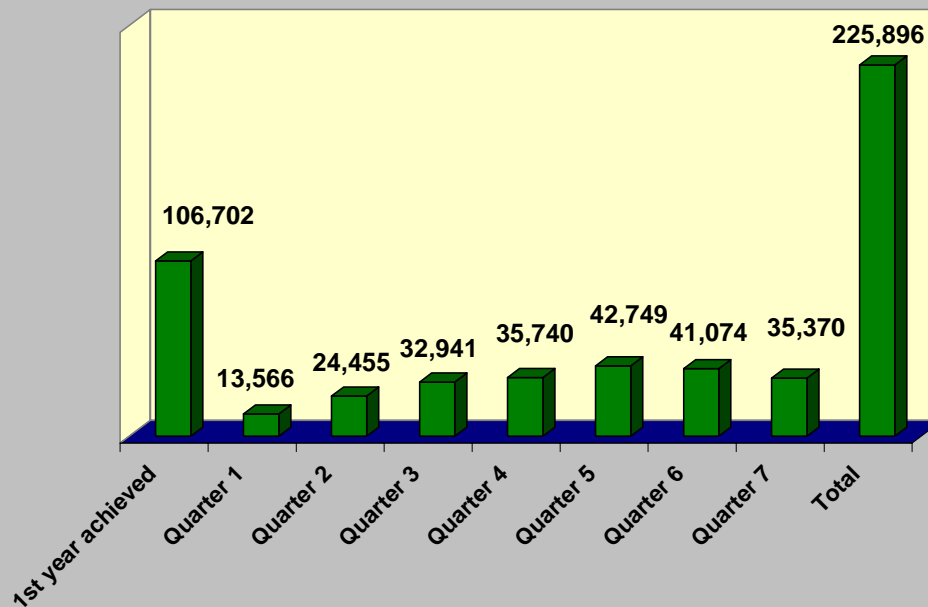

Employment Income Generated in Year 2

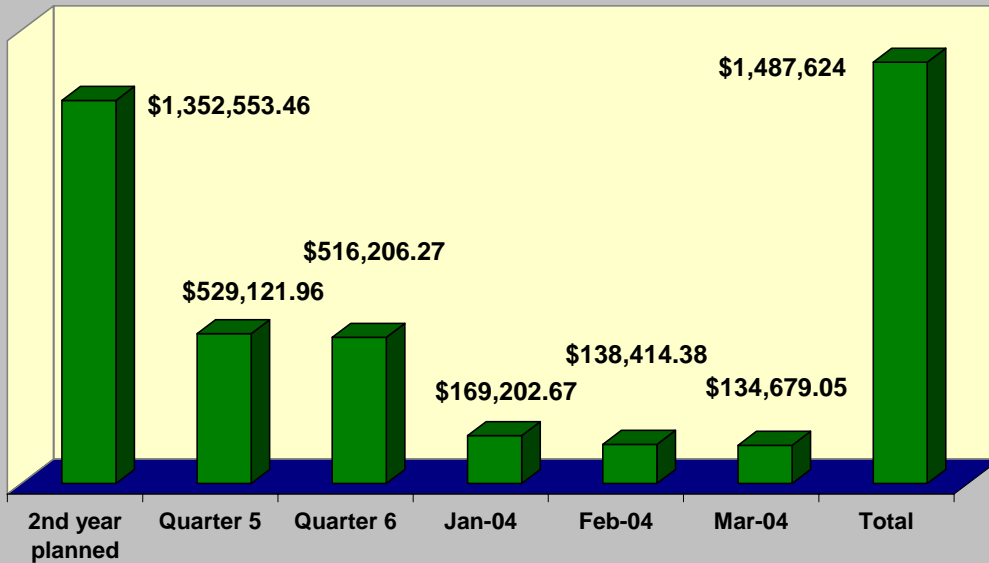



Employment Income Generated to Date

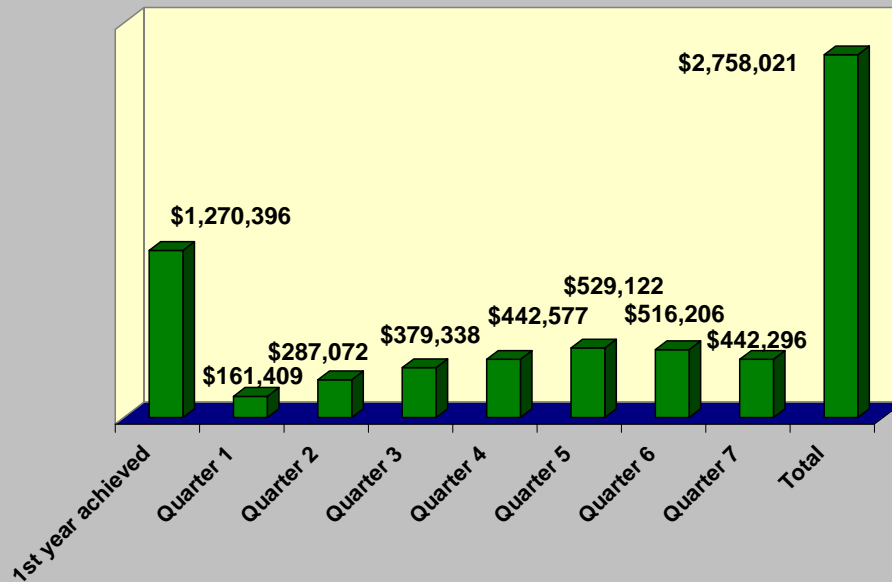


3.1.2 Waste Collected

Over the 20-month program period, PEIP/VTP removed exactly 120,475 cubic meters or (160,326 tons) of solid waste from open areas, clearing approximately 8 square kilometers of land, leaving 6,552 vacant lots clean and safe areas for children to play in. The results of these efforts are summarized in the charts below. Because much of the


solid waste removed had accumulated over the course of many years and even decades, the environmental impact of such a widespread clean-up will be felt for years to come.

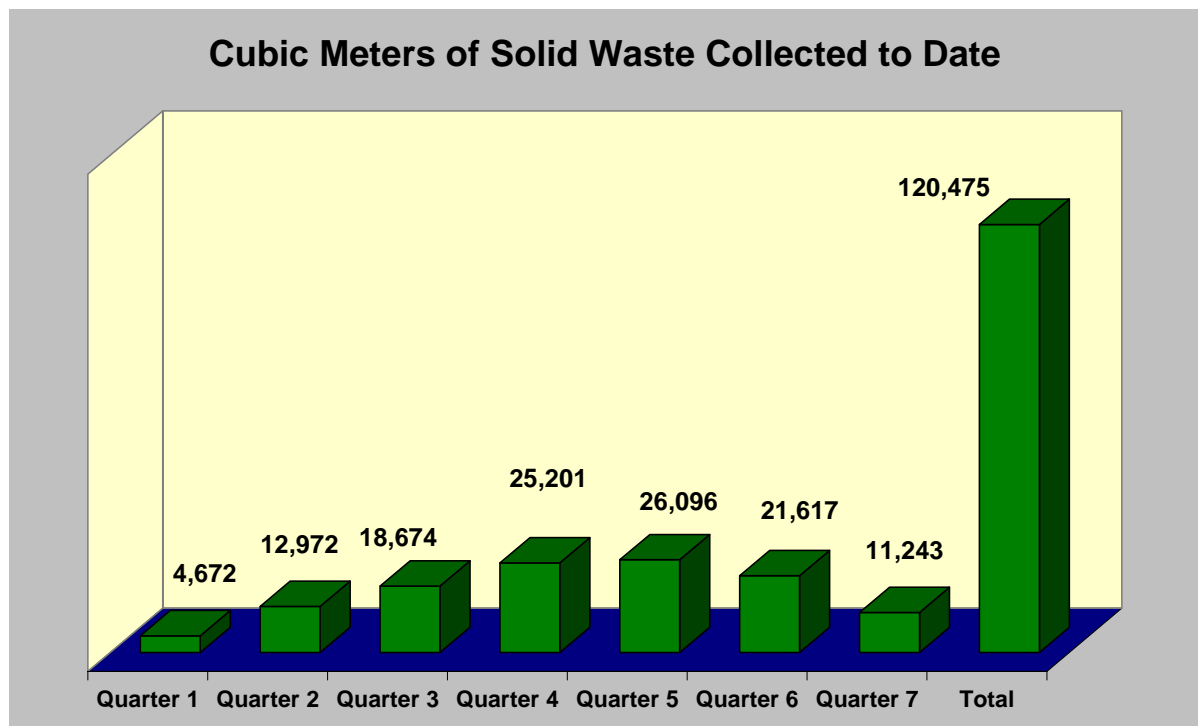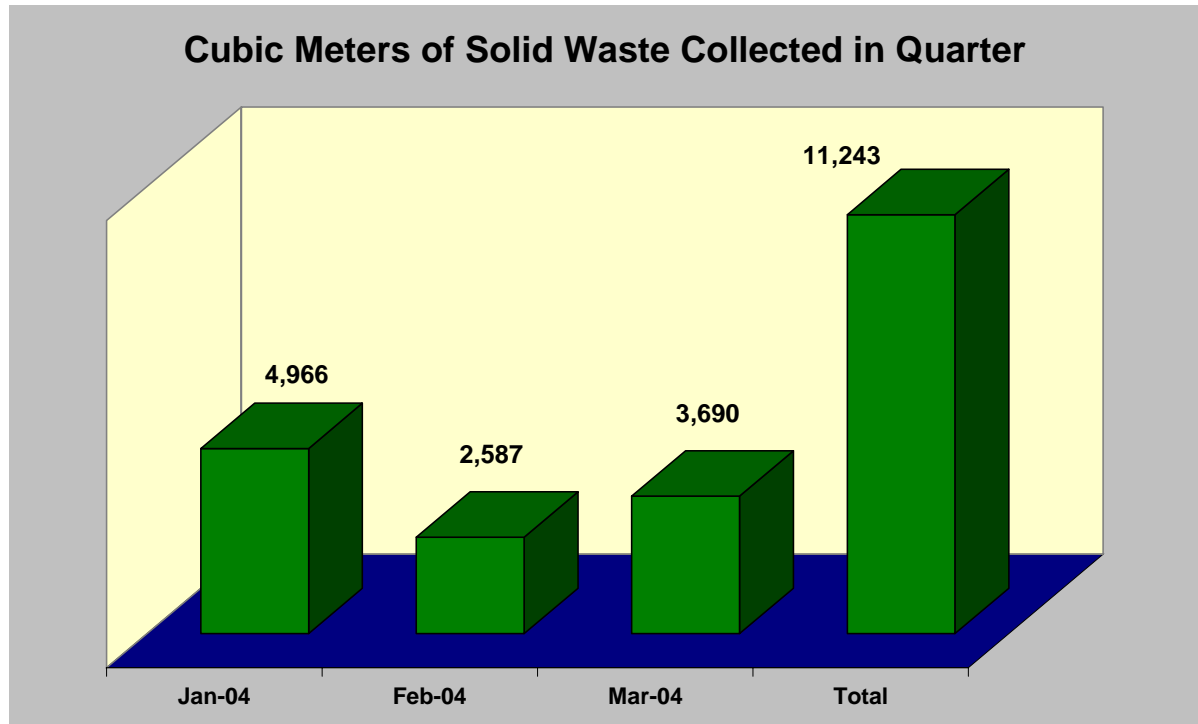


Tons of Solid Waste Collected in Year 2

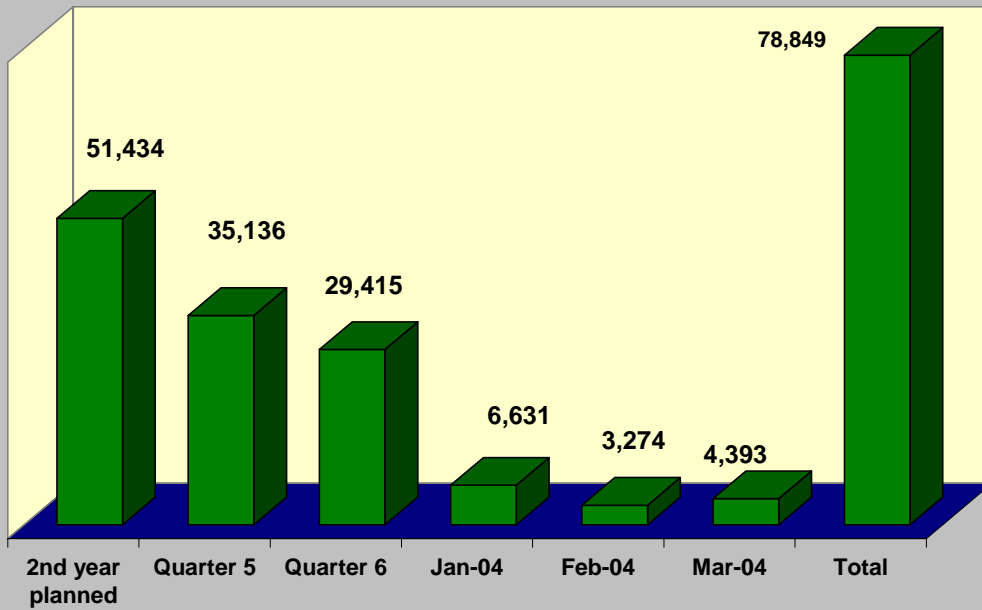


Tons of Solid Waste Collected to Date

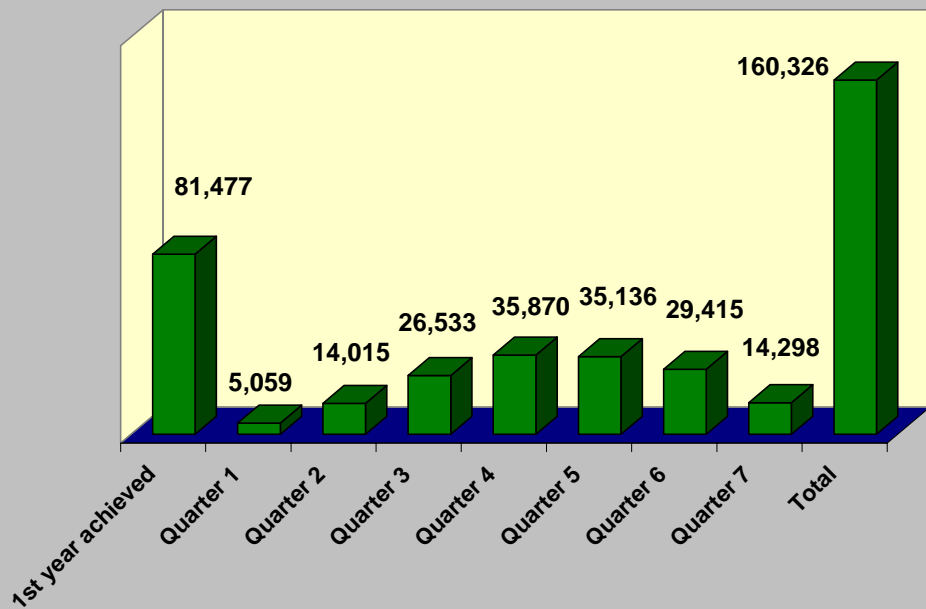


Number of Vacant Lots Cleaned in Quarter

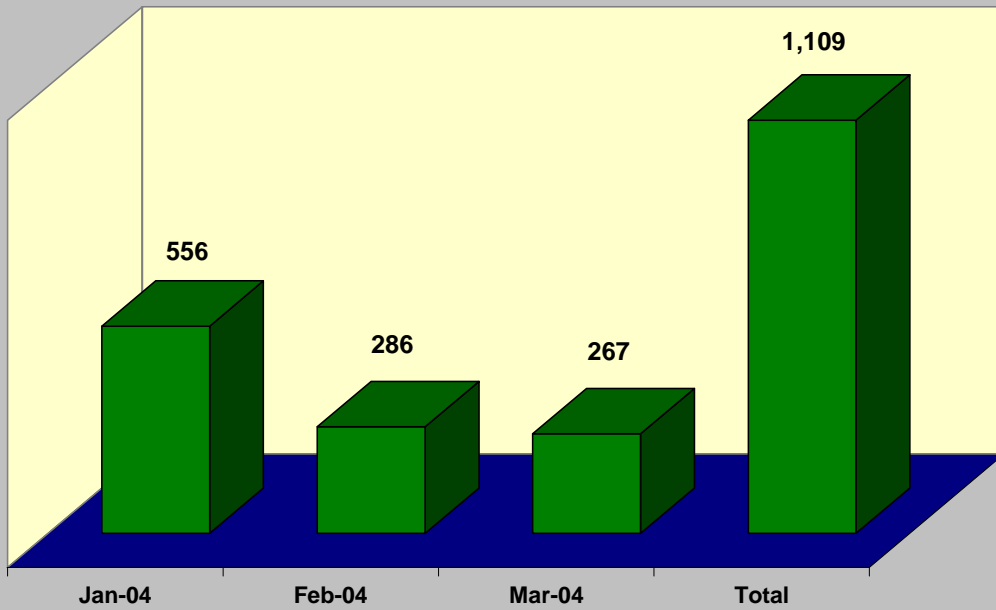


Number of Vacant Lots Cleaned to Date

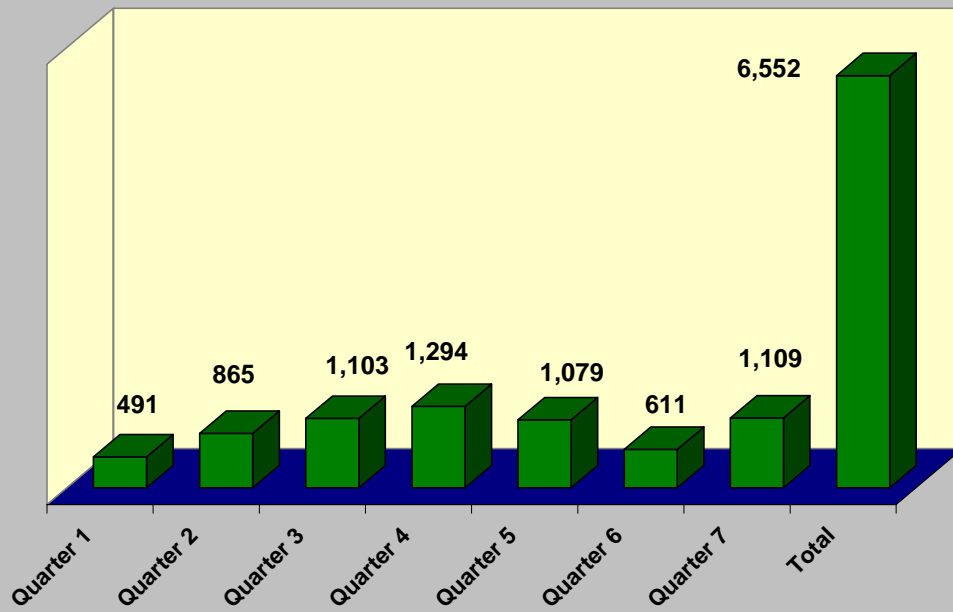

Square Meters of Vacant Lots Cleaned in Year 2

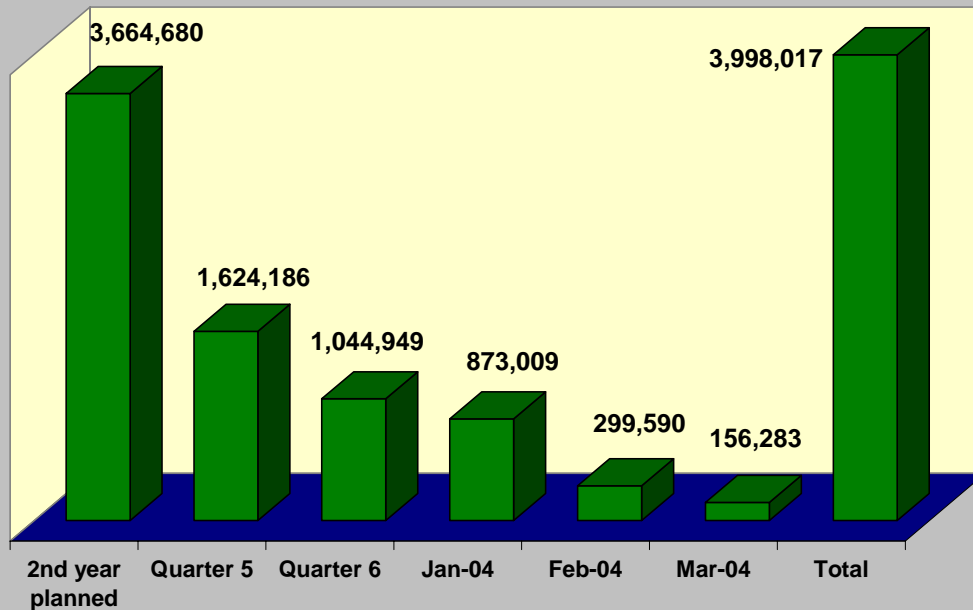



Square Meters of Vacant Lots Cleaned to Date

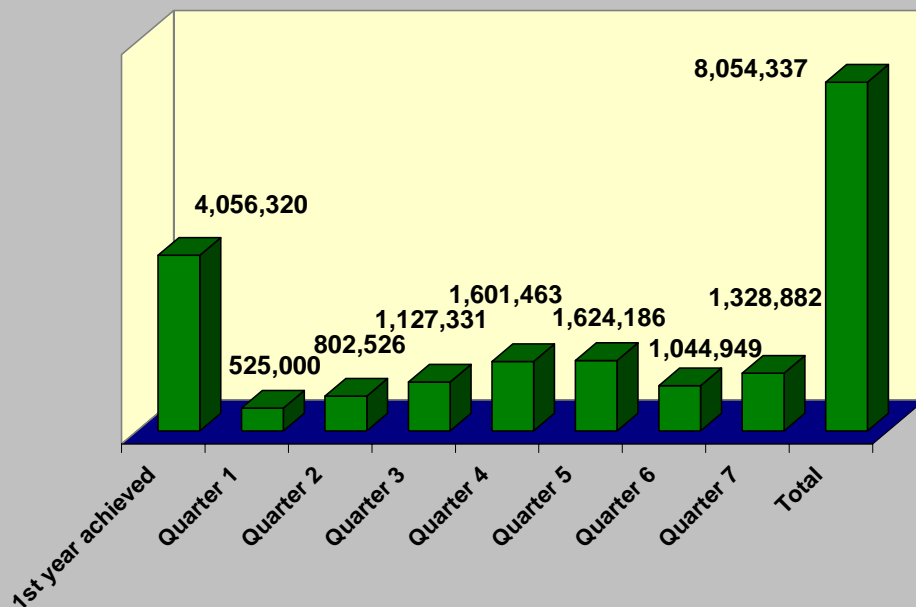


3.1.3 Survey of Waste Accumulation

PEIP/VTP's public awareness and surveying teams worked closely with the participating municipalities to develop and implement a re-dirtying rate assessment survey and a follow-up cleaning plan in anticipation of the PEIP/VTP program end.


The re-dirtying rate assessment survey and follow-up plan will be published separately by CHF. **Municipality.** The results of the survey team's efforts are summarized in the charts below.

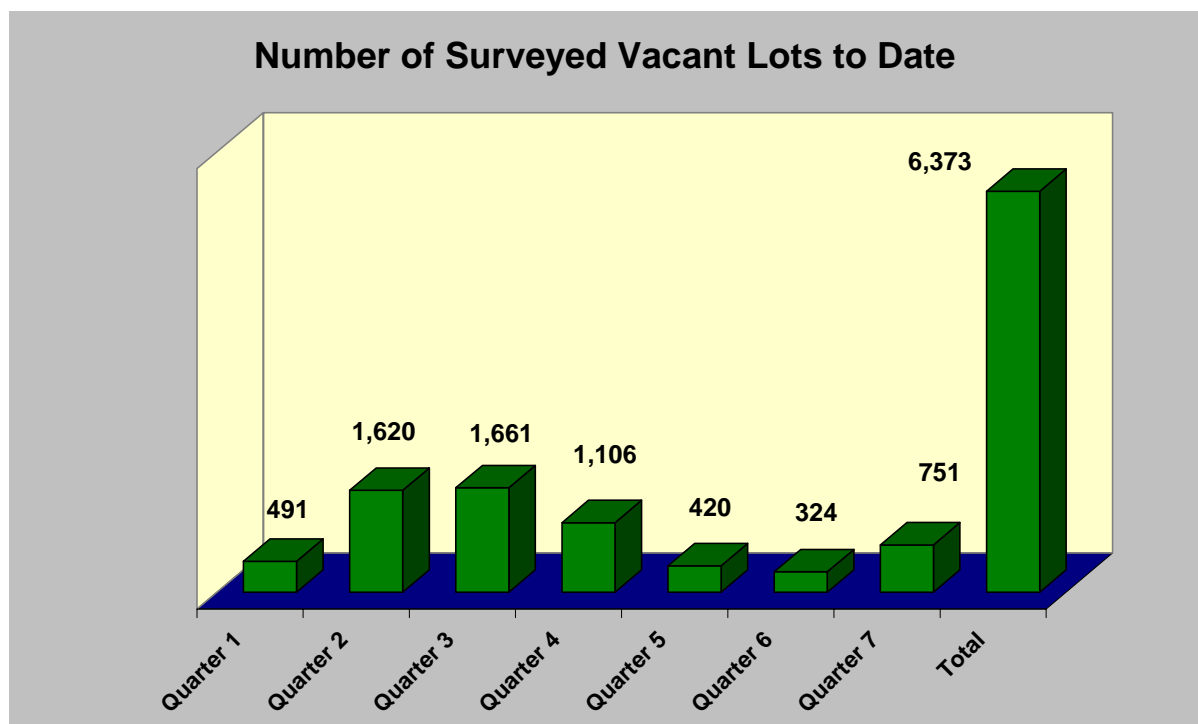
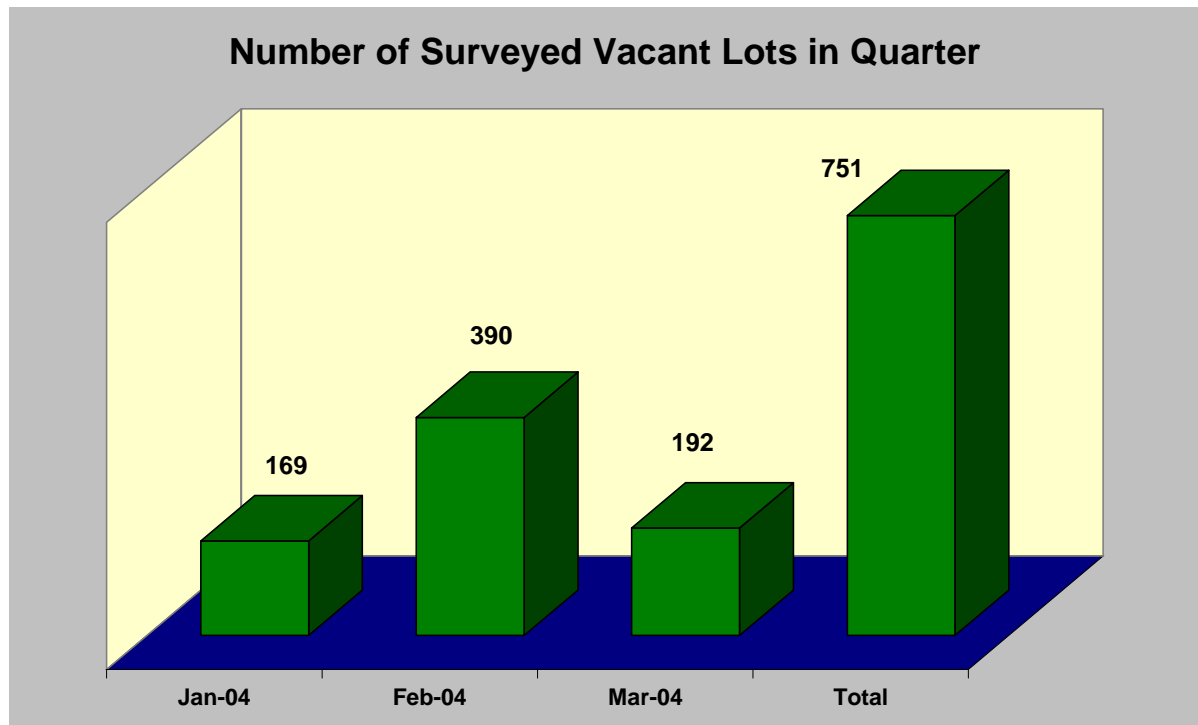


Surveyed Volume (m³) of Solid Waste in Quarter

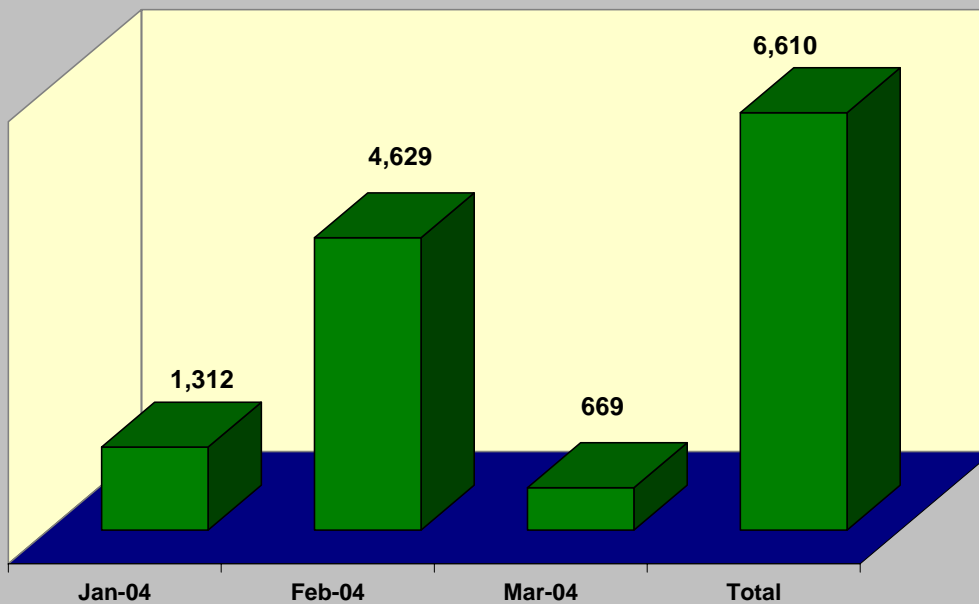

Surveyed Volume (m³) of Solid Waste to Date

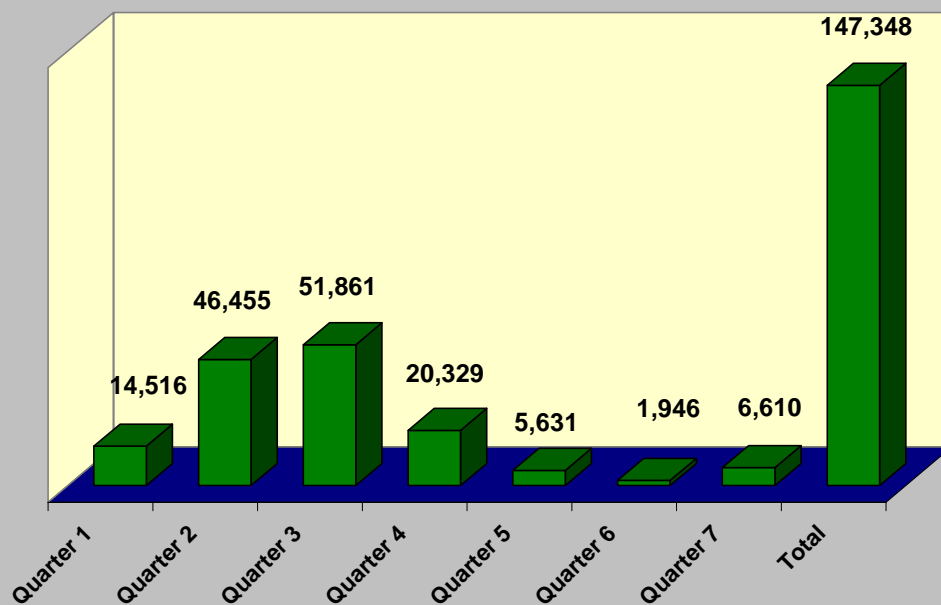

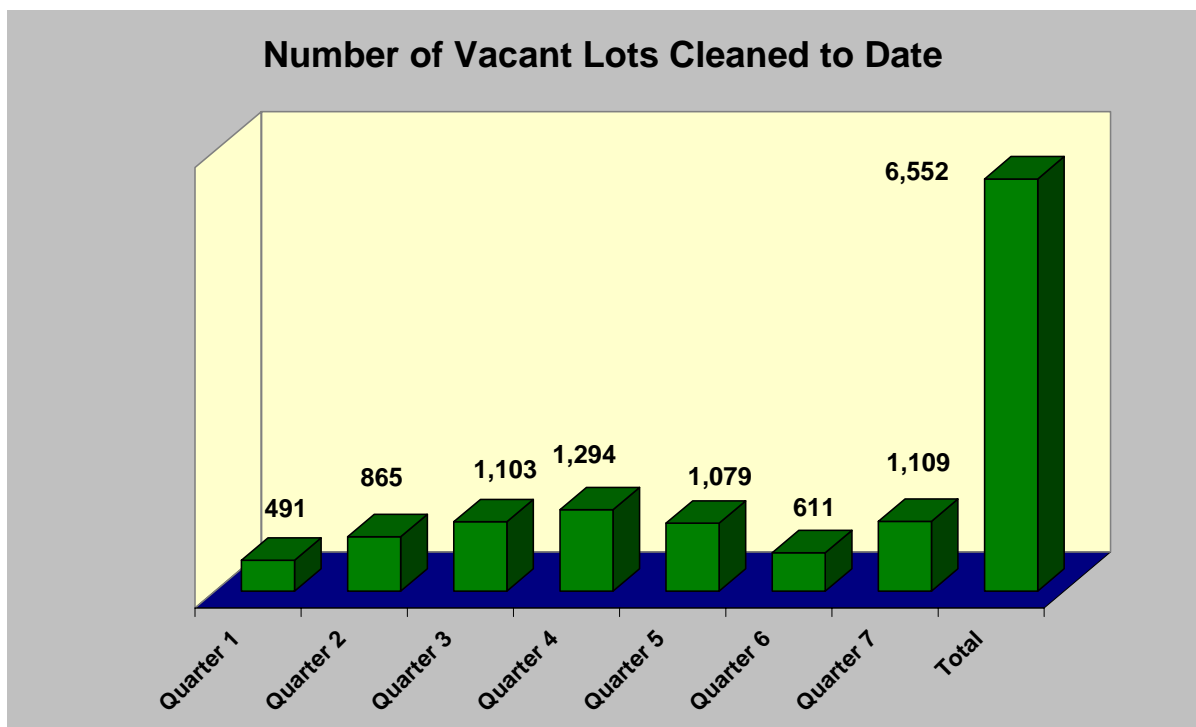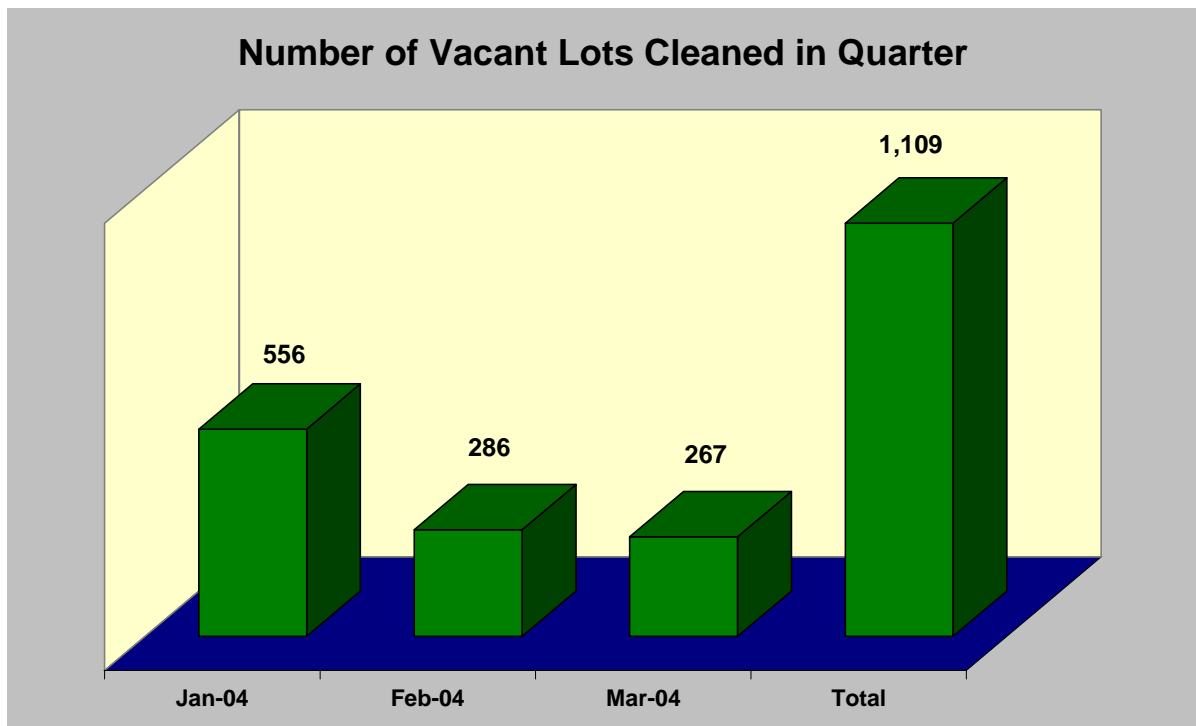

3.1.4 Public Awareness Program

CHF's community outreach team is made up of 19 women and 4 men in the West Bank, and 7 women in Gaza North. The team has made 3,633 visits in Nablus, Ramallah/Al Bireh, Jabaliya, Beit Lahia and Beit Hanoun to mosques, homes, commercial centers, NGOs, and schools. Over the last quarter alone, 15,303 Palestinians in the West Bank

and 4,154 Palestinians in North Gaza have benefited from these activities. Details of the team's visits are summarized below:

- 2,860 home visits in the six cities, primarily in areas cleaned;
- 308 visits to schools including coordination visits, planning of activities as well as participation in lectures to specified target groups and classes;
- 154 general women's meetings held;
- 188 visits to shops and commercial centers; and,
- 277 visits to other institutions.



Building Community Participation through tree planting campaigns on National Tree Day on January 14, 2004 – Nablus.

As of March 2003, more than 143,670 persons have benefited from the PEIP/ VTP community outreach team's community participation development efforts.

3.1.5 Vocational Training

The PEIP/VTP vocational training program is designed to meet the specific job training needs of the individual employment generation hires, providing vocational training during approximately 8.3% of the work week in preparation for alternative employment at project end. This has been accomplished through:


- individualized training needs surveys which assess the desired future job and skill set of each employee, and
- the location of appropriate training courses in the community.

The development and planning of vocational training within the PEIP/VTP program undergoes a rigorous training needs survey and inventory process, submitted to and approved by USAID. Emphasis is placed on the succinct identification of the particular skill set of each employee and its gaps. Thus, training varies according to the skill set of the individual worker, with some needing basic literacy skills while others benefit from computer training or interviewing techniques.

Within the PEIP/VTP program, most of the employment generation hires have expressed their desire to acquire skills needed in their own communities, thereby integrating their knowledge of the job market and future job selection. It should be noted that laborers and staff come from close to forty different communities in the four main program areas.


PEIP/VTP employment generation hires have also been provided with training on Palestinian Labor Laws, by providing the skills necessary to conduct an appraisal of work conditions, contracts and their legal rights and responsibilities.

A summary of the training results are provided below.

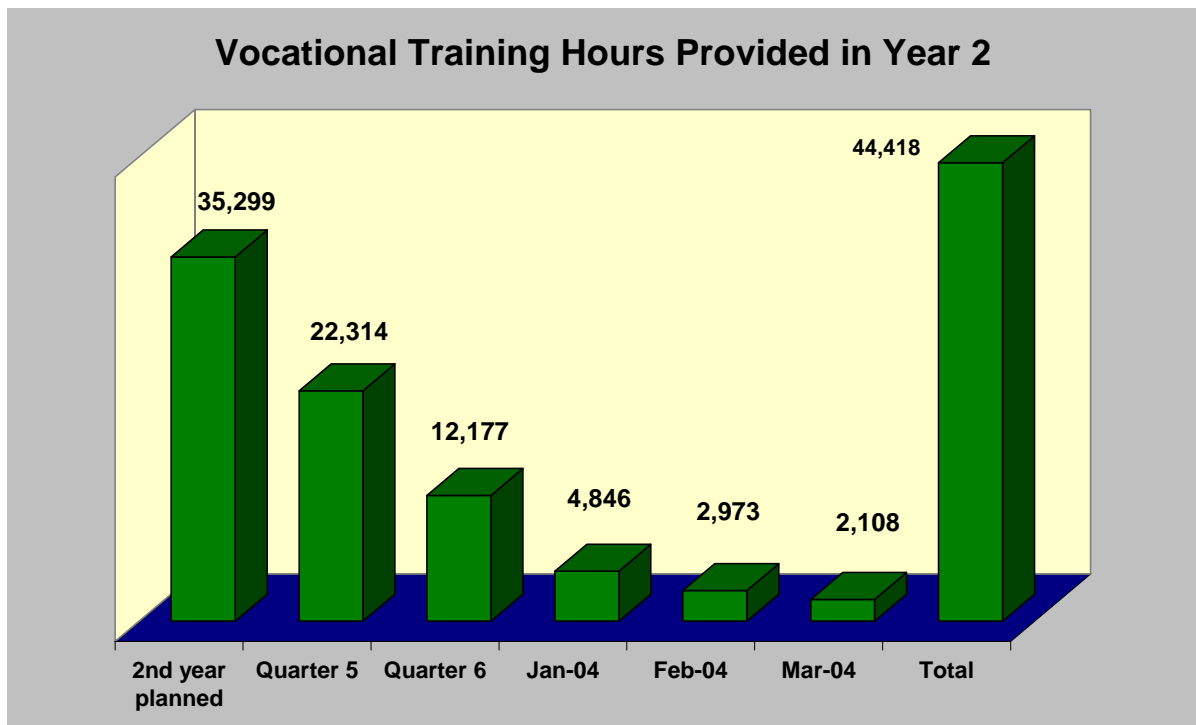

During Mr. Don McCreary visit to the Zayed Ben Haretha Elementary School in Beit Lahia town, in which the 13 CHF laborers gave a free haircut to 127 students.

Vocational Training Hours Provided to Date

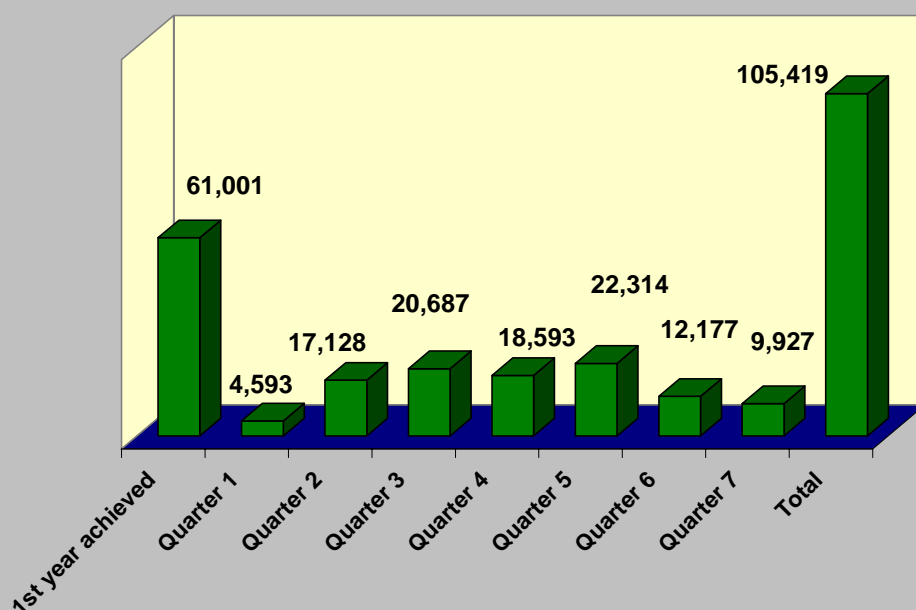

During the quarter under review, the following vocational training courses were provided: ACCESS computer course; aluminum-working blacksmithing; first aid; democracy; environmental awareness concepts; communication skills; pricing and awarding of construction bids; college lectures; gardening; MS project; laborers health; mobile phone maintenance; and computer basics.



Building community participation and environmental awareness through clean-up campaigns. CHF laborers and staff in participation with the students of Al Fajer Al Jadeed School in Al Bireh City.

3.1.6 Municipal Partnership

Cleaning activities continued as planned in cooperation with the six municipalities.

In the Gaza North, CHF staff, in participation with the Beit Hanoun Municipality and the Agricultural Development Association, implemented a planting, fencing and beautification campaign along the center isles of two newly rehabilitated roads funded under USAID's Emergency Roads Rehabilitation Project in Beit

Hanoun City. This project was very well received and appreciated by the Beit Hanoun Municipality. In addition, CHF staff in participation with the Beit Hanoun Municipality prepared the sketch plans to implement a similar project at the entrance of Beit Hanoun

town in front of the newly constructed bridge funded under USAID's Emergency Roads Rehabilitation. This, in turn, encouraged the Beit Lahia Municipality to request CHF to do a similar project at the main street which connects Sheikh Zayed City and the municipality area.

CHF laborers, in participation with the Beit Lahia Municipality, held cleaning campaigns to open several main roads that were closed due to the heavy rain in which more than 300 m³ of the construction debris was transferred.

During this quarter, the PEIP/VTP staff and surveyors, in cooperation with the three northern municipalities, finished the waste collection and re-dirtying plan for 238 vacant lots previously cleaned. The re-dirtying rate of these 238 vacant lots approached only 13% of the volume of waste.

Cleaning activities in Ramallah, Al Bireh, and Nablus continued as planned, although because of the cold and rainy weather additional hours were put into vocational training activities. The PEIP/VTP field program was formally extended till the end of April 2004.

The repair of retaining stonewalls continues in coordination with all three municipalities. In addition to the cleaning of vacant lots, CHF is currently carrying out, upon municipalities' request, painting of street curbs and planting of trees and shrubs in the center isles of newly paved roads funded under the USAID's Emergency Roads Rehabilitation Project in the West Bank.

The PEIP/VTP community outreach team and CHF laborers celebrated the national Tree Day on January 15 in cooperation with the three municipalities. The Tree Day is part of an ongoing tree planting campaign in the West Bank. During this rainy season, CHF's PEIP/VTP community outreach team and training team conducted a training program for all employment generation hires at the municipal meeting halls of Ramallah and Nablus. Training topics included environmental awareness related to solid waste management, laborers safety and security during site-work, and general health related discussions.

In Al Bireh, the PEIP/VTP outreach team completed a Solid Waste Re-use workshop at the winter camp organized in cooperation with Al Bireh Childhood Welfare Center and Al Bireh Municipality in which 35 students participated. The workshop was very successful and CHF has since received requests from the Total Communication Center for Teaching and Deaf Rehabilitation, and from Aziz Shaheen Girls School to implement similar environmental activities related to solid waste recycling and re-use.



CHF laborers and staff during a planting campaign, in which 270 students from the Zayed Bent Haretha Elementary School participated.

The Municipality of Ramallah is particularly satisfied with the stone wall construction, and requested CHF to increase the number of qualified laborers to build stone walls in the city.

In Nablus, training courses started for the municipal Environmental Health Department staff in the field of re-use and recycling of solid waste, computer basics, and environmental health related issues. PEIP/VTP community outreach team and Nablus municipality agreed on CHF's participation in an emergency plan to help remove waste accumulated during the last curfew and closure in Nablus City.

3.1.7 Coordination with Community Organizations

This quarter PEIP/VTP organized 154 general and central neighborhood meetings, 2,860 home visits, and 188 shops and commercial centers visits.

CHF community outreach teams worked with over 308 schools in the provision of student health team training, in-classroom lectures to children, and assistance in the organization and implementation of cleaning campaigns of schools and their environs.

3.1.8 Beneficiaries and Impact Indicators

In the original program proposal, CHF had identified strategic objectives, intermediate results and preliminary impact indicators for each of the principal areas of activity. The following impact indicators are part of the PEIP/VTP monitoring and evaluation plan.

1. Employment generation monitoring and evaluation

- Person months of direct employment created per month;
- Person months of spin-off employment created per month; and
- Number of person months of employment generated for women.

2. Surveying and identification of waste to be removed

- Number of vacant lots with accumulated wastes surveyed per month, and per neighborhood;
- Area of vacant lots surveyed per month, and per neighborhood;
- Volume of waste surveyed per month, and per neighborhood; and



CHF working to beautify and maintain cleanliness through stonewalls construction in Ramallah City.

- Weight of waste surveyed per month, and per neighborhood.

3. Waste collection monitoring and evaluation

- Number of vacant lots with accumulated wastes cleaned up per month, and per neighborhood;
- Area of vacant lots cleaned up per month, and per neighborhood;
- Volume of waste collected per month, and per neighborhood; and
- Weight of waste collected per month, and per neighborhood.

4. Public awareness monitoring and evaluation

- Number of public awareness materials produced;
- Number of beneficiaries of public awareness materials, disaggregated by gender;
- Number of beneficiaries of home visits and meetings, disaggregated by gender;
- Number of vacant lots and their volume of waste that need re-cleaning after previous CHF cleaning , per neighborhood;
- Number of citizens and establishments aware of their responsibilities in maintaining the cleaned lots, per neighborhood; and
- Number and quality of partnerships developed, per neighborhood.

5. Vocational training

- Number of people trained;
- Number of training hours given;
- Number of persons and training hours for women; and
- Number of trained people who find a job after the CHF program has finished.

3.2 USAID Performance Monitoring Plan

- According to the second annual implementation plan, 51,434 ton of solid waste has to be collected for the second year. As of this quarter the total amount of solid waste that has been collected for the second year is 78,849 ton.

- According to the second annual implementation plan, 35,299 training hours have to be provided for the second year. As of this quarter the total amount of hours that have been provided for the second year is 44,418 hours.
- According to the second annual implementation plan, 118,376 person days of employment have to be generated for the second year. As of this quarter 119,194 person days of employment have been generated for the second year.
- According to the second annual implementation plan, an estimated \$1,352,553.46 income for direct employment beneficiaries has to be generated for the second year. As of this quarter an estimated \$1,487,624 income for direct employment beneficiaries has been generated for the second year.



CHF's workers in participation with the Beit Hanoun Municipality and the Agricultural Development Association during a cleaning and beautification campaign along the center isles of Beit Hanoun town.

3.3 Summary of Output Indicators

The output indicators for the quarter under review can be summarized as follows:

- 35,370 person days (1,163 person months) of direct employment generated;
- On average 388 persons were employed per month under PEIP/VTP;
- 14,298 tons of solid waste collected, equivalent of 11,243 m³ of solid waste;
- 39.93 km of streets swept;
- 751 vacant lots surveyed in detail containing more than 6,610 m³ of solid waste; and
- 19,457 persons have directly benefited from the public awareness activities.

3.4 Audited Progress to Date

All of CHF's programs in Palestine and around the world are subject to an individual contract compliance and financial audit on a yearly basis. In the West Bank and Gaza, CHF contracted Abu Ghazaleh to conduct the FY 2003 annual audit. This process entails

a full fledged, five-week contract compliance and finance evaluation. The PEIP/VTP program has undergone this audit process twice since program inception.

4 Financial Management/Reporting

CHF International uses Quick Books 2002 as the standard CHF financial accounting package that has a pre-defined chart of accounts. Besides, PEIP/VTP uses a computerized payroll system, especially designed for the CHF Employment Generation Program.

5 Other Issues

None.

6 Annexes

6.1 Detailed Waste Collection Reports (Gaza North) for Current Quarter

SUMMARY OF SOLID WASTE COLLECTION & RECOLLECTION(25 December 2003 - 24 January 2004)

AREA	No.Of V.L	Streets(L.M)	Area in m2	Sand&Construction Debris		Litter Collection(Plastic Bags)			Sand&Construction Debris Transferred			Total litter , sand & construction debris transferred	
				Volume in m3	Weight in Tons	No Of P.B	Weight in kg	Volume in m3	No.Of Trips	Volume in m3	Weight In Tons	Volume in m3	Weight in tons
Jabalia	85	0	69,910	236	354	5,478	32,868	131	49	735	1,103	866	1,135
Beit Lahia	16	0	32,409	82	123	2,517	15,102	60	19	285	428	345	443
Beit Hanoun	22	750	18,150	42	62	2,919	17,514	70	4	60	90	130	108
Jabalia Recollection	10	0	4,440	34	50	585	3,510	14	3	45	68	59	71
Beit Lahia Recollection	10	0	12,850	135	203	2,347	14,082	56	10	150	225	206	239
Beit Hanoun Recollection	9	280	14,750	17	25	2,011	12,066	48	2	30	45	78	57
Jabalia Streets	0	500	0	14	21	0	0	0	1	15	23	15	23
TOTAL	152	1,530	152,509	559	838	15,857	95,142	381	88	1,320	1,980	1,701	2,075

SUMMARY OF SOLID WASTE COLLECTION & RECOLLECTION(25 January 2004 - 24 February 2004)

AREA	No.Of V.L	Streets(L.M)	Area in m2	Sand&Construction Debris		Litter Collection(Plastic Bags)			Sand&Construction Debris Transferred			Total litter , sand & construction debris transferred	
				Volume in m3	Weight in Tons	No Of P.B	Weight in kg	Volume in m3	No.Of Trips	Volume in m3	Weight In Tons	Volume in m3	Weight in tons
Jabalia	58	0	55,920	162	243	7,345	44,070	176	37	555	833	731	877
Beit Lahia	6	0	14,440	53	79	1,548	9,288	37	3	45	68	82	77
Beit Hanoun	7	0	12,900	20	29	1,634	9,804	39	0	0	0	39	10
Beit Lahia Recollection	2	0	10,500	32	47	1,280	7,680	31	2	30	45	61	53
Beit Hanoun Recollection	6	0	16,950	15	23	1,612	9,672	39	1	15	23	54	32
Jabalia Streets	0	1,950	0	44	66	33	198	1	3	45	68	46	68
TOTAL	79	1,950	110,710	325	487	13,452	80,712	323	46	690	1,035	1,013	1,116

SUMMARY OF SOLID WASTE COLLECTION & RECOLLECTION(25 February 2004 - 24 March 2004)

AREA	No.Of V.L	Streets(L.M)	Area in m ²	Sand&Construction Debris		Litter Collection(Plastic Bags)			Sand&Construction Debris Transferred			Total litter , sand & construction debris transferred	
				Volume in m ³	Weight in Tons	No Of P.B	Weight in kg	Volume in m ³	No.Of Trips	Volume in m ³	Weight In Tons	Volume in m ³	Weight in tons
Jabalia	78	0	73,975	222	333	10,380	62,280	249	50	750	1,125	999	1,187
Beit Lahia	2	0	3,700	17	25	1,495	8,970	36	2	30	45	66	54
Beit Hanoun	4	0	18,250	43	65	3,963	23,778	95	5	75	113	170	136
Jabalia Recollection	2	0	800	2	3	210	1,260	5	1	15	23	20	24
Beit Lahia Recollection	7	0	7,350	29	43	2,415	14,490	58	3	45	68	103	82
Beit Hanoun Recollection	33	0	41,990	71	107	8,042	48,252	193	5	75	113	268	161
Jabalia Streets	0	3,590	0	13	19	950	5,700	23	2	30	45	53	51
Beit Lahia Streets	0	2,150	0	18	26	284	1,704	7	2	30	45	37	47
TOTAL	126	5,740	146,065	413	620	27,739	166,434	666	70	1,050	1,575	1,716	1,741

SUMMARY OF SOLID WASTE COLLECTION & RECOLLECTION(25 December 2003 - 24 March 2004)

SUMMARY OF SOLID WASTE COLLECTION & RECOLLECTION(25 December 2003 - 24 March 2004)

													Total litter , sand & construction debris transferred	
				Sand&Construction Debris		Litter Collection(Plastic Bags)			Sand&Construction Debris Transferred					
	AREA	No.Of V.L	Streets(L.M)	Area in m ²	Volume in m ³	Weight in Tons	No Of P.B	Weight in kg	Volume in m ³	No.Of Trips	Volume in m ³	Weight In Tons	Volume in m ³	Weight in tons
1-	Jabaliala	221	0	199,805	620	930	23,203	139,218	557	136	2,040	3,060	2,597	3,199
2-	Beit Lahia	24	0	50,549	151	227	5,560	33,360	133	24	360	540	493	573
3-	Beit Hanoun	33	750	49,300	104	156	8,516	51,096	204	9	135	203	339	254
4-	Jabaliala Recollection	12	0	5,240	36	53	795	4,770	19	4	60	90	79	95
5-	Beit Lahia Recollection	19	0	30,700	195	293	6,042	36,252	145	15	225	338	370	374
6-	Beit Hanoun Recollection	48	280	73,690	103	154	11,665	69,990	280	8	120	180	400	250
7-	Jabaliala Streets	0	6,040	0	71	106	983	5,898	24	6	90	135	114	141
8-	Beit Lahia Streets	0	2,150	0	18	26	284	1,704	7	2	30	45	37	47
	TOTAL	357	9,220	409,284	1,296	1,944	57,048	342,288	1,369	204	3,060	4,590	4,429	4,932
