



**USAID** | **AFGHANISTAN**  
FROM THE AMERICAN PEOPLE

**ALTERNATIVE  
LIVELIHOODS PROGRAM—  
EASTERN REGION (ALP/E)**

**QUARTERLY REPORT  
OCTOBER – DECEMBER, 2006**

**PREPARED BY:**

**Development Alternatives Inc. (DAI)**

**IN COLLABORATION WITH:**

**Bearing Point (BP)**

**Hatch Mott MacDonald (HMM)**

**ICARDA**

**International Foundation of Hope (IF Hope)**

**Relief International (RI)**

**Social Impact (SI)**

**Jalalabad – Afghanistan**

**January 2007**

Project Name	Alternative Livelihoods Program–Eastern Region (ALP/E)
Start Date	15 February, 2005
End Date	14 February, 2009
Contract Number	GS-10F-0359M
Order Number	306-M-00-05-00515-00
Cognizant Technical Officer	Brian Bacon
Contracting Officer	Margaret Kline
Geographic Coverage	Nangarhar, Laghman, Kunar, and Nuristan Provinces



### ALP/E'S MISSION STATEMENT

The overall objective of ALP/E is to accelerate broad-based, sustainable regional economic development in the Eastern Region, providing the population with licit livelihood options, and contributing to the elimination of poppy production as an economic element. This will be accomplished by working with the public and private sectors to increase the competitiveness and diversity of regional agricultural and non-agricultural sub-sectors; improving access to markets, business services and inputs; consolidating the presence of supportive public and productive infrastructure; building public and private sector capacity to function in a competitive and transparent economy; and addressing the needs of populations heavily reliant on the poppy economy.

## TABLE OF CONTENTS

---

COMMONLY USED ACRONYMS .....	4
1. EXECUTIVE SUMMARY .....	5
2. PROGRAM OVERVIEW .....	7
2.1. ALP/E BACKGROUND.....	7
2.2. IMPLEMENTATION STRATEGY AND LIFE OF PROJECT WORK PLAN .....	7
2.3. PROVINCIAL COVERAGE .....	7
3. QUARTERLY RESULTS .....	8
3.1. AGRIBUSINESS DEVELOPMENT ACTIVITIES.....	8
3.2. PRIVATE SECTOR DEVELOPMENT ACTIVITIES.....	13
3.3. INFRASTRUCTURE DEVELOPMENT ACTIVITIES .....	15
3.4. GENDER AND MICRO – ENTERPRISE (GME) ACTIVITIES .....	23
3.5. INSTITUTIONAL CAPACITY DEVELOPMENT ACTIVITIES.....	24
3.6. COORDINATION .....	26
3.7. PROGRAM MANAGEMENT AND ADMINISTRATION .....	26
3.7.1. OPERATIONS AND PROGRAMMING.....	26
3.7.2. MONITORING AND EVALUATION .....	27
3.7.3. PROGRAM SECURITY .....	28
SUMMARY OF FIRST QUARTER 2007 SHORT TERM TECHNICAL ASSISTANCE (STTA) .....	29
ANNEX–I: ALP/E ACTIVITY LEVEL INDICATORS .....	29
ANNEX-II: ALP/E ACTIVITY LEVEL INDICATORS (ALP).....	30
ANNEX-III: ALP/E ACTIVITY LEVEL INDICATORS (ALP + AINP).....	39
ANNEX –IV: ALP/E PROGRAM ACTIVITIES AS OF DECEMBER 31, 2006.....	42
ANNEX –V: ALP/E PERSON EMPLOYED, EMPLOYMENT DAYS, AND WAGES PAID ON CFW PROJECTS THROUGH DECEMBER 31, 2006 .....	45

## COMMONLY USED ACRONYMS

---

AFC	Afghanistan Finance Company
AICC	Afghanistan International Chamber of Commerce
AINP	Afghanistan Immediate Needs Program
AL	Alternative Livelihoods
ALP	Alternative Livelihoods Program
ALP/E	Alternative Livelihoods Program—Eastern Region
AMPS	Agricultural Marketing and Production Support
AWBA	Afghan Women Business Association
AWP2	Annual Work Plan 2 (Second Year)
BCI	Business Capacity Index
CFW	Cash for Work
CJTF	NATO's Combined Joint Task Force
CNFA	Citizen's Network for Foreign Affairs
COP	Chief of Party
CTTC	Construction Trades Training Center
DAI	Development Alternatives Incorporated
DBST	Double Bitumen Surface Treatment
DCOP	Deputy Chief of Party
BDC	Business Development Center
FAO	UN Food and Agriculture Organization
GOA	Government of Afghanistan
GME	Gender and Micro-enterprise
HMM	Hatch Mott MacDonald
ICARDA	International Center for Agricultural Research in the Dry Areas
ISAF	International Security Assistance Force
IT	Information Technology
LOP	Life of Project
MIS	Market Information System
NGO	Non-governmental Organization
NRIT	Nangarhar Roads Inventory Team
NRM	Natural Resources Management
NVDA	Nangarhar Valley Development Authority
PCB	Provincial Coordinating Body
PDC	Provincial Development Council
PIP	Productive Infrastructure Program
PMP	Performance Management Plan
PRT	Provincial Reconstruction Team
PSD	Private Sector Development
RI	Relief International
RFP	Request for Proposal
STTA	Short-term Technical Assistance
TWG	Technical Working Group
TOT	Training of Trainers
USG	United States Government

## 1. EXECUTIVE SUMMARY

Development Alternatives Inc. (DAI) presents its first quarterly report for the fiscal year 2007 under the United States Agency for International Development (USAID)-funded Alternative Livelihoods Program–Eastern Region (ALP/E). This report summarizes program achievements and activities undertaken by the ALP/E's technical units from October 1, 2006 to December 31, 2006.

The security situation in the Eastern Region remains tense. Insurgent activities increased throughout the region, specifically in Kunar (Nari, Marawara and Pech Districts), and in Laghman (Alingar, Alis hing and Dawlat Shah Districts).

Highlights of ALP/E's achievements and activities during this quarter include:

- Completed the 2006 Fall Wheat Seed and Fertilizer Distribution Program, which targeted villages assessed as being likely to be making a choice between poppy and other crops. In total, 76,510 farmers received 7,651 MT of wheat seed and fertilizer. The distribution was coordinated with district representatives of the Ministry of Agriculture, district governors and shuras.
- Established robust and sustainable value chains as part of the Vegetable Marketing Program. Facilitated linkages between input suppliers, farmers and traders; and ensured that the program participants cultivated vegetables, which met the market requirements of crop type, varieties, price, volumes, quality, packaging, and timing.
- Supported four new women-operated pilot greenhouses to produce plug vegetable seedlings for demonstration and commercial farms.
- Facilitated the organization of a Regional Fruit Producers Association, building on groups already established through marketing and extension work done under the Fruit Marketing Program.
- Provided intensive training and advice in grading, packaging and marketing to regional citrus growers. As a result, local traders agreed to pay higher prices to the citrus growers.
- Identified prospective beneficiaries for the second phase of planting of fruit and nut trees on 1,500 hectares of land. To date, 4,143 farmers have signed up on 10,712 Jeribs of land.
- Supported the region's livestock production by training 1,533 women in southern Kunar and eastern Nangarhar. All the women trained are responsible for two to five cattle.
- Conducted a comprehensive assessment of risks and opportunities in commercial poultry production. In part as a result of this assessment, in November the Department of Veterinary Services in Kabul lifted the avian-flu-related ban on the importation, transportation and retailing of live chickens. Worked on establishing a regional Poultry Producers Association to encourage this sub-sector's expansion.
- Developed and distributed informational materials on the services of the Business Development Center available for the regional business community. The BDC hosted a gathering of 40 prominent local businesspeople to report on its activities over the last six months.
- Facilitated the leadership election process of the Small and Medium Enterprise Association of Jalalabad City, the largest trade association organization in the Eastern Region, composed of 66 trade unions and groups and 3,500 individual members.
- Evaluated 23 bids and awarded the Kama Road Improvement contract to SKB/Saboor Joint Venture (SKB/SMCRC).
- Completed construction work on Mashina Road in Qarghai district of Laghman.
- Handed over the first half of the Fruit and Vegetable Wholesale Market to the Jalalabad Municipality. Completed 70 shops, a new water supply, a concrete parking area and improved drainage at the facility.
- Finalized the inventory of 455 roads of total length 2,600 km in 22 districts of Nangarhar Province.

- Completed 16 CFW projects, reaching a total of 72 projects since the program began in 2005. Continued work on another 45 projects in Nangarhar, Laghman, Kunar, and Nuristan Provinces. Achieved the employment rate of 4,921 workers per day during this reporting period. Employed 24,619 individual laborers from June 2005 to December 31, 2006. Recorded 332,145 of total employment days during this quarter; reaching 1,402,007 of cumulative employment days by December 31, 2006.
- Launched a weekly radio program to showcase successful businesswomen and introduce various business topics to women in the Eastern Region.
- Finalized and released the findings of the women's business survey conducted by Kaweyan Business Development Services (KBDS). KBDS surveyed 300 businesswomen across Nangarhar, Laghman and Kunar Provinces.
- Facilitated the participation of a group of five women from the Eastern Region in the Rural Handicraft Exhibit, which took place in New Delhi, India on November 14-27. During the tradeshow, the Afghan participants held negotiations with more than 20 exporters and received several test orders for hand-embroidered shawls, jackets, and shirts.
- Began computer and English language training for members of the Jalalabad Fruit and Vegetable Wholesalers Association, Afghan Agricultural Development Association, Livestock Development Association and Input Suppliers Association.
- Started a series of general office management trainings for members of 15 trade associations, including the Fruit and Vegetable Wholesalers Association, Agricultural Input Suppliers Association, Livestock Development Association, and the Carpet Producers Association.

## **2. PROGRAM OVERVIEW**

### **2.1. ALP/E BACKGROUND**

The United States Agency for International Development (USAID) awarded the Alternative Livelihoods Program–Eastern Region (ALP/E) contract to Development Alternatives Inc. (DAI) on February 15, 2005, under MOBIS Task Order No 306-M-00-00515-00, Contract Number GS-10F-0359M. The contract has an initial value of \$108.386 million, and is scheduled to run until February 15, 2009. Current obligated funding stands at \$54.3 million. The ALP/E team comprises DAI and the following subcontractors: Bearing Point (BP), Hatch Mott MacDonald (HMM), ICARDA, IF Hope, Relief International (RI), and Social Impact (SI).

Contractually, the Alternative Livelihoods Program–Eastern Region has two overall strategic objectives: (1) licit crop production and business activity expanded in Eastern Region Provinces; and (2) unemployment and poverty reduced in Eastern Region Provinces. ALP/E’s activities fully support USAID/Afghanistan’s Strategic Plan 2005-2010, and contribute directly to success in Strategic Objective No 5 (a thriving licit economy led by the private sector).

### **2.2. IMPLEMENTATION STRATEGY AND WORK PLANS**

A USAID Technical Directive dated September 24, 2005 approved ALP/E’s Implementation Strategy and Life of Project Work Plan. The ALP/E Annual Work Plan (AWP), covering the period of October 2005 through the end of June 2006 was approved on December 10, 2005. The ALP/E Annual Work Plan for year 2 (July 2006-June 2007) was accepted by USAID on August 31, 2006.

ALP/E’s Implementation Strategy and Work Plan are based on a platform of core values and guiding principles:

- **Build a Strong Foundation**
- **Drive the Economy while Achieving Social Inclusion**
- **Stay Market Driven and Value Chain Focused**
- **Integrate Technical Assistance**
- **Emphasize Sustainability and Local Capacity AND Maintain Clear Linkages to Poppy Elimination**
- **Collaborate and Coordinate with Government Ministries, Other USAID Contractors and Grantees and Other Donors**
- **Strive for Gender Equity**

ALP/E focuses on activities that have the greatest potential for building clusters of linked businesses, expanding production, increasing income, generating employment and capturing additional benefits within the region. ALP/E’s activities include: Annual Horticulture, Perennial Horticulture, Livestock, Staple Crops/Food Security, Business Services, Natural Resources, Infrastructure, Gender and Micro-Enterprise and Capacity Building. To ensure a comprehensive and targeted implementation of its activities, ALP/E divides the project area into geographic zones. These zones are: urban/market centers; core areas; transition areas; and fringe areas.

### **2.3. PROVINCIAL COVERAGE**

ALP/E is currently active in four provinces of the Eastern Region – Nangarhar, Laghman, Kunar and Nuristan. The project has established good working relationships with its primary stakeholders and has a regular dialogue with government officials and private institutions in all four areas. The ALP/E project staff meets regularly with the provincial Technical Working Groups (TWG), the Provincial Development Councils (PDC) and provincial and local shuras. While ALP/E does not have a mandate to include every district in a province, the program strives to cover as wide an area as possible and have a positive impact throughout the provinces.

ALP/E limits its activities in certain areas due to security concerns for its staff. Specifically, insurgent activity or political unrest frequently slows work in the border districts of Nangarhar (Sherzad, Khogyani, Pachir Wa Agam, Dih Bala, Achin, Dur Baba) and the northernmost district of Laghman (Dawlat Shah). Movement in Kunar and Nuristan is usually restricted to national staff operating in the lowest profile possible. Eastern Nuristan is currently off limits to all staff.

### 3. QUARTERLY RESULTS

This section presents the progress of ALP/E's operating units in the previous quarter. A description of the principal activities for each technical unit is followed by a summary of the upcoming activities.

#### 3.1. AGRIBUSINESS DEVELOPMENT ACTIVITIES

##### 3.1.1. FALL 2006 WHEAT SEED AND FERTILIZER DISTRIBUTION PROGRAM

During the quarter, ALP/E successfully completed its Wheat Seed and Fertilizer Distribution Program (WSP), with 76,945 farmers receiving 7,694 MT of wheat seeds and fertilizers in the Eastern Region. The distribution was led by ALP/E's staff in close cooperation with district representatives of the Ministry of Agriculture, district governors, and district and local shura members.

The WSP specifically targeted areas with a recent history of poppy production that are typically neglected and difficult to work in because of their isolated location and precarious security environment. To maximize program impact, ALP/E prioritized the districts based on historic poppy data from the United Nations Office of Drug Control (UNODC). Following the district selection process, ALP/E's staff worked with district-level representatives of the Ministry of Agriculture, district governors and shuras to select specific villages for the distribution. In these targeted villages, all the farmers got sufficient seeds and fertilizers to plant one jerib of land.




Farmer receives wheat seed and fertilizer in Alishang District

*“[...] Poppy cultivation is against Islamic and democratic laws. So that our farmers can start generating licit income, the Elders of Khas Kunar are kindly requesting you to allocate more wheat seeds and fertilizers for our village [...]”*

**(From a letter addressed to ALP/E's Chief of Party)**

ALP/E's monitors were involved throughout the entire process, from selecting the target districts to drawing up beneficiary lists, and from distributing vouchers to surveying the actual input distribution amongst the selected beneficiaries, thereby ensuring accountability at all levels. ALP/E's monitors were also tasked to get a commitment from recipients not to grow poppy, emphasizing that individual farmers' failure to comply with their no-poppy pledge could impact the entire community when that village is excluded from future ALP/E programs.

Despite all the logistic and security challenges of transporting large quantities of seed and fertilizer, the entire process was implemented according to the schedule. In 2007, ALP/E will be conducting a series of surveys to quantify the total area planted with wheat and to measure its distribution program's impact.

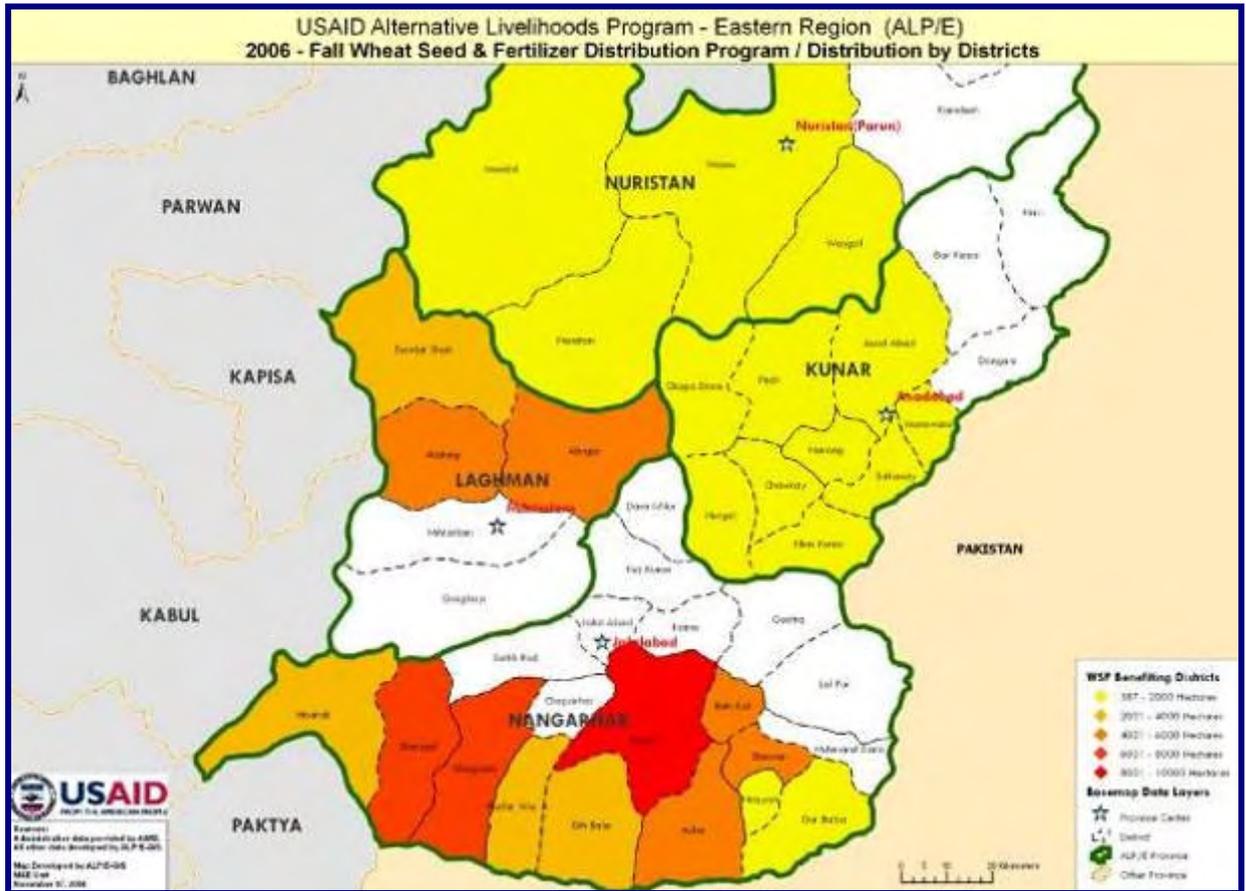

### 3. I.2. VEGETABLE MARKETING PROGRAM

ALP/E’s programs in support of the vegetable sub-sector involve a series of activities aimed at building robust and sustainable value chains. Within this context, ALP/E’s Gender and Micro-Enterprise and Agribusiness units continued establishing women-operated pilot greenhouses, increasing the total number to four during the reporting period.




Nursery operator displays gourmet lettuce plug seedlings

Each greenhouse is capable of producing up to 50,000 vegetable seedlings per a six-week cycle. The female entrepreneurs specialize in short-cycle, high-yielding gourmet vegetables and supply them to progressive farmers and vegetable traders who participate in other ALP/E’s agribusiness projects.

To promote this new for Afghanistan technology, ALP/E encouraged the pilot greenhouse owners to conduct an educational campaign for farmers on the benefits of using plug seedlings. The Gender and Micro-Enterprise and Agribusiness units assisted the plug seedling enterprises in establishing of demonstration plots, holding field days for farmers, and carrying out other promotional activities. During a few more crop cycles in 2007, ALP/E will continue its assistance to the greenhouses.



### 3. I.3. FRUIT MARKETING PROGRAM

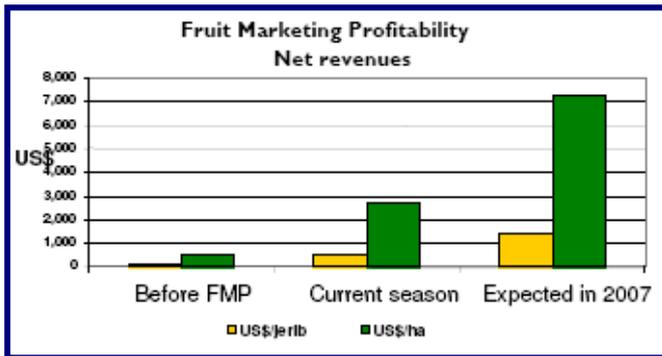

During this quarter, the Fruit Marketing Program entered a new phase. The Agribusiness and Institutional Capacity Development units facilitated the establishment of a Regional Fruit Producers Association.

In addition, ALP/E helped create Fruit Marketing Groups and introduce improvements in grading, packaging and marketing operations. This initiative faced a few challenges at the start because most producers had already received cash advances from traders for their 2006

production. Typically, traders from Kabul come during the lean season and pay in advance the equivalent of \$150 - \$200 per jerib of sweet orange for subsequent harvesting rights in that orchard. Nonetheless, ALP/E staff was able to foster a dialogue with a large number of traders and persuade them that the traders would also benefit from receiving graded and packaged fruit and procuring larger volumes through the Fruit Marketing Groups. Following these discussions, both traders and citrus growers were able to agree on a harvest price per kilogram, as compared with the pre-harvest “price per jerib”.



“Pride of the Eastern Region,” a regional brand introduced and supported by ALP/E

The Fruit Marketing Program also facilitated new market arrangements for citrus farmers. This endeavor brought together ALP/E’s field technicians, several fruit marketing groups and a small number of progressive traders. Farmers who would otherwise sell their orange harvest at Afs5,000-10,000/jerib (US\$500-\$1,000/ha)



Export shipment of fruit and vegetables from eastern Afghanistan

now sell graded and packaged fruit at Afs3/unit, which at the current productivity levels and after deducting the cost of packaging and transportation results in a net revenue of US\$2,700/ha. These market arrangements, coupled with increased productivity and harmonization of quality standards, have the potential to produce revenues of up to US\$7,000/ha in the medium term.

On November 29, when Ariana Airlines Flight 401 left Kabul International Airport for Dubai, the national airline’s aircraft carried onboard the first shipment of a new Afghan brand of fruit and vegetables—

“Pride of the Eastern Region.” ALP/E assisted Hadyatullah-Samsour Bam Ltd., a trading company from Laghman, to launch the brand and sell this trial shipment to a UAE-based fruit and vegetable dealer. Within days, the test shipment of 1,300 Kg was sold through several supermarkets and 16 high-end hotels in Dubai, generating a number of commercial follow-on orders.

### 3. I.4. EASTERN REGION ORCHARD DEVELOPMENT PROGRAM, PHASE II

ALP/E's subcontractor IF Hope continued to monitor and identify prospective beneficiaries for the second phase of its Eastern Region Orchards Development Program, which entails planting fruit and nut trees on 1,500 hectares of land. During this reporting period, IF Hope extension staff focused on the preparation of water channels, pre-planting, weeding, intercropping management, orchard design and layout, and selecting new farmers.

IF Hope also distributed sprayers amongst farmers with 2-3 Jeribs of orchards, and provided technical assistance to the participants from the first phase. Farmers were trained on maintaining the trees, weeding, irrigation, pest control, application of animal manure, laying out water channels for new and old orchards, digging pits for new trees, preparation of land for orchards and using sticks as indicators for orchard design and layout.



Farmers receive training in planting techniques

So far, 4,143 farmers have been registered for 10,712 jeribs of potential orchards. Due to low water availability, some interested farmers could not be included in the program.

### 3. I.5. SMALLHOLDER LIVESTOCK DEVELOPMENT PROGRAM

The Smallholder Livestock Development Program is one of ALP/E's activities supporting women from the Eastern Region in their livestock production. During this reporting period, ALP/E's team of female veterinary assistants reached a milestone of 1,533 graduates from their training programs. All the women trained are responsible for breeding two to five cattle.



Women smallholders get training n livestock restraint and vaccination techniques

Rural communities' leaders and government officials continued to praise the program and to request its expansion to other districts in the region. During the reporting period, ALP/E trained a second group of women technicians to expand the training to southern

Kunar and eastern Nangarhar. During the spring of 2007, these

veterinary trainers will provide technical support to 200 female participants in the ALP/E's commercial poultry program.

### 3. I.6. COMMERCIAL-SCALE LIVESTOCK PRODUCTION PROGRAM

ALP/E delivered a 12-day training course for commercial livestock producers of Nangarhar. The group consisted of progressive businesspeople who, despite the current price controls for beef, had decided to engage in intensive medium and large-scale beef operations.

Following the training course, seven of the commercial farmers convinced of the advantages of introducing animals with a better genotype sold their existing stock to replace them with improved breeds. The Livestock Team is supporting them with on-farm evaluations of the effectiveness of improved feeding schemes. Additionally, ALP/E's technical experts provide advice on a variety of matters, including how to purchase older animals with weights above 300 Kg and how to take advantage of the phase where carcass weight increases exponentially and results in a better feed conversion rate.



Commercial livestock producers undergo practical training

### 3.1.7. POULTRY DEVELOPMENT PROGRAM

During this reporting period, ALP/E continued its comprehensive assessment of the risks and opportunities for the commercial poultry production, which has been identified as one of the competitive sub-sectors in eastern Afghanistan. Partly as a result of the intervention of an ALP/E technical expert, in November 2006 the Department of Veterinary Services in Kabul lifted the avian-flu-related ban on importation, transportation and retailing of live chickens. This was an important step for the sub-sector's recovery and growth. Following the lifting of the ban, ALP/E established a Regional Poultry Producers Association to assist with the poultry sub-sector's expansion. Future activities in support of the industry will include: providing technical assistance in business planning for potential investors, facilitating linkages with financial institutions, and assisting women entrepreneurs in establishing semi-commercial poultry operations.

## UPCOMING ACTIVITIES: AGRIBUSINESS DEVELOPMENT

- Commercial Orchards Program: the establishment, care and management of 3,000 hectares of apricot, pomegranate, citrus, apple and almond.
- Planting of 1,500 hectares of 17 fruit and nut crops in 17 districts of Nangarhar and Laghman provinces.
- Building the capacity of small and medium-scale farmers and assist in the rehabilitation of their existing orchards.
- Continuing data collection from 33 wheat trials and using the existing 85 demonstration farms to test and promote promising new wheat varieties and management practices.
- Building the capacity of the 15 village based seed enterprises (VBSEs) to run profitable businesses by marketing seed from 300 hectares of improved wheat varieties planted in the winter of 2006.
- Launching the Technology Innovations for Market-Led Rehabilitation (TIMER) vegetable program.
- Starting REVAMP which will support commercial vegetable production through the establishment of sustainable supply chains and producer/wholesaler linkages.
- Establishing 10 commercial vegetable demonstration farms in partnership with private investors.
- Facilitating the participation of six traders and farmers in the Middle East Agribusiness Exhibition in Dubai in April 2007.
- Expanding the smallholder livestock training programs into Kunar and Nuristan.
- Facilitating the increase of local capacity for broiler production by 100,000 birds/year.
- Supporting the emergence and strengthening of commercial beef operations through training courses on beef management to the Commercial Livestock Producers Association.

## 3.2. PRIVATE SECTOR DEVELOPMENT ACTIVITIES

Recognizing the importance of the private sector as the engine of economic growth in the Eastern Region, ALP/E's activities aim to create an enabling environment for investors and stimulate business development in the region. The Eastern Region's Business Development Center (BDC) brings together support organizations under one roof to promote business activities in the region. Supported by ALP/E and run by Afghans, it has created a network of local businesspeople in the region and represented the eastern region at the highest levels of the national Government.

### 3.2.1. SUPPORTING REGIONAL BUSINESSES

During the reporting period, ALP/E's Private Sector Development (PSD) Unit facilitated the participation of four marble processors in the annual construction fair, which took place in October, 2006 in Dubai. This

international event was an excellent opportunity for entrepreneurs from the Eastern Region to exhibit and market their products in the Middle East.

The PSD Unit drafted the final report of an informal tax survey and discussed the survey findings with the Provincial Finance Department and Nangarhar Customs House to make a comparison between the mandated tax and the actual tax being charged at road check points. The report identified some of the constraints wholesalers face during their import-export operation between Peshawar and Jalalabad.

ALP/E worked with ICARDA STTA on the overall design of the Village Based Seed Enterprise Program (VBSE). In addition, work also continued on preparing a report on the economic sustainability of the VBSE.

ALP/E continued its cooperation with other USG-funded programs in order to support the development of agricultural producers and agribusinesses in the region. ALP/E's beneficiaries—farmers, farmer associations, and small and medium businesses—were referred to loan and grant programs available through USAID's ARIES program. Additionally, ALP/E's PSD Unit facilitated agreements with CNFA for two businesses, Azizi Food Factory and Hamisha Bahar Vegetable Dehydration. The total investment in these two projects will be \$71,200, creating 31 new full-time jobs.

### **3.2.2. BUSINESS DEVELOPMENT CENTER**

ALP/E worked with the Business Development Center on designing and distributing among the regional business community a leaflet promoting its services. The BDC also hosted a gathering of 40 businesspeople to report on its activities in the last six months and explain what services are available for at the Center. The participants expressed a particular interest in the BDC's assistance with customs formalities and compliance with the import/export regulations for various commodities.

Also during the reporting period, the BDC held a meeting with the Nangarhar Provincial Shura to brief its members on the role of ALP/E and the BDC in promoting business activities in the region.

At the request of the Afghanistan Investment Support Agency (AISA), the BDC conducted a study on what problems small and medium-size businesses in the region currently face. The BDC also mediated negotiations



**Entrepreneurs meet at the Business Development Center**

between the Afghanistan International Bank and a group of local factory owners concerning possible financing of an advertising campaign. In addition, during this quarter, the BDC provided a variety of services to its clients. These included: facilitating contacts with the Ministry of Agriculture in Kabul to assist a local trader interested in shipping olive oil to Dubai; providing support to the leadership election process of the Small and Medium Enterprise Association of Jalalabad City; and offering internet training and online search assistance to a number of entrepreneurs.

ALP/E trained the Business Development Center staff members in how to assess the effectiveness of their center's assistance to businesses through a Business Capacity Index (BCI). To date, the BDC has interviewed three business owners using the BCI tools. ALP/E also conducted a strategic planning workshop for the BDC staff. The objective was the development of a comprehensive action plan for the BDC to reach sustainability by 2008.

### **UPCOMING ACTIVITIES: PRIVATE SECTOR DEVELOPMENT**

- Monitoring progress of the approved CNFA applications.
- Improving the hygienic standards of local food production factories.
- Developing sanitation plans for two processing factories and training 40 processing factories in basic sanitation and good manufacturing practices.
- Collaborating with ARIES program for investment support.
- Coordinating with ASMED around the future of the BDC and support for local business associations.
- Working with the Nangarhar Vegetable and Fruit Wholesalers Association and the customs department.
- Developing concept notes for 20 investments and finalize 10 investment business and financial plans.
- Continuing work with the ICARDA team on the business feasibility of the VBSEs.

- Marketing of the BDC through TV programs and quarterly publications.
- Holding 4 internet trainings for 60 members of the business community.
- Providing consultation and advisory services for 180 businesspeople on various topics.
- Developing a website for BDC and opening a bank account for the BDC.

#### ***BDC ACHIEVEMENTS IN BRIEF***

- *Delivered internet and basic computer training to 33 businesspeople.*
- *Provided marketing training to 50 businesspeople and technical assistance to 336 businesses.*
- *Created the Nangarhar Construction Companies' Association, which grew from 25 to 80 members.*
- *Linked the Nangarhar Valley Development Authority's olive oil factory with international buyers.*
- *Developed 4 business plans for companies seeking investment abroad.*
- *Facilitated the registration of 24 new businesses through AISA. The newly registered companies are investing around \$1,642,000 in the regional economy, and creating 859 jobs.*
- *Renewed 30 business licenses through AISA.*
- *Assisted in negotiations to extend the lease period from 3 to 7 years at the AISA Industrial Park.*
- *Facilitated agricultural machinery leases through AFC.*
- *Conducted a study of the priority needs of the local business community.*
- *Advocated on behalf of a local ice factory's owners, saving more than \$75,000 in taxes.*
- *Negotiated a change of the Balance Sheet Tax, saving local businesses an estimated \$675,000 in fines.*
- *Trained 52 women tailors in marketing, in conjunction with the Afghan Women's Business Association.*
- *Trained 31 local factory owners in balance sheet preparation.*
- *Provided consulting services to 270 businesses.*

### **3.3. INFRASTRUCTURE DEVELOPMENT ACTIVITIES**

ALP/E's infrastructure activities focused on three areas: farm to market roads, rehabilitating irrigation systems, and flood protection projects. During this reporting period, the Infrastructure Development Unit completed a number of feasibility and pre-design works on medium-scale productive infrastructure projects in Nangarhar, Laghman and Kunar provinces, and continued 40 Cash-For-Work (CFW) projects in all four provinces. Shuras in all the CFW areas provided an assurance that poppy will not be grown in the locations receiving direct technical support. In addition, the shuras play a critical role in partnering with ALP/E to identify and design projects, ensure security at the sites and provide daily laborers for project implementation. The Infrastructure Development Unit also provided 45 students from Nangarhar with two months internship at ALP/E.

#### **3.3.1. KAMA MAIN ROAD**

As a result of the evaluation of 23 bids received for the Kama Road Improvement Project, ALP/E awarded the contract to SKB/Saboor Joint Venture (SKB/SMCRC). During this reporting period, ALP/E conducted a series of consultations with the winner to discuss various details of the contract to build Kama Road such as construction team mobilization; traffic control during construction; delays and penalties; the maintenance period; and contractor's liabilities.

#### **3.3.2. QASAM ABAD ROAD**

The technical feasibility report for Qasam Abad road was submitted to USAID on 20 September and was approved on Nov 22, 2006. Tendering is planned in the next reporting period.

### 3.3.3. CONSTRUCTION TRADES TRAINING CENTER



During the reporting period, the Construction Trades Training Center (CTTC) trained a total of 393 persons including 40 tradesmen, 42 engineers, 267 skilled workers, 11 technicians and 41 local construction company workers.

**Skilled laborers visit Shamshapoor Road in Surkhrud district of Nangarhar as part of the CTCT training course in cobblestone laying**

### 3.3.4. ABUZAI BRIDGE

Following the approval by USAID of the technical feasibility report for Abuzai Bridge on November 19, ALP/E's infrastructure team visited the site, and discussed with the Director of Laghman's RRD the responsibilities of his organization, including the mine clearance certificate, the rehabilitation of the culverts along Abuzai Bridge, and the resurfacing of the road by a joint team of RRD, Laghman Municipality and the community. Preparation of the technical specifications including the specification for the geotechnical investigations for the foundation of the bridge are in progress.

### 3.3.5. LALPUR ROAD (12 km)

The design has been completed, including a final field check on October 16. The design team visited Lalpur and checked the structures at 10+550 to 11+600. Necessary adjustments were made, the cost estimates were revised and a technical feasibility report was drafted and sent to USAID for approval. ALP/E anticipates starting the work in February 2007.

### 3.3.6. SHERZAD TO HISARAK ROAD SECTION 1

During this quarter, the design of the road profile, cross-sections and structures was completed, and the Feasibility Report was submitted to USAID for approval.

### 3.3.7. BARABAD TO MANGWAL ROAD SECTION 1(11.75 KM)

The survey of section 1, 11.75 km was completed. Typical cross sections of the road, design and drawings of structures, and cost estimates were completed. The draft technical feasibility report remained in progress at the end of this quarter.

### 3.3.8. BARABAD TO MANGWAL ROAD SECTION II (9.58 KM)

Alignment and cross section surveys, for section-2 of 9.58 km, were completed during the period from km 11+500 to 21+080. Drawings and design of the Site Plan, Alignment, and Cross sections from 2+000 to 6+000 were completed. Design of additional structures and the preparation of the technical feasibility report remain in progress.

### 3.3.9. NANGARHAR ROAD INVENTORY TEAM (NRIT)

DISTRICT NAME	NO. OF ROADS	LENGTH OF ROAD (km)
Achin	19	141
Batikot	29	131
Bihsud	46	141
Chaparhar	28	175
Dara-I-Noor	3	31
Different Districts	2	121
Dih Bala	24	158
Dur Baba	11	102

DISTRICT NAME	NO. OF ROADS	LENGTH OF ROAD (km)
Goshta	13	151
Hisarak	23	170
Kama	36	122
Khogyani	29	222
Kot	9	65
Kuz Kunar	12	74
Lal Pur	12	70
Muhmand Dara	36	106
Nazyan	8	51
Pachir Wa Agam	10	53
Rodat	25	138
Sherzad	18	179
Shinwar	28	92
Surkh Rod	34	107
<b>Total</b>	<b>455</b>	<b>2,600</b>

The Nangarhar Roads Inventory Team (NRIT) completed inventories for 455 roads of 2,600 km length in 22 districts of the province. ALP/E's GIS staff assisted the NRIT in the data entry, and provided a five-day training course in December on how to use the GIS database for planning and maintenance of the roads. A presentation was given on the achievements of NRIT to the directors of RRD, Irrigation and Public Works.

### 3.3.10. MASHINA ROAD

During this quarter, HADF, an ALP/E sub-contractor started and completed construction work on Mashina Road in Qarghai district of Laghman. The opening ceremony was held at the project site on December 17, 2006. The Governor of Laghman, the Director of RRD, the Director of Education, the Director of Agriculture, Chief of Police, the Elders of the area, Chief of Party ALP/E, USAID representatives, Director of Operations ALP/E, the Project Manager of the Infrastructure Section, and concerned staff of various departments attended the ceremony. The Governor and elders expressed their satisfaction and appreciation of ALP/E's efforts in rehabilitating roads in the province.



**Governor of Laghman (center) opens Mashina Road**

### 3.3.11. DUDRAK ROAD

Design of the road has been completed and the feasibility report is underway. The design of road, alignment and X-Sections, and typical drawings of culverts was checked on December 13, 06 and changes were proposed.

### 3.3.12. SURVEYS

During the reporting period, the ALP/E Survey Team carried out the following technical surveys:

LOCATION	LENGTH	ALIGNMENT	X-SECTIONS	REMARKS
Darunta Cobblestone Road-III	4.000 km	Setting out	Setting out	CFW
Pekha Road	7.300 km	6+500 to 7+300	6+500 to 7+300	CFW
Site plan for Aqueduct-Nurgal	0.100 km	0.100	Setting out	Survey for site plan completed
Aghrabad road in Qarghai district	2.556 km	Done	Done	Survey work completed
Nuristan District Center to Utran road	7.500 km	Alignment=5+100	X-Section=1+600	Survey work n progress

### 3.3.7. JALALABAD FRUIT AND VEGETABLE WHOLESALE MARKET

At the end of November, ALP/E handed the first half of the Wholesale Market over to the Jalalabad Municipality. ALP/E's Infrastructure team had completed 70 shops, a new water supply, a concrete parking area



**The opening ceremony of the first half of Jalalabad Wholesalers Market**

and improved the drainage at the facility. The Wholesalers' Association hosted a luncheon at the site. Work continued on construction of the new foundations and columns for the other half of the market, making a total physical progress of 84% till the end of this reporting period. The septic tanks for the new toilets were also completed except for the top slab.

### 3.3.8. CASH-FOR-WORK PROGRAM

At the end of this quarter, 16 CFW projects were completed, making a total of 72 projects completed in Nangarhar, Laghman, Kunar, and Nuristan Provinces. Work continued on another 45 projects during the reporting period. The CFW projects employed 4,921 workers, bringing the total of individual laborers employed from June 2005 through December 31, 2006 to 24,619. Total employment days recorded this quarter were 332,145, and the cumulative total reached 1,402,007 employment days from June 2005 through December 31, 2006.

Another section of the cobblestone road in Shamshapor was completed and work started on additional 14 cobblestone roads projects: ten in Nangarhar, three in Laghman and one in Nuristan province. These cobblestone road projects provided employment to 3,553 persons with 128,053 person days generated during the reporting period.

**A. CFW - Laghman Province:** Under the supervision of ALP/E, Relief International (RI) completed 28 projects and continued ten other projects since June 2005. The Darunta cobblestone road third section in Laghman started under direct implementation by ALP/E. The daily laborers employed reached 1,170 workers per day, with a cumulative total of 10,268 individual laborers employed from June 2005 through December 31, 2006. Employment days during the reporting period were 123,980 and the cumulative total reached 589,233 through December 31, 2006.

#### CFW PROJECT STATUS IN LAGHMAN PROVINCE THROUGH DECEMBER 31, 2006

PROJECT	DISTRICT	PROGRESS	IMPLEMENTER	STATUS
Darunta Bypass Cobblestone Road, First Reach	Qarghayi	100%	DAI	Completed
Darunta Bypass Cobblestone Road, Second Reach	Qarghayi	100%	DAI	Completed
Farman Khil & Jui Daman Canals	Qarghayi	100%	DAI	Completed
Dopi and Langalam Protection wall	Qarghayi	100%	RI	Completed
Char Bagh Canal reconstruction	Qarghayi	100%	RI	Completed
Kalakot and Longalam Canal reconstruction	Qarghayi	100%	RI	Completed
Shamshirabad Flood Protection	Qarghayi	100%	RI	Completed
Kakas Canal Rehabilitation	Qarghayi	0%	RI	Pending due to irrigation season

PROJECT	DISTRICT	PROGRESS	IMPLEMENTER	STATUS
Kanda Canal Rehabilitation	Qarghayi	100%	RI	Completed
Kac Aziz Khan Canal	Qarghayi	85%	RI	On going
Qardi Kac Canal	Qarghayi	70%	RI	On going
Darunta Bypass Cobblestone Road, Third Reach	Qarghayi	28%	DAI	On going
Lara Mora Road Improvement	Qarghayi	2%	DAI	On going
Deh-Zairat Protection wall	Mehtarlam	100%	RI	Completed
Karaho Protection wall	Mehtarlam	100%	RI	Completed
Tergari Protection wall	Mehtarlam	100%	RI	Completed, backfilling on going
Mulayan Protection wall	Mehtarlam	100%	RI	Completed
Shamangal Canal Reconstruction	Mehtarlam	100%	RI	Completed
Pacha Joie Canal	Mehtarlam	100%	RI	Completed
Hayadarkhani Canal Reconstruction	Mehtarlam	100%	RI	Completed
Ghundy Baba Sahib Flood protection wall	Mehtarlam	85%	RI	On going
Qala Shagee flood protection wall	Mehtarlam	93%	RI	On going
Baba Sahib Canal	Mehtarlam	100%	RI	Completed
Abuzai Flood Protection wall	Mehtarlam	83%	RI	On going
Deh-Zairat Omar Zai Village Cobble Stone Road	Mehtarlam	27%	DAI	On going
Khoja Khil Sofla Canal Rehabilitation	Alingar	100%	RI	Completed
Ghunay Nazar Khil Protection wall	Alingar	100%	RI	Completed
Qasaba Protection wall	Alingar	100%	RI	Completed
Bara Kandy and Kuza Kandy Canal Rehabilitation	Alingar	100%	RI	Completed
Purwaie Flood Protection works	Alingar	100%	RI	Completed
Mandul Flood protection works	Alingar	100%	RI	Completed
Nolo Protection wall	Alishing	100%	RI	Completed
Jamshidabad Protection wall	Alishing	100%	RI	Completed
Jamshidabad Protection wall Additional work	Alishing	100%	RI	Completed
Mustafa Kalay Protection Wall	Alishing	100%	RI	Completed
Akhund Sahib Protection Wall	Alishing	100%	RI	Completed
Qardi Salab Canal	Alishing	100%	RI	Completed
Kandi Sahib Canal	Alishing	100%	RI	Completed
Kalay Baya Canal	Alishing	90%	RI	On going

**B. CFW - Kunar Province:** In Kunar, four CFW projects were completed during the reporting period. The total completed projects reached eight and five other remained active through December 31, 2006. So far, 2,022 people have been employed with a cumulative total of 163,685 employment days through December 31, 2006.

**CFW PROJECT STATUS IN KUNAR PROVINCE THROUGH DECEMBER 31, 2006**

PROJECT	DISTRICT	PROGRESS	IMPLEMENTER	STATUS
Dandono Kotgi Canal Intake	Narang	0%	ALP	Cancelled

PROJECT	DISTRICT	PROGRESS	IMPLEMENTER	STATUS
Barnarang Road Repair	Narang	100%	ALP	Completed
Sharalow-Badil Road Repair	Narang	100%	ALP	Completed
Badil Khower Flood Protection	Narang	100%	ALP	Completed
Seend Wala Chawkay Intake	Chawkay	0%	ALP	Cancelled
Dewagal Road Repair	Chawkay	90%	ALP	Stopped/Security
Zarmandi Flood protection	Chawkay	100%	ALP	Completed
Chawkay Khower Flood Protection	Chawkay	100%	ALP	Completed
Nurgal Seend Wala Intake	Nurgal	0%	ALP	Cancelled/replaced with aquaduct and a protection wall)
Seenda Wala Canal Rehabilitation	Nurgal	100%	ALP	Completed, additional work ongoing
Nurgal Aret Road	Nurgal	92%	ALP	On going
Tora Tega Road	Nurgal	92%	ALP	On going
Daag Canal Repair	Khas Kunar	100%	ALP	Completed, additional work ongoing
Tanar Road Rehabilitation	Khas Kunar	100%	ALP	Completed, additional work ongoing
Khas Kunar Middle Road	Khas Kunar	100%	ALP	Completed
Clinic to Hakimabad road	Khas Kunar	100%	ALP	Completed

**C. CFW-Nuristan Province:** During this reporting period ALP/E extended its activities to Nuristan province and started the first Cobblestone road in Noorgram district. To date, 407 people have been employed through CFW, and the accumulated total days worked has reached 21,200.

**D. CFW - Nangarhar Province:** During this reporting period, seven CFW projects were completed bringing the cumulative total to 36 completed projects. Work continued on another 29 active projects in Nangarhar. ALP/E employed 3,314 daily laborers during the reporting period. The total number of employed people reached 11,922 in December 31, 2006. Person employment days were recorded as 155,367, and the cumulative total reached 627,889 employment days from June 2005 through December 31, 2006. Two approved CFW projects are still pending due to security constraints in the Torghar District.



**Opening of Shamshapur Cobblestone Road in Nangarhar**

The Chief of staff of USAID and other visitors from Kabul gathered with the Director of Public Works of Nangarhar to open the completed second section (7km) of Shamshapur Cobblestone Road.

#### CFW PROJECT STATUS IN NANGARHAR PROVINCE THROUGH DECEMBER 31, 2006

PROJECT	DISTRICT	PROGRESS	IMPLEMENTER	STATUS
Jalalabad Wholesale Market	Jalalabad	84%	ALP	On going
Jalalabad City Main Drain	Jalalabad	100%	ALP	Completed
Jalalabad City Road side Drains	Jalalabad	100%	ALP	Completed
Abdian Road Rehabilitation	Behsud	100%	ALP	Completed
Binigah Flood Protection Wall	Behsud	105%	ALP	Completed
Sarmarkhil Erosion Protection	Behsud	100%	ALP	Completed
Spin Jumat Embankment	Behsud	119%	ALP	On going

PROJECT	DISTRICT	PROGRESS	IMPLEMENTER	STATUS
Binigah II Flood Protection Wall	Behsud	50%	ALP	On going
Shamshapur Cobble Stone Road Pilot	Surkh Rod	100%	ALP	Completed
Kakrak Road Improvement	Surkh Rod	98%	ALP	On going
Tatang Nawab Jabar Canal Rehabilitation	Surkh Rod	100%	ALP	Completed
Sarband and Jalawanano Canal Intakes Construction	Surkh Rod	100%	ALP	Completed
Shamshapor-Daronta Road Improvement	Surkh Rod	100%	ALP	Completed
Shamshapur Cobble Stone Road second reach	Surkh Rod	100%	ALP	Completed
Shamshapur Cobble Stone Road Third reach	Surkh Rod	12%	ALP	On going
Ghauchak Cobble Stone Road Improvement	Surkh Rod	42%	ALP	On going
Mana Road Rehabilitation	Hisarak	100%	ALP	Completed
Shana Zawara Road Rehabilitation	Hisarak	100%	ALP	Completed
Sanzai Road	Hisarak	100%	ALP	Completed
Gandomak Road Rehabilitation	Sherzad	100%	ALP	Completed
Toto Road Rehabilitation	Sherzad	100%	ALP	Completed
Ashpan Flood Protection	Sherzad	100%	ALP	Completed
Petlaw Road Rehabilitation	Sherzad	90%	ALP	On going
Kodi Khil Cobble Tone Road	Sherzad	19%	ALP	On going
Surkhab Canal Intakes and Supper Passage Project	Sherzad	21%	ALP	On going
Khwaran Road Rehabilitation	Khogyani	100%	ALP	Completed
Kailagho Road Rehabilitation	Khogyani	100%	ALP	Completed
Khwaza Khil & Malam Khil Road	Khogyani	100%	ALP	Completed
Nemla Flood Protection	Khogyani	86%	ALP	Stopped
Nemla Irrigation	Khogyani	3%	ALP	Approved 30 Aug, 2006/Stopped
Nokor Khil Cobble Stone Road	Khogyani	14%	ALP	On going
Hakimabad Canal Intakes and Retaining Wall	Khogyani	2%	ALP	On going
Garatak & Chardahi Canal Intakes	Chaparhar	100%	ALP	Completed
Garatak Flood Protection Wall	Chaparhar	100%	ALP	Completed
Chardahi Flood Protection Wall	Chaparhar	100%	ALP	Completed
Sholana Flood Protection Wall	Chaparhar	116%	ALP	On going
Dawlat Zai Canal Intake	Chaparhar	100%	ALP	On going additional work
Lawangpur Village Cobble Stone Road	Chaparhar	36%	ALP	On going
Spin Jumat Road Improvement	Chaparhar	2%	ALP	On going
Pekha Flood Protection wall	Achin	100%	ALP	Completed
Deh Sarak canal Intake	Achin	100%	ALP	Completed
Terky Intake and Flood Protection	Nazyan	98%	ALP	On going
Zysar Billage Cobble Stone Road	Nazyan	30%	ALP	On going
Mahsil & Qasaba Kaly Irrigation Reservoir and Erosion Protection	Dur Baba	100%	ALP	Completed

PROJECT	DISTRICT	PROGRESS	IMPLEMENTER	STATUS
Sasobi Irrigation Reservoir & Flood Protection Wall	Dur Baba	100%	ALP	Completed
Torlala Kaly Irrigation Reservoir & Flood Protection	Dur Baba	100%	ALP	Completed
Zakhil Irrigation Canal	Shinwar	100%	ALP	Completed
Zara Sultankhil Protection Wall	Momandara	100%	ALP	Completed
Girdi Ghous Protection Wall	Momandara	100%	ALP	Completed
Basawal Banbaba Flood Protection	Momandara	8%	ALP	Stopped
Guldag Flood Protection Wall	Lal Pur	100%	ALP	Completed
Koz & Bar Bela F. Protection Wall I	Goshta	100%	ALP	Completed with additional work
Koz & Bar Bela F. Protection Wall II	Goshta	100%	ALP	Completed
Koz & Bar Bela F. Protection Wall III	Goshta	100%	ALP	Completed
Bodiali & Soraj Irrigation Rehabilitation of Reservoirs	Kuz Kunar	100%	ALP	Completed
Shega Cobble Stone Road	Kuz Kunar	31%	ALP	On going
Maidanak Road	Spin Ghar	100%	ALP	Completed
Girdi Nawagai Road	Spin Ghar	99%	ALP	On going
Hojoom Kala Chelgazi Intakes	Spin Ghar	80%	ALP	On going
Lakhi Canal Intakes	Spin Ghar	17%	ALP	On going
Inzari Khola Canal Intake	Spin Ghar	32%	ALP	On going
Shangina Yousaf Kas Canal Rehabilitation	Tor Ghar	0	ALP	Suspended/Cancel
Gachway Mirano Road Improvement	Tor Ghar	0	ALP	Suspended/Cancel
Chardehe Cobble Stone Road	Bati Kot	23%	ALP	On going
Pachir Cobble Stone Road	Pachir Wa Agam	31%	ALP	On going
Metrani Village Cobble Stone Road	Kot	17%	ALP	On going

## UPCOMING ACTIVITIES: INFRASTRUCTURE

- Preparing PIFs, budgets, and environmental assessments for the CFW projects planned under AWP2.
- Continuing implementation of the ongoing CFW projects in Nangarhar, Laghman, Kunar and Nuristan.
- Completion of the CFW program implemented by Relief International (RI) in Laghman province.
- Tendering and award of rehabilitation contracts for other approved PIP projects (road and bridge improvements) in Nangarhar and Laghman provinces.
- Continuing the program of Quality Assurance for ongoing cobblestone roads.
- Completion of all remaining work for rehabilitation of the Jalalabad Wholesale Market.
- Carrying out surveys as required for remaining PIP projects.
- Training of skilled tradesmen at CTTC.
- Regular meetings with IRD, CTTC, RRD, PW, Irrigation departments, and PDC meetings.
- Planting trees along the completed road projects and protection walls carried out.
- Internship training of 10 senior year engineering students from the University of Nangarhar.

### **3.4. GENDER AND MICRO – ENTERPRISE (GME) DEVELOPMENT ACTIVITIES**

ALP/E develops programs specifically targeting women and other vulnerable groups and promoting women and disabled in business in the Eastern Region. In addition, the Gender and Micro-enterprise (GME) Unit is responsible for mainstreaming gender in other ALP/E's program areas such as agribusiness, private sector and infrastructure. By educating women through business training and technical assistance, ALP/E provides alternatives to poppy production for women.

#### **3.4.1. MICRO-ENTERPRISE RADIO PROGRAM**

To motivate women to improve their situation, inform them about existing business support programs and publicize the GME projects, ALP/E launched a weekly gender radio talk-show. The first program aired on October 1, 2006. The topics during this period included: business for women according to Islam and Bibi Khadaija, the Prophet's wife; overview of the self help groups; interviews with business women; and credit opportunities.

#### **3.4.2. WOMEN'S NURSERY PROGRAM**

ALP/E conducted a series of three-day trainings on replanting, transplanting, fertilizing and watering for the Forestry Nursery Program's beneficiaries in Nangarhar and Laghman. The saplings will be ready for replanting in the upcoming reporting period. The GME Unit is working with Infrastructure Unit regarding site selection and landscaping.

#### **3.4.3. WOMEN'S PRIVATE SECTOR INITIATIVE**

During the reporting period, the Kaweyan Business Development Services (KBDS)'s team finalized its women business survey report and released the findings. The survey was conducted with the assistance from ALP/E to gauge the situation of female entrepreneurs in Nangarhar, Laghman and Kunar provinces. The KBDS surveyed 300 businesswomen across the three provinces. Despite certain limitations caused by security in the region, the study sheds light on the needs and constraints of women-owned businesses. Areas where women-entrepreneurs require support are: basic business management, bookkeeping, marketing and access to financing. The GME is incorporating these findings into the planning for its future activities.

#### **3.4.4. MAINSTREAMING GENDER**

ALP/E's Infrastructure and GME staff organized the opening ceremony of the Binigah, Behsud project. The GME staff also selected female cooks for the new CFW sites and recruited ten female laborers for the construction of the Jalalabad Fruit and Vegetable Wholesale Market. More than 20 women found work as daily laborers making stirrups on the Jalalabad Wholesale Market's construction site.



**Woman works in Jalalabad Wholesalers Market**

As part of its teamwork with the Agribusiness Unit, the Gender and Micro-enterprise Development Unit trained 38 women from Surkhrud, Behsud, and Bati Kot in the Vegetable Nursery Program. During the reporting period, the Surkhrud team also assisted in organizing a produce shipment from eastern Afghanistan to the UAE.

#### **3.4.5. SMALL HOLDER LIVESTOCK MANAGEMENT PROGRAM**

ALP/E-supported four female veterinary workers trained 1,100 women from Laghman and Nangarhar in the areas of livestock nutrition and management, identification and treatment of common diseases, and practices to improve productivity. The trainers will shortly begin a similar program in Kunar.

### 3.4.6. VEGETABLE PRODUCTION PROGRAM

The GME unit is working closely with ALP/E's Natural Resource Management (NRM) Specialist to develop a vegetable seedling production work plan. During this quarter, five sites were identified in Kama and Dara-I-Noor districts, and five groups, each consisting of eight women, were formed. As part of this effort, three training sessions were conducted at the vegetable seedling sites, and two more three-day programs are scheduled.

### 3.4.7. HANDICRAFTS

ALP/E facilitated the participation of a group of five women from the Eastern Region in the Rural Handicraft Exhibit, which took place in New Delhi, India on November 14-27. During the tradeshow, the Afghan participants held negotiations with more than 20 exporters and received several test orders for hand-embroidered shawls, jackets, wall hangers and shirts. The products presented by the ALP/E-supported craft-makers received a great deal of attention among the Indian news media. This event constitutes an important step toward the promotion of handicrafts from the Eastern Region in the international marketplace. Afghan handicraft producers are exploring the possibility of opening a permanent showroom in Delhi, developing a professional portfolio of their crafts, and building on the contacts established at the trade fair.



Afghan Ambassador to India visits Eastern Region's booth at the Rural Handicraft Exhibit in New Delhi

While in New Delhi, the handicraft manufacturers also had an opportunity to attend the Regional Business Conference, where they were greeted by President Karzai and other members of the Afghan delegation. Impressed with the achievements of their compatriot women entrepreneurs, high-ranking officials underscored the national government's commitment to supporting Afghan handicraft industry.

## UPCOMING ACTIVITIES

- Providing business skills, mentoring and marketing help to 132 SHGs in Nangarhar, Laghman and Kunar.
- Planting saplings in infrastructure sites, local girl schools, and Directorate of Women's Affairs.
- Finalization of plans to support the local handicraft industry.
- Helping local handicraft producers to introduce new, fresh, innovative, market driven product designs.
- Transplanting more than 250,000 high-value vegetable saplings into ALP demo plots.
- Establishing 200 semi-commercial women-owned poultry farms in Nangarhar, Laghman and Kunar.
- Reviewing the feasibility of a medium-sized poultry feed mill in Nangarhar Province.
- Facilitating the establishment of 20 women-owned fishery farms in Nangarhar, Laghman and Kunar.
- Providing six months vocational training for 90 disabled and vulnerable women of Laghman in collaboration with Afghan Blind Migration (ABM).
- Conducting a feasibility study for beekeeping in Shinwar, Achin and Deh Bala districts of Nangarhar.

## 3.5. INSTITUTIONAL CAPACITY DEVELOPMENT ACTIVITIES

ALP/E promotes the establishment of new trade associations and strengthens the capacities of existing ones by emphasizing their institutional accountability and encouraging the integration of a private sector vision into association activities. ALP/E-supported organizations include the Jalalabad Fruit and Vegetable Wholesalers Association, Agri-Inputs Suppliers Association, Vegetable Exporters Association, Regional Poultry Producers Association, Nursery Producers Association and Handicraft Marketing Association. Other activities of ALP/E's Institutional Development Unit include building the capacity of regional and provincial governmental organizations.

### 3.5. I. SUPPORT TO ASSOCIATIONS

During the quarter, members of the Jalalabad Wholesaler Association, Afghan Agricultural Development Association, Livestock Development Association and Input Suppliers Association continued the ALP/E-

sponsored computer and English language training. The Carpet Producers Association's representatives took part in the Rural Handicraft Exhibit in New Delhi where they received an order for 500 prayer rugs. ALP/E is



Presentation to the Laghman handicraft group on benefits of association formation

currently assisting the Association to work out the production and delivery details of the order. The Institutional Development team also assisted members of the Carpets Producers Association to attend the Christmas exhibition U.S. Embassy where they sold a number of carpets. Additionally, ALP/E is helping a female member represent the Carpet Producers Association at the upcoming Afghan Carpet Exhibit in New York.

ALP/E also started Office Management training for 15 members of various trade associations including Jalalabad Fruit and Vegetable Wholesalers, Agri-Input Suppliers, Livestock Development and Carpet Producers. This training will improve the ability of the associations to support their members.

### 3.5.2. SUPPORT TO DIRECTORATES OF AGRICULTURE

In response to a request from the Directorates of Agriculture of Nangarhar, Laghman and Kunar, the Institutional Capacity Building team started computer and English language courses for their staff. A four-day Project Planning Training for Nangarhar and Laghman provinces was also successfully completed.

### 3.5.3. SUPPORT TO WOMEN'S AFFAIRS DIRECTORATES

In response to a request from the Directorates of Women's Affairs (DoWA) of Nangarhar, Kunar and Laghman, in early November, 2006 ALP/E began English language and computer classes for directorate employees. In addition, ALP/E, in conjunction with KAWAYAN Training Institute developed the curriculum and conducted a proposal writing training for senior staff of the Nangarhar Women Affairs Directorate.



Proposal writing training at the Nangarhar Women's Affairs Directorate

ALP/E assisted the Ministry of Women's Affairs to develop the concept for the Eastern Region's Women's Magazine. The Institutional Capacity Development staff facilitated the gathering of reports and data for the first issue from various sources, including the Nangarhar Public Health Hospital, Tajrobawi Girls' High School, Alayi High School, Bebi Zinab High School, Bibi Hawa High School and Sawadi Hayati Girls School. The magazine is expected to be ready for printing in early 2007.

### UPCOMING ACTIVITIES: GENDER AND MICRO-ENTERPRISE

- In collaboration with DoWA, providing vocational training in wool weaving for 75 Nuristani women.
- Organizing roundtable discussions between associations and government officials.
- Organizing a study tour to Pakistan for the Eastern Region Livestock Development Association.

- Assisting the Eastern Region Fruit Growers Association with opening a bank account, training and registering with the Ministry of Justice.
- Continuing English classes, computer training and other skill training for selected associations.
- Providing office equipment to Nuristan's Women's Affairs Directorate.
- Installing solar power systems for computers in Kunar, Laghman, Nangarhar and possibly Nuristan.
- Organizing and contributing to International Women's Day to be held on March 8 in Kunar, Laghman, Nangarhar and Nuristan.
- Assisting with the printing and distribution of *Women's Magazine* for DoWA.

### **3.6. COORDINATION**

ALP/E continued to coordinate its efforts with regional, provincial and local governments and other organizations based in the Eastern Region. During the reporting period, ALP/E's representatives attended the fifth Poppy Elimination Program (PEP) meeting in Nangarhar Province, which brought together government officials, community representatives, members of the Provincial Council, PRT, IFHOPE, PAL GTZ, RTV, WFP, ACBAR, and other NGO representatives. ALP/E also participated in the provincial coordination body (PCB)'s meeting held at the Governor's house in Laghman. Other participants included directors of government departments, UNICEF, UNHCR, UNAMA, WHO, DACAAR, RI, PRT, PAL GTZ, FAO, IFHOPE, MI, and UNMACA. Additionally, ALP/E representatives attended the provincial coordination body (PCB)'s meeting in Kunar.

#### **UPCOMING ACTIVITIES: COORDINATION**

- Participation in PDC meetings in Nangarhar, Laghman, Kunar and Nuristan Provinces.
- Participation in Agriculture and Public Work TWG Meetings in Nangarhar, Laghman, Kunar and Nuristan.
- Arranging meetings with Governors and Deputy Governors for COP and Heads of departments.
- Participation in PEP, ACBAR, Counter-Narcotic Trust Fund and other official meetings.
- Distributing Biweekly, Quarterly and other reports to line ministry departments and other GOA officials.
- Receiving Community Elders in ALP/E office and arranging meetings with Heads of departments.
- Participation in Provincial Council Meetings in Nangarhar, Laghman, Kunar and Nuristan.
- Dealing with official letters from government departments and request letters from communities.

### **3.7. PROGRAM MANAGEMENT AND ADMINISTRATION**

#### **3.7.1. OPERATIONS AND PROGRAMMING**

During the quarter, the Operations and Programming Unit arranged the transportation of 1,913 tons of wheat seeds and 5,740 tons of fertilizers distributed in Kunar, Nuristan, Laghman and Nangarhar. Several new administrative and technical staff members were hired for ALP/E. Additionally, security, Lotus Note and TAMIS training was provided to unit's employees. Construction materials for CFW projects were purchased through bidding process. ALP/E's 18 armed guards and 4 other security staff were handed over to an international security company, Edinburgh International.

Highlights of Operations and Programming Unit's activities:

- Hired 5 Agribusiness Field Managers, 3 Field Technicians, 1 Annual Crops Officer, 3 Site Engineers, and 1 Translator.
- Completed annual performance evaluations for staff that completed a year of service.
- Distributed the TIMER (Annual Crops) and Perennial Horticulture RFPs to potential offerors.
- Shifted 200,000 bags of fertilizer and wheat seed from Farm Hada warehouses to Nangarhar, Kunar, Laghman and Nuristan.
- Purchased and dispatched to the project sites, different types of construction materials and tools for various CFW projects.
- Rented several types of machinery for different CFW projects in all 4 provinces.

- Conducted TAMIS and Lotus Notes training for the new staff and security training for armed guards and drivers.
- Received 15 new computers for the Agribusiness Departments in Kunar, Laghman, and Nangarhar.
- Created and translated the ALP/E video in 3 languages.
- Translated into Pashto various staff contracts, leases, policies, executive summaries and accomplishment reports.
- Biweekly reports composed, printed and distributed to various Departments.
- Prepared anti poppy agreements.
- Submitted the final copy of the KAMA DBST Road project for approval to USAID.

## **UPCOMING ACTIVITIES: OPERATIONS AND PROGRAMMING**

- Hiring a Public Outreach and Information Officer.
- Preparing for the Kama Road work.
- Providing a Tax Identification Number for staff and DAI.
- Improving the IT connection for the Kabul Office.
- Conducting Management, English Language, Computer, TAMIS and Lotus Notes training.
- Maintaining the ALP/E.
- Compiling monitoring and evaluation data for USAID and ALP/E staff to gauge progress and to provide information for strategic decision making.
- Updating the inventory in TAMIS and physical inventory of all four facilities.
- Distribution of biweekly reports to relevant departments.
- Dispatching and distributing agribusiness inputs for 30 target districts in the provinces of Nangarhar, Laghman, Kunar and Nuristan.
- Providing the Departments of Agriculture of Nangarhar, Kunar and Laghman with Solar power systems.

### **3.7.2. MONITORING AND EVALUATION**

ALP/E recognizes the importance of Monitoring and Evaluation (M&E) in assessing progress and reporting on its program impact. During this quarter, in response to the RIG audit, ALP/E took steps to further strengthen M&E by reviewing the systems, the targets and the indicators. Emphasis was placed on both quantifying impact and assessing qualitative aspects of project implementation. This upgrading of the M&E systems will continue through first quarter of 2007.

#### **A. PROJECT MONITORING**

The M&E Unit continued to spot-monitor active and completed CFW and agriculture projects in Laghman, Kunar and Nangarhar. The findings and recommendations are shared and followed up with the concerned technical Units. The CFW monitoring missions focused on: 1) physical progress (assessing whether planned physical progress was achieved); 2) financial disbursements (laborers working on cash-for-work projects were directly interviewed to determine whether they have been paid properly for work completed in CFW projects plus project financial data was reviewed with the ALP/E finance section and cross checked with labor attendance sheets and payroll); and 3) persons employed and employment days (individual laborers on each group were counted in spot checks to cross-check their physical attendance with the current record).

During the quarter, the M&E section successfully completed the initial monitoring of ALP/E's 2006 Fall Wheat Seed and Fertilizer Distribution. This has been a high profile program oriented to increase self-food reliance during the winter and offer an alternative to poppy production by providing 76,000 farmers in Kunar, Laghman, Nangarhar and Nuristan with enough certified seed and fertilizer to plant one jerib of high-yielding wheat varieties.

#### **B. GIS AND MAPPING**

ALP/E is committed to removing the technical confusion often associated with spatial planning. It provides staff members with user-friendly applications and training to facilitate their understanding of Geographic Information Systems (GIS). The M&E/GIS unit conducted the following activities:

- Successfully completed the survey, data integration, and mapping of 455 roads, totaling 2,600 Km in length in Nangarhar. The M&E GIS team briefed the provincial directors of RRD, Irrigation and Public Works on the findings and importance of the data collected by the Nangarhar Road Inventory Team.

- Collected infrastructure projects (CFW, PIP) field GPS Data and updated relevant shape files. The team developed and processed field GPS data, shape files, and prepared “MAP OF WORKS” for: Shinwar Kataly road repair, Qarghayi Kamal Pur road repair, Shinwar Spin khwar Flood Protection wall project, Batikot Chardhi Cobblestone road project and Surkh Rod Miralam Canal rehabilitation project.
- Continued work with Fruit Marketing Program (FMP) to collect, track and analyze orchards data including waypoints and polygons using the 2004 UNODC land classification for poppy.
- Made significant progress in downloading, cleaning, integrating, and analyzing ERODP GPS survey data. Work also continued with the NRIT to help them keep track of standard data collection, downloading, and cleaning field GPS data and sharing the information.
- Conducted GPS data handling and management training sessions for all of ALP/E’s technical units.
- Generated several maps including district level security risk maps, CFW and other infrastructure maps.

### C. GEOBASE UPDATE

During the reporting period, the M&E team updated GeoBase for 165 ALP/E activities including Infrastructure, Agribusiness, Gender and Micro-enterprise and Private Sector Development activities. Particular attention was paid to the budget, disbursements, detailed activity location, and detailed activity metrics and progress of the ongoing CFW projects in Nangarhar, Laghman, Kunar and Nuristan provinces. In addition, project GPS grids were entered to track the geographical locations of the projects.

### D. CAPACITY BUILDING

The M&E Section conducted four capacity building trainings for ALP and government staff and sub-contractors. The trainings focused on field monitoring techniques, data collection and reporting processes.

### UPCOMING ACTIVITIES: MONITORING AND EVALUATION

- Continue field monitoring of all ongoing and completed CFW projects
- Continue updating GeoBase
- Conduct GIS capacity building training for ALP and GoA across the region
- Review M&E systems and targets, and incorporate necessary changes
- Streamline the data collection process for all indicators and assist program managers in tracking.

### 3.7.3. PROGRAM SECURITY

Security situation in the Eastern Region remained tense during the reporting period. The AGEs/insurgents activities increased throughout the region, specifically in Kunar (Nari, Marawara and Pech Districts), and in Laghman (Alingar, Alishang and Dawlat Shah Districts). The risk of VBIED/BBIED attacks increased particularly in Nangarhar and Kunar Provinces, with reports of attackers targeting government and security positions. Additionally, a special warning was received for Jalalabad City, the Jalalabad–Torkham highway and the Jalalabad-Asadabad highway. Provincial security updates follow:

- The security situation in the Province of **Nangarhar** was relatively tense with thirteen incidents noted during the reporting period in Jalalabad. The infiltration of a new group of 25 AGEs/ Insurgents reportedly crossed the Pakistani border through the eastern districts to target government installations in the Province. The infiltration of a group of 100 AGEs through Rodat district was also reported. This group has been tasked to conduct attacks against government structures in the area. In addition, small arms fire on an NGO vehicle on the Kabul-Jalalabad Road led to a review of road missions from Jalalabad to Kabul.
- The security situation in **Laghman** was relatively calm with three incidents reported during the period. These incidents were reported in Qarghai, Alingar and Alishang districts with RPG rounds and BM-12 rockets. ALP/E continues to restrict international staff from traveling to Dawlat Shah, Alingar and Alishang Districts of Laghman Province as the situation is uncertain with continued reports of insurgents’ movements and infiltration. However, operations are going smoothly in other areas.

- The security situation in **Kunar** remained tense with fifteen incidents reported during the period. The province was assessed as being a high risk area for the aid community due to the presence of AGEs, and regular IED, RCIED and rocket attacks against government and Coalition Forces (CF). It was widely believed that Insurgents had almost complete freedom of movement in the border areas and reports indicate a group of suicide attackers entered Kunar Province to target CF, ANSF and International aid workers. ALP/E operations continued in the four districts of Narang, Nurgal, Khas Kunar and Chawkay during the reporting period.
- The CF operation in Eastern and Central **Nuristan** continued, to destroy AGE hideouts in the remote areas of Nuristan and clear the area of AGEs.

## UPCOMING ACTIVITIES

- Continue to provide perimeter and transit security for all ALP/E staff.
- Enhance security information collection and analysis.
- Adopt low-profile strategies for the high risk area missions.
- Update security database and conduct assessments as required.
- Continue monitoring security situation of whole region.
- Provide additional security training/awareness for all staff.
- Change all security staff contracts from DAI to Edinburgh International Security Company.

### Summary of this Quarter's Short-Term Technical Assistance (STTA)

NAME	TITLE	ACTIVITY	STATUS
Conrado Camacho	Cobblestone Training Advisor	Training for cobblestone roads	Completed
Anne Williams	Business Training Advisor	Business skills training and Private Sector Development	Completed
Alia Afshar	ALP/E Associate	Operational and technical support	Completed
Alvaro Pacheco	Agribusiness Advisor	Agribusiness assessment and technical assistance	Completed
Danilo Benavides	Agribusiness Advisor	Agribusiness assessment and technical assistance	Completed
David Love	Livestock Advisor	Slaughterhouse assessment	Completed
Gleyn Bledsoe	Food Safety Consultant	Food safety assessment	Completed
Bernard Twinowigoshio	Natural Resource Management Consultant	Conduct Survey for Forestry Nursery Effectiveness	Completed
Olga Zatepilina	Public Outreach and Communication Advisor	Design a strategic communications plan for 2007, streamline the reporting process, develop publicity materials	Completed

# REQUIRED USAID PERFORMANCE DATA

## Annex-I ALP/E Activity Level Indicators<sup>1</sup> Reporting Period October- December, 2006

Indicator	Unit of Measure	Added (Quarterly)	Target (Life of Project)	Total (To date)	Target (FY 07)	Target (FY 08)	By Province (To date)			
							N	L	K	Nu
Total Kms irrigation and drainage canals and karezes ALP	# km	1.9	300	153	300	300	105	32.09	15	0
ALP Kms. of rural roads repaired in poppy regions	# km	15.6	400	173.65	400	400	122	7.15	40.7	3.8
ALP/E Hectares of improved irrigation as a result of ALP infrastructure works	# hec	37	24,000	12,655	24,000	24,000	4,922	6,861	872	-

Indicator	Unit of Measure	Added (Quarterly)	Target (Life of Project)	Total (To date)	Target (FY 07)	Target (FY 08)	By Province (To date)				By Gender (To date)	
							N	L	K	Nu	Male	Female
ALP/E Amount paid in CFW in AL programs	USD	1,203,870	8,250,363	5,413,540	8,250,363	8,250,363	2,447,236	2,257,623	648,226	60,455	5,179,963	233,577
ALP/E Afghans paid through CFW salaries	#	4,921	45,000	24,619	45,000	45,000	11,922	10,268	2,022	407	23,538	1,081
ALP/E Total labor days for CFW	#	332,145	1,800,000	1,402,007	1,800,000	1,800,000	627,889	589,233	163,685	21,200	1,343,332	58,675
Afghans trained in business skills	#	1,926	7,000	4,053	5,200	7,000	2,872	826	335	20	1,280	2,773
Farmers trained in agricultural practices in targeted poppy provinces under ALP	#	1,711	175,000	96,817	155,000	175,000	55,774	26,013	15,030	-	95,284	1,533
Farmers receiving seed and fertilizer	#	76,945	177,961	169,901	177,961	177,961	100,261	37,800	27,840	4,000	169,901	-

<sup>1</sup> The tables show figures of ALP project.

# REQUIRED USAID PERFORMANCE DATA

## Annex-II ALP/E Activity Level Indicators<sup>2</sup> Reporting Period October- December, 2006

Indicator	Unit of Measure	Added (Quarterly)	Target (Life of Project)	Total (To date)	Target (FY 07)	Target (FY 08)	By Province (To date)			
							N	L	K	Nu
Total Kms irrigation and drainage canals and karezes ALP	# km	1.09	2581	2433.09	2581	2581	2386	32.09	15	0
ALP Kms. of rural roads repaired in poppy regions	# km	15.65	548	321	548	548	270	7.15	40.7	3.8
ALP/E Hectares of improved irrigation as a result of ALP infrastructure works	# hec	37	233,060	125,715	233,060	233,060	117,982	6,861	872	-

Indicator	Unit of Measure	Added (Quarterly)	Target (Life of Project)	Total (To date)	Target (FY 07)	Target (FY 08)	By Province (To date)				By Gender (To date)	
							N	L	K	Nu	Male	Female
ALP/E Amount paid in CFW in AL programs	USD	1,203,870	18,092,363	15,255,903	18,092,363	18,092,363	12,289,599	2,257,623	648,226	60,455	13,556,639	1,699,264
ALP/E Afghans paid through CFW salaries	#	4,921	179,000	158,619	179,000	179,000	145,922	10,268	2,022	407	137,526	21,093
ALP/E Total labor days for CFW	#	332,145	4,767,708	4,369,715	4,767,708	4,767,708	3,595,597	589,233	163,685	21,200	3,869,100	500,615
Afghans trained in business skills	#	1,926	7,000	4,053	5,200	7,000	2,872	826	335	20	1,280	2,773
Farmers trained in agricultural practices in targeted poppy provinces under ALP	#	1,711	175,000	96,817	155,000	175,000	55,774	26,013	15,030	-	95,284	1,533
Farmers receiving seed and fertilizer	#	76,945	177,961	169,901	177,961	177,961	100,261	37,800	27,840	4,000	169,901	-

<sup>2</sup> The tables show aggregated figures of both ALP and AINP project.

Indicator	Unit of Measure	Added(Quarter)	Target (Life of Project)	Total (To Date)	Target (FY 07)	Target (FY 08)	By Province (To Date)					
							Nangarhar	Laghman	Kunar	Nu		
Cluster (economic area) that meets standards	%	0	100	30	70	100	-	-	-	-		
Indicator	Unit of Measure	% Change (Quarter)	Target (Life of Project)	Total(To Date)	Target (FY 07)	Target (FY 08)	By Province (To Date)					
							Nangarhar	Laghman	Kunar	Nu		
Change in production of selected high value (three major) agricultural crop	USD	438,726 <sup>3</sup>	400,000	438,726	200,000	400,000	283,715	66,787	68,463	19,760		
Indicator	Unit of Measure	Added (Quarter)	Target (Life of Project)	Total (To Date)	Target (FY 07)	Target (FY 08)	By Province (To Date)					
							Nangarhar	Laghman	Kunar	Nu		
Hectares devoted to licit agricultural production	# (% of total arable land)	16,931	50,000	44,465	35,000	50,000	27,908	7,671	5,683	1,600		
Indicator	Unit of Measure	Added (Quarter)	Target (Life of Project)	Total (To Date)	Target (FY 07)	Target (FY 08)	By Province (To Date)				By Gender (To Date)	
							Nangarhar	Laghman	Kunar	Nu	Male	Female
Full-time jobs created through the expansion of licit activities	#	2,792	17,000	10,533	12,500	17,000	2,000	572	170	50	8,013	2,520
Seasonal (non-CFW) employment created through the expansion of licit activities	#	1,697	10,000	2,279	7,500	10,000	1,507	397	295	80		

<sup>3</sup> Crops planted during this season will be harvested in June 2007 (preliminary estimates based on yield increase alone)

## **Basis for estimates**

### **Change in production of selected high value (three major) agricultural crops**

These figures are based on:

**WHEAT= area planted through the WSP \* [average yield in the region (MT/ha) ] \* [avg price per MT for the period June-Sep (when most people sell)] \* 0.15. In this case we are assuming a 15% in yield attributable to the project...since the indicator requires "change", we only claim the 15% increase. There is a foot note indicating that this is an estimate subject to verification in June**

**FRUIT= Actual total sales multiplied by 0.22 which is the average price increase measured from the FMP activities**

**VEGS= Actual areas planted under ALP programs multiplied by average prices**

### **Hectares devoted to licit agricultural production**

**Actual areas planted to vegetables, wheat and fruit crops based on records from Vegetable program, WSP and FMP. Our records indicate the distribution per province.**

### **Full time jobs created through the expansion of licit activities**

**Estimation based on extrapolation from production and marketing survey (farmers + wholesalers)**

**Agriculture. 1 hectare = 0.25 FT job**

**Agricultural Trade: 1 FT job for every US\$250,000 increase in agricultural output**

**Gender: actual (SHG + Forestry nurseries + Vegetable nurseries)**

**Annex III: ALP/E Program Activities as of December 31, 2006**

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
<b>AGRIBUSINESS</b>								
1	NVDA Olive Pruning	Nangarhar	100%	100%	DAI	21-Feb-06	13-Mar-06	Completed
2	Farmers Training (TOT)	Nangarhar	100%	100%	DAI	28-Jan-06	9-Feb-06	Completed
3	Traders (Assemblers) Training	Nangarhar	100%	100%	DAI	20-Feb-06	23-Feb-06	Completed
4	Wholesalers training	Nangarhar	100%	100%	DAI	11-Feb-06	12-Feb-06	Completed
5	Influenza Training(TOT)	Nangarhar	100%	100%	DAI	27-Mar-06	28-Mar-06	Completed
6	Radio Program-Farmers Interview	Nangarhar	100%	65%	DAI	12-Feb-06	15-Jun-07	Ongoing
7	Establishment of Vegetable Wholesalers Association	Nangarhar	100%	100%	DAI	16-Feb-06	12-Mar-06	Completed
8	Orchard Survey	Nangarhar	100%	100%	DAI	3-Apr-06	18-Apr-06	Completed
9	Packaging distribution	Nangarhar	100%	100%	DAI	14-Apr-06	20-Apr-06	Completed
10	Smallholder Livestock Management Program	Nangarhar	100%	15%	DAI	1-May-05	1-May-07	Ongoing
11	Training for Commercial Nursery Owners	Nangarhar	100%	25%	DAI	1-May-06	30-Dec-07	Ongoing
12	Training for Female Nursery Owners	Nangarhar	100%	35%	DAI + RI	1-Apr-06	30-Dec-07	Ongoing
13	Forest Incentives for Livelihoods Diversification (FleLD)	Nangarhar	100%	5%	DAI	1-May-06	30-Dec-07	Ongoing
14	MIS (Market Information System)	Nangarhar	100%	50%	DAI&DoA	6-Mar-06	31-Dec-08	Ongoing
15	Eastern Region Orchards Development Program	Nangarhar	100%	40	IF Hope	5-Jul-05	14-Feb-09	Ongoing
16	Training for Afghanistan Regional Agricultural Quality Inputs	Nangarhar	100%	100	DAI			Completed
17	Agriculture Trade Fair, 2006	Nangarhar	100%	100	DAI			Completed
18	Agricultural Marketing Production Support Program	Nangarhar	100%	100%	DAI	15-Dec-05	15-Aug-06	Completed
19	Adaptive Research Technology Dissemination and Development of Seed Supply System	Nangarhar	100%	5%	ICARDA	5-Dec-06	31-Dec-08	Subcontract approval
20	Input Supply Support Program	Nangarhar	100%	97%	DAI	5-Sep-06	1-Jul-07	Ongoing
21	Intercropping Program for ERODP Beneficiaries	Nangarhar	100%	100%	DAI	6-May-06	6-Jun-06	Completed

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
22	Fruit Marketing Program	Nangarhar	100%	35%	DAI	6-May-06	31-Dec-08	Ongoing
23	Fall Wheat Seed and Fertilizer Distribution Program	Nangarhar	100%	100%	DAI&DoA	1-Jul-06	30-Nov-06	Completed
24	Eastern Region Livestock Development initiatives	Nangarhar	100%	5%	DAI	6-Jun-06	31-Dec-08	Ongoing
<b>CFW – INFRASTRUCTURE</b>								
1	Shamshapur Road – 11km	Nangarhar	100%	ongoing	DAI	February	6-Dec	Work carried-out under CFW
2	Wazir Tatang Causeway	Nangarhar	100%	0%		6-Aug	6-Nov	Work to be tendered
3	Shamshapur Cobble Stone Road Pilot	Nangarhar	100%	100%	DAI	31-Jan-06	10-May-06	Completed
4	Kakrak Road Improvement	Nangarhar	100%	92%	DAI	29-May-06	29-Aug-06	Ongoing
5	Tatang Nawab Jabar Canal Rehabilitation	Nangarhar	100%	100%	DAI	6-Jun-06	6-Sep-06	Completed
6	Sarband and Jalawanano Canal Intakes Construction	Nangarhar	100%	100%	DAI	6-Jun-06	6-Sep-06	Completed
7	Shamshapur-Daronta Road Improvement	Nangarhar	100%	100%	DAI	8-May-06	8-Aug-06	Completed
8	Shamshapur Cobble Stone Road second reach	Nangarhar	100%	100%	DAI	14-May-06	14-Sep-06	Completed
9	Shamshapur Cobble Stone Road Third reach	Nangarhar	100%	12%	DAI	13-Nov-06	13-Apr-07	Ongoing
10	Ghauchak Cobble Stone Road	Nangarhar	100%	42%	DAI	5-Oct-06	20-Feb-07	Ongoing
11	Metrani Cobble Stone	Nangarhar	100%	17%	DAI	26-Nov-06	26-Feb-07	Ongoing
12	Rodat Road - 12.3 km	Nangarhar	100%	0%	PIP	6-Aug	7-Mar	Design/ BOQ completed and technical feasibility report is being prepared
13	Kama DBST Road - 14.6 km	Nangarhar	100%	10%	PIP	6-Aug	7-Apr	Approved by USAID, tender issued
14	Gardab Irrigation	Nangarhar	100%	100%	DAI	2005	21-Feb-06	Completed
15	Khwaran Road Rehabilitation	Nangarhar	100%	100%	DAI	12-Mar-06	27-Jun-06	Completed
16	Kailagho Road Rehabilitation	Nangarhar	100%	100%	DAI	12-Mar-06	26-Jun-06	Completed
17	Khwaza Khil & Malam Khil Road	Nangarhar	100%	100%	DAI	7-Jun-06	10-Aug-06	Completed
18	Nemla Flood Protection	Nangarhar	100%	83%	DAI	28-Jun-06	30-Oct-06	Ongoing
19	Nemla Irrigation	Nangarhar	100%	3%	DAI	TBD	TBD	Approved 30 Aug, 2006
20	Sherzad to Hesarak Road	Nangarhar	30%	0%	DAI	6-Sep	7-Mar	Design ongoing.
21	Gandomak Road Rehabilitation	Nangarhar	100%	100%	DAI	13-Mar-06	27-Jun-06	Completed
22	Toto Road Rehabilitation	Nangarhar	100%	100%	DAI	12-Mar-06	29-Jun-06	Completed

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
23	Ashpan Flood Protection	Nangarhar	100%	100%	DAI	20-Mar-06	8-Jun-06	Completed
24	Petlaw Road Rehabilitation	Nangarhar	100%	90%	DAI	8-Jun-06	8-Sep-06	Ongoing
25	Mana Road Rehabilitation	Nangarhar	100%	100%	DAI	12-Mar-06	29-Jun-06	Completed
26	Shana Zawara Road Rehabilitation	Nangarhar	100%	100%	DAI	12-Mar-06	28-Jun-06	Completed
27	Sanzai Road	Nangarhar	100%	100%	DAI	2-Jul-06	12-Sep-06	Completed
28	Sherzad to Hesarak Road	Nangarhar	30%	0%	DAI	6-Sep-06	7-Mar-07	Design ongoing
29	Bodiali & Soraj Irrigation Rehabilitation of Reservoirs	Nangarhar	100%	100%	DAI	25-Apr-06	13-Jul-06	Completed
30	Zakhil Irrigation Canal	Nangarhar	100%	92%	DAI	25-Jun-06	5-Sep-06	Ongoing
31	Garatak & Chardahi Canal Intakes	Nangarhar	100%	100%	DAI	6-May-06	6-Aug-06	Completed
32	Garatak Flood Protection Wall	Nangarhar	100%	100%	DAI	30-May-06	10-Sep-06	Completed
33	Chardahi Flood Protection Wall	Nangarhar	100%	86%	DAI	30-May-06	15-Mar-07	Ongoing
34	Sholana Flood Protection Wall	Nangarhar	100%	96%	DAI	30-May-06	15-Mar-07	Ongoing
35	Dawlat Zai Canal Intake	Nangarhar	100%	109%	DAI	6-May-06	6-Aug-06	Completed
36	Lawang Pura Cobble Stone Road	Nangarhar	100%	36%	DAI	1-Oct-06	31-Jan-07	Ongoing
37	Spin Jumat Road Improvement	Nangarhar	100%	2%	DAI	24-Dec-06	30-Mar-07	Ongoing
38	Pekha Flood Protection wall	Nangarhar	100%	100%	DAI	22-Dec-05	27-Jun-06	Completed
39	Deh Sarak canal Intake	Nangarhar	100%	100%	DAI	9-Sep-06	17-Nov-06	Completed
40	Terky Intake and Flood Protection	Nangarhar	100%	98%	DAI	5-Jul-06	5-Mar-07	Ongoing
41	Mahsil & Qasaba Kaly Irrigation Reservoir and Erosion Protection	Nangarhar	100%	100%	DAI	16-Apr-06	12-Jul-06	Completed
42	Sasobi Irrigation Reservoir & Flood Protection Wall	Nangarhar	100%	100%	DAI	16-Apr-06	20-Jul-06	Completed
43	Torlala Kaly Irrigation Reservoir & Flood Protection	Nangarhar	100%	100%	DAI	27-Jun-06	5-Sep-06	Completed
44	Zara Sultankhil Protection Wall	Nangarhar	100%	100%	DAI	21-Mar-06	28-May-06	Completed
45	Girdi Ghous Protection Wall	Nangarhar	100%	100%	DAI	4-Apr-06	5-Jul-06	Completed
46	Basawal Banbaba Flood Protection	Nangarhar	100%	8%	DAI	5-Aug-06	30-Nov-06	Ongoing
47	Guldag Flood Protection Wall	Nangarhar	100%	100%	DAI	4-Apr-06	8-Jun-06	Completed
48	Koz & Bar Bela F. Protection Wall I	Nangarhar	100%	100%	DAI	11-Dec-05	25-Jul-06	Completed with additional work
49	Koz & Bar Bela F. Protection Wall II	Nangarhar	100%	100%	DAI	20-Dec-05	25-Mar-06	Completed
50	Koz & Bar Bela F. Protection Wall III	Nangarhar	100%	100%	DAI	20-Dec-05	15-Jun-06	Completed

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
51	Maidanak Road	Nangarhar	100%	100%	DAI	2005	13-Apr-06	Completed
52	Girdi Nawagai Road	Nangarhar	100%	99%	DAI	13-Jun-06	25-Sep-06	Ongoing
53	Inzari Khola Intake	Nangarhar	100%	32%	DAI	10/30/2006	1/30/2007	Ongoing
54	Hojoom Kala Chelgazi Intakes	Nangarhar	100%	80%	DAI	9/25/2006	12/31/2006	Ongoing
55	Lakhi Canal Intakes	Nangarhar	100%	17%	DAI	11/28/2006	2/28/2007	Ongoing
56	Kodi Khil Cobble Stone Raod	Nangarhar	100%	19%	DAI	10/16/2006	1/30/2007	Ongoing
57	Surkhab Canal Intake	Nangarhar	100%	21%	DAI	11/15/2006	2/15/2007	Ongoing
58	Pachir Cobble Stone	Nangarhar	100%	31%	DAI	10/16/2006	6/16/2007	Ongoing
59	Zysar Cobble Stone	Nangarhar	100%	30%	DAI	10/2/2006	3/31/2007	Ongoing
60	Shangina Yousaf Kas Canal Rehabilitation	Nangarhar	100%	0%	DAI	TBD	TBD	Project suspended due to security problems
61	Gachawy Mirano Road Improvement	Nangarhar	100%	2%	DAI	19-Jul-06	19-Oct-06	Project suspended due to security problems
62	Wholesale Market	Nangarhar	100%	84%	CFW	6-Jun	6-Oct	Work carried-out under CFW
63	Qasam Abad Road - 8 km	Nangarhar	100%	0%	PIP	6-Aug	7-Mar	Design completed, Technical Feasibility study Report preparation is in progress.
64	Jalalabad City Main Drain	Nangarhar	100%	100%	DAI	5-Mar-06	29-Mar-06	Completed
65	Jalalabad City Road side Drains	Nangarhar	100%	100%	DAI	5-Mar-06	21-Jun-06	Completed
66	Abdian Road Rehabilitation	Nangarhar	100%	100%	DAI	12-Mar-06	13-Jul-06	Completed
67	Binigah Flood Protection Wall	Nangarhar	100%	105%	DAI	19-Mar-06	19-Jul-06	Completed
68	Sarmarkhil Erosion Protection	Nangarhar	100%	100%	DAI	19-Mar-06	29-Apr-06	Completed
69	Spin Jumat Embankment	Nangarhar	100%	119%	DAI	25-Apr-06	30-Jul-06	Ongoing
70	Binigah II Flood Protection Wall	Nangarhar	100%	50%	DAI	3/10/2006	3/2/2006	Ongoing
71	Shega Cobble Stone	Nangarhar	100%	31%	DAI	11/18/2006	4/18/2007	Ongoing
72	Chardehe Cobble Stone	Nangarhar	100%	23%	DAI	11/14/2006	6/30/2007	Ongoing
73	Nokor khil Cobble Stone	Nangarhar	100%	14%	DAI	11/15/2006	6/30/2007	Ongoing
74	Hakim Abad Canal Intakes	Nangarhar	100%	2%	DAI	12/24/2006	6/30/2007	Ongoing
<b>GME</b>								
1	Establishment of Self Help Groups	Nangarhar	100%	100%	RI	15-Mar-06	31-Mar-06	Completed
2	Vocational Training of SHGs	Nangarhar	100%	100%	RI	15-Apr-06	31-May-06	Completed
3	Business Training of Trainers	Nangarhar	100%	100%	RI	13-Jun-06	24-Jun-06	Completed

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
4	Establishment of women-owned nurseries	Nangarhar	100%	15%	DAI	1-Apr-06	15-Jan-07	Ongoing
5	Selection of women for Food Service	Nangarhar	100%	0%	DAI	1-May-06	31-Jan-09	On-going
6	AWBA at the BDC	Nangarhar	100%	10%	AWBA	13-Jun-06	30-Jun-08	On-going
7	Master Business Training of Trainers	Nangarhar	100%	100%	RI	1-Feb-06	28-Feb-06	Completed
8	Business Training of SHGs	Nangarhar	100%	100%	RI	18-Mar-06	10-Apr-06	Completed
9	Women in Business Survey	Nangarhar	95%	0%	ALP/E	11-Ju-06	30-Se-06	Planned
<b>PSD</b>								
1	Business Development Center	Nangarhar	100%	100%	DAI	4-Apr-06	7-Feb-09	Ongoing
2	Formation of Board of Directors for BDC	Nangarhar	100%	100%	DAI	15-Apr-06	15-May-06	Formation completed, Board operating
3	Formation of Business Advisory Committee for BDC	Nangarhar	100%	100%	DAI	14-Feb-06	14-Feb-06	Formation completed committee operating.
4	Start Actual Operations of Business Development Center	Nangarhar	100%	On-going	DAI	4-Apr-06	Ongoing	Service delivery underway
5	Edible Oil	Nangarhar		100%	DAI	20-Dec-05	31-Dec-05	Completed
6	Technical Machinery	Nangarhar	100%	100%	DAI	1-Jun-06	1-Jul-06	Completed
7	Carpet	Nangarhar	100%	100%	DAI	3-Nov-05	15-Nov-05	Completed
8	Marble	Nangarhar	100%	100%	DAI	11-Oct-05	20-Oct-05	Completed
9	Feasibility Study for Flour Mills	Nangarhar	100%	100%	GIA/DAI	15-Dec-05	30-Nov-05	Completed
10	Tomato value chain analysis	Nangarhar	100%	100%	DAI	2-Aug-05	20-Aug-05	Completed
11	Dry fruits and Nuts	Nangarhar	100%	100%	RoP/DAI	15-Nov-05	30-Nov-05	Completed
12	Dairy	Nangarhar	100%	100%	LoL/DAI	20-Jan-06	10-Feb-05	Land o' Lakes, technical assistance from DAI.
13	Poultry	Nangarhar	100%	100%	DAI	15-Feb-06	27-Feb-05	Conducted by DAI AgBiz and PSD
14	Ice	Nangarhar	100%	100%	DAI	12-Jun-05	5-Jul-05	Completed
15	Handicraft	Nangarhar	100%	100%	DAI	1-Nov-05	1-Dec-05	Completed
16	Establishing Women Handicraft Center	Nangarhar	40%	0%	DAI	TBD	TBD	STTA planned of handicraft industry in ER.
17	Policy Report	Nangarhar	100%	0%	DAI	5-Nov-06	In planning	Further research of policy reform activities.
18	Investment Promotion Strategy	Nangarhar	100%	20%	DAI	20-Apr-05	On going	Investment promotion; general and sub sector specific
19	Investment Promotion Event	Nangarhar	100%	100%	DAI	5-Apr-06	5-Apr-06	Completed one-day general event
20	Investment promotion for flour milling	Nangarhar	100%	10%	DAI	1-May-05	On going	On going effort pending credit resources

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
21	Investment promotion for tomato processing	Nangarhar	100%	10%	DAI	1-Sep-05	On going	On going effort pending credit resources
22	Investment promotion for carpet cutting and washing facility	Nangarhar	100%	5%	DAI	1-Oct-05	On going	On going effort pending credit resources
23	Investment promotion for garment manufacturing	Nangarhar	100%	0%	DAI	1-Nov-05	On going	On going effort pending credit resources
24	Investment promotion for packaging factory	Nangarhar	100%	5%	DAI	1-Jan-06	On going	On going effort pending credit resources
25	Investment promotion for edible oil factory upgrading	Nangarhar	100%	5%	DAI	1-Oct-05	On going	On going effort pending credit resources
26	Investment promotion for vegetable dehydrates factory	Nangarhar	100%	5%	DAI	1-Apr-06	On going	On going effort pending credit resources
27	Investment promotion for milk processing	Nangarhar	75%	5%	DAI	1-Nov-05	On-going	On going effort pending credit resources
28	Regional Representative for CNFA (operating under an MOU)	Nangarhar	100%	5%	DAI	1-Aug-05	On going	DAI is representing CNFA in the ER.
29	Support the capacity building of Nangarhar Industrial Assn (NIA).	Nangarhar	100%	20%	DAI	5-Apr-05	On going	Supporting their sub-groups with T/A and investment promotion
30	Support to Afghanistan Investment Support Agency (AISA).	Nangarhar	100%	30%	DAI	1-Jan-06	On going	Office at the BDC and investment promotion
31	Support to Afghanistan Women's Business Association (AWBA).	Nangarhar	100%	30%	DAI	1-Jan-06	On going	Approval for supporting a Jalalabad office is pending
32	Support to Afghanistan Finance Company (AFC).	Nangarhar	100%	5%	DAI	1-Jan-06	On going	Support with establishment of office at the BDC, and with referrals for leasing/funding
33	Industrial Trade Show	Nangarhar	100%	100%	DAI	25-Aug-05	26-Aug-05	Completed. Preliminary planning for next Show to be held in October 2006
34	Support and Collaboration with Afghan International Chamber of Commerce (AICC).	Nangarhar	100%	5%	DAI	18-Jul-05	In planning	Planning to seek ways for collaboration between AICC and BDC (DAI)
35	Internet Cafes with Afghan Telecoms/PRT	Nangarhar	30%	0%	DAI	1-Feb-06	In planning	Involvement of private sector in the District Comm. Network (DCN) program.
36	Hygiene Program for food processors in the Eastern Region	Nangarhar	50%	0%	DAI	1-Apr-06	In planning	SOW prepared for assessment, awareness and training
37	International Wheat/Wheat Products Seminar in India	Nangarhar	100%	100%	DAI	4-Mar-06	11-Apr-06	Completed
38	International Investment conference and Exhibition in Kabul	Nangarhar	100%	100%	DAI	9-May-06	12-May-06	Completed
39	Internship Program with Nangarhar University	Nangarhar	100%	100%	DAI	Ongoing	Ongoing	Formal agreement expected by end of August.
<b>PIP – INFRASTRUCTURE</b>								

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
1	Shamshapur Road – 11.5 km	Nangarhar	100%	ongoing	DAI	Feb.06	Feb.07	Work being carried out under CFW
2	Wazir Tatang Causeway	Nangarhar	100%	0%	Contract	TBD	TBD	Pending
3	Wholesale Market	Nangarhar	100%	ongoing	DAI	June 2006	October 2006	Work being carried out under CFW
4	Kama DBST Road - 14.6 km	Nangarhar	100%	RFP announced	Contract	Nov-06	May-07	Announced RFP
5	Qasim Abad Road – 5.7 km	Nangarhar	100%	0%	Contract	Dec-06	May-07	Technical Feasibility Report completed.
6	Rodat Road - 12.3 km	Nangarhar	100%	0%	Contract	TBD	TBD	Design and BOQ completed.
7	Sherzad to Hesarak Road -28 km	Nangarhar	50%	0%	Contract	Dec-06	Mar- 07	Survey completed and design ongoing.
8	Lal Pur to Goshta Road-15km	Nangarhar	25%	0%	Contract	Dec-06	May-07	Engineering survey completed.
9	Chardy-Ghaziabad road 12.6 km	Nangarhar	10%	0%	Contract	TBD	TBD	Engineering survey has been completed.
10	Dudarak Road,6.2km	Nangarhar	10%	0%	Contract	Jan-07	Apr-07	Engineering survey has been completed.
<b>AGRIBUSINESS</b>								
1	Eastern Region Orchards Development Program	Laghman	100%	40%	IF Hope	5-Jul-05	16-Feb-09	Ongoing
2	Farmers Training (TOT)	Laghman	100%	100%	DAI	28-Jan-06	9-Feb-06	Completed
3	Traders (Assemblers) Training	Laghman	100%	100%	DAI	20-Feb-06	23-Feb-06	Completed
4	Wholesalers training	Laghman	100%	100%	DAI	11-Feb-06	12-Feb-06	Completed
5	Influenza Training(TOT)	Laghman	100%	100%	DAI	27-Mar-06	28-Mar-06	Completed
6	Radio Program-Farmers Interview	Laghman	100%	65%	DAI	12-Feb-06	15-Jun-06	Ongoing
7	Orchard Survey	Laghman	100%	100%	DAI	3-Apr-06	18-Apr-06	Completed
8	Vegetable Seed and Fertilizer distribution	Laghman	100%	100%	DAI	23-Feb-06	21-Mar-06	Completed
9	Packaging distribution	Laghman	100%	100%	DAI	14-Apr-06	20-Apr-06	Ongoing
10	Agricultural Marketing Production Support Program	Laghman	100%	100%	DAI	15-Dec-05	15-Aug-06	Completed
11	Training for Commercial Nursery Owners	Laghman	100%	25%	DAI	1-May-06	30-Dec-06	Ongoing
10	Smallholder Livestock Management Program	Laghman	100%	15%	DAI	1-May-05	1-May-07	Ongoing
11	Forest Incentives for Livelihood Diversification (FleLD)	Laghman	80%	5%	DAI	1-May-06	30-Dec-07	Ongoing
13	Input Supply Support Program	Laghman	100%	97%	DAI	5-Sep-06	6-Jul-06	Ongoing
14	Market Information System	Laghman	100%	55%	DAI&DoA	6-Mar-06	8-Dec-06	Ongoing

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
15	Intercropping Program for ERODP Beneficiaries	Laghman	100%	100%	DAI	6-May-06	6-Jun-06	Completed
16	Fruit Marketing Program	Laghman	100%	35%	DAI	6-May-06	8-Dec-06	Ongoing
17	Eastern Region Annual Crops Initiatives	Laghman	100%	0%	DAI	6-Jul-06	8-Dec-06	Ongoing
18	Eastern Region Livestock Development initiatives	Laghman	100%	5%	DAI	6-Jun-06	8-Dec-06	Ongoing
19	Adaptive Research Technology Dissemination and Development of Seed Supply System	Laghman	100%	5%	ICARDA	5-Dec-06	8-Dec-06	Pending subcontract
20	Fall Wheat Seed and Fertilizer Distribution Program	Laghman	100%	100%	DAI&DoA	1-Jul-06	30-Oct-06	Completed
<b>CFW – INFRASTRUCTURE</b>								
1	Mashina Road Improvement – 7.5 km	Laghman	100%	Tender preparation	DAI	6-Jul	6-Nov	Project awarded to HADF for improvement
2	Darunta Bypass Cobblestone Road, First Reach	Laghman	100%	100%	DAI	1-Feb-06	27-Apr-06	Completed
3	Darunta Bypass Cobblestone Road, Second Reach	Laghman	100%	100%	DAI	13-May-06	25-Aug-06	Completed
4	Farman Khil & Jui Daman Canals	Laghman	100%	100%	DAI	12-Jun-06	20-Jul-06	Completed
5	Farman Khil & Jui Daman Canals	Laghman	100%	28%	DAI	1-Nov-06	31-Mar-07	Ongoing
6	Dopi and Langalam Protection wall	Laghman	100%	100%	RI	24-Nov-05	30-Mar-06	Completed
7	Char Bagh Canal reconstruction	Laghman	100%	100%	RI	23-Feb-06	23-Jun-06	Completed
8	Kalakot and Longalam Canal reconstruction	Laghman	100%	100%	RI	16-Feb-06	16-Jun-06	Completed
9	Shamshirabad Flood Protection	Laghman	100%	100%	RI	8-Mar-06	20-Jul-06	Completed
10	Kakas Canal Rehabilitation	Laghman	100%	0%	RI	TBD	TBD	Pending due to irrigation season
11	Kanda Canal Rehabilitation	Laghman	100%	100%	RI	26-Apr-06	26-Jul-06	Ongoing
12	Kac Aziz Khan Canal	Laghman	100%	85%	RI	5-Sep-06	10-Jan-07	Ongoing
13	Qardi Kac Canal	Laghman	100%	70%	RI	TBD	TBD	Ongoing
14	Lara Mora Road Improvement	Laghman	100%	2%	RI	25-Dec-06	10-Mar-07	Ongoing
15	Nolo Protection wall	Laghman	100%	100%	RI	2005	5-Dec-05	Completed
16	Jamshidabad Protection wall	Laghman	100%	100%	RI	2005	31-Aug-05	Completed
17	Jamshidabad Protection wall Additional work	Laghman	100%	100%	RI	2005	27-Jan-06	Completed
18	Mustafa Kalay Protection Wall	Laghman	100%	100%	RI	2005	31-Aug-05	Completed

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
19	Akhund Sahib Protection Wall	Laghman	100%	100%	RI	2005	27-Dec-05	Completed
20	Qardi Salab Canal	Laghman	100%	97%	RI	16-Aug-06	30-Nov-06	On going
21	Kandi Sahib Canal	Laghman	100%	100%	RI	14-Aug-06	15-Nov-06	Completed
22	Kalay Baya Canal	Laghman	100%	90%	RI	30-Aug-06	30-Nov-06	Ongoing
23	Abuzai Bridge	Laghman	98%	0%	DAI	6-Sep	7-Sep	Awaiting finalization of Technical Feasibility Report
24	Deh-Zairat Protection wall	Laghman	100%	100%	RI	28-Sep-06	15-Mar-06	Completed
25	Karaho Protection wall	Laghman	100%	100%	RI	2005	28-Feb-06	Completed
26	Tergari Protection wall	Laghman	100%	100%	RI	20-Oct-05	30-Mar-06	Completed, backfilling on going
27	Mulayan Protection wall	Laghman	100%	100%	RI	28-Dec-05	13-Jul-06	Completed
28	Shamangal Canal Reconstruction	Laghman	100%	100%	RI	15-Feb-06	30-May-06	Completed
29	Pacha Joie Canal	Laghman	100%	100%	RI	26-Aug-06	26-Nov-06	Completed
30	Hayadarkhani Canal Reconstruction	Laghman	100%	100%	RI	6-Sep-06	9-Jun-06	Completed
31	Ghundy Baba Sahib Flood protection wall	Laghman	100%	85%	RI	10-Sep-06	20-Dec-06	Ongoing
32	Qala Shagee flood protection wall	Laghman	100%	93%	RI	10-Sep-06	20-Dec-06	Ongoing
33	Baba Sahib Canal	Laghman	100%	100%	RI	30-Aug-06	30-Nov-06	Completed
34	Deh Ziarat Omar Zai Cobble Stone Road	Laghman	100%	27%	RI	30-Aug-06	30-Nov-06	Ongoing
35	Abuzai Flood Protection wall	Laghman	100%	83%	RI	10-Mar-06	2-Mar-07	Ongoing
36	Khoja Khil Sofla Canal Rehabilitation	Laghman	100%	100%	RI	2005	19-Jan-06	Completed
37	Ghuny Nazar Khil Protection wall	Laghman	100%	100%	RI	19-Dec-05	7-Jun-06	Completed
38	Qasaba Protection wall	Laghman	100%	100%	RI	10-Dec-05	15-Apr-06	Completed
39	Bara Kandy and Kuza Kandy Canal Rehabilitation	Laghman	100%	100%	RI	24-May-06	24-Aug-06	Completed
40	Purwaie Flood Protection works	Laghman	100%	100%	RI	5-Sep-06	10-Jan-07	Completed
41	Mandul Flood protection works	Laghman	100%	100%	RI	2-Sep--6	10-Nov-06	Completed
<b>GME</b>								
1	Establishment of Self Help Groups	Laghman	100%	100%	RI	15-Mar-06	31-Mar-06	Completed
2	Vocational Training of SHGs	Laghman	100%	100%	RI	15-Apr-06	31-May-06	Completed
3	Business Training of Trainers	Laghman	100%	50%	RI	13-Jun-06	24-Jun-06	Completed
4	Smallholder Livestock Management Program	Laghman	100%	10%	DAI	1-May-05	1-May-07	On-going

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
5	Establishment of 4 women-owned nurseries	Laghman	100%	15%	DAI	1-Apr-06	15-Jan-07	On-Going
6	Master Business Training of Trainers	Laghman	100%	100%	RI	1-Feb-06	28-Feb-06	Completed
7	Selection of Women for Food Services	Laghman	100%	20%	ALP/E	1-May-06	31-Jan-09	Ongoing
<b>PIP- INFRASTRUCTURE</b>								
1	Darunta by-pass Road	Laghman	100%	Ongoing	DAI	Feb-06	Dec-06	Work being carried out under CFW
2	Mashina Road Improvement – 7.5 km	Laghman	100%	7%	Contract	2-Sep-06	15-Nov-06	Work started on 2 <sup>nd</sup> Sep.
3	Abuzai Bridge	Laghman	100%	0%	Contract	6-Nov	7-Jun	Awaiting finalization of Technical Feasibility Report
<b>AGRIBUSINESS</b>								
1	Farmers Training (TOT)	Kunar	100%	100%	DAI	28-Jan-06	9-Feb-06	Completed
2	Traders (Assemblers) Training	Kunar	100%	100%	DAI	20-Feb-06	23-Feb-06	Completed
3	Wholesalers training	Kunar	100%	100%	DAI	11-Feb-06	12-Feb-06	Completed
4	Influenza Training(TOT)	Kunar	100%	100%	DAI	27-Mar-06	28-Mar-06	Completed
5	Radio Program-Farmers Interview	Kunar	100%	65%	DAI	12-Feb-06	15-Jun-06	Ongoing
6	Packaging distribution	Kunar	100%	100%	DAI	14-Apr-06	20-Apr-06	Completed
7	Agricultural Marketing Production Support Program	Kunar	100%	100%	DAI	15-Dec-05	15-Aug-06	Completed
8	Input Supply Support Program	Kunar	100%	97%	DAI	5-Sep-06	6-Jul-06	Ongoing
9	Market Information System	Kunar	100%	55%	DAI&DoA	6-Mar-06	8-Dec-06	Ongoing
10	Eastern Region Livestock Development initiatives	Kunar	90%	5%	DAI	6-Jun-06	8-Dec-06	Ongoing
11	Forest Incentives for Livelihood Diversification (FieLD)	Kunar	80%	5%	DAI	1-May-06	30-Dec-07	Ongoing
12	Fruit Marketing Program	Kunar	100%	35%	DAI	6-May-06	8-Dec-06	Ongoing
13	Fall Wheat Seed and Fertilizer Distribution Program	Kunar	100%	100%	DAI&DoA	1-Jul-06	30-Oct-06	Completed
<b>CFW- INFRASTRUCTURE</b>								
1	Seend Wala Chawkay Intake	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
2	Dewagal Road Repair	Kunar	100%	90%	DAI	16-Apr-06	15-Sep-06	Ongoing
3	Zarmandi Flood protection	Kunar	100%	92%	DAI	27-Jun-06	10-Oct-06	Completed
4	Chawkay Khower Flood Protection	Kunar	100%	88%	DAI	10-Jul-06	10-Oct-06	Ongoing
5	Daag Canal Repair	Kunar	100%	100%	DAI	21-Feb-06	20-Jun-06	Completed, additional work on going

SN	PROJECT NAME	PROVINCE	% COMPLETED		IMPLEMENTER	ACTIVITY START DATE	ACTIVITY COMPLETION DATE	COMMENTS
			DESIGN	IMPLEMENT				
6	Tanar Road Rehabilitation	Kunar	100%	100%	DAI	21-Feb-06	12-Jun-06	Completed, additional work on going
7	Khas Kunar Middle Road	Kunar	100%	100%	DAI	14-Jun-06	25-Sep-06	Completed
8	Clinic to Hakimabad road	Kunar	100%	100%	DAI	28-Aug-06	28-Nov-06	Completed
9	Nurgal Seend Wala Intake	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar river
10	Seenda Wala Canal Rehabilitation	Kunar	100%	100%	DAI	20-Feb-06	25-Jul-06	Completed, additional work on going
11	Nurgal Aret Road	Kunar	100%	92%	DAI	18-Jun-06	25-Oct-06	Ongoing
12	Tora Tega Road	Kunar	100%	92%	DAI	11-Jul-06	11-Oct-06	Ongoing
13	Dandono Kotgi Canal Intake	Kunar	100%	0%	DAI	TBD	TBD	Pending due to water level in Kunar River
14	Barnarang Road Repair	Kunar	100%	100%	DAI	16-Apr-06	25-Jul-06	Completed
15	Sharalow-Badil Road Repair	Kunar	100%	100%	DAI	16-Apr-06	25-Jul-06	Completed
16	Badil Khower Flood Protection	Kunar	100%	88%	DAI	11-Jul-06	11-Oct-06	Ongoing
<b>GME</b>								
1	Training for Commercial Nursery Owners	Kunar	100%	20%	DAI	1-May-06	30-Dec-06	Ongoing
2	Establishment of Self Help Groups	Kunar	100%	100%	RI	15-Mar-06	31-Mar-06	Completed
3	Vocational Training of SHGs	Kunar	100%	100%	RI	30-Apr-06	25-Jun-06	Completed
4	Business Training of Trainers	Kunar	100%	0%	RI	2-Jul-06	13-Jul-06	Planned
6	Master Business Training of Trainers	Kunar	100%	100%	RI	1-Feb-06	28-Feb-06	Completed
7	Selection of Women for Food Services	Kunar	100%	20%	ALP/E	1-May-06	31-Jan-09	Ongoing
<b>AGRIBUSINESS</b>								
1	Radio Program-Farmers Interview	Nuristan	100%	65%	DAI	12-Feb-06	15-Jun-06	Ongoing
2	Fall Wheat Seed and Fertilizer Distribution Program	Nuristan	100%	100%	DAI&DoA	1-Jul-06	30-Oct-06	Completed
<b>CFW- INFRASTRUCTURE</b>								
1	Dakor-Mushfa Cobblestone Road section I	Nuristan	100%	28%	DAI	28-Sep-06	15-May-07	Ongoing

**Annex IV: ALP/E Person Employed, Employment Days, and Wages Paid on CFW Projects through December 31<sup>ST</sup>, 2006**

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
<b>Kunar Province</b>												
Kunar	Chawkay	CFW101303	Dewagal Road Improvement	177	14	191	17,752	1,304	19,056	64,679	5,216	69,895
Kunar	Chawkay	CFW101304	Zarmandai and Kulmani Flood Protection Wall	160	14	174	15,410	996	16,406	60,113	3,984	64,097
Kunar	Chawkay	CFW101306	Chawkay Khower Flood Protection Wall	160	14	174	12,197	744	12,941	50,006	2,976	52,982
Kunar	Khas Kunar	CFW101501	Daag Canal Repair	235	17	252	13,359	801	14,160	59,887	3,204	63,091
Kunar	Khas Kunar	CFW101502	Tanar Road Rehabilitation	84	6	90	4,682	328	5,010	20,148	1,312	21,460
Kunar	Khas Kunar	CFW101503	Clinic To Hakim Abad Road	90	6	96	6,174	292	6,466	24,793	1,240	26,033
Kunar	Khas Kunar	CFW101504	Khas Kunar Middle Road	77	5	82	4,711	300	5,011	22,401	1,200	23,601
Kunar	Narang	CFW101203	Bar Narang Road Improvement	216	16	232	17,845	1,422	19,267	68,329	5,688	74,017
Kunar	Narang	CFW101204	Sharalo Badil Road Improvement	200	14	214	15,924	1,216	17,140	58,596	4,864	63,460
Kunar	Narang	CFW101205	Badil Khawar Flood Protection Walls and Irrigation Intake	103	8	111	7,214	312	7,526	31,222	1,248	32,470
Kunar	Nurgal	CFW101402	Seenda Wala Canal Rehabilitation	105	8	113	8,843	539	9,382	39,403	2,156	41,559
Kunar	Nurgal	CFW101403	Nurgal Aret Road	178	14	192	20,906	1,337	22,243	74,424	5,402	79,826
Kunar	Nurgal	CFW101404	Kuz Nurgal Tora Tega Road Improvement	94	7	101	8,589	488	9,077	33,669	2,066	35,735
<b>Kunar Province</b>				1,879	143	2,022	153,606	10,079	163,685	607,670	40,556	648,226
<b>Laghman Province</b>												
Laghman	Alingar	CFW090301	Khoja Khil Sofla Canal Rehabilitation	1,329	38	1,367	11,100	408	11,508	50,538	1,632	52,170
Laghman	Alingar	CFW090302	Ghundai Nazar Khil Protection	211	8	219	25,020	2,800	27,820	70,601	10,652	81,253
Laghman	Alingar	CFW090303	Qasaba Protection Wall	201	7	208	18,989	2,554	21,543	69,308	10,216	79,524
Laghman	Alingar	CFW090304	Bar Kanday and Kuz Kanday Canal Rehabilitation	127	6	133	10,997	416	11,413	39,779	1,664	41,443
Laghman	Alingar	CFW090305	Purai Protection Wall	153	5	158	9,738	268	10,006	32,416	1,072	33,488
Laghman	Alingar	CFW090306	Mandol Protection Wall	128	5	133	7,473	184	7,657	27,627	736	28,363
Laghman	Alishing	CFW090701	Nolo Protection Wall	399	7	406	24,345	381	24,726	80,880	1,524	82,404
Laghman	Alishing	CFW090702A	Jamshidabad Protection Wall	450	4	454	21,566	164	21,730	45,645	656	46,301
Laghman	Alishing	CFW090702B	Jamshdabad Flood Protection Wall Additional Work	186	5	191	12,636	324	12,960	63,448	1,296	64,744
Laghman	Alishing	CFW090703	Mustafa Kalay Protection Wall	500	18	518	17,082	565	17,647	57,656	2,260	59,916
Laghman	Alishing	CFW090704	Akhund Sahib Protection Wall	360	9	369	24,352	482	24,834	92,565	1,928	94,493
Laghman	Alishing	CFW090705	Kandi Sahib Canal Rehabilitation	126	5	131	6,610	157	6,767	29,876	628	30,504
Laghman	Alishing	CFW090708	Qardi Salab Canal Rehabilitation	168	6	174	10,312	240	10,552	42,742	960	43,702
Laghman	Alishing	CFW090709	Kalay Baya Canal Rehabilitation	180	5	185	9,154	250	9,404	34,608	1000	35,608

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Laghman	Mihtarlam	CFW090101	Deh Zairat Protection Wall	525	10	535	34,352	898	35,250	157,444	3,592	161,036
Laghman	Mihtarlam	CFW090102	Karaho Protection Wall	209	4	213	13,744	155	13,899	52,478	620	53,098
Laghman	Mihtarlam	CFW090103	Tergari Protection Wall	331	8	339	33,494	927	34,421	123,113	3,708	126,821
Laghman	Mihtarlam	CFW090104	Mulayan Protection Wall	369	12	381	27,892	933	28,825	101,555	3,732	105,287
Laghman	Mihtarlam	CFW090105	Shamangal Canal Reconstruction	168	7	175	14,319	563	14,882	55,560	2,252	57,812
Laghman	Mihtarlam	CFW090106	Hayadarkhani Canal Reconstruction	219	4	223	5,390	173	5,563	23,437	692	24,129
Laghman	Mihtarlam	CFW090107	Pacha Joie Canal Rehabilitation	175	7	182	10,629	267	10,896	39,767	1,068	40,835
Laghman	Mihtarlam	CFW090108	Abi Zai Flood Protection Wall	166	7	173	11,488	317	11,805	48,376	1,268	49,644
Laghman	Mihtarlam	CFW090112	Ghundy Baba Flood Protection Wall	165	6	171	10,000	265	10,265	38,517	1,060	39,577
Laghman	Mihtarlam	CFW090118	Qala Shagee Protection Wall	177	8	185	10,972	288	11,260	42,203	1,152	43,355
Laghman	Mihtarlam	CFW090120	Baba Sahib Canal Rehabilitation	128	5	133	7,178	157	7,335	28,943	628	29,571
Laghman	Mihtarlam	CFW090121	Dehziarat/Omarzai village Cobble Stone Road Improvement	249	18	267	10,644	580	11,224	31,574	2,149	33,723
Laghman	Qarghayi	CFW090201	Dopi and Longalam Protection Wall	301	13	314	22,741	860	23,601	79,787	3,440	83,227
Laghman	Qarghayi	CFW090202	Char Bagh Canal Reconstruction	157	5	162	11,607	446	12,053	45,644	1,784	47,428
Laghman	Qarghayi	CFW090203	Kalakot and Longalam Canal Reconstruction	186	6	192	15,903	532	16,435	94,154	2,128	96,282
Laghman	Qarghayi	CFW090204	Daronata Road Repair (Daronta Bypass)	226	2	228	11,346	86	11,432	61,215	344	61,559
Laghman	Qarghayi	CFW090205	Shamsherabad Flood Protection	412	14	426	27,294	1,151	28,445	103,995	4,604	108,599
Laghman	Qarghayi	CFW090208	Kanda Canal Rehabilitation	149	6	155	9,856	387	10,243	39,258	1,280	40,538
Laghman	Qarghayi	CFW090209	Daronta Bypass Cobble Stone Road Second Reach	303	2	305	32,553	242	32,795	138,880	968	139,848
Laghman	Qarghayi	CFW090210	Kac Aziz khan Canal	408	6	414	20,725	353	21,078	73,698	1,412	75,110
Laghman	Qarghayi	CFW090212	Farman Khil and Jue Daman Canal	96	0	96	2,599	0	2,599	11,018	0	11,018
Laghman	Qarghayi	CFW090213	Daronta Bypass Cobble Stone Road Third Reach	150	2	152	6,636	10	6,646	19,194	40	19,234
Laghman	Qarghayi	CFW090214	Gardi Kac Canal Rehabilitation	141	5	146	9,225	267	9,492	34,911	1,068	35,979
Laghman	Qarghayi	CFW090219	Lara Mora Road Improvement	55	0	55	222	0	222	0	0	0
<b>Laghman Province</b>				9,983	285	10,268	570,183	19,050	589,233	2,182,410	75,213	2,257,623
<b>Nangarhar Province</b>												
Nangarhar	Achin	CFW081001	Deh Sarak Canal Intake Improvement	79	6	85	3,702	182	3,884	14,682	728	15,410
Nangarhar	Achin	CFW081002	Pekha Protection Flood Protection Wall	461	0	461	29,769	0	29,769	108,455	0	108,455
Nangarhar	Bati Kot	CFW081703	Chardehe Cobble Stone Road	145	13	158	4,452	388	4,840	13,218	1,603	14,821
Nangarhar	Behsud	CFW082201	Abdian Road Rehabilitation	185	0	185	7,952	0	7,952	29,204	0	29,204
Nangarhar	Behsud	CFW082202	Biniga Flood Protection Wall	78	6	84	5,093	285	5,378	20,909	1,140	22,049
Nangarhar	Behsud	CFW082203	Sammarkhil Erosion Protection	207	17	224	6,312	561	6,873	23,498	2,244	25,742
Nangarhar	Behsud	CFW082204	Spin Jumat Embankment	75	5	80	8,244	477	8,721	32,488	1,846	34,334
Nangarhar	Behsud	CFW082206	Benigah Flood Protection Embankment Stage II	91	9	100	5,287	365	5,652	14,971	1,388	16,359

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
Nangarhar	Chaparhar	CFW080601	Daulat Zai Canal Intake	133	10	143	12,320	872	13,192	49,857	3,488	53,345
Nangarhar	Chaparhar	CFW080602	Garatic and Chardahi Canal Intakes	159	13	172	7,498	563	8,061	32,367	2,252	34,619
Nangarhar	Chaparhar	CFW080603	Garatic Flood Protection Wall	142	11	153	10,667	706	11,373	43,722	2,824	46,546
Nangarhar	Chaparhar	CFW080604	Chardahi Flood Protection Wall	126	9	135	10,270	600	10,870	45,651	2,400	48,051
Nangarhar	Chaparhar	CFW080605	Sholana Flood Protection Wall	127	9	136	11,060	701	11,761	45,840	2,804	48,644
Nangarhar	Chaparhar	CFW080606	Lawangapur Village Cobble Stone Road Improvement	193	8	201	8,966	479	9,445	33,114	2,189	35,303
Nangarhar	Chaparhar	CFW080607	Spin Jumat Road Improvement	131	12	143	649	60	709	0	0	0
Nangarhar	Dur Baba	CFW081201	Mahsil and Qasaba Kalay Irrigation Reservoir and Erosion Protection	188	2	190	7,010	8	7,018	25,388	32	25,420
Nangarhar	Dur Baba	CFW081202	Sasobi Irrigation Reservoir and Flood Protection Wall	186	8	194	10,692	24	10,716	37,199	96	37,295
Nangarhar	Dur Baba	CFW081203	Torlala Kalay Irrigation Reservoir and Flood Protection	153	4	157	9,481	172	9,653	35,357	688	36,045
Nangarhar	Goshta	CFW081601	Kuz and Bar Billa Flood Protection Wall 1	244	18	262	13,384	1,147	14,531	58,446	4,588	63,034
Nangarhar	Goshta	CFW081602	Kuz and Bar Billa Flood Protection Wall 2	90	8	98	2,549	197	2,746	10,894	788	11,682
Nangarhar	Goshta	CFW081603	Kuz and Bar Billa Flood Protection Wall 3	89	6	95	5,301	382	5,683	21,391	1,528	22,919
Nangarhar	Hisarak	CFW080301	Mana Road Rehabilitation	288	26	314	20,876	1,894	22,770	73,147	7,576	80,723
Nangarhar	Hisarak	CFW080302	Shana Zawara Road Rehabilitation	116	10	126	8,454	652	9,106	31,078	2,608	33,686
Nangarhar	Hisarak	CFW080305	Sanzai Road Improvement	65	4	69	4,418	300	4,718	16,415	1,200	17,615
Nangarhar	Jalalabad	CFW080101	Jalalabad city Main Drain	63	0	63	2,622	0	2,622	11,960	0	11,960
Nangarhar	Jalalabad	CFW080102	Jalalabad city Road Side Drains	540	0	540	22,174	0	22,174	94,292	0	94,292
Nangarhar	Jalalabad	CFW080103	Whole Sale Market Rehabilitation	199	21	220	22,676	690	23,366	97,535	2,760	100,295
Nangarhar	Khogyani	CFW080505	Hakimabad Canal Intakes and Retaining Walls	54	0	54	270	0	270	0	0	0
Nangarhar	Khogyani	CFW080502	Khawaran Road Rehabilitation	146	14	160	9,153	741	9,894	37,869	2,964	40,833
Nangarhar	Khogyani	CFW080502	Kalagho Road Rehabilitation	181	16	197	9,103	781	9,884	35,253	3,124	38,377
Nangarhar	Khogyani	CFW080504	Nemla Irrigation Intakes and Canal Repair	50	4	54	302	16	318	1,165	64	1,229
Nangarhar	Khogyani	CFW080506	Khawaza khil and Malam Khil Road	48	3	51	2,718	179	2,897	16,240	716	16,956
Nangarhar	Khogyani	CFW080507	Nemla Flood Protection Works	110	7	117	7,356	424	7,780	31,078	1,696	32,774
Nangarhar	Khogyani	CFW080508	Nokor khil Cobble Stone Road	132	12	144	4,201	278	4,479	16,128	1076	17,204
Nangarhar	Kot	CFW082103	Metrani Village Cobble Stone Road	121	11	132	2,798	249	3,047	11,120	987	12,107
Nangarhar	Kuz Kunar	CFW081902	Bodiali and soraj Irrigation Rehabilitation	128	9	137	6,346	484	6,830	25,718	1,936	27,654
Nangarhar	Kuz Kunar	CFW081903	Shega Cobble Stone Road	250	18	268	6,303	412	6,715	26,415	1701	28,116
Nangarhar	Lal Pur	CFW081502	Guldag Flood Protection Wall	163	13	176	3,094	199	3,293	13,647	796	14,443
Nangarhar	Muhmand Dara	CFW081402	Zara Sultankhil Protection Wall	67	1	68	3,477	33	3,510	10,515	132	10,647
Nangarhar	Muhmand	CFW081403	Girdi Ghos Protection Wall	82	3	85	2,637	112	2,749	17,354	448	17,802

Province	District	Project No	Project Name	Person Employed			Person Employment days			Wages Paid		
				Male	Female	Total	Male	Female	Total	Male	Female	Total
	Dara											
Nangarhar	Muhmand Dara	CFW081404	Basawal Banbaba Flood Protection Wall	73	6	79	1,496	118	1,614	5,559	472	6,031
Nangarhar	Nazyan	CFW081101	Tarkhy Flood Protection Works and Irrigation Intake	143	10	153	12,377	856	13,233	43,364	3,262	46,626
Nangarhar	Nazyan	CFW081102	Zysar Village Cobble Stone Road Improvement	238	20	258	9,502	474	9,976	22,532	1,509	24,041
Nangarhar	Pachir Wa Agam	CFW080702	Pachir Cobble Stone Road	217	14	231	7,086	469	7,555	24,239	2,021	26,260
Nangarhar	Sherzad	CFW080401	Gandomak Road Rehabilitation	180	16	196	10,924	936	11,860	41,820	3,744	45,564
Nangarhar	Sherzad	CFW080402	Toto Road Rehabilitation	129	8	137	8,970	631	9,601	38,402	2,524	40,926
Nangarhar	Sherzad	CFW080403	Ashpan Flood Protection	203	18	221	10,764	971	11,735	42,961	3,884	46,845
Nangarhar	Sherzad	CFW080405	Patlaw Road Rehabilitation	109	7	116	7,053	507	7,560	34,233	2,028	36,261
Nangarhar	Sherzad	CFW080406	Surkhab Canal Intakes and Supper Passage Project	59	3	62	1,685	32	1,717	6,710	119	6,829
Nangarhar	Sherzad	CFW080407	Kodi Khil Cobble Stone Road	331	23	354	11,864	886	12,750	45,084	4,175	49,259
Nangarhar	Shinwar	CFW081301	Zakhil Wash Irrigation Canal	224	0	224	4,284	0	4,284	17,793	0	17,793
Nangarhar	Spin Ghar	CFW082301	Maidanak Road Rehabilitation	465	0	465	16,857	0	16,857	88,634	0	88,634
Nangarhar	Spin Ghar	CFW082302	Inzari Khola Canals Intakes	93	7	100	3,872	232	4,104	9,129	850	9,979
Nangarhar	Spin Ghar	CFW082303	Hajoom Kal Chelgazi Canal Intakes	132	10	142	8,139	365	8,504	22,257	1,380	23,637
Nangarhar	Spin Ghar	CFW082304	Lokhi Canal Intake and Super Passage	75	6	81	1,480	54	1,534	4,688	148	4,836
Nangarhar	Spin Ghar	CFW082305	Girdi Nawagai Road Repair	140	13	153	20,156	1,343	21,499	70,917	5,123	76,040
Nangarhar	Surkh Rod	CFW080201	Shamshapur Cobble Stone Road Pilot	393	16	409	18,773	851	19,624	92,026	3,404	95,430
Nangarhar	Surkh Rod	CFW080202	Kakrak Road Improvement	258	20	278	21,396	567	21,963	83,345	2,268	85,613
Nangarhar	Surkh Rod	CFW080203	Tatang Nawab Jabar Canal Rehabilitation	158	11	169	8,084	217	8,301	36,307	868	37,175
Nangarhar	Surkh Rod	CFW080204	Sarband and Jalawanano Canal Intake	87	7	94	5,218	308	5,526	23,423	1,232	24,655
Nangarhar	Surkh Rod	CFW080205	Shamshapur Darunta Road Improvement	283	6	289	25,208	336	25,544	93,378	1,344	94,722
Nangarhar	Surkh Rod	CFW080206	Shamshapur Cobble Stone Road Second Reach	390	16	406	39,605	1,423	41,028	160,507	5,692	166,199
Nangarhar	Surkh Rod	CFW080207	Ghauchak Cobble Stone Road Improvement	329	23	352	15,502	555	16,057	42,575	2,509	45,084
Nangarhar	Surkh Rod	CFW080208	Shamshapur Cobble Stone Road Third Reach	313	14	327	8,907	403	9,310	19,025	1,116	20,141
Nangarhar	Tor Ghar	CFW082401	Shangina Yousaf Kas Canal Rehabilitation	153	0	153	840	0	840	890	0	890
Nangarhar	Tor Ghar	CFW082402	Gachway Mirano Road Improvement	42	0	42	64	0	64	1,776	0	1,776
<b>Nangarhar Province</b>				<b>11,302</b>	<b>620</b>	<b>11,922</b>	<b>599,742</b>	<b>28,147</b>	<b>627,889</b>	<b>2,335,154</b>	<b>112,082</b>	<b>2,447,236</b>
<b>Nuristan Province</b>												
Nuristan	Nur Gram	CFW300801	Dakor Mashafa Cobblestone Road	374	33	407	19,801	1,399	21,200	54,729	5,726	60,455
<b>Nuristan Province</b>				<b>374</b>	<b>33</b>	<b>407</b>	<b>19801</b>	<b>1399</b>	<b>21200</b>	<b>54729</b>	<b>5726</b>	<b>60455</b>
<b>Grand Total</b>				<b>23,538</b>	<b>1,081</b>	<b>24,619</b>	<b>1,343,332</b>	<b>58,675</b>	<b>1,402,007</b>	<b>5,179,963</b>	<b>233,577</b>	<b>5,413,540</b>

**Note: USAID/AINP Performance Data:** i. Work Days Generated (No.): 2,967,708 ii. Salaries Paid to Laborers: \$9,842,363 iii. People Employed (No.): 134,000 iv. Irrigation Canals, drainage, ditches, and Karezes repaired or cleaned (Km): 2,281 v. Land Benefiting from Improved Irrigation (Ha): 113,060 vi. Roads Repaired (Km): 148
