



USAID
FROM THE AMERICAN PEOPLE



IOM International Organization for Migration
OIM Organisation Internationale pour les Migrations
OIM Organización Internacional para las Migraciones

COMEDOR POPULAR
ORGANIZACIÓN FEMENINA POPULAR

Post-Emergency Assistance to Displaced Groups, Receptor Communities and Vulnerable Populations Program.

Este Proyecto es financiado por el Pueblo de los Estados Unidos, a través de la Agencia para el Desarrollo Internacional USAID y con el apoyo técnico de la Organización Internacional para las Migraciones OIM

Con el apoyo económico del Pueblo de los Estados Unidos, a través de la Agencia para el Desarrollo Internacional USAID y con el apoyo técnico de la Organización Internacional para las Migraciones OIM

22 Quarterly Report •
1st January - 31st March 2006

Q2/FY06



Photo: Regional Office Huila
Hernán Portela

IOM • Carrera 14 No. 93B - 46 • Edificio Chico 94 • Bogota • COLOMBIA
Switchboard: +57.1.622 7774 • FAX: +57.1.622 341 • E.mail: IOMBogotaOPS@iom.int
oimcolombia@iom.org.co • Internet: <http://www.iom.org.co> • <http://www.iom.int>

Table of Contents

	PAGE
Summary Tables	
Summary Table – This Quarter	3
Summary Table – To Date	5
1. Executive Summary	
General Analysis	7
Sectoral Analysis	7
AfroColombians and Indigenous	7
Youth – Displacement Prevention	8
Land	8
Private Enterprise	8
Gender	9
Return	9
Operating Partners	10
Sustainability	10
Visibility	11
Security	11
2. Displacement Notes	
IOM Departments and Zones	12
3. Program Components	
A. Income Generation	16
B. Social Infrastructure and Housing	17
C. Education and Co-Existence	18
D. Health	19
E. Strengthening of Institutions and Communities	20
4. Next Quarter Priorities	21
Annexes	
Annex 1. Financial Report	
Annex 2. Glossary	
Annex 3. List Operating Partners	
Annex 4. Project Sheets for Concluded Activities	
Annex 5. Sustainability Methodology and Analysis	
Annex 6. Calendar of Events	
Annex 7. Press Coverage	
Annex 8. Training Information	

Summary Table – This Quarter

Organization:	International Organization for Migration/Colombia
Reporting Period:	January 1 st to March 31 st , 2006
New Projects Approved in Reporting Period:	21
New Project Financial Information:	New Obligations US\$751,061.00
Expenses:	US\$3,059,186,44 (Quarter) • US\$42,928,938.73 (To Date)
Projected Expenditure April – June 2006:	US\$3,000,000

Table 1. Projects Approved this Quarter – by Component, Region

Regional Office	Income Generation	Social Infrastructure and Housing	Education	Health	Institutional Strengthening	TOTAL
Norte de Santander	4	-	-	-	-	4
Santander	2	-	-	-	-	2
Valle del Cauca	2	-	-	-	-	2
Putumayo	1	-	-	-	-	1
Nariño	2	-	-	-	1	3
Caquetá	-	-	-	-	-	-
Choco	1	-	-	-	-	1
Cauca	1	1	-	-	-	2
Huila	1	-	-	1	-	2
Inter-regional	1	-	1	2	-	4
TOTAL	15	1	1	3	1	21

Table 2. Breakdown by Active and Concluded Projects – This Quarter

Region	Income Generation		Social Infrastructure and Housing		Education		Health		Institutional Strengthening		TOTAL	
	Active	Complete	Active	Complete	Active	Complete	Active	Complete	Active	Complete	Active	Complete
Norte de Santander	5	-	-	2	1	3	-	-	1	-	7	5
Santander	4	-	3	2	-	-	1	-	-	-	8	2
Valle del Cauca	5	-	5	2	-	-	1	-	1	-	12	2
Putumayo	2	-	-	-	1	-	-	-	1	3	4	3
Nariño	3	1	1	-	-	-	-	-	1	-	5	1
Caquetá	-	1	3	-	-	-	-	-	-	-	3	1
Choco	1	1	2	-	-	-	-	-	-	-	3	1
Cauca	2	-	8	1	5	-	-	-	2	-	17	1
Huila	2	-	1	-	-	-	1	-	1	-	5	-
Inter-regional	4	-	1	2	15	-	9	1	12	4	41	7
TOTAL	28	3	24	9	22	3	12	1	19	7	105	23

Table 3. Direct Beneficiaries by Component and Region – This Quarter

Region	Income Generation	Social Infrastructure and Housing	Education	Health	Institutional Strengthening	TOTAL
Norte de Santander	129	-	90	-	663	882
Santander	111	200	-	-	-	311
Valle del Cauca	128	953	-	3,465	-	4,546
Putumayo	12	-	312	-	2,681	3,005
Nariño	36	-	-	-	-	36
Caquetá	-	-	-	-	-	-
Choco	-	100	-	-	-	100
Cauca	2,123	-	413	-	88	2,624
Huila	-	-	-	-	-	-
Inter regional	121	-	2,978	474	-	3,573
TOTAL	2,660	1,253	3,793	3,939	3,432	15,077

Table 4. New Financial Obligations by Region (Quarter US\$751,061.00)

Region	Income Generation	Social Infrastructure and Housing	Education	Health	Institutional Strengthening	TOTAL
Norte de Santander	69,298.25	-	-	-	-	69,298.25
Santander	-	33,039.65	-	-	-	33,039.65
Valle del Cauca	34,874.23	-	-	-	-	34,874.23
Putumayo	-	-	-	-	-	-
Nariño	-	-	-	-	21,865.90	21,865.90
Caquetá	-	-	-	-	-	-
Choco	110,132.16	-	-	-	-	110,132.16
Cauca	26,410.82	19,823.79	-	-	-	46,234.61
Huila	3,596.49	-	-	17,621.15	-	21,217.64
Inter-regional	48,211.08	-	21,245.38	257,084.54	87,857.81	414,398.81
TOTAL	292,523.02	52,863.44	21,245.38	274,705.68	109,723.71	751,061.00

Summary Table – To Date

Organization:	International Organization for Migration/Colombia
Reporting Period:	January 1 st to March 31 st , 2006
New Projects Approved in Reporting Period:	21
New Project Financial Information:	New Obligations US\$751,061.00
Expenses:	US\$3,059,186.44 (Quarter) • US\$42,928,938.73 (To Date)
Projected Expenditure April – June 2006:	US\$3,000,000

Table 5. Total Projects Accumulated To Date (Combined Active and Concluded)

Region	Income Generation	Social Infrastructure and Housing	Education	Health	Institutional Strengthening	TOTAL
Norte de Santander	23	18	19	12	8	80
Santander	25	24	15	19	9	92
Valle del Cauca	27	28	14	15	20	104
Putumayo	14	13	16	12	13	68
Nariño	13	17	26	15	11	82
Caquetá	12	14	11	9	8	54
Chocó	7	17	4	8	4	40
Cauca	11	19	10	6	3	49
Huila	11	10	5	9	4	39
Inter-regional	13	9	30	23	49	124
TOTAL	156	169	150	128	129	732

Table 6. Breakdown of Total Active and Concluded Projects

Region	Income Generation		Social Infrastructure and Housing		Education		Health		Institutional Strengthening		TOTAL	
	Active	Complete	Active	Complete	Active	Complete	Active	Complete	Active	Complete	Active	Complete
Norte de Santander	5	18	-	18	1	18	-	12	1	7	7	73
Santander	4	21	3	21	-	15	1	18	-	9	8	84
Valle del Cauca	5	22	5	23	-	14	1	14	1	19	12	92
Putumayo	2	12	-	13	1	15	-	12	1	12	4	64
Nariño	3	10	1	16	-	26	-	15	1	10	5	77
Caquetá	-	12	3	11	-	11	-	9	-	8	3	51
Choco	1	6	2	15	-	4	-	8	-	4	3	37
Cauca	2	9	8	11	5	5	-	6	2	1	17	32
Huila	2	9	1	9	-	5	1	8	1	3	5	34
Inter-regional	4	9	1	8	15	15	9	14	12	37	41	83
TOTAL	28	128	24	145	22	128	12	116	19	110	105¹	627

Table 7. Direct Beneficiaries by Component and Region

Region	Income Generation	Social Infrastructure and Housing	Education	Health	Institutional Strengthening	TOTAL
Norte de Santander	5,117	15,818	10,531	30,122	38,101	99,689
Santander	5,404	10,859	6,542	20,491	45,005	88,301
Valle del Cauca	9,075	10,226	6,273	24,261	47,294	97,129
Putumayo	2,945	7,913	36,267	35,009	41,834	123,968
Nariño	4,727	11,319	20,610	84,520	13,748	134,924
Caquetá	4,239	26,136	11,622	15,996	22,832	80,825
Choco	2,618	27,045	3,992	15,710	3,150	52,515
Cauca	8,573	14,554	3,924	18,530	8,429	54,010
Huila	2,865	19,761	8,341	12,357	15,276	58,600
Inter-regional	56,337	26,851	20,884	65,572	121,457	291,101
TOTAL	101,900	170,482	128,986	322,568	357,126	1,081,062

¹ A decrease in the no. of projects was registered compared to the accumulated no. in the past quarter due to the cancellation of projects ID-0104, PA-0080, PA-0081, PA-0084 and PA-0086.

Table 8. Obligation by Component and Region (Quarter US\$29,078,205.85)

Region	Income Generation	Social Infrastructure and Housing	Education	Health	Institutional Strengthening	TOTAL
Norte de Santander	858,418.76	727,938.96	381,438.50	267,630.42	145,180.74	2,380,607.38
Santander	850,871.01	1,040,330.50	253,662.08	160,400.25	179,796.16	2,485,060.00
Valle del Cauca	1,214,688.22	1,274,143.40	352,553.73	618,072.67	496,763.18	3,956,221.20
Putumayo	909,733.54	408,799.17	525,396.61	444,841.43	465,338.45	2,754,109.20
Nariño	938,926.23	324,455.53	379,459.43	367,333.33	109,542.08	2,119,716.60
Caquetá	868,248.73	737,172.53	289,768.74	180,616.93	100,125.89	2,175,932.82
Chocó	278,770.31	770,881.08	260,017.16	198,761.22	50,757.07	1,559,186.84
Cauca	501,795.11	794,476.58	239,042.16	182,579.57	163,306.04	1,881,199.46
Huila	148,346.40	435,498.18	214,956.38	134,398.04	73,026.36	1,006,225.36
Inter-regional	1,105,277.38	277,407.83	2,597,630.61	973,490.25	3,806,140.92	8,759,946.99
TOTAL	7,675,075.69	6,791,103.76	5,493,925.40	3,528,124.11	5,589,976.89	29,078,205.85

1. Executive Summary

This past quarter, 21 new projects were approved. Including additions to ongoing activities, a total of US\$751,061.00 was obligated this quarter. As per table 8, to date accumulated project obligations are US\$29,078,205.85. Administrative costs are US\$5,977,666.27 of 92%.

Table 9. Obligations and Disbursements in Assistance Activities

Item	Initial Budget	Obligations	Implemented	Balance for Assistance Activities ²
Projects and Operational Cost	US\$39,737,078.74*	US\$29,078,205.85	US\$33,048,641.67	US\$192,498.11**

* Includes a still-to-be-approved mortgage amount.

** The obligations were higher, taking into account this cost might be absorbed by other Budget Lines of the Program which might not complement each other.

Table 10. Administration

Item	Initial Budget	Implemented To Date	Balance
Administration and Overhead	US\$11,058,037.26*	US\$9,880,297.06	US\$1,177,740.19

* Includes a still-to-be-approved mortgage amount.

General Analysis

In the current reporting quarter of January to March 2006, the “Post-Emergency Assistance to IDPs, Receptor Communities and Other Vulnerable Groups” Program approved 21 new projects with a total value of US\$738,780.08. To date, a total no. of 732 projects and 69 subprojects provide direct attention to 1,081,062 individual beneficiaries. The breakdown by component of assistance provided is: Income Generation 9.4%; Strengthening of Communities and Institutions 33.03%; Health 29.83%; Education and Coexistence 11.93%; and Social Infrastructure and Housing 15.76%. At the end of the current quarter 627 projects had been concluded successfully.

The Program has obligated US\$42,928,938.73 to date, of which US\$3,019,017.39 corresponds to unliquidated obligations in approved activities. Obligations – both pending and fully liquidated – of the current quarter are US\$45,947,956.12 Annex 1 provides additional detail.

Sectoral Analysis

AfroColombians and Indigenous

Since the USAID funded program began, IOM has been implementing projects aimed at providing basic services and alleviating extreme poverty among Afro-Colombians and Indigenous groups who constitute the most vulnerable groups in Colombia.

IOM has been working towards facilitating access to sustainable employment through appropriate professional and vocational training and also contributing to increase family incomes among victims of forced displacement and other vulnerable groups by supporting the creation of micro-enterprises and projects in the farming and livestock sector.

To date a total no. of 101,900 beneficiaries have been supported by the Program through income generating activities. Out of these, 23% are afrocolombians and 2.6% indigenous. This quarter, 80% of the 2,660 beneficiaries in the component were indigenous.

Spotlight On: Project PA-0089 “Strengthening and consolidation of the income generation project for IDP families in Tumaco municipality.” The project has managed to leverage new resources from FOMIPYME which will be used to strengthen training courses in accounts, finance and business and also help in motivating the beneficiaries. The project also seeks to improve the quality of products to facilitate access to markets and credit in the formal sector. The project will benefit 33 displaced Afro-Colombians. USAID’s contribution is of US\$5,595 out of a total budget of US\$46,565.

² The Obligations of Reintegration Survey and Needs Assessment (B2), OVG Reintegration Program and Child Soldiers Massive Demobilization are not included.

Youth – Displacement Prevention

Youth make up to 48% of the displaced population in Colombia. Uprooted from their homes and seeking a safe haven in large urban areas, they face suspicion, hostility, discrimination and lack of access to public services. IOM/USAID has been supporting the Colombian government through the implementation of projects meant to protect and assist youth and prevent them from being easy preys for forced recruitment into illegal armed groups or prostitution rings, sexual violence, teen pregnancy, loan-sharking, extortion and selective murders.

IOM/USAID’s intervention seeks to increase educational opportunities to enable the tapping of their potential and enhancing of their self-esteem so as to reduce the number of children and youth living on the streets.

Spotlight On: Project ID-0108 “Integral Education Assistance to Unschooled Displaced Youth Phase 1.” The promotion of artistic and sports talents and job training and orientation components contained in this project, have been constituted as a prevention strategy against recruitment into illegal groups. The initiative will also fosters necessary attitudes and competencies among the youth which helps them integrate positively and productively into the new socio-cultural environment. The interest and commitment of the Education Department of Soacha was clearly shown by their participation in the Technical Committee and the negotiation for new alliances aimed at increasing support for the sustainability of the project. USAID’s contribution is US\$150,000.00 out of a total budget of US\$171,739.13



Land

The Project Management Unit (PMU) has been planning and preparing the budget and Procurement Plan for all the components and donors that will participate in the second phase of project ID-0088 “Protection of Land and Patrimonial Assets of Displaced Populations in Colombia” (Under PILAS). 38 contracts were extended and nine consultants contracted thereby strengthening the existing field offices. The regional office in Magdalena Medio was inaugurated and a number of required personnel recruited who include: a field liaison consultant, and legal, social and cadastral specialists. The PMU has also established agreements with the Departments of Bolívar, Antioquia, Norte de Santander and Valle de Cauca. These Departments will provide locations for the Project’s field offices.

Private Enterprise

Table 11. Private Enterprise Investment

Region	To Date	This Quarter	Implementing	Completed
Norte de Santander	116,124.91	39,608.93	92,240.50	23,884.41
Santander	-	-	-	-
Valle del Cauca	208,461.70	8,987.71	60,355.63	148,106.08
Putumayo	-	-	-	-
Nariño	33,431.08	-	-	33,431.08
Caquetá	79,622.74	-	-	79,622.74
Choco	4,385.96	-	4,385.96	-
Cauca	411,285.02	-	-	411,285.02
Huila	54,367.31	4,052.63	4,052.63	50,314.68
Inter-regional	395,325.07	-	351,458.90	43,866.17
TOTAL	1,303,003.80	52,649.28	512,493.62	790,510.18

During this quarter, the Program continued consolidating and increasing participation of the private sector in projects supported by IOM. This was done through sensitization, documentation and dissemination of concepts like Corporate Social Responsibility and Socially Profitable Investment among the business community.

Spotlight On: Project ID-0129 “Strengthening of the development and marketing of products made by IDP and vulnerable populations productive business endeavors” was started as part of this initiative. This project seeks to develop a Social Marketing Strategy aiming at offering product development services, promotion and sales, as well as consultancies which will help stimulate productivity, quality and competitiveness among businesses supported during the implementation of the program.

Gender

Women are particularly vulnerable in the conflict involving illegal armed groups in Colombia and are disproportionately affected by internal displacement. Displaced women are usually victims of sexual violence and exploitation. Almost 50% of IDP households are headed by women. IOM recognizes women's pivotal roles in the sustainability and reconstruction of family and community life and the improvement of living conditions. IOM understands the leadership of women to be essential particularly within sectors that have been affected by displacement and subsequent conditions of poverty. The USAID IDP funded Program has been providing support through projects aimed at strengthening government entities response to challenges of women's participation, gender inclusion, and social assistance.

Spotlight On: Project HU-0039 “Dietary Improvement for 300 expectant and lactating displaced women implemented by the Organización Femenina Popular, ‘OFP’ in 9th and 10th communes in Neiva.” This project remodeled, endowed and opened two community restaurants and created a community market garden to supply the restaurants. 200 meals are sold daily at a cost of US\$0.6 each one, which will guarantee sustainability of the project and provide the women with an income. The project is also supporting workshops aimed at strengthening self-esteem, conflict resolution and leadership. The Sur Colombiana University has offered technical assistance for the development of the productive component. On the other hand, the Municipal's Health Department will give assistance to the expectant and nursing mothers and also provide micronutrients to children under the age of twelve, as part of the Basic Assistance Plan “PAB” activities.

USAID's contribution is of US\$17,621.15 out of a total budget of US\$19,779.74.



Return

Projects implemented this quarter mainly assisted rural housing needs with the support of Banco Agrario de Colombia, thereby providing dignified housing solutions to the beneficiary families and also achieving excellent results in community organization and the creation of integration and training spaces.

Progress was made in the implementation of the Integral Reparation Plan in Toribio and Jambalo projects targeting indigenous people from the Nasa community in Cauca. The program is currently implementing projects of income generation, food security, social infrastructure and housing. The beneficiaries are actively involved in the process through provision of unskilled labour and this has generated participation, integration and community organization among host and returnee populations.

Spotlight On: Project VA-0106 “Strengthening of four rural associations made up of 104 returnee families,” aims at supporting the reestablishment of the families through the strengthening of 4 associations constituted in phase 1. This project is a continuation of project VA-0059, “Reconstruction of social and productive capacity of rural communities in Zealandia, La Victoria and La Guinea in Dagua municipality,” which was successfully implemented with the support of Carvajal foundation. The project helped reestablish social organization through food security and also stimulated productive projects and community organization processes.

USAID is contributing US\$24,651.98 out of a total budget of US\$ 215,746.44.



Operating Partners

Table 12. Cost-Sharing Obligations per Partner Type by Region (To Date: US\$54,101,012.13)

Regional Office	Public Sector		Private Sector		Other (Church, local organizations, PIOs, etc.)	Total
	Territorial Entities	State Agencies	Private Enterprise	NGO, Non-Profits, & Mixed Entities		
Norte de Santander	1,462,094.55	384,638.93	116,124.91	1,283,505.76	104,604.79	3,350,968.94
Santander	996,745.81	627,125.84	-	1,040,122.72	365,724.03	3,029,718.39
Valle del Cauca	1,885,104.28	1,993,058.47	208,461.70	1,023,101.03	636,737.43	5,746,462.90
Putumayo	912,070.89	652,900.58	-	230,117.60	350,927.18	2,146,016.24
Nariño	1,190,020.00	753,927.44	33,431.08	327,129.27	246,756.13	2,551,263.93
Caquetá	528,670.31	484,827.84	79,622.74	424,420.32	224,286.59	1,741,827.80
Choco	434,534.70	488,563.23	4,385.96	383,952.72	190,280.14	1,501,716.76
Cauca	1,060,995.04	980,282.08	411,285.02	262,710.12	275,334.50	2,990,606.76
Huila	854,102.79	345,603.78	54,367.31	252,972.74	333,470.43	1,840,517.05
Inter-regional	445,771.44	25,304,734.79	395,325.07	1,784,005.66	1,272,076.40	29,201,913.36
TOTAL	9,770,109.81	32,015,662.96	1,303,003.80	7,012,037.94	4,000,197.62	54,101,012.13


This quarter, 21 projects were approved, 2 of them with new implementing partners from ecclesiastic and non-governmental organizations. Currently, the Program has a total number of 37 entities participating in the projects as either partners or implementers. Noteworthy, are state agencies like FOMIPYME and SENA who make up 37.8% of the entities, followed by the Catholic Church with 13.5%, and private enterprise with entities like the Coffee Growers Committee and *la Central de Cooperativas Agrarias*, 10.8%.

Participation of entities belonging to the public sector constitute 50% while the private sector and other organizations (churches, local and international ones) make up 30% and 20% respectively.

On revising the amount of funds contributed by the new partners, other associates and also implementing partners involved in the Program from before, the highest amount of funds leveraged this quarter are again concentrated in the public sector as was in the last quarter. The sector provided 94% of the co-financing with the Presidential Agency for Acción Social and International Cooperation, (Acción Social), being the highest contributor with a total amount of US\$1,315,789 for institutional strengthening and FOMIPYME with US\$ 916,402 for projects supporting productive initiatives. The entity with the highest contribution in the private sector was the Norte de Santander Coffee Growers Committee with US\$31,083 in the same framework alliance with FOMIPYME.

Graphic 1: National Counterparts

During this quarter, the largest contribution by counterparts came from the Public Sector which included state entities who contributed US\$3,842,257.85³. The largest amount in the Private Sector came from NGOs and Non Profit Making Organizations corresponding to 84% of the sector, Out of the total contribution by counterparts, the Public Sector contributed 78%. The Private Sector 15% and the remaining 7% by International Organizations, local organizations and churches.

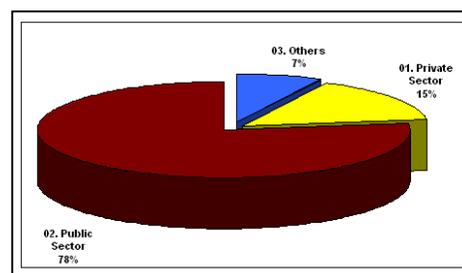

Sustainability

IOM evaluated 83 projects this quarter. The average rating was 4.04, this figure being slightly higher than the one in the previous quarter, which was 3.94. 63.85% of the evaluated activities presented high levels of sustainability, 32.5% average levels and 3.61% low levels. This is the penultimate sustainability evaluation carried out as the Program is due to end in June. The few projects which have not achieved desired sustainable levels will be strengthened in the next three months. During the period that evaluations have been carried out, it has been noted that, the aspects which have contributed most to the consolidation of processes in the course of time have been the commitment of the implementers and the participation of the community in project development. As expected, public order remains one of the key external factor that impacts negatively on the normal development of the projects and which might also affect their sustainability once the activities are

³ Through ID-0126 "Humanitarian assistance to displaced populations with an emphasis on childhood and family in emergency humanitarian assistance and socio-economic stabilization phases," by the Colombian Institute of Family Welfare - ICBF- followed by project ID-0088 by the Presidential Agency for Accion Social and International Cooperation, as well as project CH-0041 and NS-0079 through SENA and finally, 10 projects through FOMIPYME.

finalized. However, the commitment and dedication of the implementers, beneficiaries and partners involved in the projects contribute in reducing the negative effect of this situation in the project.

Visibility

The Colombian First Lady, Lina Moreno, Mr. Milton Drucker, Deputy Chief of Mission, US Embassy, Colombia and Mr. Wataru Hayashi, Japanese Ambassador, officiated in the inauguration of four classrooms, one library and two offices in the Niño Jesus de Praga Education Center in Popayan, Cauca, in February. In addition, USAID donated school supplies and equipment to be used in the “Open Doors” School Strategy developed by IOM. Other donors included *Plan Padrino* of the Office of the President, the Embassy of Japan, the National Federation of Coffee Growers, the Education Department of Popayán and the Tehillin Children’s Foundation.

Congresswoman Nita M. Lowey visited the Aqueduct of Rionegro, Popayan, Cauca, a project funded by USAID in February. During the visit, she was accompanied by Mr. Drucker, Deputy Chief of Mission, US Embassy, Colombia, Ms. Liliana Ayalde, USAID Director, Colombia, and IOM representatives. She was received by beneficiaries from 9 *Veredas* of the Popayan municipality.



The project provides water to 4,000 families who belong to displaced and vulnerable populations. The initiative has also improved the organization and participation of the community as they were all involved in the process.

The “*Curese en Salud*” campaign of the IDP health assistance was launched in January where IOM, the Presidential Agency for Acción Social and International Cooperation, the Ministry of Social Protection and the University of Cauca attended. This campaign is a result of the T-025 Constitutional Court’s Sentence in 2004, which seeks to guarantee the fundamental rights of displaced people by providing them with improved services such as health.

Security

This quarter, only Putumayo and Norte de Santander reported incidences that impacted negatively on on-going projects.

In Putumayo, an armed blockade by the FARC guerilla group was initiated on the 3rd of January upto the 10th of March and this affected field travel for some of the project operators, which in turn caused delays in the implementation of activities. The projects affected were: PU-0063, “Installation of productive projects in the Provincial Centre of the Amazonic Piedmont, identified and prioritized in the ID-0019 framework under the Baldios titling program.”; PU-0067, “Implementation of the Sole Integral Plan (PIU) in the department of Putumayo and its consolidation as public policy at a departmental and municipal level.”; PU-0066, “ Strengthening of the peasant organization in its interaction with farming and livestock colleges aimed at developing a regional development model for the lower Putumayo region.”

In Norte de Santander, the reception of the works on project NS-0056 “Protection and Education reestablishment in the corregimientos of Cartagenita, La Trinidad, Honduras, La Motilona and San Juancito in Convención and Teorama municipalities” and the final visit for NS-0077, “Construction of the first phase of the sewage system of the Corregimiento of La Gabarra, in Tibú Municipality” were not carried out due to the security situation in the area.

The crisis began in the last quarter with the holding of several armed blockades by FARC. Armed actors then expressed their discontent over the presence of humanitarian aid organizations in the area which was initially communicated to ICRC. Two MSF (Médicos Sin Fronteras) expatriates were thereafter detained for several days by FARC which forced the organization to leave the area. Two World Food Program (WFP) functionaries were also detained and their vehicle and communication equipment confiscated.

2. Displacement Notes

A. National

According to official SUR statistics, an accumulated no. of 1,784,626 IDPs were registered by the end of March, 2006. A total number of 20,004 people were displaced in the quarter.

The departments with the highest accumulated receptor figures are Antioquia with 263,559, Bolívar 125,417, Bogotá D.C 114,568, Sucre 112,308 and Magdalena, 104,313.

The departments with the highest accumulated expulsion numbers are Antioquia with 304,111, Bolívar 178,759, Magdalena 123,187, Cesar 111,193 and Chocó, 96,159.

During the quarter, the five departments with the highest reception numbers nationally were: Bogotá D.C., Huila, Cundinamarca, Córdoba and Santander. Bogotá moved from third position in the last quarter to first position in the current one.

The top three receptor departments with IOM's presence were: Huila 2,129, Santander 1,394, and Nariño 1,163.

The main expelling departments nationally were: Tolima, Meta, Caquetá, Antioquia and Bolívar.

The top three expelling departments in areas covered by IOM were: Caquetá 1,390, Nariño 982 and Huila 950.

IOM Departments and Zones

Norte de Santander: This quarter, the humanitarian intervention has been under serious threat from illegal armed actors particularly from the guerilla group, FARC. This group has expressed its discontent on the presence of international organizations in the rural areas of Catatumbo and has been involved in acts of aggression against several organizations namely OXFAM GB, Médicos Sin Fronteras-MSF, WHO and UNODC. Several members of staff working with these agencies have been detained in the rural areas of Convencion, Tibú and Sardinata. The most serious case was the detention of two MSF employees for seven days and a female doctor for two days where she was forced to attend to injured guerillas. ICRC has also suspended all its missions in Cataumbo for security reasons.

WFP suspended food supply to IDP and vulnerable groups through the territorial unit of Acción Social in the department following denouncements made by the beneficiaries and evidence found by WFP of irregularities in food distribution administered by Acción Social's workers.

During the quarter, fierce combats between illegal armed groups and public forces occurred in Tibú, Sardinata, Hacari, Teorama, San Calixto and Bucarasica, causing forced displacements, deaths and captures.

Illegal armed actors also carried out attacks on petroleum, electrical and road infrastructure in Tibú. Furthermore, they also imposed armed blockades causing transport problems.

An increase in the presence of paramilitary groups in some municipalities and a generalized rise in cases of extortions in the province of Ocaña has also been noted.

Selective killings are still going on with 73 cases reported in Cúcuta. Other cases of massacres and threats directed at journalists have also been reported.

According to SUR official data, Norte de Santander has received an accumulated no. of 55,293 people since 1996. The municipalities with the highest accumulated reception numbers are Cucuta 33,230, Convencion 7,783 and El Tarra 3597. The municipalities with the highest accumulated expulsion rates are Tibu 20,862, El Tarra 10,977 and Convención 8,280.

Santander: During the quarter, the region that presented significant events related to conflict and displacement was Magdalena Medio.

Despite the fact that the paramilitaries belonging to the Central Bolívar faction (BCB) were supposed to have demobilized, several actions have been attributed to them in the area according to information compiled by the *Observatorio de Paz Integral de Magdalena Medio*. Although there has been a considerable decrease in cases of selective killings, threats and disappearances, there has been a notable increase in warlike activities which is affecting the well-being of the civil population in the region.

Various confrontations involving the Colombian Armed Forces and illegal armed groups were reported in Cantagallo, San Pablo, Santa Rosa and Yondo municipalities.

According to the National Ombudsman office in Magdalena Medio, the civil population living in the southern part of the department have forwarded complaints over the creation of a new group made up of 300 demobilized paramilitaries and denominated as 'Las Aguilas.'

The following cases were also reported in the quarter: 11 homicides in Barrancabermeja, Aguachica, Yondo and Cantagallo; 11 cases of threats directed especially at the rural 'campesinos' living in the Notepases *veredas* in the Yondo municipality, according to a declaration made by the Rural 'Campesino' Association of Valle del Rio de Yondo and also at community leaders; 7 cases of kidnapping attributed to FARC and ELN and; destruction of property belonging to civil population on the Bucaramanga – Atlantic Coast route, an occurrence noted not to have taken place in the past three years.

Data obtained from SUR indicate that the department has received an accumulated no. of 73,197 people since 1996 and still ranks 9th nationwide. The municipalities with the highest accumulated reception nos. are Bucaramanga 25,320, Barrancabermeja 21,422 and Floriablanca 7,332. The department ranked second in reception rates this quarter. The municipalities with the highest accumulated expulsion figures are Barrancabermeja 14,312, Saban De Torres 2,660 and Puerto Wilches 2,262.

Valle del Cauca: A wave of political violence was experienced by candidates of municipalities in Buenaventura, Yumbo and councillors of Sevilla and Tulúa during this quarter. Massacres were also reported in the northern part of the department. Armed activity involving *Autodefensas* and guerrilla groups have also been reported. Despite AUC's demobilization and surrendering of territories, there are signs of territorial reconfiguration and renewed takeover in Dagua, Buenaventura as well as the in the northern part of the department. According to the OAS quarterly report, a resurgence of new groups with a "contra insurgent ideology" has appeared in Buenaventura, Riofrío, Tulúa and in areas bordering Chocó.

The department has an accumulated no. of reception of 103,323 people since 1996 and ranks sixth nationwide. The municipalities with the highest accumulated reception nos. are: Buenaventura 35,172, Cali 32,913 and Tulua 7,619. The municipalities with the highest accumulated expulsion figures are Buenaventura 31,252, Tulua 8,043 and Jamundi 5,030.

Putumayo: Since January, the department has been experiencing an armed blockade imposed by FARC which has generated violent incidents that have affected infrastructure and the civilian population too.

Following is a summary of incidences that took place in the department in the quarter: Constant electrical power outages caused by attacks on power towers; illegal traffic holds ups carried out on the Puerto Asis– Orito , Valle del Guamuez – San Miguel and Mocoa – San Juan de Villalobos, Cauca; 20 vehicles burnt and 2 bridges blown up on the Puerto Asis – Vereda Teteyé road and another one in San Miguel municipality; the Transandean oil pipeline dynamited in several points between the Puerto Asis and San Miguel municipalities ; and caravans of vehicles escorted by public forces attacked, this affecting both civilians and the forces.

All these occurrences have paralyzed river and road transport causing serious food and fuel shortages in the department. The government has imposed a curfew between 18.00hrs and 05.00hrs and established escorts for vehicle caravans.

Lastly, 500 members of AUC demobilized in the corregimiento of Santana, Puerto Asis municipality.

By the end of March, the department had an accumulated reception figure of 42,208 people. The municipalities with the highest accumulated reception figures were: Mocoa 13,869, Puerto Asis 10,887 and La Hormiga 4,034. The municipalities with the highest accumulated expulsion rates were Puerto Asis 18,271, La Hormiga 14,456 and Orito 9,017. The department ranked sixth in expulsion rates nationwide.

Nariño: During the first quarter of 2006, the offensive against drug-trafficking was intensified through the eradication of illicit crops with a total no. of 53,000 coca plants eradicated manually and 550 gallons of liquid coca, 2 tonnes of cocaine hydro chlorate and 1,499 kilos of cocaine seized; interruption of illegal road blocks and the confiscation of arms ; and the deployment of DAS, the Central Intelligence Service, and the National Police through the illicit crop eradication program. 15 people were reported dead among them 9 guerrilla members, 1 soldier and 5 policemen and 8 people injured, 6 of them civilians and several arrests made during the operations.

Other noteworthy events that affected the department during the quarter were: violence caused by street gangs, through threats and retaliations; 3 people died through various attacks and a series of assassinations were also carried out in Tumaco for unknown reasons.

An armed blockade was declared end of February aimed at impeding people from participating in the March elections for Congress. This resulted in 3,500 members of the police force being deployed to counter the action.

The Ecuadorian Military Unit on the Colombian/Ecuador border increased security measures aimed at preventing the Colombian armed conflict by illegal actors from spilling over into its borders.

The United Nations also declared Colombia as the main producer and exporter of cocaine in the world and named Nariño as the department with the highest concentration of illicit crops with a total number of 55,000 hectares with coca bushes.

The department has received an accumulated no. of 51,985 people since 1996 according to SUR latest data. The municipalities with the highest accumulated reception figures are: Pasto 19,317, Tumaco 6,902 and Samaniego 4,206. The department ranked third in receptions this quarter.

The municipalities with the highest accumulated expulsion nos. are: Tumaco 7,681, El Charco 5,786 and Barbaçoas, 4,315. The department ranked second in expulsions this quarter.

Caquetá: The municipalities with the highest no. of expulsions in the quarter were Cartagena del Chairá, Valparaíso and Puerto Rico. The main cause of displacement, especially in Cartagena del Chairá is due to the fact these are areas where frequent operations by the Colombian Armed Forces are carried out under “*Plan Patriota*” (lower Caguán area). Due to the restrictions in movement and limitations in food and medical supplies, the habitants in the rural areas of these municipalities are obliged to displace to the peri-urban areas of municipalities and eventually to other parts of the department.

Displacements in other municipalities have been caused by fear created by FARC’s armed blockades and the increased recruitment of rural children by illegal armed groups. The blockades were used to bar the population from participating in the electoral campaigns and have also seriously affected the socio-economic situation of the department. Cases of vehicles being burnt and attacks on convoys under escort have been frequent.

Threats directed at traders and closure of business premises especially in San Vicente del Caguan and Puerto Rico, have reduced transport of livestock, milk and cheese which are the main sources of income of the region.

According to sources, there is a large number of displaced people in the department who are not registered with Acción Social.

According to SUR statistics, the department has received an accumulated no. of 45,301 people since 1996. The municipalities with the highest accumulated reception nos. are: Florencia 34,389, Puerto Rico 1,684 and Cartagena del Chaira 1,632. The municipalities with the highest expulsion figures are: Cartagena del Chaira 10,400, San Vicente del Caguan 9,057 and Florencia 8,779. This quarter, the department had the highest expulsion rates in departments with IOM’s presence and was ranked seventh in accumulated expulsions rates countrywide.

Chocó: This quarter, the humanitarian crisis worsened due to the armed strike declared by FARC at the end of February. The communities affected most by restrictions to access and movement were from the the Embera Wounaan indigenous groups. These communities are located on the road between Quibdó and Medellín: El 18, Matecaña, and el Consuelo (Carmen de Atrato municipality), el 20, el 21, and el 90 (Quibdó municipality). As a consequence of the blockade, confrontations between the guerrillas and Colombian Armed forces took place where an indigenous woman was injured, a driver killed and several vehicles transporting fish burnt.

Several power towers were also blown up and a considerable number of fields mined causing one death and various injuries. Several indigenous people have been mistreated by the illegal groups trying to obtain information on suspected informers.

These events have resulted in food shortages for indigenous and afrocolombian communities living in the area. Education and health services have also been paralyzed since no vehicles are allowed to enter the area.

Several violent incidents were also reported during the electoral period. In Bagadó ,where several combats between the army and guerrillas have taken place, a child was killed and 4 adults injured during a guerilla incursion.

An S.O.S appeal was launched through a communiqué issued end of March, by the Diocese of Istmina, the Federation of Community Councils Organizations and Afro-Colombian Organizations of San Juan, the Human Rights Network of San Juan, the National Ombudsman, the *personería del medio San Juan*, *personería de Istmina*, (*personería* is an entity of the Public Ministry), the Association of Indigenous Authorities of the Wounaan-Nonan community, the Pacific Indigenous District Councils Association and the Regional Embera Wounaan-Orewa Organization. This was done to seek help in order to avoid further deaths caused by the war declared by illegal armed actors against the civil population living in the middle and lower areas of San Juan. They also made a denouncement on human rights violations and infringement against the International Humanitarian Law by the illegal groups. They reported 20 deaths, and cases of widespread tortures, disappearances, and threats which have caused terror and anxiety among the habitants.

The department had received an accumulated no. of 62,684 people by end of March. The municipalities with the highest accumulated reception rates are: Quibdó 28,783, Bojayá 9,385 and Rio Sucio, 8, 067. The municipalities with the highest accumulated expulsion rates are: Rio Sucio 25,273, Bojayá 15,283 and Quibdó 13,194.

Cauca: During the quarter, various events were reported that affected public order in the region, namely: final electoral campaign period for the Senate and Congress; threats made by FARC and directed at the civil population aimed at discouraging them from participating in the elections held in March; the increased presence of public forces in the Toribío, Jambaló and López de Micay municipalities which drew reactions from the guerilla to counter the move; the determination shown by all municipalities to continue supporting the government's democratic security policy so as to ensure a peaceful electoral period.

Although combats and attacks by illegal armed actors in rural areas of Toribío, Jambalo and Silvias were reported which raised alarm among the area residents, no massive displacements took place.

There was an increased demand for support in the Assistance and Orientation Unit in Popayan despite there being no major displacement reported in the quarter. The reason could be due to an increase in individual displacements.

According to SUR data, the department has received an accumulated no. of 44, 599 people since 1996. The municipalities with the highest accumulated reception figures are: Popayan 18,821, Silvia 7,600 and Santander de Quilichao, 2,804. The municipalities with the highest accumulated expulsion nos. are: Toribio 9,288, El Tambo 6,960 and López 4, 899.

Huila: The most serious incident this quarter was the assassination of nine councilors of Rivera municipality presumably by FARC's Teófilo Forero Mobile Column.

According to the local press, as a result of the massacre, the National Government reinforced its security presence to principally combat FARC's Teófilo Forero Mobile Column in Huila. Owing to the military counteroffensive activities, several militants were killed or captured and some FARC's camps dismantled mainly in Algeciras, Pitalito, Campoalegre, Riviera and Nieva.

For the last two years, the critical situation of public order in Algeciras has forced the councillors of this municipality to perform their duties from Nieva municipality. No signs of a let up are in sight.

In another noteworthy incidence, guerrilla groups prohibited transporters to transit through the department towards Putumayo and Caquetá.

The department has received an accumulated no. of 34,766 people since 1996, according to the latest SUR figures. The municipalities with the highest accumulated reception figures are: Neiva 17,829, Pitalito 4,959 and Garzón 2,468. The department had the highest no. of receptions this quarter in areas with IOM's presence. The municipalities with the highest accumulated expulsion nos. are: Algeciras 3,434, Neiva 2420 and Colombia 2,329.

3. Program Components

A. Income Generation

Update for the Quarter: Most of the activities in the component during this quarter were mainly concentrated on the liquidation and finalization of projects. This process included awards of capital funds and the definition of sustainability plans for others. One of the main highlights in the component was the initiation of the implementation of 10 projects co-financed by FOMIPYME at a total cost of US\$1,200,606.21, where IOM/USAID will provide US\$141,049.81. This means each 1USD contributed by IOM/USAID will be leveraged with US\$8.5.

Update by Subcomponent: Special projects. The final implementation phases of projects ID-0079-02 “Design and implementation of the Regional Centers of Orientation for IDPs, vulnerable population, entrepreneurs and micro-enterprises ‘CRODEMS’ Phase 1” and ID-0099 “Design and implementation of a tailor-made Ambient Web Software for registration, control and oversight of holdings” were scheduled to finalize last quarter but are both still undergoing programming adjustments which will serve as tools for the strengthening of the Units for Attention and Orientation and the respective implementing agencies. Project ID-0072-02 will be carrying out tests at a national level and be connected to the CRODEMS system in Acción Social and on the other hand, ID-0099 will continue being tested by implementing partners.



The deadline date for participation in IOMs award for “innovative and successful management of intervention models for socio-economic stabilization of IDPs and vulnerable populations,” was 30th March, 2006. The award is meant to stimulate the best IDP entrepreneurial projects implemented by operating entities, as well as successful IDP entrepreneurs.

Food Security

This component continues with its strategy of strengthening the social fabric through training activities and the supply of agricultural inputs that will stimulate the permanence of the vulnerable population in the countryside. In this context, project NS-0081 “Strengthening of the social fabric through food security for marginalized rural population in 9 municipalities in the middle basin of River Catatumbo,” was initiated. On the other hand, project CA-0057 “Emergency food assistance in San Vicente del Caguan and Puerto Rico in Caqueta” foresees the improvement of institutional response to food emergencies for displaced populations in these municipalities. These two projects are part of the framework agreement with Acción Social.

Labor Training for Employment

Part of the success of the projects in this subcomponent can be attributed to the linkage with strategic partners who insure the achievement of the planned objectives. This quarter, the component built further closer inter-institutional ties with SENA through the implementation of two projects, CH-0041 “Phase 1 of improvement and endowment of the productive development center of the timber chain in SENA for technical training of displaced and vulnerable populations in Chocó”, aimed at improving SENA’s capacity in the training of wood transformation processes and NS-0079 “Job Training Project” whose objective is to train and find job placements for 250 persons in the Cucuta, Ocana, Tibu municipalities and the *corregimiento* of Gabarra.

Spotlight On: Projects CU-0050, HU-0038, PA-0088, PA- 0089, NS-0082, PU-0068, SA-0093, SA-0094, VA-0105, and VA-0106. As mentioned earlier, 10 projects co-financed by FOMIPYME were initiated this quarter. IOM/USAID will provide funds for the initial activities. The implementation of the second phases of these projects will consolidate previous joint efforts involving IOM’s operators. They are mainly focusing on strengthening both individual and associative productive units as well as some of the micro-credit funds that support them. This will be carried out through improved productive and technical processes, training, marketing and management. Activities are being carried out in Cauca, Santander, Norte de Santander, Huila, Valle de Cauca, Narino and Putumayo. USAID will contribute US\$141,049.81 out of a total budget of US\$1,200,606.21.



B. Social Infrastructure and Housing

Update for the Quarter: The component is working towards finalizing projects which are currently under implementation and exit strategies have been established for each one of them.

During this final stage, a close coordination has been achieved involving counterparts, operating partners as well as beneficiaries through oversight committees aimed at overcoming obstacles that might arise. Relations between public institutions and the community have been improved and spaces for dialogue created which, will also serve in resolving disputes in future. During the quarter, the component supported a total no. of 1,253 urban based beneficiaries.

Update by Subcomponent: Housing: This quarter has been dedicated to rehabilitating urban housing geared at improving the living conditions of families in Buenaventura. The intervention has concentrated on ameliorating sanitary units, kitchens, structures, floors, roofs and carrying out activities aimed at solving the serious problem of overcrowding that face these communities. These type of projects are immersed in adverse social scenarios where the living conditions, overcrowding and the precarious level of insalubrity causes social and health related problems for IDP and receptor families that live in these neighbourhoods. Through the implementation of these type of projects, the standard of living for the population is improved and the level of vulnerability reduced.

Basic Sanitation: With the exception of project CA-0056, all the construction works of projects in Basic Sanitation have been finalized. During the quarter, community workshops were held on proper water use, hygiene habits and appropriate maintenance of the constructed systems. The communities were also sensitized on health issues since the key objective of these works is to reduce morbidity and mortality rates among the community.

Environment

Project VA-0098 “Improvement of 300 housing units in Buenaventura,” deserves highlighting for its socio-economic impact through the creation of temporary employment for the habitants in areas where the project is being implemented. This has enabled the project to achieve its objective of improving the economic conditions for both the displaced and host populations and has additionally allowed integration among the populace. The project will benefit 1,500 afrocolombians.

Spotlight On: Project CA-0056 “Construction of sanitary sewage systems for displaced and receptor population housing in La Sardina, El Portal, Villanueva, Palmeras Altas, Castillo y El Minuto de Dios neighbourhoods in Florencia, Caqueta.” This project is being implemented under the municipal development plan for Florencia and has been a result of joint effort involving various institutions which include: the Regional Government of Caqueta, the Municipality of Florencia, IMOC, SERVAF, Department of Municipal Planning and *Fundación Picachos*. The role played by the beneficiaries in the project is noteworthy. The project is a response to the serious waste water problem in the Nororiental Commune which is the biggest IDP and vulnerable population settlement in Florencia.

The project not only stands out for the positive impact it will have on the environment directed at conservation of water sources in the area, but also the acceptance it has received from different quarters. This can be observed from the commitment demonstrated by the Communal Action Committee and the local habitants in the organization and development of activities and also the commitment of institutions involved not only through funding but also through active participation in technical and operational committees which are meant to do the follow up. The management of the sewage system will be carried out by the Public Services Company of Florencia – SERVAF S.A.E.S.P a reputable company in the department and thus guarantee proper management and sustainability.

USAID’s contribution is of US\$129,310.34 out of a total budget of US\$313,905.59



C. Education and Co-Existence

Update for the Quarter: This quarter, Institutional strengthening was achieved through project ID-0096 “Integral education assistance for internally displaced people” when departmental and/or municipal committees which will monitor the implementation of flexible education modules (accelerated apprenticeship, CAFAM and psycho-social assistance training) were set up and started functioning in the nine regions with IOM’s presence. These committees are made up of members from departmental and municipal education departments, territorial units of Acción Social and IOM. Their main task will be to make sure that the planned interventions are properly orientated and suit the needs of the population.

Two modules (introductory and module 1) were designed and approved under ID-0108, “Integral education assistance for unschooled urban youth phase 1,” through which the education proposal will be structured. This project is of great importance as it demonstrates the significant progress made in the designing and implementation of new and flexible proposals.

A total number of 3,798 beneficiaries were attended to mainly in urban areas.

Documents related to the “Open Doors” School Strategy were compiled, the layout for the publication designed and a publishing house selected for the editing. The publication should be published by May, 2006.

Update by Subcomponent: Transfer of education models: 1,650 children have been attended to under ID-0096 through the implementation of the accelerated learning module in educational institutions in Narino, Huila, Caqueta, Santander, Cauca and Norte de Santander. Likewise, 66 teachers underwent training in accelerated learning and 30 in the CAFAM methodology.

Infrastructure and endowment: This quarter, the construction of the day care center, “La casa de su niño” funded by the Carla Cristina Foundation under project ID-0125 and the infrastructure works of the Gabriel Garcia Marquez Educational Institution in Soacha, in project ID-0106 were concluded.

Spotlight On: Project ID-0127, “Second International Congress for New Schools Program.” The project supported the holding of the Congress which was attended by national and international experts, academic staff and investigators among other people interested in the development of the program. Progress made by the program in Colombia and other countries was discussed and so were the best practices and lessons learnt. The evolution of the program in new contexts and highly vulnerable school populations was also deliberated on and the importance of the strategy in the promotion of basic and civic competence highlighted. The inputs from the event helped strengthen the knowledge of IOM’s regional teams who have been implementing the model among displaced and vulnerable populations.

USAID contributed US\$13,215.86.

D. Health

Update for the Quarter: In the first quarter of the year, 3,939 persons living in urban areas received health services through the implementation of 13 projects, out of whom, 82% were IDPs and 56% women. The projects are being implemented in Sierra Nevada and Serranía del Perijá, Pasto, Forencia, Mocoa, Cali, Bucaramanga, Cúcuta, Neiva, Quibdó and Popayan.

Agreements for the implementation of two projects were formalized: ID-0128 “Endowment of children’s restaurants in the Cúcuta municipality,” which will help to improve the nutritional status of 2,184 children, 77% of them belonging to displaced families. The second project, ID-0128 “Mobile Units,” will allow the strengthening of ICBF at a national level and consequently provide assistance to 40,000 people, especially children, youngsters, expectant and nursing mothers located in areas with inadequate health services. As a result, the beneficiaries will be linked to family and community social assistance projects.

Update by Subcomponent: The loss of protection and support networks caused by displacement has a greater negative impact on women and children and makes them more vulnerable to sexual abuse. The absence of subsistence conditions generates frustration, suffering and hopelessness thereby increasing violent responses in everyday life. Forty-nine territorial forensic multipliers of the National Institute of Legal Medicine were set up in the Sexual and Reproductive Health sub-component. These will facilitate forensic medicine assistance and as a result, access to justice for victims of sexual and domestic violence.

The Ministry of Social Protection initiated training in detection and assistance of mental health disorders and physical abuse for doctors, nurses and psychologists, as part of activities in ID-0120. These were carried out in Quibdó, Bucaramanga and Cali. The planning for provision of services through agreements involving territorial health authorities was also realized.

Acción Social provided support in the strengthening of local capacity in the prevention and assistance of psychological and psychosocial disturbances which cannot be handled by the affected population. This was carried out through project ID-0121 in the Health Sector Strengthening sub-component and involved a twenty hour training for forty-three (43) psychosocial operators in Neiva and forty (40) in Popayan. On the other hand, eighty-three health workers received emotional support through collective therapies which are meant to “humanize” the assistance.

The Kogui, Arhuaca, Yukpa, and Kankuamon indigenous communities located in Sierra Nevada de Santa María and Serranía del Perijá discussed the experience obtained through the healthy environment intervention in their culture. This involved adapting the “Healthy Home” PAHO/WHO strategy and instruments with a participation of 25 community representatives, the Ministry of Environment, Housing and Territorial Development, IPS DUSAKAWI and the Departmental and Municipal Health Secretariats. The implementation of the strategy will improve basic sanitation and hygiene in five (5) indigenous areas through the designing of an education strategy meant to promote healthy habits in the use of water, waste management and prevention of household accidents.

Both the 2003-2006 Institutional Indicative Plan and the strategies of ICBF’s programming consider IDP emergency assistance and socio-economic reestablishment as priority. IOM/USAID provides support to ICBF aimed at strengthening and improving its response capacity especially for IDP and vulnerable families and children.

Spotlight On: Project ID-0126 “ICBF Mobile Units”, seeks to promote psychosocial assistance by integrating specialized services with three (3) professionals in psychology, nutrition, social work and one optional one in Master of Arts, Occupational Therapy, Sociology or Anthropology. The professional team will assist people living in areas that are difficult to access due to violence or natural disasters. The coordination is being carried out by ICBF area centers and articulates strategic alliances with local authorities, health and education sectors and NGOs in order to widen the protection service network for families. 220 professionals will be employed for the 54 mobile units. USAID will contribute US\$ 233,771.93, and ICBF US\$1,359,193.82

E. Strengthening of Institutions and Communities

Update for the Quarter: This quarter, the Institutional and Community Strengthening component contributed towards the processing, dissemination and development of specialized information systems for displaced and vulnerable populations. The data collected includes surveys on the socio-demographic profiles of displaced persons, reasons behind their migration, information on the characteristics of the Afro-Colombian population in areas covered by OIM and information on priority projects for IDPs. The data will assist in the provision of discriminated information by different institutions which will reflect their work and offer an appropriate vision of these population sectors to the Colombian society. This activity supported data collecting on social, economic, demographic and cultural characteristics regarding the conditions of the displaced population and also promoted the participation of the vulnerable population in the 2005 population census and strengthened the capacity of information dissemination on the subject in the mass media in the country. To date, the component has supported 357,126 beneficiaries this being the highest no. out of the five components.

Update by Subcomponent: IOM continued providing support to the National Secretariat of Social Pastoral through the Institutional Strengthening component, for the implementation of the RUT information system and the expansion of the number of surveys carried out.

The manual on “Responsible Journalistic Coverage of Internally Forced Displacement” published by the NGO “Medios para la PAZ” with IOM’s support was presented to journalists and faculties of Social Communication. Support was also given to the National Department of Statistics, DANE, to promote the participation of Afro-Colombians in the 2005 population census.

IOM also supported the development of Sole Integral Plans (SIPs) for IDP assistance in Putumayo and Nariño. This was carried out through the Regional Capacity Strengthening component. The Program is also assisting the Valle de Cauca regional government to develop 15 municipal SIPs.

Spotlight On: Project PA-0087 “Support to the Departmental Government of Nariño in the management of the Sole Integral Plan of Reestablishment (PIUR) strategy and commencement of the implementation of projects.” The objective of this initiative is to continue with the *PIUR* processes, conduct follow up and evaluation on projects being implemented, taking into account the socio-economic dynamics of the region. The key objective of the project is to continue with the resource management phase for the implementation of the *PIUR* projects in 10 IDP receptor municipalities in Nariño identified during the process, offer accompaniment and follow-up to projects under implementation, coordinate participatory and decision making activities and identify new municipalities, projects, operators and beneficiaries. The pilot project developed in Nariño through *PIUR* has strengthened the identification capacity of the population’s needs in a more coordinated and joint manner as well as being able to articulate interinstitutional activities. It has also created a reestablishment strategy in a more efficient and permanent manner which will facilitate access to improved socio-economic conditions to IDPs through the implementation of projects in local economic development, housing and social management components.

USAID is contributing US\$21,865.90 out of a total amount of US\$63,838.62.

During the quarter, follow up was done on the development of the project financed by *UTEC* (Joint Technical Unit assigned to Acción Social) in the Cordoba municipality denominated as “Socio-Economic Alternatives for Food Security and Income Generation,.” and meetings with the Municipal Committee for IDP assistance also held.

An assembly of beneficiaries of an urban housing project in the Pasto municipality was also held whose aim was to provide information on the updates and agreements made with other cooperating institutions among them IOM and ARD.

4. Next Quarter Priorities

1. Coordinate all activities aimed at finalizing projects still undergoing implementation through strict adherence to the work schedule and follow up on the compliances of counterparts.

Annex 1.

Financial Report

Annex 2.

Glossary

OPS: Organización Panamericana de la Salud - PAHO: Pan-American Health Organization
 SAT: Sistema de Alerta Temprana - Early Warning System
 EPL: Ejército Popular de Liberación - Popular Liberation Army
 ERG - ELN: Ejército Revolucionario Guevarista - Ejército de Liberación Nacional - 'Guevarista'
 Revolutionary Army - National Liberation Army
 FARC-EP - Fuerzas Armadas Revolucionarias de Colombia - Ejército Popular - Colombian
 Revolutionary Armed Forces
 SUR: Sistema Único de Registro - Sole System for Registry
 EPS: Entidad Promotora de Salud - Health Promotion Entity
 IPS: - Institución Prestadora de Salud - Health Lending Entity
 RIAS: Red Integral de Atención en Salud - Health Assistance Integral Network
 PAB: Plan de Atención Básica - Basic Assistance Plan
 SNAIPD: Sistema Nacional de Atención a la Población Desplazada - National Assistance System for
 Internally Displaced Populations
 Agencia Presidencial para Acción Social y Cooperación Internacional (Acción Social) – Presidential
 Agency for Acción Social and International Cooperation (Acción Social)
 ICBF: Instituto Colombiano de Bienestar Familiar - Colombian Institute of Family Well-Being
 UAO: Unidad de Atención y Orientación - Assistance and Orientation Units
 SENA: Servicio Nacional de Aprendizaje – National Service of Learning
 DNP: Departamento Nacional de Planeación - National Department of Planning
 DANE: Departamento Administrativo Nacional de Estadística – Administrative Department for
 National Statistics
 CRC: Cruz Roja Colombiana - Colombian Red Cross
 FOMIPYME:- Fondo de Desarrollo Tecnológico de la Micro, Pequeña y Mediana Empresa -
 Technological Development Fund for Micro, Small and Medium Enterprises
 IMEBU:- Instituto Municipal de Empleo y Fomento Empresarial del Municipio de Bucaramanga -
 Municipal Institute for Employment and Business Fostering, Bucaramanga
 CRODEMS:- Centros Regionales de Orientación para Desplazados, Población Vulnerable,
 Emprendedores y Micro-Empresarios -Regional Orientation Centres for IDPs, At-Risk Populations,
 Micro-Enterprises and Entrepreneurs
 CORPOMIXTO:-.Corporación Mixta para el Desarrollo de las Micro-Empresas - Mixed Corporation
 for Micro-Enterprise Development
 Fiscalía General de la Nación: Director of Public Prosecutions/Attorney General
 Defensoría del Pueblo: - National Ombudsman
 Procuraduría Judicial Agraria: Agrarian Judicial Attorney
 Registraduría Nacional del Estado Civil: National Registry for Civil Status
 Registraduría General de la Nación: General Registrar's Office
 ACNUR: Alto Comisionado de Naciones Unidas para Refugiados - UNHCR: United Nations High
 Commission for Refugees
 UNODC: Oficina de las Naciones Unidas contra la Droga y el Delito - United Nations Office on Drugs
 and Crime
 UNICEF: Organización de las Naciones Unidas para la Infancia – UNICEF: United Nations Children's
 Fund
 MSF: Médicos Sin Fronteras – Doctors Without Borders
 OES: Organización de Estados Americanos – OAS: Organization of American States
 UNIPA: Unidad Indígena del Pueblo Awa – Indigenous Unit of the Awa Community

CICR: Comité Internacional de la Cruz Roja – ICRC: International Committee of the Red Cross
PIUR: Plan Integral Único de Restablecimiento - Sole Integral Plan for Reestablishment
INCODER: Instituto Colombiano de Desarrollo Rural – Colombian Institute for Rural Development
ESE: Empresa Social del Estado – State’s Social Enterprise
OCHA: Oficina de Coordinación de Asuntos Humanitarios – Office of the Coordination of Humanitarian Affairs
PMA: Programa Mundial de Alimentos – WHO: World Food Programme
UXOs: Unexploded Ordnances
ITS: Infecciones de Transmisión Sexual . STDs Sexually Transmitted Diseases
DASALUD: Departamento Administrativo de Salud – Administrative Department for Health
ADR: Asociación de Desarrollo Rural en Colombia - ARD: Association for Rural Development in Colombia
UDAPV: Unidad de Atención a Población Desplazada y Vulnerable – Unit of Assistance for IDPs and At-Risk Populations

Annex 3.

List of Operators

Item	Name	Partner Type
1	Agencia Presidencial para la Acción Social y la Cooperación Internacional	Sector Público
2	Alcaldía Municipal de Algeciras	Sector Público
3	Alcaldía Municipal de Barbacoas	Sector Público
4	Alcaldía Municipal de Barrancabermeja	Sector Público
5	Alcaldía Municipal de Belén de los Andaquíes	Sector Público
6	Alcaldía Municipal de Bojayá	Sector Público
7	Alcaldía Municipal de Bucaramanga	Sector Público
8	Alcaldía Municipal de Buenaventura	Sector Público
9	Alcaldía Municipal de Buenos Aires	Sector Público
10	Alcaldía Municipal de Buglagrande	Sector Público
11	Alcaldía Municipal de Cajibío	Sector Público
12	Alcaldía Municipal de Cali	Sector Público
13	Alcaldía Municipal de Campoalegre	Sector Público
14	Alcaldía Municipal de Cantagallo	Sector Público
15	Alcaldía Municipal de Cartagena del Chairá	Sector Público
16	Alcaldía Municipal de Chachagui	Sector Público
17	Alcaldía Municipal de Colombia	Sector Público
18	Alcaldía Municipal de Colón	Sector Público
19	Alcaldía Municipal de Consacá	Sector Público
20	Alcaldía Municipal de Contadero	Sector Público
21	Alcaldía Municipal de Convención	Sector Público
22	Alcaldía Municipal de Córdoba	Sector Público
23	Alcaldía Municipal de Corinto	Sector Público
24	Alcaldía Municipal de Cúcuta	Sector Público
25	Alcaldía Municipal de Curillo	Sector Público
26	Alcaldía Municipal de Dagua	Sector Público
27	Alcaldía Municipal de el Cerrito	Sector Público
28	Alcaldía Municipal de el Paujil	Sector Público
29	Alcaldía Municipal de el Tarra	Sector Público
30	Alcaldía Municipal de Florencia	Sector Público
31	Alcaldía Municipal de Floridablanca	Sector Público
32	Alcaldía Municipal de Garzón	Sector Público
33	Alcaldía Municipal de Girón	Sector Público
34	Alcaldía Municipal de Guachucal	Sector Público
35	Alcaldía Municipal de Ipiales	Sector Público
36	Alcaldía Municipal de Iquira	Sector Público
37	Alcaldía Municipal de Jambaló	Sector Público
38	Alcaldía Municipal de Juradó	Sector Público
39	Alcaldía Municipal de la Unión	Sector Público
40	Alcaldía Municipal de Landazurí	Sector Público
41	Alcaldía Municipal de Lebríja	Sector Público
42	Alcaldía Municipal de Linares	Sector Público
43	Alcaldía Municipal de los Andes	Sector Público
44	Alcaldía Municipal de Matanzas	Sector Público
45	Alcaldía Municipal de Milán	Sector Público
46	Alcaldía Municipal de Mocoa	Sector Público
47	Alcaldía Municipal de Morales	Sector Público
48	Alcaldía Municipal de Morelia	Sector Público
49	Alcaldía Municipal de Neiva	Sector Público
50	Alcaldía Municipal de Ocaña	Sector Público
51	Alcaldía Municipal de Palermo	Sector Público
52	Alcaldía Municipal de Pasto	Sector Público
53	Alcaldía Municipal de Pitalito	Sector Público
54	Alcaldía Municipal de Popayán	Sector Público
55	Alcaldía Municipal de Puerto Asís	Sector Público
56	Alcaldía Municipal de Puerto Leguizamo	Sector Público
57	Alcaldía Municipal de Puerto Parra	Sector Público
58	Alcaldía Municipal de Puerto Santander	Sector Público
59	Alcaldía Municipal de Puerto Wilches	Sector Público
60	Alcaldía Municipal de Pupiales	Sector Público
61	Alcaldía Municipal de Quibdó	Sector Público
62	Alcaldía Municipal de Ricaurte	Sector Público
63	Alcaldía Municipal de Rivera	Sector Público
64	Alcaldía Municipal de Rosas	Sector Público
65	Alcaldía Municipal de Samaniego	Sector Público
66	Alcaldía Municipal de San Agustín	Sector Público
67	Alcaldía Municipal de San Lorenzo	Sector Público
68	Alcaldía Municipal de San Miguel	Sector Público
69	Alcaldía Municipal de San Pablo	Sector Público
70	Alcaldía Municipal de San Pedro	Sector Público
71	Alcaldía Municipal de San Vicente del Caguán.	Sector Público
72	Alcaldía Municipal de Santa Rosa del Sur	Sector Público
73	Alcaldía Municipal de Santander de Quilichao	Sector Público
74	Alcaldía Municipal de Santiago	Sector Público
75	Alcaldía Municipal de Santiago de Cali	Sector Público
76	Alcaldía Municipal de Sardinata	Sector Público
77	Alcaldía Municipal de Simití	Sector Público
78	Alcaldía Municipal de Sotará	Sector Público
79	Alcaldía Municipal de Suratá	Sector Público

Item	Name	Partner Type
80	Alcaldía Municipal de Taminango	Sector Público
81	Alcaldía Municipal de Tello	Sector Público
82	Alcaldía Municipal de Teorama	Sector Público
83	Alcaldía Municipal de Tibú	Sector Público
84	Alcaldía Municipal de Timaná	Sector Público
85	Alcaldía Municipal de Timbio	Sector Público
86	Alcaldía Municipal de Toribío	Sector Público
87	Alcaldía Municipal de Tulua	Sector Público
88	Alcaldía Municipal de Tumaco	Sector Público
89	Alcaldía Municipal de Villa Garzón	Sector Público
90	Alcaldía Municipal de Yondó	Sector Público
91	Alcaldía Municipal de Yotoco	Sector Público
92	Alcaldía Municipal del Carmen de Atrato	Sector Público
93	Alcaldía Municipal del Hato	Sector Público
94	Alcaldía Municipal del Medio Atrato	Sector Público
95	Alcaldía Municipal el Tambo	Sector Público
96	Alcaldía Municipal la Plata	Sector Público
97	Alcaldía Municipal López de Micay	Sector Público
98	Alcaldía Municipal Valle del Guamuez	Sector Público
99	Alto Comisionado para la Paz	Sector Público
100	Banco Agrario de Colombia	Sector Público
101	Banco de la República	Sector Público
102	Caja de Compensación Familiar - COMFANDI - Valle del Cauca	Sector Público
103	Centro Auxiliar de Servicios Docentes	Sector Público
104	Centro de Educación Continuada Don Bosco	Sector Público
105	Centro de Salud de Cértequi	Sector Público
106	Centro de Salud la Dorada	Sector Público
107	Centro Hospital Municipal de Taminango	Sector Público
108	Ciudadela Educativa Siglo XXI	Sector Público
109	Colegio Agropecuario Guambiano	Sector Público
110	Colegio Agropecuario Nueva Granada	Sector Público
111	Colegio Agropecuario Valle del Guamuez	Sector Público
112	Colegio Basica San Isidro	Sector Público
113	Colegio Ciudad Mocoa	Sector Público
114	Colegio Ecológico Cuembi	Sector Público
115	Colegio Femenino Pérez Pallares	Sector Público
116	Colegio Francisco de Caldas	Sector Público
117	Colegio General la Salle	Sector Público
118	Colegio Guillermo Valencia	Sector Público
119	Colegio Jorge Eliécer Gaitán	Sector Público
120	Colegio Mixto la Florida	Sector Público
121	Colegio Roberto García	Sector Público
122	Colegio San José de Orito	Sector Público
123	Colegio Sucre de Colón	Sector Público
124	Comité Municipal de la Cruz Roja	Sector Público
125	Concentración Escolar Enrique Jensen	Sector Público
126	Consejería de Proyectos	Sector Público
127	Consejo Nacional de Planeación	Sector Público
128	CORPOAMAZONIA	Sector Público
129	Defensoría del Pueblo	Sector Público
130	Departamento Administrativo de la Presidencia de la República - DARP	Sector Público
131	Departamento Administrativo de Salud - Dasalud	Sector Público
132	Departamento Administrativo Nacional de Estadística - Dane	Sector Público
133	Departamento Nacional de Economía Solidaria - Dansocial	Sector Público
134	Dirección Departamental de Salud del Cauca	Sector Público
135	Dirección Municipal de Salud de Pasto	Sector Público
136	ECOPETROL	Sector Público
137	Empresa de Desarrollo Urbano y Vivienda de Interés Social - EDUBA	Sector Público
138	Empresa de Servicios de Florencia S.A. - E.S.P.	Sector Público
139	Empresa de Servicios Públicos de Cartagena del Chairá	Sector Público
140	Empresa de Servicios Públicos Emporito	Sector Público
141	Empresa Municipal de Servicios Públicos Domiciliarios Vigía del Fuerte - EMSPUVIF	Sector Público
142	Empresa Social del Estado - ESE - IMSALUD	Sector Público
143	Empresa Social del Estado - ESE Barancabermeja	Sector Público
144	Empresa Social del Estado Carmen Emilia Ospina	Sector Público
145	Empresa Social del Estado Hospital José María Hernández	Sector Público
146	Empresa Social del Estado Hospital Local	Sector Público
147	Empresas Municipales de Tibú	Sector Público
148	Escuela Integrada el Remolino	Sector Público
149	Escuela Mixta los Chilcos	Sector Público
150	Escuela Normal Superior Cristo Rey	Sector Público
151	Escuela Nuevo Sol	Sector Público
152	Escuela Orito 2	Sector Público
153	ESE - Imsalud	Sector Público
154	ESE Oriente de Cali	Sector Público
155	Fiscalía General de la Nación	Sector Público
156	FOMIPYME	Sector Público
157	Fondo de Servicios Docentes del Instituto Superior Industrial Nacional - ITSIN	Sector Público
158	Fondo de Servicios Docentes Escuela Fray Plácido	Sector Público

Item	Name	Partner Type
159	Fondo de Servicios Educativos Escuela Santa Barbara	Sector Público
160	Fondo Especial de Vivienda de Santiago de Cali	Sector Público
161	Fondo Financiero de proyectos de Desarrollo - Fonade	Sector Público
162	Fondo Nacional de Vivienda - Fonvivienda	Sector Público
163	Fundacion para la Educación Agropecuaria José María Obando	Sector Público
164	Fundación para la salud Divino Salvador	Sector Público
165	Gobernación de Norte de Santander	Sector Público
166	Gobernación de Nariño	Sector Público
167	Gobernación del Caquetá	Sector Público
168	Gobernación del Cauca	Sector Público
169	Gobernación del Huila	Sector Público
170	Gobernación del Putumayo	Sector Público
171	Gobernación del Valle del Cauca	Sector Público
172	Hogar Infantil el Bordo	Sector Público
173	Hospital Benito Ovalle	Sector Público
174	Hospital Civil de Ipiales	Sector Público
175	Hospital Comunal Malvinas	Sector Público
176	Hospital Erasmo Meoz de Cúcuta	Sector Público
177	Hospital Integrado de Landazurí	Sector Público
178	Hospital Ismael Roldan Valencia	Sector Público
179	Hospital la Era de Cali	Sector Público
180	Hospital Luis Ablanque de la Plata	Sector Público
181	Hospital María Inmaculada	Sector Público
182	Hospital Mario Correa Rengifo	Sector Público
183	Hospital Piloto - ESE - Jamundí	Sector Público
184	Hospital Pío XII Colón - ESE - Putumayo	Sector Público
185	Hospital Regional Noroccidental	Sector Público
186	IMOC CAQUETA	Sector Público
187	INCODER	Sector Público
188	Instituto Municipal de Deporte y Recreación	Sector Público
189	Institución Agropecuaria la Planada	Sector Público
190	Institución de la Amazonia	Sector Público
191	Institución de Nariño	Sector Público
192	Institución del Cauca	Sector Público
193	Institución Educativa Agropecuaria los Comuneros	Sector Público
194	Institución Educativa Cristobal Colón de Iquira	Sector Público
195	Institución Educativa el Guadual de Rivera	Sector Público
196	Institución Educativa el Juncal de Palermo	Sector Público
197	Institución Educativa el Tejar de Timaná	Sector Público
198	Institución Educativa Gaitana FXIW	Sector Público
199	Institución Educativa la Arcadia de Algeciras	Sector Público
200	Institución Educativa la Vega de Campoalegre	Sector Público
201	Institución Educativa Nicolás García B. de Tello	Sector Público
202	Institución Educativa Rural San Luis	Sector Público
203	Institución Educativa San Antonio del Pescado de Garzón	Sector Público
204	Institución Educativa San Luis Beltrán de Neiva	Sector Público
205	Institución Educativa Técnica San Juan Bautista	Sector Público
206	Instituto Colombiano de Bienestar Familiar - ICBF	Sector Público
207	Instituto de Educación Y Pedagogía para la Paz	Sector Público
208	Instituto de Fomento Industrial del Valle del Cauca	Sector Público
209	Instituto Departamental de Salud de Nariño	Sector Público
210	Instituto Departamental de Salud Norte de Santander	Sector Público
211	Instituto Hijas de los Sagrados Corazones de Jesus y de María	Sector Público
212	Instituto Mayor Campesino	Sector Público
213	Instituto Municipal de Deporte y Recreación de Caicedonia - IMDERCAI	Sector Público
214	Instituto Municipal de Empleo y Fomento Empresarial del Municipio de Bucaramanga	Sector Público
215	Instituto Municipal de Reforma Urbana y Vivienda de Interés Social de Guadalajara de Buga - INVIBUGA	Sector Público
216	Instituto Municipal para el Empleo en Bucaramanga - IMEBU	Sector Público
217	Instituto Nacional de Educación y Capacitación	Sector Público
218	Instituto Nacional de Medicina Legal y Ciencias Forenses	Sector Público
219	Instituto Nacional de Salud - INS	Sector Público
220	Instituto Técnico Agrícola la Plata	Sector Público
221	INURBE	Sector Público
222	IPS Dusakawi	Sector Público
223	La Empresa Social del Estado de Barrancabermeja	Sector Público
224	La Escuela Urbana Mixta San Martín	Sector Público
225	Liceo Nacional Alejandro Humboldt	Sector Público
226	Liceo Nacional Max Seidel	Sector Público
227	Metrovivienda - Cúcuta	Sector Público
228	Ministerio de Ambiente, Vivienda y Desarrollo Territorial	Sector Público
229	Ministerio de Comunicaciones	Sector Público
230	Ministerio de Cultura	Sector Público
231	Ministerio de Educación	Sector Público
232	Ministerio de Educación	Sector Público
233	Ministerio de la Protección Social	Sector Público
234	Ministerio de Salud	Sector Público
235	Municipio de Alto Baudo	Sector Público
236	Municipio de Caicedonia	Sector Público
237	Municipio de Orito	Sector Público

Item	Name	Partner Type
238	Municipio de Potosí	Sector Público
239	Municipio de Subatá	Sector Público
240	Municipio de Villa del Rosario	Sector Público
241	Municipio el Carmen	Sector Público
242	Personería Municipal de Buenaventura	Sector Público
243	Personería Municipal de Tumaco	Sector Público
244	Presidencia de la República	Sector Público
245	Procuraduría General de la Nación	Sector Público
246	Programa de Educación Rural - PER	Sector Público
247	Programa Desarrollo Seguridad y Paz Desepez - Alcaldía Municipal de Cali	Sector Público
248	Registraduría Nacional de Estado Civil	Sector Público
249	Ruben Cruz Tulúa	Sector Público
250	Secretaría de Agricultura de Jamundí	Sector Público
251	Secretaría de Educación de Antioquia	Sector Público
252	Secretaría de Educación de Cúcuta	Sector Público
253	Secretaría de Educación de Medellín	Sector Público
254	Secretaría de Educación del Putumayo	Sector Público
255	Secretaría de Educación Municipal de Popayán	Sector Público
256	Secretaría de Infraestructura Física del Municipio de Jamundí	Sector Público
257	Secretaría de Salud del Cesar	Sector Público
258	Secretaría de Salud del Municipio de Barrancabermeja	Sector Público
259	Secretaría de Salud del Municipio de Cali	Sector Público
260	Secretaría de Salud del Municipio de Cúcuta	Sector Público
261	Secretaría de Salud del Municipio de Floridablanca	Sector Público
262	Secretaría de Salud del Municipio de Jamundí	Sector Público
263	Secretaría de Salud del Municipio de Samaniego	Sector Público
264	Secretaría de Salud del Municipio de Santander	Sector Público
265	Secretaría de Salud Municipal de Buenaventura	Sector Público
266	Secretaría del Ministerio del Interior	Sector Público
267	Servicio Nacional de Aprendizaje - SENA	Sector Público
268	Servicio Seccional de Salud	Sector Público
269	Universidad Francisco de Paula Santander	Sector Público
270	Universidad de Nariño	Sector Público
271	Universidad del Cauca	Sector Público
272	Universidad del Pacífico	Sector Público
273	Universidad del Valle	Sector Público
274	Universidad Nacional de Colombia	Sector Público
275	Universidad Surcolombiana	Sector Público
276	Universidad Tecnológica del Chocó - Diego Luis Córdoba	Sector Público
277	Universidad del Valle - CIIMDER	Sector Público
278	Alberto Angelo Burbano	Sector Privado
279	Alexander Melo Ríos	Sector Privado
280	Alfonso Rocha	Sector Privado
281	AMUCIB	Sector Privado
282	Andrés Arbelaez	Sector Privado
283	Arqtecon	Sector Privado
284	Asociación Alianza Educativa	Sector Privado
285	Asociación Carmen del Cucu	Sector Privado
286	Asociación Centro Cultural Comunitario las Colinas - CECUCOL	Sector Privado
287	Asociación Colombiana de Universidades - ASCUN	Sector Privado
288	Asociación Colombiana para el avance de la ciencia - ACAC	Sector Privado
289	Asociación Comunal de Juntas del Municipio de Villa del Rosario - ASOCOMUNAL	Sector Privado
290	Asociación de Afrocolombianos Desplazados - AFRODES	Sector Privado
291	Asociación de Alcaldes de Municipios con Población Afro - AMUNAFRO	Sector Privado
292	Asociación de Amigos de la Bibliored	Sector Privado
293	Asociación de Amigos del Colegio Roberto García	Sector Privado
294	Asociación de Cabildos Indígenas del Pueblo AWÁ del Putumayo - ACIPAP	Sector Privado
295	Asociación de Comunidades Barí del Municipio de Teorama	Sector Privado
296	Asociación de Desplazados de Floridablanca - ASODEFLOR	Sector Privado
297	Asociación de Exalumnos del Colegio San Carlos	Sector Privado
298	Asociación de la Mujer y la Familia de Norte de Santander - ASOMUFA	Sector Privado
299	Asociación de Mujeres Campesinas e Indígenas de Buenaventura - AMUCIB	Sector Privado
300	Asociación de Mujeres la Esperanza	Sector Privado
301	Asociación de Padres de Familia Colegio Departamental José Celestino Mutis	Sector Privado
302	Asociación de Padres de Familia del Centro Educativo Manuela Beltrán	Sector Privado
303	Asociación de Padres de Familia Escuela el Manzano	Sector Privado
304	Asociación de Productores de Frutas de San Agustín - APROFRUSA	Sector Privado
305	Asociación de Recicladores del Caquetá y Amazonía	Sector Privado
306	Asociación de Scouts de Colombia Región Bogotá	Sector Privado
307	Asociación Defensa de los Niños Internacional Colombia	Sector Privado
308	Asociación Fuente de Vida	Sector Privado
309	Asociación Luna Roja	Sector Privado
310	Asociación Luz y Vida	Sector Privado
311	Asociación Municipal de Mujeres ASOM - Buenos Aires Cauca	Sector Privado
312	Asociación Padres de Familia Colegio Agropecuario Roberto Ruiz Monsalve	Sector Privado
313	Asociación para la Colaboración a las Personas Discapacitadas de la Tebaida	Sector Privado
314	Asociación para la Promoción Social Alternativa - MINGA	Sector Privado
315	Asociación Proyecto del Mañana Cultura y Solidaridad - PRODOCS	Sector Privado
316	Asociación Regional de Hogares Jueveniles Campesinos.	Sector Privado

Item	Name	Partner Type
317	Asociación Solidarios por la Vida - SOLIVIDA	Sector Privado
318	Asociación Tejido Humano	Sector Privado
319	Asociación Voluntariado el Sembrador	Sector Privado
320	Asociación Voluntarias Vicentinas de la Caridad	Sector Privado
321	AUGE Asesores Ltda.	Sector Privado
322	Avianca	Sector Privado
323	Bogotá Como Vamos	Sector Privado
324	CAFAM	Sector Privado
325	Caja Colombiana de Subsidio Familiar - COLSUBSIDIO	Sector Privado
326	Caja de Compensación Familiar - COMFAMILIAR - Putumayo	Sector Privado
327	Caja de Compensación Familiar COMFENALCO del Valle del Cauca	Sector Privado
328	Caja de Compensación Familiar del Cauca - COMFACAUCA	Sector Privado
329	Camara de Comercio de Bogotá	Sector Privado
330	Camara de Comercio de Cúcuta	Sector Privado
331	Camara de Comercio de Florencia	Sector Privado
332	Cámara de Comercio de Palmira	Sector Privado
333	CAMIZBA	Sector Privado
334	Caracol Televisión	Sector Privado
335	Cenpromujer Taller Abierto	Sector Privado
336	Central Cooperativa de Servicios - CENCOOSER	Sector Privado
337	Central de Cooperativas Agrarias Censoa	Sector Privado
338	Centro de Desarrollo Productivo del Cuero	Sector Privado
339	Centro de Investigación Nacional de Educación Popular - CINEP	Sector Privado
340	Centro de Promoción Integral para la Mujer y la Familia	Sector Privado
341	Centro de Rehabilitación para Adultos Ciegos	Sector Privado
342	Centro de Tecnología de Antioquia	Sector Privado
343	Centro Internacional de Investigaciones Clínico Psicológica - CEIC	Sector Privado
344	Cerámica Italia	Sector Privado
345	Club Rotario de Ipiales	Sector Privado
346	Colegio Mayor de Nuestra Señora del Rosario	Sector Privado
347	Comité de Cafeteros de Norte de Santander	Sector Privado
348	Comité de Cafeteros del Cauca	Sector Privado
349	Comite Departamental de la Cruz Roja Colombiana	Sector Privado
350	COMPRENDER	Sector Privado
351	Comunidad Cartagena del Chairá	Sector Privado
352	Comunidad de Quibdó	Sector Privado
353	Comunidad HU-0018	Sector Privado
354	Conexión Colombia	Sector Privado
355	Confecciones Femeninas de San Pablo	Sector Privado
356	Consejo Comunitario de la Acia - COCOMACIA	Sector Privado
357	Consortio Amazonia para el Desarrollo	Sector Privado
358	Consortio de Desarrollo y Paz del Magdalena Medio - CDPMM	Sector Privado
359	Consultoría para los Derechos Humanos - CODHES	Sector Privado
360	Cooperación Técnica	Sector Privado
361	Cooperativa de Caficultores del Norte de Nariño Ltda.	Sector Privado
362	Cooperativa de Impresores y Papeleros de Occidente	Sector Privado
363	Cooperativa de Municipios del Sur Ltda.	Sector Privado
364	Cooperativa el Cambio	Sector Privado
365	Cooperativa Juan Bautista Scalabrini - COOPEJUBASCA	Sector Privado
366	Coordinadora Departamental de Asociaciones de Comunidades en situación de desplazamiento - CORASDERH	Sector Privado
367	Coorporación de Servicios para el Desarrollo - PRODESA	Sector Privado
368	Coorporación Promotora de las Comunidades Municipales de Colombia - PROCOMUN	Sector Privado
369	Coperativa de Trabajo Asociado Uniseda	Sector Privado
370	COPORNARINO	Sector Privado
371	CORAMBIENTE	Sector Privado
372	CORFAS	Sector Privado
373	Corporación Agencia para el Desarrollo - ADA	Sector Privado
374	Corporacion Andaki	Sector Privado
375	Corporación Apoyo a las Víctimas de la Violencia Sociopolítica Prorecuperación Emocional - AVRE	Sector Privado
376	Corporación Autónoma Regional del Alto Magdalena - CAM	Sector Privado
377	Corporación Autónoma Regional del Valle del Cauca - CVC	Sector Privado
378	Corporación Borrascoso - Opón	Sector Privado
379	Corporación Centro de Educación Popular de Adultos Simón Rodríguez	Sector Privado
380	Corporación Cívica Daniel Gillard - COOCECAN	Sector Privado
381	Corporación Colombiana Alternativa Coca	Sector Privado
382	Corporación Colombiana de Investigación Agropecuaria - CORPOICA	Sector Privado
383	Corporacion Colombiana de Teatro	Sector Privado
384	Corporación Compartamos con Colombia	Sector Privado
385	Corporacion Comunitaria del Magdalena Medio Arco Iris	Sector Privado
386	Corporación de Acción Social Jorge Eliécer Gaitán	Sector Privado
387	Corporación de Contadores Asociados	Sector Privado
388	Corporación de Profesionales para el Desarrollo Integral Comunitario - CORPRODINCO	Sector Privado
389	Corporación de Servicios Club Rotario Quibdó	Sector Privado
390	Corporación de Voluntariado del Huila	Sector Privado
391	Corporación Desarrollo y Paz del Magdalena Medio	Sector Privado
392	Corporación Día del Niño	Sector Privado
393	Corporación Dominicana Opción Vida, Justicia y Paz	Sector Privado
394	Corporación Educativa Paz y Futuro	Sector Privado
395	Corporación el Colegio del Cuerpo	Sector Privado

Item	Name	Partner Type
396	Corporación El Minuto de Dios	Sector Privado
397	Corporacion Empresa y Futuro - CONTACTAR	Sector Privado
398	Corporación Escuela Galán	Sector Privado
399	Corporación Juntos Construyendo Futuro	Sector Privado
400	Corporacion Juventud de Barrancabermeja	Sector Privado
401	Corporación Latinoamericana Misión Rural	Sector Privado
402	Corporación Metropolitana de Planeación y Desarrollo de Bucaramanga - CORPLAN	Sector Privado
403	Corporación MUMIDAVI	Sector Privado
404	Corporación para el Desarrollo de las Microempresas	Sector Privado
405	Corporación para el Desarrollo del Oriente Colombiano - COMPROMISO	Sector Privado
406	Corporación para el Desarrollo Social y Educativo Ltda. - CORPASODE	Sector Privado
407	Corporación para el Desarrollo Social y Empresarial de los Pueblos Afrocolombianos - ECODESARROLLO	Sector Privado
408	Corporación para Estudios Interdisciplinarios y Asesoría Tecnológica	Sector Privado
409	Corporación Prodesarrollo Socio Ambiental Gente Joven	Sector Privado
410	Corporacion Propulsora de Empresas de Norte de Santander	Sector Privado
411	Corporación Social y Educativa Paz y Futuro	Sector Privado
412	Corporación Vida en Primavera - CORVIPRI	Sector Privado
413	Credibanco Visa	Sector Privado
414	Cruz Roja Colombiana	Sector Privado
415	Cruz Roja Colombiana Departamental Chocó	Sector Privado
416	Cruz Roja Seccional Departamental Nariño	Sector Privado
417	Cruz Roja Seccional Putumayo	Sector Privado
418	DHL Internacional	Sector Privado
419	Diego Hernán Gómez	Sector Privado
420	Distribuidora Y Comercializadora Dossaval Ltda.	Sector Privado
421	Econometría Consultores	Sector Privado
422	El Fondo de Solidaridad	Sector Privado
423	El Tiempo	Sector Privado
424	Empresa Asociativa de Trabajo de Profesionales Nuevos Horizontes	Sector Privado
425	Empresa Asociativa Del Trabajo - FRUTIFRES	Sector Privado
426	Empresa Comercial	Sector Privado
427	Empresa de Mujeres Capacitadas y Organizadas - EMCO	Sector Privado
428	Federación Nacional de Cafeteros de Colombia	Sector Privado
429	Federación Nacional de Comerciantes - Fenalco	Sector Privado
430	Federación Nacional de Consejos - FENACON	Sector Privado
431	Federación Nacional de Vivienda Popular - FENAVIP	Sector Privado
432	Floro Tunubalá	Sector Privado
433	Fondo de Vivienda de Popayán	Sector Privado
434	Fondo Mixto de Promoción de la Cultura y las artes de Nariño	Sector Privado
435	Fundación Aldea Global	Sector Privado
436	Fundación AlvarAlice	Sector Privado
437	Fundación Amalaka	Sector Privado
438	Fundación Ambiental los Picachos	Sector Privado
439	Fundación Ana Restrepo del Corral	Sector Privado
440	Fundacion Carcafe	Sector Privado
441	Fundación Cáritas Diocesana	Sector Privado
442	Fundación Carvajal	Sector Privado
443	Fundación Catatumbo	Sector Privado
444	Fundación CECUCOL	Sector Privado
445	Fundación Centro de Investigación Formación e Información para el Servicio Amazónico - CIFISAM	Sector Privado
446	Fundación Colombia para la Educación y la Oportunidad	Sector Privado
447	Fundación Colombia Presente	Sector Privado
448	Fundación Colombiana para la Nutrición Infantil	Sector Privado
449	Fundación Colombianitos	Sector Privado
450	Fundación Comunidad el Camino	Sector Privado
451	Fundación Corona	Sector Privado
452	Fundación CRAN	Sector Privado
453	Fundación del Alto Magdalena	Sector Privado
454	Fundación Despertar AFRO	Sector Privado
455	Fundación Dos Mundos	Sector Privado
456	Fundación Educadora Infantil Carla Cristina	Sector Privado
457	Fundación ESAWA	Sector Privado
458	Fundación Espavé	Sector Privado
459	Fundación Esperanza por un Retorno Seguro	Sector Privado
460	Fundación FES Social	Sector Privado
461	Fundación Foro Nacional por Colombia	Sector Privado
462	Fundación Haceres y Sueños	Sector Privado
463	Fundación HOCOL	Sector Privado
464	Fundación Hogar Integral	Sector Privado
465	Fundación Jera	Sector Privado
466	Fundación Juan Felipe Gómez Escobar	Sector Privado
467	Fundacion Juan Tama	Sector Privado
468	Fundación Luz y Vida	Sector Privado
469	Fundacion Manuel Mejia	Sector Privado
470	Fundación Mujer y Futuro	Sector Privado
471	Fundación Orquesta Sinfónica Juvenil del Norte de Santander - SINFONORTE	Sector Privado
472	Fundación para el Dearrollo Ambiental y Cultural de la Amazonia - FUNDARCA	Sector Privado
473	Fundación para el Desarrollo Regional Alternativo - FUNDAR	Sector Privado
474	Fundación para el Desarrollo del Magdalena Medio - FUNDESMAG	Sector Privado

Item	Name	Partner Type
475	Fundación para el Desarrollo Local Comunitario - FUNDACOMUNIDAD	Sector Privado
476	Fundación para el Desarrollo Rural Comunitario - Alternativa Comunitaria	Sector Privado
477	Fundación para el Fomento de la Iniciativa Empresarial - FUNDAEMPRESA	Sector Privado
478	Fundación para el Progreso Empresarial y Social Vallecaucano - FUNPRESOV	Sector Privado
479	Fundación para la Aplicación y Enseñanza de la Ciencias - FUNDAEC	Sector Privado
480	Fundación para la Promoción y la Educación Popular - FUNPROCEP y CORMUNORTE	Sector Privado
481	Fundación Paz y Bien	Sector Privado
482	Fundación Paz y Futuro	Sector Privado
483	Fundación Pies Descalzos	Sector Privado
484	Fundación Progresamos	Sector Privado
485	Fundación Romelio	Sector Privado
486	Fundación Seguridad y Democracia	Sector Privado
487	Fundación Si Mujer	Sector Privado
488	Fundación Social Colombiana - CEDAVIDA	Sector Privado
489	Fundación Social Utrahuilca	Sector Privado
490	Fundación Sociedad Portuaria	Sector Privado
491	Fundación Solidaridad por Colombia	Sector Privado
492	Fundación Universitaria para el Desarrollo de la Amazonia	Sector Privado
493	Fundación Vida y Futuro	Sector Privado
494	Fundación Volvamos a la Gente	Sector Privado
495	FUNDESARROLLO	Sector Privado
496	Gonzalez Muñoz y Asociados	Sector Privado
497	Grupo de Investigaciones para la Etnoeducación - CEAD	Sector Privado
498	Grupo Live	Sector Privado
499	Grupo Pre-cooperativo Integral de Mujeres Cabeza de Familia Tus Diseños	Sector Privado
500	Guillermo Aristizabal	Sector Privado
501	Guillermo Murillo Herrera	Sector Privado
502	Henry España Rodríguez	Sector Privado
503	HOCOL S.A.	Sector Privado
504	Hogar Infantil Pequeñines	Sector Privado
505	Hogar Jesus de Nazareth	Sector Privado
506	Induarco Ltda.	Sector Privado
507	Industrias Intregradas	Sector Privado
508	Instituto Cisava	Sector Privado
509	Instituto Colombiano de Antropología	Sector Privado
510	Instituto María Cano - ISMAC	Sector Privado
511	Instituto Matia Mulumba	Sector Privado
512	Instituto para el Niño Diferente - Ocaña	Sector Privado
513	Jairo Miguel Guerra	Sector Privado
514	Javier Alexander Barrero	Sector Privado
515	Jesús Eduardo Gómez	Sector Privado
516	Joaquín Gómez Schweiger	Sector Privado
517	Juan Jacobo Montenegro	Sector Privado
518	La comunidad CU-0023	Sector Privado
519	La Corporación de Servicios para el Desarrollo - PRODESA	Sector Privado
520	La Fundación Canitas Felices	Sector Privado
521	La Unión Temporal Sedecom - CORFAS	Sector Privado
522	Leo Burnett Colombiana	Sector Privado
523	Luz Emilia Jiménez	Sector Privado
524	Mario Velasco	Sector Privado
525	Mauricio Genecco Ortiz	Sector Privado
526	Medios para la Paz	Sector Privado
527	Merquemos Juntos	Sector Privado
528	Movimiento CIMARRON	Sector Privado
529	Mujeres Progresistas de Juradó	Sector Privado
530	Observatorio para la Paz	Sector Privado
531	OM Constructores Ltda.	Sector Privado
532	Ong Asociación de Profesionales para el Desarrollo del Cauca - ASPRODECA	Sector Privado
533	Opción Legal	Sector Privado
534	Organización Campesina y Caficultora del Carmen del Atrato - OCCCA	Sector Privado
535	Organización de los Pueblos Indígenas de la Amazonía Colombiana - OPIAC	Sector Privado
536	Organización Femenina Popular	Sector Privado
537	Organización Padre Luis de Riz	Sector Privado
538	Organización para el Bienestar y la Equidad - Orbes	Sector Privado
539	Organización para el Desarrollo Regional - ODR1	Sector Privado
540	Organización para la Educación y Protección Ambiental	Sector Privado
541	Organización Regional Embera Wounaan - OREWA	Sector Privado
542	Organización Regional Indígena del Valle del Cauca - ORIVAC	Sector Privado
543	Patrulla Área Civil de Bogotá	Sector Privado
544	PROFAMILIA	Sector Privado
545	Programa Jóven	Sector Privado
546	Proyecto NASA	Sector Privado
547	Publicaciones Semana S.A.	Sector Privado
548	Red de Empresas	Sector Privado
549	Royal Andina S.A.	Sector Privado
550	Sistemas Especializados de Formación S.A.	Sector Privado
551	Sociedad Portuaria	Sector Privado
552	Taller Abierto	Sector Privado
553	TELEDATOS	Sector Privado

Item	Name	Partner Type
554	Unión Soluciones Sistema de Información Ltda	Sector Privado
555	Union Temporal Fundacion Aldea Global - Armando W. Andrade	Sector Privado
556	Unión Temporal Pro-Empleo	Sector Privado
557	Universidad Javeriana	Sector Privado
558	Urdimbre Fundacion Educativa y Social	Sector Privado
559	Yacid Navarro Carvajalino	Sector Privado
560	Agencia Suiza para el Desarrollo y la Cooperación	Otros Socios
561	Alto Comisionado de las Naciones Unidas para los Refugiados - ACNUR	Otros Socios
562	ARD	Otros Socios
563	Asamblea de beneficiarios del proyecto de vivienda	Otros Socios
564	Asociación Campesina del Baudó	Otros Socios
565	Asociación Campesina para el Desarrollo Integral del Sur del Putumayo - ACADISP	Otros Socios
566	Asociación Comunal de Juntas del Municipio de Rivera	Otros Socios
567	Asociación Comunitaria Integral del Huila	Otros Socios
568	Asociación de Amigos Usuarios del Acueducto Independiente - ADAMIUAIN	Otros Socios
569	Asociación de Cabildos Indígenas del Norte	Otros Socios
570	Asociación de Caficultores de la Tebaida - ASCATE	Otros Socios
571	Asociación de Desplazados Caminando Hacia el Futuro	Otros Socios
572	Asociación de Desplazados de Altos del Paraiso - ASODESISO	Otros Socios
573	Asociación de Desplazados del Caquetá	Otros Socios
574	Asociación de desplazados por la paz - ASDEPAZ	Otros Socios
575	Asociación de Desplazados Selva Futuro	Otros Socios
576	Asociación de Familias el Nuevo Progreso	Otros Socios
577	Asociación de Familias Emprendedoras de Nariño - AFEN	Otros Socios
578	Asociación de Juntas Comunales de Cartagena del Chairá	Otros Socios
579	Asociación de Juntas Comunales de la Gabarra	Otros Socios
580	Asociación de Juntas de Acción Comunal de Mocoa	Otros Socios
581	Asociación de Mujeres Campesinas de San Agustín	Otros Socios
582	Asociación de Mujeres Desplazadas - AMUDESCO	Otros Socios
583	Asociación de Padres de Familia de Restaurantes Escolares Nuevo Milenio	Otros Socios
584	Asociación de Padres de Familia de Restaurantes Escolares Semilla	Otros Socios
585	Asociación de Plataneros del Municipio del Docello	Otros Socios
586	Asociación de Trabajadores Campesinos del Carare	Otros Socios
587	Asociación de Trabajadores Unidos Por Colombia - ATUCOL	Otros Socios
588	Asociación Departamental por los Derechos Humanos de las Comunidades Afroputumayenses	Otros Socios
589	Asociación Surcolombiana de Desplazados Internos - ASCDI	Otros Socios
590	Asociación de Desplazados Asentamiento la Paz	Otros Socios
591	Autoridad Nonam Del Medio San Juan - Anomes	Otros Socios
592	Banco Mundial	Otros Socios
593	Brokings SAIS	Otros Socios
594	Cabildo Indígena Selvas Del Putumayo	Otros Socios
595	Cabildo Mayor Indígena de Bojayá	Otros Socios
596	Caritas Diocesana - COSPAS - Corporación de servicios Pastoral Social Cúcuta	Otros Socios
597	Centro Diocesano de Migracionees y Solidaridad	Otros Socios
598	Centro Regional para el Fomento del Libro en America Latina	Otros Socios
599	CHF Internacional	Otros Socios
600	Comisión Vida Justicia y Paz de la Arquidiócesis de Cali	Otros Socios
601	Comité Internacional de la Cruz Roja	Otros Socios
602	Comité Local de Prevención y Atención de Desastres - CLPAD	Otros Socios
603	Comunidad beneficiaria Yotoco	Otros Socios
604	Comunidad Corregimiento de San Pablo	Otros Socios
605	Comunidad de Barrancabermeja	Otros Socios
606	Comunidad de Belén de los Andaquíes	Otros Socios
607	Comunidad de Buenaventura	Otros Socios
608	Comunidad de Buenos Aires	Otros Socios
609	Comunidad de Cajibío	Otros Socios
610	Comunidad de Cali	Otros Socios
611	Comunidad de Convención	Otros Socios
612	Comunidad de Corinto	Otros Socios
613	Comunidad de Cúcuta	Otros Socios
614	Comunidad de Curillo	Otros Socios
615	Comunidad de de Lebrija	Otros Socios
616	Comunidad de Florencia - Barrios (La Sardina, el Portal, Villanueva, Palmeras Altas, Castillo y el Minuto de Dios).	Otros Socios
617	Comunidad de Jambaló	Otros Socios
618	Comunidad de Jamundi	Otros Socios
619	Comunidad de la Dorada	Otros Socios
620	Comunidad de la vereda de Hoya Negra	Otros Socios
621	Comunidad de Milán	Otros Socios
622	Comunidad de Orito	Otros Socios
623	Comunidad de Paujil	Otros Socios
624	Comunidad de Popayán	Otros Socios
625	Comunidad de Rosas	Otros Socios
626	Comunidad de San Pedro	Otros Socios
627	Comunidad de Santander de Quilichao	Otros Socios
628	Comunidad de Sotará	Otros Socios
629	Comunidad de Teorama	Otros Socios
630	Comunidad de Tibú	Otros Socios
631	Comunidad de Timbio	Otros Socios
632	Comunidad de Tumaco	Otros Socios

Item	Name	Partner Type
633	Comunidad López de Micay	Otros Socios
634	Comunidad San Vicente del Caguán	Otros Socios
635	Congregación Padres Somascos	Otros Socios
636	Convenio Andrés Bello	Otros Socios
637	Corporación Andina de Fomento	Otros Socios
638	Corporación Fondo de Solidaridad del Valle del Cauca	Otros Socios
639	Corporación Paideia	Otros Socios
640	Cruz Roja Francesa	Otros Socios
641	Diakonie	Otros Socios
642	Diócesis de Florencia - Parroquia San Isidro de Valparaiso	Otros Socios
643	Diócesis de Florencia - Vicaria del Sur	Otros Socios
644	Diócesis de Istmina	Otros Socios
645	Diócesis de Málaga	Otros Socios
646	Diócesis de Mocoa - Sibundoy - Parroquia Santísima Trinidad de Orito	Otros Socios
647	Diócesis de Quibdó - Gobierno Eclesiástico	Otros Socios
648	Education Development Center	Otros Socios
649	Embajada de Japón	Otros Socios
650	Federación Colombiana Revivir	Otros Socios
651	Federación de Asociaciones de Desplazados del Putumayo - FEDEDP	Otros Socios
652	Fundación Colombo Alemana	Otros Socios
653	Fundación de Atención al Migrante	Otros Socios
654	Instituto Interamericano de Cooperación para la Agricultura - IICA	Otros Socios
655	Junta de Acción Comunal Barrio San Fernando Mpio. el Tambo	Otros Socios
656	Junta de Acción Comunal Asentamiento Humano Nueva Colombia	Otros Socios
657	Junta de Acción Comunal Barrio los Libertadores	Otros Socios
658	Junta de Acción Comunal Barrio Nuevo Milenio	Otros Socios
659	Junta de Acción Comunal Barrio Santander, Municipio de Colombia	Otros Socios
660	Junta de Acción Comunal Martha Lucia Lotero	Otros Socios
661	Médicos del Mundo	Otros Socios
662	Misionera de María Inmaculada y Santa Catalina de Sena	Otros Socios
663	Misioneras Madre Laura Provincia Popayán	Otros Socios
664	Movimondo - MOLISV	Otros Socios
665	OCHA	Otros Socios
666	Organización de Estados Iberoamericanos para la Educación - OEI	Otros Socios
667	Organización de las Naciones Unidas para el Desarrollo Industrial - ONUDI	Otros Socios
668	Organización Panamericana de Salud - Organización Mundial de la Salud	Otros Socios
669	PAH	Otros Socios
670	Parroquia Jesús María	Otros Socios
671	Parroquia del Divino Niño de Pitalito	Otros Socios
672	Parroquia San Antonio de Padua	Otros Socios
673	Parroquia San Francisco de Asís	Otros Socios
674	Parroquia San Pedro Claver	Otros Socios
675	Pastoral Social	Otros Socios
676	Pastoral Social - Diócesis de Mocoa	Otros Socios
677	Pastoral Social de Bucaramanga	Otros Socios
678	Pastoral Social de Florencia	Otros Socios
679	Pastoral Social de Ipiales	Otros Socios
680	Pastoral Social Diócesis de Tumaco	Otros Socios
681	PAX CHRISTI	Otros Socios
682	Programa conjunto. Secretariado Nacional de Pastoral Social -SNPS- Caritas Colombina y la Catolique Relief Services - CRS.	Otros Socios
683	Programa de Naciones Unidas para el Desarrollo - PNUD	Otros Socios
684	Programa Mundial de Alimentos - PMA	Otros Socios
685	Renovación Carismática Católica	Otros Socios
686	Secretariado Arquidiocesano de Pastoral Social Bucaramanga	Otros Socios
687	Secretariado Diocesano de Pastoral Social	Otros Socios
688	Secretariado Diocesano de Pastoral Social de Garzón	Otros Socios
689	Secretariado Diocesano de Pastoral Social de Neiva	Otros Socios
690	Secretariado Diocesano de Pastoral Social de Pasto	Otros Socios
691	Servicio de Pastoral Social Vicaria San Juan Bautista - SEPASVI	Otros Socios
692	Servicio Jesuita para Refugiados	Otros Socios
693	UMATA	Otros Socios
694	UNICEF	Otros Socios

Annex 4.

Project Sheets for Concluded Activities

01. Norte de Santander

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
NS-0036	Monitoring and evaluation of the results of the IOM intervention in the metropolitan area of Cúcuta	Cúcuta	USD 16,324,00	USD 14.528,37	14	0
Execution Partner		Main Achievements				
Francisco de Paula Santander University		The project achieved the following results:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Interinstitutional coordination with the Francisco de Paula Santander University to support the regional office through internships of students in their last semester. • Supported 14 interns to provide technical assistance to income generating and infrastructure projects. • Developed internships for 11 students in their final semester of civil engineering and three students in their final semester of business administration. • Created awareness on internal displacement among the interns • The interns provided accompaniment and technical assistance for the projects for displaced population. 				
December 2, 2002	March 4, 2006					
Closure Mechanism: Financial statement and final project completion statement						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
NS-0055	Strengthening a technical education system, community promotion and agriculture and livestock development with an emphasis on aquiculture in the town of San Pablo, in Teorama.	Ocaña	USD 44.162,00	USD 42.965,65	420	0
Execution Partner		Main Achievements				
Francisco de Paula Santander University – Ocaña Campus		The results of the project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • The project was implemented in the San Pablo Youth Home in Teorama. The land is owned by the municipality. • The 193.5 m2 research and alevine reproduction laboratory infrastructure was remodeled and built. • The aquaculture area was remodeled and extended to include 21 ponds for fish breeding. • A 150 m2 nursery was established with species such as corn, cacao, beans and plantain. • The San Pablo de Teorama Producers Association was strengthened and legally constituted and regulations are in place. • The project helped to establish an agriculture and livestock research program and organized an internship program with the students of the Ocaña campus of the Francisco de Paula Santander University. • A cloning nursery was built and is operating to clone and reproduce cacao vegetable material that is sold to the producers in the region. • The process to build the Institutional Education Project has begun. Currently, the region is implementing the “<i>Transformemos</i>” educational model started by the Governor’s Office. 				
January 22, 2004	January 15, 2006					
Closure Mechanism: Financial statement and final project termination statement.						
Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	

					Direct	Indirect
NS-0056	Protection and reestablishment of education in the towns of Cartagenita, La Trinidad, Honduras, La Motilona and San Juancito.	Towns of Cartagenita, La Trinidad, Honduras, La Motilona and San Juancito – Municipalities of Convención and Teorama.	USD 31.162,00	USD 31.162,00	411	0
Execution Partner		Main Achievements				
Santander Low Income Housing Federation (FESAVIP in Spanish) and the municipality of Convención		The results of the project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Provided educational material to four institutions in the towns La Trinidad, Cartagenita, San Juancito, and Honduras, in order to provide appropriate education to 411 students. • Built a 127.29 m2 multipurpose classroom that includes a kitchen (24.3 m2), a pantry (2.89 m2), two bathrooms (1.53 m2 c/u) and the main room (94.42 m2) for 60 people. • Four school cafeterias were equipped and furnished in the towns of La Trinidad, Cartagenita, San Juancito and Honduras to improve the eating conditions of 411 students. 				
September 30, 2004	January 30, 2006					
Closure Mechanism: Technical statement and final project termination statement.						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
NS-0063	Completion of the first phase of the new water system in the town of La Gabarra in the municipality of Tibú	Town of La Gabarra.	USD 65.433,00	USD 61,260,00	6,500	0
Execution Partner		Main Achievements				
Tibú Municipal Enterprises (EMTIBU in Spanish)		The first phase of the water system in the municipality of La Gabarra was completed. Following are its characteristics and the activities carried out:				
Starting date	Ending Date	<ul style="list-style-type: none"> ▪ A committee comprised of one representative of IOM the Mayor's Office, EMTIBU and the community was created to organize, direct and supervise the development of the project. ▪ The project built a water collection system, a pumping station, a propulsion line, a water treatment plant and the distribution network for the La Gabarra water system in the municipality of Tibú. ▪ A total of 6,500 beneficiaries receive potable water in the town of La Gabarra. 				
March 18, 2004	March 30, 2006					
Closure Mechanism: Technical statement and final project termination statement.						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
NS-0077	Construction of the first phase of the sewage system.	Town of La Gabarra	USD133.476,04	USD 133.476,04	1,565	0
Execution Partner		Main Achievements				
Tibú Municipal Enterprises– EMTIBU E.S.P.		<p>Following are the results of the project:</p> <ul style="list-style-type: none"> • The project generated approximately 12,000 unskilled labor daily salaries thus reactivating the local economy of the town of La Gabarra. • Obtained the support and participation of the community in the construction of the project. The workers made voluntary contributions consisting of additional non-remunerated work and each of them was assigned a specific job. These jobs consisted of the excavation of ditches for the piping to each home. • The physical goals initially established were at 4,128 ml. This was fully completed and the social impact of the project on the community is considered to be high since 5,181 ml of main piping was installed. 				
Starting date	Ending Date					
April 20, 2005	January 30, 2006					
Closure Mechanism: Final project termination statement						

02. Santander

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
SA-0059	Construction of the Pre-school Assistance Center in Ciudadela Café Madrid.	Bucaramanga	USD 102.865,28	USD 102.865,28	200	0
Execution Partner		Main Achievements				
Bucaramanga Mayor's Office		The results of the project are the following:				
Starting Date	Ending Date	<ul style="list-style-type: none"> • Built the 2,000 m2 Café Madrid Pre-School including 10 classrooms, four joint sanitary units, four washbasins, bathrooms for each classroom, library, computer room, cafeteria, two patios, teachers lounge, infirmary and coordination office. • Furnished and provided educational material for 480 students. • Increased, on a permanent basis, the pre-school educational offer to 480 children from two to six years old. • Improved and strengthened the quality of education in the Café Madrid community. 				
October 15, 2004	January 30, 2006					
Closure Mechanism: Final project completion statement						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
SA-0067	Hoya Negra Housing Project	El Hato	USD 8.884,37	USD 8.884,37	353	0
Execution Partner		Main Achievements				
El Hato Mayor's Office		The project resulted in the following:				
Starting Date	Ending Date	<ul style="list-style-type: none"> • Improved the infrastructure of 70 rural homes for an equal amount of beneficiary families. The project included improvement of living quarters, kitchen and basic sanitation thus improving the quality of life of the population targeted by this agreement 				
April 30, 2004	March 30, 2006					
Closure Mechanism: Final project completion statement.						

03. Valle del Cauca

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
VA-0079	Pilot project in the Pablo Emilio Carvajal education center	Buenaventura	USD 44.444,00	USD 34.012,93	873	0
Execution Partner		Main Achievements				
Fundación Sociedad Portuaria		The results of the project are:				
Starting Date	Ending Date	<ul style="list-style-type: none"> • The Pablo Emilio Carvajal education center was strengthened with the implementation of education models such as the Open Doors Program supported by IOM and the Friendly Schools model supported by UNICEF. The combination of these programs with ethnic education criteria and the active participation of the community made it possible to generate an educational project to serve boys and girls in situations of displacement and vulnerability in the district. • The implementation of this project in this marginal area in the municipality of Buenaventura has substantially improved the sector and its surroundings since it is based on a zonal rehabilitation concept. • The project reduced the sector's vulnerability since the area in which the project was implemented was known to have social weaknesses that affected the community and the general safety of child population. • The participation of institutions such as UNICEF, IOM, the Social Action Agency, the Municipality of Buenaventura, the Valle del Cauca Governor's Office and the Presidency of Colombia, through the Godparents Program (<i>Plan Padrino</i>) strengthened the actions of and the coordination among the institutions that support the assistance programs to displaced and vulnerable populations in the municipality of Buenaventura. • Strengthened the education component of the education center by providing material to carry out the activities programmed under the Institutional Education Project (PEI in Spanish). This will provide sustainability to the models and will guarantee access to the services provided by the PEI to boys and girls from both the institutions and the community in general. 				
March 31, 2003	March 30, 2006					
Closure Mechanisms: Final project completion statement.						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
VA-0094	Balcones del Norte I housing project for displaced populations	Guadalajara de Buga	USD 10.574,82	USD 10.574,82	80	0
Execution Partner		Main Achievements				
National Low Income Housing Federation (FENA VIP in Spanish)		The results of the project were:				
Starting date	Ending Date	<ul style="list-style-type: none"> Enhanced housing conditions for 16 displaced families located in the municipality of Guadalajara, in Buga. The quality of life of the beneficiary families has improved by building project housing and by providing psychosocial accompaniment thus providing overall assistance opportunities that will strengthen the internal structure for the individuals and the community. The project made it possible for 16 displaced families to own a home and improve on the overcrowded situation and sanitary vulnerability in the homes they previously lived in. The project generates and strengthens multi-sector opportunities associated with the assistance to displaced populations and contributes to create municipal and departmental disposition to provide assistance to IDP population. This will be reflected through the integration of displaced population in municipal affairs thus causing acceptance from and synergy with vulnerable populations in the municipality. 				
October 27, 2005	February 27, 2006					
Closure Mechanism: Final project completion statement. Technical and financial statements.						

04. Putumayo

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
PU-0045	Technical and Operational Strengthening of the Social Solidarity Network's Putumayo Territorial Unit	Department	USD 69.166.00	USD 67,147,31	15,189	0
Execution Partner		Main Achievements				
Social Solidarity Network		The results of the project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Permanent updating of the Single Registration System (SUR in Spanish) with local and regional information. • Registration of 39,218 people in the Putumayo Single Registration System • A total of 180 reports were generated for institutions of the health system, for public education entities and cooperation and humanitarian assistance agencies such as UNHCR, ICRC and IOM in order to contribute with their work in aiding displaced populations. • The institutional strengthening component made it possible to update the information of the SUR thus reducing the amount of time for the beneficiaries to receive the assistance of the Social Action Agency. 				
May 31, 2003	March 30, 2006					
Closure Mechanism: Final statement of project termination.						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
PU-0063	Productive projects start-up in areas of the provincial center of the Piedemonte Amazon region identified and given priority within the framework of Agreement 019 of the Titles for Uncultivated Plots of Land Program	Orito, Valle de Guamuez, San Miguel	USD 131.160,90	USD 131.160,90	421	0
Execution Partner		Main Achievements				
National Rural Development Institute (INCODER in Spanish)		The results of the project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Identification and selection of 76 producers/rights owners who are in the INCODER process to provide titles for uncultivated plots of land and who met the technical requirements to establish agroforestry demonstration farms with an emphasis on pepper trees. • Four of the 76 beneficiaries are from agriculture and livestock education institutions located in the municipalities of Orito, Valle de Guamuez and San Miguel. • Establishment of demonstration farms as a different alternative that will guarantee steady medium and long term income by participating in marketing channels for product placement. • Provided sustainability to the project through the participation in production marketing channels and an improvement of good practices in terms of crop management and sales orientation among the producers that will guarantee optimum quality of the products when marketed. 				
April 22, 2005	March 15, 2006					
Closure Mechanism: Final technical statement and final project termination statement.						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
PU-0064	Institutional strengthening for the Human Rights Ombudsman's Office for the implementation of an Assistance and Orientation Unit (UAO in Spanish) for Displaced Population in Puerto Asís	Puerto Asís	USD 23.504,00	USD 16.177,42	0	0
Execution Partner		Main Achievements				
Puerto Asís Mayor's Office		The results of the project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Following the remodeling and furnishing of the installations, including furniture and computers, it was possible to start providing assistance to displaced populations. • Inter-institutional coordination facilitated the design and construction of a portfolio of services and access routes to the UAO which has already been implemented. • A monthly average of 1,371 persons accessed the services of various state institutions such as the National Learning Service (SENA in Spanish), the Colombian Family Welfare Institute (ICBF in Spanish), the Municipal Human Rights Representative, the Municipal Health Office and the UAO. • Services provided to displaced populations including training, health, housing, ICBF, statements, humanitarian assistance, relocation, return to the place of origin, appeal for reinstatement, registration information (inclusion, non-inclusion, modification, extension) and registration certification for access to education services and identification have reached a monthly average of 1,371. • State institutions, the Pastoral Social Work and the Human Rights Ombudsman's Office have finally defined their working hours and are providing permanent assistance to displaced population. • Coordination with the Social Action Agency to review the possibility of supporting the operation of the UAO for one year through UTEC [(in Spanish) - the advisory body for the Social Action Presidential Agency]. This will guarantee the sustainability of the UAO, which has become an effective alternative for simplified assistance to displaced populations arriving in Puerto Asís which, according to the Social Action Agency's Single Registration System Only, is the second largest host community in the department. 				
August 29, 2005	March 27, 2006					
Closure Mechanism: Technical statement, financial statement and final project termination statement.						

05. Nariño

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
PA-0079	Socioeconomic stabilization of vulnerable populations in the municipality of Ipiales, Nariño	Ipiales	USD 301.584,10	USD 301.584,10	817	1,050
Execution Partner		Main Achievements				
CRUZ ROJA FRANCESA		The results of this project were:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Established joint work scenarios (community – institutions/organizations) to promote accompaniment and to build personal and social development processes that are critical in recovering and re-establishing better living conditions among vulnerable populations and in reducing socioeconomic vulnerability of displaced and host families in the municipality of Ipiales. • Developed three basic components: Institutional coordination and accompaniment; psychosocial support and occupational therapy; and development of productive activities and marketing strategies. • An interinstitutional support network was created with institutions and local and regional public and private sector organizations that facilitate coordination and complementation for project implementation by transferring intervention methodology. • Institutional agreements were reached that made it possible to complement the actions of the project such as the National Learning Service (SENA), <i>Fundación Salud para Todos</i>, Ipiales Pastoral Social Work, <i>Fundación Casa Madre, Recrear</i>, DLS in Ipiales, AGROCIN, <i>Corporación Unificada Nacional Superior</i> and the Municipal Unit for Technical Assistance (UMATA in Spanish). • Community integration and organization has been strengthened by generating support networks that facilitate the exchange of knowledge, experiences, capacities and resources. • Under the psychosocial component it has been possible to support the Municipal Health Office, Comfaliar and regional IPS (in Spanish) in the development of activities in rural areas. • Changes in human behavior detected among the beneficiaries, their families and the community have been reduced by promoting the development of protection factors at an individual, family and community level. • A total of 210 small productive projects that are feasible and sustainable have been financed with a total of 63 beneficiary families in urban areas, of which 57 are in a situation of displacement, and 147 vulnerable families in rural areas in the municipality of Ipiales. • The beneficiaries of the project received training on business administration (basic accounting, cooperatives, entrepreneurship and business) thus making it possible for them to record business transactions, perform basic balances and become knowledgeable of their productive units. • A Primary Health Network was created with the participation of health promoters, community leaders and civil servants. 				
June 30, 2004	January 31, 2006					
Closure Mechanism: Financial statement and final project completion statement.						

06. Caquetá

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
CA-0054	Strengthen associations and microenterprises comprised by populations that are in an economic reestablishment process in the department of Caquetá with an emphasis on the improvement of production and diversification processes.	Florencia Doncello Valparaíso (Santiago de la Selva)	USD 39.648,93	USD 39.648,93	470	122
Execution Partner		Main Achievements				
Floresncia Chamber of Commerce .		The final balance in terms of implementation of the project is the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Strengthened the project's beneficiary microenterprises by providing training on organizational issues (cooperatives, basic accounting and administration). • Provided training to three microenterprises on productive processes (dairy products, recycling, plantain production), regulatory issues and quality control. • Designed process flow charts and furnished production equipment. • Carried out surveys, research and baselines to market the products of the beneficiary microenterprises and obtained letters of intent for future purchases. • Strengthened the El Cambio Cooperative and determined the products that would be established in the market. • Strengthened plantain producers by providing training on administration (accounts, administration, organization, marketing and sales) and production processes (crop generalities, obtaining seeds, sowing methods, fertilization, plague control and potential crop by-products). Reactivated the Doncello stockpiling center to market approximately 2,882 kg of plantain monthly. 				
October 27, 2005	February 27, 2006					
Closure Mechanism: Financial statement and final project termination statement.						

07. Chocó

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
CH-0027	Reactivate trade from the Baudó River to the port of Buenaventura of plantain and natural products	Municipalities of Alto, Medio and Bajo Baudó,	USD 10.437	USD 7.346,02	0	3,000
Execution Partner		Main Achievements				
Alcaldía Municipal del Alto Baudó		<p>Following are the achievements made through this project:</p> <ul style="list-style-type: none"> • Equipped a boat with all the items necessary for commercialization of farm products in the Baudó River basin. • Strengthened 36 Local Community Councils that have an influence in the Baudó River through trading processes for the products in the region to the port of Buenaventura. • Strengthened economic, financial and business administration processes with an emphasis on cost management, prices, production strategies and product marketing in the project beneficiary communities. • By creating and starting-up two community stores food and consumer goods supplies now are included in the family basic food needs that are not produced in the zone for communities that were economically trapped by the presence of illegal armed groups. • Facilitated purchase of products included in the family basic food needs at a lower price to 36 communities in the zone by re-establishing bartering as a business organizational method that was created after the boat started operating. • Two auxiliary wooden boats used, one of them with a 15 HP motor, to transport plantain from the Baudó River tributaries to the main boat. • The families who did not have means of transportation for their products benefit from the boats since this has facilitated their work and reduced costs. • During the month the boat makes two to three trips. This has diversified the products of the family basic food needs in the municipalities of Bajo, Medio and Alto Baudó and increased the frequency of fuel and gas supplies. 				
Starting Date	Ending Date					
July 30, 2004	March 30, 2006					
Closure Mechanism: Technical statement; financial statement; final project termination statement						

08. Cauca

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
CU-0039	Basic sanitation and housing improvement.	Popayán and Buenos Aires	USD 59.919,36	USD 59.919,36	400	0
Execution Partner		Main Achievements				
Cauca Governor's Office		The results of the project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • The sanitation conditions of 80 displaced and vulnerable families improved by adapting basic sanitation that included bathrooms, kitchens, wash areas and septic tanks. • 80 displaced and vulnerable families were provided training on healthy housing techniques including issues such as water management, waste management, septic tank maintenance and self construction. • Reduced the incidence of diseases and of child morbidity and mortality caused by diarrheic and gastrointestinal conditions due to inadequate water management, food manipulation and preparation and situation of waste water and excrements. • Improvement of the quality of life of the displaced and host community by addressing basic sanitation needs in their homes. • The community has been trained and has become aware of the appropriate use and protection of water and septic tank maintenance (healthy homes). 				
July 14, 2005	January 30, 2006					
Closure Mechanism: Financial statement and final statement of project termination						

10. Inter-regional

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0047	Provide support to the Office of the Presidential Adviser for Municipalities and Regions in identifying and arranging for municipal projects directed at displaced and vulnerable populations	Countrywide	USD 108.305.00	USD 101.693,71	1,500	0
Execution Partner		Main Achievements				
Office of the Presidential Adviser for Municipalities and Regions – Social Action		Following are the results of the project:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Provided accompaniment and follow-up for projects that have been proposed and initiated by municipal and local authorities in various communities (i.e. Small Hydroelectric Plant in Guapi Brazo Seco Project). • Provided support, promoted and initiated several local public interest initiatives in areas such as local development, public services, illegal crops and plots of land acquisitions, among many others. • Provided support to the municipalities and regions that asked for support of the Office of the Presidential Adviser for Municipalities and Regions for the paperwork to acquire and/or improve properties. • Made the necessary arrangements with various government institutions such as the Ministry of the Environment, Ministry of Agriculture, Ministry of Mining and Energy, Ministry of Social Protection, governors' offices and municipal offices, among others, in order to obtain financial resources and logistical and administrative support to implement community projects. • Coordinated meetings with vulnerable, displaced and peasant populations and local and municipal authorities to generate a dialogue and reach agreements on education and training strategies (agriculture, livestock, commercial). • The "Network of Social Promoters Encounter: Expoinnovación" was held. Various innovative public investment experiences (municipal, regional and national) associated with displaced and host populations were discussed. 				
August 21, 2003	March 30, 2006					
Closure Mechanism: Final project completion statement						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0069-1	Construction of multiple homes	Santa Rosa- Sur de Bolívar; El Tambo- Cauca; El Paujil – Caquetá.	USD 333,333.00	USD 333,333.00	355	0
Execution Partner		Main Achievements				
Colombian Fund for Development Projects (Fonade in Spanish)		The results of project implementation were:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Construction of three multiple homes including the design of the following areas: kitchen and appliances; multiple classrooms; rooms for infants and walkers; sanitary units for minors and adults; inside patio with games; administrative area; water reserve tank; washing area. • Construction of three multiple homes for 324 beneficiary minors zero to six years old. • The construction created the appropriate spaces so that the minors of the beneficiary municipalities may achieve the appropriate psychomotor development. • Furnished and equipped three multiple homes with the necessary items for its appropriate operation. • Institutional coordination with the Colombian Family Welfare Institute (ICBF in Spanish) to provide orientation to the parents. • Created three cooperatives comprised of community mothers who manage the homes. 				
March 3, 2004	February 15, 2006					
Closure Mechanism: Financial statement						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0072	Remodel and extend the Altos de Cazucá school in Soacha, Bogotá D.C and build and furnish the Pies Descalzos School in Quibdó.	Soacha, Cundinamarca and Quibdó, Chocó	USD 166.413,23	USD 166.413,23	1,030	0
Execution Partner		Main Achievements				
Fundación Pies Descalzos		The results of the implementation of this project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Built and remodeled the school taking into consideration the regulations for displaced persons. • Created the areas and the appropriated conditions for student recreation and sports. • Improved the safety and hygiene conditions of the minors. • Built areas and classrooms to improve the learning processes. • A nutritional evaluation of the school children carried out which indicates that 61% of the minors had nutritional problems. • Provided food supplies that increased the nutritional condition of the children that attend school. • Training on eating habits was provided to the parents. • Extracurricular activities with a group of interdisciplinary teachers to provide accompaniment and academic catch up support in math, reading and writing. Priority was given to those minors with learning problems. • A special catch up program was created in Quibdó for 28 children who did not have the academic level that corresponded to their age. • Activities of parasite removal for minors in Altos de Cazucá under an agreement between the <i>Fundación Pies Descalzos</i> and Colsanitas, a health services provider. • Another achievement during the implementation of the project was the development of a family emotional evaluation and a services program. Individuals and their families were provided psychiatric and psychology treatment and home follow-up in the most serious cases. 				
January 27, 2004	March 30, 2006					
Closure Mechanism: Financial statement pending						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0079 - 3	Support for food security of rural families in the Pacific Coast of Nariño.	Francisco Pizarro, Mosquera, La Tola, Tumaco, Barbacoas, Roberto Payán, Maguí Payán, El Charco, Santa Bárbara and Olaya Herrera, Department of Nariño	USD 63.694.00	USD 63.694.00	19.671	0
Execution Partner		Main Achievements				
Tumaco Pastoral Social Office		<ul style="list-style-type: none"> The project increased its impact with funds contribution from 10 municipalities. The contribution from municipalities and the Department of Nariño to food security is a big step for the sustainability of the project. The beneficiaries became aware of the fact that it is beneficial to raise crops for self consumption. This was achieved through training and the various campaigns undertaken under the project. Important efforts were made to adapt the culture of food security within the context of Nariño's Pacific Coast. The project took advantage of values from the Afro-Colombian culture and traditional knowledge and recovered the types of seeds that still survive. 				
Starting date	Ending Date					
December 6, 2004	March 30, 2006					
Closure Mechanism: Final statement of project termination						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0087	Third International CODHES Seminar: Institutional and social responses to forced displacement in Colombia	Countrywide	USD 29.551,50	USD 29.551,50	50	0
Execution Partner		Main Achievements				
Consultancy for Human Rights and Displacement (CODHES in Spanish)		<p>Following are the results of the project:</p> <ul style="list-style-type: none"> The Third CODHES Seminar "Institutional and Social Responses to Forced Displacement in Colombia: Defending the Rights", held on November 2004, generated discussions about forced displacement and the humanitarian crisis in Colombia. The seminar addressed four fundamental issues: a) general situation of the humanitarian and human rights crisis; b) evaluation of the focus currently given to public policies on forced displacement; c) the role of international cooperation in finding a solution to the crisis; and d) producing proposals and strategies from a rights perspective. The seminar was attended by national and international experts, researchers, government institutions, non-government organizations, social leaders, cooperation agencies, friendly governments, control organizations and organizations for the displaced. A final report of the seminar was put together and published. 				
Starting date	Ending Date					
November 4, 2004	March 1, 2006					
Closure Mechanism: Final project termination statement						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0102	Third Afro-Colombian Institutional Strengthening Conference	Countrywide	USD 20.000,00	USD 14.248,10	200	0
Execution Partner		Main Achievements				
The Association of Mayors of Municipalities with Afro-Colombian population (AMUNAFRO in Spanish)		The implementation of the project resulted in the following: <ul style="list-style-type: none"> • Evaluated the progress being made and results achieved by the institutional strengthening of Afro-Colombian communities in the country. • The project represented an opportunity to define strategies to promote social, economic and political development of Afro-Colombian communities. • The conference was attended by national and international experts whose participation broadened the perspective not only of the needs and problems of Afro-Colombian communities but also of the possible solutions to same. 				
Starting date	Ending Date					
August 6, 2005	January 31, 2006					
Closure Mechanism: Final project termination statement.						

Code	Project Site/s	Budget	Disbursements	Beneficiaries		
				Direct	Indirect	
ID-0112	Carmen de Atrato, Tado and Bojayá (Chocó); Los Andes and El Charco (Nariño); *Matanza, *Lebrija, *Santa Rosa del Sur and Landazuri (Santander); Mercaderes, *Rosas, *La Vega and El Tambo (Cauca); Leguízamo, Mocoa, *Santiago, *Sibundoy, Puerto Caicedo, Villagarzón and *Valle del Guamuez (Putumayo); La Plata, *Isnos *La Argentina, Gigante, *Villavieja, Colombia, *Salado Blanco and *Oporapa (Huila); Convención, El Tarra, Teorama, Tibú and Sardinata (Norte de Santander)	USD 64.304,00	USD 51.102,09	9,015	0	
Execution Partner		Main Achievements				
IOM		The results of the implementation of the project are: <ul style="list-style-type: none"> • A total of 1,668 displaced families of municipalities with a high index of unsatisfied basic needs were provided support with the design of projects. • A total of 1,000 displaced families were approved social rural housing subsidies. • A total of C\$ 5,890,204,387.73 was raised, equivalent to the subsidies approved by <i>Banco Agrario</i>, . • Two types of solutions were proposed for the project: construction on plots of land owned by the beneficiaries; and housing improvement and basic sanitation. • The project had strategic partners such as the <i>Banco Agrario de Colombia</i>, the Social Action Agency and various mayors' offices. 				
Starting date	Ending Date					
September 5, 2005	March 30, 2006					
Closure Mechanism: Technical statement and final housing project completion statement.						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0113	Technical assistance to the Human Rights Ombudsman's Office to promote and monitor the exercising of the right to sexual and reproductive health.	Bogotá	USD 11.033,08	USD 11.033,080		50
Execution Partner		Main Achievements				
Profamilia		The results obtained through the implementation of the project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • Elaborated one document on the status of sexual and reproductive health promotion, assistance, monitoring and rights among internally displaced populations. • Designed and carried our actions to promote and monitor strategies associated with the right to access sexual and reproductive health. • Created a directory of society strategic stakeholders including perspectives, ethnicity, age, condition and an action plan in order to connect with civil society. • Created and implemented a monitoring system for the application of sexual and reproductive rights with an emphasis on domestic and sexual violence. • Generated a legal assistance and accompaniment system for victims of domestic and sexual violence. • Generated action plans and defense institutionalization strategies to promote and monitor sexual and reproductive health rights with an emphasis on domestic and sexual violence. 				
October 5, 2006	January 5, 2006					
Closure Mechanism: Technical and financial statements						

Code	Title	Project Site/s	Budget	Disbursements	Beneficiaries	
					Direct	Indirect
ID-0114	International Seminar: Assistance to Displaced Population in Colombia - Balance and Perspectives"	Countrywide	USD 3.282,28	USD 3.282,28	0	150
Execution Partner		Main Achievements				
Colegio Mayor de Nuestra Señora del Rosario		The achievements under this project are the following:				
Starting date	Ending Date	<ul style="list-style-type: none"> • During the "International Seminar: Assistance to Displaced Population in Colombia - Balance and Perspectives" emphasis was placed on the human rights situation of displaced populations. • The project financed the participation of 150 students who are interested in the situation of displacement in Colombia. • Various perspectives on human rights and displacement were presented and discussed during the seminar. • The seminar was an opportunity for various institutions and state and international organizations to meet and present the different perspectives of the human rights issue and its connotation as related to internally displaced populations. 				
September 14, 2005	February 20, 2006					
Closure Mechanism: Final project completion statement						

Annex 5.

Sustainability: Methodology and Analysis

SUSTAINABILITY OF THE PROJECTS OF THE IDP PROGRAM

1. GENERAL RESULTS: Evaluation of the January – March 2006 Quarter

During the first quarter in 2006 the sustainability¹ of 83 IDP projects was evaluated -- 59% of which are in the final stages of implementation – due to the proximity of the final termination date of the IDP Program, in June of this year. The following chart shows the distribution of the projects by regional office and main component:

NUMBER OF PROJECTS EVALUATED BY COMPONENT AND REGIONAL OFFICE

OFFICE	COMPONENTES					Total Number of Projects	Project %
	Education	Health	Infrastructure	Income Generation	Institutional Strengthening		
Caquetá	0	0	3	1	0	4	5%
Cauca	5	0	8	1	2	16	19%
Chocó	0	0	2	2	0	4	5%
Huila	0	1	1	2	1	5	6%
Nariño	0	0	3	2	0	5	6%
Norte de Santander	4	0	1	1	1	7	8%
Putumayo	0	0	0	1	4	5	6%
Santander	0	1	4	2	0	7	8%
Valle del Cauca	0	1	6	3	1	11	13%
Inter-Regional	9	4	0	2	4	19	23%
Total	18	7	28	17	13	83	1
%	22%	8%	34%	20%	16%	100%	

The average sustainability rate during this period is at 4.04 with 63.85% of the projects being highly sustainable, 32.5% reaching with an average level of sustainability and 3.61% with a low level of sustainability.

CONSOLIDATED RESULTS OF THE PROGRAM January – March 2006

Project Progress %	Number of Projects	Project %	Number of Projects By Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0%-30%	1	1%	0	1	0	3,70
30.1%-70%	23	28%	2	9	12	3,88
70.1%-100%	59	71%	1	17	41	4,11
Total	83		3	27	53	4.04

¹ The IDPs Program understand sustainability as the capacity to integrate the processes developed under a project or program to the institutional, social, family and/or personal dynamics in such a way that its benefits will remain over time.

The following chart shows the average sustainability rate obtained in the measurements made in each region during 2005 and in the first quarter in 2006 and the total average for the Program²:

Regional Office	18th Quarter (Jan - Mar 2005)	19th Quarter (Apr - Jun 2005)	20th Quarter (Jul - Sep 2005)	21st Quarter (Oct - Dec 2005)	22nd Quarter (Jan - Mar 2006)
Caquetá	3.42	3.64	3.63	2.96	3.04
Cauca	4.01	3.98	4.17	4.21	4.40
Chocó	3.93	4.15	4.15	4.21	3.34
Huila	4.12	4.26	4.13	4.09	3.73
Nariño	4.13	4.02	3.80	3.96	3.78
Norte de Santander	3.82	3.71	3.98	3.85	4.35
Putumayo	3.98	3.85	4.06	4.30	4.19
Santander	4.17	4.08	3.96	4.10	4.07
Valle del Cauca	3.84	4.20	3.96	3.94	4.25
Nivel Central	3.92	4.05	4.12	3.84	3.96
Total Average	3.98	4.03	4.02	3.94	4.04

In the following section the results obtained by each regional office and its corresponding analysis are described. It also explains the reasons for the high or low rates of sustainability obtained.

3. CONSOLIDATED ANALYSIS BY REGIONAL OFFICE

CAQUETÁ

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0
30,1% - 70%	2	50,%	1	1	0	2,50
70,1% - 100%	2	50%	0	2	0	3,59
Total	4		1	3	0	3,04

During the first quarter of this year the Caquetá Regional Office analyzed the sustainability situation of four projects, two of which are in the last implementation stages and two in the second stage. The results of the measurement indicate that 75% of the projects, which include an income generation project (CA0054³) and two infrastructure projects (CA0049 y CA0056⁴), have an average level of sustainability. The remaining 25%, equivalent to one project, has a low degree of sustainability (CA0055⁵).

In comparison with the previous quarter, two of the projects evaluated improved their sustainability situation: CA-0054 due to business and financial feasibility improvement and CA-0056 as a result of community organization and greater integration among its beneficiaries in the development of same. The other two projects did not change in relation to the previous quarter (Banco Agrario housing improvement project in rural areas) because no significant activities took place during this quarter.

² The fact that the composition of the projects from one quarter to the next has experienced variations due to the implementation of new projects and to the fact that completed projects are not being evaluated is a matter that should be taken into consideration.

³ CA-0054: Strengthening associations and microenterprises comprised of populations that are in an economic reestablishment process in the department of Caquetá emphasizing the improvement of production processes and product diversification.

⁴ CA-0049: Housing and basic sanitation improvement in the municipality El Paujil;

CA-0056: Building a sewage system for the homes of displaced and host families.

⁵ CA-0055: Housing and basic sanitation improvement in the villages of El Paraíso, Argentina, Rosal and others.

It should be pointed out that, despite the fact that the public order situation in the department has not been the best during the past few years the projects have not experienced long interruptions that could have changed their sustainability rate. This is due both to the commitment of the institutions involved and of the beneficiaries toward the project and to their high motivation toward implementation and completion.

CAUCA

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	6	37,5%	0	0	6	4,51
70,1% - 100%	10	62,5%	0	1	9	4,33
Total	16		0	1	15	4,40

During this period the sustainability situation of 16 projects was evaluated with the majority of them dealing with infrastructure and education. These projects received excellent reviews because they have consolidated over time and have been able to fine tune consensus building opportunities that help strengthen the sustainability of the processes once the intervention by the cooperating entities is completed.

The four projects under the education component are noteworthy because, by strengthening the educational models and the food security component they have shown significant intermediate results. It is very important to understand that food security provides significant elements for the analysis of the success or good results obtained to date with these four projects together with the establishment of educational models as the main objective.

The most noteworthy achievement is the participation of 415 students who, during the January-March 2006 period, have carried out activities that strengthen the creation of their own educational systems in accordance with the customs of the region. They are trying to connect the rural world with modernization keeping in mind the necessary respect for indigenous cultures, thus strengthening sustainability.

The fact that the cosmic view of the ethnic groups served by these projects (paeces, guambianos y coconucos) grants great importance to the participation of the parents in strengthening the community's organizational process and in raising their children, is also noteworthy.

CHOCÓ

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	2	50%	1	0	1	3,34
70.1%-100%	2	50%	1	0	1	3,35
Total	4		2	0	2	3,34

During the January-March 2006 period the Chocó Regional Office evaluated four of its projects: two under the social infrastructure and housing component and two for income generation and employment improvement. The results of the evaluation depend mainly on the status and progress of the project over time and the level of development and ownership of the activities implemented to date.

Project CH-0026⁶ for social infrastructure and housing, whose main subcomponents are rural housing and basic sanitation, has been given a high sustainability qualification because it is part of a state program (Rural Housing). Project CH-0041, under the income generation and employment improvement component, was classified as a special project with a 2.63 qualification. This project, however, is guaranteed to obtain the best results in terms of products and sustainability because it is coordinated through the National Learning Service (SENA), a well-known, serious and prestigious institution. In addition, the project is important in the process to reactivate the local economy around the forestry-lumber-furniture chain.

Furthermore, Project CH-0027⁷, also under the income generating component, obtained a 4.2 qualification in its completion phase. This is an indication of the great dedication of the key social and institutional stakeholders, such as the municipal office (counterpart) and the beneficiaries represented by the Alto Baudó community councils grouped in the Association of Alto Baudó Councils (ACABA in Spanish), who are committed to its sustainability. Finally, project CH-0040⁸ for social infrastructure and housing with an emphasis on educational material and building is a long range project despite the fact that it is a new project in terms of implementation and has a short duration regarding investment. This is due to the commitment of the education institution leading it, of partners such as the SENA and of the educational community (parents). The qualification received by this project during this quarter is at 4.05 and the tendency is toward improvement.

HUILA

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	1	20%	0	1	0	3,70
30,1% - 70%	1	20%	0	1	0	3,38
70,1% - 100%	3	60%	0	1	2	3,86
Total	5		0	3	2	3,73

Five projects were evaluated for the 22nd quarterly report: two under the income generation component, one for infrastructure, one for institutional strengthening and one in health with an average 3.73 sustainability rate.

The highest sustainability rate (4.17) was that of Project HU-0037⁹ due to the high level of empowerment associated with the operations of the Unit for Assistance and Orientation to Displaced Populations (UAO in Spanish), by both the Neiva Governor's Office, the Mayor's Office and the Social Action Agency. This was followed by Project HU-0025¹⁰ (4.0) due to the high level of approval by the beneficiaries and the significant commitment of the Mayor's Office.

The two income generation projects present a low sustainability rate because: HU-0038¹¹ has not received the Fomipyme funds to start implementation; and HU-0036¹² has just started to place the pending portfolio to strengthen or establish economic units.

⁶ CH-0026: "Banco Agrario" Housing Project in Riosucio.

⁷ Reactivate trade of plantain and natural products in the Baudó River to the Port of Buenaventura.

⁸ Building a technical bloc and a multipurpose room in the El Reposo II School

⁹ Strengthening the Unit for Assistance and Orientation to Displaced Populations (UAO) in Neiva, Huila

¹⁰ Rural housing with Banco Agrario subsidies in the municipality of Colombia

¹¹ HU-0038: Strengthening the productive units of displaced and vulnerable microentrepreneurs who are beneficiaries of the rotating fund under the IOM-CCA credit agreement

¹² HU-0036: Strengthening the small credit fund for displaced populations in Neiva.

NARIÑO

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	3	60%	0	3	0	3,53
70,1% - 100%	2	40%	0	0	2	4,15
Total	5		0	3	2	3,78

The processes generated by the post-emergency assistance projects for displaced populations in Nariño have provided long-lasting solutions to this problem thus maintaining good project sustainability conditions. Regarding the projects where IOM intervention has been completed, the level of interinstitutional coordination required for the continuity of the processes still remains.

The beneficiaries of the income generation projects have not only benefited directly through the productive units but have obtained value-added knowledge and skills development thus making it possible for them to face their situation and transform their environment. The participation of FOMIPYME has contributed to make progress on providing sustainability to the Program and to the productive units. These resources will strengthen the implementation of training processes and will improve the quality of the products and the access to new markets and to banking credits.

Furthermore, interinstitutional support networks have been created for each project with public and private entities and organizations at a local and regional level that will guarantee continuity of the actions over time. Also, community integration and organization has been strengthened by generating support networks that facilitate the exchange of knowledge, experiences and resources. Likewise, the progress made in terms of organizing and strengthening the associations for displaced populations and the democratic election and participation of its representatives in municipal and departmental communities need to be underscored.

The projects have contributed to reduce the human behavioral alterations among the beneficiaries, their families and the community by promoting the development of protection factors at a personal, family and community level thus improving coexistence. The Citizen Radio Stations have strengthened the opportunities to exercise democracy thus making it possible for the various stakeholders and institutions to take on the responsibility of building processes to improve the level and quality of life through information.

IOM, the departmental government, the Social Action Agency, the United Nations High Commissioner for Refugees (UNHCR), the Pan American Health Organization (PAHO) and the host communities have work jointly to strengthen and consolidate the strategy for the department's Single Overall Plan for Reestablishment (PIUR - *Plan Integral Único de Restablecimiento*) in order to provide continuity to the reestablishment of populations in a efficient and permanent manner.

NORTE DE SANTANDER

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	0	0%	0	0	0	0,00
70,1% - 100%	7	100%	0	1	6	4,35
Total	7		0	1	6	4,35

During the first quarter in 2006 seven project sustainability evaluations were made to projects that are in their final implementation stage which means that they have implemented at least 70% or more of the project. These projects received an average qualification at 4.35.

Project NS-0055¹³ received an average qualification of 3.71 due to the institutional and technical limitations of the implementing party. Two projects stand out: NS-0074¹⁴ (4.33) for institutional strengthening which has facilitated the presence of the Office of the Governor in the municipalities most affected by displacement to improve the response in the emergency and reestablishment stage, the information and the design of Single Overall Plans; and project NS-0077¹⁵ (4.75) to build a sewage system that exceeded the goals by more than 24% in the short term with high technical specifications.

The sustainability and success of these projects is mainly due to the previous technical evaluation, the institutional stability of the counterparts, the permanence and stability of the officials in charge, the technical experience and the exclusive dedication of the people in charge of directly implementing the projects.

PUTUMAYO

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	2	40%	0	1	1	4,22
70,1% - 100%	3	60%	0	1	2	4,17
Total	5		0	2	3	4,19

One of the strong points of the institutional strengthening projects is that the strategies have been directed at strengthening processes or programs of state organizations that are already institutionalized. This means that they are part of their mission statements. This has contributed to guarantee program continuity over time. Within the framework of project PU-0067¹⁶ (PIU), one of the greatest achievements is the inclusion of the program into the municipal and departmental public policies thus facilitating inclusion into the municipal and departmental budgets by the Executive and Legislative branches.

The weakness of the income generating component regarding sustainability of the projects is due to the fact that they are operated with private organizations that require resources to provide them continuity in spite of the fact that they have institutionalized these processes, they. In order to overcome this situation the process to select the beneficiaries was strengthened and has gone from selecting persons to support business initiatives to giving priority to those persons or groups that already have a productive unit operating and need to strengthen it (training, sales and marketing). This has facilitated the inclusion of new stakeholder into the process: the official banking system (implementing commercial credit lines with *Banco Agrario*), programs with other cooperation agencies (UTEK – UNHCR) and the state (Fomipyme, mayors' offices, provincial centers). This is the reason why to date these project have a good level of sustainability.

¹³ NS-0055: Strengthening a system for technical training, community promotion and agriculture and livestock development with an emphasis on farming in the town of San Pablo, in the municipality of Teorama.

¹⁴ NS-0074: Institutional strengthening of the Norte de Santander Municipal Office of the Interior and the Governor's Office

¹⁵ NS-0077: Building the first phase of the sewage system in the town of La Gabarra, in the municipality of Tibú.

¹⁶ PU-0067: Implementation of the Single Overall Plan in the department of Putumayo and its consolidation as a departmental and municipal public policy.

Unfortunately, during this quarter external public order situations took place that negatively affected the development of the projects thus affecting sustainability.

SANTANDER

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	2	28,6%	0	2	0	3,62
70,1% - 100%	5	71,4%	0	2	3	4,25
Total	7		0	4	3	4,07

Seven projects were evaluated during the January-March 2006 quarter reaching a 4.07 average sustainability rate which represents a slight decline compared with the previous quarter (4.10). This was due to projects SA-0091¹⁷ and SA-0092¹⁸, which obtained average sustainability levels (3.83 and 3.40 respectively). Furthermore, 71% of the projects (five projects) are in their third implementation stage and reached a 4.25 qualification and 29% (two projects) are in their second phase and were given a 3.62 qualification.

In terms of components, the health projects obtained the best rating (4.60), followed by social infrastructure and housing (4.08), which includes basic sanitation, urban housing and education infrastructure, and the income generation projects were last with 3.77.

Under the health component the local capacity strengthening strategy to increase the coverage and quality of the sector project SA-0074¹⁹ (4.60), implemented with the Landázuri Mayor's Office and the hospital, is noteworthy. The construction of the health center for the Borrascoso - Opón area, with a potential to serve 6,000 people, has already been completed and furnished. In April the center will start providing services that will be fully coordinated with the Basic Assistance Plan (PAB in Spanish) thus strengthening the sustainability of the processes.

Project SA-059-1²⁰ (4.0), under social infrastructure and housing, is noteworthy as well. The school was built and furnished as part of the Municipal Education Office's local policy to increase education services coverage. The school will provide 480 new slots for five to seven year old children in the Café Madrid neighborhood, which is the main center in Bucaramanga hosting displaced populations.

¹⁷ SA-0091: Improvement of 45 homes in Barrancabermeja

¹⁸ SA-0092: Strengthening a clothes making unit comprised of displaced women.

¹⁹ SA-0074: Building, furnishing and implementing a health program in the Borrascoso – Opón region, in the municipality of Landázuri, in the department of Santander.

²⁰ SA-0059-1: Building a pre-school services center in Ciudadela Café Madrid, in the municipality of Bucaramanga

VALLE

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	0	0%	0	0	0	0,00
70,1% - 100%	11	100,0%	0	2	9	4,25
Total	11		0	2	9	4,25

The sustainability evaluation included 11 projects, all of which are in the third implementation stage as follows: six for infrastructure, one for health, one for institutional strengthening and three for income generation. The average sustainability rate is at 4.25.

Among the group of projects that do not include infrastructure work the general average reached 4.0 (five projects). The average sustainability rate for the six social infrastructure and housing projects is at 3.7. Furthermore, compared with the previous quarter, five projects improved sustainability, three remained the same and three fell slightly.

BOGOTÁ HEADQUARTERS

Project progress %	Number of projects	% Projects	Number of Projects by Level of Sustainability			Average Sustainability Rate
			Low	Average	High	
0% - 30%	0	0%	0	0	0	0,00
30,1% - 70%	5	26,3%	0	1	4	4,17
70,1% - 100%	14	73,7%	0	7	7	3,89
Total	19		0	8	11	3,96

A total of 19 projects were evaluated by the Bogotá headquarters offices reaching a 3.96 average sustainability rate. Of these, 57.9% obtained a high sustainability rate and 42.1% were qualified as average.

As is normally the case, the sustainability situation of the projects carried out by headquarters is greater because these are designed jointly with government institutions which later on are in charge of implementing them, doing so within the framework of their normal activities. Therefore, the processes are included into their institutional framework from the beginning.

4. FINAL OBSERVATIONS

The average sustainability rate during this quarter increased slightly, from 3.94 to 4.04, compared to the previous quarter. There are two sustainability measurements left to be carried out for this Program because the activities will end by June of this year. Therefore, during the last three months that are left the projects that have not consolidated their sustainability processes will need to be strengthened, especially the three projects that obtained a low sustainability rate during this evaluation.

The evaluations carried out to date indicate that the situations that most contribute to consolidating the processes over time are the commitment of the implementing partners and the participation of the community in the development of the projects. As expected, the situation regarding public order is one of the external issues that most affect the normal development of the projects thus affecting the possibilities of undertaking sustainability processes once the activities of the project have been completed. However, the commitment of

the implementing parties, the beneficiaries and the partners involved represents a great contribution to reducing the negative impact of this situation in the project

5. METHODOLOGY INFORMATION

The sustainability evaluation concentrates on three strategic areas -- environment, stakeholders and capacities – from which 12 criteria become apparent, with criteria being the different views that can be used to analyze a process or result.

Every project obtains a sustainability rate (from a 1.00 to 5.00 scale) that makes it possible for IOM to know if the project has a low, average or high sustainability level:

Sustainability Rate	Sustainability Level
1.00 – 2.99	Low
3.00 – 3.99	Average
4.00 – 5.00	High

Likewise, IOM has taken into consideration the various stages of a project because the activities change depending on the phase. Therefore, three stages have been established according to the % of progress of the project to design the indicators. The third phase includes the projects that were completed from October to December 2004.

Project Implementation Phase	Project Progress % (Depending on duration)
First	0.00% - 30%
Second	30.1% – 70%
Third	70.1% - 100%

The methodology has a few restrictions that need to be taken into consideration when analyzing the results:

- The methodology evaluates general aspects of the projects because the indicators have been standardized so that they can be used for all the sub-components.
- The indicators do not measure the quantitative results of the projects since measurement and analysis varies according to the characteristic of each project.

The methodology operates as a warning system that allows IOM to analyze general project information. More specific indicators should be analyzed for each project in order to carry out a more in depth analysis of the results obtained through this methodology.

Annex 6.

Calendar of Events

Region	Date	PROJECT: CODE AND NAME	NATURE / DESCRIPTION OF THE EVENT	PLACE	MUNICIPALITY	SUGGESTED ATTENDANCE (CHIEF OF MISSION, DEPUTY CHIEF OF MISSION, PROGRAMS DIRECTOR PROGRAM OFFICER)	AID SUGGESTED ATTENDANCE
NORTE DE SANTANDER	4-Apr-06	NS-0074 Institutional Strengthening of the Office of the Secretary of the Interior, Governor's Office of Norte de Santander	Opening of Observatorio Social y Político	Governor's Office of Norte de Santander	Cúcuta	Program Officer IDP's and chief of mission	YES
	18-Apr-06	NS-0077 Construction of the first stage of the sewage system of corregimiento La Gabarra, municipality of Tibú.	Inauguration and delivery of the project	La Gabarra	Tibú	No	YES
	24-May-06	NS-0068 Alliances for local and regional development in the Department of Norte de Santander, through the implementation of Productive Solidarity Groups	Inauguration of the Unidad Productiva delivery of the project	Sector La Alejandra	El Zulia	Program Officer IDP's and chief of mission	YES
	25-May-06	NS-0078 "Productive pedagogical model of the chain Piscicola comercial in the young farmer's homes"	Inauguration of piscícolas work	Hogar Juvenil Campesino	Mutiscua	Program Officer IDP's and chief of mission	YES
	26-May-06	NS-0078 "Productive pedagogical model of the chain Piscicola comercial in the young farmer's homes"	Inauguration of piscícolas work	Hogar Juvenil Campesino	Chinácota	Program Officer IDP's and chief of mission	YES
	26-May-06	NS-0078 "Productive pedagogical model of the chain Piscicola comercial in the young farmer's homes"	Inauguration of piscícolas work	Hogar Juvenil Campesino	Toledo	Program Officer IDP's and chief of mission	YES
	29-May-06	NS-0079 "Project of training for the job to 250 persons in the municipalities of Cúcuta, Tibú, Ocaña y el Corregimiento de La Gabarra"	Delivery of Studies Certificate	SENA	Cúcuta	Program Officer IDP's and chief of mission	YES
	30-May-06	NS-0079 "Project of training for the job to 250 persons in the municipalities of Cúcuta, Tibú, Ocaña y el Corregimiento de La Gabarra"	Delivery of Studies Certificate	La Gabarra	Tibú	no	SECURITY PROBLEMS
	31-May-06	NS-0079 "Project of training for the job to 250 persons in the municipalities of Cúcuta, Tibú, Ocaña y el Corregimiento de La Gabarra"	Delivery of Studies Certificate	SENA	Ocaña	Program Officer IDP's and chief of mission	YES
	20 - January - 2006	CU-0034 Housing improvement and basic for 56 families in the corregimiento of Domingullo in the municipality of Santander de Quilichao - Cauca	Inauguration of 55 rural housing in Vereda Domingullo	Domingullo	Santander de Quilichao	SUGGESTED ATTENDANCE (Deputy Chief of Mission and Program Officer)	NO
	21 february 2006	CU-0027 Niño Jesus de Praga School in the El Retiro Municipality Popayan	Inauguration School's Niño Jesus de Praga	Popayan		First Lady Lina Maria Uribe - Director Program Officer	AID
	24 february 2006	CU-0039 Basic sanitation and housing improvement in municipalities of Popayán and Buenos Aires	Delivery of 80 improved houses - Popayán and Buenos Aires zone in Cauca	Santiago de Cali	Popayán	DEPUTY CHIEF OF MISSION AND PROGRAM OFFICER	NO
	20 - January - 2006	ID-0076: Health Attention to the displaced population towards the formulation, execution and monitoring of territorial integral plans	Training to establish strategic lines of Cooperation between Social Protection Minister and IOM	Bogotá	Bogotá	CHIEF OF MISSION, PROGRAMS DIRECTOR PROGRAM OFFICER AND AREA SPECIALIST	Andrew Krefft

Region	Date	PROJECT: CODE AND NAME	NATURE / DESCRIPTION OF THE EVENT	PLACE	MUNICIPALITY	SUGGESTED ATTENDANCE (CHIEF OF MISSION, DEPUTY CHIEF OF MISSION, PROGRAMS DIRECTOR PROGRAM OFFICER)	AID SUGGESTED ATTENDANCE
VALLE	Junio	VA0094 Urban Home to 25 families displaced of farmer home of Buga	Official delivery of Houses	Los Balcones del Norte	Buga	Program Officer IDP's	NO
	Junio	VA0097 Improve the infrastructure and endowment of the cafeterias School attended by the Governor's Office of Valle del Cauca.	Delivery of the cafeterias	Blanca y Terron Colorado School	Cali	Program Officer IDP's	NO
	Junio	VA0098 Improvement of home and basic sanitation for 300 families displaced and vulnerables.	Deliver of the improvements	Comuna 12	Buenaventura	Program Officer IDP's	NO
CHOCO	27 Y 28 DE ABRIL DE 2006	CH-0040 Construction and endowment of multi-purpose hall and work shop in the school El Reposo II of Quibdo and CH-0041 Adapt and edowment of the center of productive development about the chain of wood in the SENA for the tecnic training of pupulation in situation of displacement and vulnerability in the Department of Choco Phase I.	Inaguration	ZONA URBANA - BARRIO EL REPOSO II	QUIBDÓ	SUGGESTED ATTENDANCE (Chief of Mission , Program Officer IDP's, Area Specialist)	SI
CAUCA	2-Jun-06	CU-048 "Institutional Strengthening to the Association of Cabildos Indigenas of Cauca's North in its areas of health, planning and Indigena safeguard with the purpose of improve the capacity of response in front of the emergencies.	Event of Close of the Project	Bodega alta	Caloto	SUGGESTED ATTENDANCE (Chief of Mission , Program Officer IDP's, Area Specialist)	NO
	31-May-06	CU041 Food Security as cross-cutting theme in the pedagogical productive process i.e. agropecuaria gaitana fxiwCU042 Strengthening of the Security Food in the Institution of agriculture education "Los Comuneros" CU043 Adjustment and endowment of farming exploitation to improve the food security of the Farming School "El Guambiano" .CU044 Strengthening of the articulation between education and community development, through agro-food projects searching solidify the systems of crop: farms type "TUL" and traditional farm and the	Un trueque Zonal para cierre de proyectos. Change of zones for Close of the projects	Resguardo la Maria	Piendamó	SUGGESTED ATTENDANCE (Chief of Mission , Program Officer IDP's, Area Specialist)	YES
	5-Jul-06	Ampliación de la Escuela de Bellavista	Inaguration of Bellavista School	Timbiqui	Timbiqui zona urbana	Program Officer IDP's,	NO

Region	Date	PROJECT: CODE AND NAME	NATURE / DESCRIPTION OF THE EVENT	PLACE	MUNICIPALITY	SUGGESTED ATTENDANCE (CHIEF OF MISSION, DEPUTY CHIEF OF MISSION, PROGRAMS DIRECTOR PROGRAM OFFICER)	AID SUGGESTED ATTENDANCE
SANTANDER	21-Apr-06	SA-090 Formación laboral para el empleo en los sectores del cuero, calzado y confección textil	Graduations in the area of leather and Confections	Bucaramanga	Bucaramanga	Area Specialist	NO
	29-Apr-06	SA-0074 Construction, donations to and implementation of health programs in the Borrascoso region – Opón , Landazuri municipality.	Inauguration of Health Center Miralindo	Corregimiento de Miralindo	Landazuri	Area Specialist	NO
	29-Apr-06	SA-0084 Land adjudication for the at risk declared displacement zone in the municipality of Landázuri	Delivery of property titles	Corregimiento de Miralindo	Landazuri	Area Specialist	NO
	26-May-06	SA-059-1 Construction of Center of Attention for Preschool Children at Ciudadela Café Madrid in the Municipality of Bucaramanga.	Inauguration of the preschool	Preescolar Café Madrid	Bucaramanga	SUGGESTED ATTENDANCE (Program Officer IDP's, Area Specialist)	NO
	29-Jun-06	SA-089 Construction of 150 homes in the neighborhood Altos del Paraiso in Lebrija	Inauguration of homes	Altos del Paraiso* Lebrija	Lebrija	SUGGESTED ATTENDANCE (Program Officer IDP's, Area Specialist)	NO
	30-Jun-06	SA-091 Improving of 45 homes in Barrancabermeja	Inauguration of investment of Homes	Barrancabermeja	Barrancabermeja	SUGGESTED ATTENDANCE (Program Officer IDP's, Area Specialist)	NO
INTER REGIONAL Educación - Fortalecimiento Institucional	19-20-21 Abril 2006	ID-0109: InstitutionalStrengthening of the Procuraduria General de la Nación with the purpose of carrying out economical, social and cultural rights of the displaced population.	Training of regional staff of the Procuraduría General de la Nación in Caqueta in topics of economical, social and cultural rights of the displaced population.	Florencia (Caquetá)	Florencia	No	No
	26-27-28 Abril 2006	ID-0109: InstitutionalStrengthening of the Procuraduria General de la Nación with the purpose of carrying out economical, social and cultural rights of the displaced population.	Training of regional staff of the Procuraduría General de la Nación in Caqueta in topics of economical, social and cultural rights of the displaced population.	Bucaramanga (Santander) Hotel Chicamocha	Bucaramanga	No	No
	8-Apr-06	ID-0069-04 Education and mobilization processes to prevent domestic violence and promote coexistence (three pilot projects).	Socialization of main success and general development of the projects HAZ PAZ in Soacha	Coliseo General Santander. Calle 15 # 15-53en	Soacha	Nubia Pulido	No
	20-21 Abril 2006	ID-0069-04 Education and mobilization processes to prevent domestic violence and promote coexistence (three pilot projects).	Socialization at National Level	INES Av. 9 (Ferrocarri) No. 172 - 90.	Bogotá	SUGGESTED ATTENDANCE (Program Officer IDP's, Area Specialist)	Andrew Krefft

Region	Date	PROJECT: CODE AND NAME	NATURE / DESCRIPTION OF THE EVENT	PLACE	MUNICIPALITY	SUGGESTED ATTENDANCE (CHIEF OF MISSION, DEPUTY CHIEF OF MISSION, PROGRAMS DIRECTOR PROGRAM OFFICER)	AID SUGGESTED ATTENDANCE
INTER REGIONAL Generación de Ingresos	23 de mayo de 2006	ID-0124: Award OIM to good work and new models to intervention for the stabilization socio economical in the displaced and vulnerable population.	Delivery of Award	Bogota	Bogota	SUGGESTED ATTENDANCE (Chief of Mission , Program Officer IDP's, Area Specialist)	Andrew Krefft
INTER REGIONAL SALUD	20 y 21 de Abril de 2006	ID-0076 Health Attention to the displaced population towards the formulation, execution and monitoring of territorial integral plans	Final training of Health Attention	Bogotá -	Bogotá	SUGGESTED ATTENDANCE (Chief of Mission , Program Officer IDP's, Area Specialist)	Andrew Krefft
	26 al 28 de Abril de 2006	ID-117 - Strengthening of the investigation activity of Fiscalía General de la Nación about crimes of sexual and inter-family violence, where the victims are forcefully internally displaced persons and vulnerable receptor communities.	Training of investigation	Bogotá -	Bogotá	SUGGESTED ATTENDANCE (Chief of Mission , Program Officer IDP's, Area Specialist)	Andrew Krefft
	24 y 25 de Abril de 2006	ID-118 - Investment of the forensic aid to victims of violence inter-family and sexual violence and intervention to aggressors, emphasis in womens and childs with IFV S, displaced, receptors and Vulnerables.	Training of Forensic Crime	Bogotá - s	Bogotá	SUGGESTED ATTENDANCE (Program Director , Program Officer IDP's, Area Specialist)	Andrew Krefft
	25 y 26 de Abril de 2006	ID-118 - Investment of the forensic aid to victims of violence inter-family and sexual violence and intervention to aggressors, emphasis in womens and childs with IFV S, displaced, receptors and Vulnerables.	Training of Forensic Crime	Bucaramanga -	Bucaramanga	SUGGESTED ATTENDANCE (Program Director , Program Officer IDP's, Area Specialist)	NO
	27 y 28 de Abril de 2006	ID-118 - Investment of the forensic aid to victims of violence inter-family and sexual violence and intervention to aggressors, emphasis in womens and childs with IFV S, displaced, receptors and Vulnerables.	Training of Forensic Crime	Cali -	Cali	SUGGESTED ATTENDANCE (Program Director , Program Officer IDP's, Area Specialist)	NO
	27 y 28 de Abril de 2006	ID-118 - Investment of the forensic aid to victims of violence inter-family and sexual violence and intervention aggressors, emphasis in womens and childs with IFV S, displaced, receptors and Vulnerables.	Training of Forensic Crime	Medellín -Hotel	Medellín	SUGGESTED ATTENDANCE (Program Director , Program Officer IDP's, Area Specialist)	NO
	20 y 21 de Abril de 2006	ID-120 - Strengthening of the capacity of aid to physics health, mental health and social inclusion of womens, childs with IFV S, displaced, receptors and Vulnerables and intervention aggressors, in the General System of Social Security in health.	Trainig of training in Physics Health	Pasto	Pasto	SUGGESTED ATTENDANCE (Program Director , Program Officer IDP's, Area Specialist)	NO
	7 de Abril de 2006	ID-121 - System of early attention articulate to the Institutional Net of Attention of health "SAT -RIAS" in the cities of Neiva and Popayan for the attention in health of the forcefully internally displaced persons.	Training of Guarantee in Control to attention in health	Popayán	Popayán	SUGGESTED ATTENDANCE (Program Director , Program Officer IDP's, Area Specialist)	NO
7 de Abril de 2006	ID-123 - Promotion and monitoring of the rights to the sexual and reproductive health of Womans and childs and adolescent displaced and vulnerable receptors with emphasis in enter-family violence and sexual.	Training to staff of Defensoria del Pueblo	Bogotá-event 's room Profamilia	Bogotá	SUGGESTED ATTENDANCE (Program Director , Program Officer IDP's, Area Specialist)	NO	

Annex 7.

Press Coverage

Sena y Acicam capacitarán a ganaderos y mipymes

Arrancó cadena productiva del cuero

LUZ MARINA PEROZO
REDACTORA DE LA OPINIÓN

Ayer se dio inicio formal a la ejecución del proyecto de fortalecimiento de la cadena productiva del cuero-calzado y manufacturas en Norte de Santander, en el cual participan el Servicio Nacional de Aprendizaje (Sena), la Gobernación de Norte de Santander y la Asociación Colombiana de Industriales del Cuero, Calzado y Marroquinería (Acicam).

Los recursos aportados al proyecto ascienden a \$1.325 millones, de los cuales una parte se destinarán a mejorar la infraestructura física y tecnológica del Sena, y otra parte a la capacitación y asesoría a las unidades ganaderas y empresariales productoras de calzado y manufacturas en Norte de Santander.

Luis Gustavo Flórez, presidente nacional de Acicam, dijo a **La Opinión** que el proyecto contará con la asesoría de expertos internacionales así como de los instructores del Sena, con quienes se buscará desarrollar un programa de transferencia de tecnología con las experiencias que se obtengan del proyecto, con el fin de llevarla a otras regionales del Sena en el país.

Indicó Flórez que la fase de adquisición de equipos y de intervención y gestión en las unidades productivas podría estar lista antes de los próximos 60 días para iniciar el proceso formativo.

“Con este proyecto tenemos cerca de 18 actividades de gestión y estamos esperando que haya impacto en unas 100 empresas de calzado y manufacturas de Norte de Santander; asimismo, se va a capacitar directamente en los hatos ganade-



Foto: *Neranda Herrera/La Opinión*

Directivos del Sena regional, Acicam, la Gobernación y la Universidad Nacional se reunieron ayer en el Sena de Pescadero para iniciar el proyecto de fortalecimiento a la cadena productiva del cuero, el calzado y las manufacturas.

ros, para mejorar la calidad de la materia prima que es el cuero”.


Agregó que en la parte terminal de la cadena productiva, que corresponde al calzado y la marroquinería, habrá intervenciones en las áreas de diseño y manufactura del producto.

Asistentes

A la reunión para la puesta en marcha del proyecto, que se realizó ayer en la sede del Sena regional, estuvieron presentes por Aciam: Luis

Gustavo Flórez; Ladis Crespo y Guillermo Rangel, presidenta y director ejecutivo regional; el director regional y el director del Centro de Atención Multisectorial (Caim) del Sena, José Antonio Lizarazo y Fabio García, respectivamente.

Por la Gobernación asistió el secretario de Planeación Departamental, Carlos Eduardo Rodríguez y tres expertos de la Universidad Nacional, entidad que será interventora del proyecto para hacer el seguimiento y monitoreo de los resultados.

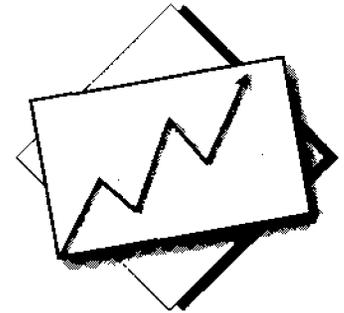

ECONOTAS

OIT advierte

(Colprensa).- La Organización Internacional del Trabajo (OIT) advirtió por intermedio de su página de internet sobre los peligros que representa el contacto y exposición con asbesto o materiales fabricados con este componente.

La OIT estima que 100 mil personas mueren cada año a causa de trabajos vinculados a la exposición al asbesto. «El cáncer ocasionado por el asbesto provocará la muerte de al menos 15.000 personas en los próximos cinco años en Japón y de más de 100 mil personas en Francia en los próximos 20 ó 25 años. En Estados Unidos, desde los años 70 han sido presentadas cientos de miles de denuncias por muertes, cáncer y problemas de salud relacionados con la exposición al asbesto, causando la bancarrota de numerosas compañías», advirtió el Organismo en su informe

Créditos, \$1 billón

(Colprensa).- Los recursos destinados a la financiación de vivienda de las familias colombianas, incluso aquellas de

Atención en salud para desplazados

Programa 'Cúrese en salud' está en marcha

Acción Social; la Organización Internacional para las Migraciones, OIM; el Ministerio de la Protección Social, y la Universidad del Cauca pusieron en marcha la campaña 'Cúrese en salud', como una respuesta a la sentencia T-025 de 2004, para garantizar los derechos fundamentales de la población desplazada.

Con el ánimo de brindar a la población desplazada una mejor atención en el tema de la salud, la Agencia Presidencial para la Acción Social y la Cooperación Internacional, Acción Social; la Organización Internacional para las Migraciones, OIM; el Ministerio de la Protección Social, y la Universidad del Cauca han puesto en marcha la estrategia comunicativa 'Cúrese en salud'.

El plan responde a lo contemplado en la sentencia T-025 de 2004, según la cual la Corte Constitucional hace un llamado a las entidades que deben atender a esta población para que sean garantizados sus derechos fundamentales.

'Cúrese en salud' se suma a los demás planes implementados por estas organizaciones en aras de adoptar medidas de prevención y atención en diferentes aspectos, para las personas que ven amenazada su calidad de vida por el flagelo del desplazamiento forzado.

Estos derechos están también fundamentados en el artículo 15 de la Ley 387 de 1997 de acuerdo con el cual "la población en situación de desplazamiento forzado interno tiene derecho a una atención humanitaria de emergencia por un espacio máximo de tres meses, prorrogables excepcionalmente por tres meses más, dependiendo de la disponibilidad presupuestal".

La campaña hace parte del proyecto de 'Fortalecimiento de la capacidad del sector salud para la atención de la población en situación de desplazamiento forzado interno en Popayán, y propuesta para planes generales en el Cauca, en el que el Alma Mater participa como ente articulador de "alianzas estratégicas entre entidades del Estado e internacionales comprometidas con



Archivo / EL LIBERAL

'CÚRESE EN salud' es una de las acciones que buscan implementar medidas de prevención y atención, para las personas que ven amenazada su calidad de vida por el desplazamiento forzado.

la atención" a esta población.

De allí que la estrategia sea desarrollada con el aporte de la Agencia de los Estados Unidos para el Desarrollo Internacional, Usaid, institución de apoyo con la cual se trabajan acciones en temas como revisión de recursos para la atención a la población mencionada, investigación de la línea base demanda - oferta en salud, formulación del Plan de Atención Básica Departamental y gestión en atención en salud de la red pública para los desplazados.

Como parte de la estrategia de divulgación, 'Cúrese en salud' puso a disposición de la población desplazada la información en varias piezas de comunicación entre las que se incluyen una cartilla didáctica en la que se condensa todo lo relacionado con los derechos en salud de la población en condición de desplazamiento.

Asimismo, es una guía básica de orientación para que aquellas personas que se ven en estas circunstancias realicen adecuadamente su proceso de inscripción al Sistema Único de

Registro, S.U.R., así como lo relacionado con el acceso de estas personas a los programas de salud y la carta de los derechos básicos de toda persona que ha sido víctima del desplazamiento forzado.

El programa aportó recursos destinados a promover, de manera más visible, la labor desarrollada por la Unidad de Atención y Orientación al Desplazado, UAO, entidad articuladora de las acciones dirigidas a esta población en la capital caucana.

A estas acciones se suman la proyección de implementar la estrategia denominada Sat-rías en salud, mediante la cual se plantea que el Centro Universitario de Salud, CUS, del barrio Alfonso López sirva como entidad prestadora de salud a desplazados, luego de ser remitidos por la Unidad de Atención y Orientación del municipio, y dos proyectos orientados a brindar asistencia en el ámbito nutricional y procesos terapéuticos para el tratamiento de la depresión, el duelo, eventos catastróficos, ansiedad, somatización, enfermedad y/o muerte.

En el marco del Plan Padrino

Embajada de Japón entregará aulas escolares en Popayán

Hoy tres instituciones educativas del Municipio serán beneficiadas con nuevas obras de infraestructura que generarán cerca de mil nuevos cupos escolares en sectores deprimidos de la capital caucana.

Varias obras de infraestructura y dotación escolar por un valor superior a los 800 millones de pesos serán entregados hoy en tres barrios de Popayán al Gobernador del Cauca, al Alcalde de Popayán y a los niños de las escuelas beneficiadas con los proyectos.

Según informó la Consejería Presidencial de Programas Especiales, en total son 13 las aulas que se entregarán, generando así 904 nuevos cupos escolares para la niñez de los sectores El Retiro, El Mirador y El Placer.

Es así como los niños de las instituciones educativas Niño Jesús de Praga, Colegio Comercial del Norte y El Mirador, recibirán hoy al Embajador de Japón, Wataru Hayashi; a la Primera Dama de la Nación, Lina María Moreno de Uribe, y la Consejera Presidencial de Programas Especiales, Ana Julieta Ruiz, y el Representante en Colombia de la Organización Internacional para las Migraciones (OIM), Diego Beltrán, quienes les harán entrega oficial de las obras cuyo costo asciende a los 818 millones 285 mil 992 pesos.


Además de estos recursos, el programa Computadores para Educar empezará a funcionar en dos de las instituciones educativas intervenidas con estos proyectos, que fueron ejecutados por la Federación Nacional de Cafeteros de Colombia.

El acto contará con la presencia de todos los involucrados en el desarrollo de estos proyectos, con el fin de observar el estado final de las obras y fortalecer la alianza de trabajo entre el Plan Padrino, la Embajada de Japón y las demás entidades que hicieron parte del proceso, así como evaluar el impacto generado con estos importantes proyectos y cómo con ellos se ha contribuido a la política de cobertura y calidad de la educación.


De igual forma, fuera de las obras que se entregarán en el Niño Jesús de Praga, la institución contará con la implementación de la estrategia Escuela de Puertas Abiertas que fue financiada por el Gobierno de los Estados Unidos a través de Usaid - OIM, y también será beneficiaria del programa 'Computadores para educar'.

Unión de esfuerzos

Para la Secretaría de Educación Municipal, Norela Perdomo de Gómez, cada uno de estos convenios suscritos entre la Embajada de Japón, el gobierno Nacional, Departamental y Municipal, son un ejemplo de la unión de esfuerzos y presupuestos para

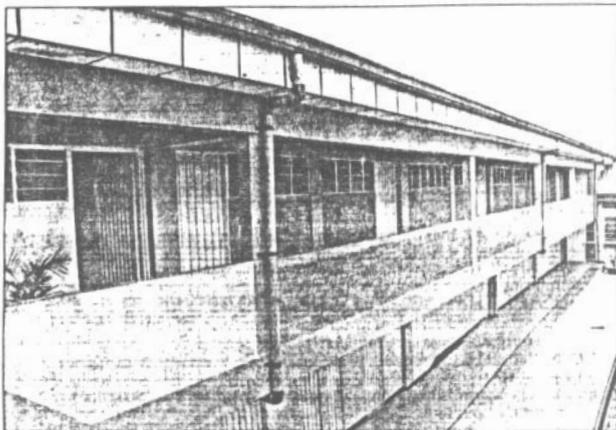

TRES AULAS escolares, un área para enfermería o depósito, entre otras, serán parte de las obras que se entregarán en el colegio El Mirador y que contaron con recursos superiores a los 223 millones de pesos.

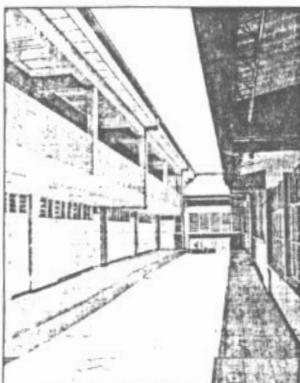

EL COSTO total de las obras asciende a los 818 millones 285 mil 992 pesos.

llevar a cabo las obras. Entre las obras que se entregarán están 4 aulas escolares, una biblioteca y una zona administrativa y otras más en el barrio El Retiro, donde está ubicada la


Institución Niño Jesús de Praga, y que contó con una inversión de 279 millones de pesos; también están tres aulas escolares, un área para enfermería o depósito, entre otras, ubicadas en el colegio El Mirador, con recursos por el orden de los 223 millones de pesos; y seis aulas y una batería sanitaria en la institución educativa Comercial del Norte, por un valor de 283 millones de pesos, recursos que fueron cofinanciados para las tres instituciones.

"A las 10:00 de la mañana empezaremos en el Niño Jesús de Praga, esperamos estar a las 11:00 de la mañana en El Mirador y a las 2:00 de la tarde en el Comercial del Norte, con esto queda demostrado que si unimos esfuerzos conseguimos muchas más cosas para la educación", señaló.

Así mismo indicó que una vez se haga entrega de estas obras la Administración Municipal continuará gestionando con los diferentes organismos internacionales y entidades del Estado nuevos recursos para beneficiar a otras comunidades educativas del Municipio, como ha sido la entrega a otras escuelas de dotación a través de programas como 'Computadores para educar'.

"Seguiremos demostrando ante el Ministerio de Educación y el Gobierno nacional, la necesidad de la continuidad en el apoyo para la calidad de la educación y del presupuesto del municipio de Popayán", comentó.

Una de las últimas acciones que adelantó la Secretaría de Educación Municipal para el proyecto fue la instalación de redes eléctricas que requería el colegio Niño Jesús de Praga, y la entrega en semanas pasadas de unos pupitres, "así que la inversión no se hace únicamente en infraestructura, igual se asumen unas responsabilidades de muebles que ha venido cumpliendo la Secretaría de Educación según su compromiso", señaló.

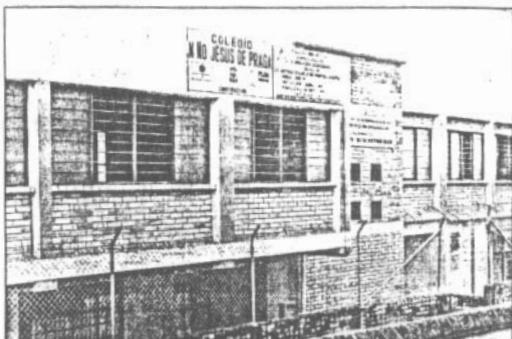

EL PROYECTO en la institución educativa Niño Jesús de Praga contó con aportes económicos del gobierno japonés, la Alcaldía Municipal de Popayán, la Gobernación del Cauca y la Federación Nacional de Cafeteros de Colombia.

En 'Emergencia educativa'

Se estudian otras opciones

Con la declaratoria de 'Emergencia educativa en el Cauca', la Secretaría de Educación viene analizando una serie de alternativas para mantener la continuidad del servicio en la región, ya que una de las dificultades por las que atraviesa el sector son las condiciones de deficiencia en que están siendo atendidos unos 21 mil niños.

"El año pasado teníamos un Banco de Oferentes que terminó el 31 de diciembre de 2005, estamos conformando uno nuevo para que quede a futuro de manera continua y que sea más sólido; estamos en ese proceso y la consolidación termina el 16 de marzo", señaló la Secretaria de Educación Departamental, Blanca Inés Chavez Jimenez.

Con la alternativa de decretar la 'Emergencia educativa' el Gobierno Departamental tiene la posibilidad de contratar, ya que el Banco de Oferentes se asemeja a una contratación directa, "una vez el Banco de Oferentes termine, estaremos contratando los docentes para estos niños que están sin atender hasta

el momento", dijo.

Otra alternativa que viene estudiando la Administración, junto con Asoinca y las otras poblaciones, es la modificación del calendario escolar, debido a que estos niños están sin estudiar.

Así mismo, otra posibilidad que se está contemplando es recuperar todo el tiempo que se ha perdido en el transcurso de estos meses a través de los contratistas, de manera que ellos recuperen dicho tiempo y puedan organizarse las clases el día sábado, o también estaría la posibilidad de extender más el calendario.

"Estamos esperando que la legalidad y el cumplimiento de la norma se den, en este momento estamos trabajando con los docentes para que mantengan a los niños en las aulas con los rectores, mien-



RECUPERAR El tiempo perdido con los contratistas actuales o extender el calendario escolar, hacen parte de las alternativas que analiza la Administración Departamental.

tras nosotros terminamos con este proceso, incluso en algunos municipios hemos hecho algunos acuerdos sin comprometer a la Administración para que se normalice la situación, los alcaldes han sido conscientes de esto y están dando unas soluciones iniciales mientras terminamos el proceso de contratación", concluyó.

Apoyo a la educación



Archivo / EL LIBERAL

LAS INSTITUCIONES educativas El Mirador, Niño Jesús de Praga y Comercial del Norte, recibirán hoy del gobierno japonés una serie de obras de infraestructura y dotación que superan una inversión de los 800 millones de pesos y que buscan generar cerca de mil nuevos cupos escolares.

Desde las 10:00 de la mañana, los delegados de las entidades responsables de la ejecución presupuestal recorrerán cada una de las instalaciones educativas en un acto

que contará con la participación de la Primera Dama de la Nación, Lina Moreno de Uribe, entre otros invitados especiales.

De igual forma, el programa 'Computadores para Educar' empezará a funcionar en dos de las instituciones educativas intervenidas con estos proyectos, y se iniciará la implementación de la estrategia 'Escuela de Puertas Abiertas' que fue financiada por el Gobierno de los Estados Unidos a través de

Usaid - OIM.

LEA / PÁG. 3A /

**SE VENDE PAPEL
PERIÓDICO POR
ARROBAS...**

INFORMES:

8242418 Ext. 100

Martes 21 de febrero de 2006 Popayán El Liberal

'Escuelas de puertas abiertas'

Una estrategia de movilización educativa

Con la implementación del programa en la institución Niño Jesús de Praga se busca atender a las poblaciones afectadas por el desplazamiento forzado.

Con el apoyo de la Embajada de los Estados Unidos la Organización Internacional para las Migraciones, OIM, además de participar en la construcción de las obras entregadas a la institución educativa Niño Jesús de Praga, inició en dicho plantel la implementación del modelo 'Escuelas de Puertas Abiertas'.

"Con este programa hemos intentado involucrar no solamente a los niños y al personal docente sino a la comunidad en general y los padres para la integración de los niños y de las familias", manifestó la Oficial de prensa de la OIM, Rocío Sanz.

Este modelo, considerado como un instrumento dinamizador y reconstructor del tejido social, brinda oportunidades para la educación y recreación a los niños y jóvenes que no tienen las posibilidades para aprender y encontrarse en ambientes creativos y constructivos; así mismo busca la integración social entre niños, jóvenes y adultos de población desplazada.

Entre los programas que ofrece están los círculos comunitarios, proyectos productivos, campeonatos en diferentes disciplinas deportivas, cursos en arte y cultura, programas académicos de alfabetización, nivelación y validación escolar; también brinda programas de educación sexual, convivencia familiar y participación ciudadana, entre otros.

Para desarrollar este tipo de programas según informó la OIM, cada centro educativo deberá construir su propio programa de acuerdo a las necesidades de la comunidad circundante y con las posibilidades de espacio, tiempo y agentes educativos de otras instituciones municipales.

De igual forma, la institución educativa o la alianza deberá gestionar los recursos ante la OIM u otra agencia de cooperación para financiar la adaptación y construcción de aulas y dotación de equipos, entre otros requerimientos.

Otros proyectos

Durante su estadía en la capital caucana el Ministro Consejero del de asuntos económicos y negocios de la Embajada norteamericana, Milton Drucker, visitó otros proyectos que la OIM ha desarrollado con fondos del gobierno de los Estados Unidos en la ciudad.

Es así como en el Hogar Infantil Pequeñitas, ubicado en la Regional del Icbf Cauca, se apoyó la construcción de un área adicional para la realización de actividades extra escolares con los niños y se dio la apertura escolar para más de 100 niños de familias desplazadas.

"He tenido la oportuni-



EL PROGRAMA busca promover nuevos espacios de integración social entre niños, jóvenes y adultos de población desplazada

dad de hablar con la gente, especialmente con los niños de las instituciones, y fue muy interesante conocer que están haciendo muchas cosas por crecer, además muestra el valor que la sociedad colombiana tiene en fomentar y mejorar la educación", señaló Drucker.

El centro escolar también ha servido para que las familias desplazadas y receptoras se reúnan y tengan un espacio para sus actividades comunes, en el que además se desarrolló la 'Escuela de puertas abiertas', donde parte de la estrategia incluye actividades para la resolución pacífica de conflictos y la integración comunitaria.

"Nosotros continuaremos apoyando con recursos de AID y también trataremos de estimular otros gobiernos a través de Naciones Unidas que esta participando con nosotros, para promover este tipo de

ayudas en la región y el país", señaló el Ministro Consejero.

Acciones a futuro

En los cinco años que lleva trabajando la OIM en Popayán, se han atendido a más de 50 mil personas, principalmente de familias desplazadas, con proyectos que han estado dirigidos a la atención educativa, generación de ingresos, y en el campo de la salud con proyectos de infraestructura.

"La semana entrante inauguraremos un proyecto de 88 viviendas para familias desplazadas en Popayán; hemos trabajado también con el gobierno local y regional con Acción Social y el Icbf para fortalecer las instituciones, de manera que ellos tengan mayor presencia en la atención a familias desplazadas y vulnerables", comentó Rocío Sanz.

Para este año habrá un cambio dentro de la atención que la OIM ha venido trabajando con población vulnerable en la región, ya que el año pasado firmó un acuerdo de alianza con la Fundación Panamericana de Desarrollo, que con la asistencia del gobierno americano, empezará a desarrollar otros cinco años de asistencia a desplazados.

"En el Cauca será la Fundación Panamericana quien continuará orientando estas acciones y nosotros la seguiremos apoyando por lo que hemos implementado tecnología y tenemos el conocimiento adquirido, para que la Fundación desarrolle las actividades relacionadas con desplazamiento", concluyó Sanz.



DELEGADOS DE LA OIM acompañaron al Ministro Consejero (8) de la Embajada norteamericana durante su visita a los proyectos ejecutados en la ciudad

Consejo Superior aplazó designación del Rector

El martes 28 de marzo se realizará la designación de Rector de la Universidad del Cauca por parte del Consejo Superior, luego de la presentación de propuestas que realicen los candidatos.

En sesión del martes 21 de febrero, el Consejo Superior modificó la Resolución por la cual se fija la fecha para la designación de Rector de la Universidad del Cauca, pasándola al 28 de marzo de 2006.

De esta manera, se cuenta con más tiempo para que los aspirantes al máximo cargo de dirección del Alma Mater puedan presentar sus propuestas y planes de trabajo ante la comunidad universitaria.

"Lo que se pretende es que el proceso interno de la Universidad, que también es eminentemente democrático y académico no se traspase para que no adquiera unas connotaciones de tipo político y se quede enmarcado dentro de lo que es la academia", manifestó el Secretario General del Alma Mater, Jorge Alberto Duque Mejía.

También se aprobaron tres fechas para la realización de foros al interior de la institución. El primero de ellos será el martes 14 de marzo con los profesores luego el jueves 16 de marzo con los estudiantes y finalmente el

martes 21 de marzo con los trabajadores y administrativos.

Los foros se realizarán en el auditorio Antonio José Lemus Guzmán de la Facultad de Ciencias de la Salud, de 8:00 del día, y cuya coordinación estará a cargo de la Secretaría General de la Universidad.

"Dentro de la misma Resolución del Consejo Superior estamos invitando a todos los estamentos para que no solamente asistan sino que promuevan la participación en dichos foros porque es la mejor forma dentro del ambiente académico de conocer que plantea o qué visión de universidad tienen quienes aspiren al cargo", señaló Duque Mejía.

El Rector que sea designado el martes 28 de marzo se estará posesionando el viernes 31 de marzo, fecha en la que se vence el actual periodo rectoral. La designación se realizará por un periodo de tres años, 2006-2009.



LOS ASPIRANTES al máximo cargo de dirección del Alma Mater contarán con más tiempo para presentar sus propuestas y planes de trabajo ante la comunidad universitaria.

Posición estudiantil

Por su parte, la representación estudiantil ante el Consejo Superior había cuestionado aspectos relacionados con la Resolución 002, en la que según manifestaron "no define fecha límite de inscripción de candidatos ni regla- menta escenarios de debate".

Así mismo señalaron que en anteriores ocasiones se habían puesto fechas límites de inscripción de candidatos y mecanismos como la consulta estudiantil y profesoral, para que los representantes de dichos estamentos delimitaran su voto de acuerdo con el resulta-

do de la misma.

"Esto le da un tinte democrático a la elección, porque al menos la comunidad conoce los candidatos y las propuestas, pero no es un mecanismo de democracia real, ya que los estudiantes y profesores solo representan dos votos en el Consejo Superior", indicaron los estudiantes en el comunicado.

Con el aplazamiento de la designación, los estudiantes esperan que se implementen mecanismos de elección con participación democrática donde haya foros para que la comunidad universitaria conozca las propuestas de los candidatos.
