



Healthy Mother/Healthy Child Results Package

Quarterly Performance Monitoring Report Option Period Quarter Five October 1 – December 31, 2002



John Snow, Inc.
Arabic Software Engineering (ArabSoft)
Clark Atlanta University
The Manoff Group, Inc.
TransCentury Associates

In collaboration with
The Ministry of Health and Population
Cairo, Egypt
and
USAID/Egypt
(Contract No. 263-C-00-98-00041-00)

January 20, 2003

BEST AVAILABLE

TABLE OF CONTENTS

Introduction ----- 01

Task One: Basic Package of Essential Services Established and Standards Defined ----- 03

Task Two: Pre/In-Service Training System Designed to Disseminate Standards to Public and Private Providers ----- 11

Task Three: Public and Private Provider Partnerships with Communities to Develop and Manage District Plans ----- 19

Task Four: Monitoring System in place to Track Utilization and Impact and Provide Feedback ----- 21

Task Five: Research Activities ----- 23

Task Seven: Better Social Community Services ----- 27

Task Ten: Small Grant Program ----- 33

Task Eleven: Commodity Procurement Program ----- 35

Task Twelve: Coordination Activities ----- 37

Contract Administration ----- 47

TABLE OF ANNEXES

Annex A - Performance Milestones Charts -----	49
Annex B - Maps of Target Governorates -----	53
Annex C - JSI Contract Staff List -----	63
Annex D - Summary of Upgraded Status of Facilities in Target Districts -----	71
Annex E - Summary of Training of Personnel in Target Districts -----	83
Annex F - Summary of Management Improvement Activities at District Level -----	101
Annex G - Summary of Management Improvement Activities at Governorate Level -----	109
Annex H - Status of Community Level Activities -----	113

TABLE OF TABLES

Table 1 – Phase II BEOC Facilities -----	03
Table 2 – Renovation Status for Phase I BEOC Facilities -----	06
Table 3 – A List of Trainings and Workshops by Date, Title, Site and Number of Trainees Conducted During the Period from October to December 2002 -----	17
Table 4 – Training Workshops on Introducing MMSS to District and Governorate Hospitals and Private Sector Providers -----	23
Table 5 – CNI – RHS Processes Conducted -----	27
Table 6 – A List of Communities Where Surveys Were implemented -----	28
Table 7 – Protocols and Modules Reproduced and Introduced to all Nursing Schools -----	38

ACRONYMS

ANC	Antenatal Care
Aswan THO	Aswan Teaching Hospital
AWP	Annual Work Plan
BBC	Basic Benefit Package
BEOC	Basic Essential Obstetrical Care
CAP	Community Action Plan
CBT	Competency Based Training
CCO HQ	Curative Care Organization Headquarters
CDA	Community Development Association
CEOC	Comprehensive Essential Obstetrical Care
CHC	Community Health Committee
CNI-DMT	Community Needs Identification and Decision Making Tool Process
CNI-RHS	Community Needs Identification Rapid Household Survey
CPAP	Continuous Positive Airway Pressure
CQI	Continuous Quality Improvement
CTO	Cognizant Technical Officer
DCOP	Deputy Chief of Party
DH	District Hospital
DNF	Death Notification Forms
DOC	Deputy Chief of Party
DSMC	District Safe Motherhood Committee
DT2	Development Training Two
ED	Emergency Department
EMRO	Eastern Mediterranean Regional Office
EMS	Emergency Medical Services
EOC	Essential Obstetrical Care
EPI/ POLIO	Expanded Program for Immunization/ Poliomyelitis
ER	Emergency Room
FGC	Female Genital Cutting
FGD	Focus Group Discussions
FP/ RH	Family Planning/ Reproductive Health
GALAE	General Authority For Literacy And Adult Education

GH	General Hospital
GIS	Geographic Information System
GOE	Government of Egypt
GSMC	Governorate Safe Motherhood Committee
GWU	George Washington University
HIO	Health Insurance Organization
HIS	Health Information System
HM/HC	Healthy Mother/Healthy Child
HSMC	Hospital Safe Motherhood Committee
HSRP	Health Sector Reform Project
HU	Health Unit
I. V.	Intra Venus
IC	Infection Control
IDSC	Information and Decision support Center (of the Cabinet)
IEC	Information, Education and Communication
IFA	Invitation for Application
IFB	Invitation for Bids
IIE/DT2	Institute of International Education/Development Training Two
IIT	Integrated Implementation Teams
IMCI	Integrated Management of Childhood Illnesses
IPC	Interpersonal Communication
ITI	International Trachoma Initiative
JSI	John Snow, Inc.
MCH	Maternal Child Health
MCH FP	Maternal and Child Health part of the Family Planning
MHIS	Management Health Information System
MMSS	Maternal Mortality Surveillance System
MOE	Ministry Of Education
MOHP	Ministry of Health and Population
MOISA	Ministry of Insurance and Social Affairs
MS	Microsoft
MVA	Manual Vacuum Aspiration
NAMRU3	Naval American Medical Research Unit 3
NC	Neonatal Care
NCPAP	Nasal Continuous Positive Airway Pressure

NCU	Neonatal Care Unit
NGO	Non Governmental Organization
NICHP	National Information Center for Health and Population
NICU	Neonatal Intensive Care Unit
NMMS	National Maternal Mortality Study
Ob/Gyn	Obstetric and Gynecology
OJT	On Job Training
OR	Operation Research
PHC	Primary Health Care
PHTAC	Population and Health Technical Advisory Committee
QA	Quality Assurance
QPMR	Quarterly Performance Monitoring Report
RFP	Request for Proposal
RFQ	Request for Quotation
RHS	Rapid Household Survey
SHIP	Students Health Insurance Program
SIF	Service Improvement Fund
SMC	Safe Motherhood Committee
SQL	Structure Query Language
TCA	Transcentury Associates
TOT	Training of Trainers
UHC	Urban Health Center
UNICEF	United Nations Children's Fund
US	United States
USAID	United States Agency for International Development
WHO	World Health Organization

INTRODUCTION

Pursuant to Section F.4.1 of the John Snow, Inc./U.S. Agency for International Development (JSI/USAID) Contract No. 263-C-00-98-00041-00, JSI is required to submit Performance Monitoring Reports summarizing the progress of major activities in process, indicating any problems encountered and proposing remedial actions as appropriate. These reports are to be submitted quarterly for calendar quarters ending the last day of March, June, September and December for each year of the Contract.

This current Quarterly Performance Monitoring Report (QPMR V) represents the fifth quarter of the Option Period contract and covers the period from October 1 through December 31, 2002.

This document is organized according to the twelve tasks of the contract along with a section on contract administration. Each task contains a narrative with the following sections:

- Accomplishments
- Constraints
- Proposed Actions to Overcome Constraints

The attached annexes document progress in the following aspects of the Project:

Annex A: Status of the Option Period Performance Milestones

Annex B: Maps of Target Governorates

Annex C: Contract Staff List

Annex D: Summary of Upgraded Status of Facilities in Target Districts

Annex E: Summary of Training of Personnel in Target Districts

Annex F: Summary of Management Improvement Activities at District Level

Annex G: Summary of Management Improvement Activities at Governorate Level

Annex H: Status of Community Level Activities

Governorate	District	BEOCs	No.
Assiut			
	Al Fath	El Fath Urban Health Center El Atawlla Integrated Hospital El Wasta Integrated Hospital	3
	El Kouseyah	El Kouseyah Maternity Beni Korra Woman Health Unit Fazara Integrated Hospital	3
	El Ghanayem	Urban Health Center, Maternity	1
Menya			
	Deer Mowas	Deer Mowas Maternity Beni-Haram Integrated H. U. Nazlat Badarman Integrated H.	3
	Fakreya	Asmant Integrated Hospital	1
	Beni-Mazar	Sandafa Integrated Hospital Beni-Ali Integrated Hospital Abu Garg Woman H. U. El Sheik Fadl Integrated Hospital	4
TOTAL			36

- A needs assessment took place in these BEOC facilities to start the process of the development of facility improvement plans. The assessments included staffing, utilization, main renovation, furniture, and equipment needs among others.

Activity No. 1.3 Assist in Facility Self Assessment and Improvement Plans and Monitor Implementation

- Preparation of the General and District hospitals profiles for the Option Period started and included:
 - Facility baseline assessment.
 - Facility plan for renovation schedules.
 - Commodity list for each hospital and status of delivery.
 - Training status.
 - Clinical performance indicators (retrospective and summary of concurrent indicators).
 - Management indicators.
 - Facility Self-Improvement Plans (EOC, NCU, OR/CSSD, etc).
- The profiles will be used to monitor, supervise and take actions for the assessed hospitals according to the findings.
- Follow-up visits on 22 hospitals took place to assess the implementation and updating of the Self-Improvement Plans and to identify and resolve problems. These 22 hospitals were as follows:
 - El Menya (Menya General Hospital, Deir Mowas District Hospital, Mallawi District Hospital, Fakreya District Hospital and Maghagha District Hospital),

- Assiut (Assiut General Hospital, New Eman General Hospital, El Eman Specialized Hospital, Badary District Hospital, Sahel Selem District Hospital, Dayrout District Hospital and Kouseyah District Hospital)
- Sohag (Sohag General Hospital, Maragha District Hospital, Saqolta District Hospital, Dar El Salam District Hospital, El Balyana District Hospital, Gerga District Hospital, Akhmeim District Hospital, Mounshaa District Hospital, Geheina District Hospital, and Tema District Hospital).
- A quarterly meeting was held to follow-up on the progress of implementing Self-Improvement Plans and it was attended by the Senior Management Team/JSI and the Undersecretaries/Director Generals/MOHP of El Menya, Assiut and Sohag governorates.
- Three meetings for Integrated Implementation Governorate Teams of Menya, Assiut and Sohag were conducted on December 16, 17 and 18, 2002 to discuss the deficiencies and problems identified by each team during its clinical supervision. The teams consisted of clinical supervisors and coordinators of the following activities: EOC, Neonatal, CSSD, OR, Anesthesia, ER, Blood Bank, Lab, Infection Control and Lead trainers in addition to implementation, MCH and management specialists from JSI Field Offices.
- During these meetings, the following issues were raised and problems related to them were discussed:
 - Staffing
 - Utilization of the department
 - Equipment
 - Supplies
 - Drugs
 - Infection Control
 - Records
 - Referral
 - Coordination between EOC, Neonatal, ER, Blood Bank, Lab.
 - Lead Trainers
 - Renovation
 - Commodities
- At the end of each meeting, Self Improvement Plans were updated.
- Implementation Teams, in cooperation with the Field Offices, are going to follow-up on solution for the raised problems with HSMC.

Activity No. 1.4 Initiate and Monitor the Implementation of the Renovation Plans

- Renovation activities were completed in El Wakf District Hospital and Qift District Hospital (Qena), Sennoures District Hospital and Tamia District Hospital (Fayoum), Nasser District Hospital (Beni Suef), El Menya General Hospital and Samalout District Hospital (Menya), Assiut General Hospital, El Eman Specialized Hospital and New Eman General Hospital (Assiut) and Sohag General Hospital (Sohag). Where as, in Somosta District Hospital (Beni Suef) renovation activities under the MOHP are still in process.
- In addition, renovation activities were completed at some of Phase II - Option Period Hospitals including: Fakreya District Hospital, Beni Mazar District

Hospital (Menya), Ghanayem District Hospital (Assiut), Gerga District Hospital, Tema District Hospital and Tahta District Hospital (Sohag).

- The blueprints of BEOC facilities/Phase I- Option Period were developed. The renovation was completed in some of these facilities and expected to be completed in the rest by the end of January 2003. The following table describes the status of renovation activities for Phase I - Option Period facilities.

Table 2. Renovation Status for Phase I BEOC Facilities

Governorate	District	Facility name	Status
Beni Suef			
	Nasser	1.Nasser Maternity Center	Only needs installation of A/C
		2.Ashmant I.H.U.	Renovated
	Somosta	1.Shantur I.H.U.	Renovated
		2.Dshtut I.H.U.	Under renovation
El Fayoum			
	Tamia	1.Tamia Maternity center	Only needs installation of A/C
		2.Sersena I.H.U.	Under renovation
	Sennoures	1.Sennoures Maternity Center	Renovated by MOHP/HMHC
		2.Fedemeen District Hospital	No need for renovation
El Menya			
	Markaz	1.Suzan Moubarak Health Center	Only needs installation of A/C
		2.Damsheer I.H.U.	Renovated
		3.Tahna Algabal I.H.	Renovated
		4.Tala I.H.	Under renovation
		5.Tahnasha I.H.	Under renovation
	Samalout	1.El Saleba R.H.U.	Renovated
		2.Qulosna I.H.	Under renovation
		3.Daqoof I.H.	Under renovation
		4.Mansheat El Sheraei I.H.	Under renovation
		5.El Baiaho I.H.	Under renovation
Assiut			
	Markaz	1.Nag Sabee I.H.	Renovated
		2.El Mateaa I.H.	Renovated
	Shark	1.Al-walidia Maternity Center	Only needs installation of A/C
	Gharb	1.Al-Arbaeen Urban Health Center	Under renovation
Sohag			
	Markaz	1.Gazereat Shandaweel I.H.	Renovated
		2.Balasfora I.H.	Under renovation

- In addition the draft blueprints of BEOC/ Phase II – Option Period facilities are being developed

Activity No. 1.5 Monitor the Delivery, Installation, Staff Training, Maintenance and Repairing of Equipment

- Commodities were delivered to Senores District Hospital (Fayoum) and Qift and El Wakf District Hospitals (Qena).
- EOC and neonatal commodities were delivered to Tamia District Hospital (Fayoum).
- As for Somosta District Hospital (Beni Suef) commodities are available and will be delivered upon renovation completion.
- Regarding the rest of Phase I Option Period hospitals, commodities will be delivered during the next quarter.
- In coordination with Task Eleven, procurement plans for 24 BEOC facilities of Phase I and 36 BEOC facilities of Phase II Option Period are completed and will be delivered early next quarter.
- The biomedical engineers visited the Ob/Gyn, Neonatal, CSSD and OR departments to review and screen available equipment status, fix found problems and provide technical assistance to the hospitals' maintenance staff.
- The visits were paid to the following hospitals:
 - Menya: Menya General Hospital, Samalout District Hospital, Beni Mazar District Hospital, Mallawi v and Edwa District Hospital.
 - Assiut: Assiut General hospital, New Eman General Hospital, El Eman Specialized Hospital, Ghanayem District Hospital and Kouseyah District Hospital.
 - Sohag: Sohag General Hospital, Gerga District Hospital, Tahta District Hospital, Tema District Hospital, Geheina District Hospital, Akhmeim District Hospital , Maragha District Hospital and Deir El Salam District Hospital.
 - Fayoum: Fayoum General Hospital, Tamia District Hospital, Sennoures District Hospital and Etsa District Hospital
 - Beni Suef: Beni Suef General Hospital, Beba District Hospital and El Fashn District Hospital.
 - Qena: Qena General Hospital, Armant District Hospital, Deshna District Hospital and Quos District Hospital.

Activity No. 1.6 Upgrade the Managerial Capacity of Hospital Management and Hospital Safe Motherhood Committees

- A new training curriculum for General and District HSMCs was developed. It includes planning, facility management and quality improvement principles. The course is planned to be covered in four days and is intended to communicate the concepts of CQI in order to continually improve health care.
- After the training workshops, HSMCs will be able to use facility improvement plans more effectively.

Activity No. 1.7 Coordinate the Phasing-out and Sustainability Plans from Target Governorates

- Preparation is under way to prepare a completion report and organize a Phase-out meeting for Beni Suef governorate by mid March 2003, and for Fayum and Qena by mid June, 2003.

Activity No. 1.8 Assist the MOHP / Urban Health Development to Pilot Test Adapted HM/HC Interventions in 1-2 Urban Slum Areas

Carry Out the Situation Analysis for Each of the Selected Slum Areas:

- Started to review Current National Policy with MOHP. A JSI team met Dr. Ahmed El-Henawy at the MOHP (November 12, 2002) to review the Current National Policy with respect to the two slum areas that had been already selected.
- The initial health facility profiles for each of the four facilities are in the process of being put together. Available service indicators for each facility were compiled and reviewed to determine past performance. District level health indicators have also been collected from HIS to help in identifying the current health status and needs of the communities.
- The main facilities are two BEOCs: Ezbat El-Matar UHC and Basateen Sharq UHC. Only limited activities will take place for CEOCs.
- A team from JSI and a representative from the Curative Care Department of the MOHP visited the two CEOC facilities: El-Khalifa General Hospital (December 22, 2002) and Imbaba General Hospital (December 23, 2002), to orient the facility staff as to the HM/HC interventions and to discuss the self-assessment process. Hospital staff was introduced to the various tools that would be used in the assessment process. The status of the existing referral system between the two BEOC and the two CEOC facilities in Cairo and Giza districts was also discussed during the site visits. The importance of improving and standardizing the referral process from BEOC facilities in order to reduce the normal delivery caseload of CEOC facilities and properly manage and refer high-risk cases in a timely manner were stressed.
- Both BEOC facilities, Ezbat El-Matar UHC and Basateen Sharq UHC, received four visits from JSI staff on November 24 and 25, 2002 and December 18 and 24, 2002. The purpose of the initial visits was to orient the facility staff as to the HM/HC intervention. Staff was also introduced to the BEOC Quality Improvement Checklists; the purpose of it was explained and they were asked to complete it as part of the Self-Assessment process. The Managerial, Clinical and Commodity components of the assessment were completed for each of the facilities. In addition, the blue print of the areas reserved for normal delivery services in Ezbat El-Matar was completed on December 8, 2002.

Assist in the Plan Development to Improve Perinatal Health Care Services and Their Utilization

- Several problem/deficiencies have been identified based on the initial facility visits. A number of observable clinical performance and managerial deficiencies have been isolated. Furthermore, gaps in the existing referral system have also been identified.
- Some of the initial areas for improvement based on the assessment were discussed with the staff of the facilities. Follow-up meetings will be scheduled to complete the Self-Assessment process and design the Self-Improvement Plans and interventions for each facility including, the specific activities involved, person responsible, time frame and budget.
- A meeting occurred on December 31, 2002 with the Curative Care representative of the MOHP and the JSI Slum Areas team to review the achieved activities and to plan for future approaches.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.2 TASK TWO: Pre/In-Service Training System Designed to Disseminate Standards to Public and Private Providers

Accomplishments

Activity No. 2.1 Disseminate Standards and Build MOHP Training Capacity

- Relevant training and other reference materials developed during the Base and Option Periods were field tested, refined and prepared for publication.
- Development of a complete set of Basic EOC training materials, that include the Basic EOC protocol, Modules and Flow Charts, were used in training activities of the primary health care physicians and pre-service trainees. The training was conducted on December 26, 2002 in Port Said and was attended by 110 participants.
- During December, both the EOC and Neonatologists Lead Trainers in Menya, Sohag and Assiut Governorates were trained on how to use the Clinical Performance Monitoring Indicators.
 - Menya from December 11-12, 2002 and was attended by 8 participants.
 - Assiut from December 30-31, 2002 and was attended by 19 participants.
 - Sohag from December 23-24, 2002 and was attended by 14 participants
- Continuous involvement of 15 Lead Trainers in Sohag, Assiut and Menya Governorates in all EOC workshops and OJT continued.
- Lead trainers are given tasks to carry out in their facilities during the periods between clinical supervisory visits. These tasks are monitored and checked by the clinical supervisors.
- Neonatal modules and checklists including all associated handouts and resources were prepared, revised and finalized.
- An Essential Obstetric Care Booklet containing case studies from the Egypt NMMS 2000 as well as a clinical analysis of each case was developed. Each case study was analyzed using a standard set of indicators. This booklet is intended for use during OJT/clinical supervisory visits to help health providers in the field develop their facility improvement plans.
- 20 Nurse Lead Trainers for Assiut, Menya, Beni Suef and Fayoum were trained in a TOT Course conducted in Assiut during the period from October 15 to 20, 2002.

Activity No. 2.2 Sustain, Organize and Implement EOC Training and Clinical Supervision

- Based on the results of maternal mortality surveillance system in the districts of Qena, Beni Suef and Fayoum governorates, technical assistance to Base Period facilities was provided, to help health providers develop improvement plans that address the contributing factors leading to maternal deaths.
- Two CEOC workshops were conducted in Sohag, the first was conducted during the period from October 8 to 17, 2002 and was attended by 23 participants and the second was conducted during the period from December 10 to 19, 2002 and was attended by 24 participants. Trainees were obstetricians

from the facilities, were trained on maternal deaths direct causes and avoidable factors, particularly substandard care.

- Continuous OJT/clinical supervisory visits were conducted to 13 districts in Fayoum, Beni Suef, Sohag, Assiut and Menya Governorates. Each of these districts is visited from six to nine days/month by clinical supervisors to ensure implementation of the EOC protocols. In addition, one day visit to all Phases II and III district hospitals of the Option Period to provide them with all CEOC training documents and to work specifically on the clinical problems that came up from the initial assessment.
- Four BEOC workshops were conducted in the following governorates. Participants were BEOC physicians from the PHC units and were trained on the Basic Essential Obstetric Care. Avoidable factors, substandard care and improvements in clinical practices were addressed during these workshops.
 - Sohag governorate and was conducted during the period from October 12 to 17, 2002 and was attended by 14 participants.
 - Menya governorate and was conducted during the period from November 2 to 7, 2002 and was attended by 18 participants.
 - Assiut governorate and was conducted during the period from October 19 to 24, 2002 and was attended by 13 participants.
 - Fayoum governorate and was conducted during the period from November 9 to 14, 2002 and was attended by 8 participants.

Activity No. 2.3 Sustain, Organize and Implement NC Training and Clinical Supervision

- Two neonatal courses were conducted in Sohag. Each was attended by 16 participants. The Basic Neonatal Care Training course was conducted during the period from October 27 to 30, 2002 whereas the Advanced Neonatal Care Training course was conducted during the period from December 9 to 14, 2002.
- One Nurse Training Courses was conducted in Fayoum and was attended by 19 nurses from Nasser NCU (Beni Suef) and Sennoures NCU (Fayoum). The course was conducted from December 21 to 26, 2002.
- One neonatal resuscitation training course was conducted in Sohag as a part of an EOC workshop with a total of 28 participants during the period from December 10 to 19, 2002. Another was conducted in Fayoum Governorate by Fayoum Lead Trainers to the health providers in Neonatal Centers & PHC unit during the period from November 24 to 25, 2002 and was attended by 23 physicians and 5 nurses.
- Technical assistance was provided to Option Period facilities through continuous visits to Phases I and II facilities in Menya, Assiut, Sohag, Beni Suef and Fayoum governorates. Each of these facilities was visited monthly by clinical supervisor for three days to ensure implementation of Neonatal Protocols.
- Moreover, technical Assistance continued to be provided to 19 Base Period facilities concentrating on CPAP therapy in units which provide this service, as well as, infection control and resuscitation trainings for Neonatal and Obstetric staff. The clinical supervisory practice concentrated on emphasizing the use and

- sustainability of the QA checklists for assessment of the training (Concurrent Checklist) and Clinical Performance (Retrospective Checklist). A total of 277 supervisory days were carried out from October to December 2002.
- The training program for I.V. fluid preparation and mixing was done in an additional three units. These units are:
 - Beni Mazar D.H. in Menya (7 physicians and 4 nurses) from October 22 to 24, 2002,
 - Nasser D.H., in Beni Suef (10 physicians and 9 nurses) from December 17 to 19, 2002,
 - Sennoures D.H. in Fayoum (8 physicians and 11 nurses) from December 29 to 31, 2002.
 - Two CPAP training workshops were conducted in Beni Suef G.H. during the period from October 28-29, 2002, attended by 11 physicians and 15 nurses and El Nasr G.H. in Port Said during the period from October 26-27, 2002 attended by 16 physicians and three nurses. The workshops were coordinated by Dr. Hany Ali, Director of The Neonatal Unit, George Washington University, Washington D.C. USA.
 - A follow up visit was conducted by Dr. Hany Ali to Fayoum G.H. during the period from October 24 to 25, 2002 to assess the implementation of CPAP following a previous workshop which was conducted six months ago in April 2002 and was attended by seven nurses and seven Health Providers.

Activity No. 2.4 Sustain, Organize and Implement Nursing Training and Clinical Supervision

- Two nursing EOC workshops were conducted in Assiut (from November 2 to 7, 2002) and Menya (from October to 30, 2002), where 47 nurses from the facilities were trained on nursing procedures in the obstetric department and delivery room.
- Technical assistance and continuous OJT/Clinical Supervisory visits to districts in Fayoum, Beni Suef, Qena, Sohag, Assiut and Menya governorates. Each of these districts was visited from six to nine days by the nurse supervisors to ensure implementation of the protocols.

Activity No. 2.5 Sustain, Organize and Implement Nurse Midwifery Training and Clinical Supervision

- A four month midwifery training course was completed in Assiut Governorate where 23 nurses were graduated, certified and licensed to be midwives. A similar course is going on in Sohag to certify and license 25 nurses.

Activity No. 2.6 Strengthen Other Clinical Support Services

2.6.1 Anesthesia Services

- Supervisory visits and OJT for safe obstetric anesthesia (preoperative visits, monitoring during operation time and at recovery time, general and regional anesthesia, and infection control) were conducted to nine facilities of the

- Option Period. Monthly supervisory visits were done in a rate of one to two visits per hospital.
 - Sohag: Sohag General Hospital, Gerga District Hospital and Tahta District Hospital,
 - Menya: Menya General Hospital, Samalout District Hospital and Fakreya District Hospital,
 - Assiut: Assiut General Hospital, EL Eman Specialized Hospital and New Eman General Hospital.
- Similar supervisory/ OJT visits were conducted for one-day /month to four facilities of the Base Period governorates:
 - Qena: Wakf District Hospital and Qift District Hospital,
 - Fayoum: Senores District Hospital and Tamia District Hospital.
- A total of 54 day-visits were conducted during the period from October to December 2002.
- An assessment of the present status of anesthesia equipment and procurement plan for the deficiencies was done.
- In Cooperation with EOC clinical supervisors, cases of maternal mortality were investigated, avoidable causes were discussed with staff and hospitals developed a self improvement plan for each facility.
- A Total of 53 BEOC physicians were trained for one day within the following BEOCs training workshops:
 - Menya, from November 2 to 7, 02 (13 participants)
 - Assiut, from October 19 to 24, 02 (15 participants)
 - Sohag, from October 12 to 17, 02 (17 participants)
 - Fayoum, from November 9 to 14, 02 (8 participants).

The objectives of the training were to explain the right way of fluid therapy, blood transfusion and how to decrease the maternal mortality rate due to blood loss.
- Anesthesia module was developed.
- A manual for anesthesia technician training program is under final editing.
- Clinical performance monitor indicators (concurrent assessment) for anesthesia were developed.

2.6.2 Emergency Medical Services (EMS)

- Service standards for EMS were completed.
- Emergency Service Manual for Physicians was drafted and is being revised.
- A binder on "Emergency Service in Upper Egypt Pilot Hospitals" was developed to summarize the process and progress of this task activity. The binder will be used for coordinated actions with relevant sectors in the Ministry of Health and Population (MOHP).
- First draft of Emergency Room Manual for Nurses (Arabic) was developed.
- An organizational structure for Emergency Departments (ED), compatible with the local context, was developed and set up in El Menya General Hospital, Samalout District Hospital (Menya Governorate), Sohag General Hospital, Tahta District Hospital (Sohag Governorate), Assiut General Hospital and El Eman Specialized Hospital (Assiut Governorate).

- OJT supervisory visits were conducted to six hospitals, four general hospitals (Menya, Sohag, Assiut and New Eman) and two districts hospitals (Samalout District Hospital and Tahta District Hospital). Visits were conducted once per month for each of the six facilities. A total of 18 visits were conducted for the six facilities during the period from October to December 2002, in addition to two visits to Qena General Hospital in October 2002. Three new district hospitals will be added, Tema in Sohag governorate, Maghagha in Menya Governorate and Kouseyah in Assiut Governorate.
- One EMS workshops were conducted in Menya for physicians during the period from December 29 to 30, 2002. 20 participants from new target facilities in addition to the General Hospital attended the workshop

2.6.3 Blood Bank Services

- Six one-day workshops were conducted on Blood Transfusion, its components, blood separation, cross matching and related complications. 113 participants were trained on the above as follows:
 - Menya: October 22-23, 2002 (33 participants)
 - Sohag: October 29-30, 2002 (41 Participants)
 - Qena: October 14-15, 2002 (39 participants)
- Blood Bank Manual was developed.
- Blood Transfusion services standards and Blood Bank monitoring checklists were developed.
- Infection Control Protocol to be used in the Blood Banks is under development.

2.6.4 Laboratory Services

- A distinction between clinical and laboratory services is emphasized to ensure high standard clinical services. The laboratory services in this context will focus on developing physician skills in requesting appropriate tests and interpreting test results, particularly in critical cases. The above mentioned activities helped in bridging the communication gap between clinicians (laboratory users) and Laboratory Service providers. Furthermore, the link between hospitals, the Governorate Health Department and the MOHP Central Laboratory Department will be better coordinated. Training of technicians on technical use of equipment will be the responsibility of the Central Laboratory Department at the MOHP as agreed.
- A Clinical Laboratory Manual was developed in June 2002.
- A list of the required investigations in General and District Hospitals was developed in conjunction with the Central Laboratory Department, MOHP.
- A list of the available investigations during and after regular working hours was developed by the Laboratory Department in each of the pilot hospitals.
- A policy on the use of Integrated Laboratory in each governorate to provide bacteriological service for those hospitals which have no such service is implemented.
- Laboratory Committees in pilot hospitals in the three governorates of the Option Period have been established. The objectives of these committees are as follows:

- Establish and monitor laboratory services at the hospital,
- Issue local guidelines,
- Solve local problems, and,
- Follow up on the use of the laboratory manual.
- A Laboratory Request Form has been developed and will be reviewed in collaboration with Central MOHP Laboratories, using the guidelines of the laboratory manual.
- A Laboratory Service Standards guide is under development and will target the laboratory committee members.

Activity No. 2.7 Infection Control Activities

- The quarterly integrated infection control OJT/Supervisory follow-up visits were conducted to the following hospitals:
 - Sohag General Hospital and Gerga District Hospital (Sohag),
 - Assiut General Hospital, El Eman Specialized Hospital and New Eman General Hospital (Assiut),
 - Menya General Hospital, Fakreya District Hospital and Samalout District Hospital (Menya),
 - Wakf District Hospital and Qift District Hospital (Qena).
- Behavior Change infection control plan was developed and divided into two phases. Phase I will focus on strengthening and mobilizing the Infection Control Committees and Teams. Phase II will focus on training and assisting Infection Control Committees and Teams in controlling sepsis by identifying the causes of infection in each hospital/facility, and designing appropriate interventions to address these issues and improve infection control. The different behaviors that would be addressed through the infection control interventions might include: hand-washing, wearing gloves, using of gowns and white coats to cover street clothing; sterilization of instruments and use of sterile instruments, appropriate use of antiseptics, etc.
- One-day training on Infection Control as part of EOC workshops was conducted in Sohag on December 7, 2002 and was attended by 24 participants.

Activity No. 2.8 Involve Private Sector Services Provided by Physicians and Pharmacists in HM/HC

- Information on private sector providers, with assistance of local syndicates, Private Sector and Pharmacy Inspection Departments, was upgraded to identify the number of private clinics, polyclinics, private hospitals and pharmacies in target governorates.
- One EOC training course was conducted for private physicians in Sohag during the period from December 18 to 19, 2002 and was attended by 24 participants.
- Three EOC training courses were conducted for private pharmacists:
 - Sohag on October 27, 2002 and was attended by 42 participants,
 - Assiut on October 21, 2002 and was attended by 29 participants,
 - Menya on October 31, 2002 and was attended by 27 participants.

Activity No. 2.9 Implement IMCI Program in New Governorates

- No activities were done this quarter.

Activity No. 2.10 Conduct Refresher Courses for Dayas

- No activities were done this quarter.

Activity No. 2.11 Teleconferencing and Off-Shore Training

- During October 2002, the eighth Teleconference session "Quality Assurance Monitoring System" was conducted with George Washington University.
- The Ninth Teleconference Session is under preparation and will deal with "Harmful Practices". It is expected to be conducted during January 2003.

Table 3. A list of Training and Workshops by date, title, site and number of trainees conducted during the period from October to December 2002

Date		Course Title	Site	# of Trainees
From	To			
October 08	October 17	CEOC Workshop	Sohag	23
October 12	October 17	BEOC Workshop	Sohag	14
October 12	October 17	BEOC Workshop	Menya	17
October 14	October 15	Blood Transfusion and its Components	Sohag	39
October 15	October 20	TOT for Nurses (Assiut, Menya, Beni Suef and Fayoum)	Assiut	20
October 19	October 24	BEOC Workshop	Assiut	13
October 19	October 24	BEOC Workshop	Sohag	15
October 19	October 24	EOC Workshop for Nurses	Menya	24
October 21		EOC Workshop fro Private Physicians	Assiut	29
October 22	October 24	I.V. Fluid Preparation and Mixing	Menya	07 Physicians 04 Nurses
October 22	October 23	Blood Transfusion and its Components	Menya	33
October 26	October 27	CPAP Workshop	Port Said	16 Physicians 03 Nurses
October 27	October 30	Basic Neonatal Care for physicians	Sohag	16
October 27		EOC Workshop fro Private Physicians	Sohag	42
October 28	October 29	CPAP Workshop	Beni Suef	11 Physicians 15 Nurses
October 29	October 30	Blood Transfusion and its Components	Assiut	41
October 31		EOC Workshop fro Private Physicians	Menya	27
November 02	November 07	BEOC Workshop	Menya	18
November 02	November 07	EOC Workshop for Nurses	Assiut	23
November 02	November 07	BEOC Workshop	Assiut	13
November 09	November 14	BEOC Workshop	Fayoum	08
November 24	November 25	Neonatal Resuscitation	Fayoum	23 Physicians 05 Nurses
December 07		Infection Control Workshop	Sohag	24
December 09	December 14	Advanced Neonatal Care for physicians	Sohag	16
December 10	December 19	CEOC Workshop	Sohag	24
December 10	December 19	Neonatal Resuscitation	Sohag	28

Date		Course Title	Site	# of Trainees
From	To			
December 11	December 12	EOC and NC Lead Trainers on the use Clinical Performance Monitoring Indicators	Menya	08
December 17	December 19	I.V. Fluid Preparation and Mixing	Beni Suef	10 Physicians 09 Nurses
December 18	December 19	EOC Workshop fro Private Physicians	Sohag	24
December 21	December 26	Neonatal Care for Nurses (Nasser NCU, Beni Suef and Sennoures NCU, Fayoum)	Fayoum	19
December 23	December 24	EOC and NC Lead Trainers on the use Clinical Performance Monitoring Indicators	Sohag	14
December 23		Midwifery Training Course	Assiut	22
December 26		Primary Health Care and Pre-Services	Port Said	110
December 29	December 31	I.V. Fluid Preparation and Mixing	Fayoum	8 Physicians 11 Nurses
December 29	December 30	EMS Workshop	Menya	20
December 30	December 31	EOC and NC Lead Trainers on the use Clinical Performance Monitoring Indicators	Assiut	19

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.3 TASK THREE: Public and Private Provider Partnerships with Communities to Develop and Manage District Plans

Accomplishments

Activity No. 3.1 Community Level Involvement

- During this Quarter, 10 community action plans were developed in ten communities in Assiut, Sohag and Menya, part of these plans will be addressed at the community level and the rest were submitted to District Health Committees and DSMCs to be incorporated in the district health plans.
- In the Base Period 25 Districts, 16 second rounds of community needs assessment (CNA) were conducted in Qena, Fayoum, and Beni Suef. The purpose was to assess the impact of HM/HC interventions on the community knowledge and practices and to compare results submitted to DSMCs, compared with the results of pre interventions CNA. The updated Community Action Plans – based on the results of the past CNA- will be incorporated into district health plans.

Activity No. 3.2 District Level Interventions

- A new training curriculum for HSMCs was developed and includes principles of planning, facility management and quality improvement; the course is planned to be covered in four days.
- A three-day workshop on management and planning was conducted in Sohag, during the period from December 22 to 24, 2002 and was attended by the 14 members of the DSMCs in two districts (Akhmeim and Geheina). Participants were asked to bring a situation analysis based on district data for MCH services for the practical training sessions of the workshops. The analysis was also used to develop district HM/HC plans based on the revised Guidelines for District Planning and Monitoring. A session on service provider sensitization was added to be an integral part of the component and agenda of the workshop. It was conducted by Task Seven staff. A training report was developed that included the results of pre/post tests, participation and course evaluation.
- A one-day workshop on October 20, 2002 was conducted in Sohag and was attended by 23 participants representing HSMC members (Sohag General Hospital, Gerga District Hospital and Tahta District Hospital). The purpose of these workshops was to introduce the commodity management system and better utilization of SIF.
- Meetings were continued for DSMC members of the 37 districts (25 Base Period, and 12 option period districts) and the drafts of district HM/HC plans were reviewed.
- Quarterly progress reports were developed by DSMCs representing achievements during the quarter of (July – September 2002) compared with their AWP, and HM/HC indicators.

Activity No. 3.3 Governorate Level Participation

- GSMCs meetings were continued, the districts quarterly progress reports were discussed during these meetings.
- A draft completion report was developed to phase out from Beni Suef governorate.
- A joint meeting was conducted in Sohag on November 4, 2002 and was attended by 68 participants, representing members of governorate/ districts SMC in addition to governorate/ districts health committees, to review achievements and districts quarterly reports

Activity No. 3.4 National Level Oversight

- The first meeting of the national SMC was held and attended by JSI COP and DCOP.
- Executive Director of HM/HC project assigned Dr. Salwa Farag as a new HM/HC counterpart for Task Three and she will participate in the coming training workshops.
- JSI consultant finalized a draft report on the utilization and management of SIF.

Activity No. 3.5 Quality Assurance

- A new curriculum on the continuous quality improvement (CQI) approach has been developed to replace the current curriculum on service standards and quality assurance. The course is part of the whole training course for HSMCs. The new course is directed to HSMCs' members and is intended to communicate the concepts of CQI in order to continually improve health care.
- A presentation about HM/HCP Continuous Quality Improvement activities was conducted to be included in the teleconference educational videotapes on November 30, 2002.
- A workshop on Quality Assurance Service Standards and Problem Solving was conducted in Sohag Governorate from December 28 to 30, 2002 and was attended by 17 participants representing the of Geheina and Akhmeim Districts SMCs. The training program aimed to enhancing capabilities in the area of quality care and improving compliance with service standards.
- In cooperation with HM/HC Project and Quality Assurance Unit, two workshops were conducted in Menya Governorate during the period from November 2 to 4, 2002 and from December 22 to 24, 2002, in an effort to support institutionalization of the MCH Quality Assurance system. Thirty participants attended the workshops representing BEOC physicians and district level supervisory teams' members.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.4 TASK FOUR: Monitoring System in place to Track Utilization and Impact and Provide Feedback

Accomplishments

Activity No. 4.1 Assist the MOHP to Set Up MHIS Centers at District Level in Coordination with Family Planning

- Currently nine district MHIS Centers in Giza are operating namely, North Giza, El Omrania, South Giza, El Haram, Giza Markaz, El Warrak, El Badrashein, El Ayat, and Boulaq El Dakrour.

Activity No. 4.2 Design and Upgrade User Friendly Software for MHIS

- A model of the new HIS Application was developed. The prototype of the new MHIS Application is completed. In addition, the Planning and Monitoring System is completed.
- Coordination with NICHP and HM/HC Project took place during this quarter. The two applications are presented to NICHP and HM/HC Project staff members. The meetings with NICHP concluded the selection of Menya and Alexandria to witness pilot implementation of the new MHIS Application and procedures.
- HM/HC and NICHP will establish an implementation team to run the pilot implementation in the mentioned governorates.
- Documentation and training materials for the new system is under development in coordination with NICHP and HM/HC Project.
- The new application is developed under Windows using MS Forms Two, Access 2000, Excel 2000, and SQL-Server. The application is designed to establish a data use environment at the governorate and district levels. Data quality control procedures and software tools were introduced as main components in the new application. Moreover, a user friendly report generator is introduced to allow MHIS technicians to develop tailored reports in addition to the predefined reports.
- The new system supports different implementation models, i.e. Single user and client server. Currently, heavy test is taking place for using Extranet environment. Districts and governorates may use different platforms and database engines. (i.e. Districts will use Access 2000 while Governorates may use SQL-Server). According to that the transfer of data is designed to be user friendly. Although the programs bear the burden of complexity, the data transfer tools are completely transparent to the user.
- The new MHIS Application is installed in MHIS Center Menya Governorate and presented to Undersecretary and technical department managers. Pilot Implementation is expected to start late January.
- Coordination with NICHP and IDSC to implement a GIS system in Menya is in process.
- In addition, Assessment for the hospital management system used by NICHP is in process to define problems and requirements for upgrade in order to be

implemented in pilot hospitals in Qena or Menya. The problem with this systems is that it needs computer resources more than what is available in the hospitals of Menya and Qena.

Activity No. 4.3 Develop and Implement a Quality Assurance Monitoring Checklist for the District MHIS Centers

- NICHP, in coordination with HM/HC Project, will start establishing a National Health Informatics Resources Database. It is suggested that the MHIS quality assurance monitoring checklist will serve as a basic tool for data collection for information technology resources.

Activity No. 4.4 Establish Monitoring Mechanisms at Facility and Community Levels

- The Data use workshops will be based on the new MHIS application and the Planning and Monitoring system.
- Curricula for two workshops were developed. One for health officers for data use, and the other for MHIS Center staff members to provide technical support for health officers in using the system.
- Currently, Tasks Four and Three are planning to conduct data use workshops in target districts in Sohag, Menya and Assiut, during April-June 2003.

Constraints

- Dokki district health officer in Giza Governorate has not assigned a room for the MHIS Center due to the unavailability of rooms in the office. The whole office is located in one room in the health office.

Proposed Actions to Overcome Constraints

- More investigations and efforts are in process to overcome this obstacle.

C.10.5 TASK FIVE: Research Activities

Accomplishments

Activity No. 5.1 Assist in the Development of Policy/Procedure Guidelines for the Maternal Mortality Surveillance System (MMSS)

- Completed.

Activity No. 5.2 Training on the Maternal Mortality Surveillance System

5.2.1 Introduction of MMSS to district, governorate hospitals and private sector providers

- The introduction of MMSS to Ob/Gyn and Anesthiologists at district/ general governorate Hospitals; and to the private sector Ob/Gyn providers was carried out as follow:

Table 4. Training Workshops on Introducing MMSS to District and Governorate Hospitals and Private Sector Providers

Governorate	Date	Number of trainees
1. Fayoum	21-22 October	27
	23-24 October	26
2. Aswan	3-4 November	23
3. Beni Suef	18-19 November	39
	20-21 November	36
Total		151

Activity No. 5.3 Implement the Maternal Mortality Surveillance System in Nine Upper Egypt Governorates

5.3.2 Supervision and Field Work Check

A MMSS Quality Monitoring Checklist was developed and tested to assess the performance of health offices, health district and health directorate in relation to the quality of filling the form regarding completeness, accuracy on one hand and timeliness of dispatching the forms from level to the others on the other hand. Three forms were used in the supervision of 53 health offices of six health districts at Sohag governorate during the period from November 23 to 28, 2003. The following are the main results of this performance exercise:

- Only 16 out of 52 health offices (31%) exceeded 50% of the performance score.
- The unavailability of Death Notification Forms in 12 out of 52 health offices (23%) has led to the use of different and old forms or use of "Balaagh El Wafaah Forms" (Ministry of Interior Death Forms).
- The routine delay in submitting Death Notification Forms (DNF) every month to the MCH District Assistant Manager instead of correctly sending it every week, led to a delay of the process of investigating the maternal death cases by the District Assistant Manager which in return led to delay in having these

maternal deaths submitted to SMC at Health Department on the governorate level on time to take corrective actions.

- Lack of coordination between different staff members at health district (District Assistant Manager, HIS Manager and Preventive Inspector) or at Health Department/ governorate level (MCH Director, Preventive Sector Director and HIS Director), led to errors in the number of female and maternal deaths.

Activity No. 5.4 Identify and Conduct Operation Research Studies

- Preparatory actions to conduct five operations researches started as follows:

OR1 A: Premixed intravenous fluid formulae for neonates for the prevention of nosocomial infection.

- Implementation of this study is currently under way at the Neonatal Unit at Kasr El Aini Hospital, Cairo University.

OR1 B: Cost-effectiveness study of premixed IV fluid formulae for neonates versus regular formulae for prevention of systemic nosocomial infections.

- Due to the importance of the topic and its relation to OR1, it was decided to include this as part of OR1 despite the difference in objectives and methodology. Design of the data collection tools is in progress.

OR 2: Cost analysis and efficiency indicators of three neonatal intensive care units in Upper Egypt

- Implementation did not start yet.

OR 3: Defining indicators and developing tools for monitoring client satisfaction for maternal and child health services from community women's perspective

- An extensive search was done to ensure that this topic was not studied before. The study will consist of two rounds of data collection, the first round, aims at identifying client satisfaction indicators from the clients' perspective, where these indicators will be used to develop tools for the routine collection of client satisfaction data. The second component of the study will test these tools to select the most suitable ones for routine data collection. Preparations for the first round of data collection are currently taking place.

OR 4: Taxonomy of maternal and child health terms

- A comprehensive list of terms used in maternal and child health were compiled by the relevant clinical staff. Draft guides for the focus group discussions and in-depth interviews were developed. All preparations for conducting the field work were completed.

OR 5: Reasons for the poor availability of blood for emergency obstetric care in Upper Egypt

- Data collection tools were completed and revised. Training materials for data collectors are almost complete.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.7 TASK SEVEN: Better Social Community Services

Accomplishments

Activity No. 7.1 Community Needs Identification and Decision-Making

- Ten five-day workshops were held in Assiut, Sohag and Menya to train Community Outreach Workers on conducting Community Needs Identification Rapid Household Survey (CNI-RHS) in 10 communities. Fifteen Outreach Workers from each community (a total of 150 Community Workers) were selected and trained on the CNI-RHS process and they conducted the process in each of the below mentioned communities.

Table 5. CNI-RHS processes conducted

Governorate	District	Community
Assiut	El-Fath	El Wasta
Sohag	Tahta	Tahta
	Akhmeim	Neida & El-Kolla
	El-Maragha	El-Gherezat & Shandaweel
Menya	Menya	Suzan Mubarak
	Deer Mowas	Nazlet Badraman & Beni Haram
	Fakreya	Fakreya

- The main objectives of the workshops were to identify through the Rapid Household Survey:
 - key behaviors related to MCH issues – whether they are followed by women or not,
 - whether danger signs during pregnancy, delivery, postpartum and care for the newborn are known by women or not,
 - main obstacles that could hinder accessing the MCH services in the communities.
- To conduct the RHS, a random sample of 50 mothers with a baby less than one year old was selected from Birth Register of the health units to be interviewed during the RHS.
- Over a five-day period, the process was conducted in each community and the results were manually tabulated and finalized for action.
- The workshops were preceded by the development of community profiles for each of the ten communities. These profiles include demographic data collected from the local administration units and health units of the communities. The main purpose of these profiles is to portray communities with their unique characteristics, services and resources.
- Following the RHS, ten CHCs workshops were conducted to:
 - 1) share the results of the RHS,
 - 2) identify the community needs/problems related to MCH issues,
 - 3) Prioritize and analyze these problems,

- 4) suggest alternatives for solutions to address these problems and meet the community needs and finally,
 - 5) develop Community Actions Plans (CAPs) to guide the community actions in this respect.
- The CAPs contain the problems/needs, their priority order, their causes, the suggested solutions, the responsible persons and the time frame for each intervention. Some of the CAPs problems/needs are addressed at the community level. Others that are beyond the capability of the community are submitted to the district to be incorporated in the district health plans.
 - The action plan workshops were attended by 300 participants who represent CHCs members, Community Outreach Workers who conducted the CNI-RHS process and Heads of the Village Executive Councils in these communities.
 - Sixteen three-day workshops were conducted for the second round of CNA in Qena, Fayoum and Beni Suef to assess impact of the HM/HC interventions on the community health knowledge and behaviors. The workshops followed the same pattern of the first Community Needs Assessment (CNA). During these workshops, a total of 240 Community Outreach Workers (15 from each community) were trained and accordingly implemented the surveys in the following communities.

Table 6. A list of communities where surveys were implemented

Governorate	District	Community
Qena	Esna	Kimam El-Mattaana
	Armant	Armant El-Heit & El-Demoqrat
	Qous	El-Aiaisha & Nagaa El-Sebai
Fayoum	Fayoum	Zawiat El-Karadsa
	Etsa	El-Gharak
Beni Suef	Beni Suef	Belivia, Barout & El-Ghamrawy
	El-Fashn	El-Fant & Delhaness
	Ehnasia	Shatter Zada
	Beba	Seds & Tansa
	El Wasta	Abu Sier

- Results of the surveys were shared with the Community Health Committees (CHC) so as to adapt the community action plans accordingly. This was achieved in 16 CHC workshops and was attended by 480 participants who represent CHCs members, the Outreach Workers who conducted the RHS and Heads of the Village Executive Councils in the targeted communities.

Activity No. 7.2 Community Health Education

7.2.1 Health Providers Sensitization

- One workshop was conducted for 14 health providers and decision-makers from the two districts of Akhmeim and Geheina in Sohag during the period from December 23 to 24, 2002. Participants were briefed on and alerted to the community perceptions and believes related to HM/HC issues. The main

objective was to take these perceptions and believes into consideration when treating their patients.

7.2.2. Integrating HM/HC Messages in the Literacy Curricula of General Authority for Literacy and Adult Education (GALAE)

- As a result of signing the Memorandum of Cooperation with GALAE for the replication of the literacy pilot - integrating health messages in the literacy curricula of GALAE - in Cairo and Giza and work with the GALAE central level trainers, four workshops were conducted as follows.
 - The first workshop was conducted for 13 national master trainers from GALAE to act as trainers for the literacy facilitators in Cairo and Giza to help replicate the experiment of integrating health messages in the literacy curricula of GALAE. The workshop was conducted from October 13 to 15, 2002 at GALAE Headquarter.
 - The second workshop was conducted for the same 13 the master trainers of GALAE to assign responsibilities and tasks in implementing the literacy activities in Cairo and Giza on December 14, 2002.
 - The third workshop was conducted for 27 literacy facilitators and supervisors from the GALAE Cairo Branch to start the activity in 20 classes in some of the slum areas in Cairo from December 15 to 18, 2002.
 - The fourth workshop was conducted for 23 literacy facilitators and supervisors from the GALAE Giza Branch to start the activity in 15 literacy classes in some of the slum areas in Giza from December 22 to 24, 2002.

Activity No. 7.3 Training of Health Educators

- An outline of the Health Education Training Curriculum has been finalized.

Activity No. 7.4 Female Genital Cutting

- Three FGC follow up workshops were conducted in Aswan, Qena, and Beni Suf governorates. The Aswan follow up workshop was conducted during the period from October 14 to 15, 2002 with 25 participants from Health Social Workers, Health Educators and Community Outreach Workers of NGO's. The follow up Workshop held in Qena was conducted from October 23 to 24, 2002 with 24 participants. In Beni Suf, the FGC follow up workshop was conducted from October 16 to 17, 2002 with 25 participants from Health Social Workers, Health Educators and Community Outreach Workers of NGO's. The Directors of Health Education and Social Workers Departments led some of the sessions.
- TOT follow up workshop was conducted in Menya during the period from September 2 to 4, 2002 and was attended by 30 participants namely: Directors of Health Education and Social Workers departments as well as NGOs Community Outreach Workers from target Governorates.
- TOT and FGC curricula were revised after being pretested in the workshops and will be printed next quarter.

Activity No.7.5 Engaging the Private Sector

- Work is pending for Minister of Health and Population approval on the Public/Private Strategy that was submitted on September 2002.

Activity No.7.6 Continuing Community Activities

- Woman Health Card was finalized; content revised and technically edited and extra illustrations were added and pretested. The Woman Health Card has been presented to HM/HC Executive Director for approval.
- Counseling Cards were pretested in Fayoum governorate, and were revised and refined based on the results to be ready for printing next quarter.
- A process of developing CDs and a project brochure to promote the project and to be used as references for other MHC projects has already started. CDs content has been developed by different task managers and will be revised next quarter for finalization.
- A tool was developed to collect success stories and lessons learned from all the different tasks and components. Success stories are being reviewed by task managers to be finalized and integrated as appropriate.
- The eighth teleconference sessions were shot and revision of the video tapes is currently in process.
- Shooting an extra teleconference on harmful practices was approved and is scheduled on January 27, 2003

Activity No. 7.7 Strengthen IPC Training for Physicians and Nurses

- Translation of the IPC one day module from English to Arabic was finalized and is in the process of being revised before printing.
- An IPC training plan was developed covering the period from January 6, 2003 to August 15, 2003.

Activity No.7.8 Taxonomy of MCH Terms

- In co-operation with task 5 (Operation Research), an RFP was sent out to four different research firms. Three proposals were received, and clarifying questions were sent to potential research firms. One firm will be selected to be contracted to start work on identifying and collecting the colloquial terms, definitions, and triggers to actions. The OR will be conducted in two phases. Phase I will be implemented in the four Option Period governorates (urban and rural districts). After which a preliminary review of the results will be conducted and if no differences were observed between urban and rural districts, then only one district will be selected from each of the remaining governorates. If there were no noticeable differences between the Phase I governorates, then an expert opinion will be sought to determine whether to continue conducting FGDs in the remaining governorates or to stop the research and use the Phase I results for all Upper Egypt governorates.

Activity No.7.9 Behavior Change

- During this quarter, a literature review of the tools to be used in developing the behavior change module has been collected. The behavior change module will be developed next quarter.
- Work is on-going to implement the Behavior Change Plan.

Activity No. 7.10 Gold Star

- A final design for the MCH Gold Star Sign for PHC health facility and hospitals was produced and made available.

Activity No.7.11 Health Education Activities to Support SHIP in Schools

- Two Health Education Guides were developed, reviewed and edited to streamline grammar, spelling and formatting:
 - The first guide is the Health Education Guide Part 2 which addresses smoking. It is a complementary part to the original one that addresses anemia and will be used by HIO Health Educators working in the Base Period governorates.
 - The second guide is the Health Education Guide for the Science Teachers who assume the responsibility of health education in the Option Period governorates. It addresses both anemia and smoking.

Activity No.7.12 Iron Supplementation Program

- Two two-day Training workshops for MOE and Al Azhar Vice Principals took place during the period from October 26 to 29, 2002. 52 Vice Principals participated in these training courses. Each vice principal conducted two hours training workshop for all class teachers in his/her school. These training courses placed more emphasis on the procedures of iron supplementation in schools.
- Schools in the current six governorates were provided with the iron tablets and registers needed for implementing the program during the remaining weeks of the school year 2002-2003. Due to financial constrains, the HIO delayed in the process of cup purchasing. Hard plastic cups were procured lastly by HIO at the central level. The quantity procured is only adequate to cover all students with one cup per student for the whole year. In the meantime, HIO Regional Departments are in the process of procuring disposable cups to supplement the shortage of cups provided by HIO at the central level. Implementation of the program is pending until the availability and delivery of cups to the target schools.

Activity No. 7.13 Pilot Testing of IEC for Smoking Prevention

- The smoking brochure was revised and a final copy was developed. The brochure will be used during the health education sessions by both health educators in the Base Period governorates and science teachers in the Option Period governorates.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.10 TASK TEN: Small Grants Program

Accomplishments

Activity No. 10.1 Management and Monitoring of the Base Period Awarded 102 Grants

- Partial payments were advanced to eighteen (18) NGOs totaling LE 203,145 for ongoing grant activities.
- Technical and Financial Close out of base period completed grants as follows:
 - Financial Close out of all eight Beni Suef awarded NGOs.
 - Financial Close out of 13 out of the 15 Fayoum awarded NGOs.
 - Technical and Financial Close out of 12 out of the 13 Qena South awarded NGOs.

Activity No. 10.2 Modify the Existing IFA and the Structure of the Review Panel

- Completed technical training for the 18 newly awarded NGOs outreach workers. The total number of community outreach workers trained is 302 as follows: Qena (111), Beni Suef (103) and Fayoum (88). The training included health messages, communication skills, management and reporting skills.
- The staff members of the six NGOs of Beni Suef were financially trained on management and reporting of the grant funds.

Activity No. 10.3 Provide Grants to Capable Local NGOs through Standardized Mechanism

- Orientation meetings for the three MOISA director generals and staff, on the HM/HC Project in general and the small grant program in particular, were conducted in Sohag on November 26, 2002, in Assiut on December 14, 2002 and in Menya on December 15, 2002.
- IFA advertising and distribution took place in 22 target districts (Sohag 11, Assiut 6 and Menya 5). The distribution of the IFA was done through the MOISA district offices, JSI Field Offices and the NGO Regional Federations.
- Orientation workshop for 84 NGO that expressed interest in Sohag through Letters of Intent was conducted from December 22 to December 25, 2002.

Activity No. 10.4 Training Awarded NGOs (Technically and Financially)

- No activities were done during this quarter.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.11 TASK ELEVEN: Commodity Procurement Program

Accomplishments

Activity No. 11.1 Commodities

- JSI/TCA completed the procurement process and issued Purchase Orders for a total of US\$ 4,081,480. The total amount committed to date is 45% of the total procurement budget.
- TCA has procured the following items this quarter per the Life of Contract Procurement Plan:
 - Offshore medical equipment.
 - Local medical furniture, equipment, and supplies.
 - Local office furniture (desks, side chairs, and file cabinets).
 - Local computing equipment for the MOHP.
- JSI received USAID approval for the proposed awards for Medical IFB #12 (nine contracts).
- JSI received USAID approval for a waiver to purchase of automatic steam sterilizers (autoclaves).
- A US RFQ was issued for CPAP supplies and the bids are being analyzed.
- Four 40 foot containers were received in Egypt from the US Freight Forwarder including office furniture and medical equipment. Additional containers are being loaded in the US for shipment in early January.
- The vehicles have been received by the Freight Forwarder and are being shipped to Egypt.
- JSI and TCA have accepted delivery and installed the following items for Base Period and Option Period recipient locations this quarter:
 - Medical equipment, furniture, and supplies in completed Option Period Phase One facilities.
 - Air conditioners for Option Period Phase One facilities (General/District Hospitals and BEOCs) and for District Health Offices.
 - Computing equipment to Sohag Governorate Health Office.
 - Office furniture, fax machines, and computing equipment (as required) to select MHIS Centers in Giza.
 - Computing equipment to the Urban Health Department.
 - Office furniture and computing equipment to Assiut and Menya HIO offices.
- Training on medical equipment was held for the JSI Clinical Supervisors.
- Meetings were held with the Preemicare representative from California on the incubators. The JSI Biomedical Engineers also accompanied her on visits to facilities in the field to inspect the machines.
- Inventory in the warehouse was maintained and a physical inventory was completed.
- The computerized Commodity Procurement Database was maintained and produced required reports. The system was revised to include additional functions.

- Distribution reports were provided to the GOE Customs Representative as required.
- A presentation on procurement activities was provided to the Integrated Implementation Teams (IIT).

Activity No.11.2 Renovations

- All the bidding, contracting and financial procedures related to renovation process were implemented according to the renovation plan.

Activity No. 11.3 Publications

- The IMCI Package (IMCI Manual and Booklet) was finalized, printed and delivered to the IMCI project.
- The Nurses' Neonatal Manual was finalized, printed and is being prepared for distribution.
- The design of the Women's Health Card was finalized and the content was technically edited. The designer has submitted five possible proofs, two of which were sent to the HM/HC Project for approval.
- The cover, spine title panels, and CD covers were designed and delivered for the Neonatal Modules. Final assembly of the modules is being completed.
- As a result of an RFQ, In and Out Shipping Company was selected to provide shipment services to deliver publications and IEC materials to JSI target governorates. A contract was developed and signed by both parties and the company started providing shipment services beginning November 1, 2002.
- Quotes were solicited for the printing of health education materials for the SHIP program and the bid analysis has been completed. The Purchase Order is pending final approval.
- A distribution plan is being refined for all publication and IEC materials currently in the JSI Publications Warehouse. This plan will be submitted to the HM/HC Project for final approval.
- Ongoing activities include:
 - Design of the commodities forms.

Constraints

- None

Proposed Actions to Overcome Constraints

- None

C.10.12 TASK TWELVE: Coordination Activities

Accomplishments

Central Safe Motherhood Committee

- The first meeting of the committee was held on November 4, 2002 and chaired by H.E. the Minister of Health and Population and membership of all the Under-Secretaries and Director Generals who are sharing the responsibility of reducing maternal and neonates mortality in Egypt as well as a number of resources academic staff from the faculties of Medicine and the Secretary General of the Physician Syndicate. The reporter of the committee, i.e. Dr. Esmat Mansour, HM/HC Executive Director, prepared a draft plan of action to follow on the results and recommendations of the NMMS: Egypt 2000. The plan, which was endorsed by the High committee, sets up a goal to reduce maternal mortality ratios from 84 per 100,000 live births in the year 2000 to 50 per 100,000 live births by the year 2007 (42%). The plan, also, defines the main issues and problems, charts, courses of action and responsible Sectors/ Departments.
- H.E. the Minister of Health and Population called on the Sectors/ Departments to cooperate and share effectively in shouldering the responsibility of implementing this plan of action as assigned. He stressed that slum and deprived remote areas need innovative approach and method to reach them with service and emphasized the need to bridge the gap between these areas and the rest of the country. Another area which the Minister placed more emphasis, is the MCH/FP/RP for their impact on maternal health and mortality and development in general.

MOHP-Intra-Ministerial Coordination

Following the first meeting of the High Committee for Safe Motherhood chaired by H.E. Minister of Health and Population and to respond to the call of H.E. for more integration and cooperation between the concerned departments/ sectors of MOHP, series of follow-up meetings were held for this purpose as follows:

A - IMCI

- JSI participated in the process of the analytical review of the implementation of IMCI in Egypt. The analytical review workshop, which was held during the period from October 23 to 24, 2002, was attended by representatives of MCH and IMCI National Program (MOHP), USAID, WHO EMRO Office and three consultants from WHO-HQ – Geneva.

B - Blood Affairs General Directorate

- A meeting was held on November 10, 2002 with the Director General of Blood Affairs, MOHP, HM/HC Research Unit and JSI. This was the first meeting to discuss the preliminary steps to implement operation research study aimed to identifying the reasons for poor availability of blood for emergency obstetric care. It is to be recalled that the MMSS revealed that hemorrhage was the

leading direct cause of maternal mortality (43%) and lack of blood contributes to 16% of all maternal deaths. The protocol for the study, tools, and methods of collecting and analyzing data and organization of the study were discussed. The point of start of conducting the operations research study will be Sohag to be followed in Assiut, Menya and Giza.

- A second meeting was held on November 17, 2002 to get feedback from the study team on the technical aspects of the study and present the general framework of implementation.

C - Private Sector General Directorate

- A meeting was held with the Director General of Private Sector Directorate on November 4, 2002 to discuss mechanisms of cooperation and coordination between HM/HC and Private Sector General Directorate to improve the quality of services provided by the private providers and their compliance with the Service Standards.
- Private Sector General Directorate started-up a process to establish a data-base for private practices by clinics and providers. It is expected that this data-base will be a first step to screen, categorize and check compliance of the private sector with laws and regulations. Dr. Assem Abdel Nasser, Director General of Private Sector General Directorate, proposed three areas of cooperation:
 - A development of supervisory System to check on the compliance with rules and laws in the area of obstetric/ gynecology.
 - Orientation and training of private providers on the protocols and standards of service.
 - Development of accreditation/ certification system.

D - Human Resources Development Central Directorate

- As follow up of the first meeting of the High Ministerial Safe Motherhood Committee, Dr. Azza El Hussein, Under Secretary for Human Resources Development- MOHP, requested hard copies and CDs of the Nursing Schools Protocols and Modules which were developed, tested and introduced in the Nursing Schools of Upper Egypt by the HM/HC with technical support of JSI/ USAID. Dr. El Hussein committed herself to reproduce and introduce the following five protocols and modules to all nursing schools run by MOHP (estimated over 200):

Table 7. Protocols and Modules reproduced and introduced to all Nursing Schools

1	Maternity Module	تمريض الولادة مرشد المدرسة
2	Maternity Protocol	تمريض الولادة
3	Pediatrics Module	تمريض الأطفال مرشد المدرسة
4	Pediatrics Protocol	تمريض الأطفال
5	First Year Community Health Module	صحة المجتمع السنة الأولى - مرشد المدرسة
6	First Year Community Health Protocol	صحة المجتمع السنة الأولى
7	Second Year Community Health Module	صحة المجتمع السنة الثانية - مرشد المدرسة
8	Second Year Community Health Protocol	صحة المجتمع السنة الثانية
9	Third Year Community Health Module	صحة المجتمع السنة الثالثة - مرشد المدرسة
10	Third Year Community Health Protocol	صحة المجتمع السنة الثالثة

E – Primary Health Care General Directorate

- Three meetings were held with the Director General of Primary Health Care MOHP on November 4, 11 and 18, 2002 to discuss two areas of cooperation and coordination:
 - Training on Essential Obstetric Care in Primary Health Care facilities.
 - Training Community Outreach Workers.
- As regards the first area, JSI provided the Director General with a hard copy and a CD of the Basic Essential Care Protocols and Modules which JSI implemented in training the physicians of the primary health care in target districts of Upper Egypt. The Director General promised to review them for final and last draft. Once the final draft is endorsed by the Director General and Executive Director – HM/HC, who assigned JSI to train the trainers who will be responsible to expand this training in all the PHC facilities of Upper Egypt and go to scale at the national level.
- Related to the first area, i.e. training of PHC staff, JSI participated in the one day workshops organized by the Primary Health Care Directorate on the “Status of Training Activities Targeted to PHC”. The workshop was held on November 20, 2002, attended by Governorate Directors of PHC and Training and was chaired by Dr. Esmat Mansour, Executive Director HM/HC and Under-Secretary for Primary Health care and Dr. Azza El Hussein, Under-Secretary for Human Resources Development.
- The following are the major topics that were discussed in this workshop:
 - Situation analysis of training targeted to PHC team of clinical and non clinical staff.
 - Development of Basic Training Package for PHC health team based on the needs of different sectors and departments of MOHP and the Basic Benefit Package (BBC).
 - Bases and mechanisms for the decentralization of the training process.
 - Development of a data-base for PHC training.
- By the end of the meeting, it was agreed to pilot, implement an integrated PHC package of training in the following five governorates: Dakahlia, Damietta, Ismailia, Beni Suef and Assiut. On the other hand, intensive efforts will be exerted to build local capacity by TOT programs to create a local training cadre capable of conducting and implementing the training package.
- Regarding the second point, JSI shared experience gained so far and materials developed to train Community Outreach Workers and Community Mobilization with the Director General and her staff. An agreement was reached to use the materials developed with technical assistance from JSI; in the meantime, JSI would get the benefit of using the service of the 400 Community Outreach Workers appointed by the Family Medicine in the HM/HC target governorates.

F – Urban Health General Directorate

- Slum Areas:
 - Slum Areas draft Action Plan has been reviewed with Dr. Henawy.
 - The issue of turning the Urban Health Center in Maternity was raised discussed and an agreement was reached with Dr. Esmat Mansour on it.

- GOE Funding for Interventions in Slum Areas:
 - Dr. Henawy indicated that MOHP has some funding for the urban areas to cover MOHP renovation costs and the costs of IMCI.
- Pilot Model for Urban HM/HC Interventions:
 - The importance of determining what resources are already available at the Ministry of Health and Population and adopting existing programs e.g. Luxor referral system, were discussed.
 - The goal is to produce a pilot model maximizing existing resources in the system so that the model is sustainable and replicable.
- Pre-service Training:
 - Two pre-service trainings will be held:
 - Mid-December a small group of 100-150 graduates who have already received some training will participate in the training.
 - April/May – the major training will be held and will include 3000 participants (the graduating class is 6000, but only expect half to participate).
 - The initial part of the training will occur in Port Said. Each governorate has multiple training centers and different hospitals for the practical clinical training.
 - Dr. Henawy agreed to reschedule the program for the Port Said portion to allocate one day for MCH instead of two hours. In addition, two weeks in the field training will be allocated for MCH.
 - JSI needs to develop a plan for what it could provide to the trainings, mentioned above, particularly, what information package (protocols, materials, etc.) JSI wants to give participants, and what kind of practical and clinical training they will receive.
 - The possibility of JSI developing posters/job aids for the training was also discussed.
 - JSI coordinated a meeting to coordinate the inputs of the speakers who will present the one day MCH component of the pre-service training and participated in the training which took place in Port Said on December 26, 2002.

G – Health Sector Reform Project

- JSI was approached by HSR to help with the process of producing their documents. JSI provided a list of printshops and a template for a Request of Proposal (RFP).

H – NICHHP

- A meeting was held on December 12, 2002 with: Dr. Sanaa the NICHHP Manager, Eng. Amir, Mr. Mohamed Abbas (NICHHP) and Eng. Khaled Abdel Fattah (JSI). Mr. Hossam Maher from NAMRU 3 attended part of the meeting. The following are the topics that were discussed and conclusions reached:

Hospital Management Systems:

- Regarding the system Implemented by Maximus in the Curative Care Organization (Nasser Institute and Heliopolis Hospital), A committee was

established by Dr. Tayseer El Sawy the NICHHP Ex-Manager to assess the System in both hospitals. The committee concluded that the operation of the system is very difficult to maintain in the two sites due to the following reasons:

- The project did not create a cadre in the hospital which is responsible for the administration of the system and trouble shooting of the system.
- There is no installable package of software in all hospitals and the Curative Care Organization Head Quarters (CCO HQ).
- As regards the system which is currently used by the NICHHP and installed in Shark El Madina Hospital in Alexandria and El Sahel Hospital in Cairo, NICHHP advised that the system needs to be upgraded. A complete description for the system and the process of the implementation will be developed soon.

Pilot Implementation of the new application HIS in Menya:

- Dr. Sanaa, Eng. Amir and Mr. Mohamed Abbas will visit JSI in the near future to attend a presentation of the new HIS application under Windows.
- NAMRU3 started to distribute computers all over 11 governorates. They do not work in Menya, However they will provide Menya Governorate MHIS center with two computers.

Implementation of GIS in Menya:

- NICHHP in coordination with Health Reform Project and with the technical assistance of CAPMAS, made automated maps loaded with health data for four governorates in Lower Egypt. Dr. Sanaa suggested that we make the GIS for Menya using the same standards used in the previous governorates. She advised JSI to calculate the cost and negotiate issues related to work with CAPMAS before proceeding.

MOHP/ HIO/ MOE (SHIP)

- On November 17, an orientation meeting was held for all the staff of MOHP- MCH General Directorate. The purpose of the meeting was to orient all MCH staff on the SHIP/ AAPP so that they can conduct program monitoring while they are doing their routine field activities. The meeting was held in HM/HC Headquarters. Fourteen staff members participated in the meeting, most of them were not involved with the SHIP activities in the past.
- On December 10, a meeting was held with MOE Central Department for Population and Environmental Education. The meeting included SHIP/ MOHP and HIO Coordinators. The meeting discussed ways and means to set up practical steps to be taken to launch the health education activities by science teachers in the governorates of Sohag, Assiut and Menya. MOE staff was very positive and willing to cooperate. A central MOE person was assigned to coordinate SHIP Health Education activities at the governorate level. She will start assuming her tasks by nominating candidates for the Science Teachers Supervisors.

MOHP/ NGOs

- Facilitated by JSI, an attempt was made in Qena governorate to create a partnership scheme between MOHP- health educators and NGOs awarded grants by USAID/ JSI. An agreement was reached to start this initiative by involving the health educators of Qena governorate in the training of the NGO community outreach workers.
- As an outcome of the coordination meeting of the two parties, they agreed on the following courses of action:
- Health educators will provide technical support to two NGOs (Al Ewaidat and El Wakf) for organizing and conducting community awareness.
- The two NGOs community outreach workers will provide support to MOHP EPI/ POLIO campaigns and outreaching households with related health messages.
- Health educators will join the NGOs Awareness Committee as members to coordinate the above activities and strengthen the cooperation.
- The NGOs Awareness Committees met with their MOHP members, on December 23 and 24, 2002 and developed a three month plan of action for cooperation.
- This initiative will be replicated in the remaining target governorates after evaluation.

USAID/ IEC Coordination Meeting

- A coordination meeting was held with Ms. Kathryn Panther, communication for Healthy Living Team Leader/ USAID, JSI COP and IEC staff on November 18, 2002.
- The purpose of the meeting was to provide a briefing on HM/HC IEC activities produced and implemented during the Base Period of the contract.
- A presentation that covers the IEC campaigns and the materials produced under the Base Period was part of the meeting. A discussion on the different areas of collaboration and the opportunity to implement a joint activity by re-airing all JSI TV spots and re-printing video films and IEC materials was also discussed. A copy of all IEC materials and video films was given to the USAID representative an agreement was reached to seek and plan for areas of collaboration in the next coming year.

TAHSEEN Project*A - Work Planning Workshop*

- JSI Chief of Party and his two deputies participated in the three day workshop organized by CATALYST Consortium/ TAHSEEN Project to develop a Workplan for the new project. The workshop that was conducted during the period from October 23 to 25, 2002 was planned to develop a Workplan with participation from the Population/ Family Planning Sector- MOHP and Managers of FP in the governorates. Formats were used to solicit the participants' contribution in identifying suggested implementing agencies as

well as technical assistance required to activities predetermined to achieve the following four themes:

- Focusing attention on priority groups. (hard to reach and hard to motivate).
- Improving quality care for the clients.
- Strengthening support systems.
- Active sustainable sectoral shares.

B – Meeting of Chiefs of Party

- A meeting between TAHSEEN and JSI Chiefs of Party took place on November 6, 2002 to exchange information and discuss mechanisms for coordination and integration between the two USAID funded projects. Agreement was reached by the end of this meeting that when TAHSEEN completed its annual Workplan, the two contractors will meet to coordinate specific activities.

C – MHIS

- Mr. Ibrahim Zaki Information Specialist accompanied by a consultant (Mr. Bashar Juma'a) from TAHSEEN Project met with JSI's MIS team on November 17, 2002 to acquaint themselves with the GIS and HIS. JSI presented and explained the MHIS system, the data base currently used (FoxPro), the new upgraded system that is under development with JSI support and the GIS component with data items that could be presented on the maps that is implemented on Excel sheets. As the GIS system is producing now maps up to the district level, TAHSEEN Project have indicated that they are looking forward to obtain maps up to the facility level. JSI team also presented the standard coding system for the ministry of health facilities and the district codes for the maps. All issues related to available GIS tools capabilities and cost were presented by JSI and discussed with TAHSEEN team during that meeting.
- TAHSEEN staff mentioned during the said meeting that they are looking forward to develop a web based GIS system but it seems that they are still in the phase of collecting information and exploring the situation. TAHSEEN promised once they got the full picture of what is going on to return back and discuss with JSI alternatives.

D – Private Sector

- A meeting was held with Mr. Jack Thomas – Technical Consultant/ TAHSEEN/ CATALYST on November 17, 2002. The purpose of the meeting was as follows:
 - Discuss mechanisms of cooperation and coordination between HM/HC and TAHSEEN / CATALYST in the area of Private Sector.
 - Discuss the necessary background information for completing the SOW for the Assessment of the "Ask-Consult" Program/ TAHSEEN/ CATALYST.

The National Population Council

- JSI attended the seminar organized by the NPC on November 4, 2002 to present the findings of the research project "The Potential for NGOs FP/RH Clinics for Providing Sustainable Quality Services". His Excellency the Minister of Health and Population inaugurated the meeting which was attended by concerned parties of MOHP, NGOs, donors and research centers and institutes.
- The research recommended that:
 - The family planning clinics run by the NGOs should include more RH services in an integrated way to be more attractive to beneficiaries, create demand and increase utilization.
 - Reschedule the service time and working hours with clear focus on having evening shifts to suit more the clients' needs.
 - Design and conduct training for providers working with NGOs clinics in order to provide the right and suitable information and message to clients on contraceptive methods and particularly on how to use them and the side effects.
 - Coordinate between MOHP and NGOs clinics to create more integration and efficiency in providing FP/RH services.

Population Council

- JSI participated in a Seminar organized by the Population Council/ Frontiers in Reproductive Health Program on October 3, 2002, to present the key findings and summary of intervention of the operation research that aimed to demonstrate how improving the quality of client-provider interaction could be achieved in large health care systems and how these improvements could be translated into positive client outcomes of family planning knowledge, method continuation rates and method satisfaction. Egypt's study is one of the global operations research projects that have been conducted in two other countries. The major outcome is that a client-centered interaction will have a positive impact on clients, providers and entire clinic.
- JSI participated in the Dissemination Meeting on December 19, 2002 for the "Facility Practices Normal Labor: An Observation Study". It is the first comprehensive study of normal labor, where the process rather than the outcome was the main point of emphasis. The tool was pre-tested for 3 days (24 hours of observation every day), changes were made after pre-testing. 188 women were included in the study, 12 of the observations were discontinued due to complications (thus not normal labor any more). 672 hours of continuous observation that is 28 continuous days. 12 observers participated in the study. The Meeting was concluded with remarks on the relevance of the findings, challenges to policy implementation and future plans.

UNICEF

- UNICEF - based on a recommendation from HM/HC Executive Director- sought the support of JSI on two related areas: TT routine and campaigns to be planned as well as clean and safe delivery. JSI provided IEC materials produced that would support such efforts and expressed its willingness in join any future planned efforts in Upper Egypt target governorates.

International Trachoma Initiative (ITI)

- ITI is in the process of introducing this initiative in Egypt in the near future. Based on advice from USAID, a meeting was held with Dr. Heba Abdel Kader, ITI representative when to discuss areas of joint work and cooperation particularly in working with NGOs and mutual supportive IEC activities.

Contract Administration

Accomplishments

- Full and part time staff positions were filled for the Option Period. A Contract Staff List detailing employee names and positions can be found in Annex C.
- The JSI organizational chart was revised with the departure of the DCOP for Technical Services. The management of Task One activities was transferred to the DCOP for Management.
- A request for change in Key Personnel was submitted to USAID as required.
- Technical and administrative visits were made to the field offices for general review and oversight.
- The JSI budget tracking tool was updated for the Option Period and actual and projected expenses were entered.
- JSI provided monthly expenditure estimates to USAID as required.
- JSI submitted an obligation request for an additional US\$5 Million.
- The Subcontracting Report (SF294) was submitted to USAID for the period ending September 30, 2002.
- The JSI PIL budget requirements were submitted and approved for year two activities.
- JSI use of PIL funds is being tracked daily and reconciled with the Project on a monthly basis.
- Invitational travel for two MOHP doctors to travel to Italy for the “Genetic Counseling Practice Workshop” was approved and financed by JSI.
- Arrangements were made by JSI for three MOHP doctors to travel to Bahrain in February to attend a conference on Primary Health Care Issues in the Arab World.
- Project inventory records were updated and reviewed for accuracy.

Constraints

- None

Proposed Actions to Overcome Constraints

- None


ANNEX A - PERFORMANCE MILESTONES CHART

MILESTONE STATUS REPORT


14/01/2003

Date Due	Task No.	Milestone	Submitted	Validated	Approved	Comments
					USAID	
15/03/2002	1	Development of CHG/HC Project Procurement Plan	14/04/2002	✓	02/06/2002	Completed
15/09/2002	2	Assist MOHP to establish 10 district IMCI training in at least one additional target governorate.	08/09/2002	✓	30/09/2002	Completed
15/09/2002	3	Health and Monitoring Systems developed and implemented for a cumulative total of 37	12/09/2002	✓	29/12/2002	Completed
15/09/2002	4	Assist MOHP to establish 10 district MHS centers.	08/09/2002	✓	31/12/2002	Completed
15/09/2002	5	Comprehensive research plan developed	12/09/2002	✓		
15/09/2002	6	Comprehensive research plan developed and implemented in 12 additional districts for a cumulative total of 37 districts.	08/09/2002	✓	30/09/2002	Completed
15/09/2002	7	15000 US\$ grants awarded to NGOs in target districts.	08/09/2002	✓	30/09/2002	Completed
15/09/2002	8	15000 US\$ grants awarded to NGOs in target districts.	12/09/2002	✓	03/10/2002	Completed
15/09/2002	9	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	10	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	11	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	12	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	13	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	14	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	15	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	16	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	17	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	18	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	19	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	20	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	21	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	22	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	23	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	24	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	25	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	26	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	27	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	28	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	29	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	30	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	31	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	32	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	33	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	34	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	35	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	36	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	37	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	38	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	39	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	40	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	41	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	42	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	43	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	44	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	45	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	46	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	47	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	48	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	49	15000 US\$ grants awarded to NGOs in target districts.				
15/09/2002	50	15000 US\$ grants awarded to NGOs in target districts.				


ANNEX B - MAPS OF TARGET GOVERNORATES

LEGEND	YES	NO
Directorate MHIS Center Upgraded		
District MHIS Center Established		
Neonatal Care Center Upgraded		
CEOC Center Upgraded		
BEOC Center Upgraded		


Beni Suef

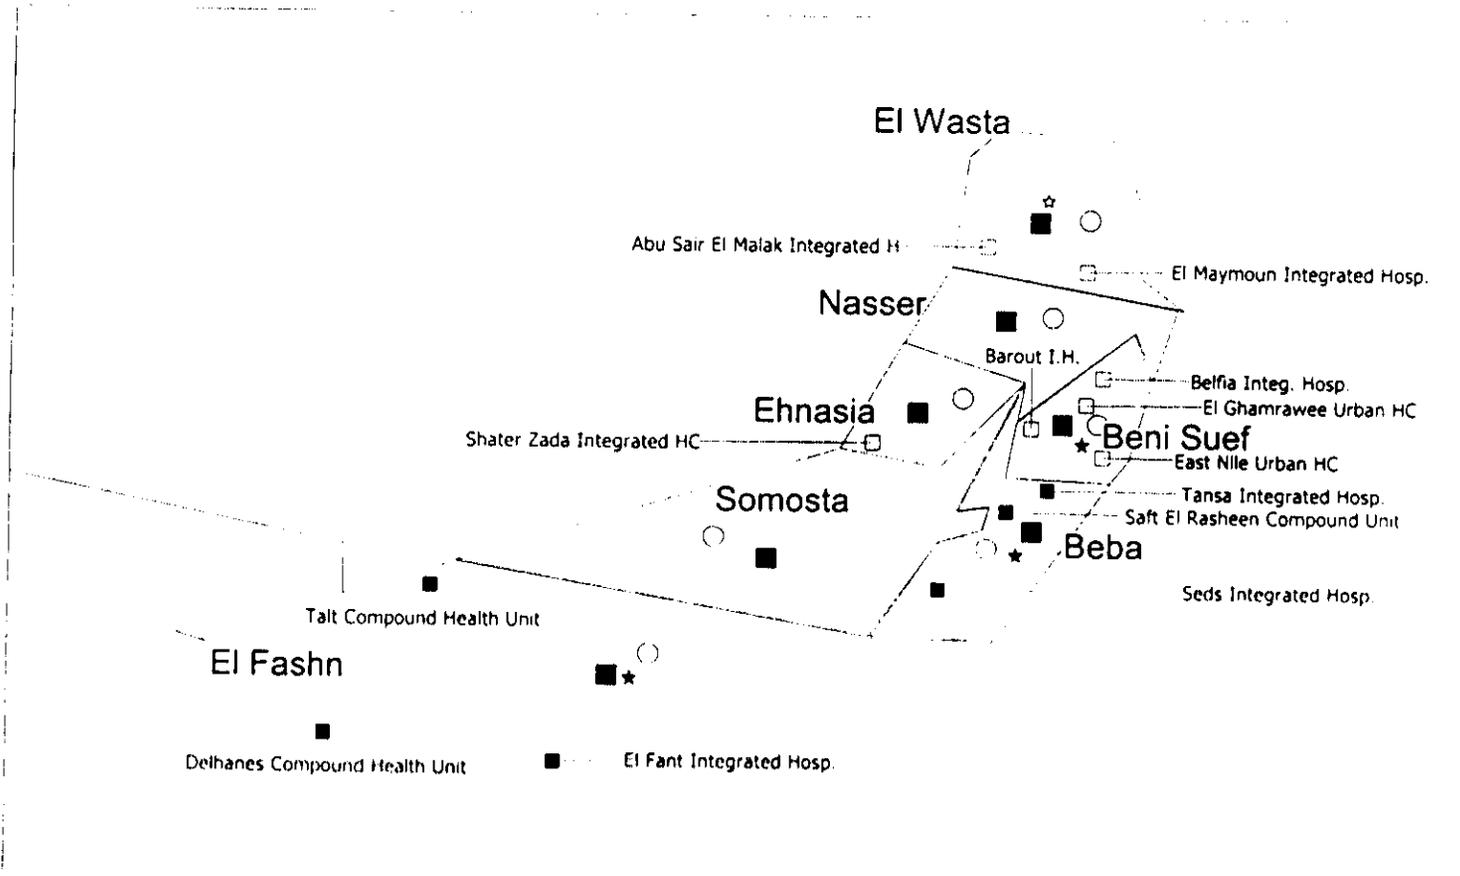


Sohag

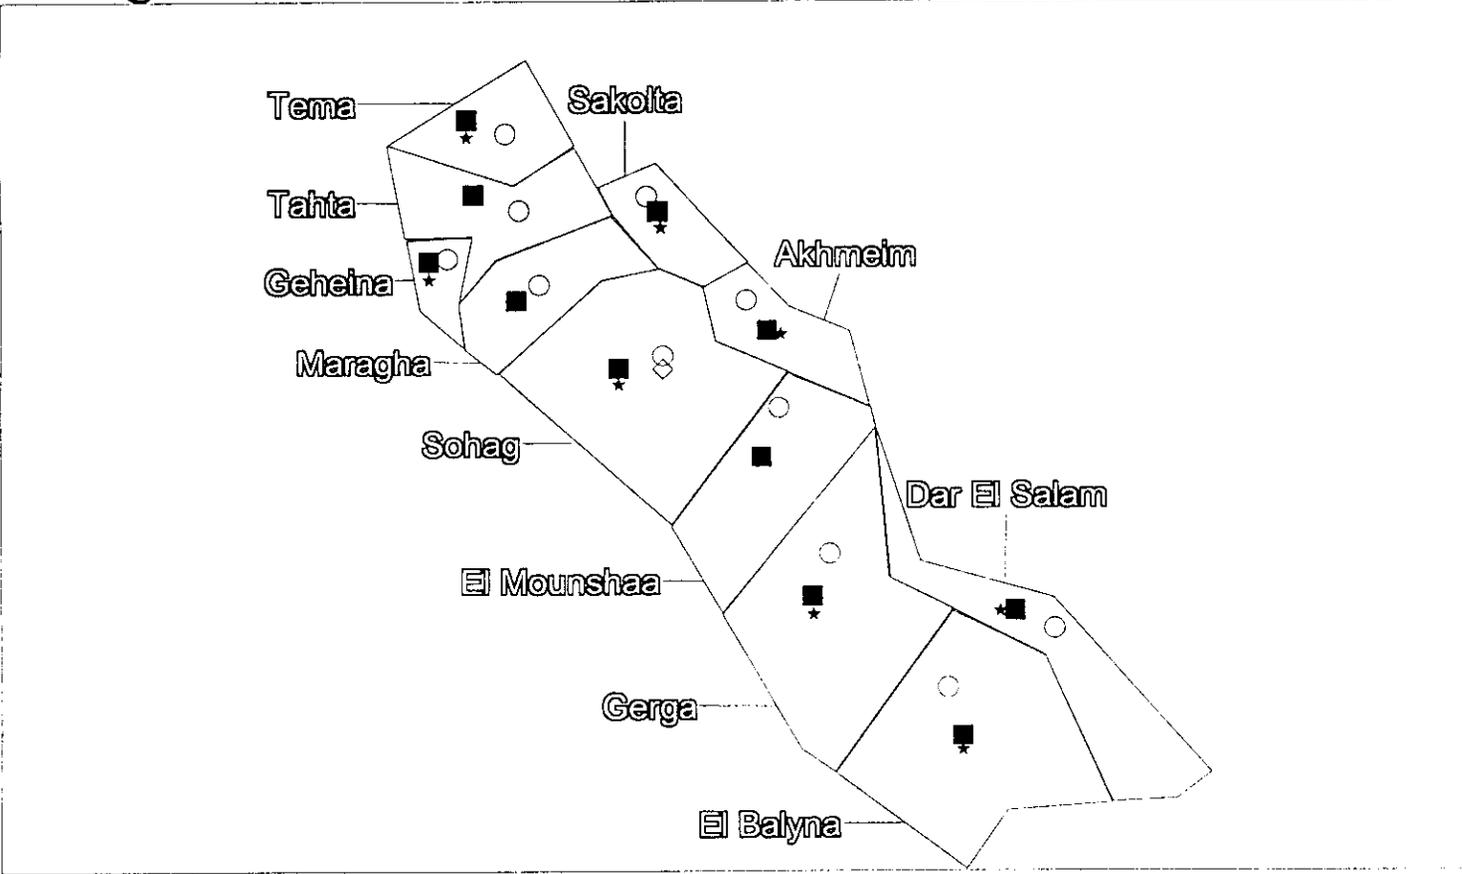


Assiut

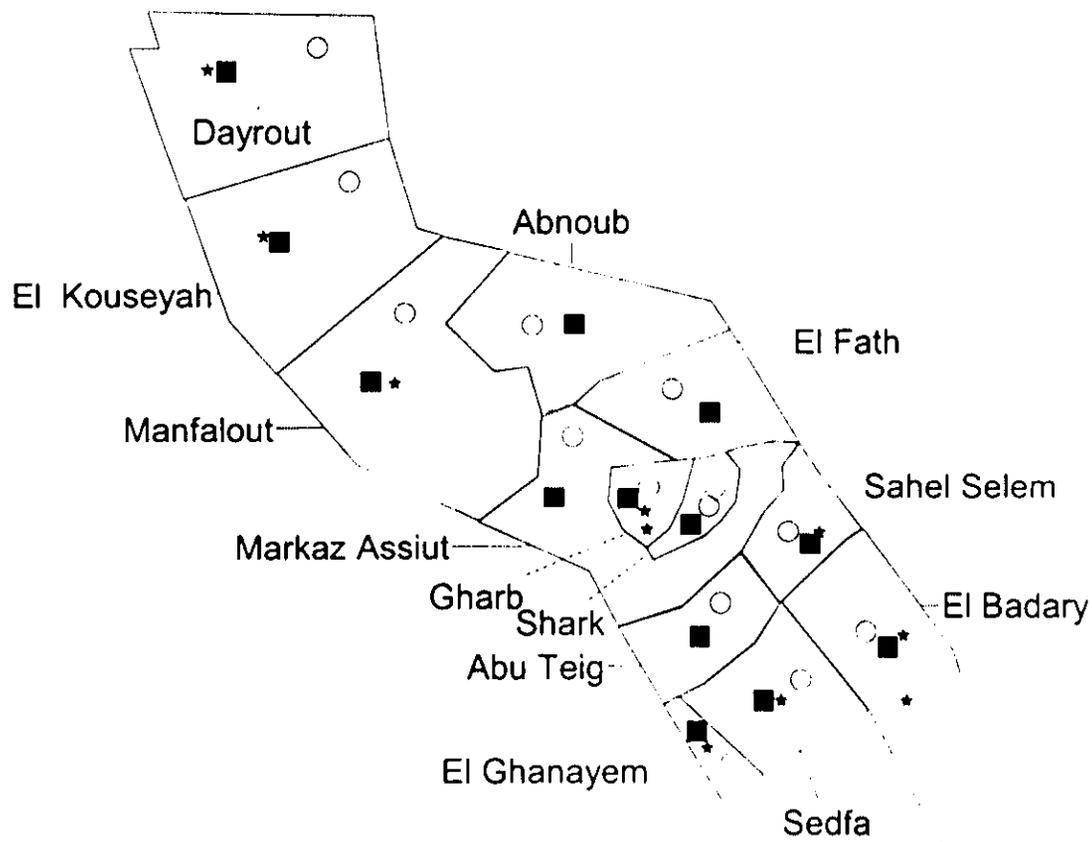


Giza

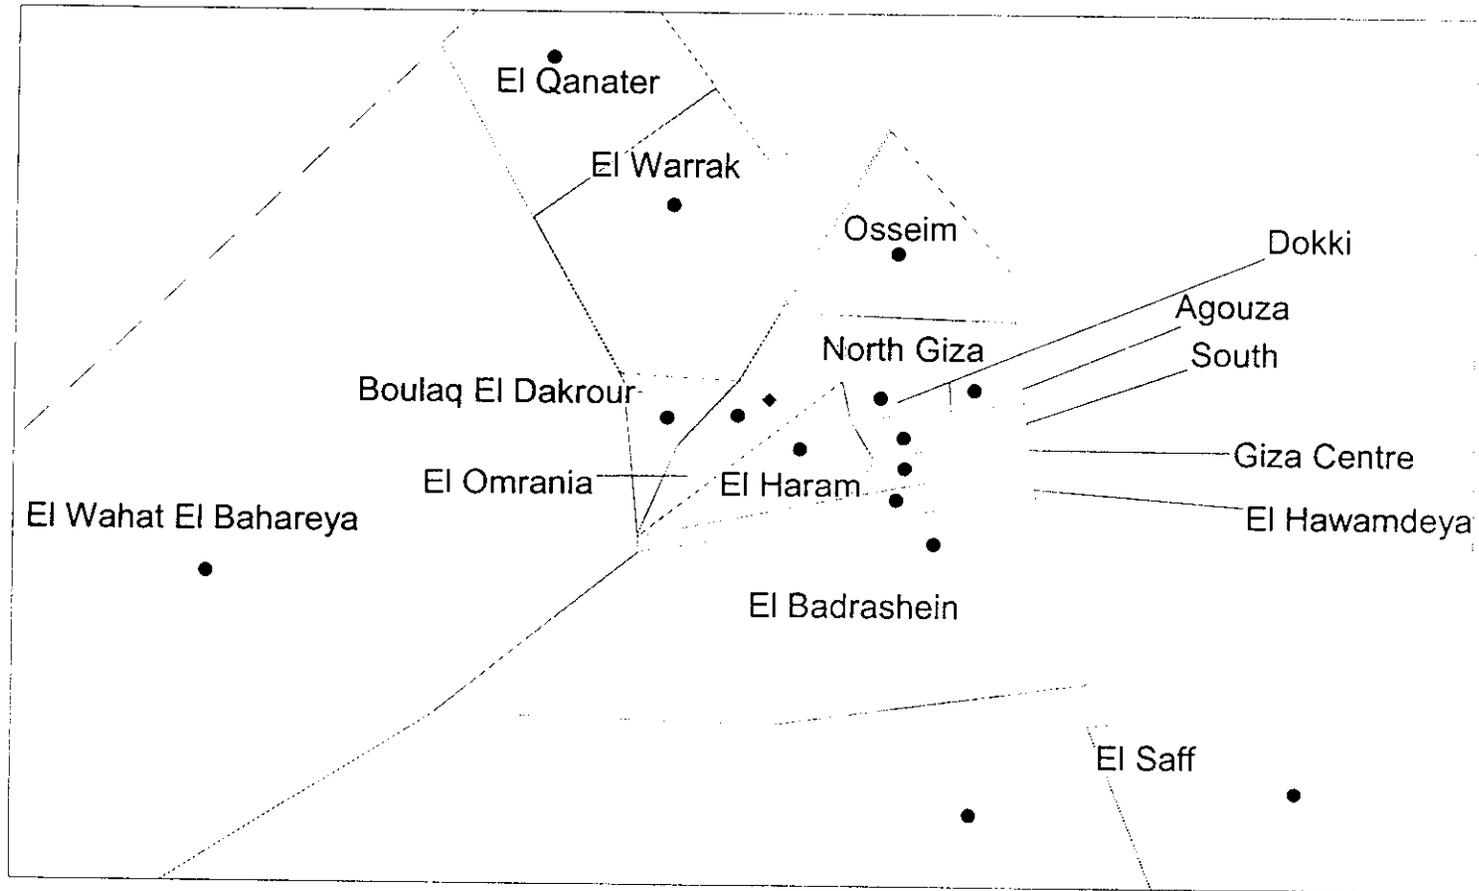

Qena

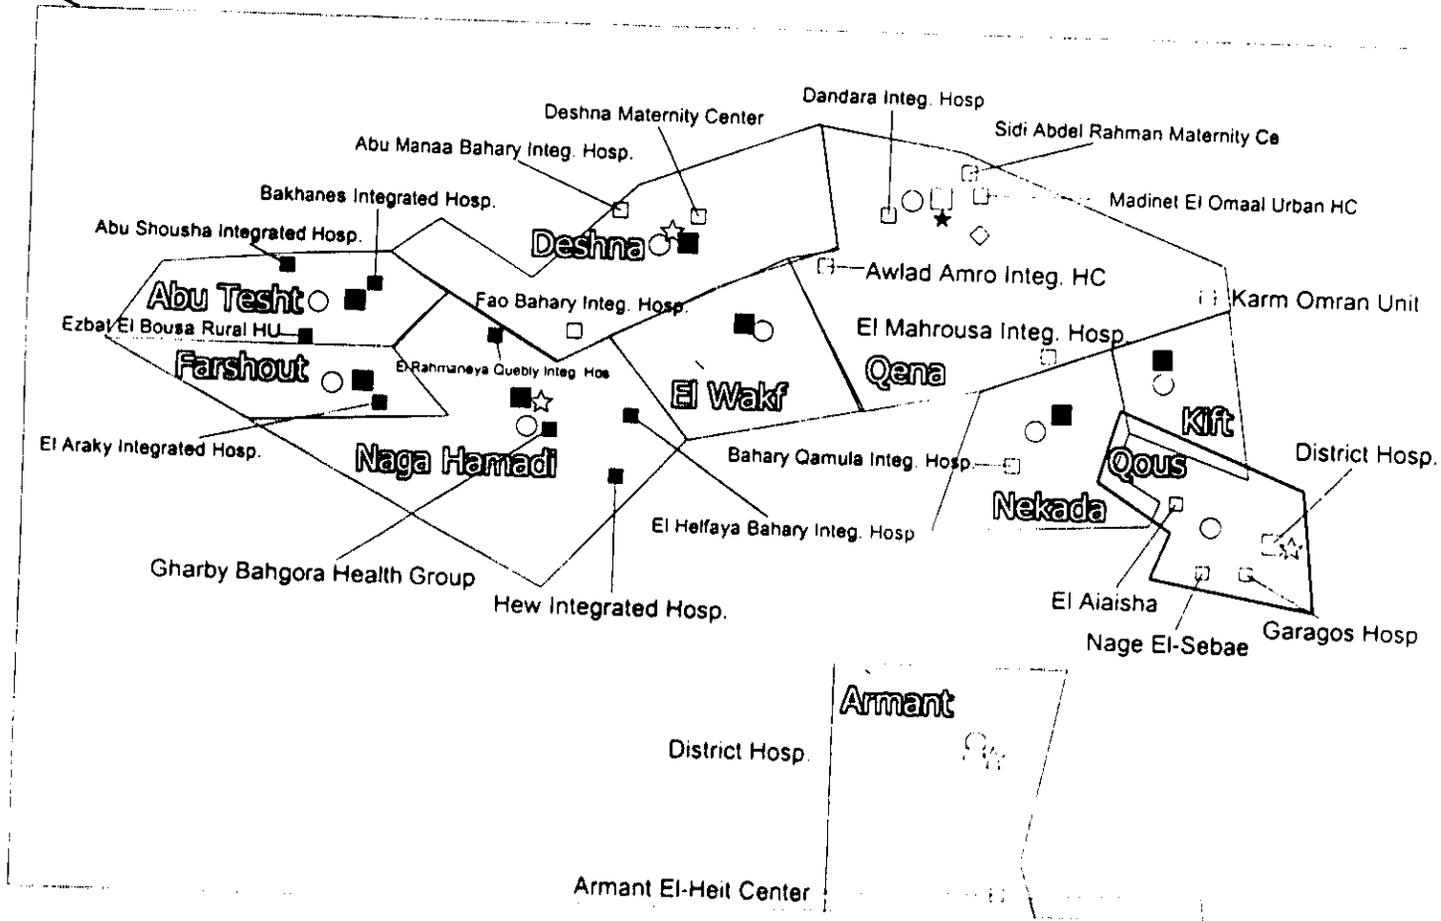

Qena

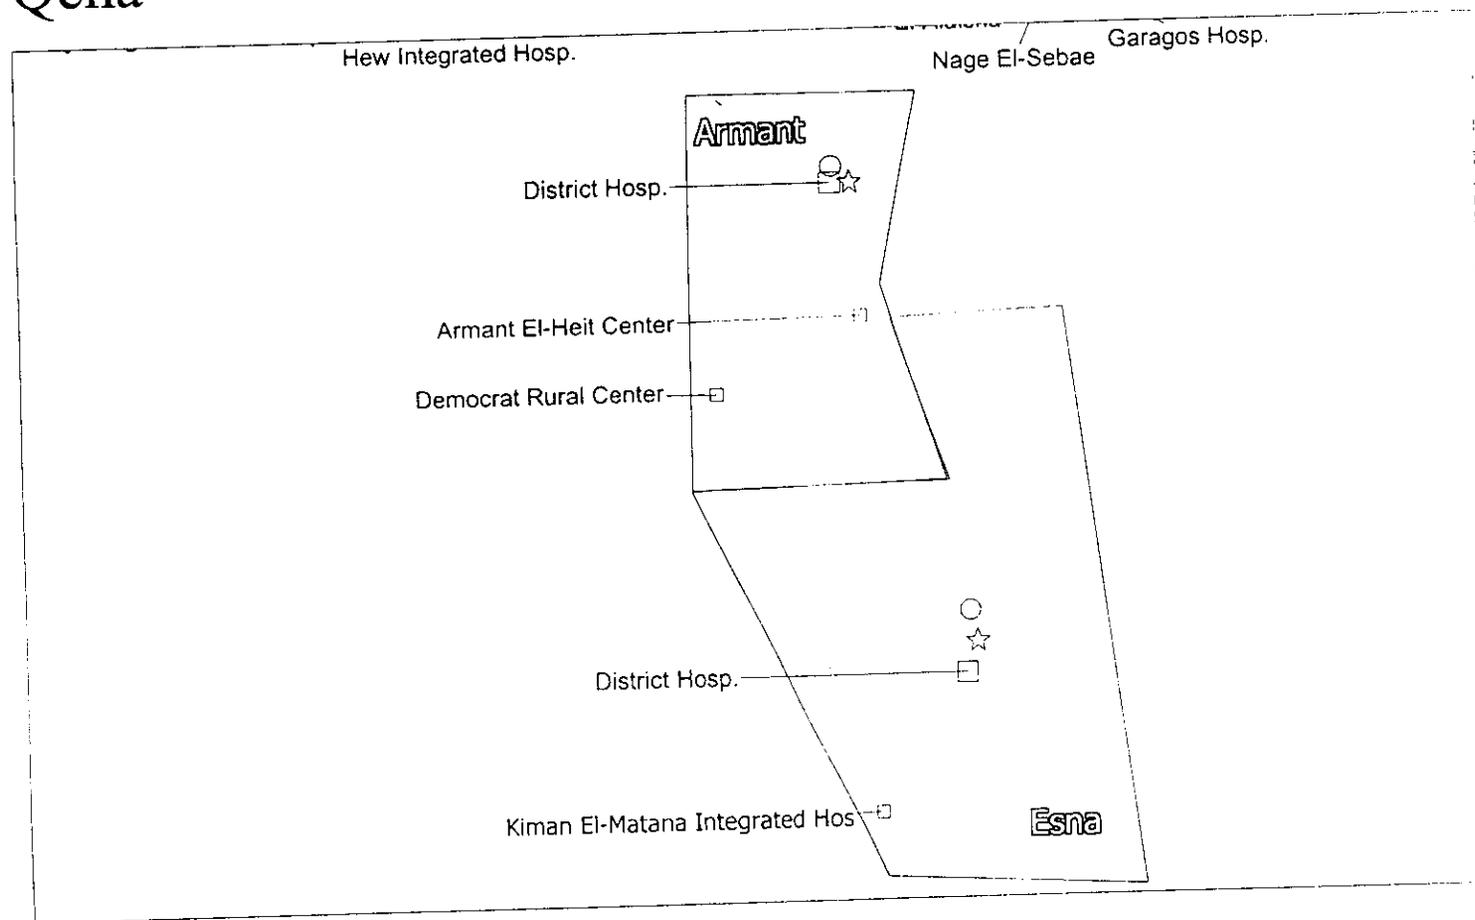

ANNEX C - JSI CONTRACT STAFF LIST

John Snow, Inc. HM/HC
Staff Names and Titles
Option Period - December 31, 2002

Names	Titles
JSI / Cairo office Full-Time Employees	
Reginald Gipson	Chief of Party
Sobhi Moharram	Deputy Chief of Party
Tom Coles	Coordinator for Tasks 1, 3, 4, 5, 7 & 10 Health Providers Training Supervisor Coordinator for Task 2
Katrina Kruhm	Project Administrator Coordinator for Task 11
Hassan El Sheikh	Implementation Team Coordinator Task Team Member: Task 1 & 2
Mohsen El-Said	Implementation Specialist (Assiut & Menya) Task Team Member: Task 1
Said Khalil	Implementation Specialist (Sohag) Task Team Member: Task 1
Dalia Raafat	Architect & Quantity Surveyor Task Team Member: Task 1
Mostafa Taher	Field Civil Engineer Task Team Member: Task 1
Ghada Sherif	Infection Control Specialist Task Team Member: Task 2
Lamiaa Mohsen	Perinatal Coordinator Task Team Member: Task 2
Mohamed Moustafa	Training Specialist Task Team Member: Task 2
George Sanad	Health Management Specialist Task Team Member: Task 3
Wafaci El-Sakkary	Quality Assurance Specialist Task Team Member: Task 3
Sherif El-Kamhawy	Quality Assurance Assistant Task Team Member: Task 3
Khaled Abdel Fattah	Senior Systems Analyst (Arabsoft) Task Team Member: Task 4
Samch Gamil	Senior Systems Engineer (Arabsoft) Task Team Member: Task 4
Adel Hakim	Maternal Mortality Surveillance System Specialist Task Team Member: Task 5
Khaled Nada	Operation Research Specialist Task Team Member: Task 5
El-Sayed Kishta	Community Outreach Worker Specialist Task Team Member: Task 10
Hani Samir Riad	Implementation Specialist (SHIP) / Community Health Coordinator Task Team Member: Task 7
Dalia Sherif	Communications Assistant Task Team Member: Task 7
Heba Rafik	Communications & Contracting Specialist Task Team Member: Task 7

Names	Titles
Khaled El-Sayed	Community Mobilization Specialist Task Team Member: Task 7
Maha Anis	Training Specialist Task Team Member: Task 7
Marwa Kamel	Communication & Public Relations Specialist Task Team Member: Task 7
Hana Abdel Megeid	SHIP Assistant Task Team Member: Task 7
Mohamed Mansour	NGO Small Grants Specialist Task Team Member: Task 10
Marion Charobim	Procurement Specialist Task Team Member: Task 11
Ola Zakaria	Administrative / Contracting Specialist Task Team Member: Task 11
Hazem Mansour	Financial Manager
Amr Obeid	Senior Accountant
Bassem Reda	Senior Accountant
Menna Alla Medhat	Accountant
Naglaa El-Bakri	Office Manager
Manar Adel	Administrative / Personnel Specialist
Rami Ezzy	Senior Network Administrator
Amr Hassan	Assistant Network Administrator
Gihan Iskandar	Senior Program Assistant (COP)
Dalia Hassan	Program Assistant (Management)
Mariam Samir	Program Assistant(MMSS)
Passant Al-Ashkar	Program Assistant (Service Development & Delivery)
Neveen Sami	Program Assistant (Health Providers Training Supervisor)
Nesrine Sobhi	Executive Secretary
Ingy Kotb	Executive Secretary
Dina Khairy	Executive Secretary / Travel Assistant
Ola Hussein	Secretary
Soha Hassan	Secretary
Nashwa Bahgat	Secretary
Roaa Ibrahim	Secretary
Dina Bahader	Receptionist/Secretary
Iris Guirguis	Data Entry Assistant
Tarek El-Nadi	Senior Driver
Ali Yassin	Driver
Hassaballah Mostafa	Driver
Ayman Mohamed	Messenger/ Expeditor
Ahmed Moawad	Messenger/ Expeditor
Mohamed Harbi	Messenger / Store-Keeper
Ayman Mirghani	Photocopy Clerk
Hassan Fawzi	Office Boy
Khaled El-Ghoneimy	Office Boy
Part-time Employees	
Nevine Hassanein	Slum Areas Development Coordinator
Mona Selim	Slum Areas Development Specialist

Names	Titles
Mohamed Rashad	Architectural & Engineering Specialist
Mohamed Magdy Al-Aasar	Field Civil Engineer
Mohamed Helmy	Electrical Engineer
Khaled Saber	Bio-Medical Engineer
Iman Radwan	Bio-Medical Engineer
Hussein Khamis	Support Services Coordinator
Sabry Hamza	EOC Coordinator
Ashraf Shawat	Anesthesiology Specialist
Amr Abul Fadl	Emergency Room Team Trainer Specialist
Salwa Teama	Hematology Specialist
Ahmed Ashraf Wegdan	Infection Control Specialist
Amr Fathi	Clinical Supervisor
Abdel-Ghaffar Mohamed	Clinical Supervisor
Ahmed Samy	Clinical Supervisor
Ahmed Mohamed	Clinical Supervisor
Assem Anwar	Clinical Supervisor
Hossam Ahmed	Clinical Supervisor
Ihab El-Nashar	Clinical Supervisor
Magdy Sweed	Clinical Supervisor
Magdy Tawfik	Clinical Supervisor
Mahmoud Rizk	Clinical Supervisor
Mahmoud Shokry	Clinical Supervisor
Mohamed Sabry	Clinical Supervisor
Mohamed Mahmoud	Clinical Supervisor
Sayed Mostafa	Clinical Supervisor
Tarek El-Dessouky	Clinical Supervisor
Yasser Abou-taleb	Clinical Supervisor
Ahmed Reda	Neonatal Clinical Supervisor
Aly Bayoumi	Neonatal Clinical Supervisor
Dahlia El-Sebaei	Neonatal Clinical Supervisor
Hanan Abdel Moneim	Neonatal Clinical Supervisor
Hisham Ali	Neonatal Clinical Supervisor
Mostafa Abdel Azeem	Neonatal Clinical Supervisor
Salah El-Din Ahmed	Neonatal Clinical Supervisor
Ismail El-Hawary	Neonatal Specialist
Nahed Fahmy	Neonatal Specialist
Maaly Guimei	Senior Nurse Advisor
Rosario Raz	Nursing Master Trainer
Madiha Mohamed	Nursing Trainer / Supervisor
Sahar Nagieb	Nursing Trainer / Supervisor
Abeer El-Kotb	Nursing Trainer / Supervisor
Sahar younes	Nursing Trainer / Supervisor
Heba Ezzat	Nursing Trainer / Supervisor
Rabab El-Sayed	Nursing Trainer / Supervisor
Randa El-Sayed	Nursing Trainer / Supervisor
Hanan Said	Nursing Trainer / Supervisor

Names	Titles
Rasha Adel	Nursing Trainer / Supervisor
Hamida Alam El-Din	Nursing Trainer / Supervisor
Nadia Abd-Allah	Nursing Trainer / Supervisor
Enayat El-Sayed	Nursing Trainer / Supervisor
Said El-Dib	Health Management Coordinator
Walid Salah	Data Management Assistant (SHIP)
Mohamed Youssef	Field Program Assistant (SHIP) / Beni Suef
Sameh Sabry	Field Program Assistant (SHIP) / Fayoum
Ola Hamdy	Community Development Trainer / Qena
Donald Benson	Publications Coordinator
Adam Taylor	Editor
Heidi Thurmon	Editor
Martha Abou El-Ella	Editor
Michelle Auld	Editor
Samantha Bramely	Editor
Alison Bichard	Technical Writer / Editor
Erin Benson	Technical Writer / Editor
Tarek El-Shimi	Technical Writer / Editor
Beni-Suef Field Office	
Besheer Mohamed	Maternal & Child Health / Management Specialist / Field Office Manager
Ahmed Assran	Community Development Specialist
Sahar Mohamed	Administrative Assistant
Fathey Korani	Office Boy
Fayoum Field Office	
Marwan Abdel Fattah	Maternal & Child Health / Management Specialist / Field Office Manager
Amal Abdel Gawad	Community Development Specialist
Ashraf Saad	Administrative Assistant
Gamal Abdel-Azeem	Driver
Rabie Khamis	Office Boy
Qena Field Office	
Mamdouh Aboul-Kassem	Maternal & Child Health Specialist / Field Office Manager
Ossama Ibrahim Mohamed	Health Planning & Management Specialist
Israa Ibrahim Raslaan	Community Development Specialist
Hussein Kamel	Field Program Assistant (SHIP), Qena & Sohag
Essam El-Sayed	Administrative Assistant
Khaled Hamdan	Driver
Mohamed Fawzi	Office Boy
Assiut Field Office	
Tarek Abdel-Wahed	Health Planning & Management Specialist/ Field Office Manager
Abdel Aziz Mohamed	Maternal & Child Health Specialist
Mohamed Youssef	Community Development Specialist
Mahmoud Ahmed	Administrative Assistant
Akram Yehia	Field Program Assistant (SHIP)

Names	Titles
Nasser Sayed	Office Boy
Minia Field Office	
Gihan Shafik	Maternal & Child Health Specialist
Amgad George	Health Planning & Management Specialist/ Field Office Manager
Mostafa Sayed	Community Development Specialist
Ahmed Hosni	Field Program Assistant (SHIP)
Samah Khalifa	Administrative Assistant
Gamal Ahmed	Office Boy
Sohag Field Office	
Gamal El-Korashy	Maternal & Child Health Specialist
Abdel-Moneim Abdel-Aziz	Health Planning & Management Specialist/ Field Office Manager
Ahmed Ramadan	Community Development Specialist
Ashraf Mostafa	Administrative Assistant
Hassan Abbas	Driver
Seoudi Fayez	Office Boy

**ANNEX D - SUMMARY OF UPGRADED STATUS OF FACILITIES
IN TARGET DISTRICTS**

Summary of Upgrade Status of Facilities in Target Districts

QPMR V		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Facility	Assessment	Renovation	Commodities	Training	
Target Governorates Total				100	57	24	21	100	2
Qena Governorate				100	100	33	0	100	0
Qena District			I	100	100	33	0	100	0
Qena District Hospital	CEOC	I					In Process		Interim
Qena District Hospital	CSSD	I				On Order	In Process		Interim
Qena District Hospital	OR	I				On Order	In Process		Interim
Ei-Wakf District			I	100	100	33	0	100	0
Ei-Wakf District Hospital	CEOC	I					In Process		Interim
Ei-Wakf District Hospital	CSSD	I				On Order	In Process		Interim
Ei-Wakf District Hospital	OR	I				On Order	In Process		Interim

Summary of Upgrade Status of Facilities in Target Districts

01/13/2003

QPMR V		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Assessment	Renovation	Commodities	Training	SMC	
Fayoum Governorate				100%	75%	42%	58%	100%	0
Sennoures District			I	100%	67%	33%	50%	100%	0
Sennoures District Hospital		CEOC	I	Completed	Completed	Completed	In Process	Completed	Interim
Sennoures District Hospital		NCU2	I	Completed	Completed	Completed	Completed	Completed	Interim
Sennoures District Hospital		CSSD	I	Completed	Completed	On Order	Completed	Completed	Interim
Sennoures District Hospital		OR	I	Completed	Completed	On Order	Completed	Completed	Interim
Maternity Center		BEOC	I	Completed	Plans	On Order	In Process	Completed	Interim
Fedmin District Hospital		BEOC	I	Completed	Plans	On Order	In Process	Completed	Interim
Tamia District				100%	83%	50%	67%	100%	0
Tamia District Hospital		CEOC	I	Completed	Completed	Completed	Completed	Completed	Interim
Tamia District Hospital		NCU2	I	Completed	Completed	Completed	Completed	Completed	Interim
Tamia District Hospital		CSSD	I	Completed	Completed	On Order	Completed	Completed	Interim
Tamia District Hospital		OR	I	Completed	Completed	On Order	Completed	Completed	Interim
Maternity Center		BEOC	I	Completed	Completed	Completed	In Process	Completed	Interim
Sersena I.H.U		BEOC	I	Completed	Construction	On Order	In Process	Completed	Interim

QPMR V			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SBC	
Beni Suef Governorate			100%	60%	33%	55%	100%	2
Nasser District		I	100%	100%	67%	55%	100%	2
Nasser District Hospital	CEOC	I						
Nasser District Hospital	NCU2	I				In Process		
Nasser District Hospital	CSSD	I						0
Nasser District Hospital	OR	I						0
Maternity Center	BEOC	I			On Order	In Process		0
Ashmunt L.H.U	BEOC	I			On Order	In Process		0
Somosta District			100%	25%	0%	60%	100%	3
Somosta District Hospital	CEOC	I		Construction	Available			Interim
Somosta District Hospital	CSSD	I		Construction	On Order			0
Somosta District Hospital	OR	I		Construction	On Order	Completed		0
Shanhar L.H.U	BEOC	I		Completed	On Order	In Process		0
Dahlut L.H.U	BEOC	I		Construction	On Order			0

QPMR V		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Facility	Assessment	Renovation	Commodities	Training	
Assiut Governorate				100%	31%	16%	11%	100%	0
Gharb Assiut District			I	100%	67%	17%	33%	100%	0
El-Eman El-Gadida		CEOC	I	Complete	On Order	On Order	In Process	Complete	0
El-Eman El-Gadida		NCU2	I	Complete	On Order	On Order	In Process	Complete	0
El-Eman El-Gadida		CSSD	I	Complete	On Order	On Order	In Process	Complete	0
El-Eman El-Gadida		OR	I	Complete	On Order	On Order	In Process	Complete	0
El-Eman El-Gadida		ER	I	Complete	0	On Order	In Process	Complete	0
Urban Health Center Alarbaeen		BEOC	I	Complete	Contract	On Order	In Process	Complete	0
Shark Assiut District			I	100%	83%	17%	17%	100%	0
Assiut General Hospital		CEOC	I	Complete	On Order	On Order	In Process	Complete	0
Assiut General Hospital		NCU2	I	Complete	On Order	On Order	In Process	Complete	0
Assiut General Hospital		CSSD	I	Complete	On Order	On Order	In Process	Complete	0
Assiut General Hospital		OR	I	Complete	On Order	On Order	In Process	Complete	0
Assiut General Hospital		ER	I	Complete	0	On Order	In Process	Complete	0
Maternity Center - Alwalidia		BEOC	I	Complete	On Order	On Order	In Process	Complete	0
Markaz Assiut District			I	100%	100%	17%	33%	100%	0
Ob/Gyn Hospital		CEOC	I	Complete	On Order	On Order	In Process	Complete	0
Ob/Gyn Hospital		NCU2	I	Complete	On Order	On Order	In Process	Complete	0
Ob/Gyn Hospital		CSSD	I	Complete	On Order	On Order	In Process	Complete	0
Ob/Gyn Hospital		OR	I	Complete	On Order	On Order	In Process	Complete	0
Nag-Sabee I.H.		BEOC	I	Complete	On Order	On Order	In Process	Complete	0
El-Moleaa I.H.		BEOC	I	Complete	On Order	On Order	In Process	Complete	0
El Ghanayem District			II	100%	100%	20%	20%	100%	0
El Ghanayem District Hospital		CEOC	II	Complete	On Order	On Order	In Process	Complete	0
El Ghanayem District Hospital		NCU2	II	Complete	On Order	On Order	In Process	Complete	0
El Ghanayem District Hospital		CSSD	II	Complete	On Order	On Order	In Process	Complete	0
El Ghanayem District Hospital		OR	II	Complete	On Order	On Order	In Process	Complete	0
UHC, Maternity		BEOC	II	Complete	On Order	On Order	In Process	Complete	0
El Kouseyah District			II	100%	0%	13%	0%	100%	0
El Kouseyah District Hospital		CEOC	II	Complete	Bid Process	On Order	In Process	Complete	0
El Kouseyah District Hospital		NCU2	II	Complete	Bid Process	On Order	In Process	Complete	0
El Kouseyah District Hospital		CSSD	II	Complete	Bid Process	On Order	In Process	Complete	0
El Kouseyah District Hospital		OR	II	Complete	Bid Process	0	In Process	Complete	0
El Kouseyah District Hospital		ER	II	Complete	Plans	0	In Process	Complete	0
El Kouseyah Maternity		BEOC	II	Complete	Plans	On Order	In Process	Complete	0
Bani Korra W.H.U		BEOC	II	Complete	Plans	On Order	In Process	Complete	0
Fazara I.H.		BEOC	II	Complete	Plans	On Order	In Process	Complete	0
El Fath District			II	100%	0%	0%	33%	100%	0
El Fath U.H.C		BEOC	II	Complete	0	On Order	In Process	Complete	0
El Atawila I.H.		BEOC	II	Complete	0	On Order	In Process	Complete	0
El Wasta I.H.		BEOC	II	Complete	0	On Order	In Process	Complete	0
Sahel Seleem District			III	100%	0%	25%	0%	100%	0
Sahel Seleem District Hospital		CEOC	III	Complete	Bid Process	On Order	In Process	Complete	0
Sahel Seleem District Hospital		NCU2	III	Complete	Bid Process	On Order	In Process	Complete	0
Sahel Seleem District Hospital		CSSD	III	Complete	Bid Process	On Order	In Process	Complete	0
Sahel Seleem District Hospital		OR	III	Complete	Bid Process	On Order	In Process	Complete	0
El Badary District			III	100%	0%	25%	0%	100%	0
El Badary District Hospital		CEOC	III	Complete	Bid Process	On Order	In Process	Complete	0
El Badary District Hospital		NCU2	III	Complete	Bid Process	On Order	In Process	Complete	0
El Badary District Hospital		CSSD	III	Complete	Bid Process	On Order	In Process	Complete	0
El Badary District Hospital		OR	III	Complete	Bid Process	On Order	In Process	Complete	0
Dayrout District			III	100%	0%	25%	0%	100%	0
Dayrout District Hospital		CEOC	III	Complete	Bid Process	On Order	In Process	Complete	0
Dayrout District Hospital		NCU2	III	Complete	Bid Process	On Order	In Process	Complete	0
Dayrout District Hospital		CSSD	III	Complete	Bid Process	0	In Process	Complete	0
Dayrout District Hospital		OR	III	Complete	Bid Process	On Order	In Process	Complete	0
Abu Teig District			III	100%	0%	0%	0%	100%	0
Abu Teig District Hospital		CEOC	III	Complete	Plans	On Order	In Process	Complete	0
Abu Teig District Hospital		CSSD	III	Complete	Plans	On Order	In Process	Complete	0
Summary				100%	30%	25%	0%	100%	0

QPMR V			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SAC	
Sedta District Hospital	CEOC	III			On Order			0
Sedta District Hospital	MCU2	III				In Process		0
Sedta District Hospital	CSSD	III		0	On Order			0
Sedta District Hospital	OR	III		0	On Order			0
Manfalout District			100	0	25	0		0
Manfalout District Hospital	CEOC	III		Plans	On Order			0
Manfalout District Hospital	MCU2	III		Plans		In Process		0
Manfalout District Hospital	CSSD	III		Plans	On Order			0
Manfalout District Hospital	OR	III		Plans	0			0
Abnoub District			100	0	0	0		0
Abnoub District Hospital	CEOC	III		Plans	On Order			0
Abnoub District Hospital	CSSD	III		Plans	On Order			0
Abnoub District Hospital	OR	III		Plans	On Order			0

QPMR V		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Assessment	Renovation	Commodities	Training	SMC	
Sohag Governorate				100%	44%	11%	0%	100%	0
Sohag District			I	100%	71%	14%	0%	100%	0
Sohag General Hospital	CEOC	I	Complete	Complete	Available	In Process	Complete	0	
Sohag General Hospital	NCU2	I	Complete	Complete	Complete	In Process	Complete	0	
Sohag General Hospital	CSSD	I	Complete	Complete	On Order	In Process	Complete	0	
Sohag General Hospital	OR	I	Complete	Complete	On Order	In Process	Complete	0	
Sohag General Hospital	ER	I	Complete	0	On Order	In Process	Complete	0	
Gezerat Shanawel I.H.	BEOC	I	Complete	Complete	On Order		Complete	0	
Balsofora I.H.	BEOC	I	Complete	Construction	On Order	In Process	Complete	0	
Tahta District			II	100%	75%	0%	0%	100%	0
Tahta District Hospital	CEOC	II	Complete	Complete	On Order	In Process	Complete	0	
Tahta District Hospital	NCU2	II	Complete	Complete	On Order		Complete	0	
Tahta District Hospital	CSSD	II	Complete	Complete	On Order	In Process	Complete	0	
Tahta District Hospital	OR	II	Complete	Complete	On Order	In Process	Complete	0	
Tahta District Hospital	ER	II	Complete	Complete	On Order	In Process	Complete	0	
Tahta Maternity Center	BEOC	II	Complete	Complete	0		Complete	0	
Shaturaa I.H.U.	BEOC	II	Complete	Plans	On Order		Complete	0	
El-Swanna I.H.	BEOC	II	Complete	Plans	On Order		Complete	0	
Gerga District			II	100%	60%	20%	0%	100%	0
Gerga District Hospital	CEOC	II	Complete	Complete	On Order	In Process	Complete	0	
Gerga District Hospital	NCU2	II	Complete	Complete	Complete		Complete	0	
Gerga District Hospital	CSSD	II	Complete	Plans	On Order	In Process	Complete	0	
				Plans	On Order	In Process	Complete	0	
El-Magarba I.H.	BEOC	II	Complete	Complete	On Order		Complete	0	
Tema District			II	100%	25%	0%	0%	100%	0
Tema District Hospital	CEOC	II	Complete	Complete	Partial		Complete	0	
Tema District Hospital	NCU2	II	Complete	Complete	Partial		Complete	0	
Tema District Hospital	CSSD	II	Complete	Plans	On Order		Complete	0	
Tema District Hospital	OR	II	Complete	Plans	On Order		Complete	0	
Tema District Hospital	ER	II	Complete	Plans	0		Complete	0	
Tema U.H.C.	BEOC	II	Complete	Plans	On Order		Complete	0	
Om Doma I.H.	BEOC	II	Complete	Plans	On Order		Complete	0	
El Rayana I.H.	BEOC	II	Complete	Plans	On Order		Complete	0	
El Balyana District			II	100%	40%	0%	0%	100%	0
El Balyana District Hospital	CEOC	II	Complete	Plans	On Order		Complete	0	
El Balyana District Hospital	CSSD	II	Complete	Complete	On Order		Complete	0	
El Balyana District Hospital	OR	II	Complete	Complete	On Order		Complete	0	
Al Sheikh Baraka W.H.U.	BEOC	II	Complete	Plans	On Order		Complete	0	
Al Sheikh Marzouk I.H.U.	BEOC	II	Complete	Plans	On Order		Complete	0	
Dar El-Salam District			II	100%	0%	20%	0%	100%	0
Dar El-Salam District Hospital	CEOC	II	Complete	Plans	On Order		Complete	0	
Dar El-Salam District Hospital	NCU2	II	Complete	Plans	Complete		Complete	0	
Dar El-Salam District Hospital	CSSD	II	Complete	Plans	On Order		Complete	0	
Dar El-Salam District Hospital	OR	II	Complete	Plans	On Order		Complete	0	
Al Naghameesh RHU	BEOC	II	Complete	Plans	On Order		Complete	0	
Saqolta District			II	100%	17%	17%	0%	100%	0
Saqolta District Hospital	CEOC	II	Complete	Plans	On Order		Complete	0	
Saqolta District Hospital	NCU2	II	Complete	Plans	Complete		Complete	0	
Saqolta District Hospital	CSSD	II	Complete	Plans	On Order		Complete	0	
Saqolta District Hospital	OR	II	Complete	Plans	On Order		Complete	0	
Saqolta Maternity	BEOC	II	Complete	Plans	On Order		Complete	0	
Al Galaweyaa I.H.	BEOC	II	Complete	Complete	On Order		Complete	0	
Geheina District			II	100%	80%	20%	0%	100%	0
Geheina District Hospital	CEOC	II	Complete	Complete	On Order		Complete	0	
Geheina District Hospital	NCU2	II	Complete	Complete	Complete		Complete	0	
Geheina District Hospital	CSSD	II	Complete	Complete	On Order		Complete	0	
Geheina District Hospital	OR	II	Complete	Complete	On Order		Complete	0	
Geheina District Hospital	OR	II	Complete	Complete	On Order		Complete	0	
Maragha District Hospital	NCU2	II	Complete	Complete	Complete	In Process	Complete	0	

Governorate District Facility	Type	Phase	Improvement Status					Upgrade Status
			Assessment	Renovation	Commodities	Training	SBC	
Maragha District Hospital	CSSD	II			On Order	In Process		0
Maragha District Hospital	OR	II			On Order	In Process		0
Shandawel LH.	BEOC	II		Plans	On Order			0
El Ghazal L.H.U.	BEOC	II		Plans	On Order			0
Akhmim District								
Akhmim District Hospital	CEOC	II		Plans	On Order			0
Akhmim District Hospital	NCU2	II		Plans				0
Akhmim District Hospital	CSSD	II		Plans	On Order			0
Akhmim District Hospital	OR	II		Plans	On Order			0
Wida LH.	BEOC	II		Plans	On Order			0
Kouba LH.	BEOC	II		Plans	On Order			0
El-Mounshaa District								
El-Mounshaa District Hospital	CEOC	II			On Order			0
El-Mounshaa District Hospital	NCU2	II			On Order			0
El-Mounshaa District Hospital	CSSD	II			On Order			0
El-Mounshaa District Hospital	OR	II			On Order			0
Maternity Center	BEOC	II		Plans	On Order			0
El Zook El Sharke LH.	BEOC	II		Plans	On Order			0
Awlad El Sheikh W.H.U.	BEOC	II		Plans	On Order			0
Awlad Hamza LH.	BEOC	II		Plans	On Order			0

QPMR V		Type	Phase	Improvement Status					Upgrade Status
Governorate	District			Facility	Assessment	Renovation	Commodities	Training	
Menya Governorate				100%	31%	10%	0%	100%	0
Menya District			I	100%	70%	10%	0%	100%	0
Menya General Hospital	CEOC	I	Complete	Complete	On Order	In Process	NA	0	
Menya General Hospital	NCU2	I	Complete	Complete	Complete	In Process	NA	0	
Menya General Hospital	CSSD	I	Complete	Complete	On Order	In Process	NA	0	
Menya General Hospital	OR	I	Complete	Complete	On Order	In Process	NA	0	
Menya General Hospital	ER	I	Complete	Complete	On Order	In Process	NA	0	
Suzan Mubarak Medical Center	BEOC	I	Complete	Complete	On Order	In Process	NA	0	
Damsheer I.H.U.	BEOC	I	Complete	Complete	On Order	In Process	NA	0	
Takas I.H.	BEOC	I	Complete	Construction	On Order	In Process	NA	0	
Tahnash I.H.	BEOC	I	Complete	Construction	On Order	In Process	NA	0	
Tahna Algabal I.H.	BEOC	I	Complete	Construction	On Order	In Process	NA	0	
Samalout District			I	100%	50%	10%	0%	100%	0
Samalout District Hospital	CEOC	I	Complete	Complete	On Order	In Process	NA	0	
Samalout District Hospital	NCU2	I	Complete	Complete	Complete	In Process	NA	0	
Samalout District Hospital	CSSD	I	Complete	Complete	On Order	In Process	NA	0	
Samalout District Hospital	OR	I	Complete	0	On Order	In Process	NA	0	
Samalout District Hospital	ER	I	Complete	Complete	On Order	In Process	NA	0	
Oulouma I.H.	BEOC	I	Complete	Construction	On Order	In Process	NA	0	
Daqoof I.H.	BEOC	I	Complete	Construction	On Order	In Process	NA	0	
El-Saleba I.H.U.	BEOC	I	Complete	Complete	On Order	In Process	NA	0	
Marshaat El-Sheraal I.H.	BEOC	I	Complete	Construction	On Order	In Process	NA	0	
El-Balaho I.H.	BEOC	I	Complete	Construction	On Order	In Process	NA	0	
Fekrya District			II	100%	80%	0%	0%	100%	0
Fekrya District Hospital	CEOC	II	Complete	Complete	On Order	In Process	NA	0	
Fekrya District Hospital	NCU2	II	Complete	Plans	0	In Process	NA	0	
Fekrya District Hospital	CSSD	II	Complete	Complete	On Order	In Process	NA	0	
Fekrya District Hospital	OR	II	Complete	Complete	On Order	In Process	NA	0	
Asmant I.H.U.	BEOC	II	Complete	Complete	On Order	In Process	NA	0	
Deir Mowas District			II	100%	50%	13%	0%	100%	0
Deir Mowas District Hospital	CEOC	II	Complete	Complete	On Order	In Process	NA	0	
Deir Mowas District Hospital	NCU	II	Complete	Bid Process	Complete	In Process	NA	0	
Deir Mowas District Hospital	CSSD	II	Complete	Complete	On Order	In Process	NA	0	
Deir Mowas District Hospital	OR	II	Complete	Complete	On Order	In Process	NA	0	
Suzan Mubarak Urban Health Center	NCU2	II	Complete	Complete	Partial	In Process	NA	0	
Deir Mowas Maternity	BEOC	II	Complete	Plans	On Order	In Process	NA	0	
Nazlat Badarman I.H.	BEOC	II	Complete	Plans	On Order	In Process	NA	0	
Bani Haram I.H.U.	BEOC	II	Complete	Plans	On Order	In Process	NA	0	
Beni Mazar District			II	100%	33%	11%	0%	100%	0
Beni Mazar District Hospital	CEOC	II	Complete	Complete	On Order	In Process	NA	0	
Beni Mazar District Hospital	NCU2	II	Complete	Complete	Complete	In Process	NA	0	
Beni Mazar District Hospital	CSSD	II	Complete	Complete	On Order	In Process	NA	0	
Beni Mazar District Hospital	OR	II	Complete	0	On Order	In Process	NA	0	
Beni Mazar District Hospital	ER	II	Complete	0	0	In Process	NA	0	
Sandafa I.H.	BEOC	II	Complete	0	On Order	In Process	NA	0	
Bani Ali I.H.	BEOC	II	Complete	0	On Order	In Process	NA	0	
Abu Garg W.H.C	BEOC	II	Complete	0	On Order	In Process	NA	0	
El Sheikh Fadl I.H.	BEOC	II	Complete	0	On Order	In Process	NA	0	
Maghagha District			III	100%	0%	25%	0%	100%	0
Maghagha District Hospital	CEOC	III	Complete	Plans	On Order	In Process	NA	0	
Maghagha District Hospital	NCU2	III	Complete	Plans	Complete	In Process	NA	0	
Maghagha District Hospital	CSSD	III	Complete	Plans	On Order	In Process	NA	0	
Maghagha District Hospital	OR	III	Complete	Plans	On Order	In Process	NA	0	
Maghagha District Hospital	ER	III	Complete	Complete	0	In Process	NA	0	
Mattay District			III	100%	0%	0%	0%	100%	0
Mattay District Hospital	CEOC	III	Complete	Plans	On Order	In Process	Complete	0	
Mattay District Hospital	NCU2	III	Complete	Plans	Partial	In Process	NA	0	
Mattay District Hospital	CSSD	III	Complete	Plans	On Order	In Process	NA	0	
El Edwa District			III	100%	0%	0%	0%	100%	0
El Edwa District Hospital	CEOC	III	Complete	Plans	On Order	In Process	Complete	0	

Summary of Upgrade Status of Facilities in Target Districts

QPMR V			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SAC	
El Edwa District Hospital	NCU2	III		Plans	Partial			0
El Edwa District Hospital	CSSD	III		Plans	0			0
El Edwa District Hospital	OR	III		Plans	On Order			0
Mallawi District		III	100%	0%	25%			0
Mallawi District Hospital	CEOC	III		Bid Process	On Order			0
Mallawi District Hospital	NCU2	III		Bid Process		In Process		0
Mallawi District Hospital	CSSD	III		Bid Process	On Order			0
Mallawi District Hospital	OR	III		Bid Process	0			0

Summary of Upgrade Status of Facilities in Target Districts

01/13/2003

QPMR V			Improvement Status					Upgrade Status
Governorate District Facility	Type	Phase	Assessment	Renovation	Commodities	Training	SMC	
Giza Governorate			0%	3%	0%	0%	0%	0
North Giza District			0%	0%	0%	0%	0%	0
El-Tahrir District Hospital	CEOC	IV	0	0	0	0%	0%	0
El-Tahrir District Hospital	NCU2	IV	0	0	On Order		0	0
El Agouza District			0%	0%	0%	0%	0%	0
Embaba General Hospital	CEOC	IV	0	0	0		0	0
Embaba General Hospital	NCU3	IV	0	0	On Order		0	0
El Omrania District			0%	0%	0%	0%	0%	0
El Omrania District Hospital	CEOC	IV	0	0	0	0%	0%	0
South Giza District			0%	50%	0%	0%	0	0
Om El-Masryeen Hospital	CEOC	IV	0	0	0		0%	0
Om El-Masryeen Hospital	NCU2	IV	0	0	On Order		0	0
El-Haram District			0%	0%	0%	0%	0%	0
El-Haram District Hospital	CEOC	IV	0	0	0	0%	0%	0
6th October Hospital	NCU2	IV	0	0	On Order		0	0
Markaz Giza District			0%	0%	0%	0%	0%	0
Markaz Giza District Hospital	CEOC	IV	0	0	0		0	0
Abu El-Nomros Hospital	NCU2	IV	0	0	On Order		0	0
Warak District			0%	0%	0%	0%	0%	0
Warak District Hospital	CEOC	IV	0	0	0	0%	0%	0
Oseim District			0%	0%	0%	0%	0%	0
Oseim District Hospital	CEOC	IV	0	0	0	0%	0%	0
Hawamdeya District			0%	0%	0%	0%	0%	0
Hawamdeya District Hospital	CEOC	IV	0	0	0	0%	0%	0
Hawamdeya District Hospital	NCU2	IV	0	0	On Order		0	0
El Badrashein District			0%	0%	0%	0%	0%	0
El Badrashein District Hospital	CEOC	IV	0	0	0	0%	0%	0
El Badrashein District Hospital	NCU2	IV	0	0	On Order		0	0
El Ayat District			0%	0%	0%	0%	0%	0
El Ayat District Hospital	CEOC	IV	0	0	0	0%	0%	0
El Saff District			0%	0%	0%	0%	0%	0
El Saff District Hospital	CEOC	IV	0	0	0	0%	0%	0
Elfeih District			0%	0%	0%	0%	0%	0
Elfeih District Hospital	CEOC	IV	0	0	0	0%	0%	0
El Wahat Baharia District			0%	0%	0%	0%	0%	0
El Wahat Baharia District Hospital	CEOC	IV	0	0	0	0%	0%	0
El Wahat Baharia District Hospital	NCU2	IV	0	0	On Order		0	0
Menshaat El Qanater District			0%	0%	0%	0%	0%	0
Menshaat El Qanater District Hospital	CEOC	IV	0	0	0	0%	0%	0
El Dokki District			0%	0%	0%	0%	0%	0
El Dokki District Hospital	CEOC	IV	0	0	0	0%	0%	0
Om El-Abtal Hospital	NCU2	IV	0	0	On Order		0	0
Boulaq El Dakroul District			0%	0%	0%	0%	0%	0
Boulaq El Dakroul Hospital	CEOC	IV	0	0	0	0%	0%	0
Boulaq El Dakroul Hospital	NCU2	IV	0	0	On Order		0	0

ANNEX E - SUMMARY OF TRAINING OF PERSONNEL IN TARGET DISTRICTS

QPMR V Governorate District	Phase	Physicians			Nurses			Lead Trainers		
		EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
Target Governorates Total		12	57	69	121	72	193	2	3	5
Qena Governorate			0		6		6			
Qift District					4		4			
Qift District Hospital					3		3			
Qift District Hospital					1		1			
Qift District Hospital										
El-Wakf District					4		4			
El-Wakf District Hospital					3		3			
El-Wakf District Hospital					1		1			
El-Wakf District Hospital										
Fayoum Governorate		4	4	8	23	4	32	2	1	3
Sennoures District					18		18			
Sennoures District Hospital					10		10			
Sennoures District Hospital										
Sennoures District Hospital					8		8			
Sennoures District Hospital										
Maternity Center										
Fedmia District Hospital										
Tamia District		4	4	8	10	4	14	2	1	3
Tamia District Hospital		4		4	5		5	2		2
Tamia District Hospital			4	4		4	4		1	1
Tamia District Hospital					5		5			
Tamia District Hospital										
Maternity Center										
Sarsena LH.U										
Beni Suef Governorate					25		25			
Nasser District					14		14			
Nasser District Hospital					10		10			
Nasser District Hospital										
Nasser District Hospital					4		4			
Nasser District Hospital										
Maternity Center										
Ashmant LH.U										
Somoesta District					11		11			
Somoesta District Hospital					6		6			
Somoesta District Hospital					5		5			
Somoesta District Hospital										
Shantur LH.U										
Dahut LH.U										
Assiut Governorate		8	7	15	22		22			
Gharb Assiut District		5	5	10	5		5			
El-Eman El-Gadida		5		5						
El-Eman El-Gadida			5	5						
El-Eman El-Gadida					5		5			
El-Eman El-Gadida										
El-Eman El-Gadida										
Urban Health Center Alarbaeen										
Shark Assiut District					9		9			
Assiut General Hospital										
Assiut General Hospital										
Assiut General Hospital					9		9			
Assiut General Hospital										
Assiut General Hospital										
Maternity Center - Ahwalidia										
Merkez Assiut District					6		6			
Ob/Gyn Hospital										
Ob/Gyn Hospital										
Ob/Gyn Hospital					6		6			

Summary of Training of Personnel in Target Districts

01/13/2003

QPMR V		Phase	Physicians			Nurses			Lead Trainers		
Governorate	District		EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
	Ob/Gyn Hospital	I									
	Nag-Sabee I.H.	I									
	El-Moteaa I.H.	I									
	El Ghanayem District	II				2		2			
	El Ghanayem District Hospital	II									
	El Ghanayem District Hospital	II									
	El Ghanayem District Hospital	II				2		2			
	El Ghanayem District Hospital	II									
	UHC, Maternity	II									
	El Kouseyah District	II									
	El Kouseyah District Hospital	II									
	El Kouseyah District Hospital	II									
	El Kouseyah District Hospital	II									
	El Kouseyah District Hospital	II									
	El Kouseyah District Hospital	II									
	El Kouseyah Maternity	II									
	Bani Korra W.H.U	II									
	Fazara I.H.	II									
	El Fath District	II	3		3						
	El Fath U.H.C	II									
	El Atawla I.H.	II	3		3						
	El Wasta I.H.	II									
	Sahel Seleem District	III									
	Sahel Seleem District Hospital	III									
	Sahel Seleem District Hospital	III									
	Sahel Seleem District Hospital	III									
	Sahel Seleem District Hospital	III									
	El Badary District	III									
	El Badary District Hospital	III									
	El Badary District Hospital	III									
	El Badary District Hospital	III									
	El Badary District Hospital	III									
	Dayrout District	III									
	Dayrout District Hospital	III									
	Dayrout District Hospital	III									
	Dayrout District Hospital	III									
	Dayrout District Hospital	III									
	Abu Teig District	III									
	Abu Teig District Hospital	III									
	Abu Teig District Hospital	III									
	Abu Teig District Hospital	III									
	Sedfa District	III									
	Sedfa District Hospital	III									
	Sedfa District Hospital	III									
	Sedfa District Hospital	III									
	Sedfa District Hospital	III									
	Manfalout District	III		2	2						
	Manfalout District Hospital	III									
	Manfalout District Hospital	III		2	2						
	Manfalout District Hospital	III									
	Manfalout District Hospital	III									
	Abnoub District	III									
	Abnoub District Hospital	III									
	Abnoub District Hospital	III									
	Abnoub District Hospital	III									
	Sohag Governorate					12		12			
	Sohag District	I				4		4			
	Sohag General Hospital	I									
	Sohag General Hospital	I									
	Sohag General Hospital	I				4		4			
	Sohag General Hospital	I									

QPMR V Governorate District	Phase	Physicians			Nurses			Lead Trainers		
		EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
Sohag General Hospital	I									
Gezirat Shanawel LH.	I									
Balsofora LH.	I									
Tanta District	II				3		3			
Tanta District Hospital	II									
Tanta District Hospital	II									
Tanta District Hospital	II				3		3			
Tanta District Hospital	II									
Tanta District Hospital	II									
Tanta Maternity Center	II									
Shaturaa LH.U.	II									
El-Swanina LH.	II									
Gerga District	II				3		3			
Gerga District Hospital	II									
Gerga District Hospital	II									
Gerga District Hospital	II				3		3			
Gerga District Hospital	II									
El-Magarba LH.	II									
Tema District	II									
Tema District Hospital	II									
Tema District Hospital	II									
Tema District Hospital	II									
Tema District Hospital	II									
Tema District Hospital	II									
Tema U.H.C.	II									
Om Doma LH.	II									
El Rayana LH.	II									
El Balyana District	II									
El Balyana District Hospital	II									
El Balyana District Hospital	II									
El Balyana District Hospital	II									
Al Sheikh Baraka W.H.U	II									
Al Sheikh Marzouk LH.U	II									
Dar El-Salam District	II									
Dar El-Salam District Hospital	II									
Dar El-Salam District Hospital	II									
Dar El-Salam District Hospital	II									
Dar El-Salam District Hospital	II									
Al Naghameesh RHU	II									
Saqofa District	II									
Saqofa District Hospital	II									
Saqofa District Hospital	II									
Saqofa District Hospital	II									
Saqofa District Hospital	II									
Saqofa Maternity	II									
Al Galaweyaa LH	II									
Geheina District	II									
Geheina District Hospital	II									
Geheina District Hospital	II									
Geheina District Hospital	II									
Geheina District Hospital	II									
Enelbis LH	II									
Maragha District	II				2		2			
Maragha District Hospital	II									
Maragha District Hospital	II									
Maragha District Hospital	II				2		2			
Maragha District Hospital	II									
Shandawel LH.	II									
El Gherizat LH.U.	II									
Akhmeim District	II									
Akhmeim District Hospital	II									

QPMR V Governorate District	Phase	Physicians			Nurses			Lead Trainers		
		EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
Akhmeim District Hospital	II									
Akhmeim District Hospital	II									
Akhmeim District Hospital	II									
Nida I.H.	II									
Koalla I.H.	II									
El-Mounshaa District	II									
El-Mounshaa District Hospital	II									
El-Mounshaa District Hospital	II									
El-Mounshaa District Hospital	II									
El-Mounshaa District Hospital	II									
Maternity Center	II									
El Zook El Sharkis I.H.	II									
Awlad El Sheikh W.H.U	II									
Awlad Hamza I.H.	II									
Menya Governorate			7	7	26	3	29			
Menya District	I				18		18			
Menya General Hospital	I									
Menya General Hospital	I				18		18			
Menya General Hospital	I									
Menya General Hospital	I									
Menya General Hospital	I									
Suzan Mubarak Medical Center	I									
Damsheer I.H.U.	I									
Talaa I.H.	I									
Tahnash I.H.	I									
Tahna Algabal I.H.	I									
Samalout District	I				4		4			
Samalout District Hospital	I									
Samalout District Hospital	I									
Samalout District Hospital	I				4		4			
Samalout District Hospital	I									
Samalout District Hospital	I									
Quloana I.H.	I									
Dagoof I.H.	I									
El-Saleba I.H.U.	I									
Mansheat El-Sheraai I.H.	I									
El-Balaho I.H	I									
Fekrya District	II				4		4			
Fekrya District Hospital	II									
Fekrya District Hospital	II									
Fekrya District Hospital	II				4		4			
Fekrya District Hospital	II									
Asmant I.H.U.	II									
Deir Mowas District	II		7	7		3	3			
Deir Mowas District Hospital	II									
Deir Mowas District Hospital	II									
Deir Mowas District Hospital	II									
Deir Mowas District Hospital	II									
Suzan Mubarak Urban Health Center	II		7	7		3	3			
Deir Mowas Maternity	II									
Naziat Badarman I.H.	II									
Bani Haram I.H.U	II									
Beni Mazar District	II									
Beni Mazar District Hospital	II									
Beni Mazar District Hospital	II									
Beni Mazar District Hospital	II									
Beni Mazar District Hospital	II									
Beni Mazar District Hospital	II									
Sandafa I.H	II									
Bani Ali I.H	II									
Abu Garg W.H.C	II									

QPMR V		Physicians			Nurses			Lead Trainers		
Governorate	Phase	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
El Sheikh Fadi LH	II									
Maghagha District	III									
Maghagha District Hospital	III									
Maghagha District Hospital	III									
Maghagha District Hospital	III									
Maghagha District Hospital	III									
Maghagha District Hospital	III									
Mattay District	III									
Mattay District Hospital	III									
Mattay District Hospital	III									
Mattay District Hospital	III									
Mattay District Hospital	III									
El Edwa District	III									
El Edwa District Hospital	III									
El Edwa District Hospital	III									
El Edwa District Hospital	III									
El Edwa District Hospital	III									
Mallawi District	III									
Mallawi District Hospital	III									
Mallawi District Hospital	III									
Mallawi District Hospital	III									
Mallawi District Hospital	III									
Giza Governorate			39	39		65	65		2	2
North Giza District	IV		5	5		10	10			
El-Tahrir District Hospital	IV									
El-Tahrir District Hospital	IV		5	5		10	10			
El Agouza District	IV		8	8		15	15			
Embaba General Hospital	IV									
Embaba General Hospital	IV		8	8		15	15			
El Omrania District	IV									
El Omrania District Hospital	IV									
South Giza District	IV		8	8		11	11			
Om El-Masryeen Hospital	IV									
Om El-Masryeen Hospital	IV		8	8		11	11			
El-Haram District	IV									
El-Haram District Hospital	IV									
6th October Hospital	IV					2	2			
Markaz Giza District	IV		7	7		8	8			
Markaz Giza District Hospital	IV									
Abu El-Nomros Hospital	IV		7	7		8	8			
Warak District	IV									
Warak District Hospital	IV									
Oseim District	IV									
Oseim District Hospital	IV									
Hawamdeya District	IV		5	5		12	12			
Hawamdeya District Hospital	IV									
Hawamdeya District Hospital	IV		5	5		12	12			
El Badrashain District	IV									
El Badrashain District Hospital	IV									
El Badrashain District Hospital	IV									
El Ayat District	IV									
El Ayat District Hospital	IV									
El Saff District	IV									
El Saff District Hospital	IV									
Elfeih District	IV									
Elfeih District Hospital	IV									
El Wahat Baharia District	IV					2	2			
El Wahat Baharia District Hospital	IV									
El Wahat Baharia District Hospital	IV					2	2			
Menshaat El Qanater District	IV									
Menshaat El Qanater District Hospital	IV									

Summary of Training of Personnel in Target Districts

01/13/2003

QPMR V		Physicians			Nurses			Lead Trainers		
Governorate District	Phase	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total	EOC Training	Neonatal Training	Total
		El Dokki District	IV							
El Dokki District Hospital	IV									
Om El-Abtal Hospital	IV									
Boulaq El Dakroul District	IV		6	6		7	7		2	2
Boulaq El Dakroul Hospital	IV									
Boulak El Dakroul Hospital	IV		6	6		7	7		2	2

**ANNEX F - SUMMARY OF MANAGEMENT IMPROVEMENT
ACTIVITIES AT DISTRICT LEVEL**

QPMR V	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Target Governorates Total		36	33	15	227	231	113	16			15				132
Qena Governorate		2	2	2	30	32	22	2			2				6
Qena District		1	Yes	Yes	15	15	11	1		Yes				Yes	4
Qena District Hospital		1	Yes												
Qena District Hospital		1	NA												
Qena District Hospital		1	NA												
El-Wafd District		1	Yes	Yes	15	17	11	1		Yes				Yes	4
El-Wafd District Hospital		1	Yes												
El-Wafd District Hospital		1	NA												
El-Wafd District Hospital		1	NA												
Fayoum Governorate		2	2	2	30	34	20	2			2			2	9
Sennoures District		1	Yes	Yes	14	16	10	1		Yes				Yes	4
Sennoures District Hospital		1	Yes												
Sennoures District Hospital		1	NA												
Sennoures District Hospital		1	NA												
Sennoures District Hospital		1	NA												
Maternity Center		1	NA												
Fedain District Hospital		1	NA												
Tamia District		1	Yes	Yes	16	18	10	1		Yes				Yes	5
Tamia District Hospital		1	Yes												
Tamia District Hospital		1	NA												
Tamia District Hospital		1	NA												
Tamia District Hospital		1	NA												
Maternity Center		1	NA												
Sersena L.H.U		1	NA												
Beni Suef Governorate		2	2	2	30	40	15	2			2			2	8
Nasser District		1	Yes	Yes	12	20	6	1		Yes				Yes	4
Nasser District Hospital		1	Yes												
Nasser District Hospital		1	NA												
Nasser District Hospital		1	NA												
Nasser District Hospital		1	NA												
Maternity Center		1	NA												
Ashmant L.H.U		1	NA												
Somoeta District		1	Yes	Yes	18	20	6	1		Yes				Yes	4
Somoeta District Hospital		1	Yes												
Somoeta District Hospital		1	NA												
Somoeta District Hospital		1	NA												
Shanbar L.H.U		1	NA												
Dahut L.H.U		1	NA												
Assiut Governorate		12	13	3	33	55	15	3			3			11	45
Gharb Assiut District		1	Yes	Yes	11	25	5	1		Yes				Yes	4
El-Eman El-Gadida		1	Yes												
El-Eman El-Gadida		1	NA												
El-Eman El-Gadida		1	NA												
El-Eman El-Gadida		1	NA												
El-Eman El-Gadida		1	NA												
Urban Health Center Alarbaeen		1	NA												
Shark Assiut District		1	Yes	Yes	12	15	5	1		Yes				Yes	4
Assiut General Hospital		1	Yes												
Assiut General Hospital		1	NA												
Assiut General Hospital		1	NA												
Assiut General Hospital		1	NA												
Assiut General Hospital		1	NA												
Maternity Center - Alwalidia		1	NA												
Markaz Assiut District		1	Yes	Yes	15	15	5	1		Yes				Yes	6

Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Ob/Gyn Hospital	I	Yes													
Ob/Gyn Hospital	I	NA													
Ob/Gyn Hospital	I	NA													
Ob/Gyn Hospital	I	NA													
Nag-Sabee I.H.	I	NA													
El-Moteaa I.H.	I	NA													
El Ghanayem District	II	1	Yes										Yes	4	
El Ghanayem District Hospital	II	Yes													
El Ghanayem District Hospital	II	NA													
El Ghanayem District Hospital	II	NA													
El Ghanayem District Hospital	II	NA													
UHC, Maternity	II	NA													
El Kouseyah District	II	1	Yes										Yes	4	
El Kouseyah District Hospital	II	Yes													
El Kouseyah District Hospital	II	NA													
El Kouseyah District Hospital	II	NA													
El Kouseyah District Hospital	II	NA													
El Kouseyah District Hospital	II	NA													
El Kouseyah Maternity	II	NA													
Bani Korra W.H.U	II	NA													
Fazara I.H.	II	NA													
El Fath District	II		Yes												
El Fath U.H.C	II	NA													
El Atawla I.H.	II	NA													
El Wasta I.H.	II	NA													
Sahel Seleem District	III	1	Yes										Yes	4	
Sahel Seleem District Hospital	III	Yes													
Sahel Seleem District Hospital	III	NA													
Sahel Seleem District Hospital	III	NA													
Sahel Seleem District Hospital	III	NA													
El Badary District	III	1	Yes										Yes	4	
El Badary District Hospital	III	Yes													
El Badary District Hospital	III	NA													
El Badary District Hospital	III	NA													
El Badary District Hospital	III	NA													
Dayrout District	III	1	Yes												
Dayrout District Hospital	III	Yes													
Dayrout District Hospital	III	NA													
Dayrout District Hospital	III	NA													
Dayrout District Hospital	III	NA													
Abu Teig District	III	1	Yes										Yes	4	
Abu Teig District Hospital	III	Yes													
Abu Teig District Hospital	III	NA													
Abu Teig District Hospital	III	NA													
Sedfa District	III	1	Yes										Yes	4	
Sedfa District Hospital	III	Yes													
Sedfa District Hospital	III	NA													
Sedfa District Hospital	III	NA													
Sedfa District Hospital	III	NA													
Manfalout District	III	1	Yes										Yes	4	
Manfalout District Hospital	III	Yes													
Manfalout District Hospital	III	NA													
Manfalout District Hospital	III	NA													
Manfalout District Hospital	III	NA													
Abnoub District	III	1	Yes										Yes	4	
Abnoub District Hospital	III	Yes													

QPMR V	Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
										2001	2002	2003	2004	2005		
	Abouab District Hospital	III	NA													
	Abouab District Hospital	III	NA													
	Sohag Governorate		11	11	3	65	69	24	6		3			11	13	
	Sohag District	I	1	Yes	Yes	20	20	8	2		Yes			Yes	8	
	Sohag General Hospital	I	Yes													
	Sohag General Hospital	I	NA													
	Sohag General Hospital	I	NA													
	Sohag General Hospital	I	NA													
	Sohag General Hospital	I	NA													
	Generat Shanawel LH.	I	NA													
	Baleofora LH.	I	NA													
	Tanta District	II	1	Yes	Yes	20	20	8	2		Yes			Yes	4	
	Tanta District Hospital	II	Yes													
	Tanta District Hospital	II	NA													
	Tanta District Hospital	II	NA													
	Tanta District Hospital	II	NA													
	Tanta District Hospital	II	NA													
	Tanta Maternity Center	II	NA													
	Shataras L.H.U.	II	NA													
	El-Swanma LH.	II	NA													
	Gerga District	II	1	Yes	Yes	18	22	8	2		Yes			Yes	4	
	Gerga District Hospital	II	Yes													
	Gerga District Hospital	II	NA													
	Gerga District Hospital	II	NA													
	Gerga District Hospital	II	NA													
	El-Magarba LH.	II	NA													
	Tema District	II	1	Yes												
	Tema District Hospital	II	Yes													
	Tema District Hospital	II	NA													
	Tema District Hospital	II	NA													
	Tema District Hospital	II	NA													
	Tema District Hospital	II	NA													
	Tema U.H.C.	II	NA													
	Om Doma LH.	II	NA													
	El Rayana LH.	II	NA													
	El Balyana District	II	1	Yes										Yes	4	
	El Balyana District Hospital	II	Yes													
	El Balyana District Hospital	II	NA													
	El Balyana District Hospital	II	NA													
	Al Sheikh Baraka W.H.U	II	NA													
	Al Sheikh Marzouk L.H.U	II	NA													
	Dar El-Salam District	II	1	Yes										Yes	4	
	Dar El-Salam District Hospital	II	Yes													
	Dar El-Salam District Hospital	II	NA													
	Dar El-Salam District Hospital	II	NA													
	Dar El-Salam District Hospital	II	NA													
	Al Noghameesh RHU	II	NA													
	Saqolta District	II	1	Yes										Yes	4	
	Saqolta District Hospital	II	Yes													
	Saqolta District Hospital	II	NA													
	Saqolta District Hospital	II	NA													
	Saqolta District Hospital	II	NA													
	Saqolta Maternity	II	NA													
	Al Galawyyaa LH	II	NA													
	Gehelna District	II	1	Yes			7							Yes	4	
	Gehelna District Hospital	II	Yes													

QPMR V	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Geheina District Hospital	II	NA													
Geheina District Hospital	II	NA													
Geheina District Hospital	II	NA													
Enebis I.H	II	NA													
Maragha District	II	1	Yes										Yes	4	
Maragha District Hospital	II	Yes													
Maragha District Hospital	II	NA													
Maragha District Hospital	II	NA													
Maragha District Hospital	II	NA													
Shandaweel I.H.	II	NA													
EI Gherizat I.H.U.	II	NA													
Akhmeim District	II	1	Yes		7								Yes	4	
Akhmeim District Hospital	II	Yes													
Akhmeim District Hospital	II	NA													
Akhmeim District Hospital	II	NA													
Akhmeim District Hospital	II	NA													
Nida I.H.	II	NA													
Koalla I.H.	II	NA													
El-Mounshaa District	II	1	Yes										Yes	5	
El-Mounshaa District Hospital	II	Yes													
El-Mounshaa District Hospital	II	NA													
El-Mounshaa District Hospital	II	NA													
El-Mounshaa District Hospital	II	NA													
Maternity Center	II	NA													
EI Zook EI Sharkis I.H.	II	NA													
Awlad EI Sheikh W.H.U	II	NA													
Awlad Hamza I.H.	II	NA													
Menya Governorate		9	9	3	34	60	16	3			3		9	38	
Menya District	I	1	Yes	Yes	11	20	5	1		Yes			Yes	6	
Menya General Hospital	I	Yes													
Menya General Hospital	I	NA													
Menya General Hospital	I	NA													
Menya General Hospital	I	NA													
Suzan Mubarak Medical Center	I	NA													
Damsheer I.H.U.	I	NA													
Talaa I.H.	I	NA													
Tahnash I.H.	I	NA													
Tahna Algabal I.H.	I	NA													
Samalout District	I	1	Yes	Yes	11	20	5	1		Yes			Yes	4	
Samalout District Hospital	I	Yes													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Samalout District Hospital	I	NA													
Quloana I.H.	I	NA													
Daqoof I.H.	I	NA													
EI-Safeba I.H.U.	I	NA													
Mansheat EI-Sheraai I.H.	I	NA													
EI-Baiaho I.H	I	NA													
Fekrya District	II	1	Yes	Yes	12	20	6	1		Yes			Yes	4	
Fekrya District Hospital	II	Yes													
Fekrya District Hospital	II	NA													
Fekrya District Hospital	II	NA													
Fekrya District Hospital	II	NA													
Asmant I.H.U.	II	NA													

QPMR V	Governorate District	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DHC Established	DHC Staff Trained
										2001	2002	2003	2004	2005		
Deir Mowas District																
	Deir Mowas District	II	1	Yes											Yes	4
	Deir Mowas District Hospital	II	Yes													
	Deir Mowas District Hospital	II	NA													
	Deir Mowas District Hospital	II	NA													
	Deir Mowas District Hospital	II	NA													
	Suzan Mubarak Urban Health Center	II	NA													
	Deir Mowas Maternity	II	NA													
	Nazhat Baderman LH	II	NA													
	Beni Haram LHU	II	NA													
Beni Mazar District																
	Beni Mazar District	II	1	Yes											Yes	4
	Beni Mazar District Hospital	II	Yes													
	Beni Mazar District Hospital	II	NA													
	Beni Mazar District Hospital	II	NA													
	Beni Mazar District Hospital	II	NA													
	Beni Mazar District Hospital	II	NA													
	Sandafa LH	II	NA													
	Beni Ali LH	II	NA													
	Abu Garg W.H.C	II	NA													
	El Sheikh Fadi LH	II	NA													
Maghagha District																
	Maghagha District	III	1	Yes											Yes	4
	Maghagha District Hospital	III	Yes													
	Maghagha District Hospital	III	NA													
	Maghagha District Hospital	III	NA													
	Maghagha District Hospital	III	NA													
	Maghagha District Hospital	III	NA													
Matay District																
	Matay District	III	1	Yes											Yes	4
	Matay District Hospital	III	Yes													
	Matay District Hospital	III	NA													
	Matay District Hospital	III	NA													
	Matay District Hospital	III	NA													
El Edwa District																
	El Edwa District	III	1	Yes											Yes	4
	El Edwa District Hospital	III	Yes													
	El Edwa District Hospital	III	NA													
	El Edwa District Hospital	III	NA													
	El Edwa District Hospital	III	NA													
Mallawi District																
	Mallawi District	III	1	Yes											Yes	4
	Mallawi District Hospital	III	Yes													
	Mallawi District Hospital	III	NA													
	Mallawi District Hospital	III	NA													
	Mallawi District Hospital	III	NA													
Giza Governorate																
North Giza District																
	North Giza District	IV													Yes	4
	El-Tahrir District Hospital	IV														
	El-Tahrir District Hospital	IV	NA													
	El Agouza District	IV													Yes	4
	Embaba General Hospital	IV														
	Embaba General Hospital	IV	NA													
	El Omrania District	IV													Yes	4
	El Omrania District Hospital	IV														
South Giza District																
	South Giza District	IV													Yes	4
	Om El-Masryeen Hospital	IV														
	Om El-Masryeen Hospital	IV	NA													
El-Haram District																
	El-Haram District	IV													Yes	4
	El-Haram District Hospital	IV														
	6th October Hospital	IV	NA													
Markaz Giza District																
	Markaz Giza District	IV													Yes	4

QPMR V	Phase	FSMC Established & Trained	DSMC Established	DHC Established	DSMC Members Trained	DHC Members Oriented	DSMC Meetings	DSMC/DHC Joint Meetings	Annual District Health Plan Developed					DIC Established	DIC Staff Trained
									2001	2002	2003	2004	2005		
Markaz Giza District Hospital	IV														
Abu El-Nomros Hospital	IV	NA													
Warak District	IV												Yes	4	
Warak District Hospital	IV														
Oseim District	IV												No	4	
Oseim District Hospital	IV														
Hawamdeya District	IV												No	4	
Hawamdeya District Hospital	IV	NA													
El Badrashein District	IV												Yes	4	
El Badrashein District Hospital	IV														
El Badrashein District Hospital	IV	NA													
El Ayat District	IV												Yes	4	
El Ayat District Hospital	IV														
El Saff District	IV												No	4	
El Saff District Hospital	IV														
Elfeih District	IV												No	4	
Elfeih District Hospital	IV														
El Wahat Baharia District	IV												No	4	
El Wahat Baharia District Hospital	IV														
El Wahat Baharia District Hospital	IV	NA													
Menshaat El Qanater District	IV												No	4	
Menshaat El Qanater District Hospital	IV														
El Dokki District	IV												No	4	
El Dokki District Hospital	IV														
Om El-Abtal Hospital	IV	NA													
Boulaq El Dakrour District	IV												Yes	4	
Boulaq El Dakrour Hospital	IV														
Boulaq El Dakrour Hospital	IV	NA													

ANNEX G - SUMMARY OF MANAGEMENT IMPROVEMENT ACTIVITIES AT GOVERNORATE LEVEL

QPMR V		No. of Districts	GSMC Established & Trained	GHC Established & Oriented	GSMC Meetings	Joint GSMC/GHC Meetings	GSMC Members Trained	GHC Members Oriented	Governorate Information Center Upgraded
Governorate									
Totals		56	6	6	42	8	80	79	6
Qena		2	Yes	Yes	11	2	14	7	Yes
Fayoum		2	Yes	Yes	9	2	16	16	Yes
Beni Suef		2	Yes	Yes	6	1	10	10	Yes
Assiut		13	Yes	Yes	5	1	14	16	Yes
Sohag		11	Yes	Yes	7	1	14	12	Yes
Menya		9	Yes	Yes	4	1	12	18	Yes
Giza		17							

ANNEX H - STATUS OF COMMUNITY LEVEL ACTIVITIES

QPMR V		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Target Governorates Total				100	40	39	35
Qena Governorate				6	2	2	2
Q ft District				3	1	1	1
Qft District Hospital		CEOC	1	Yes	Yes	Yes	Yes
Qft District Hospital		CSSD	1	Yes	NA	NA	NA
Qft District Hospital		OR	1	Yes	NA	NA	NA
El-Wakf District				3	1	1	1
El-Wakf District Hospital		CEOC	1	Yes	Yes	Yes	Yes
El-Wakf District Hospital		CSSD	1	Yes	NA	NA	NA
El-Wakf District Hospital		OR	1	Yes	NA	NA	NA

Status of Community Level Activities

01/13/2003

QPMR V						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Fayoum Governorate						
Sennoures District						
Sennoures District Hospital	CEOC	I	6	2	2	2
Sennoures District Hospital	NICU2	I	Yes	NA	NA	NA
Sennoures District Hospital	CSSD	I	Yes	NA	NA	NA
Sennoures District Hospital	OR	I	Yes	NA	NA	NA
Maternity Center	BEOC	I	Yes	Yes	Yes	Yes
Fedmin District Hospital	BEOC	I	Yes	Yes	Yes	Yes
Tamia District						
Tamia District Hospital	CEOC	I	6	2	2	2
Tamia District Hospital	NCU2	I	Yes	NA	NA	NA
Tamia District Hospital	CSSD	I	Yes	NA	NA	NA
Tamia District Hospital	OR	I	Yes	NA	NA	NA
Maternity Center	BEOC	I	Yes	Yes	Yes	Yes
Sersena I.H.U	BEOC	I	Yes	Yes	Yes	Yes

QPMR V		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Beni Suef Governorate				11	4	4	4
Nasser District			1	6	2	2	2
Nasser District Hospital	CEOC	1		Yes	NA	NA	NA
Nasser District Hospital	NCU2	1		Yes	NA	NA	NA
Nasser District Hospital	CSSD	1		Yes	NA	NA	NA
Nasser District Hospital	OR	1		Yes	NA	NA	NA
Maternity Center	BEOC	1		Yes	Yes	Yes	Yes
Ashmant L.H.U	BEOC	1		Yes	Yes	Yes	Yes
Somosta District			1	5	2	2	2
Somosta District Hospital	CEOC	1		Yes	NA	NA	NA
Somosta District Hospital	CSSD	1		Yes	NA	NA	NA
Somosta District Hospital	OR	1		Yes	NA	NA	NA
Shanbur L.H.U	BEOC	1		Yes	Yes	Yes	Yes
Dshkut L.H.U	BEOC	1		Yes	Yes	Yes	Yes

QPMR V						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Assiut Governorate						
Gharb Assiut District						
		I	6	1	1	4
El-Eman El-Gadida	CEOC	I	Yes	NA	NA	1
El-Eman El-Gadida	NCU2	I	Yes	NA	NA	NA
El-Eman El-Gadida	CSSD	I	Yes	NA	NA	NA
El-Eman El-Gadida	OR	I	Yes	NA	NA	NA
El-Eman El-Gadida	ER	I	Yes	NA	NA	NA
Urban Health Center Alarbaeen	BEOC	I	Yes	Yes	Yes	Yes
Shark Assiut District						
		I	6	1	1	1
Assiut General Hospital	CEOC	I	Yes	NA	NA	NA
Assiut General Hospital	NCU2	I	Yes	NA	NA	NA
Assiut General Hospital	CSSD	I	Yes	NA	NA	NA
Assiut General Hospital	OR	I	Yes	NA	NA	NA
Assiut General Hospital	ER	I	Yes	NA	NA	NA
Maternity Center - Alwalidia	BEOC	I	Yes	Yes	Yes	Yes
Markaz Assiut District						
		I	6	2	2	2
Ob/Gyn Hospital	CEOC	I	Yes	NA	NA	NA
Ob/Gyn Hospital	NICU	I	Yes	NA	NA	NA
Ob/Gyn Hospital	CSSD	I	Yes	NA	NA	NA
Ob/Gyn Hospital	OR	I	Yes	NA	NA	NA
Nag-Sabee I.H.	BEOC	I	Yes	Yes	Yes	Yes
El-Moteaa I.H.	BEOC	I	Yes	Yes	Yes	Yes
El Ghanayem District						
		II				
El Ghanayem District Hospital	CEOC	II		NA	NA	NA
El Ghanayem District Hospital	NCU2	II		NA	NA	NA
El Ghanayem District Hospital	CSSD	II		NA	NA	NA
El Ghanayem District Hospital	OR	II		NA	NA	NA
UHC, Maternity	BEOC	II				
El Kouseyah District						
		II				
El Kouseyah District Hospital	CEOC	II		NA	NA	NA
El Kouseyah District Hospital	NCU2	II		NA	NA	NA
El Kouseyah District Hospital	CSSD	II		NA	NA	NA
El Kouseyah District Hospital	OR	II		NA	NA	NA
El Kouseyah District Hospital	ER	II		NA	NA	NA
El Kouseyah Maternity	BEOC	II				
Bani Korra W.H.U	BEOC	II				
Fazara I.H.	BEOC	II				
El Fath District						
		II		3	2	
El Fath U.H.C	BEOC	II		Yes	Yes	
El Atawia I.H.	BEOC	II		Yes		
El Wasta I.H.	BEOC	II		Yes	Yes	
Sahel Seleem District						
		III				
Sahel Seleem District Hospital	CEOC	III		NA	NA	NA
Sahel Seleem District Hospital	NCU2	III		NA	NA	NA
Sahel Seleem District Hospital	CSSD	III		NA	NA	NA
Sahel Seleem District Hospital	OR	III		NA	NA	NA
El Badary District						
		III				
El Badary District Hospital	CEOC	III		NA	NA	NA
El Badary District Hospital	NCU2	III		NA	NA	NA
El Badary District Hospital	CSSD	III		NA	NA	NA
El Badary District Hospital	OR	III		NA	NA	NA
Dayrout District						
		III				
Dayrout District Hospital	CEOC	III		NA	NA	NA
Dayrout District Hospital	NCU2	III		NA	NA	NA
Dayrout District Hospital	CSSD	III		NA	NA	NA
Dayrout District Hospital	OR	III		NA	NA	NA
Abu Teig District						
		III				
Abu Teig District Hospital	CEOC	III		NA	NA	NA
Abu Teig District Hospital	CSSD	III		NA	NA	NA
Abu Teig District Hospital	OR	III		NA	NA	NA

QPMR V		Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Governorate	District Facility						
Sedfa District			III				
	Sedfa District Hospital	CEOC	III		NA	NA	NA
	Sedfa District Hospital	NCU2	III		NA	NA	NA
	Sedfa District Hospital	CSSD	III		NA	NA	NA
	Sedfa District Hospital	OR	III		NA	NA	NA
Mansafout District			III				
	Mansafout District Hospital	CEOC	III		NA	NA	NA
	Mansafout District Hospital	NCU2	III		NA	NA	NA
	Mansafout District Hospital	CSSD	III		NA	NA	NA
	Mansafout District Hospital	OR	III		NA	NA	NA
Abnoub District			III				
	Abnoub District Hospital	CEOC	III		NA	NA	NA
	Abnoub District Hospital	CSSD	III		NA	NA	NA
	Abnoub District Hospital	OR	III		NA	NA	NA

QPMR V						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Sohag Governorate			28	10	10	8
Sohag District			7	2	2	2
Sohag General Hospital	CEOC	I	Yes	NA	NA	NA
Sohag General Hospital	NCU2	I	Yes	NA	NA	NA
Sohag General Hospital	CSSD	I	Yes	NA	NA	NA
Sohag General Hospital	OR	I	Yes	NA	NA	NA
Sohag General Hospital	ER	I	Yes	NA	NA	NA
Gezerat Shanawael I.H.	BEOC	I	Yes	Yes	Yes	Yes
Balsofora I.H.	BEOC	I	Yes	Yes	Yes	Yes
Tahta District			8	3	3	3
Tahta District Hospital	CEOC	II	Yes	NA	NA	NA
Tahta District Hospital	NCU2	II	Yes	NA	NA	NA
Tahta District Hospital	CSSD	II	Yes	NA	NA	NA
Tahta District Hospital	OR	II	Yes	NA	NA	NA
Tahta District Hospital	ER	II	Yes	NA	NA	NA
Tahta Maternity Center	BEOC	II	Yes	Yes	Yes	Yes
Shaturaa I.H.U.	BEOC	II	Yes	Yes	Yes	Yes
El-Swamna I.H.	BEOC	II	Yes	Yes	Yes	Yes
Gerga District			5	1	1	1
Gerga District Hospital	CEOC	II	Yes	NA	NA	NA
Gerga District Hospital	NCU2	II	Yes	NA	NA	NA
Gerga District Hospital	CSSD	II	Yes	NA	NA	NA
Gerga District Hospital	OR	II	Yes	NA	NA	NA
El-Magarba I.H.	BEOC	II	Yes	Yes	Yes	Yes
Tema District						
Tema District Hospital	CEOC	II		NA	NA	NA
Tema District Hospital	NCU2	II		NA	NA	NA
Tema District Hospital	CSSD	II		NA	NA	NA
Tema District Hospital	OR	II		NA	NA	NA
Tema District Hospital	ER	II		NA	NA	NA
Tema U.H.C.	BEOC	II				
Om Doma I.H.	BEOC	II				
El Rayana I.H.	BEOC	II				
El Balyana District						
El Balyana District Hospital	CEOC	II		NA	NA	NA
El Balyana District Hospital	CSSD	II		NA	NA	NA
El Balyana District Hospital	OR	II		NA	NA	NA
Al Sheikh Baraka W.H.U	BEOC	II				
Al Sheikh Marzouk I.H.U	BEOC	II				
Dar El-Salam District						
Dar El-Salam District Hospital	CEOC	II		NA	NA	NA
Dar El-Salam District Hospital	NCU2	II		NA	NA	NA
Dar El-Salam District Hospital	CSSD	II		NA	NA	NA
Dar El-Salam District Hospital	OR	II		NA	NA	NA
Al Naghameesh RHU	BEOC	II				
Saqolta District						
Saqolta District Hospital	CEOC	II		NA	NA	NA
Saqolta District Hospital	NCU2	II		NA	NA	NA
Saqolta District Hospital	CSSD	II		NA	NA	NA
Saqolta District Hospital	OR	II		NA	NA	NA
Saqolta Maternity	BEOC	II				
Al Galaweyaa I.H	BEOC	II				
Geheina District			2			
Geheina District Hospital	CEOC	II		NA	NA	NA
Geheina District Hospital	NCU2	II		NA	NA	NA
Geheina District Hospital	CSSD	II		NA	NA	NA
Geheina District Hospital	OR	II	Yes	NA	NA	NA
Enails I.H	BEOC	II	Yes			
Maragha District				2	2	
Maragha District Hospital	CEOC	II		NA	NA	NA

QPMR V						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Maragha District Hospital	NCU	II		NA	NA	NA
Maragha District Hospital	CSSD	II		NA	NA	NA
Maragha District Hospital	OR	II		NA	NA	NA
Shandawel I.H.	BEOC	II		Yes	Yes	
EI Gharzal L.H.U.	BEOC	II		Yes	Yes	
Akhmeim District		II	6	2	2	2
Akhmeim District Hospital	CEOC	II	Yes	NA	NA	NA
Akhmeim District Hospital	NCU2	II	Yes	NA	NA	NA
Akhmeim District Hospital	CSSD	II	Yes	NA	NA	NA
Akhmeim District Hospital	OR	II	Yes	NA	NA	NA
Nida I.H.	BEOC	II	Yes	Yes	Yes	Yes
Koalla I.H.	BEOC	II	Yes	Yes	Yes	Yes
EI-Mounshaa District		II				
EI-Mounshaa District Hospital	CEOC	II		NA	NA	NA
EI-Mounshaa District Hospital	NCU2	II		NA	NA	NA
EI-Mounshaa District Hospital	CSSD	II		NA	NA	NA
EI-Mounshaa District Hospital	OR	II		NA	NA	NA
Maternity Center	BEOC	II				
EI Zook EI Sharhis I.H.	BEOC	II				
Awlad EI Sheikh W.H.U	BEOC	II				
Awlad Hamza I.H.	BEOC	II				

QPMR V						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Menya Governorate						
Menya District						
		I	10	5	5	5
Menya General Hospital	CEOC	I	Yes	NA	NA	NA
Menya General Hospital	NCU2	I	Yes	NA	NA	NA
Menya General Hospital	CSSD	I	Yes	NA	NA	NA
Menya General Hospital	OR	I	Yes	NA	NA	NA
Menya General Hospital	ER	I	Yes	NA	NA	NA
Suzan Mubarak Medical Center	BEOC	I	Yes	Yes	Yes	Yes
Damsher I.H.U.	BEOC	I	Yes	Yes	Yes	Yes
Talaa I.H.	BEOC	I	Yes	Yes	Yes	Yes
Tahnash I.H.	BEOC	I	Yes	Yes	Yes	Yes
Tahna Algalal I.H.	BEOC	I	Yes	Yes	Yes	Yes
Samalout District						
		I	10	5	5	5
Samalout District Hospital	CEOC	I	Yes	NA	NA	NA
Samalout District Hospital	NCU2	I	Yes	NA	NA	NA
Samalout District Hospital	CSSD	I	Yes	NA	NA	NA
Samalout District Hospital	OR	I	Yes	NA	NA	NA
Samalout District Hospital	ER	I	Yes	NA	NA	NA
Oulosna I.H.	BEOC	I	Yes	Yes	Yes	Yes
Daqoof I.H.	BEOC	I	Yes	Yes	Yes	Yes
El-Saleba I.H.U.	BEOC	I	Yes	Yes	Yes	Yes
Mansheat El-Sheraai I.H.	BEOC	I	Yes	Yes	Yes	Yes
El-Baiaho I.H.	BEOC	I	Yes	Yes	Yes	Yes
Fekrya District						
		II	5	1	1	1
Fekrya District Hospital	CEOC	II	Yes	NA	NA	NA
Fekrya District Hospital	NCU2	II	Yes	NA	NA	NA
Fekrya District Hospital	CSSD	II	Yes	NA	NA	NA
Fekrya District Hospital	OR	II	Yes	NA	NA	NA
Asmant I.H.U.	BEOC	II	Yes	Yes	Yes	Yes
Deir Mowas District						
		II		2	2	2
Deir Mowas District Hospital	CEOC	II		NA	NA	NA
Deir Mowas District Hospital	NCU2	II		NA	NA	NA
Deir Mowas District Hospital	CSSD	II		NA	NA	NA
Deir Mowas District Hospital	OR	II		NA	NA	NA
Suzan Mubarak Urban Health Center	NCU2	II		NA	NA	NA
Deir Mowas Maternity	BEOC	II				
Nazlat Badarnan I.H.	BEOC	II		Yes	Yes	Yes
Bani Haram I.H.U.	BEOC	II		Yes	Yes	Yes
Beni Mazar District						
		II				
Beni Mazar District Hospital	CEOC	II		NA	NA	NA
Beni Mazar District Hospital	NCU2	II		NA	NA	NA
Beni Mazar District Hospital	CSSD	II		NA	NA	NA
Beni Mazar District Hospital	OR	II		NA	NA	NA
Beni Mazar District Hospital	ER	II				
Sandafa I.H.	BEOC	II				
Bani Ali I.H.	BEOC	II				
Abu Garg W.H.C.	BEOC	II				
El Sheikh Fadl I.H.	BEOC	II				
Maghagha District						
		III				
Maghagha District Hospital	CEOC	III		NA	NA	NA
Maghagha District Hospital	NCU2	III		NA	NA	NA
Maghagha District Hospital	CSSD	III		NA	NA	NA
Maghagha District Hospital	OR	III		NA	NA	NA
Maghagha District Hospital	ER	III				
Mattay District						
		III				
Mattay District Hospital	CEOC	III		NA	NA	NA
Mattay District Hospital	NCU2	III		NA	NA	NA
Mattay District Hospital	CSSD	III		NA	NA	NA
Mattay District Hospital	OR	III		NA	NA	NA
El Edwa District						
		III				

QPMR V						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
EI Edwa District Hospital	CEOC	III		NA	NA	NA
EI Edwa District Hospital	NCU	III		NA	NA	NA
EI Edwa District Hospital	CSSD	III		NA	NA	NA
EI Edwa District Hospital	OR	III		NA	NA	NA
Mallawi District		III				
Mallawi District Hospital	CEOC	III		NA	NA	NA
Mallawi District Hospital	NCU2	III		NA	NA	NA
Mallawi District Hospital	CSSD	III		NA	NA	NA
Mallawi District Hospital	OR	III		NA	NA	NA

QPMR V						
Governorate District Facility	Type	Phase	Providers Sensitized (Number of Facilities)	Community Health Committee Established	Community Needs Assessment Conducted	Community Action Plan Developed
Giza Governorate						
North Giza District						
North Giza District Hospital	CEOC	IV		NA	NA	NA
North Giza District Hospital	NCU2	IV	NA	NA	NA	NA
El Agouza District						
El Agouza District Hospital	CEOC	IV		NA	NA	NA
El Agouza District Hospital	NCU3	IV	NA	NA	NA	NA
El Omrania District						
El Omrania District Hospital	CEOC	IV		NA	NA	NA
South Giza District						
South Giza District Hospital	CEOC	IV		NA	NA	NA
South Giza District Hospital	NCU2	IV	NA	NA	NA	NA
El-Haram District						
El-Haram District Hospital	CEOC	IV		NA	NA	NA
El-Haram District Hospital	NCU2	IV	NA	NA	NA	NA
Markaz Giza District						
Markaz Giza District Hospital	CEOC	IV		NA	NA	NA
Markaz Giza District Hospital	NCU2	IV	NA	NA	NA	NA
Warak District						
Warak District Hospital	CEOC	IV		NA	NA	NA
Oseim District						
Oseim District Hospital	CEOC	IV		NA	NA	NA
Hawamdeya District						
Hawamdeya District Hospital	CEOC	IV		NA	NA	NA
Hawamdeya District Hospital	NCU2	IV	NA	NA	NA	NA
El Badrashein District						
El Badrashein District Hospital	CEOC	IV		NA	NA	NA
El Badrashein District Hospital	NCU2	IV	NA	NA	NA	NA
El Ayat District						
El Ayat District Hospital	CEOC	IV		NA	NA	NA
El Saff District						
El Saff District Hospital	CEOC	IV		NA	NA	NA
Elfeih District						
Elfeih District Hospital	CEOC	IV		NA	NA	NA
El Wahat Baharia District						
El Wahat Baharia District Hospital	CEOC	IV		NA	NA	NA
El Wahat Baharia District Hospital	NCU2	IV	NA	NA	NA	NA
Menshaat El Qanater District						
Menshaat El Qanater District Hospital	CEOC	IV		NA	NA	NA
El Dokki District						
El Dokki District Hospital	CEOC	IV		NA	NA	NA
El Dokki District Hospital	NCU2	IV	NA	NA	NA	NA
Boulaq El Dakroun District						
Boulaq El Dakroun Hospital	CEOC	IV		NA	NA	NA
Boulaq El Dakroun Hospital	NCU2	IV	NA	NA	NA	NA
