



**USAID**  
FROM THE AMERICAN PEOPLE

## **QUARTERLY REPORT #16**

### **HELPING ADDRESS RURAL VULNERABILITIES AND ECOSYSTEM STABILITY (HARVEST) PROGRAM**



**October – December 2014**

This publication was produced for review by the United States Agency for International Development. It was prepared by Fintrac Inc. under contract # AID-442-C-11-00001 with USAID/Cambodia.



**Fintrac Inc.**

[www.fintrac.com](http://www.fintrac.com)

[info@fintrac.com](mailto:info@fintrac.com)

US Virgin Islands  
3077 Kronprindsens Gade 72  
St. Thomas, USVI 00802  
Tel: (340) 776-7600  
Fax: (340) 776-7601

Washington, D.C.  
1400 16<sup>th</sup> St. NW, Suite 400  
Washington, D.C. 20036 USA  
Tel: (202) 462-8475  
Fax: (202) 462-8478

**Cambodia HARVEST**

No. 34 Street 310  
Sangkat Beong Keng Kang I  
Khan Chamkamorn, Phnom Penh, Cambodia  
Tel: 855 (0) 23 996 419  
Fax: 855 (0) 23 996 418

*Cover Photo: A husband and wife harvest their wet-season rice in Siem Reap province in November.*

*Photo by Cambodia HARVEST*

# **QUARTERLY REPORT #16**

## **HELPING ADDRESS RURAL VULNERABILITIES AND ECOSYSTEM STABILITY (HARVEST) PROGRAM**

**October – December 2014**

The author's views expressed in this publication do not necessarily reflect the views of the United States Agency for International Development or the United States Government.

# CONTENTS

<b>EXECUTIVE SUMMARY.....</b>	<b>1</b>
<b>I. INTRODUCTION.....</b>	<b>3</b>
I.1    Program Description.....	3
I.2    Geographic Focus .....	3
I.3    Client Portfolio.....	4
I.4    Implementing Partners.....	4
<b>2. PROGRAM COMPONENTS.....</b>	<b>7</b>
2.1    Food Availability Increased .....	7
2.2    Increased Food Access through Rural Income Diversification .....	11
2.3    Natural Resource Management and Resilience to Climate Change Increased .....	12
2.4    Capacity of Public, Private, & Civil Society to Address Food Security & Climate Change ..	14
<b>3. ACTIVITIES PLANNED FOR NEXT QUARTER.....</b>	<b>17</b>
<b>ANNEX I: YEAR FIVE PERFORMANCE WORK PLAN .....</b>	<b>19</b>
<b>ANNEX II: CLIENT INFORMATION .....</b>	<b>27</b>
<b>ANNEX III: SNAPSHOTS.....</b>	<b>69</b>
<b>ANNEX IV: PROVINCIAL MAPS .....</b>	<b>73</b>
<b>ANNEX V: PROCUREMENT PROGRESS REPORT .....</b>	<b>77</b>
<b>ANNEX VI: FINANCIAL SUMMARY .....</b>	<b>82</b>

## EXECUTIVE SUMMARY

Cambodia HARVEST is a five-year food security program focused on increasing incomes for 70,000 rural Cambodian households as part of the United States Feed the Future and Global Climate Change initiatives. This is the program's sixteenth quarterly report and highlights major achievements and activities for the period of October to December 2014.

As Cambodia HARVEST enters its fifth year of operation, the program has trained more than a quarter of a million people in agriculture, natural resource management, and food security concepts. This quarter, the program's wet-season rice farmers had their largest and most successful harvest yet, despite serious floods affecting large parts of the four target provinces. Agribusinesses receiving Public Private Alliance funds began installing equipment and undergoing training that will strengthen their respective value chains and benefit thousands of farmers.

Under the nutrition component, community-based savings funds dispensed hundreds of loans to poor households to help them start microenterprises that will strengthen food security and increase incomes. A carbon assessment found that Cambodia has avoided emissions equivalent to 1.5 million tons of carbon dioxide as a result of the program's work in the Central Cardamoms Protected Forest, an amount equal to the emissions produced by 300,000 cars in one year.

### Highlights this quarter include:

- Program-supported farmers and agribusinesses generated \$4.3 million in incremental sales.
- 37,472 wet-season rice farmers harvested their fields, resulting in average yield increases of 50 percent and income increases of 56 percent.
- Commercial horticulture and household garden clients increased their average yields by a combined 256 percent, strengthening food security and boosting household incomes.
- 146 community-based savings funds have provided 1,472 loans worth nearly \$60,000 to spur microenterprise development.
- 11 Public Private Alliance recipients have begun making \$2.4 million worth of improvements to their businesses.
- Six partner community fisheries graduated from the program after receiving technical assistance designed to strengthen their ability to protect critical resources.
- Community forests are using technology introduced by the program that converts waste generated by bamboo furniture and handicraft producer groups into charcoal and energy.
- A mobile media campaign is delivering climate change and biodiversity conservation messages to 30 community forestry groups with a total population of 37,576.

### Food Availability Increased

Cambodia HARVEST is working to increase the availability of food to meet the everyday dietary needs of Cambodians.

- 106,862 farmers have applied new technologies or management practices, 242 percent of the total program target of 44,100.
- 41,773 hectares are under improved technologies or management practices, 193 percent of the total program target of 21,600.
- The dietary diversity of women of reproductive age improved to 5.7 food groups consumed from six of Feed the Future's nine foods essential to dietary diversity, a 24 percent increase over the baseline number of 4.6.



### **Increased Food Access through Rural Income Diversification**

The program is strengthening the ability of Cambodians to generate income through economic activities to increase their capacity to purchase food.

- Cambodia HARVEST linked 46 horticulture producer groups with two district- and provincial-level vegetable buyers this quarter, resulting in 436 metric tons of new sales worth \$133,458. To date, these linkages have resulted in 1,358 metric tons of new sales worth \$407,961.
- Incremental sales from farm-level rice, horticulture, and aquaculture totaled \$3.2 million this quarter, bringing the total to \$17.2 million, 164 percent of the total program target of \$10.5 million.
- \$1.1 in incremental sales have been collected at the small- and medium-sized enterprise levels this quarter, bringing the total to \$10.67 million, 112 percent of the total program target of \$9.5 million.

### **Natural Resource Management and Resilience to Climate Change**

The program is working to protect the country's globally significant natural resources, which are an essential source of economic activity and food security for Cambodians.

- 30,484 people received training in natural resource management or biodiversity conservation, exceeding the total program target of 27,000.
- 1.5 million tCO<sub>2</sub> of greenhouse gas emissions (measured in metric tons of CO<sub>2</sub> equivalent) reduced or sequestered as a result of program assistance, 68 percent of the total life of the program target of 2.2 million tCO<sub>2</sub>.

### **Capacity of Public, Private, and Civil Society to Address Food Security and Climate Change**

Cambodia HARVEST is strengthening the capacity of Cambodians to manage and resolve challenges related to food security and global climate change.

- 3,280 stakeholders have increased their capacity to adapt to the effects of climate variability and change this quarter, bringing the total to 39,548, 117 percent of the cumulative target of 33,875 and 87 percent of the total program target of 45,500.
- 1,444 agribusinesses and households received small-scale loans totaling \$1.9 million this quarter, bringing the total to \$8 million worth of loans for 8,470 agribusinesses and households, 242 percent of the total program target of 3,500.
- Thirty-six climate change mitigation tools, technologies, and methodologies have been developed, tested, or adopted, 113 percent of the total program target of 32.

### **Overall Training and Technical Assistance**

- Technical assistance extended to 87,404 rural households to date, 125 percent of the total program target of 70,000. Among these, 8,129 (9.3 percent) were extreme poor, 116 percent of the total program target of 7,000.
- To date, 267,093 people have received agriculture and food security training through demonstration sites, interactive field days, mobile kitchens, and one-on-one technical assistance, 191 percent of the 140,000 people targeted over the life of the program.

# I. INTRODUCTION

## I.1 PROGRAM DESCRIPTION


Cambodia HARVEST develops sound, agriculture-focused solutions to poor productivity, postharvest losses, malnutrition, lack of market access, environmental degradation, and the effects of climate change on vulnerable rural populations. The program is based on an **intensive extension methodology** in which program technicians visit their client farmers every week to provide targeted, hands-on technical assistance. In this way, Cambodia HARVEST ensures its tens of thousands of rural clients not only see short-term gains, but also build the necessary skills and knowledge to continue succeeding long after the program is finished.

The overarching goals of Cambodia HARVEST are to improve food availability; increase food access through rural income diversification; improve natural resource management and resilience to climate change; and strengthen the capacity of the public and private sectors and civil society to address food security and climate change.

## I.2 GEOGRAPHIC FOCUS

Cambodia HARVEST is working in 36 out of the 42 districts that make up the four target provinces. The program has provided technical assistance in 1,421 villages around the Tonle Sap Lake: 349 in Battambang, 367 in Pursat, 346 in Siem Reap, and 359 in Kampong Thom. Figure 1 shows the geographic dispersal of Cambodia HARVEST target communes. More detailed regional maps are included in Annex IV.

**Figure 1: Cambodia HARVEST Clients**

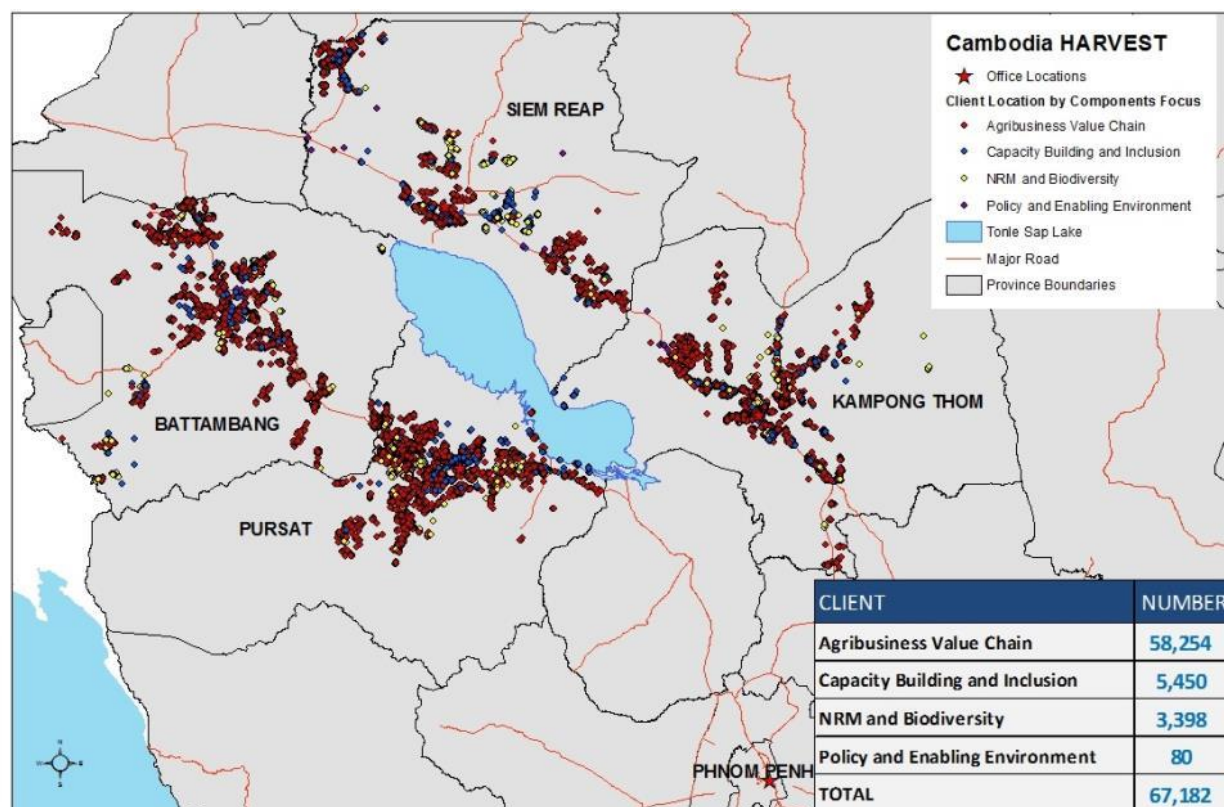

### 1.3 CLIENT PORTFOLIO

Because farmers are more likely to adopt new practices if they see the benefits first-hand, Cambodia HARVEST uses demonstration sites – established on client and lead client farms, households, or those of farmer groups or agribusinesses – to illustrate the effects of program techniques and technologies. To date, the program has directly worked with a total of 19,759 field demonstration clients (17,415 horticulture and rice; 2,018 aquaculture, hatchery, and cage culture; 144 schools; 63 health centers; and 119 forestry) and 598 partner clients (441 input suppliers; 49 rice millers; 77 commune councils; and 31 branches of nine microfinance institutions).

#### Definitions

- **Lead demonstration client:** A designated demonstration client who uses his/her plot to illustrate technology to other demonstration clients or beneficiaries within a village.
- **Demonstration client:** Farmers or individuals who demonstrate program techniques and technologies to nearby farmers under a co-investment agreement.
- **Partner client:** Communities or agribusinesses assisted by the program.
- **Client (farmer) group:** One lead demonstration client with a number of beneficiary farmers.
- **Producer group:** A number of farmers who come together as a group to leverage market options.
- **Beneficiary:** Farmers or individuals who receive indirect technical assistance from the program.
- **Participants:** Farmers or individuals who attend trainings.

### 1.4 IMPLEMENTING PARTNERS

Cambodia HARVEST has partnered with 21 field-based NGOs with 343 technicians to implement activities in horticulture, rice, forestry, aquaculture and fisheries, nutrition, and vocational skills training, as shown in Figure 2 below.

**Figure 2: Cambodia HARVEST Implementing Partners**

Partner NGOs	Agriculture/ Nutrition	Rice	NRM/ Forestry	Aquaculture/ Fisheries	Business Development Services	Operations Management	Fish Processing	Capacity Development
Action for Development (AFD)	✓		✓					
Agriculture Technology Services Association (ATSA)	✓	✓			✓		✓	
Aphivat Strey (AS)	✓	✓		✓				
Buddhism for Development (BFD)	✓							
Conservation International (CI)							✓	
Environmental Protection and Development Organization (EPDO)			✓	✓				
Farmer Livelihood Development (FLD)	✓				✓	✓		
Fauna & Flora International (FFI)			✓					
Human Resource and Rural Economic Development Organization (HURREDO)	✓	✓	✓					
IDE Cambodia		✓						
Irrigation Service Center (ISC)		✓						✓
Lom Orng Organization (LOO)	✓	✓				✓		
Partnership for Development in Kampuchea (PADEK)				✓				
Ponleur Kumar (PK)	✓	✓	✓					
Prom Vihear Thor Organization (PVT)			✓	✓				



Partner NGOs	Agriculture/ Nutrition	Rice	NRM/ Forestry	Aquaculture/ Fisheries	Business Development Services	Operations Management	Fish Processing	Capacity Development
Reproductive and Child Health Alliance (RACHA)	✓							
Rural Economic & Agriculture Development Agency (READA)	✓							
Srer Khmer (SK)	✓	✓						
Village Support Group (VSG)	✓	✓	✓	✓				
Wathnakpheap (WP)	✓							
Wildlife Conservation Society (WCS)				✓				
<b>Total = 21</b>								

Cambodia HARVEST continues to collaborate with numerous Cambodian government agencies, donors, local and international organizations, educational institutions, and private sector firms. Figure 3 shows the program's major counterparts with whom staff members collaborate regularly.

**Figure 3: Select Cambodia HARVEST Counterpart and Stakeholder Collaboration**

Government & Universities	Donor Organizations	Finance Institutions	Private Sector & Other	Public Private Alliances
Commune Councils	Asian Development Bank (ADB)	ACLEDA Bank Plc.	Advancing Engineering Consultants	Lay Song Rice Mill
Fisheries Administration	Collaborative Research Support Program	Angkor Mikrohianhvatho (Kampuchea) Co. Ltd	Agrisource (Cambodia) Ltd.	Chhum Lay Rice Mill
Forestry Administration	Food and Agriculture Organization (FAO)	Cambodia Microfinance Association	Aruna Technology	Lim Theanghy Rice Mill
General Directorate of Agriculture	International Finance Corporation (IFC)	Hattha Kaksekar Limited	Auburn University USA	Asia Agri Group Co., Ltd (AAG)
Ministry of Agriculture, Forestry, and Fisheries	Peace Corps	Intean Poalroath Rongroeurng Ltd.	Cambodian Agribusiness Development Facility	Ratha Da Hatchery
Ministry of Environment	Voluntary Service Overseas	KREDIT Microfinance Institution Plc.	Chhieng Long Trading Co. Ltd	Prum Bunthai Enterprises
Ministry of Land Management, Urban Planning and Construction	World Bank	SAMIC Microfinance	CSB Co. Ltd	Chea Chanthou Rice Mill
Ministry of Water Resources and Meteorology	World Health Organization (WHO)	Sathapana Limited	Federation of Rice Millers Association	Sen Reth Rice Mill
Ministry of Women's Affairs	CAVAC	Thaneakea Phum (Cambodia) Ltd.	Horticulture Collaborative Research Support Program	Tong Ry Rice Mill
Office of the Council of Ministers	GIZ	VisionFund Cambodia	Integrated Modern Irrigation Solution (Cambodia) Co. Ltd	Sroy Kimse Rice Mill
Provincial Department of Agriculture	World Food Program (WFP)	CANADIA Bank Plc.	International Rice Research Institute (IRRI)	Asia Irrigation
Provincial Department of Education, Youth and Sport	USAID – Supporting Forestry and Biodiversity (SFB)		Kasevisiddh Group Co. Ltd	

<b>Government &amp; Universities</b>	<b>Donor Organizations</b>	<b>Finance Institutions</b>	<b>Private Sector &amp; Other</b>	<b>Public Private Alliances</b>
Provincial Department of Health	USAID - NOURISH		Ly Hong Chhoy Co. Ltd	
Provincial Department of Water Resources and Meteorology / Pursat	USAID - AgriLearn		Malysan Group Co. Ltd	
Provincial Department of Women's Affairs	USAID - WorldFish		Papaya Co. Ltd	
University of Battambang	USAID – Capacity Building of Cambodia's Local Organization Program (CBCLO)		USAID – IPM Innovation Lab	
National Institute of Public Health (NIPH)	USAID – Khmer HIV/AIDS NGO Alliance (KHANA)		DuPont Cambodia	
Prek Leap National College of Agriculture	International Fund for Agricultural Development (IFAD)		Emerging Markets Consulting (EMC)	
Royal University of Phnom Penh (RUPP)	Program for Appropriate Technology in Health (PATH)		Cambodia Development Resource Institute (CDRI)	
Royal University of Agriculture (RUA)			Inter-Green Consult (IGC)	
			International Institute for Education (IIE)	
			Weidemann Associates (Crown Agents USA)	

## 2. PROGRAM COMPONENTS

### 2.1 FOOD AVAILABILITY INCREASED

Cambodia HARVEST's work in this area focuses on enhancing agricultural input and production systems; introducing improved crop varieties and modern agricultural techniques; diversifying rural production systems; and strengthening the agricultural policy framework.

#### Agriculture Input and Production Systems Enhanced

- **Wet-season rice harvest results in yield and income increases.** The program's 37,472 wet-season rice farmers harvested their fields this quarter, leading to average yield increases of 50 percent over baseline, from 2 tons to 3 tons per hectare. The harvest resulted in a total net production increase of approximately 44,966 metric tons of paddy, valued at more than \$11.2 million. With these gains, the farmers increased their household incomes by 56 percent over baseline. Program farmers achieved these results despite a severe drought that hit most of Battambang and parts of the other three target provinces. Cambodia HARVEST provides wet-season farmers with a wide range of technical assistance through 3,027 demonstration farmers, who saw the highest yield increases at an average of 82 percent over baseline.
- **Farmers begin dry-season rice cultivation.** With the end of the monsoon rains in November, dry-season rice farmers began cultivating their fields. Cambodia HARVEST will work with approximately 4,500 farmers this season. Program technicians are training these farmers in good agricultural practices designed to increase productivity and crop quality.
- **Household vegetable clients make further gains.** The program's 11,814 client and beneficiary household vegetable farmers continued to improve their productivity this quarter, strengthening food security and increasing the availability of nutritious vegetables in their villages. These farmers increased their productivity by 250 percent over baseline, resulting in income increases of 361 percent through the sale of excess crops to local buyers and neighboring households. The program is currently working with 9,563 demonstration clients and 2,251 beneficiary households who are adopting the program's techniques.
- **Commercial horticulture farmers increase their yields and incomes.** The program's 5,195 commercial horticulture clients and beneficiary households increased their yields by 262 percent this quarter, resulting in income gains of 336 percent. Commercial horticulture farmers are increasing the availability of food by providing buyers with a steady source of fresh, nutrient-rich vegetables, lessening reliance on imports from Vietnam and Thailand. Cambodia HARVEST is currently working with 4,229 demonstration clients and 966 beneficiary households who are adopting the program's techniques.
- **Vegetable nurseries generate promising early results.** Ten members from 10 horticulture producer groups have built vegetable seedling nurseries using contributions from Cambodia HARVEST's



*Photo by Cambodia HARVEST*

*Vegetable nurseries like this one in Kampong Thom are supplying horticulture producer group members and local farmers with a consistent source of affordable, high-quality vegetable seedlings.*

technology fund. These nurseries are generating additional income for owners and are supplying producer group members and non-program farmers with a consistent source of affordable, high-quality vegetable seedlings. As a result, customer farmers do not have to grow their own seedlings, saving them time and money. Although the project is in its early stages, results thus far have been promising. Five of the older nurseries established one year ago have generated average sales of \$823, resulting in average incomes of \$380 per nursery. The five other newly established nurseries have only recently begun operations.

- **Distributors introduce soluble fertilizers.** Focusing on plant nutrition requirements, Cambodia HARVEST has requested two large input distributors to source and begin carrying three new soluble fertilizer formulations (magnesium sulphate, calcium nitrate, and potassium chloride) that can be injected through drip irrigation systems. All Cambodia HARVEST commercial horticulture farmers are now using these new soluble products, which were previously unavailable in the country. In addition to providing the required elements for optimum plant growth, these soluble fertilizers take less time to apply and are readily absorbed through the irrigation system.
- **Aquaculture farmers see strong results.** This quarter, 674 aquaculture clients and beneficiaries completed at least one pond harvest cycle, resulting in yield increases of 268 percent and income increases of 125 percent over baseline. To date, the program's 1,807 aquaculture farmers have seen yield increases of 263 percent and income increases of 112 percent over baseline, producing 1,048 tons of fish with a total market value of \$2 million. On average, clients consume 20 percent of the fish they raise, allowing them to supplement their diets with protein and save money on food purchases.
- **Hatcheries improve their operations.** With program assistance, 12 client fish hatcheries are increasing the supply of quality fingerlings available to Cambodian aquaculture farmers. To date, the hatcheries have increased their fingerling productivity by 548 percent over baseline, from an average of 185,110 fingerlings to 1.2 million, and increased their incremental sales by 697 percent. In addition, the hatcheries have increased the average weight of their fingerlings by 196 percent and reduced their stocking mortality by 45 percent, both of which are important indicators of fingerling quality. Improving the production capacity and fingerling quality of fish hatcheries in Cambodia is essential for the long-term sustainability and expansion of the sector. This quarter, the program held a workshop for hatchery personnel on topics such as oxygen use and safety, broodstock selection and stocking, and fry and fingerling handling and transport.

### Rural Production Systems Diversified

- **Program increases number of poor, women, and young clients.** In four years of operation, Cambodia HARVEST has steadily increased the percentage of its clients who are poor, women, and under the age of 30. Currently, 9.3 percent of its clients are extreme poor (ID1), a 3.3 percent increase over 2011; 54.2 percent of its clients are women, a 20.4 percent increase over 2011; and 20.3 percent of its clients are youth, an 8.8 percent increase over 2011. Cambodia HARVEST's focus on social inclusion is ensuring that all segments of Cambodian society benefit from program activities.

CATEGORY	FY 2011	FY 2012	FY 2013	FY 2014
Poor level 1	6.0%	8.9%	8.3%	9.3%
Poor level 2	9.3%	11.9%	12.1%	12.3%
Poor level 1 & 2	15.4%	20.8%	20.4%	21.6%
Women	33.8%	53.5%	50.0%	54.2%
Youth	11.5%	17.9%	18.3%	20.3%

- **Household dietary diversity improves.** This quarter, 9,935 people attended Cambodia HARVEST nutrition training and field day events, bringing the total number of people who have received program nutrition training to date to 93,805. These activities have improved the dietary diversity of participants, according to the results of the most recent quarterly performance monitoring survey. On average, the women of reproductive age surveyed eat from 5.7 of Feed the Future's nine food groups essential to dietary diversity, a 24 percent increase over the baseline number of 4.6. Cambodia HARVEST is on track to reach its total program target of an average of six food groups consumed.
- **Savings funds spur microenterprise development.** The program's 146 savings funds continued to fund microenterprise development by providing credit to contributing members. The savings funds, which are composed of 2,305 people belonging to community-based food security and nutrition groups, crossed several major thresholds this quarter:
  - In the first six months of savings and lending activities, members saved more than \$50,000.
  - They leveraged their savings to provide 1,472 loans worth nearly \$60,000.
  - They earned more than \$2,500 in interest, thereby increasing the value of their assets by 5 percent.



*Photo by Cambodia HARVEST*

*Members of a community-based savings fund tend to their books in Pursat. The program's 146 funds have dispensed nearly \$60,000 in loans that are helping to spur microenterprise development in rural villages.*

Four savings funds in Pursat demonstrate the effectiveness of this model. Despite being small and made up of very poor members, the funds were able to provide loans to 24 members and increase the value of their assets by an average of 3.6 percent. Members used the money to begin raising pigs, buy fertilizer for rice, and pay for medical care. These groups are now entering the second cycle of their activities and are recruiting new members.

- **Mobile kitchens teach nutrition concepts in remote areas.** The program's mobile kitchens trained 35,432 participants this quarter on nutrition and hygiene concepts. To date, the eight motorbike-pulled vendor carts have trained 102,204 participants, 81 percent of them women, in 1,010 villages located in difficult-to-reach rural areas. The mobile kitchens are targeted to reach 117,477 participants by the end of the program. Village health volunteers are assisting the food cart teams, gaining additional knowledge about nutrition and helping with demonstrations.
- **School meals activity benefits from support.** Cambodia HARVEST is collaborating with the World Food Program (WFP) to increase the nutritional content of meals provided through two pilot school programs in Siem Reap. The ultimate goal of the activity is for commune councils to allot money from their annual budgets to fund school breakfasts. This quarter, the program trained 34 personnel from WFP and its local partner, Plan International, on aspects of nutrition, food safety, and hygiene that are relevant to the school meals activity. The participants learned the basics of family nutrition – with a focus on the nutritional needs of school-age children and good practices in food safety, hygiene, and sanitation at schools – to enable them to work with cooks who prepare school meals and other staff at schools in



four provinces. In addition, Cambodia HARVEST trained eight cooks and school storekeepers on new recipes and improvements in food safety and hygiene practices.

- **Commune councils strengthen nutrition capacity.** Cambodia HARVEST is continuing to partner with local government in an effort to strengthen nutrition practices in rural households. This quarter, the program trained 39 commune council members who are designated as focal points on women and children in their communes. The training will help the focal points more effectively invest commune funds in nutrition-related activities. The focal points are now collaborating with program-supported food security and nutrition groups to plan and facilitate community action events related to nutrition, hygiene, and sanitation. Also, the focal points are refining their work plans for community outreach to schedule activities and strengthen the messaging on nutrition and hygiene.

### Strengthen Agriculture Policy Framework

- **Consultation workshop gathers feedback on extension policy.** This quarter, the program organized the seventh event in a series of eight regional and national consultation workshops on the Agricultural Extension Policy. Presided over by the Secretary of State of the Ministry of Agriculture, Forestry, and Fisheries, the event in Phnom Penh drew nearly 100 participants from the government, development partners, and other stakeholders. Attendees provided feedback that will be incorporated into a final version of the document that will be submitted for adoption by the ministry in early 2015. When formalized, the agricultural extension policy will enable farmers to better access improved technologies through government extension programs and non-government entities.

**Figure 4: Status of Cambodia HARVEST Policy Reforms**

Policy/Regulation/Analysis	Stage 1: Analysis / Inception	Stage 2: Drafting	Stage 3: Presen- tation	Stage 4: Adoption	Stage 5: Implem- entation	Status	Govt. Priority
1. Legal Aspects of Exporting Cambodian Rice Originating in Foreign Countries	✓	✓	✓	N.A	N.A	Done	
2. Biodiversity Targets and Indicators for National Biodiversity Strategic and Action Plan (NBSAP)	✓	✓	✓	✓	✓	Done	
3. National Protected Area Strategic Management Framework	✓	✓	✓	✓	✓	Done	
4. National Seed Policy	N.A	✓	✓	2015	2015	Ongoing	High
5. Prakas on Seed Quality Certification	✓	✓	✓	2015	2015	Ongoing	High
6. Agricultural Extension Policy	✓	✓	Q2, 2015	2015	2015	Ongoing	Very high
7. Sub-decree of Uniform of Seed Inspectors (Khmer)	✓	✓	✓	2015	2015	Ongoing	High
8. National Seed Standards	✓	✓	✓	2015	2015	Ongoing	High
9. Plant Breeders' Rights (DUS testing)	✓	✓	✓	2015	2015	Ongoing	High
10. Draft Law on Quality and Safety of Agricultural Products	✓	✓	✓	2015	2015	Ongoing	High

<b>11. Revision of National Biodiversity Strategic and Action Plan (NBSAP)</b>	✓	✓	Q2, 2015	2015	2015	Ongoing	Very high
<b>12. Procedure to Register Biological Control Agents</b>	✓	Q2, 2015	Q3, 2015	2015	2016	Ongoing	High
<b>13. Development of benefit sharing mechanism in community forests</b>	Q2, 2015	Q3, 2015	2015	2015	2015	Ongoing	High
<b>14. Horticulture Strategic Development Plan</b>	Q2, 2015	2015	2015	2015	2016	Ongoing	Very high
<b>15. Joint Prakas on Service Fee for Seed Quality Control</b>	Q2, 2015	Q3, 2015	Q2, 2015	2015	2016	Ongoing	High
<b>16. Joint Prakas on Seed Quality Inspection Policing</b>	Q2, 2015	Q3, 2015	Q2, 2015	2015	2016	Ongoing	High

## 2.2 INCREASED FOOD ACCESS THROUGH RURAL INCOME DIVERSIFICATION

Cambodia HARVEST works to strengthen postharvest systems; improve market access and linkages to smallholders; expand rural employment generation; and increase investment in marketing infrastructure.

### Postharvest Systems Strengthened

- **Horticulture producer groups generate increased sales.** The program's 46 commercial horticulture producer groups have generated 1,358 metric tons of new sales worth \$407,961. Forming producer groups, which have an average of 16 members each, helps help farmers attract more buyers for their crops, resulting in higher sales volumes and prices. The groups also work together to choose vegetables and growing cycles that maximize market opportunities. To date, the program has linked partner producer groups with 93 district- and provincial-level buyers.
- **Public Private Alliance recipients begin activities.** The 11 recipients of Public Private Alliance funds have begun installing equipment and participating in training designed to increase business and farmer productivity, improve overall product quality, lower operating and farming costs, and strengthen technical knowledge. The partner agribusinesses received a total of more than \$1 million in Public Private Alliance funds, which, when combined with the \$1.4 million co-invested by the companies, brings the total value of the alliances to \$2.4 million. This quarter:
  - **Horticulture:** In the area of horticulture extension for agribusinesses, 26 personnel from three agriculture input distributors received a two-week hands-on training course from Cambodia HARVEST technicians. In addition, the businesses established 55 demonstration sites out of a planned 214 commercial horticulture and 54 rice demonstration sites.



Photo by Cambodia HARVEST

Public Private Alliance funds are helping rice millers like this one in Pursat install new equipment and improve their operations. The alliances will result in \$2.4 million in new investment in 11 agribusinesses.

- **Aquaculture:** The partner fish hatchery is building improved infrastructure and installing enhanced technology that will increase its fingerling output from the current volume of 100,000 to 1 million fingerlings per year. Construction is expected to be complete by the end of February.
- **Rice:** Seven small- and medium-sized rice mills have invested in machinery, equipment, and storage units to improve their competitiveness and increase incomes of approximately 3,500 local rice farmers by strengthening demand for paddy. Five of the rice mills have finished installing equipment such as dryers, color sorters, and other milling equipment. The remaining two rice mills will finish this work by February 2015.
- **Rice seed cooperatives build facilities.** Through the Cambodia HARVEST technology fund, three rice seed cooperatives with a total of 344 members have nearly finished building storage facilities for both harvested and milled paddy. The new facilities, worth \$38,000 each, are capable of storing up to 45 tons of paddy apiece. This will allow farmers to store their rice and sell it when prices are favorable. All of the facilities are expected to be fully operational by the start of the 2015 dry season.

### **Value of Incremental Sales Increased at the Farm and Small- and Medium- Enterprise Level**

- **Value of incremental sales increased at the farm and enterprise level.** Program horticulture, rice, and aquaculture clients saw incremental sales increases of \$3.3 million this quarter, bringing the total value of incremental sales increases to date to \$17.2 million, 164 percent of the total program target of \$10.5 million. To date, rice farmers experienced incremental sales increases of \$2.3 million, horticulture farmers \$783,000, and aquaculture farmers \$130,000.
- **Agribusinesses increase incremental sales.** Agricultural input suppliers and small- and medium-sized rice mills reported incremental sales increases of \$1.1 million this quarter, bringing the total amount to date to \$10.6 million, 112 percent of the total program target of \$9.5 million.
- **Input suppliers increase revenues.** The 400 client input suppliers that have been with the program long enough to generate results have increased their revenues by 72 percent over baseline, according to the results of a survey conducted this quarter. The program works with input suppliers to improve the quality of goods and services available to local farmers and increase the incomes of families running these microenterprises. To date, Cambodia HARVEST has provided a range of assistance to input suppliers, including extension training on good agriculture practices; shop and inventory upgrades designed to improve sales; training on bookkeeping and other business administration techniques; and linkages with microfinance institutions to increase access to credit. Natural Resource Management and Resilience to Climate Change Increased

## **2.3 NATURAL RESOURCE MANAGEMENT AND RESILIENCE TO CLIMATE CHANGE INCREASED**

The program is working to enhance the enabling environment for sustainable resource management; improve environmental monitoring and management; and increase the economic benefits of natural resource management and conservation.

### **Enabling Environment for Sustainable Resource Management Enhanced**

- **Community forests prepare for commercial harvesting of poles.** This quarter, four of the 10 partner community forests made progress in drafting plans for establishing pilot commercial harvesting enterprises designed to generate a new source of revenue for their

communities. With technical assistance from Cambodia HARVEST and approval from the Forestry Administration, the communities will sustainably harvest small diameter pole-sized trees, which will be sold for construction use to local and retail markets. Forest areas are sectioned off into one-hectare blocks where specific diameter trees are marked and harvested on an annual basis. A rotation system is established where the same blocks are harvested again when a given percentage of the younger trees reach harvestable size, which usually takes between two to three years. The poles can sustain annual harvests worth approximately \$800 per hectare.

- **Community forests replant rattan.** Two community forests conducted rattan replenishment plantings on nearly 11 hectares of land, bringing the total amount of land replanted with rattan to 65 hectares. When mature, rattan can sustain annual harvests worth \$200-\$300 per hectare, providing funding that is vital to local communities and the long-term survival of non-timber product user groups.
- **Charcoal technology converts bamboo waste into energy.** Two non-timber forest product groups have begun using new technology introduced by Cambodia HARVEST that converts waste generated from bamboo furniture and handicraft producer groups into charcoal and energy. When used in tandem, the low-cost charcoal-making setup, fabricated waste-oil charcoal-producing kilns, and fabricated molds produce energy efficient briquettes that have a range of benefits. The briquettes recycle waste and offer an alternative source of fuel that saves time and money and reduces pressure on surrounding natural resources. At this early stage in the activity, group members are using the briquettes for home consumption, but they will consider selling them in the future. Cambodia HARVEST is testing the technology on a pilot basis and, should it prove economical, will introduce it to clients and government and development partners.
- **Non-timber producer groups develop new products.** Cambodia HARVEST's 38 non-timber forest product groups developed 35 new designs for bamboo furniture and handicrafts this quarter, bringing the total to 88 to date, increasing market opportunities for group members. The new designs are of a higher quality, have better utility and more ergonomic designs, and will fetch better prices than conventional products. On average, partner non-timber forest product groups have increased their sales by 430 percent, and boosted their profits by 535 percent, over baseline numbers. The producers, most of whom are women, make the products on a casual basis to supplement their household incomes.

### Environmental Monitoring and Management Improved

- **Survey captures emissions reductions.** Cambodia has avoided emissions equivalent to 1.5 million tons of carbon dioxide since 2012 as a result of the program's work in the Central Cardamoms Protected Forest. This is equal to the emissions produced by 300,000 cars in one year and is worth \$8.8 million on the international carbon market, based on 2013 prices. Cambodia HARVEST calculated the savings using the AFOLU Carbon Calculator, a tool developed by Winrock and USAID. The tool determines the amount of emissions saved through improved forest protection, reduced deforestation, and decreased degradation of natural resources, among other areas. The program supports improved management and protection of the 402,000-hectare Central Cardamoms Protected Forest, an area with globally significant biodiversity. Cambodia HARVEST is currently in the process of drafting a five-year management plan for the forest, in addition to training and equipping rangers who monitor the area.
- **Community fisheries graduate.** This quarter, six partner community fisheries graduated from the program after demonstrating their ability to monitor and protect their resources.

The communities reported that they have tripled the fish populations under their management and significantly increased the number of illegal fishing activities they have detected. Cambodia HARVEST continues to work with nine partner community fisheries on a range of issues. This quarter, community fisheries dropped 600 tree stumps into refuge ponds to help protect fish populations in protected areas and surrounding rice fields.



Photo by Cambodia HARVEST

*Members of a community fishery patrol a refuge pond in Pursat. Six of the program's partner community fisheries graduated this quarter, having substantially strengthened their monitoring and management capabilities.*

- **Framework developed by program guides government's protected area plan.** A policy framework developed by Cambodia HARVEST is guiding the creation of a key government plan that will govern the management of the country's protected areas. The Ministry of Environment has begun developing the National Protected Area Strategy Management Plan, which is based on the National Protected Area Strategy Management Framework that Cambodia HARVEST helped the government create last year. The plan will help guide all future investments and activities in 23 protected areas, six protected forests, and eight fish sanctuaries across Cambodia. The plan is expected to be finalized and approved by the government in February 2015.
- **Government drafts Prek Toal management plan.** The program is assisting the Ministry of Environment in drafting a new five-year management plan for Prek Toal Core Area. The plan will govern management and protection of resources and wildlife in the 21,000-hectare protected area, which is home to one of the largest remaining colonies of large water birds in Southeast Asia, including many globally endangered species. In support of the drafting process, program subcontractor Wildlife Conservation Society helped the ministry hold consultation meetings on the draft at the national, provincial, and village levels. The final draft of the management plan is currently in circulation at the ministry, and it is hoped that it will be adopted in early 2015.

## 2.4 CAPACITY OF PUBLIC, PRIVATE, & CIVIL SOCIETY TO ADDRESS FOOD SECURITY & CLIMATE CHANGE

Cambodia HARVEST works with local partners to increase the capacity of producer groups and private sector networks; enhance the capacity for adaptive research and extension; and establish the capacity for climate adaptation and mitigation.

### Capacity of Producer Groups and Private Sector Networks Increased

- **Microfinance institutions increase credit available to farmers.** With Cambodia HARVEST assistance, 1,444 farmers and agribusinesses received loans worth \$1.9 million this quarter. To date, 8,400 farmers have received loans worth \$7 million, and 70 agribusinesses have received loans worth \$1 million. Lack of access to credit hinders productivity in rural areas, impeding economic growth and food security. In order to build the capacity of lenders, Cambodia HARVEST trained 76 personnel from the program's seven partner microfinance institutions this quarter. In addition, representatives from client microfinance institutions participated in 47 field days attended by 1,571 farmers and owners of agribusinesses, providing a forum for lenders to form relationships with potential customers and disseminate information about their products.



## Capacity for Adaptive Research and Extension Enhanced

- **University students begin *Trichoderma* trials.** The program began a series of field trials that are training five students from the University of Battambang on how to run field comparison studies. The students are collecting data on a weekly basis to demonstrate the effectiveness of *Trichoderma*, a bio-control agent used in commercial horticulture against soil fungal pathogens. In addition, the university laboratory is assessing the quality of commercial products available in Cambodia.
- **Training strengthens agricultural extension services.** Cambodia HARVEST is training 54 members of the public and private sectors to improve their ability to provide agricultural extension services. The training is strengthening the participants' knowledge of commercial horticulture, with topics such as land preparation, drip irrigation installation, fertilization, integrated pest management, chemical safety, postharvest, and general farm management systems, in addition to gender and nutrition concepts. This quarter:
  - Public sector: The program established 27 horticulture demonstration plots as part of its one-year collaboration with four provincial departments of agriculture. The sites, which have been primarily established on land belonging to local farmers, allow provincial agriculture field staff to demonstrate Cambodia HARVEST's techniques to farmers in their areas. Last quarter, the program began training 27 provincial field staff on techniques modeled on the program's successful agricultural techniques.
  - Private sector: Cambodia HARVEST began training 27 staff members from three input supply distributors that are participating in the Public Private Alliance. The training is designed to improve the services the companies provide to farmers and retail input suppliers, with the ultimate aim of making them sustainable players in their value chains.

## Capacity for Climate Adaptation and Mitigation Established

- **Forum highlights importance of community forests.** The program participated in the Mekong Climate Change Forum, a high-profile regional event held this quarter in Siem Reap. The forum allowed more than 200 participants to exchange knowledge and experience related to climate change adaptation, with a focus on efforts to deal with the trans-boundary effects of climate change. Representatives from subcontractor Fauna & Flora International gave a presentation on the importance of community forests, which Cambodia HARVEST supports, in helping countries adapt to the effects of climate change. Participants included government officials, academics, and climate experts, in addition to representatives from Mekong River organizations, development agencies, civil society, and the private sector.
- **Mobile campaign reaches forest communities.** The program launched a mobile media campaign this quarter that will deliver global climate change and biodiversity conservation messaging to 30 community forestry groups with a total population of 37,576. The communities are in remote areas and were not exposed to the national broadcast media campaign conducted by the program last year. The mobile campaign showcases excerpts from short films and TV spots that will improve understanding and



Photo by Cambodia HARVEST

A mobile media campaign is educating more than 35,000 people in 30 community forestry groups about global climate change and biodiversity conservation.

awareness of key climate change and biodiversity conservation issues. In addition, the mobile team will disseminate a number of posters and leaflets with similar themes. Campaign events take place in the evenings and typically attract 100 to 300 people.

### **Operations Support**

- **Regional delegates tour program activities.** At the request of the Cambodian government, Cambodia HARVEST organized visits to program activities for 40 representatives from the International Fund for Agricultural Development (IFAD). The delegates, who were from Afghanistan, Bangladesh, China, and Mongolia, among other countries, were in Cambodia for the IFAD Asia and Pacific Regional Workshop. They toured program sites in Angkor Thom district, where they viewed activities related to nutrition, horticulture, aquaculture, and marketing. Program representatives and clients presented an overview of the activities and showed their farms. The Angkor Thom district governor gave a speech to open the tour.

### 3. ACTIVITIES PLANNED FOR NEXT QUARTER

#### **Food Availability Increased**

- Continue dry-season rice activities for approximately 4,500 clients, including 350 demonstration sites.
- Complete the construction of rice storage warehouses for rice cooperatives in Pursat, Battambang, and Kampong Thom, and deliver technical training on improved rice production.
- Begin the process of graduating Phase 2 commercial horticulture and home garden clients.
- Complete the installation of irrigation systems with all Phase 2 commercial horticulture clients.
- Begin trials of new technology such as insect-proof netting (row covers) for tomato and pepper crops.
- Form 26 new commercial horticulture producer groups.
- Construct four new horticulture seedling nurseries.
- Begin agrochemical training with 60 new input suppliers.
- As part of the Public Private Alliance, complete the construction of new buildings and tanks at the Ratha Da fish hatchery.
- As part of the Public Private Alliance, complete construction of new storage facilities and procurement of processing equipment for Tong Ry and Sroy Kimse rice mills.

#### **Increased Food Access through Rural Income Diversification**

- Collaborate with the World Food Program to encourage schools with gardens to grow vegetables for the organization's school meals program.
- Build the capacity of village health volunteers in approximately 500 villages in the areas of family nutrition, growth monitoring, and good hygiene and sanitation.
- Train 200 focal points on women and children at the district and commune levels in the areas of family nutrition, growth monitoring, and good hygiene and sanitation.

#### **Natural Resource Management and Resilience to Climate Change**

- Begin drafting five-year management plan for Central Cardamoms Protected Forest in collaboration with the Forestry Administration and other stakeholders.
- Complete the National Biodiversity Status Update Report in collaboration with the Ministry of Environment.
- Finalize the National Biodiversity Strategy and Action Plan.
- Train rangers in the Central Cardamoms on biodiversity monitoring and camera trapping.
- Begin sustainable harvesting of timber resources at 10 community forests.
- Graduate 38 non-timber forest product groups.
- Develop watershed management plans of action for one district each in Battambang and Pursat.

## **Capacity of Public, Private, and Civil Society to Address Food Security and Climate Change**

- Collaborate with the Council for Agriculture and Rural Development and USAID to organize a national nutrition forum.
- Conduct financial reviews and financial management capacity building sessions with eight partner NGOs.
- Deliver refresher training to seven local partner organizations on operations policies, compliance, monitoring and evaluation, and communications and reporting.
- Begin a one-month internship program for 12 fourth-year undergraduate students in the area of field research.
- Support two participants from Royal University of Agriculture and Fisheries Administration to attend the World Inland Fisheries conference in Rome.

# ANNEX I: YEAR FIVE PERFORMANCE WORK PLAN

N°	Activity Description	Cumulative as of Year 4		Year 5 (Oct 2014 - Sep 2015)					Year 6 (Oct 2015 - Jun 2016)				TOTAL EXPECTED LOP	Deliverables	Responsibilities	Progress Monitor (as of December 31st, 2014)				
		Target	Actual	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Q4 Jul-Sep	Total	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Total				Status	To Date Target	To Date Actual	Balance from LOP target	Comments
1	<b>Agriculture (Crops) Program</b>																			
1.1	Development and production of technical manuals and other training materials for agriculture (crops)	75	75										75	Technical manuals and other training materials produced		Done	75	75	0	
1.1.1	Rice	10	10										10	# produced	AG	Done	10	10	0	
1.1.2	Horticulture	23	18										18	# produced	AG	Done	18	18	0	
1.1.3	Postharvest	6	5										5	# produced	POST	Done	5	5	0	
1.1.4	Inputs and agriculture practices	36	42										42	# produced	AG, SI, BDS	Done	42	42	0	
1.2	Identify and form farmer groups (lead clients and clients)																			
1.2.1	Rice beneficiaries signed up	32,000	40,645										40,645	Farmers/households	AG (others)	++	40,645	40,827	-182	
1.2.2	Lead clients (demonstration sites) active	15,000	13,359	2,310				2,310					15,669	Active lead/demo clients up to date	AG (others)	x	15,669	15,275	394	To be accomplished in 2015 with village saving groups clients.
1.2.2.1	Rice demonstration sites (certified seed, GAPs, etc.)	3,000	3,580										3,580	Lead/Demo clients	AG (others)	++	3,580	3,623	-43	
1.2.2.2	Commercial horticulture demonstration sites	2,000	2,089										2,089	Lead/Demo clients	AG (others)	Done	2,089	2,089	0	
1.2.2.3	Home garden demonstration sites	10,000	7,690	2,310				2,310					10,000	Lead/Demo clients	AG (others)	x	10,000	9,563	437	To be accomplished in 2015 with village saving groups clients.
1.2.3	Graduated clients	5,810	5,877					2,724		3,201	2,300	5,501	14,102	Lead/Demo clients graduated from the program	AG (others)	+	5,877	6,524	7,578	
1.2.3.1	Rice	760	498		2,724			2,724					3,222	Graduated lead/demo clients	AG (others)	+	498	1,145	2,077	
1.2.3.2	Commercial horticulture	850	895							985			1,880	Graduated lead/demo clients	AG (others)	=	895	895	985	
1.2.3.3	Home garden	4,200	4,484							2,216	2,300	4,516	9,000	Graduated lead/demo clients	AG (others)	=	4,484	4,484	4,516	
1.2.4	Forestry community horticulture																			
1.2.4.1	Forestry community horticulture demonstration sites	15	17										17	Lead/Demo clients	AG (others)	Done	17	17	0	
1.2.4.2	Forestry community horticulture client	300	350										350	Clients	AG (others)	Done	350	350	0	
1.2.5	Evaluate, develop plan, and implement plan to incorporate village-level agriculture extension volunteers as program clients (in coordination with relevant government agencies)	210	27										27	Clients will be for the duration of the program, improve their technical skills for increased outreach and improved sustainable service delivery post-project (and to provide an income incentive for their services now)	Relevant government agencies, village/commune leaders, SI, Ag/Aquaculture	Done	27	27	0	
1.2.6	Scaling up activities	4,500	922	1,078				500	1,578				2,500	Scaling up client	AG (others)	+	2,000	2,140	360	
1.2.6.1	Commercial horticulture demonstration sites (vegetable scaling up)	3,000	922	1,078				1,078					2,000	Commercial horticulture Lead/Demo clients	AG (others)	++	2,000	2,140	-140	Done
1.2.6.2	Commercial staple crop producers (producer scaling up)	1,500	-					500	500				500	Producers with staple crops including corn, mung and soya beans	AG (others)	=	-	-	500	To be accomplished by LOP.
1.3	<b>Demonstrate new technologies (Technology Fund procurement and distribution for client farms)</b>																			
1.3.1	Increase adoption of new/improved technologies within target communities (e.g. drip irrigation, raised bed, trellis netting, etc.)	26	27										27	# individual new/improved technologies introduced to farmer folk in target communities	AG	Done	27	27	0	
1.3.2	Fruit tree seedlings (2 seedlings per home garden client)	13,976	10,517										10,517	Seedlings distributed	AG, OPS, SI (others)	Done	10,517	10,517	0	
1.3.3	Commercial drip irrigation systems	1,300	2,056	100	200	400		700					2,756	Systems procured, distributed and installed	AG, OPS (others)	++	2,156	3,239	-483	
1.3.4	Low cost home garden drip irrigation systems	6,350	5,084	100	200	216		516					5,600	Systems procured, distributed and installed	AG, OPS (others)	=	5,184	5,184	416	Drip irrigation system installation is an on-going process. It will be completed by Q3-2015.
1.3.5	Drip irrigation systems at school gardens	104	144										144	Systems procured, distributed and installed	AG, OPS (others)	Done	144	144	0	
1.3.6	Health centers assisted	63	63											Health centers identified and assisted	AG, OPS (others)	Done	63	63	0	
1.4	<b>Small-Scale Infrastructure Investments</b>																			
1.4.1	Redesign and rehabilitation of existing canal irrigation systems	3	3										3	Irrigation canals rehabilitated	AG, OPS (ae)	Done	3	3	0	
1.5	Extension visits to demonstration farms (by program agronomists and trained alliance partners)	174,621	228,926	18,000	18,000	18,000	20,379	74,379	9,000	8,000	695	17,695	321,000	Extension visits to lead/demo farms by program agronomists and trained alliance partners	AG (others)	+	246,926	313,608	7,392	
1.6	Group training on demonstration farms (by program agronomists and trained alliance partners)	504,496	616,114	25,000	25,000	27,752	27,752	105,504	8,000	6,000	382	14,382	736,000	Participants in all training types (training to include production, postharvest, business skills, marketing, other topics)	AG, POST, MKT, SI, BDS (others)	+	641,114	672,321	63,679	
1.7	Participants in village-level community field days (by program agronomists and trained alliance partners)	120,857	154,226	12,000	12,000	11,072	11,071	46,143	6,000	5,000	631	11,631	212,000	Participants in field day training type (training to include production, postharvest, business skills, marketing, other topics)	AG, POST, MKT, SI, BDS (others)	+	166,226	169,205	42,795	
1.8	Farm chemical safety training (participants)	58,402	67,454	6,198	6,800	6,800	6,800	26,598	3,000	2,000	948	5,948	100,000	Participants in FCS training	AG (input alliance partners, others)	+	73,652	76,992	23,008	
1.9	<b>USAID CRSP Integrated Pest Management activity</b>																			
1.9.1	Plant diagnostic training activities for universities, government, and private sector,	2	2				1	1				1	1	Field and laboratory trainings will be conducted for the identification and control of plant diseases	AG, HORTCRSP and RUA	=	2	2	2	
1.9.2	Trichoderma evaluations on selected commercial horticulture clients.	43	43										43	Growth and production data will be taken on 20 commercial horticulture sites, reviewed and submitted to USAID CRSP	AG, HORTCRSP and RUA	Done	43	43	0	
2	<b>Aquaculture &amp; Fisheries Program</b>																			
2.1	Development and production of technical manuals and other training materials for aquaculture and fisheries	16	16										16	Technical manuals and other training materials produced	FISH, AQUA	Done	16	16	0	
2.2	Increase adoption of new/improved technologies within target communities (e.g. improved cages, O <sub>2</sub> meters, pH testing, etc.)	16	16										16	Individual new/improved technologies introduced to fisher folk in target communities	FISH, AQUA	Done	16	16	0	



N°	Activity Description	Cumulative as of Year 4		Year 5 (Oct 2014 - Sep 2015)					Year 6 (Oct 2015 - Jun 2016)				TOTAL EXPECTED LOP	Deliverables	Responsibilities	Progress Monitor (as of December 31st, 2014)				
		Target	Actual	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Q4 Jul-Sep	Total	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Total				Status	To Date Target	To Date Actual	Balance from LOP target	Comments
<b>2.3</b>	<b>Aquaculture Program</b>																			
2.3.1	Establishment of low- and medium input aquaculture demonstration ponds with lead clients (Low input in conjunction with home gardens)	600	632										632	Demonstration ponds established (lead clients)	AQUA	Done	632	632	0	
		1,200	1,353										1,353	Other low-input aquaculture clients	AQUA	Done	1,353	1,353	0	
2.3.2	Establishment of household based hatchery clients	15	15										15	Demonstration fish hatcheries	AQUA	Done	15	15	0	
2.3.3	Establishment of Med-sized Commercial hatcheries	2	1										1	Commercial Hatcheries	AQUA	Done	1	1	0	
2.3.4	TA Extension Visits/Group Trainings on demonstration aquaculture ponds (by program technicians and trained alliance partners)	25,629	31,952	2,315	2,315	2,315	2,103	9,048	20	20		40	41,040	# Demo site TA Extension Visit/Group Training (individual/group)	AQUA	+	34,267	35,156	5,884	
2.3.5	Participants at TA Extension Visits/Group Trainings on demonstration aquaculture ponds	73,971	90,683	4,480	4,480	4,480	3,877	17,317	20	20		40	108,040	Participants at demo site extension visit/training	AQUA	+	95,163	101,360	6,680	
2.3.6	Village-level Field Day Training Events	1,635	1,763	100	133	150	150	533	2	2		4	2,300	# Field day training events	AQUA	+	1,863	1,972	328	
2.3.7	Participants in village-level Field Day Training Events	46,452	46,617	3,670	3,670	3,670	3,885	14,895	20	20		40	61,552	Community members attending aquaculture Field Day Training Events	AQUA	+	50,287	52,245	9,307	
2.3.8	Technical Assistance to Fisheries Administration on defined priority initiatives (specific initiatives to be determined)	3	2				1	1					3	Initiatives initiated with Fisheries Administration; ongoing implementation	AQUA	=	2	2	1	
2.3.9	Development of "Cambodia Inland Fish farmers' Input Suppliers Guide" (to improve the accessibility of aquaculture inputs through identification of local producers (fingerlings) and importers (feed, equipment))	1	1										1	Fish farmers Supply Guide produced (ongoing updates and dissemination)	AQUA	Done	1	1	0	
2.3.10	Technical Assistance to the University of Battambang on defined aquaculture priority initiative (Specific initiatives TBD)	3	2				1	1					3	Initiatives initiated with the University of Battambang, on going implementation	AQUA	=	2	2	1	Activities were completed, there is no further initiative required.
<b>2.4</b>	<b>Fisheries Program</b>																			
2.4.1	Establishment of Demo sites with Community Fisheries (CFI) Partner Clients (Refuge Ponds, Cage Culture, etc.)																			
2.4.1.1	Community Refuge Ponds/Fish Sanctuary	15	15										15	Community Refuge Ponds demonstration sites established	FISH	Done	15	15	0	
2.4.1.2	Cage culture demo sites with lead clients in floating villages on Tonle Sap	33	36										36	Cage culture demonstration sites with lead clients in floating villages on Tonle Sap established	FISH	Done	36	36	0	
2.4.1.3	Development of refuge pond/fish sanctuary action plan	15	15										15	Refuge pond / fish sanctuary action plan	FISH	Done	15	15	0	
2.4.2	Extension Visits to CFI lead clients/demonstration sites	2,400	3,743	150	150	150	100	550	10			10	4,303	Extension visits	FISH	+	3,893	4,082	221	
2.4.3	Conduct Conservation Field Training Events w/ target CFI communities	317	363	12	12	12	12	48	2			2	413	Field Days to raise awareness on sustainable community fisheries	FISH	+	375	378	35	
2.4.4	Participants in technical assistance and training events on sustainable fisheries (communities to receive effective community-based management training)	24,919	24,311	12	12	12	12	48	5			5	24,364	Participants in training and TA events	FISH	++	24,323	25,039	-675	
2.4.5	Facilitate CFI Congress meetings at target CFIs	12	12		1	1	1	3					15	Congress Meetings	FISH	+	12	13	2	
2.4.6	Fish Sanctuary and/or Refuge Pond watch towers	9	6										6	Sanctuary/Refuge Pond Watch Towers	FISH	Done	6	6	0	
<b>3</b>	<b>NRM, Environment and Climate Change</b>																			
<b>3.1</b>	<b>Global Climate Change</b>																			
3.1.1	Design a spatial database (geo-located digital photographs, land use survey forms, forest and soil survey databases, etc.)	1	1										1	Report, GIS maps, database	ARUNA	Done	1	1	0	
3.1.2	Develop a REDD+ Feasibility Study for the Central Cardamoms Protected Forest (CCPF)	1	1										1	REDD+ Feasibility Study for CCPPF	FFI/ARUNA	Done	1	1	0	
3.1.2.1	Conduct Opportunity Cost Analysis of competing land uses (socio-economic assessment) for CCPPF	1	1										1	A component of Feasibility Study	FFI	Done	1	1	0	
3.1.2.2	Analysis of Human Disturbance over time (roads, settlements, etc.) in the CCPPF	1	1										1	A component of Feasibility Study	FFI/ARUNA	Done	1	1	0	
3.1.3	Field-based forest carbon inventory training for Government	1	1										1	20 government staff trained on latest international standard carbon inventory techniques. Also rough estimate of carbon value for CCPPF	FFI	Done	1	1	0	
3.1.4	Translation of key GCC/REDD documents from English to Khmer	1	1										1	Translation of key GCC/REDD documents from English to Khmer	FFI	Done	1	1	0	
3.1.5	Local Capacity Development in GCC																			
3.1.5.1	Development and delivery of GCC/REDD/PES courses at RUPP	1	1										1	Curriculum developed and delivered for RUPP	FFI	Done	1	1	0	
3.1.5.2	Development and delivery of Remote Sensing and GIS courses for REDD analysis at RUA	1	1										1	Curriculum developed and delivered for RUA	ARUNA	Done	1	1	0	
3.1.5.3	Development and delivery of 3-day officially recognized training courses on GCC/REDD for national government counterparts (in conjunction with RUPP)	20	35										35	Trained FA (and MoE) staff from departments responsible for Climate Change/REDD	FFI	Done	35	35	0	
3.1.5.4	Training for local government (commune and district, including PA staff) on climate change, mitigation	65	65										65	Participants (estimated 4 events)	FFI	Done	65	65	0	
3.1.5.5	Certified Training of FA Staff in GIS and Remote Sensing Software	5	5										5	FA staff trained	ARUNA	Done	5	5	0	
3.1.5.6	Custom training of FA staff in land cover mapping methodology/REDD	10	10										10	FA staff trained	ARUNA	Done	10	10	0	

N°	Activity Description	Cumulative as of Year 4		Year 5 (Oct 2014 - Sep 2015)					Year 6 (Oct 2015 - Jun 2016)				TOTAL EXPECTED LOP	Deliverables	Responsibilities	Progress Monitor (as of December 31st, 2014)				
		Target	Actual	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Q4 Jul-Sep	Total	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Total				Status	To Date Target	To Date Actual	Balance from LOP target	Comments
3.2	<b>NRM/Biodiversity Conservation</b>																			
3.2.1	Establishment of Lead Client Demo sites on NTFFPs (bamboo, rattan, water hyacinth)	83	87										87	Demonstration sites identified and established	FFI/NRM	++	87	88	-1	
		466	491										491	HtHs participating in demonstration sites (lead clients, other clients, and new employment)	FFI/NRM	++	491	581	-90	
3.2.2	Establishment of bamboo and rattan commercial plantings demo sites	16	16										16	1 bamboo and 1 rattan site in each province	FFI/NRM	Done	16	16	0	
3.2.3	Bamboo and Rattan enriched planting (hectares)	50	60			50		50					110	Hectares of enrichment planting	FFI/NRM	+	60	65	45	
3.2.4	Pilot bamboo charcoal briquetting technology	2			2			2					2	1 pilot briquetting facility per province	FFI/NRM	=	-	-	2	
3.2.5	Establishment of province-based NTFF producer organizations	3	2										2	4 organizations developed	FFI/NRM	Done	2	2	0	
3.2.6	TA Extension Visits and/or Group Training at NRM demonstration sites (by program technicians and trained alliance partners)	12,749	16,831	1,000	1,000	1,000	278	3,278			291	291	20,400	# TA Extension Visits and/or Group Training per month per NRM Demo site	FFI/NRM	+	17,831	18,281	2,119	
3.2.7	Participants at TA Extension Visits/Group Trainings on NRM demonstration sites	79,060	94,553	5,000	5,000	5,000	1,701	16,701			1,746	1,746	113,000	Participants at TA Extension Visits and/or Group Trainings	FFI/NRM	+	99,553	101,899	11,101	
3.2.8	Village-level Field Day Training Events	1,085	1,258	64	60	60	20	204			48	48	1,510	# Field day events	FFI/NRM	+	1,322	1,371	139	
3.2.9	Participants in village-level community field day events (community based management training)	32,771	38,957	3,250	3,250	3,250	1,153	10,903			1,440	1,440	51,300	Participants	FFI/NRM	+	42,207	42,217	9,083	
3.2.10	<b>Establish &amp; Implement Community Conservation Activities</b>																			
3.2.10.1	Tree nurseries	7	7										7	Tree nurseries	FFI/NRM	Done	7	7	0	
3.2.10.2	Wood lots and Agro-forestry areas	24	24										24	Lots & Sites / Village	FFI/NRM	Done	24	24	0	
3.2.11	<b>Provide Technical Support to CF</b>																			
3.2.11.1	Silviculture training to CFs	15	-	15	15			30					30	Trainings delivered	FFI/NRM	x	15	4	26	
3.2.11.2	CF registration/inventory/mgmt. plan TA support	32	32										32	Signing ceremonies, inventories and/or mgmt. plans completed (CF dependent)	FFI/NRM	Done	32	32	0	
3.2.11.3	Pilot commercial activities in target CF's	6	-		5	5		10					10	Commercial Enterprises developed	FFI/NRM	=	-	-	10	
3.2.11.4	Implement Forest Restoration (dry land/flooded areas)	31	30.5										31	Ha of flooded forest reforested	FFI/NRM	Done	31	30.5	0	
		97	97										97	Ha of dry forest reforested	FFI/NRM	Done	97	97	0	
3.2.12	Technical support to RGC on PA Mgmt.	423,000	423,000										423,000	Ha in areas of biological significance under improved NRM	FFI/NRM	Done	423,000	423,000	0	
3.2.13	Establishment of District-level watershed management committees	6	4	2				2					6	Watershed mgmt. committees established in 4 provinces (4 in Pursat/Battambang, and 2 in Kampong Thom)	FFI/NRM	x	6	5		One remaining site will be established by 2015.
4	<b>Social Inclusion &amp; Nutrition Program</b>																			
4.1	<b>Mainstream social inclusion target groups into all program activities</b>																			
4.1.1	Total poor clients as a percentage of total clients	35%	19%	25%	25%	25%	25%	25%					25%	% of total clients that are both from poor 1 & 2	SI, ALL (others)	x	25%	21.6%	3.4%	Activities to be accomplished by the end of 2015.
4.1.2	Extreme poor clients as a percentage of total clients	15%	8%	10%	10%	10%	10%	10%					10%	% of clients that are extreme poor	SI, ALL (others)	x	10%	9.3%	0.7%	
4.1.3	Average poor clients as a percentage of total clients	20%	11%	15%	15%	15%	15%	15%					15%	% of clients that are average poor (poor 2)	SI, ALL (others)	x	15%	12.3%	2.7%	
4.1.4	Women clients as a percentage of total clients	50%	54%	50%	50%	50%	50%	50%					50%	% of clients that are women	SI, ALL (others)	++	50%	54.2%	-4.2%	
4.1.5	Youth clients as a percentage of total clients	30%	20%	30%	30%	30%	30%	30%					30%	% of clients that are youth (based on RGC definition)	SI, ALL (others)	x	30%	20.3%	9.7%	Activity to be accomplished by the end of 2015.
4.2	<b>Design and implement specific projects and activities for target social inclusion groups</b>																			
4.2.1	Operation & Maintenance training for mechanized farm machinery																			
4.2.1.1	Village-based training	15,403	11,403										11,403	# participants receiving training	SI, BDS	Done	11,403	11,403	0	
4.2.1.2	Center-based training	60	133					60					193	# participants selected for training	SI, BDS	=	133	133	60	
4.2.1.3	Village-based/mobile rice millers	600	1,070					400					1,470	# millers receiving training	SI	+	1,070	1,203	267	
4.2.2	Women's fish processing project	400	593										593	Individuals/MSMEs that received TA, training and mentoring to improve and/or expand a) hygiene/sanitation, b) equipment, c) market strategies.	SI (lead), Market, BDS (others)	Done	593	593	0	
4.2.3	Financial literacy training	10,692	25,268					3,508					28,776	Number of participants in village receiving training	SI, BDS, Finance	++	25,268	42,347	-13,571	
4.2.3.1	Food Security Nutrition Groups	4,000	6,044										6,044	Number of participants in village receiving training	SI, BDS, Finance	++	6,044	13,360	-7,316	
4.2.3.2	Horticulture component	3,300	12,927					3,000					15,927	Number of participants in village receiving training	SI, BDS, Finance	++	12,927	17,307	-1,380	
4.2.3.3	Rice component	1,050	2,432					200					2,632	Number of participants in village receiving training	SI, BDS, Finance	++	2,432	5,938	-3,306	
4.2.3.4	Aquaculture & fisheries component	400	1,781					100					1,881	Number of participants in village receiving training	SI, BDS, Finance	++	1,781	3,544	-1,663	
4.2.3.5	Input suppliers & hatcheries	1,450	1,417	33	50			83					1,500	Number of participants in village receiving training	SI, BDS, Finance	x	1,450	1,417	83	Activity to be completed by Q2- 2015.
4.2.3.6	Forestry component (including NTFFP)	342	548					58					606	Number of participants in village receiving training	SI, BDS, Finance	++	548	662	-56	
4.2.3.7	Women fish processors	150	119	60	71			131					250	Number of participants in village receiving training	SI, BDS, Finance	x	179	119	131	Activity to be completed by Q2-2015.

N°	Activity Description	Cumulative as of Year 4		Year 5 (Oct 2014 - Sep 2015)					Year 6 (Oct 2015 - Jun 2016)				TOTAL EXPECTED LOP	Deliverables	Responsibilities	Progress Monitor (as of December 31st, 2014)				
		Target	Actual	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Q4 Jul-Sep	Total	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Total				Status	To Date Target	To Date Actual	Balance from LOP target	Comments
4.2.4	Savings-led microfinance												147	Number of funds established	SI, BDS, Finance	Done	147	147	0	
4.2.4.1	Savings funds established	80	147																	
4.2.4.2	Members received training/mentoring	1,200	2,440										2,440	Number of members received training/mentoring	SI, BDS, Finance	Done	2,440	2,440	0	
4.2.5	Mushroom growing	500	-		200	200		400					400	People from vulnerable groups receive training/TA to establish mushroom growing microenterprises	SI, BDS, Finance	Cancelled	-	-	400	Activity was cancelled, associated funds diverted to nutrition activities.
4.3	<b>Nutrition</b>																			
4.3.1	Family nutrition education delivered at household and community levels																			
4.3.1.1	Training participants under home garden demonstration sites	53,000	59,379										59,379	Participants in nutrition education activities targeting household-level	SI	++	59,379	63,049	-3,670	
4.3.1.2	Training FNSG participants	11,500	34,065	10,000	10,000	6,000	6,000	32,000	6,000			6,000	72,065	Participant in family nutrition training	SI	+	44,065	54,414	17,651	
4.3.1.3	Training participants besides home garden demonstration sites	118,456	166,412	10,000	10,000	10,000	9,544	39,544					205,956	Participants in nutrition education activities targeting household-level	Other component besides SI	+	176,412	188,078	17,878	
4.3.1.4	Training participants under mobile kitchen project	52,000	77,477	10,000	10,000	10,000	8,000	38,000	2,000			2,000	117,477	Participants in nutrition education activities	SI, ALL (others)	+	87,477	102,204	15,273	Training activities planned and scheduled for the following quarter.
4.3.2	Community initiatives to increase knowledge and improve behavior related to food security and nutrition																			
4.3.2.1	Community based nutrition activities																			
4.3.2.1.1	Number of health centers participating	63	63										63	Clients will be for the duration of the program, improve their technical skills for increased outreach and improved sustainable service delivery post-project (and to provide an income incentive for their services now)	Relevant government agencies, village/commune leaders, SI, Ag/Aquaculture	Done	63	63	0	
4.3.2.1.2	Number of HC staff participating	300	350	25	25			50					400	Number of HC staff trained	SI (others)	++	375	510	-110	
4.3.2.1.3	Number of schools participating	130	144										144	Schools have received garden training	SI (others)	Done	144	144	0	
4.3.2.1.4	Number of students participating	17,373	19,565	1,000	1,000	627		2,627					22,192	# of students trained	SI (others)	+	20,565	20,571	1,621	
4.3.2.2	Awareness training for commune councils	361	296	40	40	40	34	154					450	Participants trained	SI (others)	+	336	423	27	
4.3.3	Nutritional analyses of traditional foods including dietary surveys of sample client households	1	1										1	Nutritional analyses conducted for	SI (others)	Done	1	1	0	
4.4	<b>Wide-Scale Awareness and Social Marketing</b>																			
4.4.1	Design and deliver technical, public awareness and training modules for use at district, commune and community levels that focus on a) dissemination of technical information, and b) HARVEST issues such as environment, climate change and food security/nutrition	20	24										24	Training modules designed and delivered	SI, COM, ALL (others)	Done	24	24	0	
4.4.2	Design and deliver technical modules and short-term training courses for use to develop capacity of local NGOs, government agencies and other partners that focus on selected HARVEST issues (e.g., gender & social inclusion, family nutrition, CCA, technical agriculture)	25	30										30	Training modules/courses designed and delivered	SI, COM, ALL (others)	Done	30	30	0	
4.4.3	Develop and deliver social marketing and behavior change programming using TV, radio and other media to reach general public audience on issues that complement HARVEST work in agriculture, fisheries, NRM, nutrition, etc.	4	5		1	1	2	4					9	Programming developed and delivered	SI, COM, ALL (others)	=	5	5	4	
5	<b>Capacity Building - BDS Providers</b>																			
5.1	<b>NGOs &amp; CBO Alliance Partners (USAID FORWARD Initiative)</b>																			
5.1.1	Selection of NGO & CBO Partners to provide extension and other services to program's target communities (covering agriculture crops, aquaculture, fisheries, forestry/NRM)	26	30										30	CBOs and NGOs enter program (signed subcontracts and field activities commence)	SI (with support from OPS and ALL)	Done	30	30	0	
5.1.2	<b>Capacity Building of CBO/NGO Partners</b>																			
5.1.2.1	Development of improved financial, accounting, procurement systems, including improved staff capabilities (and understanding of USG procurement regulations for future direct contracting with USAID)	On-going	On-going					On-going						Systems improved and staff trained	OPS	On-going	On-going	On-going	N/A	
5.1.2.2	Development of improved systems and staff capabilities in monitoring and evaluation	On-going	On-going					On-going						Systems improved and staff trained	M&E	On-going	On-going	On-going	N/A	
5.1.2.3	Technical training of NGO field-based staff (through mentor relationships with program technicians)	On-going	On-going					On-going						Field staff trained & skills improved	ALL	On-going	On-going	On-going	N/A	
5.2	<b>Input supplier enhancement and training programs</b>	400	400	20	20	20		60					460	Input suppliers active in program and receiving technical assistance and training	BDS (lead) with support from AG, FISH, etc.	+	420	432	28	
5.2.1	Technical skills training (agronomy, postharvest, chemical safety, biologicals, etc.) to input supplier owners and staff	1,600	1,592	30	20	20		70					1,662	Input suppliers (including staff and family members) participated in training events	AG, POST, FISH	++	1,622	1,677	-15	
5.2.2	Shop & inventory upgrades (expansion of products offered, particularly new technologies being promoted by the project)	250	271	5	15	10		30					301	Shops upgraded with new products and customer information boards	AG, POST, FISH, BDS	+	276	277	24	
5.2.3	New services offered (tractor/equipment rentals, seeding, seedlings, etc.)	128	127	2	5	5	5	17					144	Input stores offering new services to target clients	AG, FISH, BDS	+	129	132	12	
5.2.4	Expanded relationships with national and provincial input supply chains as well as selected international companies in Cambodia	100	124	2	5	5	2	14	2	2		4	142	Input suppliers entering into formal distributor relationships	BDS, AG, FISH	+	126	134	8	
5.2.5	Demonstration plots installed at input supply locations (with available land) to promote new technologies and products	105	123		1			1					124	Input stores with demo plots and input suppliers trained	AG, FISH (others)	++	123	130	-6	
5.2.6	Distribution of technical information materials	22	22		1			1					23	Technical bulletins made available to input suppliers	COM, BDS	=	22	22	1	
		370,000	408,570		120			120					408,690	Copies distributed to input suppliers customers and stakeholders	All	++	408,570	424,209	-15,519	
5.2.7	Improved business skills and partnerships	2,497	2,691		10	20		30					2,721	Trainings (including study tours) and technical assistance on business skills and services	BDS	+	2,691	2,699	22	
5.3	<b>NRM / value chain micro enterprise BDS training</b>	41	42	10	10	5		25					67	Micro enterprises trained	BDS, NRM	x	52	42	25	Activity to be completed by end of FY2015.
5.4	<b>Seedling nurseries constructed</b>	6	7	3	2	2		7					14	Seedling nursery businesses	BDS	=	10	10	4	

N°	Activity Description	Cumulative as of Year 4		Year 5 (Oct 2014 - Sep 2015)					Year 6 (Oct 2015 - Jun 2016)				TOTAL EXPECTED LOP	Deliverables	Responsibilities	Progress Monitor (as of December 31st, 2014)				
		Target	Actual	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Q4 Jul-Sep	Total	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Total				Status	To Date Target	To Date Actual	Balance from LOP target	Comments
6	<b>Marketing &amp; Market Analysis</b>																			
6.1	Crop and product-specific market surveys	7	7										7	Crop and product specific market surveys produced and disseminated	MKT	Done	7	7	0	
6.2	General market surveys and information sharing for HARVEST and government																			
6.2.1	Survey market prices and share findings with technicians (every week at one major market in town)	247	329	12	12	12	12	48	12			12	389	Market price surveys conducted	MKT	++	341	440	-51	
6.2.2	Survey demand from buyers and share findings with technicians (every month from three markets/prov.)	61	127	4	4	4	4	16	4			4	147	Market demand surveys conducted and disseminated	MKT	++	131	161	-14	
6.3	Specific market surveys (wider level – village/market structure, market acceptance) and sharing for HARVEST and government	4	4										4	Other market surveys conducted (with updates in later years)	MKT	Done	4	4	0	
6.3.1	NTPF market study (rattan and bamboo)	2	2										2	# of NTPF market survey conducted	MKT	Done	2	2	0	
6.3.2	National/regional level market study	5	3										3	# of national / regional market study	MKT	Done	3	3	0	
6.3.3	Other specific market study	6	4										4	# of other specific market survey conducted	MKT	Done	4	4	0	
6.4	Identify and establish formal and informal markets/buyers for program clients and others																			
6.4.1	Identify buyers	563	565	5	5	5		15					580	Buyers identified	MKT	+	570	574	6	
6.4.2	Link buyers and producers through field days, direct individual clients and producer groups	1,700	1,596	15	30	15		60					1,656	Linkage made	MKT	++	1,611	2,452	-796	
6.4.3	Marketing workshop for buyers	14	10	2	4	4		10					20	Workshops conducted	MKT	=	12	12	8	
6.5	Evaluate and help implement simple market information reporting and dissemination methods (e.g. mobile phone MMS price and buyer opportunities)																			
6.5.1	Evaluate potential systems and identify partners (government and others)	1	1										1	Evaluation report completed, system designed, partner(s) identified	MKT	Done	1	1	0	
6.6	Train counterparts, trade associations and government staff in market analysis methodologies for agriculture and other target crops/products	230	240	20	25	25	20	90					330	Counterpart staff trained in market analysis	MKT	+	260	267	63	
7	<b>Finance &amp; Financial Services</b>																			
7.1	Develop Credit Information Sharing mechanism (CIS) so that farmers have access to various financial products available in the market (# villages)	120	100	5	5	5	5	20					120	Credit information system within target villages (billboards)	FIN	Cancelled	105	100	20	Activity was cancelled, associated funds diverted to marketing workshops.
7.2	Train MFI lending staff in agricultural loan analysis and assessment	532	623	10	10	10	10	40	12			12	675	MFI and other financial institution lending staff training in agricultural loan analysis	FIN, AG, AQUA	++	633	699	-24	
7.3	Linking farmers to MFI through agriculture field days	7,158	10,300	200	200	200	200	800	240			240	11,340	Number of farmers participated in field days	FIN, AG, AQUA	++	10,500	11,871	-531	
7.4	Produce financial assessment tools and cash flows for all primary target products	14	12		1	1		2					14	Assessments tools and cash flows produced (with ongoing updates)	FIN, POST, AG, AQUA	=	12	12	2	
7.5	Assist agribusinesses (mills, NTPF, input suppliers) in developing business plans, feasibility studies, and loan applications	50	49			1		1					50	Agribusinesses assisted with development of business plans, feasibility studies, and/or loan applications	POS, FIN, BDS, POST, AG, AQUA (emc)	=	49	49	1	
7.6	Train rice millers in post-harvest management machinery operations and maintenance rice standards, business plan, business formalization, etc.	80	32	18	10	10	10	48					80	# of rice millers	FIN	x	50	32	48	Activity to be completed by the end of FY2015.
7.7	Evaluate pilot small-scale warehouse receipts program for rice at community levels	1	1										1	Pilot (community-level) warehouse receipts programs for rice implemented	FIN, POL, AG (STTA)	Done	1	1	0	
7.8	Train small agribusinesses and commercial horticulture clients on record keeping to increase working capital	360	349	60	60	60	71	251					600	Input stores and others accessing financing from banks, distributors, or other sources	FIN, BDS, AG	+	409	560	40	
7.9	Private public partnerships																			
7.9.1	Universities & development partners	3	4										4	Provincial lab established and operating	BDS, AG and POL	Done	4	4	0	
7.9.2	Agri-businesses	10	11										11	# of partner alliance join co-investment	AG and All	Done	11	11	0	
8	<b>Policy, Analysis, and Enabling Environment</b>																			
8.1	Comprehensive review of RGC agricultural strategy policies and documents (compare what we have to their priorities)	-	-											RGC agriculture strategies	POL	=	-	-	N/A	
8.2	Support to public sector counterparts for effective policies and regulations that improve efficiencies and enabling environment																			
8.2.1	Sub-decree of Uniform of Seed Inspectors (Khmer)	1	1					On-going					1	Policies and regulations as a result of program assistance	POL, AG	Done	1	1	0	
8.2.2	National Seed Standards	1	1					On-going					1	Policies and regulations as a result of program assistance	POL, AG	Done	1	1	0	
8.2.3	Prakas on Seed Quality Certification	1	1					On-going					1	Policies and regulations as a result of program assistance	POL, AG	Done	1	1	0	
8.2.4	National Seed Policy	1	1					On-going					1	Policies and regulations as a result of program assistance	POL, AG	Done	1	1	0	
8.2.5	Assist MAFF in producing regulations on plant breeders rights	1	1					On-going					1	One regulation on plant breeders rights	POL, AG	Done	1	1	0	
8.2.6	Assist MAFF in preparing technical procedures on quality rice seeds production	1	-					On-going					1	Technical procedure (code of conduct) on quality rice seeds production	POL, AG, STTA	On-going	On-going	On-going	1	
8.2.7	Legal aspects of exporting Cambodian rice produced from foreign rice seeds	1	1					On-going					1	Technical Study Report Completed	POL, AG, STTA	Done	1	1	0	
8.2.8	Assist relevant government agencies to establish food safety regulations	1	1					On-going					1	Food safety regulations established	POL, AG, POST	Done	1	1	0	
8.2.9	Develop code of practice for grades and standards for rice for the RGC (in cooperation with other development partners, MoC and private sector)	-	-					On-going					-	Code of practice (grades and standards) development for rice	POL, AG	Cancelled	-	-	0	Activity dropped since the government priorities changed.
8.2.9	Assist RGC in preparing policies or regulations promoting sustainable NRM and conservation (includes laws, sub-decrees, and directives on biodiversity and conservation)																			

N°	Activity Description	Cumulative as of Year 4		Year 5 (Oct 2014 - Sep 2015)					Year 6 (Oct 2015 - Jun 2016)				TOTAL EXPECTED LOP	Deliverables	Responsibilities	Progress Monitor (as of December 31st, 2014)				
		Target	Actual	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Q4 Jul-Sep	Total	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Total				Status	To Date Target	To Date Actual	Balance from LOP target	Comments
8.2.9.1	Assist MoE (GDANCP) to revise NBSAP – Phase 1 (2013)	1	1					On-going					1	Policies and regulations as a result of program assistance	POL, NRM	Done	1	1	0	
8.2.9.2	Assist MoE (GDANCP) to develop Framework Strategy for development of National Protected Areas Strategic Management Plan	1	1					On-going					1	Policies and regulations as a result of program assistance	POL, NRM	Done	1	1	0	
8.2.9.3	Assist FA to develop benefit sharing mechanisms in community forests	-	-					On-going					-	Policies and regulations as a result of program assistance	POL, NRM	Done	-	-	0	
8.2.9.4	Assist MoE (GDANCP) to revise NBSAP – Phase 2 (2014)	-	-					On-going					-	Policies and regulations as a result of program assistance	POL, NRM	Done	-	-	0	
8.2.10.5	Assist FA to review the effectiveness of Community Forestry Implementation [Dropped]	-	-					On-going					-	Policies and regulations as a result of program assistance	POL, NRM	Done	-	-	0	Activity dropped since the government priorities changed
8.2.10	Assist MAFF in developing policy on agriculture extension	-	-					On-going					1	Policies and regulations as a result of program assistance	POL, AG	On-going	On-going	On-going	1	
8.2.11	Assist MAFF in drafting joint Prakas on Seed Quality Inspection	-	-					On-going					-	Policies and regulations as a result of program assistance	POL, AG	On-going	On-going	On-going	0	
8.2.12	Assist MAFF to draft joint Prakas on Service Feed for Seed Quality Inspection	-	-					On-going					-	Policies and regulations as a result of program assistance	POL, AG	Done	-	-	0	
8.2.13	Assist MAFF in developing horticulture strategic plan	-	-					On-going				On-going	-	Policies and regulations as a result of program assistance	POL, AG	Done	-	-	0	To be initiated
8.2.15	Policy document on agriculture equipment imports	-	-					On-going					1	Policies and regulations as a result of program assistance	POL, AG	=	-	-	1	
8.2.14	Assist MAFF in registering biological products	-	-					On-going					-	Policies and regulations as a result of program assistance	POL, AG	Done	-	-	0	
8.2.17	Assist MAFF in developing rice drying strategies [Dropped]	-	-					On-going					1	Policies and regulations as a result of program assistance	POL, AG	=	-	-	1	Activity dropped in 2013.
8.3	<b>Analytic Cross-Cutting</b>																			
8.3.1	Conduct a feasibility study and provide recommendations for private warehouse receipts systems for rice	1	1										1	Evaluation to lead to specific activities that will be detailed in updated work plan	POL, FIN, AG, STTA (emc)	Done	1	1	0	
8.3.2	Social economic assessments of potential irrigation projects for certified rice and high value crops	16	16										16	Economic assessments of potential irrigation projects conducted	AG, POL	Done	16	16	0	
8.3.3	Product costs and profitability analysis	22	22										22	Production cost surveys conducted	POL, M&E, AG	Done	22	22	0	
8.4	<b>National, provincial and local government coordination</b>																			
8.4.1	Project level coordination in working on policy and enabling environment related activities	On-going	On-going					On-going						Coordination, processes	POL	On-going	On-going	On-going	N/A	
8.4.2	Participation at Provincial government Level NGO Coordination Forums	On-going	On-going					On-going						Coordination, processes	POL, ALL	On-going	On-going	On-going	N/A	
8.4.3	Coordination with technical line departments (national & provincial) in target districts – including regular meetings, field days and other program events, dissemination of project communications, extension staff attachments	On-going	On-going					On-going						Coordination, processes	POL, ALL	On-going	On-going	On-going	N/A	
8.4.4	Coordination at district, commune and village levels -- including regular meetings, field days and other program events, dissemination of project communications, extension staff attachments	On-going	On-going					On-going						Coordination, processes	POL, ALL	On-going	On-going	On-going	N/A	
9	<b>Limited Participant Training Program</b>																			
9.1	Development of local participant training programs with local universities (including potential field internships with program technicians)	40	43										43	Participants in programs developed with local universities (including field internships with program technicians)	TRAIN, ALL	++	43	48	-5	
9.2	Identification and development of shorter-term certificate based programs in critical technical needs areas (local, regional and US)	106	170										170	Placements in shorter-term programs (local, regional and US)	TRAIN (ie), ALL	++	170	174	-4	
9.3	Identification and development of longer-term (e.g. MSc) programs in critical technical needs areas (US)	6	6										6	Placements in longer-term programs at US institutions	TRAIN (ie), ALL	Done	6	6	0	
9.4	Identification and development of longer-term (e.g. MSc) programs in critical technical needs areas (regional)	4	4										4	Placements in longer-term programs at regional institutions	TRAIN (ie), ALL	Done	4	4	0	
9.5	Identification and development of longer-term Cambodian-based programs (e.g. MScs) in critical technical needs areas (e.g. nutrition, biodiversity)	66	56										56	Placements in longer-term programs at local institutions	TRAIN, ALL	Done	56	56	0	
9.6	Limited skills and vocational trainings (youth and poor households)	13,000	13,040										13,040	Priority will be given to women to increase the availability of trained practical agronomists and other specialists to improve their technical skills for future employment	SI, AG, FISH, NRM	Done	13,040	13,040	0	
9.6.1	Community nutrition and saving groups training	5,800	8,484										8,484	People trained	SI, AG	Done	8,484	8,484	0	
9.6.1.1	Food security & nutrition groups	4,000	6,044										6,044	People trained	SI, AG	Done	6,044	6,044	0	
9.6.1.2	Saving fund groups	1,800	2,440										2,440	People trained	SI, AG	Done	2,440	2,440	0	
9.6.2	Fish processing (phase 2)	275	287										287	People trained	SI, FISH	Done	287	287	0	
9.6.2.1	Fish processing on poor women on flooded villages	175	229										229	People trained	SI, FISH	Done	229	229	0	
9.6.2.2	Fish processing - value added aquaculture	100	101										101	People trained	SI, FISH	Done	101	101	0	
9.6.3	Small machinery operational and maintenance training	8,170	8,403										8,403	People trained	SI	Done	8,403	8,403	0	
9.6.3.1	Small machinery operational and maintenance training - rice millers	1,170	1,180										1,180	People trained	SI	Done	1,180	1,180	0	
9.6.3.2	Small machinery operational and maintenance training - equipment owners	7,000	7,923										7,923	People trained	SI	Done	7,923	7,923	0	



N°	Activity Description	Cumulative as of Year 4		Year 5 (Oct 2014 - Sep 2015)					Year 6 (Oct 2015 - Jun 2016)				TOTAL EXPECTED LOP	Deliverables	Responsibilities	Progress Monitor (as of December 31st, 2014)				
		Target	Actual	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Q4 Jul-Sep	Total	Q1 Oct-Dec	Q2 Jan-Mar	Q3 Apr-Jun	Total				Status	To Date Target	To Date Actual	Balance from LOP target	Comments
<b>10</b>	<b>Monitoring &amp; Evaluation</b>																			
<b>10.1</b>	<b>Performance Monitoring Plan</b>																			
10.1.1	Indicators reviewed on regular basis to meet future USAID/W/TF and USAID/Cambodia guidance and needs	On-going	On-going					On-going					On-going	-	New indicators added as required based on changing USAID requirements	M&E	On-going	On-going	On-going	N/A
10.1.2	PIRS finalized for any new indicators and/or adjusted for changes in USAID indicator definitions	On-going	On-going					On-going					On-going	-	PIRS added or amended as required	M&E	On-going	On-going	On-going	N/A
10.1.3	PMP indicator targets reviewed based on results; adjusted as required with USAID approval	On-going	On-going					On-going					On-going	-	PMP indicator targets reviewed on annual basis	M&E	On-going	On-going	On-going	N/A
<b>10.2</b>	<b>Workplan Performance Monitoring</b>																			
10.2.1	Workplan Performance Monitoring Plan developed for each annual workplan (to capture activity deliverables targets, including sources, timing, verification, and methodologies)	3	3	1				1	1				1	5	Workplan Performance Monitoring Plans developed	M&E	=	4	4	1
10.2.2	Collection and compilation of data for activity deliverable targets; monthly reports to program management (including quarterly and annual comprehensive reports)	25	37	3	3	3	3	12	3	3			6	55	Monthly reports on workplan progress (including more comprehensive quarterly and annual reports)	M&E	=	40	40	15
<b>10.3</b>	<b>CIRIS M&amp;E System Management</b>																			
10.3.1	Customization of CIRIS M&E system for HARVEST indicators (PMP and workplan)	1	1										1		CIRIS customized as required	M&E, IT	Done	1	1	0
10.3.2	Ongoing data collection by project staff for performance monitoring	On-going	On-going					On-going					On-going	-	All project staff enter data on on-going (daily) basis into CIRIS	ALL, M&E	On-going	On-going	On-going	N/A
10.3.3	Design of customized CIRIS reports for program management and field technicians	1	1										1		New customized reports designed as required based on management and field technician staff needs	M&E, IT	Done	1	1	0
10.3.4	CIRIS data import tools for alliance partner NGOs	1	1										1		Tools developed in Y1 Q1, ongoing customization as required	M&E, IT	Done	1	1	0
10.3.5	CIRIS data validation (identification of outliers, missing data, and field-based validation)	On-going	On-going					On-going					On-going	-	CIRIS data validated on regular basis	M&E	On-going	On-going	On-going	N/A
<b>10.4</b>	<b>Alliance Partner M&amp;E Reporting Systems</b>																			
10.4.1	All partner alliances include individual M&E plans (tied to HARVEST higher level indicators, as well as workplan deliverable targets)	On-going	On-going	On-going											M&E plans developed with each partner as alliance initiated with program	M&E	On-going	On-going	On-going	N/A
10.4.2	Partner alliance staff training in program M&E methodology	On-going	On-going					On-going							Partner M&E staff trained to meet subcontract M&E requirements	M&E	On-going	On-going	On-going	N/A
10.4.3	Data collection and validation from program alliance partners (for inclusion in CIRIS and other databases)	On-going	On-going					On-going					On-going		Data collected and validated from program partners, imported into CIRIS and/or other databases as required	M&E	On-going	On-going	On-going	N/A
<b>10.5</b>	<b>Baseline Survey and Impact Evaluations</b>																			
<b>10.5.1</b>	<b>Baseline Survey</b>																			
10.5.1.1	Subcontractor selected and subcontract signed for baseline survey	1	1										1		Subcontractor selected and subcontract signed (October)	M&E, STTA	Done	1	1	0
10.5.1.2	Baseline methodology finalized with baseline survey subcontractor and specialized STTA (including: sample size and method of calculation; matching criteria for treatment/control groups; identification of treatment/control sites to participate in the survey)	1	1										1		Methodology finalized for baseline survey (October)	survey subcontractor, STTA, M&E	Done	1	1	0
10.5.1.3	Finalization of survey instruments (including field testing)	1	1										1		Survey instruments designed, tested and finalized (early November)	baseline survey subcontractor, STTA, M&E	Done	1	1	0
10.5.1.4	Identification of survey respondents	1	1										1		Survey respondents identified (early November)	baseline survey subcontractor, STTA, M&E	Done	1	1	0
10.5.1.5	Baseline survey field data collection	1	1										1		Field data collection for baseline survey data (Nov-Jan)	baseline survey subcontractor	Done	1	1	0
10.5.1.6	Prepare SPSS shell and enter data (with adequate quality control measures and cleaning data of all errors)	1	1										1		SPSS shell created (Nov); data entered (Nov-Jan)	baseline survey subcontractor	Done	1	1	0
10.5.1.7	Final baseline survey report (with data)	1	1										1		Final report with data submitted to USAID (Feb)	baseline survey subcontractor, STTA	Done	1	1	0
<b>10.6</b>	<b>Other Special M&amp;E Surveys</b>																			
10.6.1	Input supplier sales	10	10	1	1	1	1	4					14		Surveys conducted	M&E, BDS	=	11	11	3
10.6.2	Performance Monitoring field surveys	11	11	1	1	1	1	4	1	1			2		Surveys conducted	M&E	=	12	12	5
10.6.3	Replication Surveys	2	2			1	1	2					4		Surveys conducted to identify households benefiting from demonstration sites	M&E, STTA, AG	=	2	2	2
10.6.4	NRM baseline survey	1	1										1		Survey report	M&E, Out-sourced subcontractor	Done	1	1	0
10.6.5	NRM follow up survey	1	-			1		1					1		Survey report	M&E, Out-sourced subcontractor	=	-	-	1
10.6.6	Nutrition Survey	-	-			1		1					1		In-house survey conducted	M&E	=	-	-	1
10.6.7	Farm machinery survey				1								1		In-house survey conducted	M&E	=	-	-	1
<b>10.7</b>	<b>Other Reporting</b>																			
10.7.1	Quarterly/annual report preparation	15	15	1	1	1	1	4	1	1	1		3		Quarterly/annual report produced and distributed	COM, M&E, ALL	=	16	16	6
10.7.2	Success story production	51	51	4	4	4	4	16	4	4			8		Success stories produced and distributed	COM, M&E, ALL	=	55	55	20
10.7.3	Monthly Project Bulletins	41	41	3	3	3	3	12	3	1			4		Monthly bulletins produced and disseminated	COM, M&E, ALL	=	44	44	13

<b>Status Key</b>	
Done	Completed
+	Ahead of Schedule
++	Completed/Surpassed
=	On Schedule
Cancelled	Cancelled, see comments column for specific details
X	Behind Schedule
On-going	To be continued

## ANNEX II: CLIENT INFORMATION

Cambodia HARVEST Target Villages -- Clients & Farmer beneficiaries, Sector Focus, and Target HHs/Populations (as of December 31, 2014)																												
Location				Category																		Target Populations						
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O & M village	#FTF village	#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2
Pursat	Bakan	Boeng Bat Kandal	Bat Kandaol			131															■		■	168	761	4%	11%	15%
Pursat	Bakan	Boeng Bat Kandal	Boeng Chhuk			109															■		■	136	640	8%	17%	25%
Pursat	Bakan	Boeng Bat Kandal	Doung Chrum		9	224															■		■	307	1,491	6%	12%	18%
Pursat	Bakan	Boeng Bat Kandal	Ou		5	162															■		■	249	1,138	16%	8%	24%
Pursat	Bakan	Boeng Bat Kandal	Preah Ampil			180															■		■	186	877	9%	17%	26%
Pursat	Bakan	Boeng Bat Kandal	Samraong		14	135															■		■	142	669	7%	13%	20%
Pursat	Bakan	Boeng Bat Kandal	Svay																		■			99	438	23%	20%	42%
Pursat	Bakan	Boeng Bat Kandal	Svay Chrum		9	114															■		■	162	772	5%	19%	24%
Pursat	Bakan	Boeng Bat Kandal	Tram Seh		3	106							1								■		■	217	1,437	13%	14%	27%
Pursat	Bakan	Boeng Bat Kandal	Robang Romeas																		■			314	1,321	2%	5%	7%
Pursat	Bakan	Boeng Bat Kandal	Tuol Thmea																		■			114	583	6%	20%	26%
Pursat	Bakan	Boeng Bat Kandal	Ruessei Ta Man																		■			219	1,075	9%	9%	19%
Pursat	Bakan	Boeng Khnar	Boeng Khnar								2		1		2	12					■	■		436	1,825	10%	12%	22%
Pursat	Bakan	Boeng Khnar	Chamkar Leu													2					■	■		226	972	13%	23%	36%
Pursat	Bakan	Boeng Khnar	Daeum Chres		9	156										1					■	■	■	216	942	3%	10%	13%
Pursat	Bakan	Boeng Khnar	Khnach Romeas		11	45															■		■	219	824	2%	23%	25%
Pursat	Bakan	Boeng Khnar	Krasang Kruo		20											1					■	■	■	265	1,133	9%	12%	22%
Pursat	Bakan	Boeng Khnar	Preah Mlu																		■			207	876	2%	17%	19%
Pursat	Bakan	Boeng Khnar	Prey Damrei																		■			209	875	4%	19%	23%
Pursat	Bakan	Boeng Khnar	Prey Phdau																		■			235	1,055	12%	13%	25%
Pursat	Bakan	Boeng Khnar	Prey Svay	6	46	1											1	27			■		■	240	1,084	9%	21%	30%
Pursat	Bakan	Boeng Khnar	Rung																		■			329	1,682	7%	9%	16%
Pursat	Bakan	Boeng Khnar	Sakar		1																■		■	239	1,094	14%	17%	31%
Pursat	Bakan	Boeng Khnar	Trach Kraol																		■			101	469	18%	21%	39%
Pursat	Bakan	Boeng Khnar	Voat Chreae			127															■		■	202	885	5%	15%	20%
Pursat	Bakan	Khnar Totueng	Bak Meaek	11	38	184															■	■	■	236	889	8%	15%	23%
Pursat	Bakan	Khnar Totueng	Daeum Roka	9	29	99															■	■	■	101	369	5%	20%	25%
Pursat	Bakan	Khnar Totueng	Damnak Thnong	37	22	181										2					■	■	■	213	913	7%	7%	15%
Pursat	Bakan	Khnar Totueng	Kamprak Koun			51										1					■	■	■	126	476	7%	13%	20%
Pursat	Bakan	Khnar Totueng	Kaoh Krabei			45															■	■	■	99	372	11%	12%	23%
Pursat	Bakan	Khnar Totueng	Kaoh Svay	25		105															■	■	■	251	1,034	9%	12%	21%
Pursat	Bakan	Khnar Totueng	Kaoh Voat	11		57															■	■	■	189	975	9%	16%	24%
Pursat	Bakan	Khnar Totueng	Khnar Totueng	13	37	117					1	1	1			1					■	■	■	190	832	7%	11%	17%

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2
Pursat	Bakan	Khnar Totueng	Krouch Saeuch	1	44	107																96	440	5%	19%	24%		
Pursat	Bakan	Khnar Totueng	Phteah Sla	13	55	138																163	700	7%	18%	26%		
Pursat	Bakan	Khnar Totueng	Boeng Chhuk																			193	910	7%	19%	25%		
Pursat	Bakan	Khnar Totueng	Tuol Angkrong	13		43																54	226	4%	11%	15%		
Pursat	Bakan	Me Tuek	Angkanh										1									262	1,070	5%	9%	14%		
Pursat	Bakan	Me Tuek	Trang																			220	986	15%	13%	27%		
Pursat	Bakan	Me Tuek	Ma																			98	396	2%	17%	19%		
Pursat	Bakan	Me Tuek	Kdat		3																	332	1,404	10%	13%	23%		
Pursat	Bakan	Me Tuek	Me Tuek		4																	181	891	7%	7%	13%		
Pursat	Bakan	Me Tuek	Ou Preal																			227	1,123	11%	16%	27%		
Pursat	Bakan	Me Tuek	Kaoh khsach		8																	157	625	No data	9%	9%		
Pursat	Bakan	Me Tuek	Samraong Prey Khiev																			180	838	4%	9%	13%		
Pursat	Bakan	Me Tuek	Chen Tay																			341	1,484	7%	11%	18%		
Pursat	Bakan	Me Tuek	Ta Mom		23																	348	1,644	5%	7%	12%		
Pursat	Bakan	Me Tuek	Paolao																			183	929	9%	21%	30%		
Pursat	Bakan	Me Tuek	Cha Yov																			212	849	4%	11%	15%		
Pursat	Bakan	Ou Ta Paong	Anlong Kray	4	20	99											2					223	1,056	11%	23%	34%		
Pursat	Bakan	Ou Ta Paong	Bat Kokir Chas	14	23	117											1					162	949	13%	17%	31%		
Pursat	Bakan	Ou Ta Paong	Bat Kokir Thmei		28	79																323	1,271	11%	16%	26%		
Pursat	Bakan	Ou Ta Paong	Chamkar Khloy		26	124																215	973	5%	27%	31%		
Pursat	Bakan	Ou Ta Paong	Chamkar Ou		15	111											1					160	881	15%	14%	30%		
Pursat	Bakan	Ou Ta Paong	Oknha Moan		15																	189	940	21%	9%	30%		
Pursat	Bakan	Ou Ta Paong	Ou Bat																			89	549	12%	14%	26%		
Pursat	Bakan	Ou Ta Paong	Ou Ta Paong		31								1				3					301	1,634	16%	19%	34%		
Pursat	Bakan	Ou Ta Paong	Phsar Andaet	12	47	108											1					227	1,146	14%	19%	32%		
Pursat	Bakan	Ou Ta Paong	Prey Krabau																			131	990	14%	15%	29%		
Pursat	Bakan	Ou Ta Paong	Prey Yeang																			64	336	21%	10%	30%		
Pursat	Bakan	Ou Ta Paong	Robaoh Reang		43	124					1						1					211	1,155	12%	20%	32%		
Pursat	Bakan	Ou Ta Paong	Samraong Pok																			155	700	8%	31%	39%		
Pursat	Bakan	Ou Ta Paong	Sdok Khlouk																			329	1,864	16%	15%	31%		
Pursat	Bakan	Ou Ta Paong	Srah Mkak		13												4					265	1,211	15%	16%	30%		
Pursat	Bakan	Ou Ta Paong	Srah Run														3					145	693	7%	18%	25%		
Pursat	Bakan	Ou Ta Paong	Ta Nai																			135	621	14%	15%	30%		
Pursat	Bakan	Ou Ta Paong	Tuol Rokeang		6																	117	559	19%	14%	34%		
Pursat	Bakan	Rumlech	Damnakh Trach			67											1					100	389	13%	20%	32%		
Pursat	Bakan	Rumlech	Kampong Kdei	9	48																	115	724	10%	19%	28%		
Pursat	Bakan	Rumlech	Kaoh Khcheay			84																100	489	20%	11%	31%		

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations					
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2	
Pursat	Bakan	Rumlech	Khvav	5		94																■	■	■	250	937	8%	18%	26%
Pursat	Bakan	Rumlech	Lhong			68																■		■	74	616	14%	17%	30%
Pursat	Bakan	Rumlech	Pnov			107																■	■	■	135	678	14%	10%	24%
Pursat	Bakan	Rumlech	Pralay Rumdeng	33	51	87					1					1						■	■	■	110	503	6%	9%	15%
Pursat	Bakan	Rumlech	Prasat	6	35	139					1											■	■	■	210	977	16%	13%	28%
Pursat	Bakan	Rumlech	Rumlech	12	45	95					1	1	1			1						■	■	■	205	896	6%	18%	24%
Pursat	Bakan	Rumlech	Rung Ta Kok	12	38																	■	■	■	233	976	19%	20%	39%
Pursat	Bakan	Rumlech	Sdok Khla			137																■		■	178	798	15%	16%	31%
Pursat	Bakan	Rumlech	Thmei			64																■		■	80	297	3%	29%	32%
Pursat	Bakan	Rumlech	Koun Tnaot																			■			121	480	12%	13%	26%
Pursat	Bakan	Snam Preah	Andoung Krasang													3						■	■		323	1,406	11%	18%	29%
Pursat	Bakan	Snam Preah	Andoung Sanbuor			77																■		■	201	994	11%	10%	21%
Pursat	Bakan	Snam Preah	Anlong Mean		38	91											1	16	1	10		■	■		190	835	8%	16%	24%
Pursat	Bakan	Snam Preah	Araen			80					1											■		■	137	539	11%	14%	26%
Pursat	Bakan	Snam Preah	Bak Pring																			■			226	799	16%	16%	32%
Pursat	Bakan	Snam Preah	Chambak Meas																			■			272	1,296	21%	10%	31%
Pursat	Bakan	Snam Preah	Cheung Phleung		19												1	13				■		■	136	698	16%	9%	25%
Pursat	Bakan	Snam Preah	Dangkieb Kdam													1						■	■		132	561	17%	11%	29%
Pursat	Bakan	Snam Preah	Kampeaeng Svay	7	8						1		1				1	19	1	9		■		■	137	698	10%	15%	25%
Pursat	Bakan	Snam Preah	Kaoh Krasang		34	113											1	11				■		■	131	611	9%	5%	14%
Pursat	Bakan	Snam Preah	Khmar													3						■	■		289	1,366	20%	4%	23%
Pursat	Bakan	Snam Preah	Krapeu Rou													2						■	■		206	909	16%	10%	26%
Pursat	Bakan	Snam Preah	Pnov			90																■		■	239	1,005	2%	24%	26%
Pursat	Bakan	Snam Preah	Sameakki																			■			158	775	6%	22%	28%
Pursat	Bakan	Snam Preah	Sdok Svay		22	72										1	1	16	1	9		■		■	219	1,037	15%	12%	27%
Pursat	Bakan	Snam Preah	Snam Preah									1				3						■	■		144	615	15%	12%	27%
Pursat	Bakan	Snam Preah	Svay at																			■			110	473	16%	17%	33%
Pursat	Bakan	Snam Preah	Thnuoh Ta Chab		57	1																■	■	■	304	1,414	8%	10%	18%
Pursat	Bakan	Snam Preah	Tram Peaer													1						■	■		225	1,024	17%	18%	35%
Pursat	Bakan	Snam Preah	Tuol Khmaer																			■			179	806	11%	16%	27%
Pursat	Bakan	Svay Doun Kaev	Chrab			80																■		■	141	624	11%	28%	39%
Pursat	Bakan	Svay Doun Kaev	Kampang			123										2						■		■	197	905	1%	10%	11%
Pursat	Bakan	Svay Doun Kaev	Kampout ang			59										1						■		■	85	356	46%	30%	76%
Pursat	Bakan	Svay Doun Kaev	Nikom Leu		22	143										2						■		■	394	1,875	16%	27%	43%
Pursat	Bakan	Svay Doun Kaev	Svay Doun Kaev Muoy			88							1			6						■		■	354	1,549	4%	15%	19%
Pursat	Bakan	Svay Doun Kaev	Svay Doun Kaev Pir																			■			80	333	13%	13%	25%
Pursat	Bakan	Svay Doun Kaev	Tuol Samraong																			■			41	230	21%	8%	28%



Location				Category																		#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Pursat	Bakan	Svay Doun Kaev	Svay Sa																			64	287	8%	14%	22%			
Pursat	Bakan	Svay Doun Kaev	Thmei																			99	452	12%	2%	14%			
Pursat	Bakan	Ta Lou	Rohal Til										1									425	2,326	5%	20%	25%			
Pursat	Bakan	Ta Lou	Ta Lou										1									384	1,827	5%	16%	21%			
Pursat	Bakan	Ta Lou	Tuol Thma																			123	460	7%	10%	17%			
Pursat	Bakan	Ta Lou	Prey Roung																			305	1,252	8%	8%	15%			
Pursat	Bakan	Ta Lou	Tayang Sa																			104	476	20%	9%	29%			
Pursat	Bakan	Ta Lou	Tuol Chreav																			90	472	9%	20%	28%			
Pursat	Bakan	Ta Lou	Kouk Rumlo																			108	455	4%	25%	29%			
Pursat	Bakan	Ta Lou	Chhnal Moan																			145	617	10%	16%	26%			
Pursat	Bakan	Ta Lou	Serei Kunthea																			216	1,014	18%	9%	27%			
Pursat	Bakan	Ta Lou	Prey Veang																			318	1,494	9%	17%	26%			
Pursat	Bakan	Ta Lou	Buor Chres																			95	546	19%	17%	36%			
Pursat	Bakan	Ta Lou	Prey Tao																			137	575	13%	10%	23%			
Pursat	Bakan	Ta Lou	Baos Ko																			236	1,075	12%	9%	21%			
Pursat	Bakan	Ta Lou	Som Sant																			493	2,387	17%	11%	28%			
Pursat	Bakan	Ta Lou	Prahal		45																	431	1,843	14%	19%	33%			
Pursat	Bakan	Ta Lou	Thmei		14																	322	1,527	9%	15%	24%			
Pursat	Bakan	Ta Lou	Tuol Totueng																			93	394	3%	20%	23%			
Pursat	Bakan	Ta Lou	Tang Kouk																			383	2,100	7%	3%	10%			
Pursat	Bakan	Ta Lou	Boeng Kak																			224	909	11%	14%	26%			
Pursat	Bakan	Trapeang Chorn	Bakan	5	61	118							1			1						291	1,294	12%	11%	23%			
Pursat	Bakan	Trapeang Chorn	Boeng Prei		41																	267	1,364	6%	13%	19%			
Pursat	Bakan	Trapeang Chorn	Buor Sragnae	19		164																222	843	10%	15%	25%			
Pursat	Bakan	Trapeang Chorn	Chamkar Ou	18	55						1											182	862	16%	7%	23%			
Pursat	Bakan	Trapeang Chorn	Kab Kralanh	10	48	95																155	566	6%	25%	31%			
Pursat	Bakan	Trapeang Chorn	Kandoeng Meas		14						1											193	1,433	8%	18%	26%			
Pursat	Bakan	Trapeang Chorn	Kaoh Andat																			215	915	9%	14%	24%			
Pursat	Bakan	Trapeang Chorn	Kaoh Kaev													1						372	1,399	16%	9%	25%			
Pursat	Bakan	Trapeang Chorn	Kaoh Svay								1	1										136	842	7%	20%	27%			
Pursat	Bakan	Trapeang Chorn	Kraol Krabei											1								245	1,258	11%	19%	30%			
Pursat	Bakan	Trapeang Chorn	Ou Rumchek	15	67	92					2					4						283	1,339	14%	14%	28%			
Pursat	Bakan	Trapeang Chorn	Pit Trang																			139	635	10%	26%	36%			
Pursat	Bakan	Trapeang Chorn	Poulyum	2	33	107					1											189	1,050	16%	6%	22%			
Pursat	Bakan	Trapeang Chorn	Preah Chambak	17		119																233	1,230	10%	19%	29%			
Pursat	Bakan	Trapeang Chorn	Snay Toul			61																125	509	12%	25%	38%			
Pursat	Bakan	Trapeang Chorn	Srae Lvea	34	51																	227	1,185	15%	8%	24%			

Location				Category																#Mobile kitchen village	#O & M village	#TFV village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M			#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2
Pursat	Bakan	Trapeang Chorn	Stueng Kambot		46	119																	203	881	7%	13%	19%
Pursat	Bakan	Trapeang Chorn	Thmei		9	60																	119	636	24%	15%	39%
Pursat	Bakan	Trapeang Chorn	Trapeang Chorn			63										3							375	2,302	2%	26%	28%
Pursat	Kandieng	Anlong Vil	Boeng Chhuk		23												1	16					106	476	21%	19%	40%
Pursat	Kandieng	Anlong Vil	Kampong Krabei		16												1	12					56	240	13%	14%	27%
Pursat	Kandieng	Anlong Vil	Kaoh Krasang		35												1	14					69	334	21%	4%	25%
Pursat	Kandieng	Anlong Vil	Kbal Romeas		22												1	15	1	11			92	437	12%	19%	31%
Pursat	Kandieng	Anlong Vil	Phlov Krabei		17												1	22					56	278	9%	9%	18%
Pursat	Kandieng	Anlong Vil	Preaek Chheu Trav		27												1	15					96	446	27%	16%	43%
Pursat	Kandieng	Anlong Vil	Preaek Ta Kong		15												1	19	1	12			60	342	18%	8%	27%
Pursat	Kandieng	Anlong Vil	Preaek Ta Vong		13								1				1	19					88	417	23%	No data	23%
Pursat	Kandieng	Anlong Vil	Voat pou Muoy		38												1	14					82	368	16%	7%	23%
Pursat	Kandieng	Anlong Vil	Voat Pou Ti Pir		3												1	17	1	9			51	273	8%	18%	26%
Pursat	Kandieng	Anlong Vil	Chey Chumneah																				106	469	29%	13%	42%
Pursat	Kandieng	Anlong Vil	Kanhcheu Bay Dach																				62	311	16%	7%	23%
Pursat	Kandieng	Anlong Vil	Phteah Kor																				92	418	30%	19%	50%
Pursat	Kandieng	Anlong Vil	Anlong Vil																				58	283	7%	16%	23%
Pursat	Kandieng	Kandieng	Boeng Chhuk		36						1						1	18	1	12			164	710	11%	22%	33%
Pursat	Kandieng	Kandieng	Kampong Krasang Kra		26											2	1	17	1	14			98	428	11%	25%	36%
Pursat	Kandieng	Kandieng	Kampong Krasang Leu		14												1	16	1	12			77	299	4%	22%	26%
Pursat	Kandieng	Kandieng	Prey Kdei Kandal		14												1	20	1	12			54	252	17%	15%	32%
Pursat	Kandieng	Kandieng	Prey Kdei Kraom		20												1	19	1	14			96	379	13%	25%	38%
Pursat	Kandieng	Kandieng	Stueng Kraom		4																		85	403	17%	19%	36%
Pursat	Kandieng	Kandieng	Stueng Leu		1																		75	355	15%	17%	32%
Pursat	Kandieng	Kandieng	Svay Yeang																				67	364	20%	14%	34%
Pursat	Kandieng	Kandieng	Kandieng										1										71	366	17%	8%	25%
Pursat	Kandieng	Kandieng	Kandieng Knong																				66	295	12%	26%	38%
Pursat	Kandieng	Kandieng	Sya		7																		109	468	19%	13%	32%
Pursat	Kandieng	Kanhchor	Phlov Luong						1								1	14	1	12			218	1,077	3%	16%	18%
Pursat	Kandieng	Kanhchor	Pou Andaet														1	15					195	718	2%	15%	16%
Pursat	Kandieng	Kanhchor	Preaek Trabaek														1	21					342	1,557	6%	19%	24%
Pursat	Kandieng	Kanhchor	Samraong														1	21					200	836	11%	15%	26%
Pursat	Kandieng	Kaoh Chum	Ampil Kanhchrinh																				95	449	12%	20%	32%
Pursat	Kandieng	Kaoh Chum	Anlong Hab	2	49						1						1	18					171	774	6%	21%	28%
Pursat	Kandieng	Kaoh Chum	Damrei Sa																				182	896	8%	17%	26%
Pursat	Kandieng	Kaoh Chum	Dang Lang		11												1	22					150	759	12%	24%	36%
Pursat	Kandieng	Kaoh Chum	Dang Rung		33						1						1	22	1	10			177	794	15%	17%	31%

Location				Category																#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M			#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Pursat	Kandieng	Kaoh Chum	Kien																				194	1,353	7%	25%	32%
Pursat	Kandieng	Kaoh Chum	Phteah Pring																				96	434	7%	28%	35%
Pursat	Kandieng	Kaoh Chum	Sdok Chum																				278	1,238	5%	22%	27%
Pursat	Kandieng	Kaoh Chum	Spean		46												1	25					183	844	9%	15%	24%
Pursat	Kandieng	Kaoh Chum	Tuol Ku																				181	781	14%	15%	28%
Pursat	Kandieng	Srae Sdok	Bakur										1	1									283	1,254	18%	9%	26%
Pursat	Kandieng	Srae Sdok	Pou										1										113	552	18%	11%	29%
Pursat	Kandieng	Srae Sdok	Trang																				170	782	6%	17%	23%
Pursat	Kandieng	Srae Sdok	Saen Chey																				121	591	7%	18%	24%
Pursat	Kandieng	Srae Sdok	Sarieng																				78	403	12%	13%	25%
Pursat	Kandieng	Srae Sdok	Kdei Chhvit																				183	893	23%	4%	27%
Pursat	Kandieng	Srae Sdok	Banteay Traok																				140	634	1%	15%	16%
Pursat	Kandieng	Srae Sdok	Enthyey																				117	707	11%	11%	22%
Pursat	Kandieng	Srae Sdok	Phteah Kaoh																				92	391	9%	11%	20%
Pursat	Kandieng	Veal	Tuol Pongro																				83	350	11%	31%	42%
Pursat	Kandieng	Svay Luong	Chreaeng		68						1						1	33					204	984	11%	7%	18%
Pursat	Kandieng	Svay Luong	Ka Kou		14						1						1	11					60	666	6%	7%	13%
Pursat	Kandieng	Svay Luong	Pou Laeung		43												1	19	1	11			91	446	5%	30%	35%
Pursat	Kandieng	Svay Luong	Sanlung		16											1	1	15	1	11			66	356	8%	22%	30%
Pursat	Kandieng	Svay Luong	Svay Chambak		14												1	23	1	10			87	376	29%	15%	44%
Pursat	Kandieng	Svay Luong	Svay Yeang		37												1	14					104	494	15%	25%	40%
Pursat	Kandieng	Sya	Sya		22	99																	139	552	11%	21%	31%
Pursat	Kandieng	Sya	Voat Lieb			76																	147	628	20%	11%	31%
Pursat	Krakor	Anlong Tnaot	Chrolong		24																		118	527	5%	12%	17%
Pursat	Krakor	Anlong Tnaot	Kandal								1						2						227	1,267	4%	9%	13%
Pursat	Krakor	Anlong Tnaot	Khleang Moeung														2						226	918	7%	2%	9%
Pursat	Krakor	Anlong Tnaot	Papet	5	24												1	15					214	903	6%	12%	18%
Pursat	Krakor	Anlong Tnaot	Phsar														6						332	1,948	4%	7%	11%
Pursat	Krakor	Anlong Tnaot	Thkoul Thum	10	34	130											1	12	1	9			210	825	3%	4%	7%
Pursat	Krakor	Anlong Tnaot	Totueung																				94	483	10%	3%	13%
Pursat	Krakor	Anlong Tnaot	Banteay Krang																				182	739	3%	10%	13%
Pursat	Krakor	Anlong Tnaot	La Bak																				73	267	11%	9%	20%
Pursat	Krakor	Anlong Tnaot	Tuol Mikak																				203	830	5%	1%	6%
Pursat	Krakor	Anlong Tnaot	Khla Krapeu																				226	873	8%	8%	16%
Pursat	Krakor	Anlong Tnaot	Tonsay Kol																				100	587	9%	10%	19%
Pursat	Krakor	Ansa Chambak	San Sar			122																	194	844	3%	20%	23%
Pursat	Krakor	Ansa Chambak	Thkoul Touch			66																	286	1,224	8%	7%	15%

Location				Category																		#Mobile kitchen village	#O & M village	#TFV village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Pursat	Krakor	Ansa Chambak	Kbaldamrei		10																		226	972	8%	17%	25%		
Pursat	Krakor	Ansa Chambak	arang Pruoch		3																		158	662	14%	5%	19%		
Pursat	Krakor	Boeng Kantuot	Boeng			126							1										153	655	4%	9%	13%		
Pursat	Krakor	Boeng Kantuot	Chor Chork			68																	70	357	13%	11%	24%		
Pursat	Krakor	Boeng Kantuot	Kandol Sa			102																	153	678	7%	11%	17%		
Pursat	Krakor	Boeng Kantuot	Ou Anhchanh			75																	110	435	6%	20%	26%		
Pursat	Krakor	Boeng Kantuot	Pou Angkrang	15		148																	192	756	10%	9%	18%		
Pursat	Krakor	Boeng Kantuot	Pou Khoeun																				153	636	3%	18%	21%		
Pursat	Krakor	Boeng Kantuot	Ta Kaev Kraom			97																	151	602	10%	10%	20%		
Pursat	Krakor	Boeng Kantuot	Thlea M'am	11		100	17																127	553	13%	11%	24%		
Pursat	Krakor	Boeng Kantuot	Thmei			88																	125	544	3%	19%	23%		
Pursat	Krakor	Boeng Kantuot	Trapeang Kantuot			108																	151	680	5%	11%	17%		
Pursat	Krakor	Boeng Kantuot	Trapeang Khley	18		147																	177	722	7%	13%	20%		
Pursat	Krakor	Chheu Tom	Bamnak																				351	1,495	13%	7%	19%		
Pursat	Krakor	Kampong Luong	Phum Buon																				365	1,445	8%	42%	50%		
Pursat	Krakor	Kampong Pou	Chek Chau			129																	323	1,337	4%	15%	20%		
Pursat	Krakor	Kampong Pou	Kampong La		4	132		28															355	1,512	30%	12%	42%		
Pursat	Krakor	Kampong Pou	Moat Prey		1	170																	240	1,058	20%	17%	36%		
Pursat	Krakor	Kampong Pou	Pou Kod																				154	618	11%	16%	28%		
Pursat	Krakor	Kampong Pou	Pou Robang			113							1										220	1,027	12%	10%	22%		
Pursat	Krakor	Kampong Pou	Roluos Kandal		6	115	37																132	537	30%	9%	39%		
Pursat	Krakor	Kampong Pou	Roluos Khang Kaeut			74																	86	402	6%	13%	19%		
Pursat	Krakor	Kampong Pou	Sna Reach			54																	104	428	21%	24%	45%		
Pursat	Krakor	Kbal Trach	Chheu Teal Khpos			95																	241	978	5%	21%	26%		
Pursat	Krakor	Kbal Trach	Kampong Leu					33															382	1,593	20%	11%	31%		
Pursat	Krakor	Kbal Trach	Kandal													1							178	927	7%	8%	15%		
Pursat	Krakor	Kbal Trach	Kralanh		6																		365	1,157	14%	3%	17%		
Pursat	Krakor	Kbal Trach	Phsar																				195	646	7%	4%	12%		
Pursat	Krakor	Kbal Trach	Samraong										1										237	1,031	8%	25%	33%		
Pursat	Krakor	Kbal Trach	Srae Ruessei																				86	386	15%	12%	27%		
Pursat	Krakor	Kbal Trach	Totueng																				153	597	9%	20%	29%		
Pursat	Krakor	Kbal Trach	Trapeang Rumdenh			160		19															345	1,834	17%	19%	36%		
Pursat	Krakor	Kbal Trach	Trapeang Smach																				159	1,038	16%	13%	29%		
Pursat	Krakor	Kbal Trach	Doung																				104	342	8%	17%	25%		
Pursat	Krakor	Ou Sandan	Chong Khlong																				226	865	16%	4%	20%		
Pursat	Krakor	Ou Sandan	Krang Thum	22	31	131	57			1							2						175	793	8%	18%	26%		
Pursat	Krakor	Ou Sandan	Ou ach Kok	19	32	109	3			1	2	1					1						215	852	12%	5%	16%		

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Pursat	Krakor	Ou Sandan	Ou Akol				15	28														242	1,358	12%	17%	29%		
Pursat	Krakor	Ou Sandan	Ou Sandan	11		129																129	513	18%	5%	23%		
Pursat	Krakor	Ou Sandan	Puttream	9		116					2											153	652	7%	10%	17%		
Pursat	Krakor	Ou Sandan	Thnoeng	17	17	104	18			1												125	497	3%	17%	20%		
Pursat	Krakor	Ou Sandan	Doung Chuor																			141	633	12%	10%	22%		
Pursat	Krakor	Ou Sandan	Ou Ta Prok																			168	858	11%	12%	22%		
Pursat	Krakor	Sna Ansa	Ansa Kdam		6	172										1						194	847	24%	10%	34%		
Pursat	Krakor	Sna Ansa	Beng	7	23	92					1											153	719	11%	23%	34%		
Pursat	Krakor	Sna Ansa	Chi Cheh			76																83	339	48%	7%	55%		
Pursat	Krakor	Sna Ansa	Krang Veaeng	7	26	27																204	1,011	21%	15%	36%		
Pursat	Krakor	Sna Ansa	Sarovoan		13												1	21	1	11		93	427	32%	12%	44%		
Pursat	Krakor	Sna Ansa	Sna Ansa			88						1	1			2						99	455	16%	24%	40%		
Pursat	Krakor	Sna Ansa	Svay Sa		1	93										1						120	516	14%	19%	33%		
Pursat	Krakor	Sna Ansa	Thmei		12	78																108	467	12%	23%	35%		
Pursat	Krakor	Sna Ansa	Veal Vong													1						153	724	17%	22%	39%		
Pursat	Krakor	Tnaot Chum	Bangkong Khmum							1												178	870	10%	5%	15%		
Pursat	Krakor	Tnaot Chum	Boeng Veal	2	14				Joint DTL		1											250	1,234	13%	9%	22%		
Pursat	Krakor	Tnaot Chum	Chambak Thum		33	136			Joint DTL													259	1,248	10%	2%	12%		
Pursat	Krakor	Tnaot Chum	Chheu Teal	14	31	110					2		1									194	1,214	8%	11%	19%		
Pursat	Krakor	Tnaot Chum	Dang Tuek Leach	4	34	80			1		1											131	602	1%	16%	17%		
Pursat	Krakor	Tnaot Chum	Kandal		35	81			Joint DTL													146	726	7%	10%	16%		
Pursat	Krakor	Tnaot Chum	Krabei Sa		15																	153	772	9%	8%	17%		
Pursat	Krakor	Tnaot Chum	Prey Khla													1						176	747	8%	10%	18%		
Pursat	Krakor	Tnaot Chum	Saen Pen	8	31	99																120	599	3%	9%	13%		
Pursat	Krakor	Tnaot Chum	Ta Kaev Leu													1						113	478	11%	12%	22%		
Pursat	Krakor	Tnaot Chum	Tbaeng Chrum	13	33	157					1											217	957	2%	5%	7%		
Pursat	Krakor	Tnaot Chum	Thmei		18																	598	2,608	14%	16%	30%		
Pursat	Krakor	Tnaot Chum	Tram									1										179	895	3%	7%	10%		
Pursat	Krong Pursat	Chamraeun Phal	Doun Ei		30						1						1	18				149	1,003	14%	9%	23%		
Pursat	Krong Pursat	Chamraeun Phal	Kampong Stoung		23	99			1								1	26				215	1,055	46%	35%	81%		
Pursat	Krong Pursat	Chamraeun Phal	Ou Roka		39											1	1	14				158	949	10%	21%	30%		
Pursat	Krong Pursat	Chamraeun Phal	Ou Tong			71																189	895	17%	11%	28%		
Pursat	Krong Pursat	Chamraeun Phal	Svay Meas		31	117											1	24				120	612	8%	39%	48%		
Pursat	Krong Pursat	Chamraeun Phal	Tuol Kruos		21																	337	1,698	34%	7%	41%		
Pursat	Krong Pursat	Lolok Sa	Chumrum Siem		21												1	17				135	893	10%	9%	19%		
Pursat	Krong Pursat	Lolok Sa	Dab Bat		50						1		1			1	1	19	1	5		252	1,149	7%	4%	10%		
Pursat	Krong Pursat	Lolok Sa	Damnak Ampil		26	105											1	15				198	960	5%	6%	12%		



Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Pursat	Krong Pursat	Lolok Sa	Kaoh		8												1	16	1	10	■		■	235	1,042	15%	8%	24%
Pursat	Krong Pursat	Lolok Sa	Khmar		40												1	26			■		■	171	884	4%	4%	8%
Pursat	Krong Pursat	Lolok Sa	Phsar Leu		5						1					1					■			100	442	2%	11%	13%
Pursat	Krong Pursat	Lolok Sa	Voat Luong		26						2					1	1	16			■		■	221	1,096	6%	14%	20%
Pursat	Krong Pursat	Lolok Sa	Lolok Sar																		■			126	524	3%	13%	16%
Pursat	Krong Pursat	Phteah Prey	Dangkear		48												1	18			■		■	201	818	2%	20%	22%
Pursat	Krong Pursat	Phteah Prey	Kok		56												1	29			■		■	176	846	11%	13%	24%
Pursat	Krong Pursat	Phteah Prey	Ou Sdau																		■			155	750	1%	7%	7%
Pursat	Krong Pursat	Phteah Prey	Peal Nheak Muoy												2	1						■		753	4,602	No data	No data	No data
Pursat	Krong Pursat	Phteah Prey	Peal Nheak Pir													2								719	2,757	No data	No data	No data
Pursat	Krong Pursat	Phteah Prey	Ra													1								321	1,345	1%	8%	9%
Pursat	Krong Pursat	Phteah Prey	Tnaot Tret																		■			178	801	4%	14%	18%
Pursat	Krong Pursat	Prey Nhi	Bak Roteh										1											224	1,112	10%	11%	21%
Pursat	Krong Pursat	Prey Nhi	Krang Ta Saen			151																	■	168	851	15%	13%	28%
Pursat	Krong Pursat	Prey Nhi	Moan Chae												1									193	1,058	14%	13%	27%
Pursat	Krong Pursat	Prey Nhi	Sala Kumru			38																■		95	498	14%	4%	17%
Pursat	Krong Pursat	Prey Nhi	Srah Srang			45																■		72	320	10%	12%	22%
Pursat	Krong Pursat	Roleab	Ou Thkov		68												1	21			■		■	614	2,819	6%	16%	22%
Pursat	Krong Pursat	Roleab	Preaek Tnaot											1							■			179	822	1%	6%	7%
Pursat	Krong Pursat	Roleab	Prey Ovma	10	44	110											1	18			■		■	495	2,257	5%	8%	13%
Pursat	Krong Pursat	Roleab	Roleab		31						1		1			1	1	31			■		■	541	3,302	13%	14%	27%
Pursat	Krong Pursat	Roleab	Tuol Mkak	10	29	79											1	13			■		■	323	1,665	5%	9%	14%
Pursat	Krong Pursat	Svay at	Krang Pophleak	1																	■		■	201	868	3%	29%	32%
Pursat	Krong Pursat	Svay at	Ou Sdau																		■			189	821	11%	18%	29%
Pursat	Krong Pursat	Svay at	Sthani												3						■			410	1,552	9%	18%	26%
Pursat	Krong Pursat	Svay at	Svay at		19											1	1	19			■		■	209	912	21%	9%	30%
Pursat	Krong Pursat	Svay at	Trang																		■			88	457	6%	24%	31%
Pursat	Phnum Kravanh	Bak Chenhchien	Bak Chenhchien		56											1	1	20			■		■	397	1,821	8%	18%	26%
Pursat	Phnum Kravanh	Bak Chenhchien	Krabau Chrum		64	116					1					2	1	15			■		■	310	1,710	5%	17%	23%
Pursat	Phnum Kravanh	Bak Chenhchien	Ou Ruessel		41	57					2		1			4	1	19			■		■	222	1,161	10%	13%	24%
Pursat	Phnum Kravanh	Bak Chenhchien	Ou Rumchang		75	103										1	1	22			■		■	416	1,771	6%	20%	26%
Pursat	Phnum Kravanh	Bak Chenhchien	Tuol Pongro			62																■		82	385	6%	6%	13%
Pursat	Phnum Kravanh	Bak Chenhchien	Chan Serei													2								64	295	8%	16%	25%
Pursat	Phnum Kravanh	Leach	Bak Trakuon		10																■		■	135	558	20%	7%	27%
Pursat	Phnum Kravanh	Leach	Baoh Puoy		11																■		■	210	1,300	15%	10%	25%
Pursat	Phnum Kravanh	Leach	Krouch Chhmar																		■			258	1,045	9%	9%	18%
Pursat	Phnum Kravanh	Leach	Leach													5					■	■		302	1,624	14%	10%	24%

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2
Pursat	Phnum Kravanh	Leach	Paen																		■			315	1,540	20%	5%	25%
Pursat	Phnum Kravanh	Leach	Pech Ban													1					■	■		283	1,435	19%	11%	30%
Pursat	Phnum Kravanh	Leach	Sbov Rik										1								■			229	1,030	15%	9%	24%
Pursat	Phnum Kravanh	Leach	Ta Nuk																		■			165	639	7%	14%	20%
Pursat	Phnum Kravanh	Phteah Rung	Bat Rumduol	14	6	129										11					■	■	■	529	2,157	9%	15%	24%
Pursat	Phnum Kravanh	Phteah Rung	Chongruk			184																	■	410	1,816	11%	18%	29%
Pursat	Phnum Kravanh	Phteah Rung	Damnak Kansaeng		6	80																	■	120	510	17%	13%	30%
Pursat	Phnum Kravanh	Phteah Rung	Kandal			91															■		■	246	1,229	25%	2%	28%
Pursat	Phnum Kravanh	Phteah Rung	Kaoh Svay			76															■		■	181	758	10%	13%	23%
Pursat	Phnum Kravanh	Phteah Rung	Kranham			111															■		■	389	1,459	15%	13%	28%
Pursat	Phnum Kravanh	Phteah Rung	Phteah Rung		12	141															■		■	305	1,234	13%	15%	28%
Pursat	Phnum Kravanh	Phteah Rung	Prey Kanlang	26		176																	■	242	1,031	8%	11%	19%
Pursat	Phnum Kravanh	Phteah Rung	Prohoas Kbal			94															■		■	193	847	11%	20%	30%
Pursat	Phnum Kravanh	Phteah Rung	Sdok Khtum			102																	■	229	1,137	15%	7%	22%
Pursat	Phnum Kravanh	Phteah Rung	Ta Sas			101							1										■	373	1,619	16%	10%	26%
Pursat	Phnum Kravanh	Phteah Rung	Thlok Dangkao	17		127										3						■	■	365	1,614	5%	9%	15%
Pursat	Phnum Kravanh	Prongil	Kampeaeng		11						1	1	1			2					■	■	■	326	1,341	15%	14%	29%
Pursat	Phnum Kravanh	Prongil	Ou Bak Tra		42		61			1	1										■	■	■	522	2,492	22%	7%	29%
Pursat	Phnum Kravanh	Prongil	Ou Srav		38																■	■	■	302	1,418	19%	11%	29%
Pursat	Phnum Kravanh	Prongil	Prongil							1											■			513	2,009	15%	10%	25%
Pursat	Phnum Kravanh	Prongil	Samraong Yea																		■			194	856	16%	14%	30%
Pursat	Phnum Kravanh	Prongil	Svay Pak		1											2					■	■	■	361	1,452	16%	11%	27%
Pursat	Phnum Kravanh	Rokat	Veal Vong		1																		■	471	2,163	6%	16%	22%
Pursat	Phnum Kravanh	Rokat	Prey Smach		8																		■	168	817	9%	18%	27%
Pursat	Phnum Kravanh	Rokat	Prey Khlong		14																		■	204	814	14%	15%	29%
Pursat	Phnum Kravanh	Samraong	Angkrong		13																■		■	647	2,866	9%	29%	37%
Pursat	Phnum Kravanh	Samraong	Ou Heng		13																■		■	198	916	11%	16%	26%
Pursat	Phnum Kravanh	Samraong	Preaek Bei		1																■		■	188	896	8%	19%	27%
Pursat	Phnum Kravanh	Samraong	Preaek Muoy		14							1									■	■	■	459	1,893	14%	14%	27%
Pursat	Phnum Kravanh	Samraong	Preaek Pir										1								■			240	1,973	14%	16%	30%
Pursat	Phnum Kravanh	Samraong	Rovieng		32		44			1	1										■	■	■	221	960	17%	14%	31%
Pursat	Phnum Kravanh	Samraong	Samraong Muoy			42															■	■	■	145	643	9%	9%	19%
Pursat	Phnum Kravanh	Samraong	Samraong Pir		7																■		■	426	1,863	6%	10%	16%
Pursat	Phnum Kravanh	Samraong	Veal		82		74			1	1										■	■	■	258	1,174	14%	17%	30%
Pursat	Phnum Kravanh	Samraong	Ou Preal		20																		■	91	403	13%	15%	28%

Location				Category																				Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O & M village	#FTF village	#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Pursat	Phnum Kravanh	Santreae	Kol Totueng		25		12			1	1													313	1,446	15%	8%	23%
Pursat	Phnum Kravanh	Santreae	Santreae									1												139	1,205	13%	13%	26%
Pursat	Phnum Kravanh	Santreae	Srae Popeay																					199	928	15%	14%	29%
Sub-Total Pursat	5	41	367	645	3,977	13,415	338	108	3	9	45	10	29	2	8	141	59	1,092	20	213	332	102	221	74,189	344,364	11%	14%	24%

Location				Category																	Target Populations							
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O&M village	#FTF village	#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Battambang	Aek Phnum	Kaoh Chiveang	Anlong Ta Uor	7					1															432	2,362	27%	11%	38%
Battambang	Aek Phnum	Kaoh Chiveang	Preaek Toal	8					1															735	3,928	21%	3%	24%
Battambang	Aek Phnum	Peam Aek	Doun Teav										1											449	1,976	7%	27%	34%
Battambang	Aek Phnum	Peam Aek	Ka Rohal	4	28	35											1	21	1	18				272	1,226	16%	27%	43%
Battambang	Aek Phnum	Peam Aek	Kong Tum	5	32	1											1	15	1	11				305	1,475	27%	27%	54%
Battambang	Aek Phnum	Peam Aek	Kouk Doung			92																		434	1,930	16%	38%	54%
Battambang	Aek Phnum	Peam Aek	Peam Aek	7	24											1	1	19	1	13				461	1,829	10%	17%	27%
Battambang	Aek Phnum	Peam Aek	Preaek Chdaor	19	74	112					1						1	25	1	21				749	3,637	13%	33%	46%
Battambang	Aek Phnum	Peam Aek	Suos Ei	4	71												1	18	1	15				427	1,954	8%	16%	24%
Battambang	Aek Phnum	Peam Aek	Ta Kom	7	36	81											1	21	1	19				238	1,018	16%	27%	44%
Battambang	Aek Phnum	Preaek Khpob	Khvet		5							1												395	1,436	4%	4%	9%
Battambang	Aek Phnum	Preaek Khpob	Ou Kambot	27		170																		485	2,157	2%	16%	18%
Battambang	Aek Phnum	Preaek Khpob	Preaek Khpos	11																				368	1,423	5%	18%	23%
Battambang	Aek Phnum	Preaek Khpob	Preaek Snao	9		57																		434	2,116	1%	20%	21%
Battambang	Aek Phnum	Preaek Khpob	Sna Pi Mukh		3																			350	1,382	3%	9%	12%
Battambang	Aek Phnum	Preaek Luong	Bak Amraek	15	45																			302	1,552	19%	39%	58%
Battambang	Aek Phnum	Preaek Luong	Bak Roteh																					222	1,117	12%	34%	46%
Battambang	Aek Phnum	Preaek Luong	Doun Ent																					249	1,078	30%	7%	37%
Battambang	Aek Phnum	Preaek Luong	Preaek Luong	16	6	128																		470	2,842	10%	18%	28%
Battambang	Aek Phnum	Preaek Luong	Rohal Suong	9	41	79			1															373	1,584	21%	28%	50%
Battambang	Aek Phnum	Preaek Luong	Sdei Kraom	6	49	1					1						1	17	1	17				320	1,578	26%	18%	44%
Battambang	Aek Phnum	Preaek Luong	Sdei Leu	12								1												368	1,691	8%	24%	33%
Battambang	Aek Phnum	Preaek Norint	Ansang Sak			97																		288	1,168	9%	32%	41%
Battambang	Aek Phnum	Preaek Norint	Doung Mea	3	30	40			Joint RS							1								189	768	8%	21%	29%
Battambang	Aek Phnum	Preaek Norint	Preaek Krouch		3																			286	1,304	7%	29%	37%
Battambang	Aek Phnum	Preaek Norint	Preaek Norint	12							1		1											480	2,165	6%	20%	26%
Battambang	Aek Phnum	Preaek Norint	Preaek Ta Chraeng											1										533	2,448	11%	17%	28%
Battambang	Aek Phnum	Preaek Norint	Preaek Trab			96			1								1	13						365	1,826	10%	22%	32%
Battambang	Aek Phnum	Preaek Norint	Reach Doun Kaev			21																		234	974	4%	23%	27%
Battambang	Aek Phnum	Preaek Norint	Rohal Suong	6	30	161					1					2								342	1,355	13%	20%	34%
Battambang	Aek Phnum	Preaek Norint	Sdei	7	31	126			Joint RS			1				2								266	1,119	14%	19%	33%
Battambang	Aek Phnum	Preaek Norint	Svay Chrum	7	3																			318	1,413	6%	31%	36%
Battambang	Aek Phnum	Samraong Knong	Kampong Sambuor									1												554	2,300	3%	26%	29%
Battambang	Banan	Bay Damram	Bay Damram			5										3								297	1,762	5%	9%	14%
Battambang	Banan	Bay Damram	Kampong Chaeng			23																		175	817	5%	23%	28%
Battambang	Banan	Bay Damram	Kanhchroung		2	14																		102	470	9%	10%	19%
Battambang	Banan	Bay Damram	Krala Peas		7	15										1								307	1,348	4%	16%	20%

Location				Category																		#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Battambang	Banan	Bay Damram	Prey Totueng			5																	279	1,449	2%	8%	10%		
Battambang	Banan	Bay Damram	Sdau			3																	177	788	13%	16%	29%		
Battambang	Banan	Bay Damram	Ta Song		11	7										1							135	658	15%	5%	20%		
Battambang	Banan	Bay Damram	Tuol Chranieng			7																	224	984	3%	7%	10%		
Battambang	Banan	Chaeng Mean Chey	Doung				1																337	1,500	34%	23%	57%		
Battambang	Banan	Chheu Teal	Anlok Kaong							Joint Ban.			1			1							137	662	7%	28%	35%		
Battambang	Banan	Chheu Teal	Anlong Ta Mei		9											2							399	1,498	13%	22%	34%		
Battambang	Banan	Chheu Teal	Annachet		18												1	18	1	18			283	1,344	6%	25%	31%		
Battambang	Banan	Chheu Teal	Bay Damram		9							1	1			2							302	1,331	10%	13%	22%		
Battambang	Banan	Chheu Teal	Braboh		29					Joint Ban.													202	914	15%	13%	28%		
Battambang	Banan	Chheu Teal	Chamkar Svay		8					Joint Ban.						1							255	1,183	10%	23%	33%		
Battambang	Banan	Chheu Teal	Chhak Pou		9																		95	861	12%	21%	33%		
Battambang	Banan	Chheu Teal	Chheu Teal													2							388	1,796	13%	14%	27%		
Battambang	Banan	Chheu Teal	Doung		20		44			Joint Ban.													151	615	3%	13%	16%		
Battambang	Banan	Chheu Teal	Khmar		43											1	1	17	1	14			240	1,008	11%	13%	24%		
Battambang	Banan	Chheu Teal	Svay Prakeab		45																		211	1,101	17%	19%	36%		
Battambang	Banan	Chheu Teal	Thkov				1			Joint Ban.						1							186	818	8%	28%	36%		
Battambang	Banan	Chheu Teal	Bat Sala		11																		415	2,412	7%	19%	26%		
Battambang	Banan	Chheu Teal	Kampong Srama		7																		270	1,202	8%	15%	23%		
Battambang	Banan	Chheu Teal	Kampong Chamlang																				278	1,228	11%	20%	31%		
Battambang	Banan	Kantueu Muoy	Voat Kantueu		9		27																207	984	7%	12%	18%		
Battambang	Banan	Kantueu Muoy	Kampong Ampil		12																		168	725	10%	6%	16%		
Battambang	Banan	Kantueu Muoy	Svay Prey		2																		145	709	4%	12%	16%		
Battambang	Banan	Kantueu Pir	Banan		18					2													476	2,040	9%	29%	38%		
Battambang	Banan	Kantueu Pir	Post Kantueu									1											139	573	26%	35%	61%		
Battambang	Banan	Phnum Sampov	Kampouv		9	5																	338	1,605	19%	37%	56%		
Battambang	Banan	Phnum Sampov	Krapeu Cheung			195										2							650	2,627	2%	11%	13%		
Battambang	Banan	Phnum Sampov	Kouk Ampil		4																		251	1,051	12%	22%	35%		
Battambang	Banan	Phnum Sampov	Chaeng Kdar		21																		250	1,072	7%	30%	37%		
Battambang	Banan	Phnum Sampov	Sampov Lech			9																	365	1,665	6%	7%	13%		
Battambang	Banan	Snoeng	Boeng Chaeng			168																	323	1,369	22%	34%	57%		
Battambang	Banan	Snoeng	Boeng Krasal			84																	479	2,232	19%	19%	38%		
Battambang	Banan	Snoeng	Boeng Prei			112																	521	2,572	17%	11%	27%		
Battambang	Banan	Snoeng	Kor																				222	1,934	7%	32%	40%		
Battambang	Banan	Snoeng	Preah Srae																				332	2,501	7%	14%	21%		
Battambang	Banan	Snoeng	Rumchey		15	119	16			1													385	1,808	9%	21%	30%		
Battambang	Banan	Snoeng	Sambuor Meas							Joint Ban.													350	1,650	12%	45%	56%		



Location				Category																		#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Populatio n	%HH P1	%HH P2	%HH P1&P2	
Battambang	Banan	Snoeng	Samraong			140																206	1,897	40%	32%	71%			
Battambang	Banan	Snoeng	Snoeng Kaeut			175				1			1									400	1,930	20%	29%	49%			
Battambang	Banan	Snoeng	Snoeng Lech			136																276	1,540	15%	29%	44%			
Battambang	Banan	Snoeng	Peak Sbaek																			308	1,181	7%	18%	24%			
Battambang	Banan	Ta Kream	Andong Neang																			185	918	23%	30%	53%			
Battambang	Banan	Ta Kream	Ou Pong Moan			257																525	2,487	11%	37%	48%			
Battambang	Banan	Ta Kream	Ou Ta Nhea			315										2						354	1,563	26%	26%	52%			
Battambang	Banan	Ta Kream	Paoy Svay			114										1						298	1,614	16%	13%	29%			
Battambang	Banan	Ta Kream	Prey Phdau			40																213	1,131	29%	12%	41%			
Battambang	Banan	Ta Kream	Slab Pang																			442	1,785	31%	29%	60%			
Battambang	Banan	Ta Kream	Ta Kream			259										1						339	1,546	19%	27%	46%			
Battambang	Banan	Ta Kream	Ta Ngaen			188										1						836	3,476	19%	32%	51%			
Battambang	Banan	Ta Kream	Thmei			152										4						415	2,398	25%	26%	51%			
Battambang	Banan	Ta Kream	Dangkut Thnong																			347	1,603	34%	40%	74%			
Battambang	Banan	Ta Kream	Anlong Svay																			416	2,442	29%	34%	62%			
Battambang	Bavel	Bavel	Dach Proat											1								339	1,596	16%	5%	21%			
Battambang	Bavel	Bavel	Doun Av		4	42																156	780	30%	13%	43%			
Battambang	Bavel	Bavel	Prey Totueng Pir											1								539	2,316	14%	14%	28%			
Battambang	Bavel	Bavel	Sang Reang		8	40																415	2,004	18%	9%	27%			
Battambang	Bavel	Bavel	Svay Chrum		40	69																248	1,185	7%	14%	20%			
Battambang	Bavel	Bavel	Bavel Pir		1																	442	1,980	11%	3%	14%			
Battambang	Bavel	Kdol Tahen	Khleang											1								No data	No data	No data	No data	No data			
Battambang	Bavel	Khnach Romeas	Ballang Leu	9	41	107					1					1						263	1,317	13%	3%	15%			
Battambang	Bavel	Khnach Romeas	Ballang Mean Chey		28	78					1					1						125	630	10%	15%	25%			
Battambang	Bavel	Khnach Romeas	Khnach Romeas	6	43	83					3		1									629	3,223	4%	10%	14%			
Battambang	Bavel	Khnach Romeas	Koah Ream	10	12							1				7						491	2,318	11%	5%	16%			
Battambang	Bavel	Khnach Romeas	Prey Sangha	18	60	62					1					5						376	1,931	7%	15%	22%			
Battambang	Bavel	Khnach Romeas	Rung Ampil	13	26	24																276	1,656	9%	5%	13%			
Battambang	Bavel	Khnach Romeas	Svay Sa	5	16	57										1						164	811	13%	12%	25%			
Battambang	Bavel	Klaeng Meas	Chrang Bak		44																	241	1,097	22%	16%	39%			
Battambang	Bavel	Klaeng Meas	Khleang		3																	95	511	14%	7%	21%			
Battambang	Bavel	Klaeng Meas	Ou Doun Pov		23																	190	824	8%	11%	19%			
Battambang	Bavel	Klaeng Meas	Kampong Mkak		3																	130	584	15%	4%	18%			
Battambang	Bavel	Lvea	Boeng Samraong			99																255	1,150	12%	8%	20%			
Battambang	Bavel	Lvea	Kbal Spean											1								217	1,005	12%	8%	20%			
Battambang	Bavel	Lvea	Ping Pong			107																301	1,092	16%	5%	21%			
Battambang	Bavel	Lvea	Ream Sena											1								248	1,013	10%	8%	18%			

Location				Category																			#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs	Population				%HH P1	%HH P2	%HH P1&P2		
Battambang	Bavel	Lvea	Svay Prey			111																	■	251	1,189	10%	12%	22%		
Battambang	Bavel	Lvea	Lvea Chas		9																		■	216	1,059	16%	5%	21%		
Battambang	Bavel	Prey Khpos	Pou		9																		■	265	1,363	19%	9%	27%		
Battambang	Bavel	Prey Khpos	Prey Khpos		7																		■	235	926	14%	16%	30%		
Battambang	Krong Battambang	Kdol Doun Teav	Kantuot									1												266	1,355	5%	15%	20%		
Battambang	Krong Battambang	Kdol Doun Teav	Chong Preaek		13																		■	240	1,197	11%	16%	28%		
Battambang	Krong Battambang	Ou Char	Anhchanh												1									445	2,767	4%	17%	21%		
Battambang	Krong Battambang	Ou Char	Prey Koun Sek											1										219	1,255	6%	34%	40%		
Battambang	Krong Battambang	Ou Char	Kab Kou Thmei																			■	665	4,465	3%	24%	27%			
Battambang	Krong Battambang	Ou Mal	Boeng Reang			80																■	■	366	1,621	9%	23%	32%		
Battambang	Krong Battambang	Ou Mal	Dak Sasar			56																■	■	232	1,139	12%	19%	31%		
Battambang	Krong Battambang	Ou Mal	Kouk Ponley			49	20															■	■	227	1,110	17%	12%	28%		
Battambang	Krong Battambang	Ou Mal	Koun Sek			58																■	■	140	645	19%	16%	35%		
Battambang	Krong Battambang	Ou Mal	Ou Mal			11								1								■	■	185	843	18%	29%	47%		
Battambang	Krong Battambang	Ou Mal	Prey Dach		48	56											1	17	1	15		■	■	221	902	20%	17%	37%		
Battambang	Krong Battambang	Ou Mal	Voat Roka		34	45											1	20	1	17		■	■	301	1,471	9%	29%	38%		
Battambang	Krong Battambang	Ou Mal	Prey Roka																			■		202	779	8%	22%	30%		
Battambang	Krong Battambang	Ou Mal	Andoung Pring																			■		336	1,480	7%	20%	27%		
Battambang	Krong Battambang	Ou Mal	Sala Balat		1																	■		250	1,150	11%	29%	40%		
Battambang	Krong Battambang	Preaek Preah Sdach	Ou Khcheay												1									296	1,813	10%	27%	37%		
Battambang	Krong Battambang	Rotanak	Rumchek Buon		13										1								■	779	4,090	5%	13%	19%		
Battambang	Krong Battambang	Rotanak	Rumchek Pram												1									212	1,176	5%	14%	19%		
Battambang	Krong Battambang	Svay Pao	Mphey Osakphea												1									565	3,981	3%	5%	9%		
Battambang	Krong Battambang	Svay Pao	Preaek Moha Tep												2									1,082	6,894	2%	13%	16%		
Battambang	Krong Battambang	Tuol Ta Aek	Tuol Ta Aek													1								1,187	6,011	5%	14%	19%		
Battambang	Krong Battambang	Voat Kor	Ballang		64						1						1	24	1	23		■	■	360	2,595	8%	12%	21%		
Battambang	Krong Battambang	Voat Kor	Chrab Krasang	1	50												1	17	1	14		■	■	638	3,547	9%	11%	20%		
Battambang	Krong Battambang	Voat Kor	Damnak Luong		1										1		1	20	1	18		■		428	2,419	10%	9%	19%		
Battambang	Krong Battambang	Voat Kor	Khsach Pouy								1											■		430	2,418	5%	15%	20%		
Battambang	Krong Battambang	Voat Kor	Voat Kor									1											■	666	3,527	6%	14%	20%		
Battambang	Krong Battambang	Voat Kor	Kampong Seima																			■		322	1,956	8%	11%	19%		
Battambang	Koas Krala	Preah Phos	Boeng Preah Kralanh		12																		■	36	184	8%	32%	41%		
Battambang	Koas Krala	Hab	Chambak		1																		■	129	515	27%	29%	56%		
Battambang	Koas Krala	Hab	Trapeang Dang Tuek		2																		■	83	304	12%	47%	58%		
Battambang	Koas Krala	Hab	Hab		5																		■	180	774	18%	18%	36%		
Battambang	Koas Krala	Hab	Sameakki		4																		■	128	459	27%	39%	67%		
Battambang	Koas Krala	Koas Krala	Voat		4																		■	98	445	27%	31%	58%		

Location				Category																		#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Battambang	Koas Krala	Koas Krala	Damnak Kakaoh		2																		65	430	41%	28%	70%		
Battambang	Koas Krala	Thipakdei	Kantuot		2																		225	1,016	19%	25%	43%		
Battambang	Koas Krala	Thipakdei	Samraong		1																		157	759	37%	35%	71%		
Battambang	Moung Ruessei	Chrey	Chong Chamnay	13	37	13											3						456	2,051	4%	28%	31%		
Battambang	Moung Ruessei	Chrey	Chrey Cheung	6	21	79						1					2						317	1,480	5%	18%	23%		
Battambang	Moung Ruessei	Chrey	Chrey Muoy	9	25	56																	154	732	21%	11%	32%		
Battambang	Moung Ruessei	Chrey	Chrey Pir											1									315	1,617	26%	18%	45%		
Battambang	Moung Ruessei	Chrey	Doun Tri																				450	2,056	25%	15%	40%		
Battambang	Moung Ruessei	Chrey	Mreah Prov	18	36	162					1												297	1,482	19%	13%	32%		
Battambang	Moung Ruessei	Chrey	Tuol Ta Thon	6	18	74																	183	921	7%	25%	32%		
Battambang	Moung Ruessei	Kakaoh	Chak Thum			81																	447	2,034	6%	19%	25%		
Battambang	Moung Ruessei	Kakaoh	Chak Touch			72																	423	1,846	13%	28%	41%		
Battambang	Moung Ruessei	Kakaoh	Kakaoh			97						1											380	2,059	16%	18%	34%		
Battambang	Moung Ruessei	Kakaoh	Ph"ieng			52																	262	1,161	16%	24%	41%		
Battambang	Moung Ruessei	Kakaoh	Srae Ou			54																	460	2,163	14%	25%	38%		
Battambang	Moung Ruessei	Kakaoh	Tuol Prum Muoy																				402	1,937	18%	32%	50%		
Battambang	Moung Ruessei	Kear	Kear Bei																				234	1,130	12%	16%	29%		
Battambang	Moung Ruessei	Kear	Kear Muoy	14	15	72											1						237	1,234	7%	22%	28%		
Battambang	Moung Ruessei	Kear	Kear Pir																				171	739	13%	18%	31%		
Battambang	Moung Ruessei	Kear	Koh Thkov																				314	1,474	19%	12%	31%		
Battambang	Moung Ruessei	Kear	Ou Kriet											1			1						415	2,110	22%	5%	27%		
Battambang	Moung Ruessei	Kear	Pou Muoy														1						354	1,714	10%	6%	16%		
Battambang	Moung Ruessei	Kear	Pou Pir														1						365	1,576	10%	13%	23%		
Battambang	Moung Ruessei	Kear	Ream Kon														3						459	2,258	14%	10%	24%		
Battambang	Moung Ruessei	Kear	Roka Chhmoul																				315	1,492	13%	6%	18%		
Battambang	Moung Ruessei	Kear	Run																				243	1,164	9%	22%	31%		
Battambang	Moung Ruessei	Kear	Ta Nak																				315	1,871	11%	13%	24%		
Battambang	Moung Ruessei	Moung Ruessei	Moung											1			2						367	1,573	2%	7%	9%		
Battambang	Moung Ruessei	Moung Ruessei	Pralay		1																		149	710	4%	11%	15%		
Battambang	Moung Ruessei	Prey Touch	Koun Khlong			152																	415	2,041	17%	14%	31%		
Battambang	Moung Ruessei	Prey Touch	Prey Damrei		4	168																	431	2,074	21%	11%	32%		
Battambang	Moung Ruessei	Prey Touch	Prey Touch			122						1											284	1,420	16%	18%	33%		
Battambang	Moung Ruessei	Prey Touch	Boeng Pring		27																		174	793	23%	7%	30%		
Battambang	Moung Ruessei	Prey Touch	Thmei		5																		295	1,305	15%	17%	31%		
Battambang	Moung Ruessei	Prey Touch	Prean Nil		13																		199	1,488	19%	13%	32%		
Battambang	Moung Ruessei	Robas Mongkol	Koun K'aek Muoy	17	23	92						1					1						237	1,086	12%	15%	28%		
Battambang	Moung Ruessei	Robas Mongkol	Koun K'aek Pir											1			1						306	1,425	16%	12%	28%		

Location				Category																		#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Battambang	Moung Ruessei	Robas Mongkol	Robas Mongkol	21	36	77																	204	926	12%	10%	22%		
Battambang	Moung Ruessei	Robas Mongkol	Anlong Koub		11																		203	781	4%	25%	28%		
Battambang	Moung Ruessei	Robas Mongkol	Boeng Bei		7																		280	1,289	11%	25%	35%		
Battambang	Moung Ruessei	Robas Mongkol	Anlong Tamok		1																		260	1,156	16%	11%	26%		
Battambang	Moung Ruessei	Ta Loas	Chong Pralay		26	88					1	1					2						258	1,199	10%	13%	23%		
Battambang	Moung Ruessei	Ta Loas	Ma Naok																				315	1,765	16%	16%	32%		
Battambang	Moung Ruessei	Ta Loas	Pralay Sdau		14	35																	156	666	5%	24%	30%		
Battambang	Moung Ruessei	Ta Loas	Sdei Stueng		19	120																	215	1,005	22%	18%	40%		
Battambang	Moung Ruessei	Ta Loas	Stueng Thmei	9	14	84											2						187	782	4%	7%	11%		
Battambang	Moung Ruessei	Ta Loas	Suosdei																				373	1,786	19%	16%	36%		
Battambang	Moung Ruessei	Ta Loas	Tras	4	34	78																	227	963	17%	15%	32%		
Battambang	Moung Ruessei	Ta Loas	Veal		22	34																	152	602	23%	8%	31%		
Battambang	Moung Ruessei	Ta Loas	Voat Chas																				185	833	9%	17%	26%		
Battambang	Phnom Proek	Chak Krey	Spean Tumneap		9																		343	1,715	27%	No data	27%		
Battambang	Phnom Proek	Chak Krey	Anlong Krouch		8																		211	923	25%	23%	47%		
Battambang	Phnom Proek	Chak Krey	Phnum Prampir		10																		1,068	5,038	24%	20%	44%		
Battambang	Rotonak Mondol	Andaek Haeb	Andaek Haeb		5																		159	662	3%	20%	23%		
Battambang	Rotonak Mondol	Phlov Meas	Chi Pang									1											101	818	19%	22%	41%		
Battambang	Rotonak Mondol	Phlov Meas	Ou Traeng				29			Joint PM							1	18	1	15				350	1,476	26%	14%	40%	
Battambang	Rotonak Mondol	Phlov Meas	Phlov Meas				49			1			1				1	17	1	17				267	2,484	29%	14%	43%	
Battambang	Rotonak Mondol	Phlov Meas	Sek Sak				14			Joint PM													190	795	30%	22%	53%		
Battambang	Rotonak Mondol	Phlov Meas	Tuek Sab							Joint PM													75	360	18%	17%	35%		
Battambang	Rotonak Mondol	Sdau	Baribour		19																		147	607	11%	27%	38%		
Battambang	Rotonak Mondol	Sdau	Dangkot		12																		195	833	20%	46%	66%		
Battambang	Rotonak Mondol	Sdau	Sdau		2																		531	2,394	6%	12%	18%		
Battambang	Rotonak Mondol	Sdau	Kouk Choar		8																		94	376	12%	21%	33%		
Battambang	Rotonak Mondol	Sdau	Banang		5																		335	1,597	19%	23%	42%		
Battambang	Rotonak Mondol	Traeng	Chi Sang				24																331	1,582	28%	16%	44%		
Battambang	Rotonak Mondol	Traeng	Phcheav				5																590	2,973	7%	20%	26%		
Battambang	Rotonak Mondol	Traeng	Chea Montrei		9																		318	1,424	20%	13%	33%		
Battambang	Rotonak Mondol	Traeng	Kilou Samprambe		12																		459	2,450	9%	20%	29%		
Battambang	Rukhak Kiri	Mukh Reah	Dang Hoa		19																		139	667	7%	15%	22%		
Battambang	Rukhak Kiri	Mukh Reah	Svay Yar		10																		159	585	22%	2%	24%		
Battambang	Rukhak Kiri	Basak	Chhouk		6																		198	1,540	18%	24%	42%		
Battambang	Rukhak Kiri	Preaek Chik	Preaek Taven		19																		605	3,439	6%	15%	21%		
Battambang	Rukhak Kiri	Preaek Chik	Thnom		10																		219	1,095	10%	11%	20%		
Battambang	Rukhak Kiri	Preaek Chik	Khnach Ampor		8																		323	1,516	13%	22%	35%		

Location				Category																		#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Battambang	Rukhak Kiri	Preaek Chik	Siem		3																		165	766	5%	17%	21%		
Battambang	Rukhak Kiri	Preaek Chik	Chhkae Kham Praeus		4																		326	1,495	9%	17%	26%		
Battambang	Rukhak Kiri	Preaek Chik	Preaek Chik		6																		371	1,495	12%	13%	26%		
Battambang	Rukhak Kiri	Prey Tralach	Pralay Dabprambei				9																613	3,487	29%	26%	55%		
Battambang	Rukhak Kiri	Prey Tralach	Prey Ampaon				7																367	1,623	25%	9%	33%		
Battambang	Rukhak Kiri	Prey Tralach	Sreah Thort				9																163	707	46%	38%	84%		
Battambang	Rukhak Kiri	Prey Tralach	Prey Tralach				2																307	1,307	10%	35%	46%		
Battambang	Samlout	Kampong Lpov	Svay Chrum									1											185	830	6%	38%	43%		
Battambang	Samlout	Samlout	Bueng Run									1	1										546	2,496	10%	13%	23%		
Battambang	Samlout	Sung	Kandal		57		51			1	1											■	■	■	357	1,497	18%	15%	33%
Battambang	Samlout	Sung	Srae Reach		10																		■		101	530	3%	16%	19%
Battambang	Samlout	Sung	Sung Muoy									1													279	1,217	5%	11%	17%
Battambang	Samlout	Ta Sanh	Ou Sngout										1												314	1,236	17%	28%	46%
Battambang	Samlout	Ta Taok	Peam									1													54	268	19%	49%	68%
Battambang	Samlout	Ta Taok	Phnum Rai		26		45			1	1												■	■	247	1,135	31%	34%	66%
Battambang	Sangkae	Anlong Vil	Ou Muni Muoy			3																■	■	474	1,994	41%	14%	56%	
Battambang	Sangkae	Anlong Vil	Ou Muni Pir			1																■	■	180	845	35%	24%	59%	
Battambang	Sangkae	Anlong Vil	Svay Kang		49												1	22	1	20		■	■	464	3,039	8%	24%	32%	
Battambang	Sangkae	Anlong Vil	Beng																			■		513	2,783	6%	25%	31%	
Battambang	Sangkae	Anlong Vil	Chrab Veal																			■		307	1,351	4%	17%	21%	
Battambang	Sangkae	Anlong Vil	Anlong Vil																			■		1,020	4,134	7%	31%	37%	
Battambang	Sangkae	Anlong Vil	Puk Chhma																			■		171	857	8%	22%	30%	
Battambang	Sangkae	Anlong Vil	Chumnik																			■		462	2,256	20%	15%	35%	
Battambang	Sangkae	Anlong Vil	Spong																			■		180	872	32%	21%	53%	
Battambang	Sangkae	Kampong Preah	Kampong Preah			4						1											■		532	2,225	15%	24%	40%
Battambang	Sangkae	Kampong Preah	Srah Kaev	1		4																	■		508	2,443	11%	32%	43%
Battambang	Sangkae	Kampong Prieng	Kach Roteh		1	48							1									■	■	298	1,386	23%	4%	26%	
Battambang	Sangkae	Kampong Prieng	Kbal Thnal		23	105											1	20	1	20		■	■	363	1,750	14%	21%	35%	
Battambang	Sangkae	Kampong Prieng	Os Tuk	2		207																■	■	526	2,557	22%	10%	32%	
Battambang	Sangkae	Kampong Prieng	Sala Trav			47																■	■	233	1,174	34%	22%	56%	
Battambang	Sangkae	Kampong Prieng	Sambok Ak		46	160					1						1	15				■	■	507	2,412	17%	21%	38%	
Battambang	Sangkae	Kampong Prieng	Thmei		43	34						1					1	22	1	19		■	■	286	1,642	7%	16%	23%	
Battambang	Sangkae	Norea	Norea Muoy									1												413	2,167	12%	22%	34%	
Battambang	Sangkae	Ou Dambang Muoy	Baoh Pou			109																■	■	708	4,079	11%	19%	29%	
Battambang	Sangkae	Ou Dambang Muoy	Ou Khcheay	20	18	59					1						1	29	1	26		■	■	432	2,020	2%	15%	17%	
Battambang	Sangkae	Ou Dambang Muoy	Ou Sralau	8	16	133											1	20	1	19		■	■	579	3,264	10%	17%	27%	
Battambang	Sangkae	Ou Dambang Muoy	Samraong Kaong			117																■	■	169	837	17%	30%	47%	

Location				Category																	#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Battambang	Sangkae	Ou Dambang Muoy	Voat Ta Moem																			626	3,550	3%	8%	11%		
Battambang	Sangkae	Ou Dambang Muoy	Voat Chaeng																			216	1,106	3%	32%	35%		
Battambang	Sangkae	Reang Kesei	Boeng Veaeng			49								1								125	699	6%	12%	18%		
Battambang	Sangkae	Reang Kesei	Damnak Dangkao			45																162	982	16%	29%	45%		
Battambang	Sangkae	Reang Kesei	Kakaoh Kambot			38																111	625	2%	23%	24%		
Battambang	Sangkae	Reang Kesei	Prey Svay			70																208	1,041	33%	24%	57%		
Battambang	Sangkae	Reang Kesei	Reang Kesei		25	63							1				1	24	1	15		231	1,231	5%	13%	18%		
Battambang	Sangkae	Reang Kesei	Reang Kraol		21	110					1						1	24	1	17		331	1,641	10%	19%	29%		
Battambang	Sangkae	Reang Kesei	Svay Cheat			80																351	1,501	6%	21%	27%		
Battambang	Sangkae	Reang Kesei	Tuol Snuol			35																159	1,029	12%	14%	26%		
Battambang	Sangkae	Reang Kesei	Voat Kandal		22	123											1	26	1	20		321	1,205	11%	27%	38%		
Battambang	Sangkae	Roka	Ambaeng Thngae		19	129											1	28	1	24		241	1,167	38%	13%	51%		
Battambang	Sangkae	Roka	Chhung Tradak			11											1	24	1	18		425	1,898	9%	22%	31%		
Battambang	Sangkae	Roka	Pou Batdambang		20	167			1								1	18	1	18		238	1,150	17%	26%	42%		
Battambang	Sangkae	Roka	Roka		42	165					1		1				1	20	1	20		482	2,608	11%	27%	38%		
Battambang	Sangkae	Roka	Ta Haen Muoy		58	147					1						1	23	1	21		339	1,870	20%	41%	61%		
Battambang	Sangkae	Roka	Ta Haen Pir		45	122											1	27	1	17		204	1,455	8%	34%	42%		
Battambang	Sangkae	Ta Pun	Basaet	17																		874	3,788	25%	23%	49%		
Battambang	Sangkae	Ta Pun	Ta Pon			4																461	2,283	26%	20%	45%		
Battambang	Sangkae	Voat Ta Muem	Anlong Lvea		24	38					1						1	29	1	17		303	1,274	10%	26%	36%		
Battambang	Sangkae	Voat Ta Muem	Kampong Chlang	7	56	62											1	22	1	21		790	3,410	5%	16%	21%		
Battambang	Sangkae	Voat Ta Muem	Ou Khcheay	15	18												1	22	1	22		491	2,219	8%	29%	37%		
Battambang	Sangkae	Voat Ta Muem	Ou Sralau		45												1	15	1	14		635	2,968	4%	17%	21%		
Battambang	Sangkae	Voat Ta Muem	Sla Kram	2	44						1		1				1	20	1	20		370	1,584	13%	25%	37%		
Battambang	Sangkae	Voat Ta Muem	Kampong Ampil																			757	5,225	10%	24%	34%		
Battambang	Thma Koul	Anlong Run	Char			47																220	1,242	14%	12%	26%		
Battambang	Thma Koul	Anlong Run	Sla Slak			51																174	962	42%	16%	58%		
Battambang	Thma Koul	Anlong Run	Souphi			66																240	1,279	18%	3%	21%		
Battambang	Thma Koul	Bansay Traeng	Bansay Traeng			61						1	1									323	1,534	6%	11%	17%		
Battambang	Thma Koul	Bansay Traeng	Kaong Kang	10	19	52											1	20	1	16		208	849	6%	25%	31%		
Battambang	Thma Koul	Bansay Traeng	Spean		22	36											1	15	1	15		448	2,099	8%	20%	28%		
Battambang	Thma Koul	Bansay Traeng	Ta Kay			72																234	992	24%	9%	33%		
Battambang	Thma Koul	Bansay Traeng	Thmea		31												1	16				240	1,042	37%	17%	54%		
Battambang	Thma Koul	Bansay Traeng	Thmei			50					1											413	1,994	17%	21%	38%		
Battambang	Thma Koul	Bansay Traeng	Tuol Ta Sokh	9	22												1	21	1	21		190	909	13%	26%	39%		
Battambang	Thma Koul	Boeng Pring	Boeng Pring		26	151					1	1	1	1			1	16				974	4,723	16%	27%	43%		
Battambang	Thma Koul	Boeng Pring	Ou Nhor		29	106										1	1	22	1	17		501	2,382	12%	31%	42%		



Location				Category																		#Mobile kitchen village	#O&M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Populatio n	%HH P1	%HH P2	%HH P1&P2	
Battambang	Thma Koul	Boeng Pring	Paoy Ta Sek		15	139											1	19	1	19	<div></div>		<div></div>	408	2,177	22%	27%	49%	
Battambang	Thma Koul	Boeng Pring	Snuol Kaong			130															<div></div>		<div></div>	125	1,033	20%	32%	52%	
Battambang	Thma Koul	Chrey	Anlong Run																		<div></div>			176	982	30%	17%	48%	
Battambang	Thma Koul	Chrey	Chrey			43										1					<div></div>	<div></div>	<div></div>	291	1,398	10%	24%	34%	
Battambang	Thma Koul	Chrey	Chrey Thmei			68								1							<div></div>	<div></div>	<div></div>	127	1,186	31%	26%	57%	
Battambang	Thma Koul	Chrey	Hai San										1									<div></div>		609	2,659	13%	34%	47%	
Battambang	Thma Koul	Chrey	Ka Kou			58															<div></div>		<div></div>	356	1,906	14%	23%	37%	
Battambang	Thma Koul	Chrey	Kbal Khmaoch	2	23	81					1	1				1					<div></div>	<div></div>	<div></div>	326	1,765	27%	23%	50%	
Battambang	Thma Koul	Chrey	Kruos			73															<div></div>		<div></div>	219	974	5%	28%	33%	
Battambang	Thma Koul	Chrey	Popeal Khae			62								1							<div></div>		<div></div>	535	2,397	1%	21%	23%	
Battambang	Thma Koul	Chrey	Prey Totueng		32	84											1	18	1	18	<div></div>		<div></div>	426	1,907	19%	19%	37%	
Battambang	Thma Koul	Chrey	Svay Chrum		15	93											2				<div></div>	<div></div>	<div></div>	340	1,389	18%	18%	36%	
Battambang	Thma Koul	Chrouy Sdau	Chrouy Sdau		66	361						1		1			1	18			<div></div>		<div></div>	651	3,120	5%	22%	27%	
Battambang	Thma Koul	Chrouy Sdau	Nikom Knong	14	44	91					1						1	19	1	16	<div></div>		<div></div>	963	4,948	14%	4%	18%	
Battambang	Thma Koul	Chrouy Sdau	Nikom Krau		58	139											1	19	1	17	<div></div>		<div></div>	590	3,128	12%	9%	21%	
Battambang	Thma Koul	Kouk Khmum	Chhkae Koun		23	211								1			1	24	1	21	<div></div>	<div></div>	<div></div>	446	1,972	26%	9%	35%	
Battambang	Thma Koul	Kouk Khmum	Chranieng	8	36	181											1	25	1	19	<div></div>		<div></div>	285	1,295	21%	20%	41%	
Battambang	Thma Koul	Kouk Khmum	Kandal Cheung																		<div></div>			168	847	11%	20%	30%	
Battambang	Thma Koul	Kouk Khmum	Kandal Tboung									1									<div></div>			355	1,467	4%	20%	24%	
Battambang	Thma Koul	Kouk Khmum	Kien Kaes Muoy			128					1			1							<div></div>	<div></div>	<div></div>	527	2,120	8%	15%	23%	
Battambang	Thma Koul	Kouk Khmum	Kien Kaes Pir			253															<div></div>		<div></div>	613	3,480	16%	16%	32%	
Battambang	Thma Koul	Kouk Khmum	Kouk Khmum	15	52	203					2		1			1	1	20	1	15	<div></div>	<div></div>	<div></div>	233	1,053	22%	19%	41%	
Battambang	Thma Koul	Kouk Khmum	Ta Meakh	11	19												1	20	1	20	<div></div>		<div></div>	290	1,191	19%	20%	39%	
Battambang	Thma Koul	Ou Ta Ki	Kakaoh			6															<div></div>		<div></div>	326	1,313	10%	34%	44%	
Battambang	Thma Koul	Ou Ta Ki	Ou Ta Ki	5	35	1							1			2					<div></div>	<div></div>	<div></div>	842	3,806	29%	9%	37%	
Battambang	Thma Koul	Ou Ta Ki	Popeal Khae									1				1					<div></div>	<div></div>		665	2,874	58%	42%	100%	
Battambang	Thma Koul	Ou Ta Ki	Prey Dach																		<div></div>			315	1,531	45%	14%	59%	
Battambang	Thma Koul	Ou Ta Ki	Trang			100										3					<div></div>	<div></div>	<div></div>	466	1,950	16%	23%	38%	
Battambang	Thma Koul	Ou Ta Ki	Tras	6	73	41										1					<div></div>	<div></div>	<div></div>	480	1,837	27%	20%	47%	
Battambang	Thma Koul	Rung Chrey	Ballang Kraom	19	22	128						1		1		2					<div></div>	<div></div>	<div></div>	476	1,962	7%	13%	20%	
Battambang	Thma Koul	Rung Chrey	Kouk Khpos		22	82					1	1	1			1						<div></div>	<div></div>	219	1,118	8%	9%	17%	
Battambang	Thma Koul	Rung Chrey	Paoy Rumchey																				<div></div>	108	510	11%	30%	41%	
Battambang	Thma Koul	Rung Chrey	Prakeab		45	120					1					4					<div></div>	<div></div>	<div></div>	666	3,336	4%	7%	11%	
Battambang	Thma Koul	Rung Chrey	Preah Ponlea	14	30	128										2						<div></div>	<div></div>	597	2,498	15%	10%	24%	
Battambang	Thma Koul	Rung Chrey	Rung Chrey	14	36	91					2					3					<div></div>	<div></div>	<div></div>	290	1,329	10%	14%	24%	
Battambang	Thma Koul	Rung Chrey	Tuol	9	22	42					1					1					<div></div>	<div></div>	<div></div>	152	709	27%	10%	37%	
Battambang	Thma Koul	Ta Meun	Ang Cheung	7	52	46			1				1								<div></div>	<div></div>	<div></div>	335	1,714	9%	15%	23%	

Location				Category																				Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O&M village	#FTF village	#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Battambang	Thma Koul	Ta Meun	Chrouy Mtes	2	22	29															■	■	■	262	1,255	10%	2%	12%
Battambang	Thma Koul	Ta Meun	Kouk Trab		10	81										1					■	■	■	528	2,580	5%	7%	11%
Battambang	Thma Koul	Ta Meun	Krasang		10																■		■	266	1,453	12%	8%	20%
Battambang	Thma Koul	Ta Meun	Samraong	4	10	124															■	■	■	177	791	5%	13%	18%
Battambang	Thma Koul	Ta Meun	Ta Sei	20	34											3					■	■	■	587	2,627	8%	5%	12%
Battambang	Thma Koul	Ta Meun	Thma Koul Cheung													1					■	■		394	2,078	6%	5%	11%
Battambang	Thma Koul	Ta Meun	Thmei	13	42	39															■	■	■	446	2,324	13%	4%	16%
Battambang	Thma Koul	Ta Meun	Tumneab									1				2					■	■		121	474	7%	No data	7%
Battambang	Thma Koul	Ta Meun	Tumpung Cheung																		■			329	1,340	7%	10%	18%
Battambang	Thma Koul	Ta Pung	Ang Tboung		1																■		■	345	1,749	12%	24%	36%
Battambang	Thma Koul	Ta Pung	Tumpung Tboung																		■			359	1,955	31%	69%	100%
Battambang	Thma Koul	Ta Pung	Kaksekam	1							1			1		4					■		■	356	1,546	5%	23%	28%
Battambang	Thma Koul	Ta Pung	Kouk Kduoch													1					■			612	2,757	5%	23%	28%
Battambang	Thma Koul	Ta Pung	Paoy Samraong								1					1					■			656	2,805	3%	18%	21%
Battambang	Thma Koul	Ta Pung	Paoy Yong											1							■			579	2,529	8%	33%	41%
Battambang	Thma Koul	Ta Pung	Thma Koul Tboung									1				1					■			333	1,415	2%	10%	12%
Sub-Total Battambang	12	71	349	635	3,782	13,577	353	0	6	7	37	31	22	19	8	108	52	1,059	47	847	220	97	248	119,096	579,129	13%	19%	32%

Cambodia HARVEST Target Villages -- Clients & Farmer beneficiaries, Sector Focus, and Target HHs/Populations (as of December 31, 2014)																												
Location				Category																	Target Populations							
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O & M village	#FTF village	#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Siem Reap	Angkor Chum	Char Chhuk	Doun Sva											1										192	1,063	1%	7%	8%
Siem Reap	Angkor Thum	Chob Ta Trav	Chob	5	51						1		1				1	16						153	873	10%	31%	41%
Siem Reap	Angkor Thum	Chob Ta Trav	Pong Tuek	6	31						1						1	22						250	1,246	12%	21%	33%
Siem Reap	Angkor Thum	Chob Ta Trav	Prasat		24												1	24	1	14				148	685	22%	29%	51%
Siem Reap	Angkor Thum	Chob Ta Trav	Toap Svay	9	25												1	30	1	9				297	1,205	33%	24%	57%
Siem Reap	Angkor Thum	Chob Ta Trav	Trapeang Tuk																					97	642	17%	27%	44%
Siem Reap	Angkor Thum	Leang Dai	Bampenh Reach	11	18						1						1	21	1	8				162	682	23%	25%	48%
Siem Reap	Angkor Thum	Leang Dai	Doun Ov																					200	742	25%	18%	43%
Siem Reap	Angkor Thum	Leang Dai	Kouk Kreul		2																			118	618	29%	21%	50%
Siem Reap	Angkor Thum	Leang Dai	Leang Dai	3	36												1	35	1	30				295	1,083	26%	32%	58%
Siem Reap	Angkor Thum	Leang Dai	Phlong		47						1	1	1			2	1	19						388	1,742	21%	15%	36%
Siem Reap	Angkor Thum	Leang Dai	Samraong	6	47												1	29	1	24				459	1,993	12%	19%	30%
Siem Reap	Angkor Thum	Leang Dai	Spean Thmei		23																			84	457	43%	15%	58%
Siem Reap	Angkor Thum	Leang Dai	Ta Prok	4	29												1	24	1	15				243	1,482	26%	15%	42%
Siem Reap	Angkor Thum	Leang Dai	Trapeang Svay	4	38	25											1	29	1	10				235	1,132	27%	18%	45%
Siem Reap	Angkor Thum	Peak Snaeng	Chob Saom	6	37																			147	715	15%	30%	46%
Siem Reap	Angkor Thum	Peak Snaeng	Khting																					120	532	12%	33%	45%
Siem Reap	Angkor Thum	Peak Snaeng	Lieb																					89	391	41%	26%	67%
Siem Reap	Angkor Thum	Peak Snaeng	Peak Snaeng Chas																					228	1,119	27%	24%	51%
Siem Reap	Angkor Thum	Peak Snaeng	Peak Snaeng Thmei	9	48						1	1	1			2								422	1,994	29%	20%	48%
Siem Reap	Angkor Thum	Peak Snaeng	Sandan	6	35						1													156	752	28%	25%	53%
Siem Reap	Angkor Thum	Svay Chek	Bos Ta Trav		2	115				Joint SC														184	1,028	11%	33%	44%
Siem Reap	Angkor Thum	Svay Chek	Kandaol		41	80				Joint SC						1								247	1,084	11%	15%	26%
Siem Reap	Angkor Thum	Svay Chek	Kouk Kak		30	80				Joint SC														193	1,074	2%	13%	15%
Siem Reap	Angkor Thum	Svay Chek	Preah Kou Chas							Joint SC														67	318	15%	31%	46%
Siem Reap	Angkor Thum	Svay Chek	Svay Chek		48	120	6			1	1	1	1			1								246	1,117	1%	14%	15%
Siem Reap	Angkor Thum	Svay Chek	Ta Trav		13	89	8			Joint SC	1													267	1,444	11%	19%	30%
Siem Reap	Banteay Srei	Tbaeng	Skun				50			1														202	939	6%	7%	13%
Siem Reap	Banteay Srei	Tbaeng	Tbaeng Kaeut													1								350	1,626	2%	11%	13%
Siem Reap	Banteay Srei	Tbaeng	Tbaeng Lech		15	31							1											295	1,254	19%	19%	38%
Siem Reap	Banteay Srei	Tbaeng	Voat													1								197	894	5%	16%	20%
Siem Reap	Banteay Srei	Tbaeng	Ta Pen																					108	596	43%	10%	52%
Siem Reap	Banteay Srei	Tbaeng	Srah Khvav																					402	2,097	22%	11%	32%
Siem Reap	Banteay Srei	Tbaeng	Kouk Lean Thmei																					205	908	15%	31%	45%
Siem Reap	Banteay Srei	Tbaeng	Sasei																					94	585	28%	16%	44%
Siem Reap	Banteay Srei	Tbaeng	Thmar Choul																					68	303	17%	33%	50%
Siem Reap	Banteay Srei	Rumchek	Rovieng				18																	108	506	12%	24%	36%
Siem Reap	Banteay Srei	Khmar Sanday	Banteay Srei																					379	2,027	18%	23%	41%

Location				Category																#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M			#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Siem Reap	Chi Kraeng	Chi Kraeng	Chi Kraeng		1	10																	93	477	3%	5%	8%
Siem Reap	Chi Kraeng	Chi Kraeng	Kampong													2							148	724	14%	24%	38%
Siem Reap	Chi Kraeng	Chi Kraeng	Kampong Snao Kaeut		25	15																	93	437	14%	24%	38%
Siem Reap	Chi Kraeng	Chi Kraeng	Kampong Snao Lech			6																	126	554	4%	26%	30%
Siem Reap	Chi Kraeng	Chi Kraeng	Pring			1																	264	1,150	17%	31%	48%
Siem Reap	Chi Kraeng	Chi Kraeng	Sandan		13																		57	375	5%	21%	26%
Siem Reap	Chi Kraeng	Kampong Kdei	Kampong Kdei Muoy									1		2									113	576	2%	2%	4%
Siem Reap	Chi Kraeng	Kampong Kdei	Kampong Kdei Pir													1							148	1,072	2%	4%	6%
Siem Reap	Chi Kraeng	Kampong Kdei	Ponlueu Preah Phos	18	45																		152	777	5%	17%	22%
Siem Reap	Chi Kraeng	Kampong Kdei	Sala			33																	91	502	7%	21%	28%
Siem Reap	Chi Kraeng	Kampong Kdei	Sangkae Mean Chey		3																		127	745	11%	21%	32%
Siem Reap	Chi Kraeng	Kampong Kdei	Trapeang Chrey		13		25																91	465	24%	28%	52%
Siem Reap	Chi Kraeng	Kouk Thlok Kraom	Doun Reach		1																		187	817	20%	8%	28%
Siem Reap	Chi Kraeng	Kouk Thlok Kraom	Doun Sokh		6																		207	1,023	15%	14%	29%
Siem Reap	Chi Kraeng	Kouk Thlok Kraom	Ta Tor		26																		175	875	12%	15%	28%
Siem Reap	Chi Kraeng	Kouk Thlok Kraom	Thmei											1									132	649	9%	15%	24%
Siem Reap	Chi Kraeng	Kouk Thlok Kraom	Thnal Ta Set		37																		219	1,061	18%	11%	29%
Siem Reap	Chi Kraeng	Kouk Thlok Kraom	Trapeang Trav		18																		132	679	22%	7%	29%
Siem Reap	Chi Kraeng	Kouk Thlok Leu	Prey Thum		13																		380	1,776	10%	9%	19%
Siem Reap	Chi Kraeng	Kouk Thlok Leu	Thlok Smach		3																		117	504	5%	20%	25%
Siem Reap	Chi Kraeng	Kouk Thlok Leu	Ta Phnhea		2																		304	1,444	5%	13%	18%
Siem Reap	Chi Kraeng	Kouk Thlok Leu	Thnal		1																		154	854	23%	24%	46%
Siem Reap	Chi Kraeng	Kouk Thlok Leu	Trapeang veaeng		3																		99	491	14%	29%	43%
Siem Reap	Chi Kraeng	Kouk Thlok Leu	Khla khmum		1																		280	1,321	18%	7%	25%
Siem Reap	Chi Kraeng	Kouk Thlok Leu	Slaeng Kaong		1																		128	608	9%	12%	21%
Siem Reap	Chi Kraeng	Lveaeng Ruessei	Chambak Khpos		62												1	22	1	15			178	920	17%	12%	29%
Siem Reap	Chi Kraeng	Lveaeng Ruessei	Knong		16	55											1	29	1	24			140	533	5%	9%	14%
Siem Reap	Chi Kraeng	Lveaeng Ruessei	Kouk Ampil			28																	247	921	20%	14%	34%
Siem Reap	Chi Kraeng	Lveaeng Ruessei	Lveaeng Ruessei	4	13	53											1	14	1	12			216	1,092	5%	11%	16%
Siem Reap	Chi Kraeng	Lveaeng Ruessei	Prey Totueng			84																	302	1,963	10%	13%	23%
Siem Reap	Chi Kraeng	Lveaeng Ruessei	Ta Nguon			31																	137	665	8%	20%	28%
Siem Reap	Chi Kraeng	Lveaeng Ruessei	Ta Ong																				368	1,666	16%	9%	25%
Siem Reap	Chi Kraeng	Pongro Kraom	Pongro Muoy			41																	280	1,278	7%	23%	30%
Siem Reap	Chi Kraeng	Pongro Kraom	Pongro Pir	5	27	60											1	19					186	1,003	12%	14%	25%
Siem Reap	Chi Kraeng	Pongro Kraom	Pou		31	93											1	25	1	14			271	1,110	4%	10%	13%
Siem Reap	Chi Kraeng	Pongro Kraom	Thmei	9		77																	160	871	7%	22%	29%
Siem Reap	Chi Kraeng	Ruessei Lok	Krouch	5	92	97																	410	1,918	6%	11%	17%
Siem Reap	Chi Kraeng	Ruessei Lok	Ruessei Lok		34	82											1	29	1	23			485	2,391	15%	24%	39%

Location				Category																#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G				#SF-M	#HHs	Population	%HH P1	%HH P2
Siem Reap	Chi Kraeng	Ruessei Lok	Samraong Kanhchaot	3		6																322	1,415	27%	23%	50%	
Siem Reap	Chi Kraeng	Ruessei Lok	Spean Touch	3	12	101											1	31	1	9		285	1,233	7%	20%	28%	
Siem Reap	Chi Kraeng	Ruessei Lok	Totueng Thngai		19	26											1	21				505	2,354	18%	13%	31%	
Siem Reap	Chi Kraeng	Ruessei Lok	Trapeang Run		31																	160	718	14%	23%	38%	
Siem Reap	Chi Kraeng	Ruessei Lok	Yeang		4																	251	1,392	6%	16%	22%	
Siem Reap	Chi Kraeng	Sangvaeuy	Damrei Chhlang	8	14	27					1					4						265	1,634	6%	17%	22%	
Siem Reap	Chi Kraeng	Sangvaeuy	Kansaeng							1												377	2,095	7%	4%	11%	
Siem Reap	Chi Kraeng	Sangvaeuy	Ou		27	31																285	1,744	3%	11%	14%	
Siem Reap	Chi Kraeng	Sangvaeuy	Peak Spea		2																	352	1,657	6%	9%	14%	
Siem Reap	Chi Kraeng	Sangvaeuy	Ta Prum		35																	386	1,960	14%	11%	25%	
Siem Reap	Chi Kraeng	Sangvaeuy	Thnal Dach		14																	205	1,033	9%	10%	19%	
Siem Reap	Chi Kraeng	Spean Thnot	Lvea			65																131	660	10%	23%	34%	
Siem Reap	Chi Kraeng	Spean Thnot	Ou Kraom		15												1	17	1	10		176	808	17%	29%	46%	
Siem Reap	Chi Kraeng	Spean Thnot	Ou Leu		17		25										1	14	1	8		110	586	20%	21%	41%	
Siem Reap	Chi Kraeng	Spean Thnot	Samraong	5	22	54											1	23	1	9		103	629	26%	35%	60%	
Siem Reap	Chi Kraeng	Spean Thnot	Spean Thnot Muoy		47	97											1	24	1	19		284	1,362	4%	13%	17%	
Siem Reap	Chi Kraeng	Spean Thnot	Spean Thnot Pir		33	130					1						1	24	1	16		206	1,470	10%	12%	22%	
Siem Reap	Chi Kraeng	Spean Thnot	Thnal Kaeng		43	29											1	25	1	11		150	758	23%	27%	50%	
Siem Reap	Chi Kraeng	Spean Thnot	Thnal Louk			108															230	1,070	13%	20%	33%		
Siem Reap	Chi Kraeng	Spean Thnot	Totea	6	1	60																81	389	24%	34%	57%	
Siem Reap	Chi Kraeng	Spean Thnot	Ta Yon		1																	61	332	24%	39%	63%	
Siem Reap	Kralanh	Kampong Thkov	Khsach											1								115	713	3%	13%	16%	
Siem Reap	Kralanh	Kralanh	Pechchour											1								335	1,543	1%	7%	7%	
Siem Reap	Kralanh	Sranal	Kumru		1									1								265	1,161	3%	10%	13%	
Siem Reap	Krong Siem Reap	Chreav	Boeng		27	148																147	850	11%	18%	29%	
Siem Reap	Krong Siem Reap	Chreav	Bos Kralanh		51	23																262	1,276	26%	34%	60%	
Siem Reap	Krong Siem Reap	Chreav	Chreav		47	217					2	1	1			3						259	1,263	6%	5%	11%	
Siem Reap	Krong Siem Reap	Chreav	Khmar		16	32					1										1,016	5,091	6%	9%	15%		
Siem Reap	Krong Siem Reap	Chreav	Krasang		5	173															229	1,321	6%	5%	11%		
Siem Reap	Krong Siem Reap	Chreav	Ta Chek		44	140										1					198	971	11%	8%	19%		
Siem Reap	Krong Siem Reap	Chreav	Veal		51	299											1	20	1	12	1,000	378	1,921	9%	8%	17%	
Siem Reap	Krong Siem Reap	Nokor Thum	Anhchanh		19																	656	3,257	16%	38%	54%	
Siem Reap	Krong Siem Reap	Nokor Thum	areaks Svay		4																	131	638	13%	21%	34%	
Siem Reap	Krong Siem Reap	Nokor Thum	Srah Srang Cheung		5																	194	1,036	5%	26%	31%	
Siem Reap	Krong Siem Reap	Sala Kamraeuk	Trapeang Traeng																		1,000	218	1,027	No data	No data	No data	
Siem Reap	Krong Siem Reap	Sala Kamraeuk	Voat Bour												2							1,095	5,269	4%	4%	8%	
Siem Reap	Krong Siem Reap	Sala Kamraeuk	Voat Svay											1								951	5,864	2%	4%	6%	
Siem Reap	Krong Siem Reap	Sambuor	Chrey	11	25	116															1,000	137	641	10%	14%	23%	

Location				Category																		#Mobile kitchen village	#O & M village	#FTF village	Target Populations			
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2
Siem Reap	Krong Siem Reap	Sambuor	Pnov	8	21												1	25	1	10		179	836	3%	15%	18%		
Siem Reap	Krong Siem Reap	Sambuor	Sambour		12						1	1	1				1					229	1,088	6%	8%	13%		
Siem Reap	Krong Siem Reap	Sambuor	Ta Kong	2	24												1	18	1	10		160	778	5%	22%	27%		
Siem Reap	Krong Siem Reap	Sambuor	Veal	7	25	83																283	1,370	8%	15%	23%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Boeng	3	5	39																198	996	14%	19%	34%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Khnar	3	4	44																149	757	22%	18%	40%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Kouk Doung		1	64										1						145	734	8%	21%	29%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Krasang	7	3	33																120	492	5%	10%	16%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Popis	3	1	20																94	467	8%	20%	28%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Prama	4	17	17																167	852	20%	24%	44%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Prey Krouch	12	23	63																166	722	16%	26%	42%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Prey Pou		6	23																83	437	12%	8%	20%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Roka	5	4	30																158	990	14%	22%	36%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Ta Ros	6	2	24																134	769	13%	27%	39%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Totea	4	5	29																110	513	8%	12%	20%		
Siem Reap	Krong Siem Reap	Sangkat Krabei Riel	Trapeang Veaeng	9	3	35										2						101	532	18%	17%	35%		
Siem Reap	Krong Siem Reap	Siem Reab	Kakranh											1								575	3,000	13%	3%	15%		
Siem Reap	Krong Siem Reap	Siem Reab	Pou	5		5									1	4						570	3,257	14%	1%	15%		
Siem Reap	Krong Siem Reap	Siem Reab	Pralay			38																173	951	14%	8%	22%		
Siem Reap	Krong Siem Reap	Siem Reab	Spean Chreav			34																565	3,118	15%	10%	25%		
Siem Reap	Krong Siem Reap	Sla Kram	Chong Kausu		7										2	1						2,127	11,451	No data	No data	No data		
Siem Reap	Krong Siem Reap	Sla Kram	Dak Pou												1							536	3,338	5%	10%	15%		
Siem Reap	Krong Siem Reap	Sla Kram	Treang																			1,019	6,570	17%	8%	25%		
Siem Reap	Krong Siem Reap	Srangae	Chanlaong	18	28	132					1											127	896	12%	21%	33%		
Siem Reap	Krong Siem Reap	Srangae	Kaksekam		5											2						310	1,735	5%	9%	13%		
Siem Reap	Krong Siem Reap	Srangae	Prey Thum		15							1					1	17				139	693	31%	12%	43%		
Siem Reap	Krong Siem Reap	Srangae	Roka Thum	1	22												1	21	1	10		106	574	33%	11%	44%		
Siem Reap	Krong Siem Reap	Srangae	Srangae	2	10	60							1			1						169	903	27%	9%	37%		
Siem Reap	Krong Siem Reap	Srangae	Ta Chak	21	39	55																88	520	19%	31%	51%		
Siem Reap	Krong Siem Reap	Srangae	Thnal		45												1	20	1	10		384	1,881	12%	13%	25%		
Siem Reap	Krong Siem Reap	Svay Dankum	Kantrak			49										1						356	2,145	13%	17%	29%		
Siem Reap	Krong Siem Reap	Svay Dankum	Kouk Krasang			45																225	1,145	13%	18%	31%		
Siem Reap	Krong Siem Reap	Svay Dankum	Mondol Pir												1							80	463	No data	No data	No data		
Siem Reap	Krong Siem Reap	Svay Dankum	Pou Bos			28																189	754	22%	26%	48%		
Siem Reap	Krong Siem Reap	Svay Dankum	Svay Prey			81										1						202	1,003	28%	10%	38%		
Siem Reap	Krong Siem Reap	Svay Dankum	Ta Phul												1							568	3,352	No data	No data	No data		
Siem Reap	Krong Siem Reap	Nokor Thum	Kravan		5																	235	1,142	24%	31%	55%		
Siem Reap	Krong Siem Reap	Sangkat Tuek Vil	Chrey		8																	279	1,420	7%	3%	10%		

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Siem Reap	Krong Siem Reap	Sangkat Tuek Vil	Banteay Chheu		5																		■	248	1,132	7%	9%	16%
Siem Reap	Krong Siem Reap	Sangkat Tuek Vil	Prei Thmei		1																		■	212	1,131	23%	3%	26%
Siem Reap	Krong Siem Reap	Sangkat Ampil	Bos Thum		4																		■	56	224	4%	18%	22%
Siem Reap	Krong Siem Reap	Sangkat Ampil	Trapeang Run		8																		■	164	793	15%	17%	33%
Siem Reap	Krong Siem Reap	Sangkat Ampil	Thnal Bak		7																		■	89	421	14%	26%	39%
Siem Reap	Krong Siem Reap	Sangkat Ampil	Ta Pang		1																		■	120	537	15%	34%	49%
Siem Reap	Krong Siem Reap	Sangkat Ampil	Kiri Meanon		3																		■	270	1,322	18%	43%	61%
Siem Reap	Prasat Bakong	Bakong	Stueng				25			1													■	277	1,325	2%	19%	21%
Siem Reap	Prasat Bakong	Bakong	Ovlaok										1										■	424	1,812	2%	11%	12%
Siem Reap	Prasat Bakong	Bakong	Loley																				■	321	1,516	2%	11%	14%
Siem Reap	Prasat Bakong	Bakong	Thnal Trang																				■	321	1,528	5%	15%	19%
Siem Reap	Prasat Bakong	Bakong	Kouk Trach																				■	200	995	7%	10%	17%
Siem Reap	Prasat Bakong	Bakong	Ta Phouk																				■	166	757	2%	10%	12%
Siem Reap	Prasat Bakong	Ballangk	Prum Kod						1														■	173	832	7%	12%	19%
Siem Reap	Prasat Bakong	Ballangk	Krapeu																				■	153	734	11%	4%	15%
Siem Reap	Prasat Bakong	Ballangk	Kouk Ruessei																				■	156	718	2%	6%	8%
Siem Reap	Prasat Bakong	Ballangk	Popel																				■	81	429	12%	11%	22%
Siem Reap	Prasat Bakong	Ballangk	Snar Sangkream										1										■	232	1,137	13%	5%	18%
Siem Reap	Prasat Bakong	Ballangk	Trach																				■	275	1,297	3%	14%	17%
Siem Reap	Prasat Bakong	Ballangk	Thlok Kambot																				■	98	499	6%	9%	15%
Siem Reap	Prasat Bakong	Ballangk	Ta Koy																				■	115	587	12%	3%	16%
Siem Reap	Prasat Bakong	Kandaek	Kouk Thlok		14	23																	■	335	1,659	3%	2%	5%
Siem Reap	Prasat Bakong	Kandaek	Kouk Tnaot									1	1										■	316	1,617	5%	10%	15%
Siem Reap	Prasat Bakong	Kandaek	L"ak													1							■	197	887	4%	12%	17%
Siem Reap	Prasat Bakong	Kandaek	Spean K"ae													1							■	374	1,686	9%	12%	21%
Siem Reap	Prasat Bakong	Kandaek	Trapeang Tuem		31	29										3							■	283	1,297	7%	11%	18%
Siem Reap	Prasat Bakong	Kandaek	Chrey																				■	389	2,155	6%	6%	12%
Siem Reap	Prasat Bakong	Kandaek	Ou																				■	326	1,543	4%	5%	8%
Siem Reap	Prasat Bakong	Kandaek	Chres																				■	263	1,164	10%	8%	18%
Siem Reap	Prasat Bakong	Kandaek	Khun Mouk																				■	221	1,059	7%	11%	18%
Siem Reap	Prasat Bakong	Kandaek	Trang																				■	196	1,064	6%	6%	12%
Siem Reap	Prasat Bakong	Kantreang	Angkrong														6						■	229	1,257	1%	4%	6%
Siem Reap	Prasat Bakong	Kantreang	Kantreang									1	1				1						■	274	1,215	4%	5%	9%
Siem Reap	Prasat Bakong	Kantreang	Souphi														1						■	273	1,447	3%	6%	9%
Siem Reap	Prasat Bakong	Kantreang	Sret Khang Kaeut																				■	260	1,274	3%	4%	7%
Siem Reap	Prasat Bakong	Kantreang	Sret Khang Lech		4	14											1						■	164	1,083	3%	4%	7%
Siem Reap	Prasat Bakong	Kantreang	Ta Trav	23	8	20																	■	243	1,154	3%	3%	6%
Siem Reap	Prasat Bakong	Kantreang	Trapeang Thnal	4	9						1												■	210	1,142	6%	2%	9%



Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations			
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFi	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFi	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2
Siem Reap	Prasat Bakong	Kantreang	Pongro																			284	1,208	3%	9%	12%	
Siem Reap	Prasat Bakong	Mean Chey	Chea Sman	11																		185	1,011	5%	21%	26%	
Siem Reap	Prasat Bakong	Mean Chey	Doun Num	10																		249	1,300	4%	17%	21%	
Siem Reap	Prasat Bakong	Trapeang Thum	Roka Kambot													1						197	973	18%	6%	23%	
Siem Reap	Puok	Kaev Poar	Kouk Ruessei										1									202	1,039	8%	10%	18%	
Siem Reap	Puok	Kaev Poar	Thmei																			94	435	3%	18%	21%	
Siem Reap	Puok	Kaev Poar	Roka Yea																			140	778	16%	13%	29%	
Siem Reap	Puok	Kaev Poar	Kouk Pou																			167	840	1%	7%	8%	
Siem Reap	Puok	Kaev Poar	Svay Chek																			156	864	9%	16%	26%	
Siem Reap	Puok	Kaev Poar	Peam Ta Uor																			236	1,229	11%	22%	32%	
Siem Reap	Puok	Kaev Poar	Kamphem																			217	1,015	2%	13%	15%	
Siem Reap	Puok	Kaev Poar	Prey Danghaeum																			128	798	8%	4%	12%	
Siem Reap	Puok	Mukh Paen	Ta Trav																			216	1,067	8%	23%	31%	
Siem Reap	Puok	Mukh Paen	Kouk Run																			152	684	17%	22%	39%	
Siem Reap	Puok	Mukh Paen	Trakiet																			189	881	14%	24%	38%	
Siem Reap	Puok	Mukh Paen	Mukh Paen																			225	1,107	7%	25%	32%	
Siem Reap	Puok	Mukh Paen	Sva Huol																			228	977	8%	12%	20%	
Siem Reap	Puok	Mukh Paen	Kouk Reang																			203	959	6%	27%	33%	
Siem Reap	Puok	Khnat	Chrolong										1									218	966	19%	23%	41%	
Siem Reap	Puok	Khnat	Prey Thlok					1														168	838	15%	23%	37%	
Siem Reap	Puok	Khnat	Boeng Khnar																			122	628	16%	16%	32%	
Siem Reap	Puok	Khnat	Pralay																			185	931	3%	20%	23%	
Siem Reap	Puok	Khnat	Svay																			127	623	16%	22%	37%	
Siem Reap	Puok	Khnat	Prey Kmeng																			101	595	3%	15%	18%	
Siem Reap	Puok	Khnat	Ampil Peam																			299	1,383	17%	15%	31%	
Siem Reap	Puok	Khnat	Khnat																			200	1,052	9%	12%	21%	
Siem Reap	Puok	Khnat	Kouk Trach																			221	1,065	14%	13%	27%	
Siem Reap	Puok	Khnat	Kouk Snuol																			276	1,153	28%	10%	38%	
Siem Reap	Puok	Khnat	Trameng																			102	552	11%	27%	38%	
Siem Reap	Puok	Puok	Chambak Haer											1								497	2,546	6%	4%	9%	
Siem Reap	Puok	Puok	Kouk Chuon													1						123	614	2%	2%	4%	
Siem Reap	Puok	Puok	Kouk Thmei										1	1		2						376	2,348	2%	3%	4%	
Siem Reap	Puok	Puok	Puok Chas			101								1								307	1,424	2%	4%	6%	
Siem Reap	Puok	Puok	Kouk Doung																			274	1,604	4%	6%	10%	
Siem Reap	Puok	Puok	Kouk Srok																			215	1,163	No data	4%	4%	
Siem Reap	Puok	Puok	Ou Ta Prak																			232	964	5%	9%	14%	
Siem Reap	Puok	Puok	Kampong Ta Yang																			233	1,156	No data	4%	4%	
Siem Reap	Puok	Puok	Prayut																			249	1,409	1%	4%	5%	

Location				Category																#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFi	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M			#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2
Siem Reap	Puok	Puok	Ta Tok																				238	1,286	3%	6%	9%
Siem Reap	Puok	Puok	Puok Thmei																				109	616	3%	4%	6%
Siem Reap	Puok	Samraong Yea	Ampil		3	93																	181	748	4%	6%	10%
Siem Reap	Puok	Samraong Yea	Doun Sva		1	152																	301	1,479	14%	14%	27%
Siem Reap	Puok	Samraong Yea	Prasat													1							215	1,092	3%	2%	6%
Siem Reap	Puok	Samraong Yea	Prey Veang			114																	283	1,372	3%	7%	9%
Siem Reap	Puok	Samraong Yea	Samraong Yea													1							129	553	6%	7%	13%
Siem Reap	Puok	Samraong Yea	Ta Chet													2							183	828	3%	9%	12%
Siem Reap	Puok	Sasar Sdam	Sasar Sdam										1	1		1							179	871	No data	6%	6%
Siem Reap	Puok	Sasar Sdam	Svay													2							376	1,735	0%	8%	9%
Siem Reap	Puok	Sasar Sdam	Kouk Pnov																				137	696	1%	10%	10%
Siem Reap	Puok	Sasar Sdam	Pongro Thmei																				107	648	No data	9%	9%
Siem Reap	Puok	Sasar Sdam	Chan Ta Say																				146	707	4%	21%	24%
Siem Reap	Puok	Sasar Sdam	Kouk Run																				153	971	3%	10%	14%
Siem Reap	Puok	Sasar Sdam	Kouk Chas																				66	323	No data	No data	No data
Siem Reap	Puok	Sasar Sdam	Kouk Kandal																				105	466	1%	16%	17%
Siem Reap	Puok	Sasar Sdam	Pongro Chas																				178	885	4%	10%	14%
Siem Reap	Puok	Lvea	Lvea																				306	1,506	11%	24%	35%
Siem Reap	Puok	Lvea	Roka																				175	867	13%	18%	31%
Siem Reap	Puok	Lvea	Snao																				157	939	6%	12%	18%
Siem Reap	Puok	Lvea	Stueng Preah Srok																				254	1,426	9%	27%	36%
Siem Reap	Puok	Lvea	Kumru																				138	760	17%	25%	42%
Siem Reap	Puok	Lvea	Preah Angk Trong																				122	573	13%	30%	43%
Siem Reap	Puok	Lvea	Doun Tro																				204	991	6%	9%	15%
Siem Reap	Puok	Yeang	Yeang										1										331	1,403	2%	21%	23%
Siem Reap	Puok	Yeang	Chong Thnal																				235	1,085	14%	19%	33%
Siem Reap	Puok	Yeang	Sokh San																				131	678	6%	25%	32%
Siem Reap	Puok	Yeang	Soun Sa																				130	675	17%	19%	36%
Siem Reap	Puok	Yeang	Kanhchan Kuy																				221	1,056	5%	16%	28%
Siem Reap	Soutr Nikom	Chan Sa	Baek Kamphleung	12	49	30										3							130	584	10%	13%	23%
Siem Reap	Soutr Nikom	Chan Sa	Chan Sar Cheung		4		55			1													52	264	12%	17%	29%
Siem Reap	Soutr Nikom	Chan Sa	Chan Sar Tboung																				83	380	9%	20%	28%
Siem Reap	Soutr Nikom	Chan Sa	Chbar Leu																				108	576	8%	20%	27%
Siem Reap	Soutr Nikom	Chan Sa	Choam																				131	527	8%	29%	36%
Siem Reap	Soutr Nikom	Chan Sa	Chub																				98	552	7%	33%	40%
Siem Reap	Soutr Nikom	Chan Sa	Doun Diev																				163	853	6%	15%	21%
Siem Reap	Soutr Nikom	Chan Sa	Kansaeng Kraom				20																116	665	12%	15%	28%
Siem Reap	Soutr Nikom	Chan Sa	Kansaeng Leu				15																116	568	11%	16%	27%

Location				Category																#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M			#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2
Siem Reap	Soutr Nikom	Chan Sa	Kouk Chen	20	18	36																	137	693	3%	15%	18%
Siem Reap	Soutr Nikom	Chan Sa	Kouk Toeng																				97	441	15%	20%	35%
Siem Reap	Soutr Nikom	Chan Sa	Sanlaong										1										96	459	14%	25%	38%
Siem Reap	Soutr Nikom	Chan Sa	Srae Prei																				128	519	13%	20%	33%
Siem Reap	Soutr Nikom	Chan Sa	Svay sa																				66	345	22%	6%	29%
Siem Reap	Soutr Nikom	Chan Sa	Ta Taok Cheung																				43	69	28%	12%	40%
Siem Reap	Soutr Nikom	Chan Sa	Ta Taok Kandal																				119	540	26%	17%	43%
Siem Reap	Soutr Nikom	Chan Sa	Thnal									1											55	231	6%	15%	20%
Siem Reap	Soutr Nikom	Chan Sa	Trapeang Tuk																				95	488	14%	17%	31%
Siem Reap	Soutr Nikom	Chan Sa	Ta Taok Lech																				116	544	19%	15%	34%
Siem Reap	Soutr Nikom	Dam Daek	Dam Daek Phsar													2							360	1,995	4%	5%	9%
Siem Reap	Soutr Nikom	Dam Daek	Dam Daek Thmei													1							172	885	1%	4%	5%
Siem Reap	Soutr Nikom	Dam Daek	Doun Hong											1									209	1,183	18%	13%	30%
Siem Reap	Soutr Nikom	Khnar Pou	Bos				39			Joint Chob						1	1	24	1	10			235	1,444	14%	8%	22%
Siem Reap	Soutr Nikom	Khnar Pou	Bos Thum							1													93	637	9%	7%	16%
Siem Reap	Soutr Nikom	Khnar Pou	Chhuk							Joint Chob							1	32	1	24			99	596	12%	11%	22%
Siem Reap	Soutr Nikom	Khnar Pou	Chob				8			1							1	13	1	12			93	427	21%	21%	41%
Siem Reap	Soutr Nikom	Khnar Pou	Damrei Chhlang				13			Joint Chob						2	1	20	1	16			87	440	44%	11%	55%
Siem Reap	Soutr Nikom	Khnar Pou	Rumdeng				4			Joint Chob							1	12	1	11			135	734	15%	22%	37%
Siem Reap	Soutr Nikom	Khnar Pou	Sambat				9			Joint Chob							1	26	1	16			155	745	15%	14%	29%
Siem Reap	Soutr Nikom	Khnar Pou	Samraong				25			Joint Chob							1	21	1	10			241	1,159	10%	10%	20%
Siem Reap	Soutr Nikom	Kien Sangkae	Thnal Chaek											1									324	1,554	11%	13%	24%
Siem Reap	Soutr Nikom	Popel	Damrei Koun													2							191	909	16%	18%	35%
Siem Reap	Soutr Nikom	Popel	Prey Lean										1			3							292	1,508	10%	26%	36%
Siem Reap	Soutr Nikom	Popel	Trapeang Phong													3							158	847	14%	11%	24%
Siem Reap	Soutr Nikom	Popel	Trapeang Trom													1							252	1,204	9%	16%	24%
Siem Reap	Soutr Nikom	Popel	Trapeang Trav				20																164	870	7%	16%	23%
Siem Reap	Soutr Nikom	Popel	Trapeang Prei																				117	625	5%	19%	24%
Siem Reap	Soutr Nikom	Popel	Koul Thmei																				157	831	1%	27%	27%
Siem Reap	Soutr Nikom	Popel	Kriel Pong																				102	408	13%	26%	39%
Siem Reap	Soutr Nikom	Popel	Popel Kandal																				101	470	21%	18%	39%
Siem Reap	Soutr Nikom	Popel	Koul																				155	794	7%	14%	21%
Siem Reap	Soutr Nikom	Popel	Popel Lech																				78	377	6%	6%	13%
Siem Reap	Soutr Nikom	Samraong	Bet Meas													3							152	721	7%	16%	23%
Siem Reap	Soutr Nikom	Samraong	Samraong Khang Cheu									1		1		2							283	1,590	4%	16%	20%
Siem Reap	Soutr Nikom	Samraong	Samraong Khang Tbou										1										324	1,547	8%	7%	14%
Siem Reap	Soutr Nikom	Samraong	Stueng		10	29																	294	1,243	12%	9%	21%
Siem Reap	Soutr Nikom	Samraong	Svay Chrum	7	27	26																	207	1,022	7%	19%	26%

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations						
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFi	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Populatio n	%HH P1	%HH P2	%HH P1&P2		
Siem Reap	Soutr Nikom	Samraong	Thnal Chaek	11	8	41										5						<div></div>	<div></div>	<div></div>	180	806	10%	19%	29%	
Siem Reap	Soutr Nikom	Samraong	Bat Dangkao																			<div></div>			242	882	19%	11%	30%	
Siem Reap	Soutr Nikom	Samraong	Angkunh																			<div></div>			198	993	7%	25%	32%	
Siem Reap	Soutr Nikom	Samraong	Krang Khcheay																			<div></div>			188	993	10%	22%	33%	
Siem Reap	Srei Snam	Chrouy Neang Nguon	Ampov Dieb		39	128					1											<div></div>	<div></div>	<div></div>	352	2,108	7%	20%	27%	
Siem Reap	Srei Snam	Chrouy Neang Nguon	Chrouy Neang Nguon		35								1			15	1	29	1	14		<div></div>	<div></div>	<div></div>	343	1,729	7%	16%	23%	
Siem Reap	Srei Snam	Chrouy Neang Nguon	Ruessei Sanh		27	63											1	24	1	14		<div></div>	<div></div>	<div></div>	72	373	9%	11%	20%	
Siem Reap	Srei Snam	Chrouy Neang Nguon	Sdau Pok		11	86																<div></div>	<div></div>	<div></div>	96	493	6%	21%	28%	
Siem Reap	Srei Snam	Chrouy Neang Nguon	Trom Khang Cheung		22	145																<div></div>	<div></div>	<div></div>	159	673	7%	14%	21%	
Siem Reap	Srei Snam	Chrouy Neang Nguon	Trom Khang Tboung		29	116					1	1					1	25	1	13		<div></div>	<div></div>	<div></div>	164	856	3%	11%	14%	
Siem Reap	Srei Snam	Chrouy Neang Nguon	Yeay Mei Thmei		19																	<div></div>	<div></div>	<div></div>	241	1,153	25%	14%	38%	
Siem Reap	Srei Snam	Klang Hay	Klang Hay		30	82											1	26	1	8		<div></div>	<div></div>	<div></div>	87	469	13%	25%	38%	
Siem Reap	Srei Snam	Klang Hay	Kouk Thkov			63																<div></div>	<div></div>	<div></div>	76	360	2%	12%	13%	
Siem Reap	Srei Snam	Klang Hay	Lbaeuk			100																<div></div>	<div></div>	<div></div>	104	441	6%	25%	31%	
Siem Reap	Srei Snam	Klang Hay	Pongro Bat Chan			93																<div></div>	<div></div>	<div></div>	99	373	30%	10%	40%	
Siem Reap	Srei Snam	Klang Hay	Samraong		44	80																<div></div>	<div></div>	<div></div>	76	367	19%	23%	42%	
Siem Reap	Srei Snam	Klang Hay	Slaeng Kong			32																<div></div>	<div></div>	<div></div>	38	194	8%	18%	26%	
Siem Reap	Srei Snam	Klang Hay	Slaeng Ta Vet			127																<div></div>	<div></div>	<div></div>	142	666	1%	13%	14%	
Siem Reap	Srei Snam	Klang Hay	Sleng Chas			44															<div></div>		<div></div>	69	296	17%	22%	39%		
Siem Reap	Srei Snam	Moung	Kambaor		19	124							1				1	29	1	7		<div></div>	<div></div>	<div></div>	192	1,006	17%	22%	39%	
Siem Reap	Srei Snam	Moung	Khvaek		32	148											1	24				<div></div>	<div></div>	<div></div>	175	944	18%	16%	34%	
Siem Reap	Srei Snam	Moung	Lvea		15	169											1	25	1	8		<div></div>	<div></div>	<div></div>	210	1,277	13%	16%	28%	
Siem Reap	Srei Snam	Moung	Moung Khang Cheung		31	127											1	34	1	11		<div></div>	<div></div>	<div></div>	232	1,278	9%	14%	23%	
Siem Reap	Srei Snam	Moung	Moung Khang Tboung		16	101											1	28				<div></div>	<div></div>	<div></div>	156	770	5%	19%	23%	
Siem Reap	Srei Snam	Prei	Krabau			80																<div></div>	<div></div>	<div></div>	81	416	3%	13%	16%	
Siem Reap	Srei Snam	Prei	Krouch Char			91															<div></div>	<div></div>	<div></div>	96	579	1%	9%	10%		
Siem Reap	Srei Snam	Prei	Prei Muoy			181						1										<div></div>	<div></div>	<div></div>	232	1,211	1%	10%	11%	
Siem Reap	Srei Snam	Prei	Prei Pir			169							1									<div></div>	<div></div>	<div></div>	204	1,002	1%	12%	13%	
Siem Reap	Srei Snam	Prei	Tram Sasar		20	149					1											<div></div>	<div></div>	<div></div>	200	1,110	3%	14%	13%	
Siem Reap	Srei Snam	Slaeng Spean	Chamkar Chek		13	104					1											<div></div>	<div></div>	<div></div>	202	1,407	16%	19%	36%	
Siem Reap	Srei Snam	Slaeng Spean	Chranieng			109						1	1										<div></div>	<div></div>	<div></div>	176	875	10%	16%	26%
Siem Reap	Srei Snam	Slaeng Spean	Damnak Damrei		10												1	33					<div></div>	<div></div>	<div></div>	100	554	1%	5%	6%
Siem Reap	Srei Snam	Slaeng Spean	Phnum Dei		16																		<div></div>	<div></div>	<div></div>	179	763	6%	12%	18%
Siem Reap	Srei Snam	Slaeng Spean	Preah Khsaet		5																		<div></div>	<div></div>	<div></div>	45	260	7%	23%	30%
Siem Reap	Srei Snam	Slaeng Spean	Slaeng Spean		41												1	14				<div></div>	<div></div>	<div></div>	459	2,222	9%	24%	33%	
Siem Reap	Srei Snam	Slaeng Spean	Thlok		55												1	20	1	9			<div></div>	<div></div>	<div></div>	242	1,288	8%	16%	24%
Siem Reap	Srei Snam	Tram Sasar	Beng			101																	<div></div>	<div></div>	<div></div>	145	913	5%	17%	22%
Siem Reap	Srei Snam	Tram Sasar	Neang Sraong		19	105											1	37	1	15			<div></div>	<div></div>	<div></div>	148	797	11%	11%	23%

Location				Category																				Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O & M village	#FTF village	#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Siem Reap	Srei Snam	Tram Sasar	Pongro		19	150											1	24	1	12			■	218	1,278	10%	22%	32%
Siem Reap	Srei Snam	Tram Sasar	Rumdeng		23												1	19					■	177	993	12%	8%	20%
Siem Reap	Srei Snam	Tram Sasar	Thlok			79																	■	150	756	8%	11%	19%
Siem Reap	Svay Leu	Svay Leu	Chob Kraom											1										152	662	2%	11%	13%
Sub-Total Siem Reap	11	58	346	364	2,904	8,073	365	0	2	7	20	14	24	17	8	101	52	1,226	41	542	191	99	180	74,964	379,512	9.9%	14%	23.5%

Cambodia HARVEST Target Villages -- Clients & Farmer beneficiaries, Sector Focus, and Target HHs/Populations (as of December 31, 2014)																												
Location				Category																	Target Populations							
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFi	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O & M village	#FTF village	#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Kampong Thom	Baray	Bailangk	Prey Ta Trav												1									259	1,276	6%	4%	10%
Kampong Thom	Baray	Boeng	Boeng Kandal		5																		■	427	1,997	8%	20%	28%
Kampong Thom	Baray	Boeng	Boeng Khang Cheung		7																		■	459	1,991	8%	14%	22%
Kampong Thom	Baray	Boeng	Boeng Khang Tboung		6																		■	463	2,006	6%	15%	22%
Kampong Thom	Baray	Sou Young	Khloy Khang Kaeut		4																		■	199	877	23%	24%	47%
Kampong Thom	Baray	Sou Young	Khloy Khang Lech		5																		■	166	816	19%	21%	41%
Kampong Thom	Baray	Sou Young	Sangkom Mean Chey		1																		■	60	241	17%	29%	47%
Kampong Thom	Baray	Svay Phleung	Paparak		2																		■	123	527	28%	23%	52%
Kampong Thom	Baray	Triel	Pnov				10																	57	244	20%	33%	53%
Kampong Thom	Baray	Pongro	Thnal Kaeng		3																		■	279	1,629	25%	10%	35%
Kampong Thom	Baray	Pongro	Srah Sambuor		5																		■	334	2,001	13%	22%	35%
Kampong Thom	Baray	Pongro	Pongro		4																		■	297	1,555	9%	13%	22%
Kampong Thom	Baray	Pongro	Ta Prey		1																		■	216	1,134	9%	13%	22%
Kampong Thom	Baray	Pongro	Tradak Pong		2																		■	369	2,020	19%	15%	34%
Kampong Thom	Baray	Pongro	Ang Tong		2																		■	195	843	No data	No data	No data
Kampong Thom	Baray	Chhuk Khsach	Kdam Ha		13																		■	342	1,558	6%	10%	15%
Kampong Thom	Baray	Chreaneang	Trapeang veaeng		6																		■	122	654	37%	13%	51%
Kampong Thom	Baray	Chreaneang	Siem Reang		1																		■	336	1,959	19%	8%	27%
Kampong Thom	Baray	Andoung Pou	Chiveakpheap		11																		■	223	1,023	3%	7%	9%
Kampong Thom	Kampong Svay	Chey	Koun Tnaot				9			1			1									■		93	426	23%	24%	47%
Kampong Thom	Kampong Svay	Chey	Lvea																			■		105	477	12%	22%	34%
Kampong Thom	Kampong Svay	Chey	Mohar	7	28	63						1					1	16				■	■	293	1,744	28%	10%	38%
Kampong Thom	Kampong Svay	Chey	Prey Tob																			■		196	1,150	11%	12%	24%
Kampong Thom	Kampong Svay	Chey	Ta Theav		34	65											1	14				■	■	125	662	42%	14%	56%
Kampong Thom	Kampong Svay	Chey	Trapeang areaks		35	87					1						1	25	1	25		■	■	202	1,646	23%	24%	47%
Kampong Thom	Kampong Svay	Damrei Slab	Damrei Slab			43																■	■	153	714	20%	14%	34%
Kampong Thom	Kampong Svay	Damrei Slab	Kab Thlok	11		72																■	■	175	789	11%	12%	23%
Kampong Thom	Kampong Svay	Damrei Slab	Sangkum	11		78																■	■	160	971	14%	3%	17%
Kampong Thom	Kampong Svay	Damrei Slab	Voa Yeav			82																■	■	270	1,163	12%	10%	21%
Kampong Thom	Kampong Svay	Kampong Kou	Bou Pueng																			■		181	870	20%	12%	32%
Kampong Thom	Kampong Svay	Kampong Kou	Kampong Kou Kraom			66																■	■	253	1,703	13%	26%	38%
Kampong Thom	Kampong Svay	Kampong Kou	Kampong Kou Leu			86							1									■	■	288	1,277	22%	20%	42%
Kampong Thom	Kampong Svay	Kampong Kou	Kaoh Krob Bay			113																■	■	304	1,482	19%	18%	37%
Kampong Thom	Kampong Svay	Kampong Kou	Khsach Chi Ros																			■		414	2,099	13%	17%	30%
Kampong Thom	Kampong Svay	Kampong Svay	Anlong Krasang																			■		145	705	27%	26%	53%
Kampong Thom	Kampong Svay	Kampong Svay	Chong Prey		46	56					1											■	■	224	1,136	20%	18%	39%
Kampong Thom	Kampong Svay	Kampong Svay	Chrang Kraham		11	49			1								1	1	23			■	■	210	1,085	28%	22%	50%
Kampong Thom	Kampong Svay	Kampong Svay	Enteak Komar	5	23						1						1	21	1	15		■	■	413	2,204	24%	21%	45%
Kampong Thom	Kampong Svay	Kampong Svay	Kampong Svay		27						1						1					■	■	227	1,238	14%	12%	27%

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations			
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFi	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#Hhs	Population	%HH P1	%HH P2
Kampong Thom	Kampong Svay	Kampong Svay	Ou Sala																			249	1,329	20%	13%	33%	
Kampong Thom	Kampong Svay	Kampong Svay	Prey Preah		32	82			1													136	644	10%	31%	42%	
Kampong Thom	Kampong Svay	Kampong Svay	Sou Chey		18																	181	906	21%	19%	41%	
Kampong Thom	Kampong Svay	Kampong Svay	Ta Am		18												1	1	24			145	758	31%	23%	54%	
Kampong Thom	Kampong Svay	Kampong Svay	Ta Paong		16	75											3	1	16			274	1,447	21%	17%	38%	
Kampong Thom	Kampong Svay	Kampong Svay	Tiem Chas		49	135					2	1	1				3					431	2,003	9%	17%	26%	
Kampong Thom	Kampong Svay	Kampong Svay	Tnaot			136																327	1,689	13%	15%	27%	
Kampong Thom	Kampong Svay	Kdei Doung	Kdei Doung		8	77						1										419	2,097	10%	11%	21%	
Kampong Thom	Kampong Svay	Kdei Doung	Ou Sambuor	12	31	148																291	1,427	11%	11%	22%	
Kampong Thom	Kampong Svay	Kdei Doung	Peam Kraeng	6		169											3					328	1,652	18%	11%	29%	
Kampong Thom	Kampong Svay	Kdei Doung	Slaeng	3		82											1					151	676	13%	9%	22%	
Kampong Thom	Kampong Svay	Ni Pechr	Doun Chhuk			63																145	733	9%	15%	24%	
Kampong Thom	Kampong Svay	Ni Pechr	Nipechr ka			117																326	1,525	17%	17%	34%	
Kampong Thom	Kampong Svay	Ni Pechr	Nipechr Kha			121																327	1,551	2%	11%	13%	
Kampong Thom	Kampong Svay	Prey Kuy	Prey Kuy		42																	219	880	5%	7%	12%	
Kampong Thom	Kampong Svay	Prey Kuy	Prey Kuy Kor		43	83						1										241	1,064	6%	6%	13%	
Kampong Thom	Kampong Svay	Prey Kuy	Bendei																			107	544	11%	22%	33%	
Kampong Thom	Kampong Svay	San Kor	Balang		21	31												1	16			155	716	22%	16%	38%	
Kampong Thom	Kampong Svay	San Kor	Chey	4		117																177	798	14%	11%	26%	
Kampong Thom	Kampong Svay	San Kor	Kbel	4	23	103											1	1	20	1	19	441	2,177	22%	10%	31%	
Kampong Thom	Kampong Svay	San Kor	Krasang Ka	8	29	134												1	22	1	21	411	2,361	12%	11%	23%	
Kampong Thom	Kampong Svay	San Kor	Krasang Kha	5		84																456	2,107	12%	11%	23%	
Kampong Thom	Kampong Svay	San Kor	Prasat	6	20	80												1	16			158	707	13%	15%	27%	
Kampong Thom	Kampong Svay	San Kor	San Kor Kha	21	17	127					1	1						1	14	1	14	475	2,581	9%	14%	24%	
Kampong Thom	Kampong Svay	San Kor	San Kor Ka														3					91	549	10%	4%	14%	
Kampong Thom	Kampong Svay	San Kor	Tang Krouch	4	39													1	21	1	19	100	605	19%	16%	35%	
Kampong Thom	Kampong Svay	San Kor	Veal			47							1									191	1,189	14%	3%	17%	
Kampong Thom	Kampong Svay	San Kor	Sampov Meas																			365	1,800	13%	14%	27%	
Kampong Thom	Kampong Svay	San Kor	Slaeng Khpos																			163	688	24%	10%	33%	
Kampong Thom	Kampong Svay	Tbaeng	Ba Kong	11	41	1					1						2	1	23	1	21	257	1,463	11%	7%	18%	
Kampong Thom	Kampong Svay	Tbaeng	Chheu Teal			106																201	1,123	10%	12%	21%	
Kampong Thom	Kampong Svay	Tbaeng	Pou	6	34	107												1	18	1	17	202	1,103	18%	5%	24%	
Kampong Thom	Kampong Svay	Tbaeng	Ruessei Cheah	5	42	71											3	1	21	1	19	248	1,178	8%	10%	17%	
Kampong Thom	Kampong Svay	Tbaeng	Ta Ream	10	26	64						1					3	1	26	1	20	323	1,643	20%	12%	31%	
Kampong Thom	Kampong Svay	Tbaeng	Tbaeng Kha	10		80																259	1,319	18%	10%	28%	
Kampong Thom	Kampong Svay	Tbaeng	Tbaeng Ka																			254	1,455	18%	10%	27%	
Kampong Thom	Kampong Svay	Tbaeng	Tram Khla	7	37	67												1	24	1	23	195	974	13%	1%	14%	
Kampong Thom	Kampong Svay	Tbaeng	Srangae																			94	477	20%	8%	28%	
Kampong Thom	Kampong Svay	Tbaeng	Prey Pras																			168	948	12%	16%	28%	



Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Kampong Thom	Kampong Svay	Tbaeng	Ta Am																			82	420	19%	17%	35%		
Kampong Thom	Kampong Svay	Tbaeng	Phlong																			131	763	20%	15%	35%		
Kampong Thom	Kampong Svay	Tbaeng	Boeng Andaeng																			180	876	18%	8%	26%		
Kampong Thom	Kampong Svay	Tbaeng	Ou Ambaeng																			93	586	25%	20%	45%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Kouk Nguon	4	52	44				1	1	1										208	967	5%	8%	13%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Krasang		21	45											1	25	1	23		245	1,075	1%	6%	7%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Lvea Choum	5	45	92	10				1											222	1,153	5%	25%	30%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Lvey																			149	621	6%	28%	34%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Ou Rumdeng	2	9		42										1	21	1	18		195	867	7%	16%	24%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Prasat																			122	559	8%	14%	22%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Prey Preal Ka	2	29	48											1	24	1	20		233	1,061	9%	8%	17%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Prey Preal Kha	3	31	49					1		1				1	15				266	1,125	2%	8%	9%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Romeang Ngoab		28	81											1	20	1	19		155	718	1%	7%	9%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Rung																			193	816	2%	15%	17%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Samraong	3	25	56					1											111	484	4%	11%	15%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Serei Vongs	16	19	100	39															196	882	6%	9%	15%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Skon							1												102	723	24%	9%	32%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Snao	3	22	97																262	1,096	No data	6%	6%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Thnal Baek	4	9						2						3					522	2,339	1%	7%	9%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Thnal Baek Kor		10																	224	980	1%	7%	9%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Trapeang Chompuk																			134	638	2%	22%	24%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Trapeang Prolit																			158	635	3%	19%	22%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Trapeang Ruessei		34	95											1	12				157	789	2%	9%	11%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Trapeang Thma																			139	603	1%	21%	21%		
Kampong Thom	Kampong Svay	Trapeang Ruessei	Voa Yeav																			108	495	10%	23%	33%		
Kampong Thom	Krong Stueng Saen	Achar Leak	Achar Leak	1	1								1	1		2						582	2,671	6%	12%	18%		
Kampong Thom	Krong Stueng Saen	Achar Leak	Krachab		7									1		1						543	2,113	5%	14%	19%		
Kampong Thom	Krong Stueng Saen	Achar Leak	Prey Banlich																			410	1,698	8%	6%	14%		
Kampong Thom	Krong Stueng Saen	Damrei Choan Khla	Balang Khang Kaeut											1								338	1,606	6%	15%	21%		
Kampong Thom	Krong Stueng Saen	Damrei Choan Khla	Balang Khang Lech		1										1							596	2,939	5%	18%	23%		
Kampong Thom	Krong Stueng Saen	Damrei Choan Khla	Damrei Choan Khla												1							309	1,308	No data	No data	No data		
Kampong Thom	Krong Stueng Saen	Kampong Krabau	Kampong Krabau												2	1						279	1,300	2%	16%	18%		
Kampong Thom	Krong Stueng Saen	Kampong Roteh	Kampong Thum												1							751	3,487	7%	5%	12%		
Kampong Thom	Krong Stueng Saen	Kampong Roteh	Kampong Roteh													1						323	1,527	28%	9%	38%		
Kampong Thom	Krong Stueng Saen	Kampong Thum	Phum Ti Bei																			47	210	No data	No data	No data		
Kampong Thom	Krong Stueng Saen	Kampong Thum	Phum Ti Pram Pir										1									140	632	No data	No data	No data		
Kampong Thom	Krong Stueng Saen	Kampong Thum	Phum Ti Muoy																			126	676	No data	No data	No data		
Kampong Thom	Krong Stueng Saen	Ou Kanthor	Boeng Lies																			76	371	25%	23%	48%		
Kampong Thom	Krong Stueng Saen	Ou Kanthor	Ou Kanthor Khang Cheung			6																219	1,040	9%	18%	27%		

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Kampong Thom	Krong Stueng Saen	Ou Kanthor	Ou Kanthor Khang Tboung	16	24	150					1	1				4						416	1,734	10%	19%	28%		
Kampong Thom	Krong Stueng Saen	Ou Kanthor	Preaek Sbov			42										2						438	1,978	13%	20%	33%		
Kampong Thom	Krong Stueng Saen	Prey Ta Hu	Kdei												1	1						513	1,885	6%	11%	17%		
Kampong Thom	Krong Stueng Saen	Prey Ta Hu	Prey Ta Hu	5	23	95						1					1	20	1	19		532	2,243	12%	17%	29%		
Kampong Thom	Krong Stueng Saen	Prey Ta Hu	Sla Kaet		15												1	11				441	1,848	17%	18%	36%		
Kampong Thom	Krong Stueng Saen	Srayov	Chambak	9	21	42											1	20	1	18		250	1,212	7%	16%	23%		
Kampong Thom	Krong Stueng Saen	Srayov	Kampong Samraong	3	49	20					1											258	1,162	7%	22%	29%		
Kampong Thom	Krong Stueng Saen	Srayov	Kamraeng		20	48										1	1	20	1	16		227	878	4%	9%	13%		
Kampong Thom	Krong Stueng Saen	Srayov	Mneav	7	13												1	19	1	16		323	1,409	3%	10%	13%		
Kampong Thom	Krong Stueng Saen	Srayov	Pou Saen Snay													1						349	1,543	8%	20%	28%		
Kampong Thom	Krong Stueng Saen	Srayov	Pou Ta Un		4																	303	1,413	12%	14%	26%		
Kampong Thom	Krong Stueng Saen	Srayov	Pramat dei	5	62						1					2						173	729	17%	6%	22%		
Kampong Thom	Krong Stueng Saen	Srayov	Puk Yuk	4	41									1		1	1	29	1	22		520	2,552	4%	6%	10%		
Kampong Thom	Krong Stueng Saen	Srayov	Roka																			547	2,557	7%	9%	17%		
Kampong Thom	Krong Stueng Saen	Srayov	Roluos		10	129					1											314	1,417	13%	16%	29%		
Kampong Thom	Krong Stueng Saen	Srayov	Srayov Cheung	8	31	81					1						1	27	1	21		465	2,029	12%	18%	30%		
Kampong Thom	Krong Stueng Saen	Srayov	Srayov Tboung	4	29	132					1		1									318	1,374	14%	22%	36%		
Kampong Thom	Krong Stueng Saen	Srayov	Trapeang Veaeng	15	26							1	1			3	1	22	1	21		339	1,563	6%	22%	28%		
Kampong Thom	Prasat Ballangk	Doung	Doung		6																	261	1,145	3%	11%	15%		
Kampong Thom	Prasat Ballangk	Doung	Ta Mom		2																	247	1,238	8%	14%	22%		
Kampong Thom	Prasat Ballangk	Kraya	Kraya Cheung		2																	324	1,636	9%	12%	21%		
Kampong Thom	Prasat Ballangk	Kraya	Kraya Tboung		25																	382	1,895	7%	15%	21%		
Kampong Thom	Prasat Ballangk	Kraya	Bos Thum		9											1						133	618	13%	12%	25%		
Kampong Thom	Prasat Ballangk	Kraya	Baray		16																	210	801	10%	15%	25%		
Kampong Thom	Prasat Ballangk	Phan Nheum	Prohut							1												223	1,087	4%	12%	16%		
Kampong Thom	Prasat Ballangk	Phan Nheum	Smaonh																			137	697	12%	25%	36%		
Kampong Thom	Prasat Ballangk	Phan Nheum	Phdiek																			203	935	14%	12%	26%		
Kampong Thom	Prasat Ballangk	Phan Nheum	Sochol																			295	1,403	4%	6%	10%		
Kampong Thom	Prasat Ballangk	Phan Nheum	Kranhung																			108	589	8%	15%	23%		
Kampong Thom	Prasat Ballangk	Sa Kream	Sakream Cheung		6																	178	875	11%	21%	31%		
Kampong Thom	Prasat Ballangk	Sa Kream	Ou Khsang		4																	268	1,648	6%	10%	16%		
Kampong Thom	Prasat Ballangk	Sa Kream	Kan Teak		5																	266	1,511	14%	10%	24%		
Kampong Thom	Prasat Ballangk	Sala Visai	Andas																			120	564	5%	21%	26%		
Kampong Thom	Prasat Ballangk	Sala Visai	Bos Veaeng	13	46	72	61			1	2											143	729	7%	15%	22%		
Kampong Thom	Prasat Ballangk	Sala Visai	Chamnar																			92	392	9%	37%	46%		
Kampong Thom	Prasat Ballangk	Sala Visai	Chey			69																93	452	3%	14%	17%		
Kampong Thom	Prasat Ballangk	Sala Visai	Dang Anteak		28												1	25	1	17		203	1,073	6%	30%	36%		
Kampong Thom	Prasat Ballangk	Sala Visai	Khmak Thmei	5	25												1	17				201	1,038	19%	24%	44%		
Kampong Thom	Prasat Ballangk	Sala Visai	Kokir																			171	831	26%	16%	43%		

Location				Category																	#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFi	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M				#HHs	Population	%HH P1	%HH P2	%HH P1&P2
Kampong Thom	Prasat Ballangk	Sala Visai	Kvan Tieng				29			1												132	717	26%	15%	42%		
Kampong Thom	Prasat Ballangk	Sala Visai	Ou Krouch		4																	93	487	4%	27%	31%		
Kampong Thom	Prasat Ballangk	Sala Visai	Ruessei Duoch	10	25		33			1	1											102	527	19%	29%	48%		
Kampong Thom	Prasat Ballangk	Sala Visai	Sala Popel																			24	113	26%	22%	48%		
Kampong Thom	Prasat Ballangk	Sala Visai	Sala Visai									1	1			4						321	2,270	8%	15%	23%		
Kampong Thom	Prasat Ballangk	Sala Visai	Srae		10																	220	906	4%	24%	28%		
Kampong Thom	Prasat Ballangk	Sala Visai	Trapeang Kraol	3	31	63	13									1	1	22	1	19		96	589	6%	13%	19%		
Kampong Thom	Prasat Ballangk	Sala Visai	Trapeang Phdiek																			115	599	19%	21%	41%		
Kampong Thom	Prasat Ballangk	Sala Visai	Trapeang Thma Chas																			134	715	15%	26%	41%		
Kampong Thom	Prasat Ballangk	Sala Visai	Trapeang Thma Thmei																			73	356	No data	No data	No data		
Kampong Thom	Prasat Ballangk	Sala Visai	Veal Lpeak																			178	894	9%	32%	41%		
Kampong Thom	Prasat Ballangk	Sameakki	Chan Serei		3																	148	671	1%	15%	16%		
Kampong Thom	Prasat Ballangk	Sameakki	Thmei		3																	214	1,029	6%	12%	18%		
Kampong Thom	Prasat Ballangk	Tuol Kreul	Chonlus									1										162	1,015	6%	17%	23%		
Kampong Thom	Prasat Ballangk	Tuol Kreul	Krapeu																			57	277	6%	17%	23%		
Kampong Thom	Prasat Ballangk	Tuol Kreul	Mreak Ka		28												1	14				185	927	5%	16%	21%		
Kampong Thom	Prasat Ballangk	Tuol Kreul	Mreak Kha		45						1						1	17	1	14		118	601	12%	14%	25%		
Kampong Thom	Prasat Ballangk	Tuol Kreul	Thnal																			195	1,031	26%	18%	44%		
Kampong Thom	Prasat Ballangk	Tuol Kreul	Thum																			103	482	32%	11%	42%		
Kampong Thom	Prasat Ballangk	Tuol Kreul	Tuol Kreul																			212	1,033	5%	23%	28%		
Kampong Thom	Prasat Sambour	Chhuk	Chhuk Stueng		31							1	1			3	1	28	1	23		173	910	5%	11%	16%		
Kampong Thom	Prasat Sambour	Chhuk	Prasat		13												1	17	1	15		227	1,093	8%	24%	32%		
Kampong Thom	Prasat Sambour	Chhuk	Veal Veaeng		1																	358	1,588	19%	19%	37%		
Kampong Thom	Prasat Sambour	Chhuk	S"lier		16												1	22	1	17		120	553	10%	26%	35%		
Kampong Thom	Prasat Sambour	Chhuk	Chhuk Boeng													4						135	515	2%	6%	8%		
Kampong Thom	Prasat Sambour	Sambour	At Su		28						1						1	16				216	1,196	21%	8%	29%		
Kampong Thom	Prasat Sambour	Sambour	Char																			114	467	8%	10%	18%		
Kampong Thom	Prasat Sambour	Sambour	Char Chrum																			153	896	9%	18%	27%		
Kampong Thom	Prasat Sambour	Sambour	Cheay Sampov		29												1	23	1	15		198	1,110	3%	13%	16%		
Kampong Thom	Prasat Sambour	Sambour	Chramas		40						1											237	1,021	3%	14%	17%		
Kampong Thom	Prasat Sambour	Sambour	Chranieng																			78	422	11%	28%	39%		
Kampong Thom	Prasat Sambour	Sambour	Kampong Chheu Teal		37	55					2	1	1			3						487	2,116	4%	4%	8%		
Kampong Thom	Prasat Sambour	Sambour	Kouk K'aek																			311	1,309	34%	26%	61%		
Kampong Thom	Prasat Sambour	Sambour	Ou Kru Kae		30												1	23	1	17		211	894	7%	13%	19%		
Kampong Thom	Prasat Sambour	Sambour	Pou Tret																			54	252	32%	6%	38%		
Kampong Thom	Prasat Sambour	Sambour	Pralay																			71	324	22%	12%	34%		
Kampong Thom	Prasat Sambour	Sambour	Preaek																			125	680	8%	8%	17%		
Kampong Thom	Prasat Sambour	Sambour	Sambour		49											3	1	19	1	16		323	1,390	13%	14%	28%		
Kampong Thom	Prasat Sambour	Sambour	Samret		25												1	14				169	628	22%	20%	42%		

Location				Category																		#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Hhs				Population	%HH P1	%HH P2	%HH P1&P2	
Kampong Thom	Prasat Sambour	Sambour	Trapeang Chuk		37	53					1													165	706	8%	17%	25%	
Kampong Thom	Prasat Sambour	Sraeung	Andoung Bei																					63	358	38%	5%	43%	
Kampong Thom	Prasat Sambour	Sraeung	Anlong Slaeng																					34	131	6%	19%	25%	
Kampong Thom	Prasat Sambour	Sraeung	Beng		28		20			1	1													110	479	32%	21%	54%	
Kampong Thom	Prasat Sambour	Sraeung	Boeng Khvaek																					26	106	10%	17%	27%	
Kampong Thom	Prasat Sambour	Sraeung	Choam Boeng									1												177	726	16%	12%	28%	
Kampong Thom	Prasat Sambour	Sraeung	Sraeung																					148	609	19%	11%	30%	
Kampong Thom	Prasat Sambour	Sraeung	Svay																					141	677	17%	17%	34%	
Kampong Thom	Prasat Sambour	Sraeung	Thmei																					241	911	7%	7%	14%	
Kampong Thom	Prasat Sambour	Sraeung	Tnaot Chuor																					58	249	4%	4%	7%	
Kampong Thom	Prasat Sambour	Sraeung	Tumnob																					364	3,538	18%	23%	41%	
Kampong Thom	Prasat Sambour	Tang Krasau	Chi Neang																					44	236	22%	31%	53%	
Kampong Thom	Prasat Sambour	Tang Krasau	Choam		9																			242	1,262	13%	12%	25%	
Kampong Thom	Prasat Sambour	Tang Krasau	Kampong Chheu Teal																					221	990	8%	1%	9%	
Kampong Thom	Prasat Sambour	Tang Krasau	Kampong krasang																					93	455	1%	17%	18%	
Kampong Thom	Prasat Sambour	Tang Krasau	Kouk Srok																					272	1,327	17%	10%	27%	
Kampong Thom	Prasat Sambour	Tang Krasau	Krabau Sraong																					62	360	9%	18%	26%	
Kampong Thom	Prasat Sambour	Tang Krasau	Pralay																					95	510	3%	17%	20%	
Kampong Thom	Prasat Sambour	Tang Krasau	Prey Kdei																					181	727	5%	9%	14%	
Kampong Thom	Prasat Sambour	Tang Krasau	Souriya																					76	312	7%	18%	24%	
Kampong Thom	Prasat Sambour	Tang Krasau	Ta Paong		11																			76	376	4%	13%	17%	
Kampong Thom	Prasat Sambour	Tang Krasau	Tang Krang																					158	631	3%	9%	12%	
Kampong Thom	Prasat Sambour	Tang Krasau	Tang Krasau																					475	2,125	3%	7%	10%	
Kampong Thom	Prasat Sambour	Tang Krasau	Tang Stoung																					129	446	5%	2%	7%	
Kampong Thom	Prasat Sambour	Tang Krasau	Thmei																					62	240	6%	10%	16%	
Kampong Thom	Prasat Sambour	Tang Krasau	Tuek Andoung										1											243	1,064	5%	17%	22%	
Kampong Thom	Sandan	Chheu Teal	Boeng Pra		3																			152	650	2%	10%	11%	
Kampong Thom	Sandan	Chheu Teal	Chheu Teal		16																			90	318	6%	9%	15%	
Kampong Thom	Sandan	Chheu Teal	Samret		5																			210	1,242	5%	8%	13%	
Kampong Thom	Sandan	Chheu Teal	Veal Pring Kraom		7																			187	958	15%	21%	36%	
Kampong Thom	Sandan	Chheu Teal	Kampong Ta Baen		6																			120	588	3%	15%	17%	
Kampong Thom	Sandan	Chheu Teal	Kae Rang		8																			222	854	2%	4%	6%	
Kampong Thom	Sandan	Mean Chey	Roneam		13											1								218	912	54%	46%	100%	
Kampong Thom	Sandan	Mean Chey	Trabaek		4																			140	584	3%	4%	7%	
Kampong Thom	Sandan	Mean Chey	Rumpuh		1																			145	692	3%	4%	6%	
Kampong Thom	Sandan	Mean Chey	Choam Phal		11																			205	843	9%	3%	12%	
Kampong Thom	Sandan	Ngan	Troeb		6																			94	438	9%	16%	25%	
Kampong Thom	Sandan	Ngan	Veal Pring Leu		3		6																	74	362	18%	8%	26%	
Kampong Thom	Sandan	Ngan	Samphi		8																			115	585	6%	18%	24%	

Location				Category																		#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Kampong Thom	Sandan	Ngan	Ngon		9																	365	1,706	10%	1%	11%			
Kampong Thom	Sandan	Ngan	Sralau		1																	98	497	10%	15%	25%			
Kampong Thom	Sandan	Ngan	Ou Tnaot		2																	105	498	1%	15%	16%			
Kampong Thom	Sandan	Sandan	Prasat Andaet		4																	169	775	8%	9%	17%			
Kampong Thom	Sandan	Sandan	Prey kokir		8																	138	669	6%	11%	17%			
Kampong Thom	Sandan	Sandan	Ba Chey		5																	231	983	1%	13%	14%			
Kampong Thom	Sandan	Sandan	Kampong Trabaek		4																	197	802	2%	7%	8%			
Kampong Thom	Sandan	Tum Ring	Tum Ar				5			1												319	1,412	8%	9%	17%			
Kampong Thom	Sandan	Klaeng	Klaeng		14																	112	445	6%	10%	17%			
Kampong Thom	Santuk	Boeng Lvea	Boeng Lvea		9	102					1	1										357	7,030	7%	16%	23%			
Kampong Thom	Santuk	Boeng Lvea	Kaoh Bangkov																			668	2,963	5%	14%	18%			
Kampong Thom	Santuk	Boeng Lvea	Sangkruoh																			227	1,265	18%	26%	43%			
Kampong Thom	Santuk	Boeng Lvea	Tbaeng		11	72					1											195	1,656	25%	22%	47%			
Kampong Thom	Santuk	Boeng Lvea	Trapeang Prei																			219	989	2%	15%	17%			
Kampong Thom	Santuk	Boeng Lvea	Trapeang Tuem																			665	1,904	3%	6%	9%			
Kampong Thom	Santuk	Chroab	Chey Mongkol																			351	1,693	16%	17%	33%			
Kampong Thom	Santuk	Chroab	Sdok Sdam																			317	1,535	8%	26%	34%			
Kampong Thom	Santuk	Chroab	Tuol Vihear																			308	1,494	9%	13%	21%			
Kampong Thom	Santuk	Kakaoh	Chey Sbai		36												1	18	1	13		298	1,452	18%	23%	42%			
Kampong Thom	Santuk	Kakaoh	Chey Chumneah		23	33											1	22	1	20		360	1,626	10%	19%	28%			
Kampong Thom	Santuk	Kakaoh	Chi Meakh		30												1	22	1	21		353	1,474	24%	14%	38%			
Kampong Thom	Santuk	Kakaoh	Kiri Von																			239	952	17%	22%	39%			
Kampong Thom	Santuk	Kakaoh	Sala Santuk																			153	628	3%	23%	26%			
Kampong Thom	Santuk	Kakaoh	Samnak								1											278	1,336	12%	14%	27%			
Kampong Thom	Santuk	Kakaoh	Santuk Knong		33												1	20				231	1,002	22%	16%	39%			
Kampong Thom	Santuk	Kakaoh	Santuk Krau		17																	213	910	6%	17%	23%			
Kampong Thom	Santuk	Kakaoh	Svay Kal		9						1	1	1				1	11				253	1,182	13%	15%	29%			
Kampong Thom	Santuk	Kakaoh	Tboung Krapeu		47												1	19	1	14		289	1,346	16%	14%	30%			
Kampong Thom	Santuk	Kampong Thma	Chheu Teal																			139	677	8%	17%	25%			
Kampong Thom	Santuk	Kampong Thma	Kampong Thma													7						304	1,161	11%	16%	27%			
Kampong Thom	Santuk	Kampong Thma	Kang Sau													1						104	534	No data	2%	2%			
Kampong Thom	Santuk	Kampong Thma	Khley		22	37					1											296	1,598	8%	24%	32%			
Kampong Thom	Santuk	Kampong Thma	Khwaek	4	20	115					1					1						162	630	2%	7%	9%			
Kampong Thom	Santuk	Kampong Thma	Prey Phlu	3	14	88																113	537	9%	27%	36%			
Kampong Thom	Santuk	Kampong Thma	S'ang	2	9	84																108	439	16%	28%	44%			
Kampong Thom	Santuk	Kampong Thma	Snao	3	23	178																269	990	8%	21%	29%			
Kampong Thom	Santuk	Kampong Thma	Thon Moung								1	1	1			1						210	869	4%	6%	10%			
Kampong Thom	Santuk	Kampong Thma	Tuol Sangkae		10	95																231	1,014	21%	15%	35%			
Kampong Thom	Santuk	Kraya	Tok																			301	1,362	8%	18%	27%			

Location				Category																		#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Kampong Thom	Santuk	Prasat	Banteay Yumreach	5	30	186					1	1	1				2					313	1,438	1%	9%	10%			
Kampong Thom	Santuk	Prasat	Chambak Chrum		35																	308	1,628	5%	11%	16%			
Kampong Thom	Santuk	Prasat	Leav	3	28				1	1												224	1,148	8%	11%	19%			
Kampong Thom	Santuk	Prasat	Prasat	4	18				Joint Leav								4					220	1,148	13%	7%	21%			
Kampong Thom	Santuk	Prasat	Sampung																			96	460	15%	12%	27%			
Kampong Thom	Santuk	Prasat	Sivottha	1	30	198					1											342	1,792	5%	7%	11%			
Kampong Thom	Santuk	Prasat	Ta Nhaok	11	18	97			Joint Leav		2											193	1,004	8%	14%	21%			
Kampong Thom	Santuk	Prasat	Tnaot Chum																			48	253	5%	8%	14%			
Kampong Thom	Santuk	Prasat	Traeuy Myab	6	35	118			Joint Leav													265	1,192	5%	13%	18%			
Kampong Thom	Santuk	Tang Krasang	Chambak Khang Cheung																			210	1,117	9%	18%	27%			
Kampong Thom	Santuk	Tang Krasang	Chheu Lving						1													114	562	3%	14%	17%			
Kampong Thom	Santuk	Tang Krasang	Prampir Meakkakra																			247	1,315	7%	21%	28%			
Kampong Thom	Santuk	Tang Krasang	Sang Khleang																			365	1,796	9%	10%	19%			
Kampong Thom	Santuk	Tang Krasang	Sangkom Thmei		34												1	16				218	982	9%	17%	26%			
Kampong Thom	Santuk	Tang Krasang	Tang Krasang									1	1									355	1,481	8%	11%	19%			
Kampong Thom	Santuk	Tang Krasang	Thomm Neath	2	46																	255	1,247	8%	16%	24%			
Kampong Thom	Santuk	Tang Krasang	Tuol Chan																			329	1,449	7%	11%	18%			
Kampong Thom	Santuk	Tang Krasang	Veang Cheung		16						1						1	21	1	17		263	1,146	10%	17%	27%			
Kampong Thom	Santuk	Tang Krasang	Veang Tboung																			279	1,621	13%	21%	34%			
Kampong Thom	Santuk	Tboung Krapeu	Ampuh																			146	632	25%	10%	36%			
Kampong Thom	Santuk	Tboung Krapeu	Chong Da																			321	1,454	24%	11%	35%			
Kampong Thom	Santuk	Tboung Krapeu	Kal Mekh			88																312	1,386	14%	24%	38%			
Kampong Thom	Santuk	Tboung Krapeu	Panhnh Chi	6	18	80						1					4					298	1,568	7%	12%	19%			
Kampong Thom	Santuk	Tboung Krapeu	Pou Khav										1				3					261	1,356	3%	12%	15%			
Kampong Thom	Santuk	Ti Pou	Nimitt		31							1	1				1	23	1	19		262	1,055	6%	17%	22%			
Kampong Thom	Santuk	Ti Pou	Samraong			39																56	249	19%	26%	45%			
Kampong Thom	Santuk	Ti Pou	Ta Preach		25	76											1	23	1	20		128	695	8%	16%	24%			
Kampong Thom	Santuk	Ti Pou	Ti Pou		27	101																165	726	9%	25%	34%			
Kampong Thom	Santuk	Ti Pou	Trapeang Trom																			93	445	10%	17%	27%			
Kampong Thom	Santuk	Ti Pou	Thmei																			133	702	9%	8%	16%			
Kampong Thom	Santuk	Ti Pou	Choam Thnanh																			112	612	11%	16%	27%			
Kampong Thom	Stoung	Banteay Stoung	Banteay Stoung			71																303	1,246	6%	22%	28%			
Kampong Thom	Stoung	Banteay Stoung	Beng			52																218	1,059	19%	19%	38%			
Kampong Thom	Stoung	Banteay Stoung	Chambak Pannhna			129																246	1,178	6%	20%	26%			
Kampong Thom	Stoung	Banteay Stoung	Chheu Teal			72																156	787	10%	20%	30%			
Kampong Thom	Stoung	Banteay Stoung	Ko Kruos			41																83	509	4%	32%	36%			
Kampong Thom	Stoung	Banteay Stoung	Kouk Sandaek			47																69	377	16%	21%	36%			
Kampong Thom	Stoung	Banteay Stoung	Ponlea Chey			55																270	1,023	26%	15%	42%			
Kampong Thom	Stoung	Banteay Stoung	Roluos			64																153	737	20%	10%	29%			

Location				Category																		#Mobile kitchen village	#O & M village	#FTF village	Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFI	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#HHs				Population	%HH P1	%HH P2	%HH P1&P2	
Kampong Thom	Stoung	Banteay Stoung	Sla Kar			96																238	1,238	14%	17%	31%			
Kampong Thom	Stoung	Banteay Stoung	Sraom Daek			72																201	911	18%	10%	28%			
Kampong Thom	Stoung	Banteay Stoung	Pou																			111	516	34%	20%	54%			
Kampong Thom	Stoung	Banteay Stoung	Ta Maeu			35																66	304	43%	6%	49%			
Kampong Thom	Stoung	Chamnar Kraom	Chamnakh			64																263	1,238	8%	10%	18%			
Kampong Thom	Stoung	Chamnar Kraom	Chi ab			46																268	1,453	14%	10%	24%			
Kampong Thom	Stoung	Chamnar Kraom	Lieb			37																80	363	20%	16%	35%			
Kampong Thom	Stoung	Chamnar Kraom	Neang Noy	8		107																194	973	14%	17%	31%			
Kampong Thom	Stoung	Chamnar Kraom	Preah Neangkoal	7		157																325	1,686	5%	15%	20%			
Kampong Thom	Stoung	Chamnar Kraom	Sampoar	3		124								1								288	1,367	4%	16%	20%			
Kampong Thom	Stoung	Chamnar Kraom	Sandan			85																236	1,297	12%	29%	41%			
Kampong Thom	Stoung	Chamnar Kraom	Spean Krong			65																481	2,249	15%	10%	24%			
Kampong Thom	Stoung	Chamnar Kraom	Srei Rongit			95																210	1,039	6%	16%	22%			
Kampong Thom	Stoung	Chamnar Leu	K'en			80																375	1,922	7%	14%	21%			
Kampong Thom	Stoung	Chamnar Leu	Khmak			120																265	1,341	8%	20%	28%			
Kampong Thom	Stoung	Chamnar Leu	Kor			69																201	913	8%	16%	24%			
Kampong Thom	Stoung	Chamnar Leu	Lhong			82																195	1,053	17%	11%	28%			
Kampong Thom	Stoung	Chamnar Leu	Phlaoch			63																139	600	11%	16%	28%			
Kampong Thom	Stoung	Chamnar Leu	Prasat			107																223	1,322	10%	25%	35%			
Kampong Thom	Stoung	Chamnar Leu	Srang			68																231	1,225	18%	19%	37%			
Kampong Thom	Stoung	Chamnar Leu	Thlok			32																175	938	7%	16%	23%			
Kampong Thom	Stoung	Chamnar Leu	Trapeang Choar			64																258	1,336	19%	5%	23%			
Kampong Thom	Stoung	Msar Krang	Chi Meas		1																	255	1,223	2%	26%	29%			
Kampong Thom	Stoung	Kampong Chen Tboung	Kampong Chen											2								291	1,506	1%	8%	9%			
Kampong Thom	Stoung	Kampong Chen Tboung	Leap Tong											2								425	2,128	0%	3%	3%			
Kampong Thom	Stoung	Kampong Chen Tboung	Chheu Teal																			319	1,534	1%	2%	3%			
Kampong Thom	Stoung	Kampong Chen Tboung	Svay Sa																			257	1,448	5%	11%	16%			
Kampong Thom	Stoung	Kampong Chen Tboung	Chi Youk																			100	508	7%	10%	17%			
Kampong Thom	Stoung	Kampong Chen Tboung	Nguon Siem																			249	1,235	7%	11%	19%			
Kampong Thom	Stoung	Peam Bang	Doun Sdaeng					44														144	752	4%	19%	23%			
Kampong Thom	Stoung	Peam Bang	Peam Bang					44														192	998	14%	13%	27%			
Kampong Thom	Stoung	Peam Bang	Pechakrei					22														74	374	8%	33%	40%			
Kampong Thom	Stoung	Pralay	Angk Khloam											1								243	1,353	5%	8%	13%			
Kampong Thom	Stoung	Rung Roeang	Bos Ta Saom			79																190	903	3%	16%	19%			
Kampong Thom	Stoung	Rung Roeang	Botum Kaeut			39																108	502	16%	24%	40%			
Kampong Thom	Stoung	Rung Roeang	Botum Lech			38																174	779	3%	30%	33%			
Kampong Thom	Stoung	Rung Roeang	Kantaeub			5																82	397	17%	24%	41%			
Kampong Thom	Stoung	Rung Roeang	Kantong Rong			50																119	513	12%	23%	35%			
Kampong Thom	Stoung	Samprouch	Mochheay											1								138	777	12%	27%	38%			



Location				Category																				Target Populations				
Province	District	Commune	Village	#Fish	#Hort.	#Rice	#Fsty	#Fish Pro.	#CFi	#CF	#SG	#Com. FS/N	#HC	#RM	#Bran. of MFI	#BDS	#FS/N-G	#FS/N-M	#SF-G	#SF-M	#Mobile kitchen village	#O & M village	#FTF village	#Hts	Population	%HH P1	%HH P2	%HH P1&P2
Kampong Thom	Stoung	Samprouch	Lvea																					147	739	28%	7%	34%
Kampong Thom	Stoung	Samprouch	Krasang Chrum Cheung																					187	931	28%	30%	58%
Kampong Thom	Stoung	Samprouch	Kouk Snay																					122	661	18%	30%	48%
Kampong Thom	Stoung	Samprouch	Pradet																					128	588	29%	10%	40%
Kampong Thom	Stoung	Samprouch	Trach Chrum																					224	1,113	36%	3%	39%
Kampong Thom	Stoung	Samprouch	Krasang Chrum Tboung																					126	811	20%	33%	52%
Kampong Thom	Stoung	Samprouch	Chambak khpos																					168	696	34%	36%	70%
Kampong Thom	Stoung	Samprouch	Slak Kranh			69																		198	1,030	9%	18%	26%
Sub-Total Kampong Thom	8	62	359	374	3,129	9,397	277	110	4	9	42	22	19	11	7	91	55	1,097	38	703	267	112	218	79,975	390,883	11%	14%	25%
Grand Total in Four Provinces	36	232	1,421	2,018	13,792	44,462	1,333	218	15	32	144	77	94	49	31	441	218	4,474	146	2,305	1,010	410	867	348,224	1,693,888	11.6%	15.5%	27.0%

- Notes:
1. # Hort – Horticulture-Client
  2. # Rice – Rice-Client
  3. # Fish – Fish-Client
  4. # Fsty – Forestry-Client
  5. # CFi – Community Fishery-Partner client
  6. # CF – Community Forestry-Partner client
  7. # Fish Pro. – Fish Processing-Client
  8. # BDS – Business Development Service-Partner client
  9. # SG – School Garden-Partner client
  10. # Com. FS/N – Commune Food Security/Nutrition-Partner client
  11. # HC – Health center-Partner client
  12. # RM – Rice miller-Partner client
  13. # Bran. of MFI – Branch of Micro-Finance Institution-Partner client
  14. #FS/N-G – Food Security and Nutrition Group-Partner client
  15. #FS/N-M – Food Security and Nutrition Member-Client
  16. #SF-G – Savings Fund Group-Partner client
  17. #SF-M – Savings Fund Member-Client
  18. FTF village – Feed The Future village

*19. O & M village – Operation and Machinery village*

*20. %HH P1 – percentage of household poor level 1 (extreme poor)*

*21. %HH P2 – percentage of household poor level 2 (normal poor)*

*22. %HH P1 & P2 – percentage of household poor (levels 1 and 2 combined)*

*Sources: Client data (Fintrac CIRIS, December 2014); Commune Database and IDPoor (Ministry of Planning, 2013)*

## ANNEX III: SNAPSHOTS



Cambodia HARVEST | Helping Address  
Rural Vulnerabilities and Ecosystem STability

### SNAPSHOT

#### Schools Educate Children about Farm Chemical Safety

**Armed with knowledge, students improve safety in their communities.**



*Photo by Cambodia HARVEST*

Students at a primary school in Kampong Thom province participate in a farm chemical training session. To date, Cambodia HARVEST has trained 5,367 children on this topic.

**“We thought nothing about safety. We didn’t wear gloves or masks when we sprayed chemicals.”**

*- SamOurn Srey Oun, a 15-year-old student.*

Like many young Cambodians, SamOurn Srey Oun helps with her family’s rice farm in Pursat province. When she finishes class, the 15-year-old secondary school student assists with tasks in the field. Until recently, SamOurn did not realize how dangerous some of this work could be. She handles fertilizers and other agro-chemicals, which, when not used properly, can cause harm to her own health and those around her, not to mention the environment.

“We thought nothing about safety,” she said. “We didn’t use protective gloves and masks when we sprayed chemicals. We wore long sleeves, but that was all.”

SamOurn began to understand the risks of not following safety precautions when applying chemicals after she took a training class organized by Cambodia HARVEST earlier this year at her school. Using interactive, hands-on techniques, a program specialist spent a full day teaching her, and 38 other seventh and eighth graders, about the safe handling of agro-chemicals. Topics included how to read and understand warning labels; how to properly wear protective gear such as masks and smocks; and how to apply safe amounts of chemicals to crops.

“Before taking the class, I was not familiar with any of these concepts. Now we follow them on our farm,” SamOurn said.

To date, 5,367 students have participated in the agro-chemical safety course. The training is part of Cambodia HARVEST’s school garden initiative, in which students learn important nutrition and agronomy concepts by tending to vegetable gardens established by the program on school grounds. Upon completing the agro-chemical course, the children educate other members of their communities, passing on potentially lifesaving lessons to their families and neighbors.

Samreth Rang, a classmate of SamOurn’s, has convinced his family to adopt safer behavior. “My uncle used to spray the field wearing only shorts. But now I’ve persuaded him to wear all of the proper protective gear. He now knows how important farm chemical safety is,” Samreth said.

Cambodia HARVEST • Snapshot • October 2014



## Cambodia HARVEST | Helping Address Rural Vulnerabilities and Ecosystem STability

# SNAPSHOT

## Community Groups Take Lead on Food Security

### Ensure Sustainable Impact on Nutrition and Hygiene



Photo by Cambodia HARVEST

Members of a food security and nutrition group participate in a cooking demonstration in Siem Reap Province. The groups organize community events to address nutrition and hygiene needs in their areas.

**“We’re making an impact in our community, and we’re making our own decisions about how to do it.”**

*- Sam Sokhut, a member of a food security and nutrition group in Siem Reap Province.*

Sam Sokhut is a member of a food security and nutrition group in Siem Reap Province. Since joining the village-based collective of 36 members in early 2014, she has helped start a savings fund that provides small loans to members; participated in cooking demonstrations; and helped build an inexpensive hand-washing station meant to be replicated by other members.

“We’re making an impact in our community, and we’re making our own decisions about how to do it,” Sam said.

Cambodia HARVEST has helped establish 218 food security and nutrition groups, the first of their kind in the country. To date, 5,033 people have registered as members, 93 percent of which are women. The groups bring together community members who want to learn how to improve food security and nutrition in their families and communities. Cambodia HARVEST is encouraging them to manage their own affairs, ensuring sustainability for years to come.

Many food security and nutrition groups have begun planning community actions, in which they identify a need in their area and address it with training events or other activities. These activities promote a variety of important concepts, including food safety and growth monitoring, a technique that ensures the healthy development of children in the first 1,000 days of life.

The groups have also established savings funds that support the development of nutrition-focused microenterprises. The funds allow members who make regular contributions to take out loans to support farming activities or small businesses. In less than half a year, the 146 funds have collected \$42,200 in contributions and provided 1,184 loans worth \$44,263. The funds are increasing access to credit for the poor by offering better interest rates than banks or microfinance institutions.

Sam is the secretary of her group’s savings fund, which has provided loans for the establishment of fruit-selling businesses and the expansion of family farms. She has no doubt that her group is well prepared to tackle future challenges. “I’m sure we’ll continue to make a positive impact for many years,” she said.

Cambodia HARVEST • Snapshot • November 2014





## Cambodia HARVEST | Helping Address Rural Vulnerabilities and Ecosystem STability

### SNAPSHOT

## With Program Support, Agribusinesses Boom

### Input Distributors Offer Products that Help Farmers Succeed



*Photo courtesy of Papaya Trading Company*

Chiv Vandy, the head of input distributor Papaya Trading Company, has seen his business expand since Cambodia HARVEST agronomists began recommending drip irrigation systems and other inputs.

**“The market for our products is rapidly expanding.”**

*– Chiv Vandy, head of Papaya Trading Company*

For years, Chiv Vandy tried to convince Cambodian farmers to use drip irrigation systems. As the head of the Papaya Trading Company, an agricultural input supply distributor with a national reach, he was in a position to sell the yield-boosting technology to thousands of farmers. “But my customers didn’t want it. I made very few sales,” he said.

With help from Cambodia HARVEST, Papaya’s drip irrigation sales have skyrocketed by 85 percent over the past three years. The program’s agronomists are promoting the systems as part of a broader horticulture technical package that also includes improved seed varieties, plastic mulch, and trellising – all of which Papaya distributes. In addition, the program has trained Papaya’s staff on a range of concepts, including integrated pest management, chemical safety, and dietary nutrition.

Over the past three years, the size of his staff has increased by 30 percent. “Cambodia HARVEST has been great for my business,” Chiv said.

Papaya is one of a number of Cambodian input supply businesses that have benefitted from working alongside Cambodia HARVEST. Prior to the program’s arrival, only two companies in the entire country sold drip irrigation systems. Now, five do. Agribusinesses specializing in seeds, fertilizers, and fish feed have also popped up or expanded, strengthening their respective value chains.

But it’s not just the businesses that have benefitted. Farmers in rural areas – the end users in the value chain – now have reliable access to a range of inputs that are essential to increasing their yields and improving their household incomes.

Village retail input suppliers – the family-run businesses in rural areas that sell directly to farmers – have also benefitted. With their shelves now stocked with program-endorsed products, their sales have increased by 70 percent, and they are better prepared to offer farmers the support and advice they need to succeed. “The market for our products is rapidly expanding. I’m very happy with how my business has grown,” Chiv said.

Cambodia HARVEST • Snapshot • December 2014



## Cambodia HARVEST | Helping Address Rural Vulnerabilities and Ecosystem STability

### SNAPSHOT

## Agriculture Officials Strengthen Skills and Knowledge

### Partnerships improve government extension services.



Photo by Cambodia HARVEST

Ep Soklean is one of 27 local agricultural officials to receive intensive training on Cambodia HARVEST's methodology. These officials are responsible for training thousands of farmers in good agricultural practices.

**"I'm really motivated to do the work, because I know I have great things to teach farmers."**

*- Ep Soklean, official with the Siem Reap Provincial Department of Agriculture*

Ep Soklean provides agricultural extension services for the Siem Reap Provincial Department of Agriculture by training farmers on techniques designed to boost productivity. Provincial officials like Ep have influence over thousands of farmers, regularly offering them guidance on a range of agricultural issues.

So it made sense when Cambodia HARVEST formed partnerships with four provincial departments of agriculture in late 2014. By promoting the program's methodology, department officials will expose numerous farmers to techniques and technologies proven to increase yields and incomes.

"Cambodia HARVEST has introduced simple, effective technology that works," Ep said. "I encourage all of my farmers to use these techniques."

In addition to helping farmers, the partnerships are building the capacity of government agriculture officials. As part of the one-year activity, 27 provincial and district personnel took part in an intensive training course. The sessions offered guidance on technical topics such as land preparation, drip irrigation, and integrated pest management, along with instruction on gender and nutrition concepts.


The program has also established 27 demonstration plots on land owned by farmers or provincial departments of agriculture. Local officials are using these plots to offer farmers hands-on training. With their bounty of healthy-looking vegetables, the plots also act as advertisements, enticing people to participate.

Before attending the training, Ep had a hard time putting her knowledge into practice. "Now I can see how it works," she said. She's also been exposed to effective practices that she'd never encountered before, such as soil substrate and live barriers.


Ep is already receiving visits from curious villagers, and a Cambodian-run organic vegetable company recently organized a trip to her office's demonstration plot. She is eager to reach as many people as possible. "I'm really motivated to do the work, because I know I have great things to teach farmers," she said.

Cambodia HARVEST • Snapshot • December 2014

## ANNEX IV: PROVINCIAL MAPS

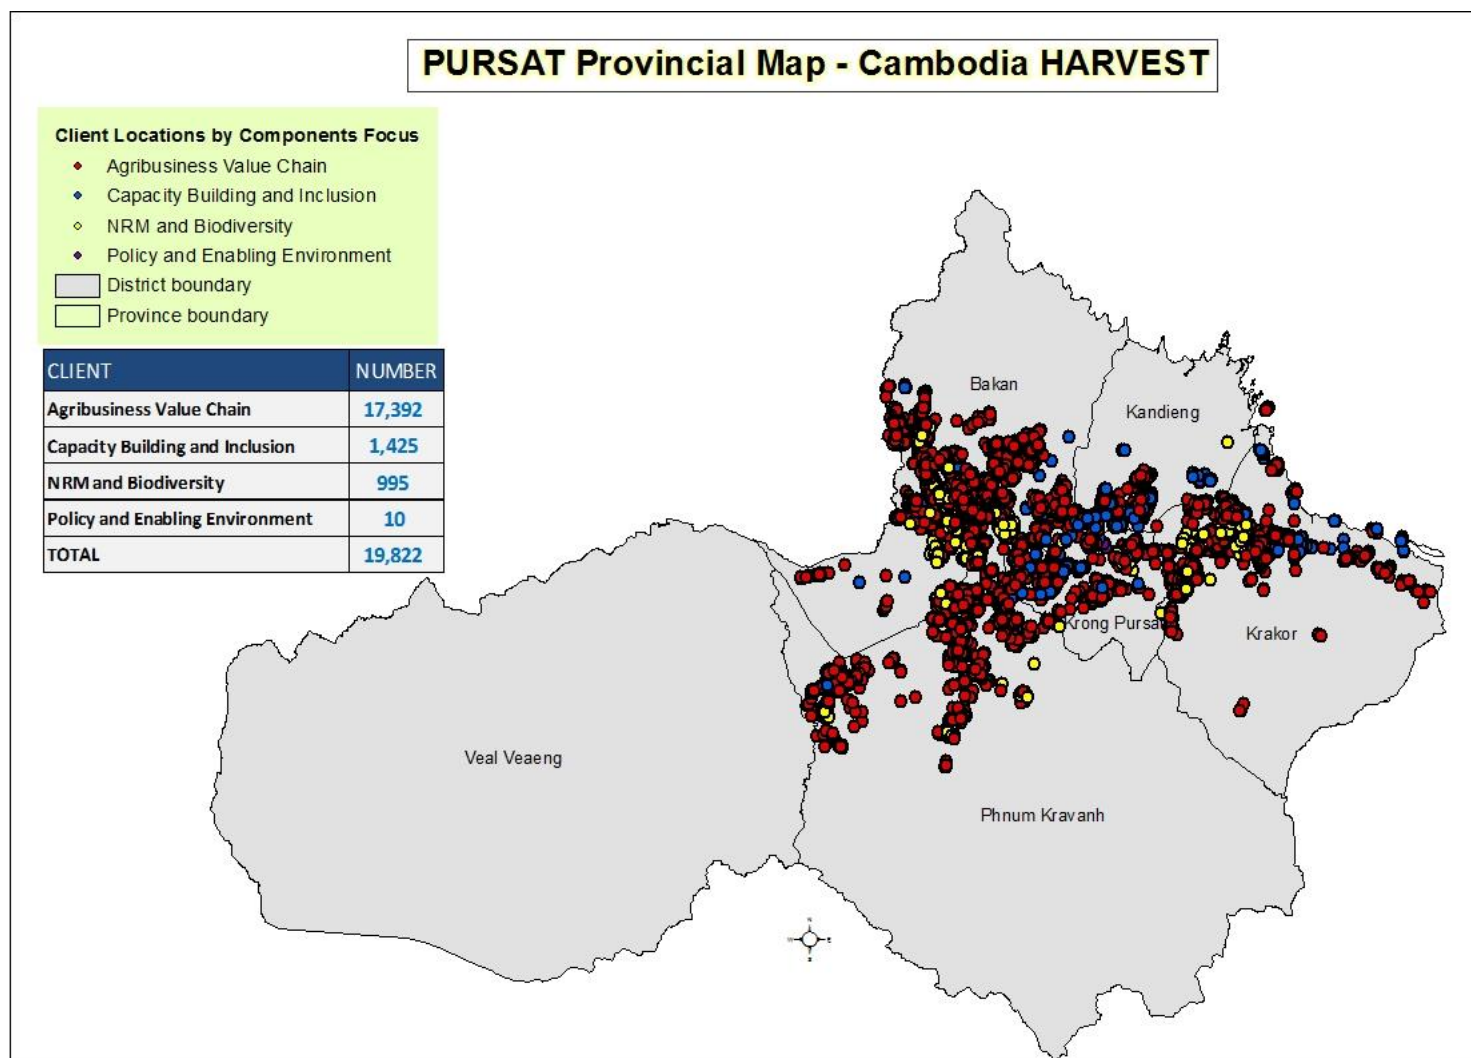




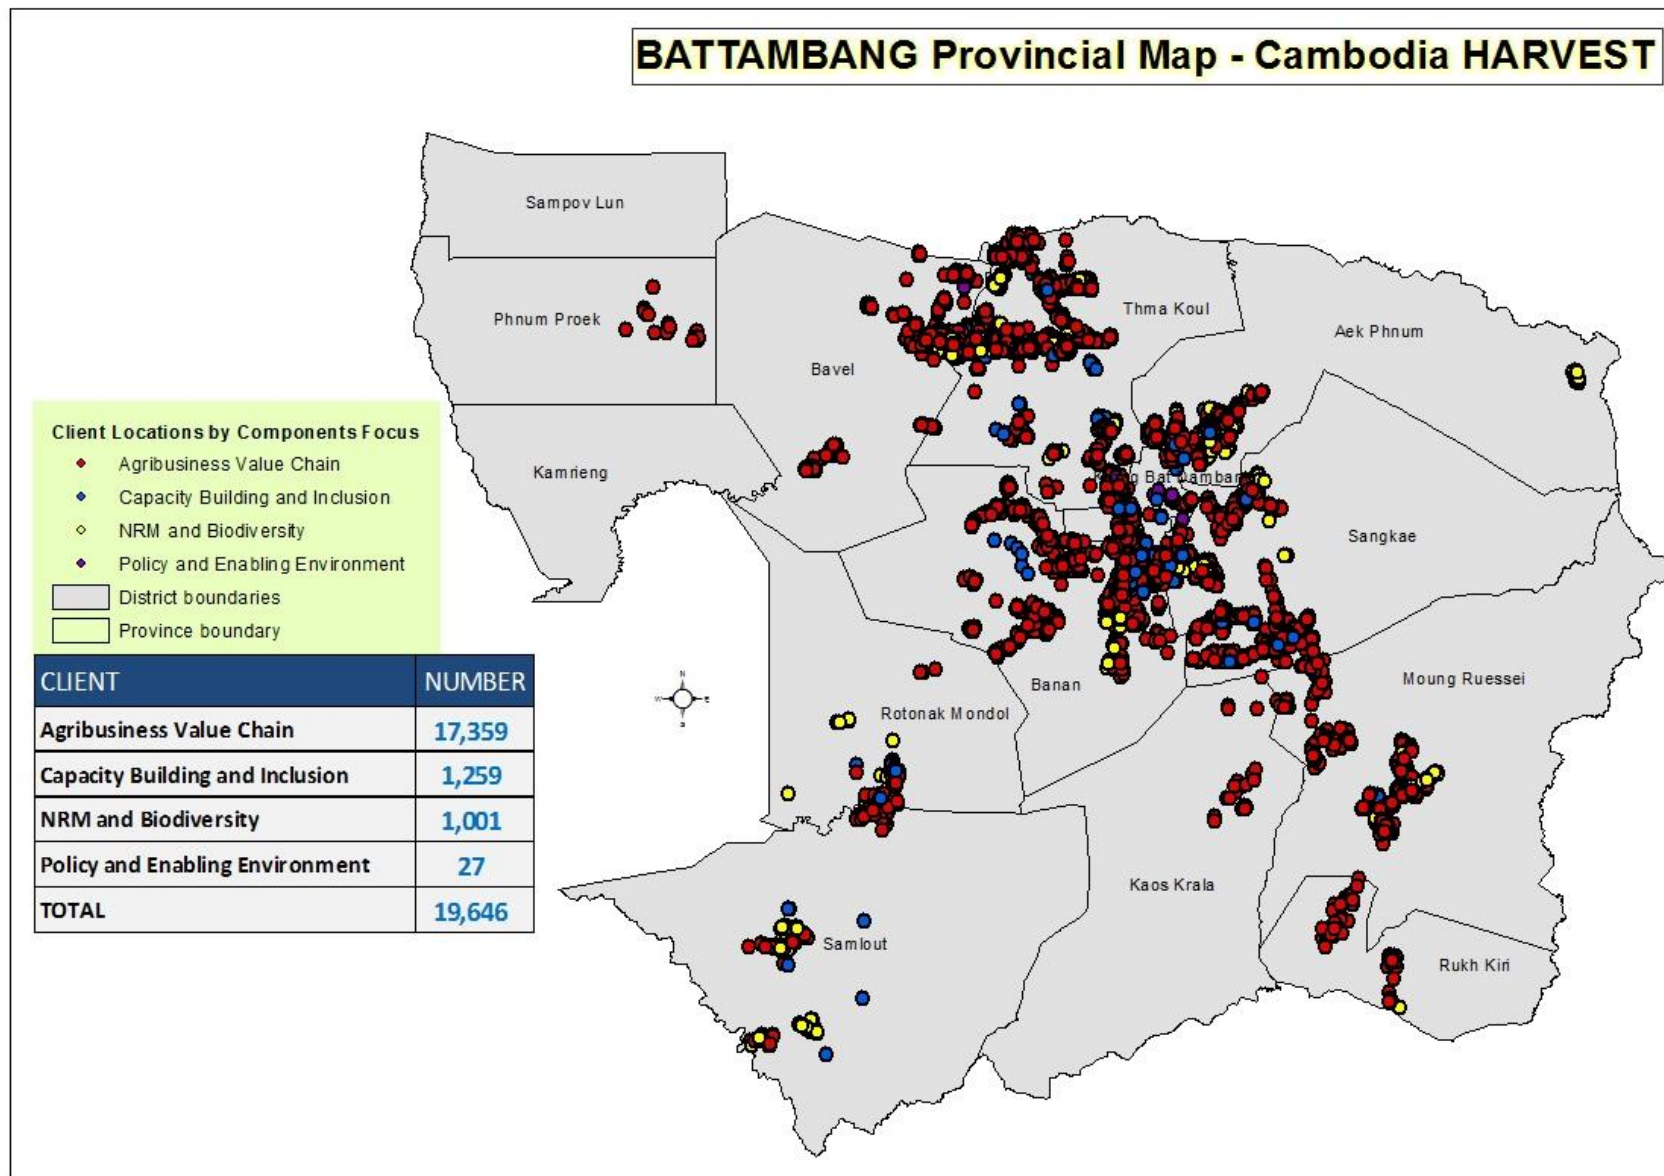


## SIEM REAP Provincial Map - Cambodia HARVEST

### Client Locations by Component Focus

- ◆ Agribusiness Value Chain
- ◆ Capacity Building and Inclusion
- ◆ NRM and Biodiversity
- ◆ Policy and Enabling Environment
- District boundaries
- Province boundary

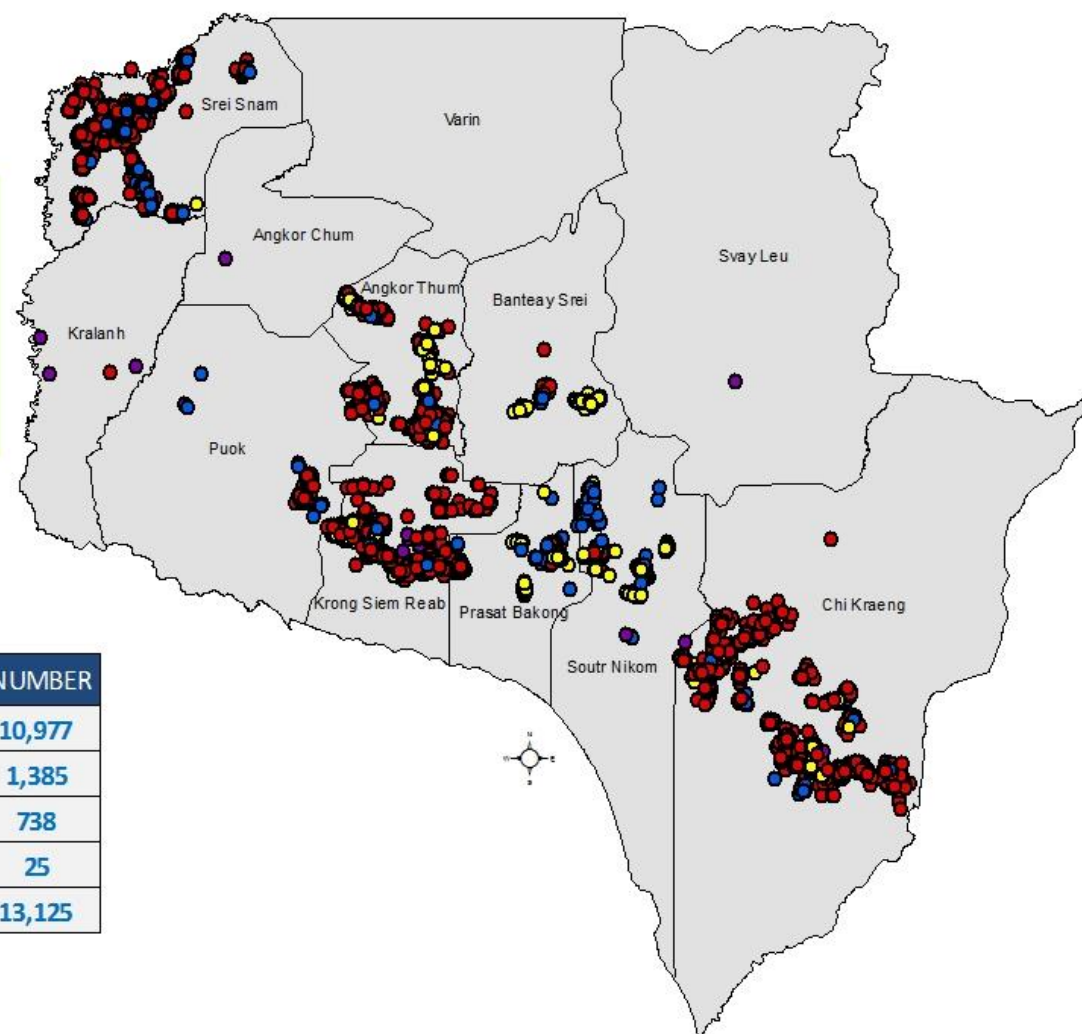

CLIENT	NUMBER
Agribusiness Value Chain	10,977
Capacity Building and Inclusion	1,385
NRM and Biodiversity	738
Policy and Enabling Environment	25
<b>TOTAL</b>	<b>13,125</b>

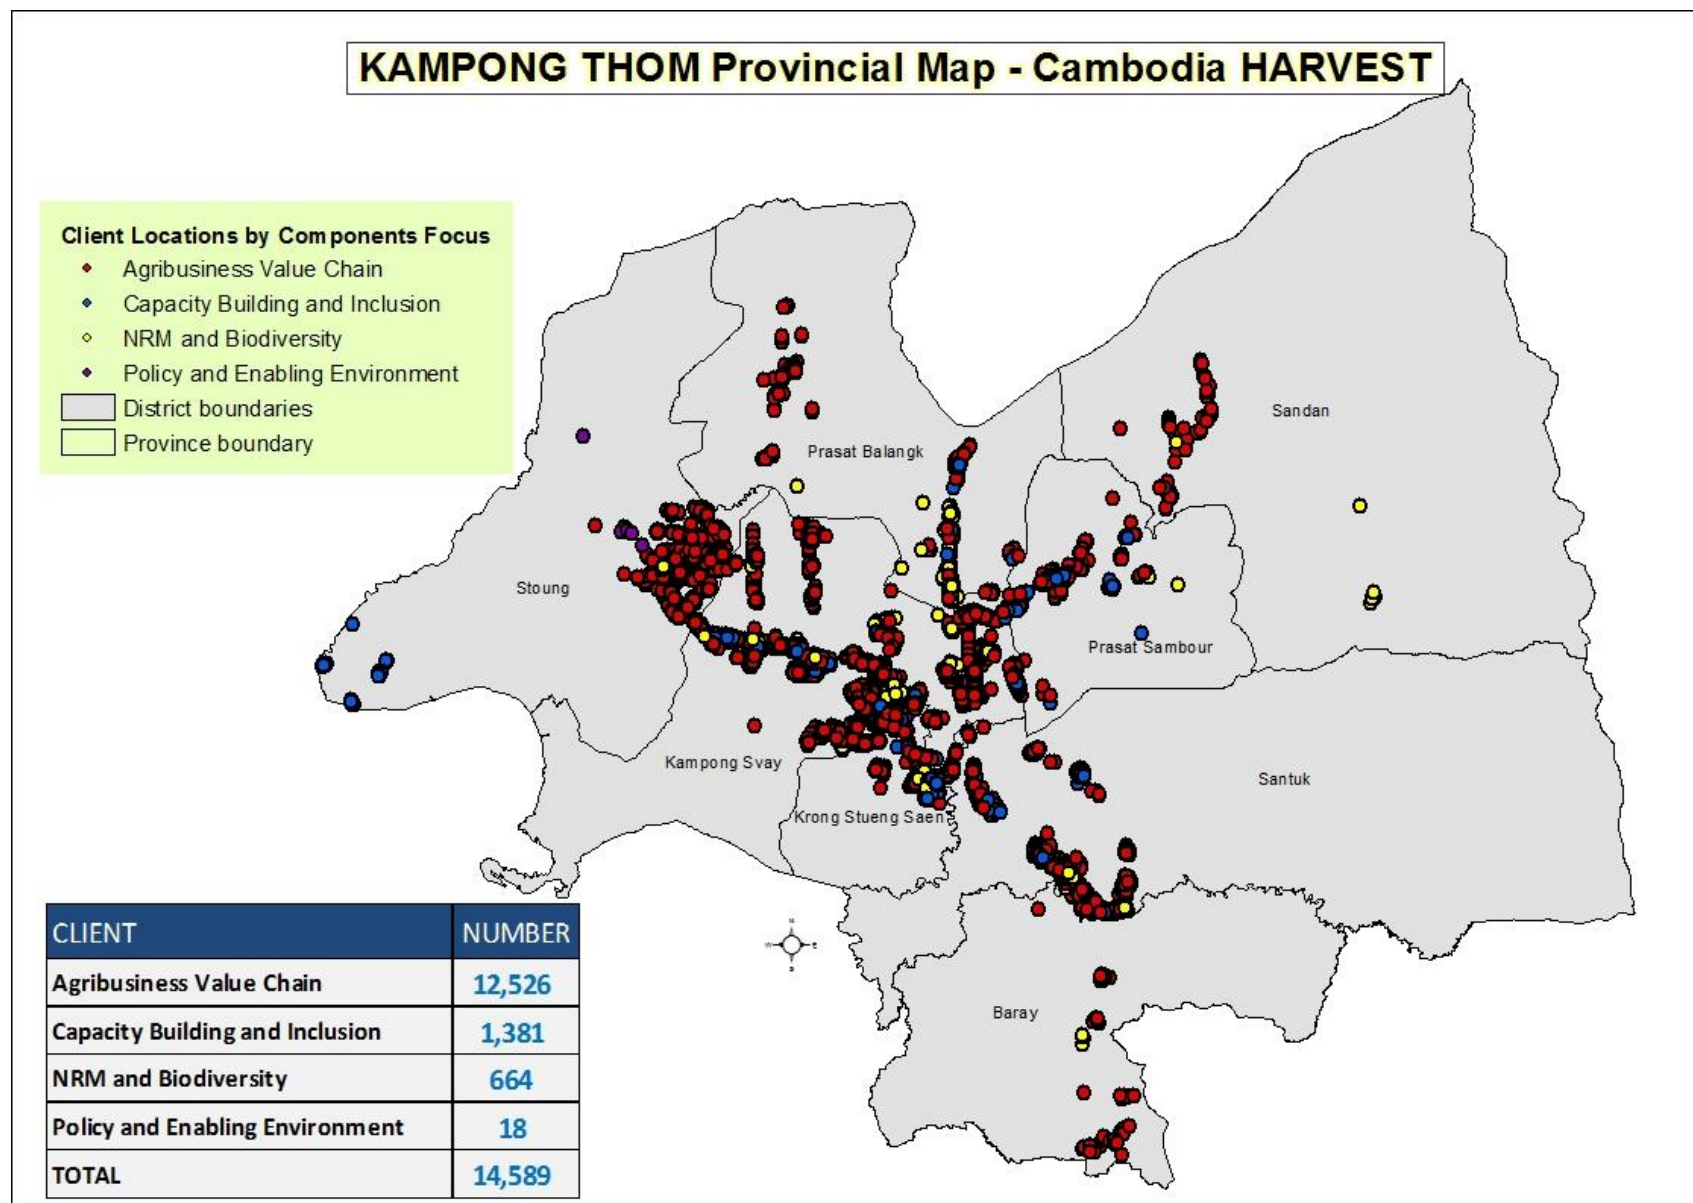

## ANNEX V: PROCUREMENT PROGRESS REPORT

Cambodia HARVEST Technology and Subcontractor Activity Report							
#	Technology Fund Awards	Cost Category	Budgeted	Expended	Balance	Status	Completion Date
01	Field Soil Sampling for Rice and Vegetable Clients	TF 01	\$ 13,772.48	\$ 13,742.00	\$ 30.48	Open	
02	Seed and Planting Material	TF 02	\$ 3,698.60	\$ 3,698.60	\$ 0.00	Closed	11/11/2013
03	Fish Day Promotion at Community Fisheries	TF 03	\$ 15,439.56	\$ 14,614.56	\$ 825.00	Closed	9/30/2011
04	Youth Workshops	TF 04	\$ 4,748.13	\$ -	\$ 4,748.13	Cancelled	12/31/2012
05	Fertilizer and Lime for Field Demonstration Sites	TF 05	\$ 850,218.00	\$ 168,753.57	\$ 681,464.43	Open	
06	Field Based Seminars, Workshops and Other Trainings	TF 06	\$ 295,410.00	\$ 295,410.00	\$ 0.00	Closed	12/31/2012
07	Agriculture Field Technology Inputs and Equipment	TF 07	\$ 1,116,923.00	\$ 1,062,449.27	\$ 54,473.73	Open	
08	SME and Input Supplier Technology Inputs and Equipment	TF 08	\$ 279,500.00	\$ 49,591.87	\$ 229,908.13	Open	
09	Irrigation Equipment and Canal Rehabilitation	TF 09	\$ 3,329,000.00	\$ 2,267,560.15	\$ 1,061,439.85	Open	
10	Aquaculture Inputs and Equipment	TF 10	\$ 1,849,405.00	\$ 850,794.73	\$ 998,610.27	Open	
11	NRM and Forestry Equipment and Activities	TF 11	\$ 340,243.70	\$ 132,091.68	\$ 208,152.02	Open	
12	Canal Rehabilitation Activities associated with AE (Subcontracts 23 and 24)	TF 12	\$ 126,233.00	\$ 98,304.00	\$ 27,929.00	Closed	
13	Polyum Canal Rehabilitation with AE sub 26	TF 13	\$ 97,250.00	\$ 97,250.00	\$ 0.00	Closed	6/13/2013
14	Community Fisheries	TF 14	\$ 628,438.00	\$ 188,199.22	\$ 440,238.78	Open	
15	Aquaculture Hatchery Equipment	TF 15	\$ 82,285.00	\$ 30,557.60	\$ 51,727.40	Open	
16	Rice Production and Postharvest Inputs	TF 16	\$ 538,378.50	\$ 192,528.65	\$ 345,849.85	Open	
17	Women's Fish Processing	TF 17	\$ 95,064.00	\$ 20,739.14	\$ 74,324.86	Open	
18	Family Nutrition Program	TF 18	\$ 129,722.00	\$ 128,932.82	\$ 789.18	Open	
19	Seeds and Planting Material for Phase II	TF 19	\$ 534,445.00	\$ 92,538.55	\$ 441,906.45	Open	
<b>Total Technology Funds Assigned</b>			<b>\$ 10,330,173.97</b>	<b>\$ 5,707,756.41</b>	<b>\$ 4,622,417.56</b>		

#	Fixed Price Subcontractor	Cost Category	Budgeted	Expended	Balance	Status	Completion Date
01	Weidemann Associates Inc. Subcontract	SUB2	\$802,800.00	\$96,387.90	\$706,412.10	Open	12/21/2015
02	Auburn University Subcontract	SUB1	\$1,123,558.00	\$167,893.94	\$955,664.06	Open	12/21/2015
03	Institute of International Education Subcontract	SUB3	\$942,868.00	\$273,021.77	\$669,846.23	Open	12/21/2015
04	Aruna Technology Limited Fixed Price Contract	SUB4	\$148,000.00	\$148,000.00	\$0.00	Closed	8/10/2011
05	Fauna and Flora International Fixed Price Contract	PF1	\$56,311.00	\$56,311.00	\$0.00	Closed	5/9/2011
06	Emerging Markets Consulting Fixed Price Contract	SUB5	\$38,607.25	\$38,607.26	(\$0.01)	Closed	6/13/2011
07	Emerging Markets Consulting	SUB5	\$65,310.86	\$65,310.86	\$0.00	Closed	11/10/2011
08	Emerging Markets Consulting Fixed Price	SUB5	\$27,406.50	\$27,406.50	\$0.00	Closed	11/28/2011
09	Fauna and Flora International	PF1	\$30,406.00	\$30,406.00	\$0.00	Closed	9/30/2011
10	Village Support Group (VSG) -	PF3	\$134,059.00	\$134,059.00	\$0.00	Closed	4/1/2013
11	Environmental Protection and Development Organization (EPDO)	PF2	\$88,208.00	\$88,208.00	\$0.00	Closed	2/28/2013
12	Agriculture Technology Services Association (ATSA) - Rural Integrated Farming for Food Security and Nutrition	PF5	\$118,578.00	\$118,578.00	\$0.00	Closed	5/30/2013
13	Srer Khmer (SK) - Pursat Food Security and Nutrition Initiative	PF5	\$155,985.00	\$155,985.00	\$0.00	Closed	5/30/2013
14	Farmer Livelihood Development (FLD) - Food Security and Nutrition Initiative	PF5	\$135,074.00	\$135,074.00	\$0.00	Closed	4/1/2013
15	Buddhism for Development (BFD) - Sustainable Livelihoods - Better Nutrition	PF5	\$98,196.00	\$98,196.00	\$0.00	Closed	4/1/2013
16	Aphivat Strey (AS) - Improving Food Security of Farmers and Fishers	PF4	\$115,850.00	\$115,850.00	\$0.00	Closed	5/30/2013
17	Ponleur Kumar (PK) - Community Forestry and FS/N	PF2	\$165,545.00	\$165,545.00	\$0.00	Closed	6/30/2013
18	Prom Vihear Thor (PVT)	PF3	\$86,952.00	\$86,952.00	\$0.00	Closed	2/28/2013
19	Aruna Technology - Climate Change Mitigation	SUB4	\$352,175.00	\$352,175.00	\$0.00	Closed	5/31/2013
20	PATH Training of Trainers Program on Family Nutrition	PF5	\$85,065.00	\$85,065.00	\$0.00	Closed	12/23/2011
21	FFI - Climate Change Mitigation	PF1	\$349,671.76	\$349,671.76	\$0.00	Closed	7/31/2013
22	FFI - NRM and Biodiversity Conservation	PF1	\$1,925,572.00	\$1,925,573.45	(\$1.45)	Closed	3/27/2014
23	Advancing Engineering (AE) - Prey Sangha Canal Rehabilitation		\$0.00	\$0.00	\$0.00	Moved to TF12	5/30/2012
24	Advancing Engineering (AE) - Plov Luogn Canal Rehabilitation		\$0.00	\$0.00	\$0.00	Moved to TF12	7/30/2012
25	Wildlife Conservation Society (WCS) - Prek Toal Core Area	PF2	\$250,409.51	\$246,384.73	\$4,024.78	Open	9/31/2014
26	Advancing Engineering (AE) - Polyum Canal Rehabilitation	TF13	\$0.00	\$0.00	\$0.00	Moved to TF13	6/30/2013
27	Reproductive And Child Alliance (RACHA) - Mobile Kitchen Project	PF5	\$92,084.36	\$92,084.36	\$0.00	Closed	1/31/2014
28	EMC - Paddy Warehouse Roundtable Session	SUB5	\$13,210.45	\$13,210.45	\$0.00	Closed	4/30/2012
29	17 Triggers - Video Series	SUB5	\$18,682.96	\$18,682.96	\$0.00	Closed	8/31/2012
30	Lom Orng Organization - Ag Machineries Operation and Maintenance	SUB5	\$35,683.37	\$35,683.37	\$0.00	Closed	7/13/2012
32	FLD - Basic Knowledge and Proper Use of Agrochemicals	PF5	\$29,304.43	\$29,304.43	\$0.00	Closed	9/21/2013
33	SK - Basic Knowledge and Proper Use of Agrochemicals	PF5	\$11,785.00	\$11,785.00	\$0.00	Closed	10/31/2012



#	Fixed Price Subcontractor	Cost Category	Budgeted	Expended	Balance	Status	Completion Date
34	ATSA - Basic Knowledge and Proper Use of Agrochemicals	PF5	\$35,461.00	\$35,461.00	\$0.00	Closed	6/30/2013
35	MEDIA One - Video Series	SUB5	\$9,073.06	\$9,073.06	\$0.00	Closed	6/8/2012
36	CDRI - Baseline Survey (replaced by Sub 45)	SUB5	\$148,630.73	\$0.00	\$148,630.73	Cancelled	3/30/2013
37	PADEK-Aquaculture in Siem Reap & Kampong Thom	PF3	\$95,392.00	\$95,392.00	\$0.00	Closed	7/31/2013
38	Action for Development (AFD) - NRM in Kampong Thom	PF2	\$56,333.00	\$56,333.00	\$0.00	Closed	7/31/2013
39	HURREDO-FS/A and Forestry in Siem Reap	PF2	\$145,941.00	\$145,941.00	\$0.00	Closed	7/31/2013
40	Rural Economic & Agriculture Development Agency	PF5	\$80,660.00	\$80,660.00	\$0.00	Closed	7/31/2013
41	Conservation International-Women's Fish Processing Project in PUR	PF3	\$86,924.90	\$86,924.90	(\$0.00)	Closed	9/15/2013
42	iDE Cambodia in Siem Reap	PF5	\$62,963.00	\$62,963.00	\$0.00	Closed	6/30/2013
43	Famer Livelihood Development- Agr. Machinery Operation Training	PF5	\$34,100.55	\$34,100.55	\$0.00	Closed	9/30/2012
44	Lom Orng	PF5	\$79,689.18	\$79,689.18	\$0.00	Closed	9/30/2012
45	CDRI - Baseline Survey	SUB5	\$160,300.73	\$160,300.73	\$0.00	Closed	3/31/2013
46	ATSA-Women's Fish Processing Project in KPT	PF3	\$61,969.00	\$61,969.00	\$0.00	Closed	11/30/2013
47	READA- Mobile Kitchen in KPT	PF5	\$92,771.09	\$92,771.09	\$0.00	Closed	5/30/2014
48	Lom Om - O & M Training 2	PF5	\$130,309.63	\$130,309.63	\$0.00	Closed	4/30/2013
49	Farmer Livelihood Development (FLD) - O & M Training 2	PF5	\$49,213.68	\$49,213.68	\$0.00	Closed	6/30/2013
51	Wathnakpheap-FS/A in Kampong Thom	PF5	\$86,484.00	\$86,484.00	\$0.00	Closed	7/31/2013
52	ATSA-FS/A in Kampong Thom	PF5	\$129,062.00	\$129,062.00	\$0.00	Closed	7/31/2013
53	Srer Khmer-FS/A in Kampong Thom	PF5	\$130,819.00	\$130,819.00	\$0.00	Closed	7/31/2013
54	VSG - FS/A in Siem Reap	PF5	\$91,942.00	\$91,942.00	\$0.00	Closed	7/31/2013
55	Srer Khmer (SK) - Pursat Food Security and Nutrition Initiative	PF5	\$149,004.43	\$149,004.43	\$0.00	Closed	6/30/2014
56	Environmental Protection and Development Organization (EPDO)	PF2	\$101,849.00	\$101,849.00	\$0.00	Closed	7/31/2014
57	Aphivat Strey (AS) - Improving Food Security of Farmers and Fishers	PF4	\$189,196.35	\$189,196.35	\$0.00	Closed	6/30/2014
58	CamAg-Soil Sampling & Analysis in Pursat					Cancelled	
59	Prom Vihear Thor (PVT)	PF3	\$87,160.23	\$87,160.23	\$0.00	Closed	7/31/2014
60	ATSA - Rural Integrated Farming for Food Security and Nutrition in PUR	PF5	\$221,645.00	\$221,645.00	\$0.00	Closed	6/30/2014
61	Ponleur Kumar (PK) - Community Forestry and FS/N	PF2	\$238,172.00	\$238,172.00	\$0.00	Closed	6/30/2014
62	Village Support Group (VSG) - in Battambang	PF3	\$184,097.00	\$184,097.00	\$0.00	Closed	6/30/2014
63	Buddhism for Development (BFD) - Sustainable Livelihoods - Better Nutrition	PF5	\$84,987.00	\$84,987.00	\$0.00	Closed	7/31/2014
65	ATSA- Food Security/Agriculture and Rice Initiative	PF5	\$68,492.36	\$68,492.36	\$0.00	Closed	1/31/2014
66	Srer Khmer- Food Security/Agriculture and Rice Initiative	PF5	\$57,791.51	\$57,791.51	\$0.00	Closed	1/31/2014
67	PADEK-Aquaculture in Siem Reap & Kampong Thom	PF3	\$34,209.67	\$34,209.67	\$0.00	Closed	1/31/2014

#	Fixed Price Subcontractor	Cost Category	Budgeted	Expended	Balance	Status	Completion Date
68	READA- FS/A in Siem Reap	PF5	\$32,246.00	\$32,246.00	\$0.00	Closed	1/31/2014
69	VSG - FS/A in Siem Reap	PF5	\$47,532.72	\$47,532.72	\$0.00	Closed	1/31/2014
70	HURREDO-FS/A and Forestry in Siem Reap	PF2	\$67,688.84	\$67,688.84	\$0.00	Closed	1/31/2014
71	AFD- FS/A and Forestry in Kampong Thom	PF2	\$68,551.00	\$68,551.00	\$0.00	Closed	1/31/2014
72	IGC - Inter-Green Consultants - NRM Baseline Study	SUB5	\$10,995.00	\$10,995.00	\$0.00	Closed	10/18/2013
73	iDE Cambodia in Siem Reap	PF5	\$38,535.00	\$38,535.00	\$0.00	Closed	6/30/2014
74	Lom Orng (LOO)- Mobile Kitchen Project in Battambang	PF5	\$106,669.47	\$78,935.40	\$27,734.07	Open	1/31/2015
75	READA- Mobile Kitchen in Siem Reap	PF5	\$108,201.67	\$80,069.20	\$28,132.47	Open	1/31/2015
76	CI-Fish Processing	PF4	\$133,276.15	\$79,965.69	\$53,310.46	Open	2/28/2015
77	PADEK-Aquaculture in Siem Reap & Kampong Thom	PF3	\$133,564.40	\$68,117.00	\$65,447.40	Open	11/30/2015
78	SK-Food Security/Agriculture and Rice Initiative	PF5	\$262,820.00	\$128,516.00	\$134,304.00	Closed	11/30/2015
79	CDRI-Replication Survey	SUB5	\$21,986.00	\$21,986.00	\$0.00	Closed	4/30/2014
80	ATSA-Food Security and Agriculture in Kampong Thom	PF5	\$316,288.00	\$154,980.00	\$161,308.00	Closed	11/30/2015
81	VSG - FS/A in Siem Reap	PF5	\$192,207.00	\$94,948.00	\$97,259.00	Closed	11/30/2015
82	READA-Food Security and Agriculture in Siem Reap	PF5	\$204,238.00	\$101,707.00	\$102,531.00	Closed	11/30/2015
83	AFD- FS/A and Forestry in Kampong Thom	FP2	\$399,754.00	\$199,076.00	\$200,678.00	Closed	11/30/2015
84	HURREDO-FS/A and Forestry in Siem Reap	PF2	\$393,432.00	\$195,926.00	\$197,506.00	Closed	11/30/2015
85	AE-Canal Rehabilitation Follow-up work	SUB5	\$19,834.00	\$4,961.00	\$14,873.00	Open	6/30/2014
86	RACHA-Mobile Kitchens in Pursat	PF5	\$116,424.00	\$69,856.00	\$46,568.00	Open	3/31/2015
87	SK-Savings Fund Facilitators in Kampong Thom and Pursat	LPTP	\$51,562.00	\$24,233.00	\$27,329.00	Open	10/31/2015
88	READA-Savings Fund Facilitators in Siem Reap	LPTP	\$34,320.00	\$16,130.00	\$18,190.00	Open	10/31/2015
89	HURREDO-Savings Fund Facilitators in Siem Reap	LPTP	\$33,178.00	\$15,592.00	\$17,586.00	Open	10/31/2015
90	ATSA-Savings Fund Facilitators in Pursat and Kampong Thom	LPTP	\$36,318.00	\$17,067.00	\$19,251.00	Open	10/31/2015
91	AS-Savings Fund Facilitators in Battambang	LPTP	\$18,158.00	\$8,683.00	\$9,475.00	Open	10/31/2015
92	VSG-Savings Fund Facilitators in Battambang and Siem Reap	LPTP	\$51,701.00	\$24,299.00	\$27,402.00	Open	10/31/2015
93	Irrigation Service Center (ISC) - FWUC Capacity Building in Pursat	SUB5	\$87,927.00	\$46,088.00	\$41,839.00	Open	10/31/2015
94	Ponleur Kumar (PK) - Saving Fund Facilitators in Pursat and Battambang	LPTP	\$52,699.00	\$24,757.00	\$27,942.00	Open	10/31/2015
95	Action for Development (AFD) - Saving Fund Facilitators in Kampong Thom	LPTP	\$34,207.00	\$16,258.00	\$17,949.00	Open	10/31/2015
96	ATSA-Plant Nutrition and Fertilizer Management Training	PF5	\$16,444.00	\$16,444.00	\$0.00	Closed	10/15/2014
97	FFI-NRM and Biodiversity Conservation	PF1	\$1,063,518.00	\$508,206.00	\$555,312.00	Open	7/15/2015
98	Lom Orng-Basics of Operation and Maintenance of Rice Milling Machinery for Small Scale Rice Millers	PF5	\$82,889.00	\$82,889.00	\$0.00	Closed	9/30/2014

#	Fixed Price Subcontractor	Cost Category	Budgeted	Expended	Balance	Status	Completion Date
99	Advancing Engineering Consulting (AE)-Design and Project Management Services	SUB5	\$44,798.00	\$33,598.50	\$11,199.50	Open	12/31/2014
100	Srer Khmer (SK) - Food Security and Nutrition Initiative in Pursat	PF5	\$122,989.00	\$41,387.56	\$81,601.44	Open	10/10/2015
101	Agriculture Technology Services Association (ATSA) - Food Security and Nutrition in Pursat	PF5	\$197,434.00	\$71,078.00	\$126,356.00	Open	10/10/2015
102	Aphivat Strey (AS) - Improving Food Security of Farmers and Fishers	PF4	\$209,357.00	\$75,369.00	\$133,988.00	Open	10/10/2015
103	Ponleur Komar (PK)-Food Security/Agriculture and Forestry	PF2	\$305,167.00	\$109,863.00	\$195,304.00	Open	10/10/2015
104	Village Support Group (VSG)-Food Security/Agriculture and Forestry	PF3	\$196,710.00	\$70,818.00	\$125,892.00	Open	11/15/2015
105	Rural Economic & Agriculture Development Agency (READA) - Mobile Kitchens in Kampong Thom	PF5	\$103,200.00	\$41,280.00	\$61,920.00	Open	8/17/2015
106	Environmental Protection and Development Organization (EPDO) - Agriculture, Aquaculture, and Forestry in PUR	PF2	\$206,081.00	\$68,699.00	\$137,382.00	Open	10/31/2014
109	Agriculture Technology Services Association (ATSA) - Agrichemical Training for Inputs Suppliers in Kampong Thom, Siem Reap, Battambang and Pursat Province	PF05	\$22,582.00	\$5,645.00	\$16,937.00	Open	3/31/2015
<b>Total Subcontractor Funds Assigned</b>			<b>\$16,327,484.80</b>	<b>\$11,060,402.02</b>	<b>\$5,267,082.78</b>		



## ANNEX VI: FINANCIAL SUMMARY

(Please see separate attached file.)

## **Cambodia HARVEST**

**No. 34 Street 310 | Sangkat  
Beong Keng Kang I  
Khan Chamkamorn | Phnom Penh | Cambodia  
Tel: 855 (0) 23 996 419  
Fax: 855 (0) 23 996 418**

**[harvest@fintrac.com](mailto:harvest@fintrac.com)  
[www.CambodiaHARVEST.org](http://www.CambodiaHARVEST.org)**
